



# SAS/OR® 14.2 User's Guide

## Project Management

The correct bibliographic citation for this manual is as follows: SAS Institute Inc. 2016. *SAS/OR® 14.2 User's Guide: Project Management*. Cary, NC: SAS Institute Inc.

**SAS/OR® 14.2 User's Guide: Project Management**

Copyright © 2016, SAS Institute Inc., Cary, NC, USA

All Rights Reserved. Produced in the United States of America.

**For a hard-copy book:** No part of this publication may be reproduced, stored in a retrieval system, or transmitted, in any form or by any means, electronic, mechanical, photocopying, or otherwise, without the prior written permission of the publisher, SAS Institute Inc.

**For a web download or e-book:** Your use of this publication shall be governed by the terms established by the vendor at the time you acquire this publication.

The scanning, uploading, and distribution of this book via the Internet or any other means without the permission of the publisher is illegal and punishable by law. Please purchase only authorized electronic editions and do not participate in or encourage electronic piracy of copyrighted materials. Your support of others' rights is appreciated.

**U.S. Government License Rights; Restricted Rights:** The Software and its documentation is commercial computer software developed at private expense and is provided with RESTRICTED RIGHTS to the United States Government. Use, duplication, or disclosure of the Software by the United States Government is subject to the license terms of this Agreement pursuant to, as applicable, FAR 12.212, DFAR 227.7202-1(a), DFAR 227.7202-3(a), and DFAR 227.7202-4, and, to the extent required under U.S. federal law, the minimum restricted rights as set out in FAR 52.227-19 (DEC 2007). If FAR 52.227-19 is applicable, this provision serves as notice under clause (c) thereof and no other notice is required to be affixed to the Software or documentation. The Government's rights in Software and documentation shall be only those set forth in this Agreement.

SAS Institute Inc., SAS Campus Drive, Cary, NC 27513-2414

November 2016

SAS® and all other SAS Institute Inc. product or service names are registered trademarks or trademarks of SAS Institute Inc. in the USA and other countries. ® indicates USA registration.

Other brand and product names are trademarks of their respective companies.

SAS software may be provided with certain third-party software, including but not limited to open-source software, which is licensed under its applicable third-party software license agreement. For license information about third-party software distributed with SAS software, refer to <http://support.sas.com/thirdpartylicenses>.

# Contents

---

Chapter 1.	What's New in SAS/OR 14.2 . . . . .	1
Chapter 2.	Using This Book . . . . .	3
Chapter 3.	Introduction to Project Management . . . . .	9
Chapter 4.	The CPM Procedure . . . . .	53
Chapter 5.	The PM Procedure . . . . .	301
Chapter 6.	The Microsoft Project Conversion Macros . . . . .	353
Chapter 7.	The DTREE Procedure . . . . .	381
Chapter 8.	The GANTT Procedure . . . . .	483
Chapter 9.	The NETDRAW Procedure . . . . .	661
Chapter 10.	The Projman Application . . . . .	773
Chapter 11.	The Earned Value Management Macros . . . . .	845
Appendix A.	Glossary of Project Management Terms . . . . .	933
Appendix B.	Glossary of Earned Value Management Terms . . . . .	947

<b>Subject Index</b>	<b>953</b>
----------------------	------------

<b>Syntax Index</b>	<b>981</b>
---------------------	------------



# Acknowledgments

---

## Credits

---

### Documentation

Writing	Gehan A. Corea, Charles B. Kelly, Radhika V. Kulkarni, Michelle Opp, Lindsey Puryear, Tien-yi D. Shaw, Keqi Yan
Editing	Anne Baxter, Virginia Clark, Ed Huddleston, Donna Sawyer
Documentation Support	Tim Arnold, Natalie Baerlocher, Remya Chandran, Melanie Gratton, Richard Liu, Jianzhe Luo, Michelle Opp, Girish Ramachandra, Daniel Underwood
Technical Review	Marianne Bohinski, Tonya Chapman, Marc-david Cohen, Donna Fulenwider, Phil Gibbs, Barbara J. Hoopes, Tao Huang, Edward P. Hughes, John Jasperse, Charles B. Kelly, Emily Lada, Michelle Opp, Bengt Pederson, Rob Pratt

---

## Software

The procedures in SAS/OR software were implemented by the Operations Research and Development Department. Substantial support was given to the project by other members of the Analytical Solutions Division. Core Development Division, Display Products Division, Graphics Division, and the Host Systems Division also contributed to this product.

In the following list, the names of the developers currently supporting the procedure are listed first. Other developers previously worked on the procedure.

CPM	Lindsey Puryear, Radhika V. Kulkarni
DTREE	Tien-Yi D. Shaw
GANTT	Gehan A. Corea, Lindsey Puryear, Radhika V. Kulkarni
NETDRAW	Lindsey Puryear, Radhika V. Kulkarni
PM	Gehan A. Corea, Radhika V. Kulkarni
PROJMAN	Charles B. Kelly
EVM Macros	Lindsey Puryear
Microsoft Conversion Macros	Liping Cai, Gehan A. Corea, Keqi Yan

## Support Groups

Software Testing	Nitin Agarwal, Marianne Bohinski, Liping Cai, Tao Huang, Edward P. Hughes, John Jasperse, Charles B. Kelly, Emily Lada, Bengt Pederson, Rob Pratt, Tugrul Sanli, Kaihong Xu
Technical Support	Tonya Chapman

## Acknowledgments

Many people have been instrumental in the development of SAS/OR software. The individuals acknowledged here have been especially helpful.

G. Jack Theurer	G. Theurer Associates
Lance Broad	New Zealand Ministry of Forestry
Richard Brockmeier	Union Electric Company
Ken Cruthers	Goodyear Tire & Rubber Company
Patricia Duffy	Auburn University

Richard A. Ehrhardt	University of North Carolina at Greensboro
Paul Hardy	Babcock & Wilcox
Don Henderson	ORI Consulting Group
Dave Jennings	Lockheed Martin
Vidyadhar G. Kulkarni	University of North Carolina at Chapel Hill
Wayne Maruska	Basin Electric Power Cooperative
Bruce Reed	Auburn University
Charles Rissmiller	Lockheed Martin
David Rubin	University of North Carolina at Chapel Hill
John Stone	North Carolina State University
Keith R. Weiss	ICI Americas Inc.

The final responsibility for the SAS System lies with SAS Institute alone. We hope that you will always let us know your opinions about the SAS System and its documentation. It is through your participation that SAS software is continuously improved.



# Chapter 1

## What's New in SAS/OR 14.2

### Contents

---

Overview . . . . .	1
Mathematical Optimization Updates . . . . .	1
Solver Performance Improvements . . . . .	1
Discrete-Event Simulation Updates . . . . .	2

---

### Overview

SAS/OR 14.2 includes performance improvements in the LP, MILP, network, and NLP solvers.

SAS Simulation Studio 14.2, a component of SAS/OR 14.2 for Windows environments, enhances its selection of modeling blocks. Details include the following:

- The new Caster block makes it easier to transfer complex objects (entities, observations, and so on) within a model.
- The Queue block adds extended queueing controls that you can use to help prevent a queue from becoming blocked.

---

### Mathematical Optimization Updates

---

#### Solver Performance Improvements

Several optimization solvers have been updated in SAS/OR 14.2, and as a result they have significantly improved their performance over that of SAS/OR 14.1. The LP, MILP, NLP, and network solver algorithms all reduce the time they require to solve benchmark optimization problems. These improvements also include the decomposition (DECOMP) algorithm for LP and MILP. You should expect to be able to solve individual optimization problems of these types more quickly. If you invoke one of these optimization solvers repeatedly (for example, within a loop), the reduction in overall solution time should be much more pronounced.

---

## Discrete-Event Simulation Updates

SAS Simulation Studio 14.2, which provides a graphical environment for building and working with discrete-event simulation models, makes two notable improvements.

The new Caster block provides a compact means of transferring more complex objects such as observations and data models between blocks in a simulation model. In SAS Simulation Studio 14.2, you can assign a generic object as an entity attribute and then use a Caster block to “cast” the object back to its original type and output it to the receiving block. However, note that the Caster block does *not* function as an object type converter. You must be aware of the original type of the objects that you are transferring and ensure that the receiving block expects the same value type.

The new **Extended Queueing Controls** on the Queue block broaden your control over how entities flow into and out of a Queue block. The primary purpose of these new controls is to help you lessen the likelihood that a Queue block becomes blocked. Blocking can occur if the first entity in the queue is unable to flow to any downstream block in the model. This prevents subsequent entities in the queue from exiting, even if they would be eligible to exit if they were in the first position in the queue.

# Chapter 2

# Using This Book

## Contents

---

Purpose . . . . .	3
Organization . . . . .	3
Typographical Conventions . . . . .	5
Conventions for Examples . . . . .	5
Additional Graphics Options by Procedure . . . . .	6
Accessing the SAS/OR Sample Library . . . . .	7
Online Documentation . . . . .	7
Additional Documentation for SAS/OR Software . . . . .	7

---

## Purpose

*SAS/OR User's Guide: Project Management* provides a complete reference for the project management procedures in SAS/OR software. This book serves as the primary documentation for the CPM, DTREE, GANTT, NETDRAW, and PM procedures.

This chapter describes the organization of this book and the conventions that are used in the text and example code. To gain full benefit from using this book, familiarize yourself with the information presented in this section and refer to it when needed. The section “[Additional Documentation for SAS/OR Software](#)” on page 7 refers to other documents that contain related information.

---

## Organization

Chapter 3 contains a brief overview of the project management procedures in SAS/OR software and provides an introduction to project management methodology and the use of the project management tools in the SAS System. That chapter also describes the flow of data between the procedures and how the components of the SAS System fit together.

The remaining chapters describe the CPM, DTREE, GANTT, NETDRAW, and PM procedures, the earned value management macros, the Microsoft Project conversion macros, and the PROJMAN application. Each procedure description is self-contained; you need to be familiar with only the basic features of the SAS System and with SAS terminology to use most procedures. The statements and syntax necessary to run each procedure are presented in a uniform format throughout this book.

The following list summarizes the types of information provided for each procedure:

**Overview** provides a general description of what the procedure does. It outlines major capabilities of the procedure and lists all input and output data sets that are used with it.

**Getting Started** illustrates simple uses of the procedure in a few short examples. It provides introductory hands-on information for the procedure.

**Syntax** constitutes the major reference section for the syntax of the procedure. First, the statement syntax is summarized. Next, functional summary tables list all the statements and options in the procedure, classified by function. In addition, the online version includes a Dictionary of Options, which provides an alphabetical list of all options. Following these tables, the PROC statement is described, and then all other statements are described in alphabetical order. The mode-specific options (line-printer, full-screen, and graphics options) for the DTREE, GANTT, and NETDRAW procedures are described alphabetically under appropriate subheadings.

**Details** describes the features of the procedure, including algorithmic details and computational methods. This section explains how the various options interact with each other, describes input and output data sets in greater detail (with definitions of the output variables) and explains the format of printed output, if any.

**Examples** consists of examples that are designed to illustrate the use of the procedure. Each example includes a description of the problem and lists the options highlighted that are by the example. The example shows the data and the SAS statements needed and includes the output that is produced. You can duplicate the examples by copying the statements and data and running the SAS program. The SAS Sample Library contains the code that is used to run the examples shown in this book; consult your SAS Software representative for specific information about the Sample Library. Cross-reference tables in each chapter list all the options and statements illustrated by the different examples in that chapter.

**References** lists references that are relevant to the chapter.

---

## Typographical Conventions

This book uses various type styles, as explained by the following list:

roman	is the standard type style used for most text.
UPPERCASE ROMAN	is used for SAS statements, options, and other SAS language elements when they appear in the text. However, you can enter these elements in your own SAS code in lowercase, uppercase, or a mixture of the two. This style is also used for identifying arguments and values (in the syntax specifications) that are literals (for example, to denote valid keywords for a specific option).
UPPERCASE BOLD	is used in the “Syntax” section to identify SAS keywords, such as the names of procedures, statements, and options.
<b>bold</b>	is used to identify menu items.
VariableName	is used for the names of SAS variables and data sets when they appear in the text.
<i>oblique</i>	is used to indicate an option variable for which you must supply a value (for example, DUPLICATE= <i>dup</i> indicates that you must supply a value for <i>dup</i> ).
<i>italic</i>	is used for terms that are defined in the text, for emphasis, and for publication titles.
<b>monospace</b>	is used to show examples of SAS statements. In most cases, this book uses lowercase type for SAS code. You can enter your own SAS code in lowercase, uppercase, or a mixture of the two.

---

## Conventions for Examples

Most of the output shown in this book is produced with the following SAS System options:

```
options linesize=80 pagesize=60 nonumber nodate;
```

In addition, most of the graphics output shown in this book are produced with the following options:

```
goptions hpos=80 vpos=32 ypixels=800;
```

The remaining graphics options used in this book depend on the type of output and on the procedure used to create the output. The general options for half-page portrait, full-page portrait, and full-page landscape output are as follows:

### **Half-Page Portrait**

```
goptions hsize=5.75 in vsize=4.0 in;
```

### **Full-Page Portrait**

```
goptions hsize=5.75 in vsize=8.0 in;
```

### **Full-Page Landscape**

```
goptions hsize=8.0 in vsize=5.75 in
      border rotate=landscape;
```

## **Additional Graphics Options by Procedure**

### **GANTT Procedure**

The following PATTERN statements are used to create the color output from PROC GANTT:

```
pattern1 c=green   v=s;
pattern2 c=green   v=e;
pattern3 c=red     v=s;
pattern4 c=magenta v=e;
pattern5 c=magenta v=s;
pattern6 c=cyan    v=s;
pattern7 c=black   v=e;
pattern8 c=blue    v=s;
pattern9 c=brown   v=s;
```

### **NETDRAW Procedure**

The following GOPTIONS and PATTERN statements are used to create the color output from PROC NETDRAW:

```
goptions cback=ligr;
pattern1 v=e c=green;
pattern2 v=e c=red;
pattern3 v=e c=magenta;
pattern4 v=e c=blue;
pattern5 v=e c=cyan;
```

## DTREE Procedure

The following GOPTIONS statement is used to create the color output from PROC DTREE:

```
goptions cback=ligr ctext=black;
```

## Accessing the SAS/OR Sample Library

The SAS/OR Sample Library includes many examples that illustrate the use of SAS/OR software, including the examples used in this documentation. To access these sample programs from the SAS windowing environment, select **Help** from the main menu and then select **Getting Started with SAS Software**. On the **Contents** tab, expand the **Learning to Use SAS**, **Sample SAS Programs**, and **SAS/OR** items. Then click **Samples**.

## Online Documentation

This documentation is available online with the SAS System. To access SAS/OR documentation from the SAS windowing environment, select **Help** from the main menu and then select **SAS Help and Documentation**. On the **Contents** tab, expand the **SAS Products** and **SAS/OR** items. Then expand the book you want to view. You can search the documentation by using the **Search** tab.

You can also access the documentation by going to <http://support.sas.com/documentation>.

## Additional Documentation for SAS/OR Software

In addition to *SAS/OR User's Guide: Project Management*, these other documents can be helpful when you are using SAS/OR software:

### ***SAS/OR User's Guide: Bill of Material Processing***

provides documentation for the BOM procedure and all bill of material postprocessing SAS macros. The BOM procedure and SAS macros enable you to generate different reports and to perform several transactions to maintain and update bills of material.

### ***SAS/OR User's Guide: Constraint Programming***

provides documentation for the constraint programming procedure in SAS/OR software. This book serves as the primary documentation for the CLP procedure.

### ***SAS/OR User's Guide: Local Search Optimization***

provides documentation for the local search optimization procedures in SAS/OR software. This book serves as the primary documentation for the GA procedure, which uses genetic algorithms to solve optimization problems, and the OPTLSO procedure, which performs parallel hybrid derivative-free optimization.

**SAS/OR User's Guide: Mathematical Programming**

provides documentation for the mathematical programming procedures in SAS/OR software. This book serves as the primary documentation for the OPTLP, OPTMILP, OPTMODEL, and OPTQP procedures, the various solvers called by the OPTMODEL procedure, and the MPS-format SAS data set specification.

**SAS/OR User's Guide: Mathematical Programming Examples**

supplements the *SAS/OR User's Guide: Mathematical Programming* with additional examples that demonstrate best practices for building and solving linear programming, mixed integer linear programming, and quadratic programming problems. The problem statements are reproduced with permission from the book *Model Building in Mathematical Programming* by H. Paul Williams.

**SAS/OR User's Guide: Mathematical Programming Legacy Procedures**

provides documentation for the older mathematical programming procedures in SAS/OR software. This book serves as the primary documentation for the INTPOINT, LP, NETFLOW, and NLP procedures. Guidelines are also provided on migrating from these older procedures to the newer OPTMODEL family of procedures.

**SAS/OR User's Guide: Network Optimization Algorithms**

provides documentation for a set of algorithms that can be used to investigate the characteristics of networks and to solve network-oriented optimization problems. This book also documents PROC OPTNET, which invokes these algorithms and provides network-structured formats for input and output data.

**SAS Simulation Studio: User's Guide**

provides documentation on using SAS Simulation Studio, a graphical application for creating and working with discrete-event simulation models. This book describes in detail how to build and run simulation models and how to interact with SAS software for analysis and with JMP software for experimental design and analysis.

# Chapter 3

## Introduction to Project Management

### Contents

---

Overview . . . . .	<b>9</b>
Data Flow . . . . .	<b>10</b>
The CPM Procedure . . . . .	10
The GANTT Procedure . . . . .	11
The NETDRAW Procedure . . . . .	12
The PM Procedure . . . . .	13
Communication between Procedures . . . . .	14
Decision Support Systems . . . . .	<b>16</b>
Decision Analysis . . . . .	<b>16</b>
The DTREE Procedure . . . . .	17
Examples . . . . .	<b>17</b>
Example 3.1: Project Definition . . . . .	18
Example 3.2: Work Breakdown Structure . . . . .	20
Example 3.3: Project Scheduling and Reporting . . . . .	21
Example 3.4: Summary Report . . . . .	23
Example 3.5: Resource-Constrained Scheduling . . . . .	25
Example 3.6: Multiple Projects . . . . .	30
Example 3.7: Sequential Scheduling of Projects . . . . .	38
Example 3.8: Project Cost Control . . . . .	40
Example 3.9: Subcontracting Decisions . . . . .	47
Project Management Systems . . . . .	<b>50</b>
The Projman Application . . . . .	<b>51</b>
Web-Based Scheduling Systems . . . . .	<b>51</b>
Microsoft Project Conversion Macros . . . . .	<b>51</b>
Earned Value Management Macros . . . . .	<b>52</b>
References . . . . .	<b>52</b>

---

### Overview

This chapter briefly describes how you can use SAS/OR software for managing your projects. This chapter is not meant to define all the concepts of project management; several textbooks on project management explain the basic steps involved in defining, planning, and managing projects (for example, Moder, Phillips, and Davis 1983). Briefly, a *project* is defined as any task comprising a set of smaller tasks that need to be

performed, either sequentially or in parallel. Projects can be small and last only a few minutes (for instance, running a set of small computer programs), or they can be mammoth and run for several years (for example, the construction of the Channel Tunnel).

SAS/OR software has four procedures that can be used for planning, controlling, and monitoring projects: the **CPM** and **PM** procedures for scheduling project activities subject to precedence, time, and resource constraints; the **GANTT** procedure for displaying the computed schedule; and the **NETDRAW** procedure for displaying the activity network. These procedures integrate with the SAS System so that you can easily develop a customized project management system. The **Projman application**, a user-friendly graphical user interface included as part of SAS/OR software, is one such system.

This chapter gives a brief introduction to the CPM, GANTT, NETDRAW, and PM procedures and shows how you can use the SAS System for project management.

In addition to these four procedures and the Projman application, which are the major tools for the *traditional* functions associated with project management, SAS/OR software also contains a procedure for decision analysis, the **DTREE** procedure. *Decision analysis* is a tool that attempts to provide an analytic basis for management decisions under uncertainty. It can be used effectively as an integral part of project management methods. A brief introduction to PROC DTREE is provided in the section “[Decision Analysis](#)” on page 16.

---

## Data Flow

This section provides an overview of how project information is stored in the SAS System in data sets and how these data sets are used by the CPM, GANTT, NETDRAW, and PM procedures. Maintaining the project information in SAS data sets enables you to merge project information easily from several sources, summarize information, subset project data, and perform a wide variety of other operations using any of the many procedures in SAS software. Each of the SAS/OR procedures also defines a SAS macro variable that contains a character string indicating whether or not the procedure terminated successfully. This information is useful when the procedure is one of the steps in a larger program.


---

## The CPM Procedure

PROC CPM does the project scheduling and forms the core of the project management functionality in SAS/OR software. It uses activity precedence, time, and resource constraints, and holiday and calendar information to determine a feasible schedule for the project. The precedence constraints between the activities are described using a network representation, either in Activity-On-Arc (AOA) or Activity-On-Node (AON) notation, and input to PROC CPM in an Activity data set. The two different representations are described in Chapter 4, “[The CPM Procedure](#).[“](#) The Activity data set can also specify time constraints on the activities and resource requirement information. The Activity data set is required. Resource availability information can be specified using another data set, referred to here as the Resource data set. Holiday, workday, and other calendar information is contained in the Holiday, Workday, and Calendar data sets; each of these data sets is described in detail in Chapter 4, “[The CPM Procedure](#).[“](#) The schedule calculated by PROC CPM using all the input information and any special scheduling options is saved in an output data set, referred to as the Schedule data set. For projects that use resources, individual resource schedules for each activity can be saved in a Resource Schedule output data set. Resource usage information can also be saved in another output data set, referred to as the Usage data set. [Figure 3.1](#) illustrates all the input and output data sets that

are possible with PROC CPM. In the same figure, `_ORCPM_` is the SAS macro variable defined by PROC CPM.

**Figure 3.1** Input and Output Data Flow in PROC CPM

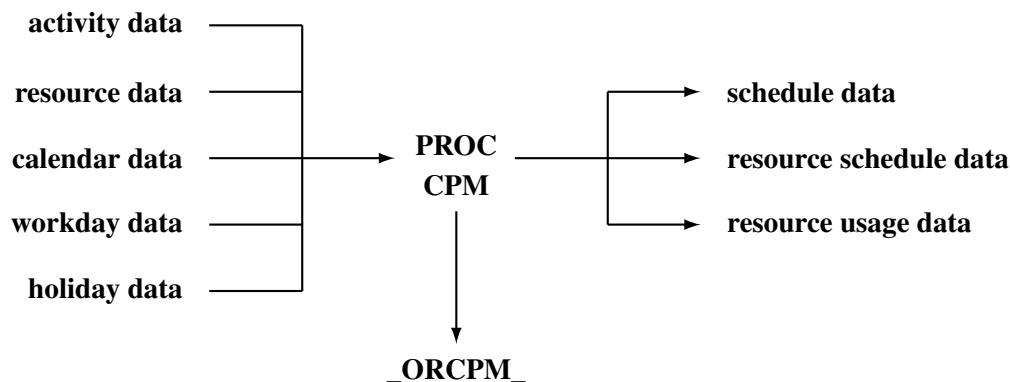

The three output data sets produced by PROC CPM contain all the information about the schedule and the resource usage; these data sets can be used as input to either PROC GANTT or PROC NETDRAW or to any of the several reporting, charting, or plotting procedures in the SAS System.

The Schedule data set can also contain additional project information such as project ID, department and phase information, accounting categories, and so on, in the form of ID variables passed to it from the Activity input data set with the ID statement. These variables can be used to produce customized reports by reordering, subsetting, summarizing, or condensing the information in the Schedule data set in various ways.

## The GANTT Procedure

PROC GANTT draws, in line-printer, high-resolution graphics, or full-screen mode, a bar chart of the schedules computed by PROC CPM. Such a bar chart is referred to as a Gantt chart in project management terminology. In addition to the Schedule data set, PROC GANTT can also use the Calendar, Workday, and Holiday data sets (that were used by PROC CPM when scheduling the activities in the project) to mark holidays and weekends and other nonwork periods appropriately on the Gantt chart. You can indicate target dates, deadlines, and other important dates on a Gantt chart by adding CHART variables to the Schedule data set. Furthermore, the GANTT procedure can indicate milestones on the chart by using a DURATION variable in the Schedule data set.

Precedence information can be used by PROC GANTT in either Activity-on-Node or Activity-on-Arc format to produce a Logic bar chart that shows the precedence relationships between the activities. The precedence information, required for drawing the network logic, can be conveyed to PROC GANTT using the Activity data set or a Logic data set, as described in Chapter 8, “[The GANTT Procedure](#).”


The Gantt procedure also supports an [automatic text annotation](#) facility, using the Label data set, which is designed specifically for labeling Gantt charts independently of the SAS/GRAF Annotate facility. The specifications in this data set enable you to print label strings with a minimum of effort and data entry while providing the capability for more complex chart labeling situations.

The Gantt procedure is Web-enabled. The `HTML=` option enables you to specify a variable in the Schedule data set that defines a URL for each activity. If you route the Gantt chart to an HTML file using the Output

Delivery System, then you can click on a schedule bar and browse text or other descriptive information about the associated activity. You also use this information to create custom HTML files with drill-down graphs. PROC GANTT also produces an [Imagemap](#) data set that contains the outline coordinates for the schedule bars used in the Gantt chart that can be used to generate HTML MAP tags.

As with PROC CPM, PROC GANTT also defines a macro variable named `_ORGANTT` that has a character string indicating if the procedure terminated successfully. [Figure 3.2](#) illustrates the flow of data in and out of PROC GANTT.

**Figure 3.2** Input and Output Data Flow in PROC GANTT

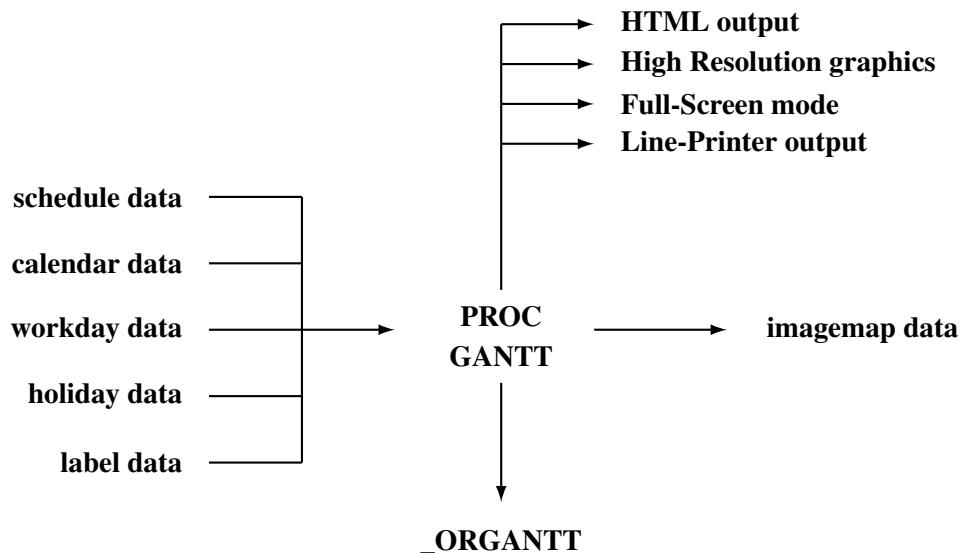

## The NETDRAW Procedure

PROC NETDRAW draws project networks. The procedure automatically places the nodes in the network and draws the arcs connecting them, using the (activity, successor) relationship as specified by the Network data set described in Chapter 9, “[The NETDRAW Procedure](#).”

The Network data set, used as input to PROC NETDRAW, can be an Activity data set, a Schedule data set, or a Layout data set, as described in [Chapter 9](#).

If a Schedule data set, output by PROC CPM, is used as the Network data set, the network diagram also contains all the schedule times calculated by PROC CPM. The procedure can draw the diagram in line-printer mode as well as in high-resolution graphics mode. Further, you can invoke the procedure in full-screen mode, which enables you to scroll around the network to view different parts of it; in this mode, you can also modify the layout of the network by moving the nodes of the network.

By default, PROC NETDRAW uses the topological ordering of the activity network to determine the X coordinates of the nodes. In a time-based network diagram, the nodes can be ordered according to any SAS date, time, or datetime variable in the Network data set. In fact, PROC NETDRAW enables you to align the nodes according to any numeric variable in this data set, not just the start and finish times.


You can produce a zoned network diagram by identifying a ZONE variable in the input data set, which divides the network into horizontal bands or zones. This is useful in grouping the activities of the project according to some appropriate classification. The NETDRAW procedure also draws tree diagrams. This feature can be used to draw work breakdown structures or other organizational diagrams (see [Example 3.2](#)).

PROC NETDRAW produces an output data set (Layout data set), which contains the positions of the nodes and the arcs connecting them. This output data set can also be used as an input data set to PROC NETDRAW; this feature is useful when the same project network is drawn several times during the course of a project. You may want to see the updated information drawn on the network every week; you can save computer resources by using the same node placement and arc routing, without having the procedure recompute it every time. PROC NETDRAW defines the macro variable `_ORNEDR`, which contains a character string indicating if the procedure terminated successfully.

The NETDRAW procedure is also Web-enabled (like PROC GANTT), and it supports the `HTML=` and `IMAGEMAP=` options.

[Figure 3.3](#) illustrates the flow of data in and out of PROC NETDRAW.


**Figure 3.3** Input and Output Data Flow in PROC NETDRAW

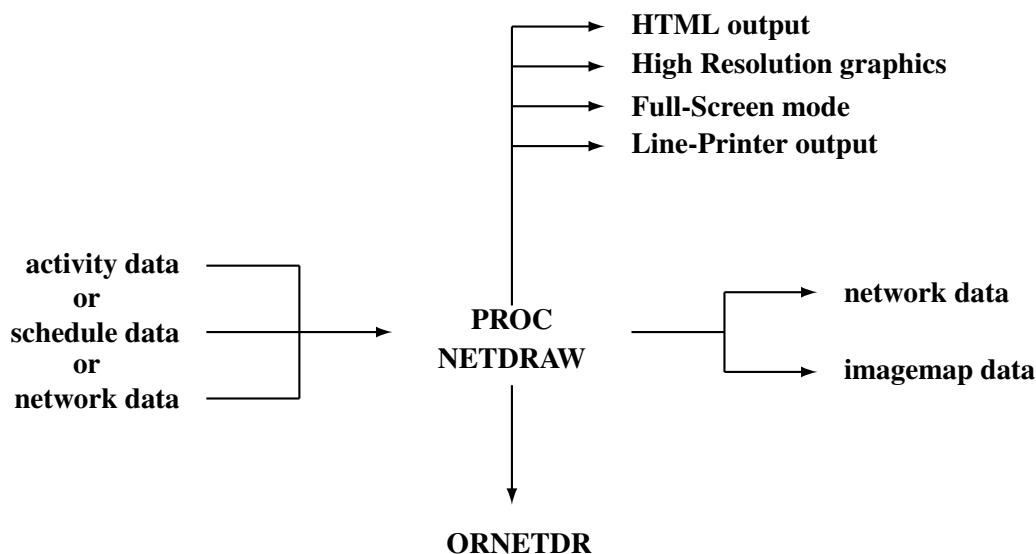


---

## The PM Procedure


PROC PM is an interactive procedure that can be used for planning, controlling, and monitoring a project. The syntax and the scheduling features of PROC PM are virtually the same as those of PROC CPM; there are a few differences, which are described in Chapter 5, “[The PM Procedure](#).” As far as the flow of data is concerned (see [Figure 3.4](#)), the PM procedure supports an additional data set that can be used to save and restore preferences that control the project view. The scheduling engine used by the PM procedure is the same as the one used by PROC CPM; the same macro variable, `_ORCPM_`, is used to indicate if the schedule was computed successfully.

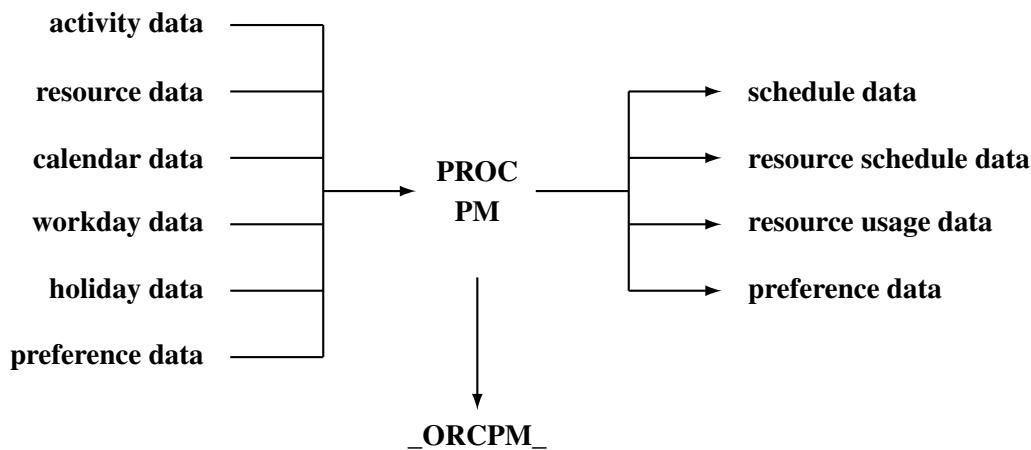**Figure 3.4** Input and Output Data Flow in PROC PM


---

## Communication between Procedures


Figure 3.1, Figure 3.2, Figure 3.3, and Figure 3.4 illustrate the data flow going in and out of each of the four procedures: CPM, GANTT, NETDRAW, and PM, respectively. The data sets described in the previous sections store project information and can be used to communicate project data between the procedures in the SAS System. Figure 3.5 shows a typical sequence of steps in a project management system built around these procedures.

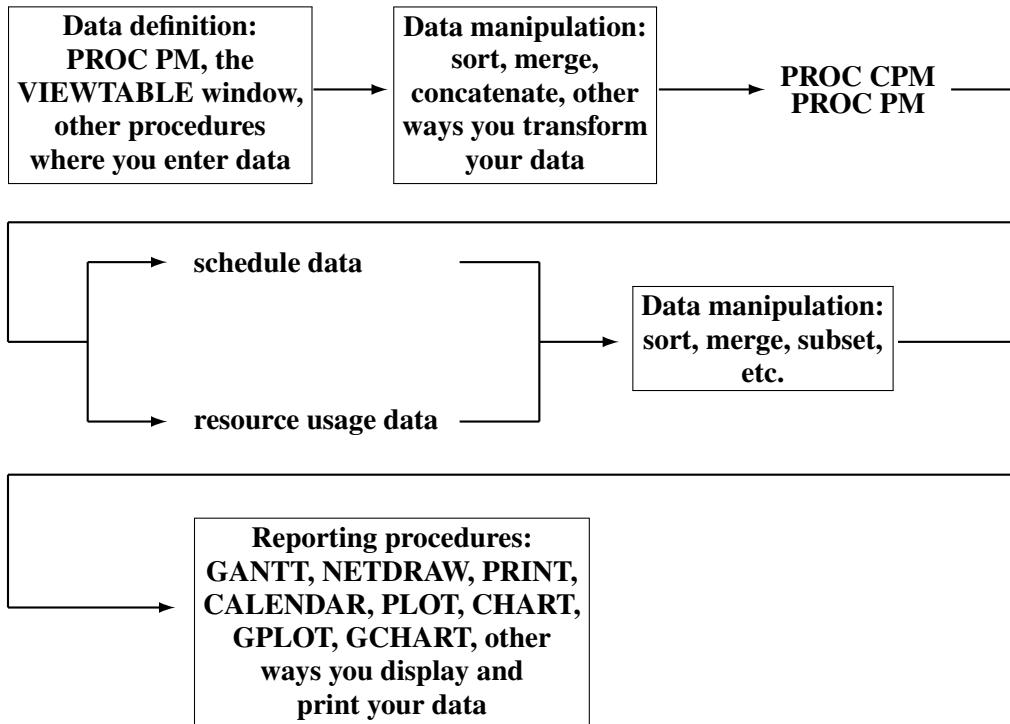**Figure 3.5** Using the SAS System for Project Management

Of course, this is only one possible scenario of the use of these procedures. In addition, you may want to use PROC NETDRAW to check the logic of the network diagram before scheduling the project using PROC CPM. Further, the data flow shown in [Figure 3.5](#) may represent only the first iteration in a continuous scheme for monitoring the progress of a project. As the project progresses, you may update the data sets, including actual start and finish times for some of the activities, invoke PROC CPM again, produce updated Gantt charts and network diagrams, and thus continue monitoring the project.

For example, a project management system designed for scheduling and tracking a major outage at a power plant may include the steps illustrated in [Figure 3.6](#). In the sequences of steps illustrated in both these figures, you can use PROC PM to update most of the activity information using the procedure's graphical user interface.

Thus, SAS/OR software provides four different procedures designed for performing many of the traditional project management tasks; these procedures can be combined in a variety of ways to build a customized comprehensive project management system. The section “[Examples](#)” on page 17 illustrates several applications of the procedures in typical project management situations.

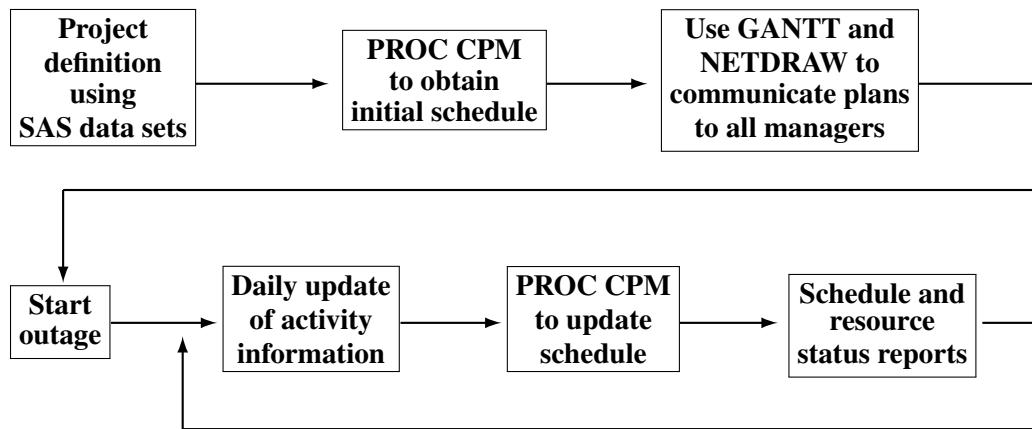**Figure 3.6** Scheduling a Power Plant Outage

## Decision Support Systems

In addition to the CPM, GANTT, NETDRAW, and PM procedures, which are the major tools for the traditional functions associated with project management, SAS/OR software has several procedures that can be used to create a many-faceted Decision Support System. Traditional CPM/PERT techniques form only one part of effective project management and may be considered as a specialized application of Decision Support Systems (Williams and Boyd 1990). SAS/OR software contains several mathematical programming procedures that can be used to design effective systems for solving inventory control, transportation, network flow, transshipment, product-mix, cutting stock problems, and so on. These procedures are discussed in detail in *SAS/OR User's Guide: Mathematical Programming*.

Decision analysis is another important tool that is receiving recognition as a component of project management. The next section briefly describes PROC DTREE and the role it can play in making important decisions in project management.

---

## Decision Analysis

There are several stages in the course of a project when critical decisions are to be made regarding the future path that is to be followed. In fact, the most crucial decision might be to decide at the beginning whether to embark on the project or not. Other important decisions that could benefit from using decision analysis tools may be subcontract awarding, subproject termination in a research and development (R&D) environment, what-if analysis, and so on. Decision analysis techniques can be used effectively in such situations to help make decisions under uncertainty.


---

## The DTREE Procedure

PROC DTREE interprets a decision problem represented in SAS data sets, finds the optimal decisions, and plots on a line printer or a graphics device the decision tree showing the optimal decisions. A decision tree contains two types of nodes: decision nodes and chance nodes. A decision node represents a stage in the problem where a decision is to be made that could lead you along different paths through the tree. A chance node represents a stage in the problem where some uncertain factors result in one of several possible outcomes, once again leading you to different branches of the tree, with associated probabilities.

The structure of a decision model is given in the STAGEIN= data set. This data set, described in detail in Chapter 7, “[The DTREE Procedure](#),” specifies the name, type, and attributes of all outcomes for each stage in your model. This is the only data set that is required to produce a diagrammatic representation of your decision problem. To evaluate and analyze your decision model, you need to specify the PROBIN= and PAYOFFS= data sets. The PROBIN= data set specifies the conditional probabilities for every event in your model. The PAYOFFS= data set specifies the value of each possible scenario (sequence of outcomes). The objective is to use the information summarized in these data sets to determine the optimal decision based on some measure of performance. One common objective is to maximize the expected value of the return. [Figure 3.7](#) illustrates the data flow for PROC DTREE.

**Figure 3.7** Input and Output Data Flow in PROC DTREE

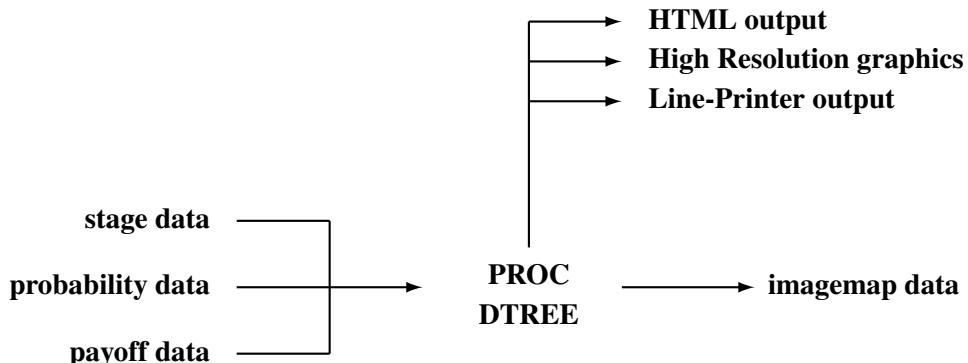

You can use PROC DTREE to display, evaluate, and summarize your decision problem. The procedure can be used to plot the decision tree in line-printer or graphics mode. The optimal decisions are highlighted on the output. Further, a summary table can be displayed listing all paths through the decision tree along with the cumulative reward and the evaluating values of all alternatives for that path. The summary table indicates the optimal evaluating value for each path with an asterisk. The procedure can also perform sensitivity analysis and what-if analysis. A simple decision problem is described in [Example 3.9](#).

---

## Examples

In this section, a few simple examples illustrate some of the basic data flow concepts described in this chapter. More detailed examples of each procedure are provided in the corresponding chapters and can also be found in *SAS/OR Software: Project Management Examples*.

---

## Example 3.1: Project Definition

Suppose you want to prepare and conduct a market survey (Moder, Phillips, and Davis 1983) to determine the desirability of launching a new product. As a first step, you need to identify the steps involved. Make a list of the tasks that need to be performed and obtain a reasonable estimate of the length of time needed to perform each task. Further, you need to specify the order in which these tasks can be done. The following DATA step creates a SAS data set, *survey*, representing the project. This Activity data set contains a representation of the Survey project in Activity-On-Node format; a brief discussion of the two types of representations is given in Chapter 4, “The CPM Procedure.” The data set contains a variable *activity* listing the basic activities (tasks) involved, a variable *duration* specifying the length of time in days needed to perform the tasks, and, for each task, the variables *succ1*–*succ3*, which indicate the immediate successors. An *ID* variable is also included to provide a more informative description of each task. Thus, the activity ‘Plan Survey’ takes four days. Once the planning is done, the tasks ‘Hire Personnel’ and ‘Design Questionnaire’ can begin. The Activity data set also contains a variable named *phase* associating each activity with a particular phase of the project.

```

data survey;
  input id      $ 1-20
        activity $ 22-29
        duration
        succ1    $ 34-41
        succ2    $ 43-50
        succ3    $ 52-59
        phase    $ 61-69;
  label phase = 'Project Phase'
        id     = 'Description';
  datalines;
Plan Survey      plan sur 4  hire per design q      Plan
Hire Personnel   hire per 5  trn per               Prepare
Design Questionnaire design q 3  trn per  select h print q  Plan
Train Personnel   trn per  3  cond sur             Prepare
Select Households select h 3  cond sur             Prepare
Print Questionnaire print q 4  cond sur            Prepare
Conduct Survey    cond sur 10 analyze             Implement
Analyze Results   analyze 6                         Implement
;

```

The data set *survey* can be input to PROC CPM, which calculates how long the project will take given the current estimates of the durations. As a first step, you may want to graph the project network using PROC NETDRAW. In the initial stages of defining the tasks in a project, it is useful to see how the tasks relate to each other and perhaps modify some of the relationships. The following program invokes PROC NETDRAW; the *ZONE=* option is used to create a zoned network diagram with the activities grouped according to the phase of the project to which they correspond. The network diagram is shown in Output 3.1.1.

```

goptions hpos=100 vpos=55 border;
pattern1 v=e c=green;
pattern2 v=e c=red;
pattern3 v=e c=magenta;

title ' ';
title2 h=2.5 'Conducting a Market Survey';


```

```

proc netdraw data=survey graphics;
  actnet/act=activity
    succ=(succ1-succ3)
    separatearcs
    xbetween=3 pcompress
    id=(id)
    height=2
    nodefid
    nolabel
    zone=phase
    zonepat
    frame;
run;

```

**Output 3.1.1** Network Diagram of SURVEY Project

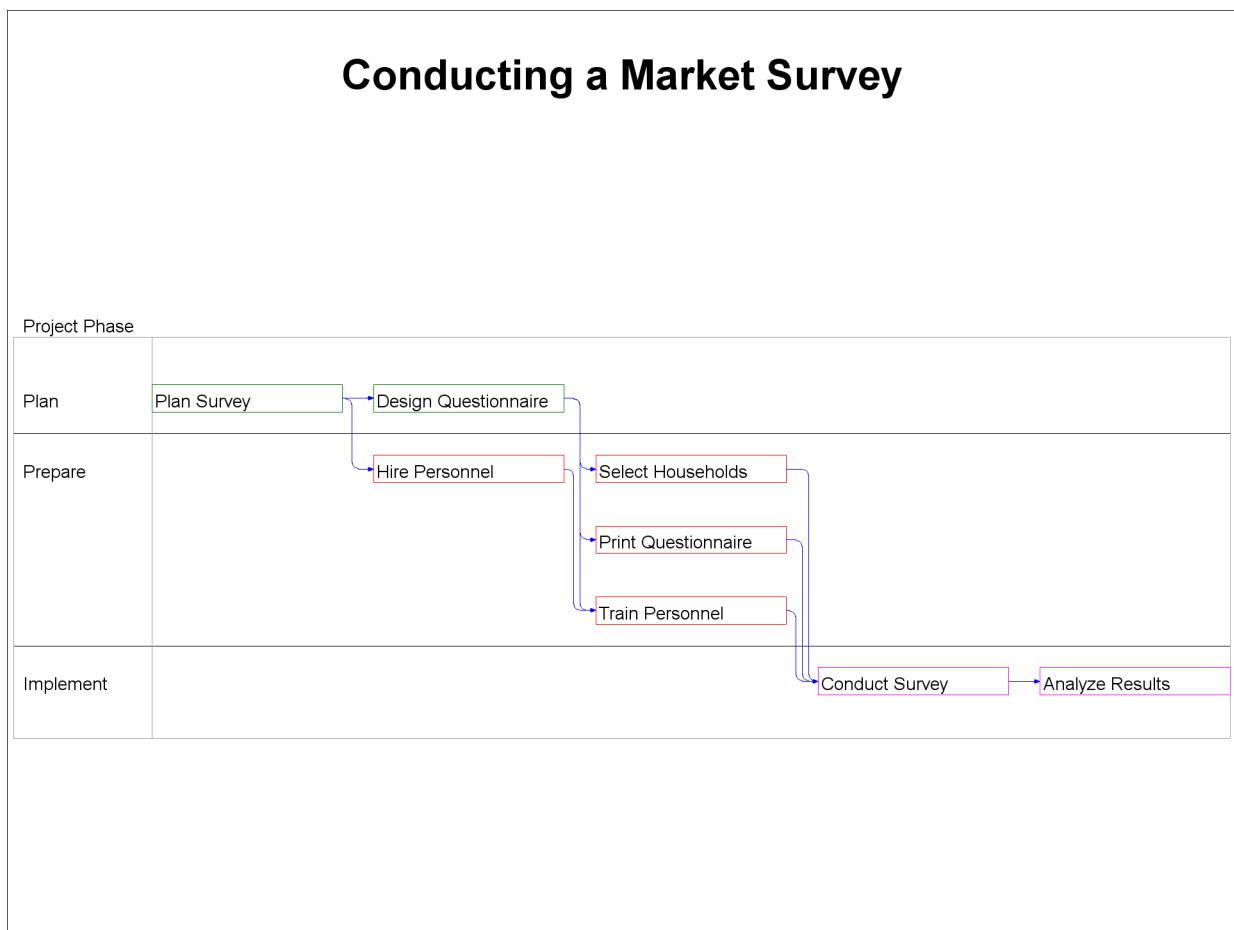

---

## Example 3.2: Work Breakdown Structure

A tree diagram is a useful method of visualizing the work breakdown structure (WBS) of a project. For the survey project, the activities are divided into three phases. In this example, the NETDRAW procedure is used to represent the work breakdown structure of the project. The following program saves the data in a Network data set that is input to PROC NETDRAW. The TREE option is used to draw the WBS structure in the form of a tree (Output 3.2.1).

```


data wbs;
  input parent  $ 1-10
        child   $ 12-21
        style;
  datalines;
Survey    Plan          1
Survey    Prepare       1
Survey    Implement     1
Plan      Plan S.      2
Plan      Design Q.    2
Prepare   Hire P.      3
Prepare   Train P.    3
Prepare   Select H.   3
Prepare   Print Q.    3
Implement Conduct S.  4
Implement Analyze R.  4
Plan S.          2
Design Q.        2
Hire P.          3
Train P.         3
Select H.        3
Print Q.         3
Conduct S.       4
Analyze R.       4
;

pattern1 v=s c=black;
pattern2 v=s c=green;
pattern3 v=s c=blue;
pattern4 v=s c=red;

title  h=2.0  'Conducting a Market Survey';
title2 h=1.4  'Work Breakdown Structure';

proc netdraw data=wbs graphics;
  actnet/act=parent
    succ=child coutline=black tree rotatetext
    ctext=white font=swiss rectilinear
    htext=3 compress rotate
    ybetween=3 xbetween=50 pattern=style
    centerid;
run;

```

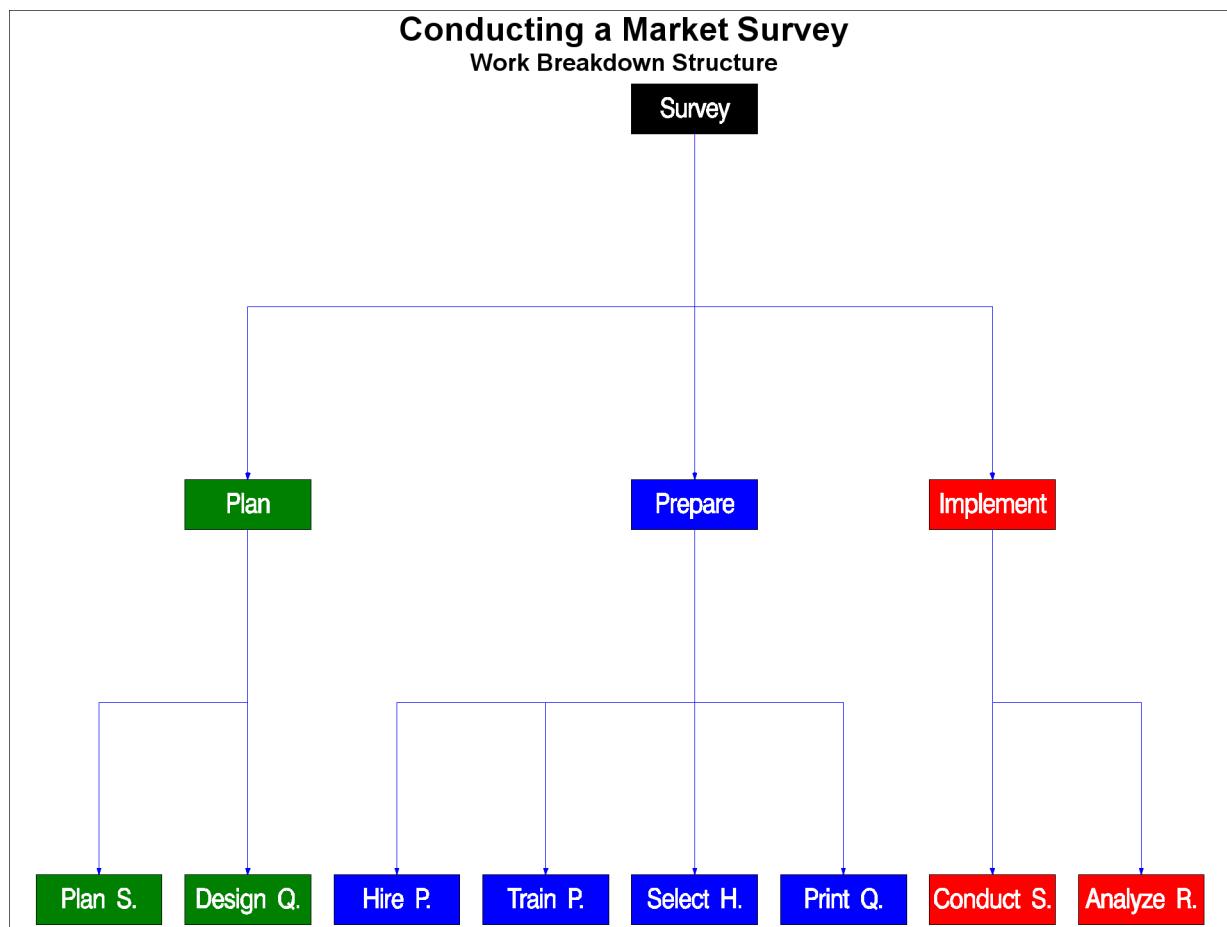**Output 3.2.1** Work Breakdown Structure of SURVEY Project**Example 3.3: Project Scheduling and Reporting**

Having defined the project and ensured that all the relationships have been modeled correctly, you can schedule the activities in the project by invoking PROC CPM. Suppose the activities can occur only on weekdays, and there is a holiday on July 4, 2003. Holiday information is passed to PROC CPM using the Holiday data set `holidata`. The following statements schedule the project to start on July 1, 2003. The early and late start schedules and additional project information are saved in the output data set `survschd`. The output data set produced by PROC CPM can then be used to generate a variety of reports. In this example, the data set is first sorted by the variable `E_START` and then displayed using the `PRINT` procedure (see Output 3.3.1).

```

data holidata;
  format hol date7.;
  hol = '4jul03'd;
run;

proc cpm data=survey date='1jul03'd out=survschd
  interval=weekday holidata=holidata;
activity activity;
  
```

```

successor  succ1-succ3;
duration   duration;
id         id phase;
holiday    hol;
run;

proc sort;
  by e_start;
run;

title  'Conducting a Market Survey';
title2 'Early and Late Start Schedule';

proc print;
run;

```

### Output 3.3.1 Project Schedule: Listing

#### Conducting a Market Survey Early and Late Start Schedule

Obs	activity	succ1	succ2	succ3	duration	id	phase
1	plan sur	hire per	design q			4	Plan Survey
2	hire per	trn per				5	Hire Personnel
3	design q	trn per	select h	print q		3	Design Questionnaire
4	select h	cond sur				3	Select Households
5	print q	cond sur				4	Print Questionnaire
6	trn per	cond sur				3	Train Personnel
7	cond sur	analyze				10	Conduct Survey
8	analyze					6	Analyze Results

Obs	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
1	01JUL03	07JUL03	01JUL03	07JUL03	0	0
2	08JUL03	14JUL03	08JUL03	14JUL03	0	0
3	08JUL03	10JUL03	09JUL03	11JUL03	1	0
4	11JUL03	15JUL03	15JUL03	17JUL03	2	2
5	11JUL03	16JUL03	14JUL03	17JUL03	1	1
6	15JUL03	17JUL03	15JUL03	17JUL03	0	0
7	18JUL03	31JUL03	18JUL03	31JUL03	0	0
8	01AUG03	08AUG03	01AUG03	08AUG03	0	0

The schedule produced by PROC CPM is then graphed by invoking PROC GANTT, as shown in the following code. The CALENDAR procedure or NETDRAW procedure can also be used to display the schedule. The Gantt chart produced is shown in [Output 3.3.2](#). Note that the precedence relationships are displayed on the Gantt chart.

```

goptions hpos=80 vpos=43;
pattern1 c=green v=s;      /* duration of a non-critical activity */
pattern2 c=green v=e;      /* slack time for a noncrit. activity */
pattern3 c=red   v=s;      /* duration of a critical activity */
pattern4 c=magenta v=e;   /* slack time for a supercrit. activity */
pattern5 c=magenta v=s;   /* duration of a supercrit. activity */

```


```

pattern6 c=cyan v=s;      /* actual duration of an activity */
pattern7 c=black v=e;     /* break due to a holiday */

title c=black h=2.5 'Conducting a Market Survey';
title2 c=black h=1.5 'Early and Late Start Schedule';
proc gantt graphics data=survsched holidata=holidata;
  chart / holiday=(hol) interval=weekday
        skip=2 height=1.4 nojobnum
        compress noextra
        activity=activity succ=(succ1-succ3)
        cprec=blue caxis=black ;
  id   id phase;
run;

```

Output 3.3.2 Gantt Chart of SURVEY Project

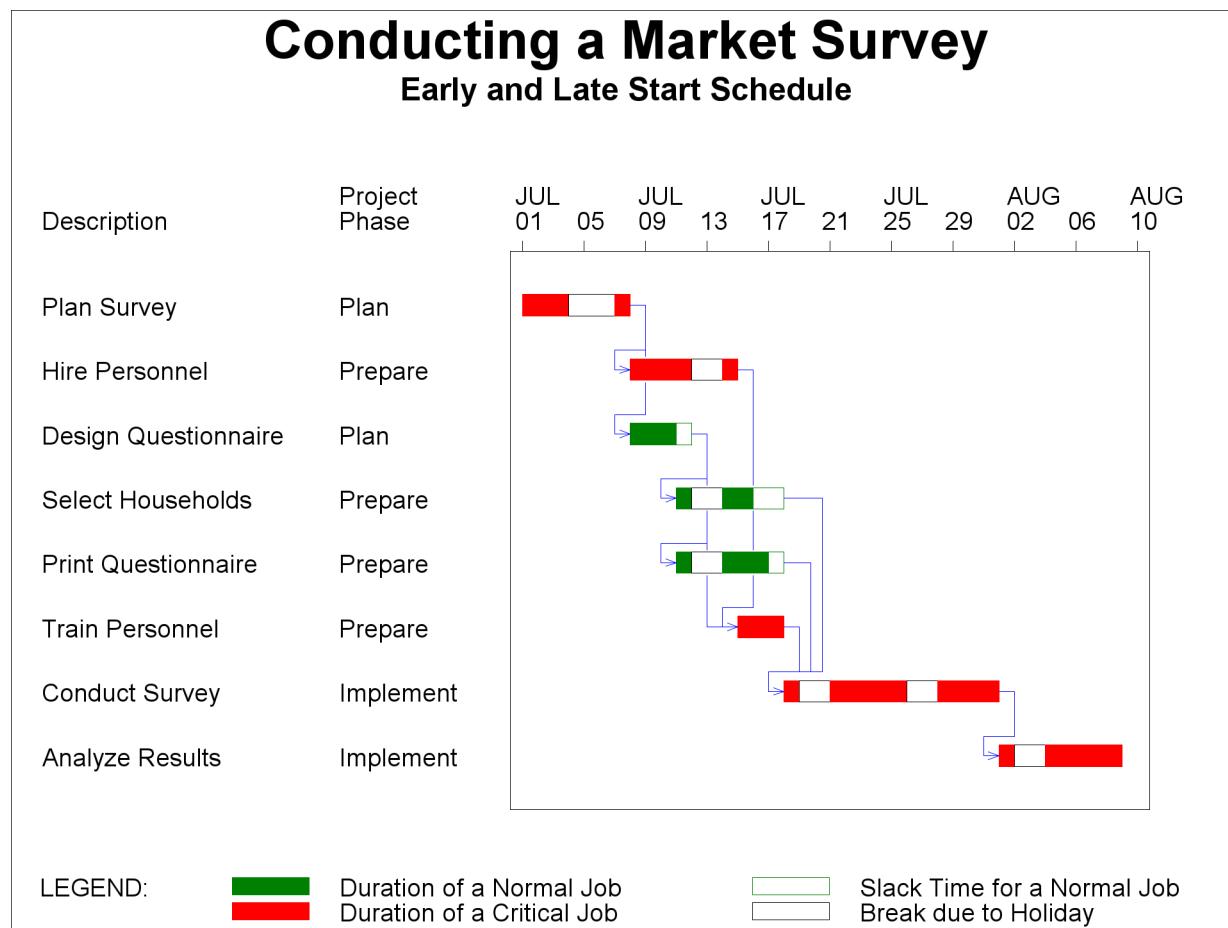

## Example 3.4: Summary Report

As mentioned in the section “Data Flow” on page 10, the output data set can be manipulated in several different ways. You can subset the project data to report progress on selected activities, or you can produce reports sorted by a particular field or grouped according to a natural division of the project activities. For large projects, you may want to get a summarized view of the schedule, with the start and finish times of only the major phases of the project.

For the survey project, suppose that you want a condensed report, containing only information about the start and finish times of the three different phases of the project. The following program summarizes the information in the data set `survschd` and produces a Gantt chart of the summarized schedule (shown in Output 3.4.1).

```

proc sort data=survschd;
  by phase;
  run;

proc summary data=survschd;
  by phase;
  output out=sumsched min(e_start)= max(e_finish)= ;
  var e_start e_finish;
  run;

proc sort data=sumsched;
  by e_start;
  format e_start e_finish date7. ;
  run;


pattern1 c=green v=s;
pattern2 c=green v=e;
pattern3 c=red   v=s;
pattern4 c=magenta v=e;
pattern5 c=magenta v=s;
pattern6 c=cyan  v=s;
pattern7 c=black  v=e;

goptions hpos=80 vpos=43;

title c=black h=3 'Conducting a Market Survey';
title2 c=black h=2 'Summarized Schedule';

proc gantt data=sumsched graphics
  holidata=holidata;
  id phase;
  chart / nojobnum
    nolegend
    interval=weekday
    height=2.0 skip=4
    ref='01jul03'd to '15aug03'd by week
    caxis=black
    cref=gray
    holiday=(hol);
  run;

```

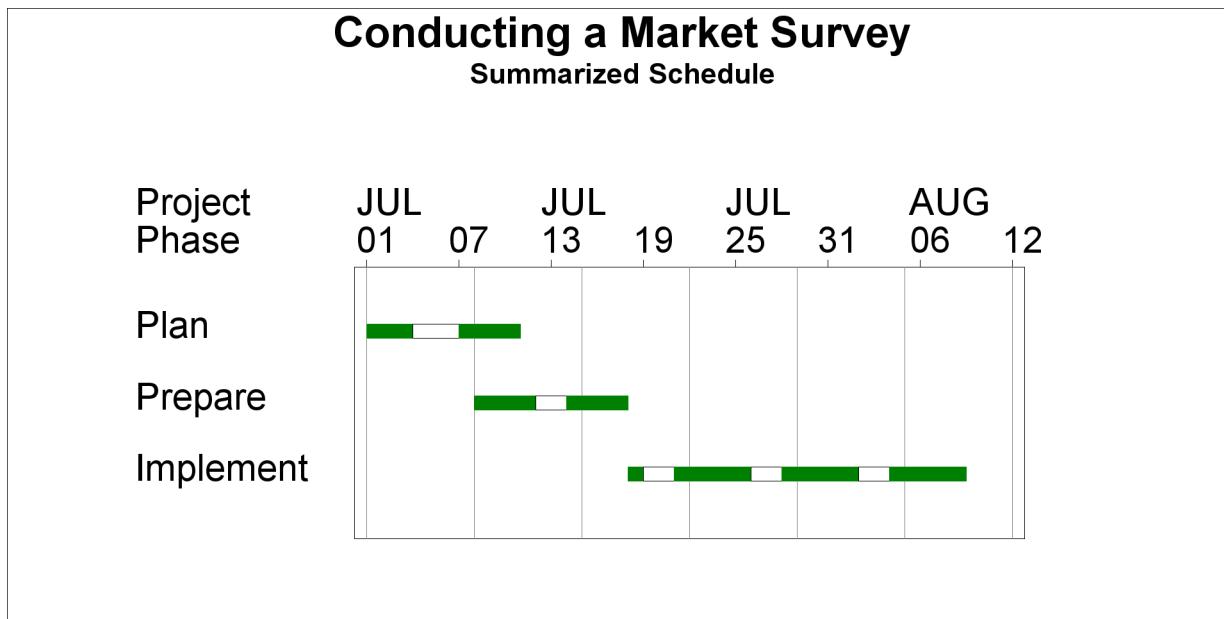**Output 3.4.1** Summary Gantt Chart of SURVEY Project

### Example 3.5: Resource-Constrained Scheduling

The previous two examples illustrated some of the reports that can be generated using the Schedule output data set produced by PROC CPM. This section illustrates the use of PROC CPM to perform resource-constrained scheduling and to obtain a resource Usage output data set for generating reports of resource utilization during the course of a project. A primary concern in data processing centers is the number of processors needed to perform various tasks. Given a series of programming tasks, a common question faced by a data center operator is how to allocate computer resources to the various tasks.

Consider a simple job that involves sorting six data sets A, B, C, D, E, and F, merging the first three into one master data set, merging the last three into another comparison data set, and then comparing the two merged data sets. The precedence constraints between the activities (captured by the variables task and succ), the time required by the activities (the variable dur), and the resource required (the variable processor) are shown in the following code:

```

data program;
  format task $8. succ $8. ;
  input task & succ & dur processor;
  datalines;
Sort A   Merge 1    5   1
Sort B   Merge 1    4   1
Sort C   Merge 1    3   1
Sort D   Merge 2    6   1
Sort E   Merge 2    4   1
Sort F   Merge 2    6   1
Merge 1  Compare   5   1
Merge 2  Compare   4   1
Compare  .         5   1
;

```

If the programming project is scheduled (in absolute units) without any resource constraints, it will take 15 time units for completion and will require a maximum availability of six processors. Suppose now that only two processors are available. The `resin` data set limits the availability of the resource to 2, and PROC CPM is invoked with two input data sets (Activity data set `program` and Resource data set `resin`) to produce a resource-constrained schedule.

PROC CPM produces two output data sets. The Schedule data set (`progschd`) contains the resource-constrained schedule (`S_START` and `S_FINISH` variables) in addition to the early and late start unconstrained schedules. The Usage data set (`progrout`) shows the number of processors required at every unit of time, if the early start schedule or the late start schedule or the resource-constrained schedule were followed, in the variables `eprocessor`, `lprocessor`, and `rprocessor`, respectively; the variable `aprocessor` shows the number of processors remaining after resource allocation. The two output data sets are displayed in [Output 3.5.1](#).

```

data resin;
  input per processor;
  datalines;
0 2
;

proc cpm data=program resin=resin
           out=progschd resout=progrout;
  activity task;
  duration dur;
  successor succ;
  resource processor/per=per;
run;

title 'Scheduling Programming Tasks';
title2 'Data Set PROGSCHD';
proc print data=progschd;
run;

title2 'Data Set PROGROUT';
proc print data=progrout;
run;

```

The Schedule and Usage data sets, displayed in [Output 3.5.1](#), can be used to generate any type of report concerning the schedules or processor usage. In the following program, the unconstrained and constrained schedules are first plotted using PROC GANTT (see [Output 3.5.2](#)).

**Output 3.5.1** Data Sets PROGSCHD and PROGROUT

**Scheduling Programming Tasks**  
**Data Set PROGSCHD**

Obs	task	succ	dur	processor	S_START	S_FINISH	E_START	E_FINISH	L_START	L_FINISH
1	Sort A	Merge 1	5	1	0	5	0	5	0	5
2	Sort B	Merge 1	4	1	6	10	0	4	1	5
3	Sort C	Merge 1	3	1	10	13	0	3	2	5
4	Sort D	Merge 2	6	1	0	6	0	6	0	6
5	Sort E	Merge 2	4	1	11	15	0	4	2	6
6	Sort F	Merge 2	6	1	5	11	0	6	0	6
7	Merge 1	Compare	5	1	13	18	5	10	5	10
8	Merge 2	Compare	4	1	15	19	6	10	6	10
9	Compare		5	1	19	24	10	15	10	15

**Scheduling Programming Tasks**  
**Data Set PROGROUT**

Obs	_TIME_	Eprocessor	Lprocessor	Rprocessor	Aprocessor
1	0	6	3	2	0
2	1	6	4	2	0
3	2	6	6	2	0
4	3	5	6	2	0
5	4	3	6	2	0
6	5	3	4	2	0
7	6	2	2	2	0
8	7	2	2	2	0
9	8	2	2	2	0
10	9	2	2	2	0
11	10	1	1	2	0
12	11	1	1	2	0
13	12	1	1	2	0
14	13	1	1	2	0
15	14	1	1	2	0
16	15	0	0	2	0
17	16	0	0	2	0
18	17	0	0	2	0
19	18	0	0	1	1
20	19	0	0	1	1
21	20	0	0	1	1
22	21	0	0	1	1
23	22	0	0	1	1
24	23	0	0	1	1
25	24	0	0	0	2

```


goptions hpos=80 vpos=43;

title h=2.5 'Scheduling Programming Tasks';
title2 h=1.5 'Comparison of Schedules';
proc gantt data=progschd graphics;

```

```
chart / height=1.5 increment=2 caxis=black;
id task;
run;
```

Output 3.5.2 Gantt Chart Comparing Schedules

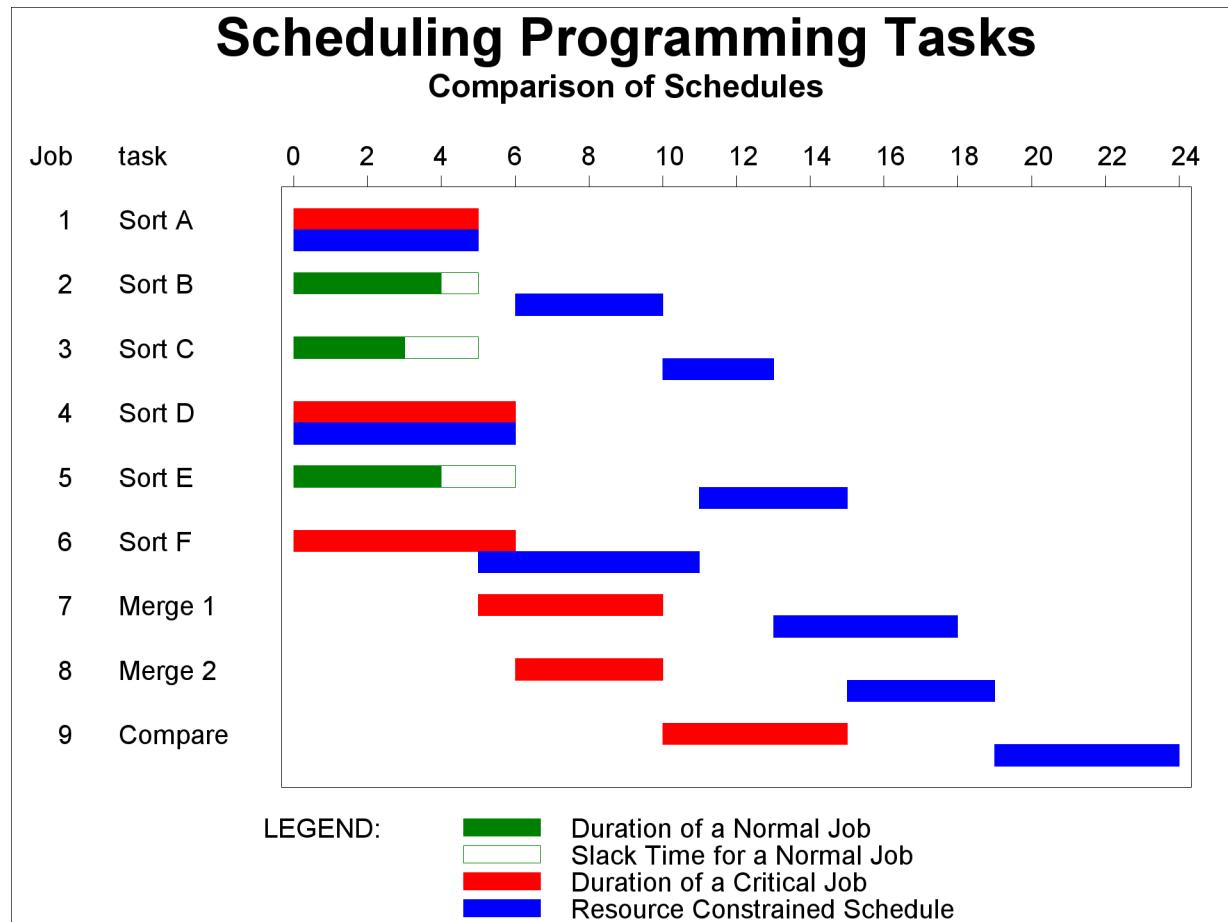

Next, the GPLOT procedure is invoked using the Usage data set to compare the unconstrained and the constrained usage of the resource (see Output 3.5.3).

```
/* Create a data set for use with PROC GPLOT */
data plotout;
  set progrout;
  label _time_='Time of Usage';
  label processor='Number of Processors';
  label resource='Type of Schedule Followed';
  resource='Constrained';
  processor=rprocessor; output;
  resource='Early Start';
  processor=eprocessor; output;
run;
```


```

axis1 minor=none width=3;
axis2 length=80 pct;
symbol1 i=steplj c=red;
symbol2 i=steplj l=3 c=green;

title2 h=1.5 'Comparison of Processor Usage';
proc gplot data=plotout;
  plot processor * _time_ = resource/ vaxis=axis1
                                haxis=axis2
                                caxis=black;
run;

```

Output 3.5.3 Plot Comparing Resource Usage

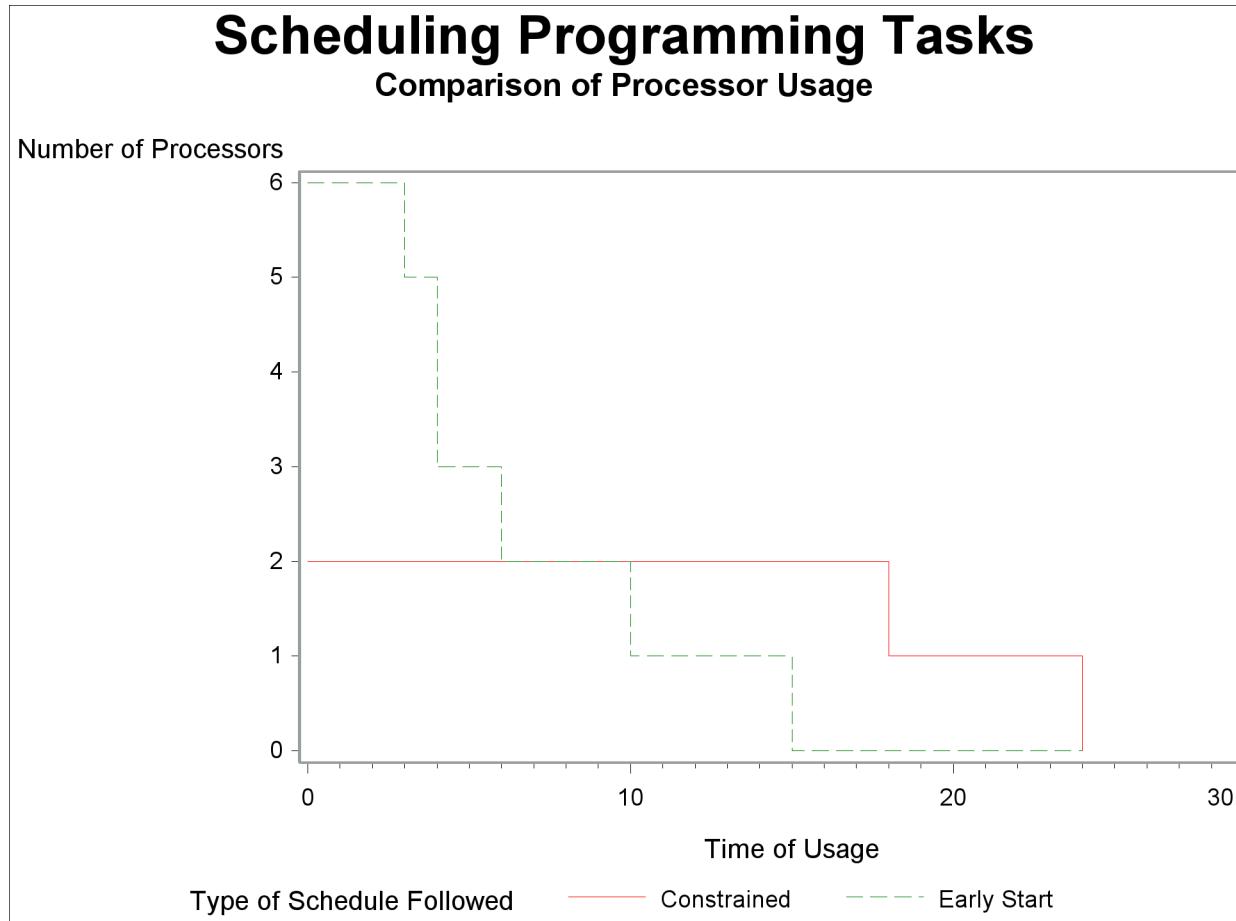


## Example 3.6: Multiple Projects

Often a project is divided into several subprojects, each of which is then broken into activities with precedence constraints. For reporting or accounting purposes, it may be essential to group activities or to aggregate the information pertaining to activities in a given group. Sometimes, totally different projects use a common pool of resources and you may want to schedule all the projects using the common pool; you may want to vary the priority with which the resources are allotted to the activities on the basis of the projects to which they belong. Often, you have several projects that are essentially the same, with only a few minor differences; these projects may also share a common pool of resources. In such cases, you may want to have a project *template* listing all the activities and their precedence relationships; for each specific project you can copy the template, make any modifications that are necessary for the given scenario, and determine the project schedule accordingly.

This example illustrates some of these possibilities for a multiproject scenario. The project is first scheduled using PROC CPM, and then the PM procedure is used with the same input data set to illustrate the project displayed in the PM Window.

**Output 3.6.1** Network Diagram for Project Book

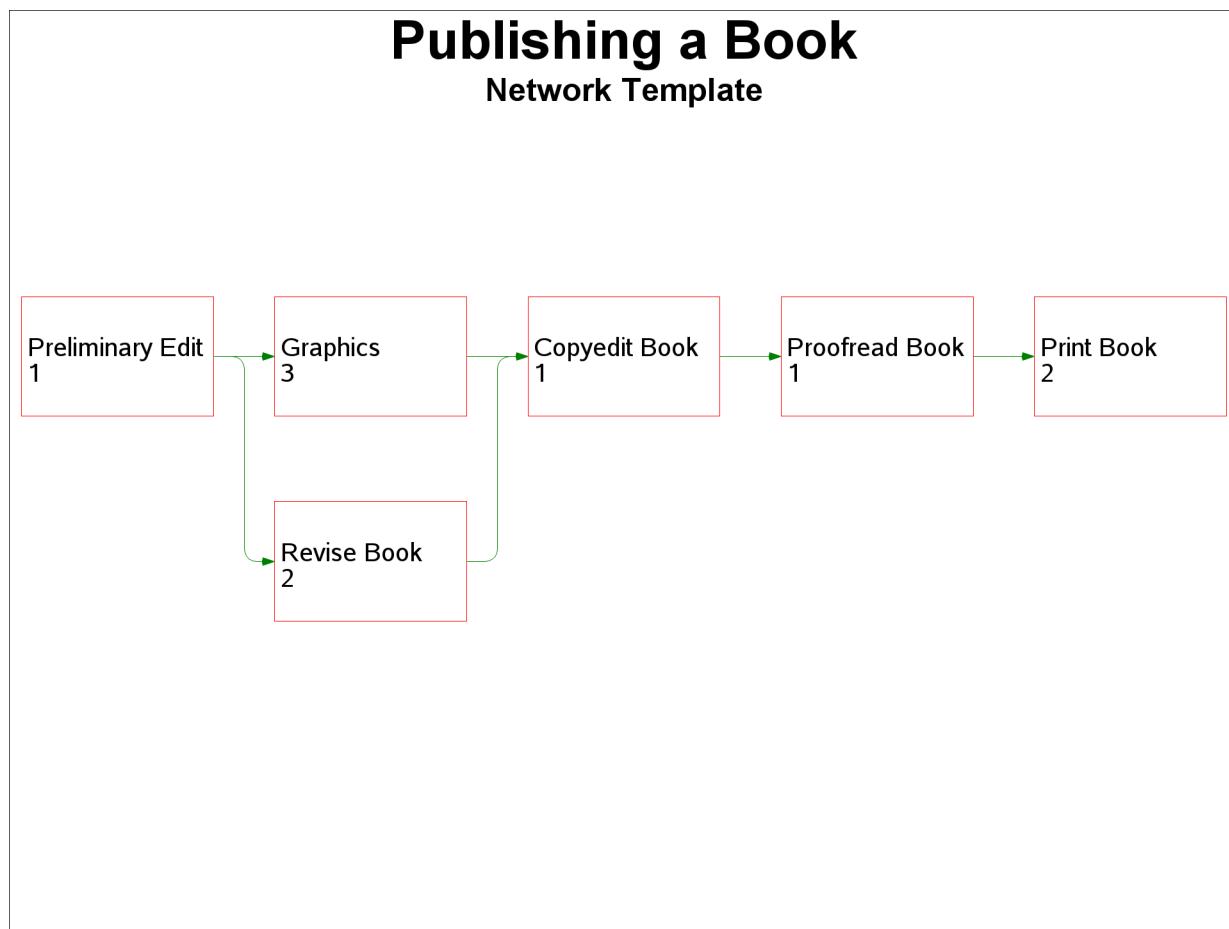

Consider a publishing company that accepts manuscripts from different authors for publication. The publication of each book can be treated as a project. Thus, at a given point in time, several projects, almost identical in nature, may be in progress. Some of the resources that may be needed are a technical editor, a copyeditor, and a graphic artist. All the books that are currently being worked on share a common pool of these resources. This example uses a simplified version of such a scenario to illustrate some of the ways in which you can handle multiple projects competing for the same pool of resources.

The network in [Output 3.6.1](#) represents some of the tasks required to publish one book and the precedence constraints among these tasks; the durations in the diagram are in weeks. Suppose that the *generic* project data are in the data set book, which is displayed in [Output 3.6.2](#). This data set is used as a *template* for creating the Activity data set for any book publishing project.

Suppose that the company is working on two books simultaneously. The editor and artist must now allocate their time between the two books. The following program uses the *template* data set book to create Activity data sets book1 and book2 corresponding to the publication of each book. Any modifications to the generic project data can be made in the DATA step or by using PROC PM. In this example, the duration for the first activity, ‘Preliminary Edit,’ is changed to two weeks for the second book. The two Activity data sets book1 and book2 are also displayed in [Output 3.6.2](#).

```

data book1;
length act $6. succ $6.;
set book;
subproj = "Book 1";
act = "B1"||task;
if succ ^= " " then succ = "B1"||succ;
run;

data book2;
length act $6. succ $6.;
set book;
subproj = "Book 2";
act = "B2"||task;
if act = "B2PEDT" then dur = 2;
if succ ^= " " then succ = "B2"||succ;
run;

title 'Publishing Book 1';
proc print data=book1;
var subproj task act succ id dur editor artist;
run;

title 'Publishing Book 2';
proc print data=book2;
var subproj task act succ id dur editor artist;
run;

```

**Output 3.6.2** Template and Activity Data Sets for Book Publishing Example

**Publishing Book 1**

Obs	subproj	task	act	succ	id	dur	editor	artist
1	Book 1	PEDT	B1PEDT	B1REV	Preliminary Edit	1	1	.
2	Book 1	PEDT	B1PEDT	B1GRPH	Preliminary Edit	1	1	.
3	Book 1	REV	B1REV	B1CEDT	Revise Book	2	1	.
4	Book 1	GRPH	B1GRPH	B1CEDT	Graphics	3	.	1
5	Book 1	CEDT	B1CEDT	B1PRF	Copyedit Book	1	1	.
6	Book 1	PRF	B1PRF	B1PRNT	Proofread Book	1	1	.
7	Book 1	PRNT	B1PRNT		Print Book	2	.	.

**Publishing Book 2**

Obs	subproj	task	act	succ	id	dur	editor	artist
1	Book 2	PEDT	B2PEDT	B2REV	Preliminary Edit	2	1	.
2	Book 2	PEDT	B2PEDT	B2GRPH	Preliminary Edit	2	1	.
3	Book 2	REV	B2REV	B2CEDT	Revise Book	2	1	.
4	Book 2	GRPH	B2GRPH	B2CEDT	Graphics	3	.	1
5	Book 2	CEDT	B2CEDT	B2PRF	Copyedit Book	1	1	.
6	Book 2	PRF	B2PRF	B2PRNT	Proofread Book	1	1	.
7	Book 2	PRNT	B2PRNT		Print Book	2	.	.

As a next step, the data sets for the two subprojects are combined to form an Activity data set for the entire project. A variable priority is assigned the value ‘1’ for activities pertaining to the first book and the value ‘2’ for those pertaining to the second one. In other words, Book 1 has priority over Book 2. The Resource data set specifies the availability for each of the resources to be 1. The input data sets, books and resource, are displayed in [Output 3.6.3](#).

```

data books;
  set book1 book2;
  if subproj = "Book 1" then priority = 1;
  else priority = 2;
  run;

data resource;
  input avdate & date7. editor artist;
  format avdate date7.;
  datalines;
1jan03   1   1
;

title 'Publishing Books 1 and 2';
proc print data=books;
  var subproj priority task act succ id dur editor artist;
  run;

title 'Resources Available';
proc print data=resource;
  run;

```

**Output 3.6.3** Input Data Sets for Book Publishing Example**Publishing Books 1 and 2**

Obs	subproj	priority	task	act	succ	id	dur	editor	artist
1	Book 1	1	PEDT	B1PEDT	B1REV	Preliminary Edit	1	1	.
2	Book 1	1	PEDT	B1PEDT	B1GRPH	Preliminary Edit	1	1	.
3	Book 1	1	REV	B1REV	B1CEDT	Revise Book	2	1	.
4	Book 1	1	GRPH	B1GRPH	B1CEDT	Graphics	3	.	1
5	Book 1	1	CEDT	B1CEDT	B1PRF	Copyedit Book	1	1	.
6	Book 1	1	PRF	B1PRF	B1PRNT	Proofread Book	1	1	.
7	Book 1	1	PRNT	B1PRNT		Print Book	2	.	.
8	Book 2	2	PEDT	B2PEDT	B2REV	Preliminary Edit	2	1	.
9	Book 2	2	PEDT	B2PEDT	B2GRPH	Preliminary Edit	2	1	.
10	Book 2	2	REV	B2REV	B2CEDT	Revise Book	2	1	.
11	Book 2	2	GRPH	B2GRPH	B2CEDT	Graphics	3	.	1
12	Book 2	2	CEDT	B2CEDT	B2PRF	Copyedit Book	1	1	.
13	Book 2	2	PRF	B2PRF	B2PRNT	Proofread Book	1	1	.
14	Book 2	2	PRNT	B2PRNT		Print Book	2	.	.

**Resources Available**

Obs	avdate	editor	artist
1	01JAN03	1	1

PROC CPM is then invoked to schedule the project to start on January 1, 2003. The PROJECT statement is used to indicate the subproject to which each activity belongs. The data set bookschd (displayed in Output 3.6.4) contains the schedule for the entire project. The ADDACT option on the PROC CPM statement adds observations for each of the subprojects, ‘Book 1’ and ‘Book 2,’ as well as one observation for the entire project. These observations are added at the end of the list of the observations corresponding to the observations in the input data set. The Usage data set booksout is also displayed in Output 3.6.4.

```

proc cpm data=books resin=resource
  out=bookschd resout=booksout
  date='1jan03'd interval=week
  addact;
  act      act;
  dur      dur;
  succ     succ;
  resource editor artist / per=avdate avp rcp
                           rule=actprty actprty=priority
                           delayanalysis;
  id      id task;
  project subproj;
run;

```

Compare the E\_START and S\_START schedules (in the data set bookschd) and note that on January 1, the activity ‘B1PEDT’ for Book1 is scheduled to start while the preliminary editing of book 2 (activity B2PEDT) has been postponed, due to subproject ‘Book 1’ having priority over subproject ‘Book 2.’ On January 22, there is no activity belonging to subproject ‘Book 1’ that demands an editor; thus, the activity ‘B2PEDT’ is scheduled to start on that day. As a result, the editor is working on an activity in the second project for two weeks starting from January 22, 2003; when ‘B1CEDT’ is ready to start, the editor is not available, causing a delay in this activity. Thus, even though the first book has priority over the second book, the scheduling algorithm does not keep a resource waiting for activities in the first project. However, if you enable activity splitting, you can reclaim the resource for the first book by allowing activities in the second project to be split, if necessary. For details regarding the scheduling algorithm allowing splitting of activities, see Chapter 4, “The CPM Procedure.”

**NOTE:** The entire project finishes on April 1, 2003; resource constraints have delayed project completion by four weeks. The variable R\_DELAY in the Schedule data set bookschd indicates the amount of delay in weeks caused by resource constraints. The value of R\_DELAY does not include any delay in the activity that is caused by a resource delay in one of its predecessors. See [Example 4.15](#) in Chapter 4, “The CPM Procedure,” for more details about the R\_DELAY variable.

**Output 3.6.4** Data Sets BOOKSCHD and BOOKSOUT**Schedule for Project BOOKS**

Obs	subproj	PROJ_DUR	PROJ_LEV	act	succ	dur	id	task	editor	artist	S_START
1	Book 1	.		2 B1PEDT	B1REV	1	Preliminary Edit	PEDT	1	.	01JAN03
2	Book 1	.		2 B1PEDT	B1GRPH	1	Preliminary Edit	PEDT	1	.	01JAN03
3	Book 1	.		2 B1REV	B1CEDT	2	Revise Book	REV	1	.	08JAN03
4	Book 1	.		2 B1GRPH	B1CEDT	3	Graphics	GRPH	.	1	08JAN03
5	Book 1	.		2 B1CEDT	B1PRF	1	Copyedit Book	CEDT	1	.	05FEB03
6	Book 1	.		2 B1PRF	B1PRNT	1	Proofread Book	PRF	1	.	12FEB03
7	Book 1	.		2 B1PRNT		2	Print Book	PRNT	.	.	19FEB03
8	Book 2	.		2 B2PEDT	B2REV	2	Preliminary Edit	PEDT	1	.	22JAN03
9	Book 2	.		2 B2PEDT	B2GRPH	2	Preliminary Edit	PEDT	1	.	22JAN03
10	Book 2	.		2 B2REV	B2CEDT	2	Revise Book	REV	1	.	19FEB03
11	Book 2	.		2 B2GRPH	B2CEDT	3	Graphics	GRPH	.	1	05FEB03
12	Book 2	.		2 B2CEDT	B2PRF	1	Copyedit Book	CEDT	1	.	05MAR03
13	Book 2	.		2 B2PRF	B2PRNT	1	Proofread Book	PRF	1	.	12MAR03
14	Book 2	.		2 B2PRNT		2	Print Book	PRNT	.	.	19MAR03
15		9		1 Book 1		.			.	.	01JAN03
16		10		1 Book 2		.			.	.	22JAN03
17		13		0		.			.	.	01JAN03

Obs	S_FINISH	E_START	E_FINISH	L_START	L_FINISH	R_DELAY	DELAY_R	SUPPL_R
1	07JAN03	01JAN03	07JAN03	08JAN03	14JAN03	0		
2	07JAN03	01JAN03	07JAN03	08JAN03	14JAN03	0		
3	21JAN03	08JAN03	21JAN03	22JAN03	04FEB03	0		
4	28JAN03	08JAN03	28JAN03	15JAN03	04FEB03	0		
5	11FEB03	29JAN03	04FEB03	05FEB03	11FEB03	1	editor	
6	18FEB03	05FEB03	11FEB03	12FEB03	18FEB03	0		
7	04MAR03	12FEB03	25FEB03	19FEB03	04MAR03	0		
8	04FEB03	01JAN03	14JAN03	01JAN03	14JAN03	3	editor	
9	04FEB03	01JAN03	14JAN03	01JAN03	14JAN03	3	editor	
10	04MAR03	15JAN03	28JAN03	22JAN03	04FEB03	2	editor	
11	25FEB03	15JAN03	04FEB03	15JAN03	04FEB03	0		
12	11MAR03	05FEB03	11FEB03	05FEB03	11FEB03	0		
13	18MAR03	12FEB03	18FEB03	12FEB03	18FEB03	0		
14	01APR03	19FEB03	04MAR03	19FEB03	04MAR03	0		
15	04MAR03	01JAN03	25FEB03	08JAN03	04MAR03	0		
16	01APR03	01JAN03	04MAR03	01JAN03	04MAR03	3		
17	01APR03	01JAN03	04MAR03	01JAN03	04MAR03	0		

**Output 3.6.4** *continued***Resource Usage for Project BOOKS**


<b>Obs</b>	<b>_TIME_</b>	<b>Reditor</b>	<b>Aeditor</b>	<b>Rartist</b>	<b>Aartist</b>
<b>1</b>	01JAN03	1	0	0	1
<b>2</b>	08JAN03	1	0	1	0
<b>3</b>	15JAN03	1	0	1	0
<b>4</b>	22JAN03	1	0	1	0
<b>5</b>	29JAN03	1	0	0	1
<b>6</b>	05FEB03	1	0	1	0
<b>7</b>	12FEB03	1	0	1	0
<b>8</b>	19FEB03	1	0	1	0
<b>9</b>	26FEB03	1	0	0	1
<b>10</b>	05MAR03	1	0	0	1
<b>11</b>	12MAR03	1	0	0	1
<b>12</b>	19MAR03	0	1	0	1
<b>13</b>	26MAR03	0	1	0	1
<b>14</b>	02APR03	0	1	0	1

The output data sets bookschd and booksout can be used to produce graphical reports of the schedule and the resource usage. In particular, the Schedule data set can be used to produce a zoned, time-scaled network diagram as shown in [Output 3.6.5](#). The program used to produce the network diagram is shown in the following code. In this example, only the leaf tasks (those without any subtasks) are used to draw the network diagram. Further, the activities are aligned according to the resource-constrained start times and grouped according to the subproject.

```
goptions hpos=98 vpos=60;

pattern1 v=e c=green;
pattern2 v=e c=red;


title c=black h=4 'Schedule for Project Books';
proc netdraw data=bookschd(where=(proj_dur=.)) graphics;
  actnet / act=act succ=succ
    id=(task) nodefid nolabel
    xbetween=8 htext=3 pcompress
    zone=subproj zonepat zonespace
    align=s_start separatearcs;
  label subproj = 'Subproject';
run;
```

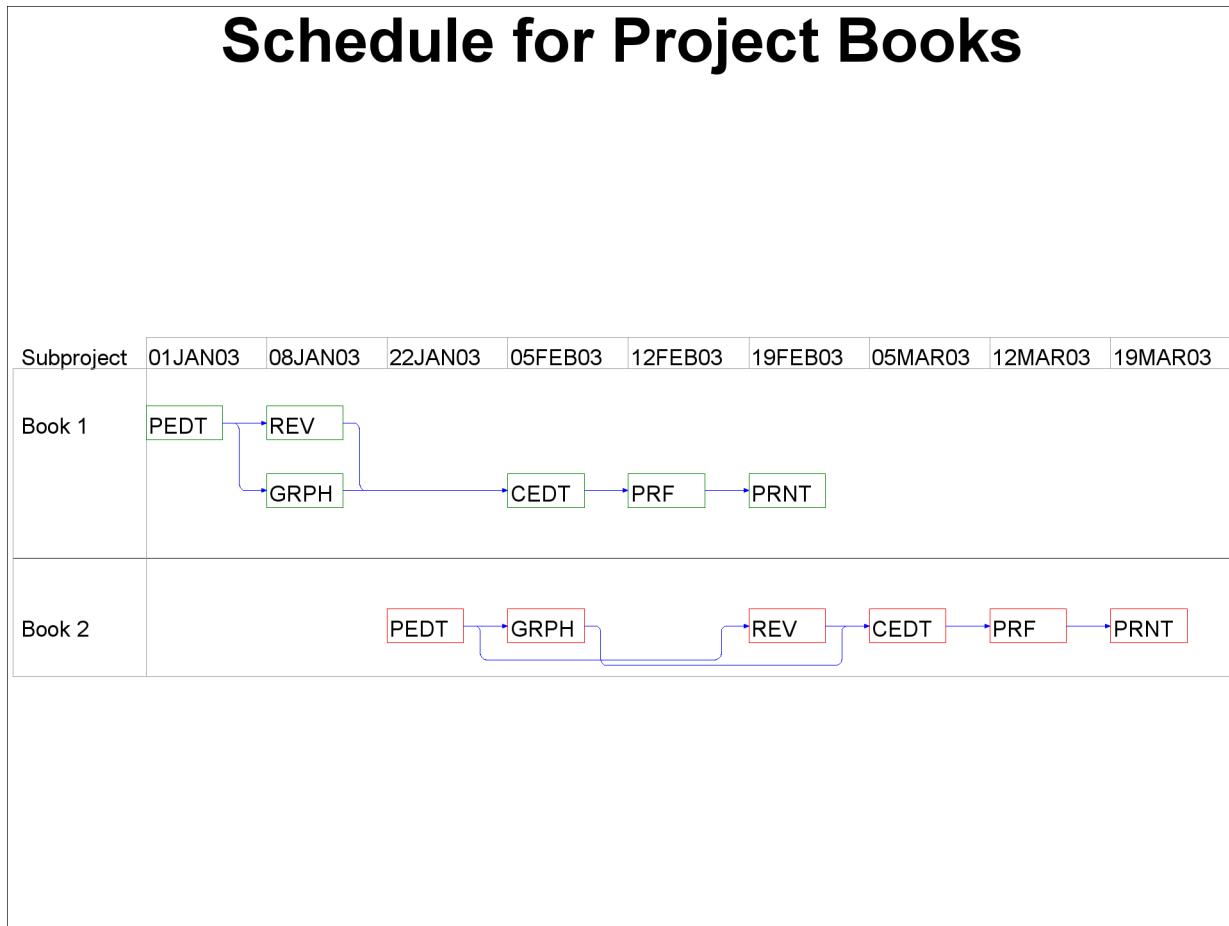**Output 3.6.5** Resource Constrained Schedule for Project Books

The same project can also be scheduled using the PM procedure, as shown in the following statements. The resulting PM Window is shown in [Output 3.6.6](#). The advantage with using PROC PM is that you can use the PM Window to edit the activity information, such as the durations, resource requirements, and so forth.

```

proc pm data=books resin=resource
         out=pmsched resout=pmrout
         date='1jan03'd interval=week;
act      act;
dur      dur;
succ     succ;
resource editor artist / per=avdate
                  avp rcp
                  rule=actprty
                  actprty=priority
                  delayanalysis;
id      id task;
project  subproj;
run;
```

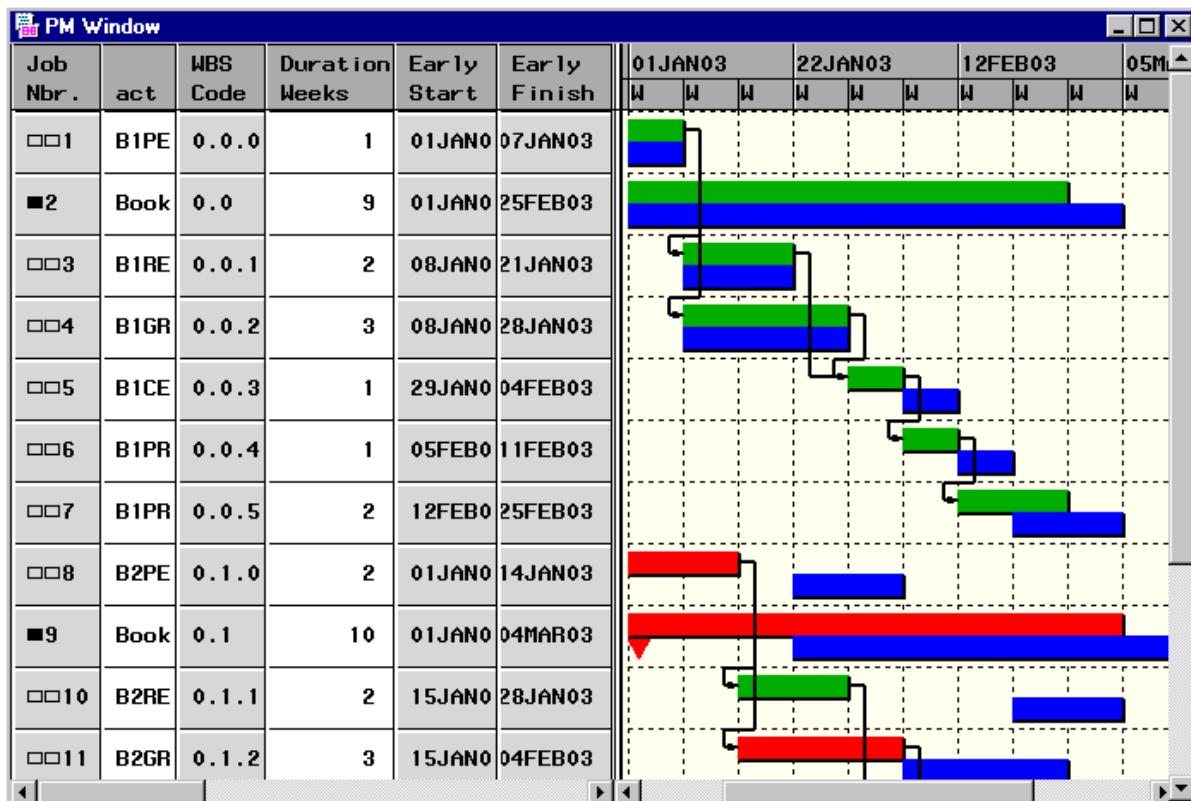**Output 3.6.6** PM Window on Book Project

### Example 3.7: Sequential Scheduling of Projects

Suppose the schedule displayed in Output 3.6.4 is not acceptable; you want the first book to be finished as soon as possible and do not want resources to be claimed by the second book at the cost of the first book. One way to accomplish this is to enable activities related to the second book to be split whenever the first book demands a resource currently in use by the second book. If you do not want activities to be split, you can still accomplish your goal by sequential scheduling. The structure of the input and output data sets enables you to schedule the two subprojects sequentially.

This example illustrates the sequential scheduling of subprojects ‘Book 1’ and ‘Book 2.’ The following program first schedules the subproject ‘Book 1’ using the resources available. The resulting schedule is displayed in Output 3.7.1. The Usage data set bk1out is also displayed in Output 3.7.1.

```
/* Schedule the higher priority project first */
proc cpm data=book1 resin=resource
  out=bk1schd resout=bk1out
  date='1jan03'd interval=week;
  act      act;
  dur      dur;
  succ     succ;
  resource editor artist / per=avdate avp rcp;
  id      id;
run;
```

**Output 3.7.1** Sequential Scheduling of Subprojects: Book 1  
**Schedule for sub-project BOOK1**

Obs	act	succ	dur	id	editor	artist	S_START	S_FINISH	E_START	E_FINISH	L_START	L_FINISH
1	B1PEDT	B1REV	1	Preliminary Edit	1	.	01JAN03	07JAN03	01JAN03	07JAN03	01JAN03	07JAN03
2	B1PEDT	B1GRPH	1	Preliminary Edit	1	.	01JAN03	07JAN03	01JAN03	07JAN03	01JAN03	07JAN03
3	B1REV	B1CEDT	2	Revise Book	1	.	08JAN03	21JAN03	08JAN03	21JAN03	15JAN03	28JAN03
4	B1GRPH	B1CEDT	3	Graphics	.	1	08JAN03	28JAN03	08JAN03	28JAN03	08JAN03	28JAN03
5	B1CEDT	B1PRF	1	Copyedit Book	1	.	29JAN03	04FEB03	29JAN03	04FEB03	29JAN03	04FEB03
6	B1PRF	B1PRNT	1	Proofread Book	1	.	05FEB03	11FEB03	05FEB03	11FEB03	05FEB03	11FEB03
7	B1PRNT		2	Print Book	.	.	12FEB03	25FEB03	12FEB03	25FEB03	12FEB03	25FEB03

**Resource Usage for sub-project BOOK1**

Obs	_TIME_	Reditor	Aeditor	Rartist	Aartist
1	01JAN03	1	0	0	1
2	08JAN03	1	0	1	0
3	15JAN03	1	0	1	0
4	22JAN03	0	1	1	0
5	29JAN03	1	0	0	1
6	05FEB03	1	0	0	1
7	12FEB03	0	1	0	1
8	19FEB03	0	1	0	1
9	26FEB03	0	1	0	1

The Usage data set produced by PROC CPM has two variables, Aeditor and Aartist, showing the availability of the editor and the artist on each day of the project, *after* scheduling subproject ‘Book 1.’ This data set is used to create the data set remres, listing the remaining resources available, which is then used as the Resource input data set for scheduling the subproject ‘Book 2.’ The following program shows the DATA step and the invocation of PROC CPM.

The schedule for publishing ‘Book 2’ is displayed in Output 3.7.2. The Usage data set bk2out is also displayed in Output 3.7.2. Note that this method of scheduling has ensured that ‘Book 1’ is not delayed; however, the entire project has been delayed by two more weeks, resulting in a total delay of six weeks.

```
/* Construct the Resource availability data set */
/* with proper resource names */
```

```
data remres;
  set bk1out;
  avdate=_time_;
  editor=aeditor;
  artist=aartist;
  keep avdate editor artist;
  format avdate date7. ;
  run;
```

```
proc cpm data=book2 resin=remres
  out=bk2schd resout=bk2out
  date='1jan03'd interval=week;
  act      act;
  dur      dur;
```

```

succ      succ;
resource editor artist / per=avdate avp rcp;
id        id;
run;

```

### Output 3.7.2 Sequential Scheduling of Subprojects: Book 2

#### Schedule for sub-project BOOK2

Obs	act	succ	dur	id	editor	artist	S_START	S_FINISH	E_START	E_FINISH	L_START	L_FINISH
1	B2PEDT	B2REV	2	Preliminary Edit	1	.	12FEB03	25FEB03	01JAN03	14JAN03	01JAN03	14JAN03
2	B2PEDT	B2GRPH	2	Preliminary Edit	1	.	12FEB03	25FEB03	01JAN03	14JAN03	01JAN03	14JAN03
3	B2REV	B2CEDT	2	Revise Book	1	.	26FEB03	11MAR03	15JAN03	28JAN03	22JAN03	04FEB03
4	B2GRPH	B2CEDT	3	Graphics	.	1	26FEB03	18MAR03	15JAN03	04FEB03	15JAN03	04FEB03
5	B2CEDT	B2PRF	1	Copyedit Book	1	.	19MAR03	25MAR03	05FEB03	11FEB03	05FEB03	11FEB03
6	B2PRF	B2PRNT	1	Proofread Book	1	.	26MAR03	01APR03	12FEB03	18FEB03	12FEB03	18FEB03
7	B2PRNT		2	Print Book	.	.	02APR03	15APR03	19FEB03	04MAR03	19FEB03	04MAR03

#### Resource Usage for sub-project BOOK2

Obs	_TIME_	Reditor	Aeditor	Rartist	Aartist
1	12FEB03	1	0	0	1
2	19FEB03	1	0	0	1
3	26FEB03	1	0	1	0
4	05MAR03	1	0	1	0
5	12MAR03	0	1	1	0
6	19MAR03	1	0	0	1
7	26MAR03	1	0	0	1
8	02APR03	0	1	0	1
9	09APR03	0	1	0	1
10	16APR03	0	1	0	1

### Example 3.8: Project Cost Control

Cost control and accounting are important aspects of project management. Cost data for a project may be associated with activities or groups of activities, or with resources, such as personnel or equipment. For example, consider a project that consists of several subprojects, each of which is contracted to a different company. From the contracting company's point of view, each subproject can be treated as one cost item; all the company needs to know is how much each subproject is going to cost. On the other hand, another project may contain several activities, each of which requires two types of labor, skilled and unskilled. The cost for each activity in the project may have to be computed on the basis of how much skilled or unskilled labor that activity uses. In this case, activity and project costs are determined from the resources used. Further, for any project, there may be several ways in which costs need to be summarized and accounted for. In addition to determining the cost of each individual activity, you may want to determine periodic budgets for different departments that are involved with the project or compare the actual costs that were incurred with the budgeted costs.

It is easy to set up cost accounting systems using the output data sets produced by PROC CPM, whether costs are associated with activities or with resources. In fact, you can even treat cost as a consumable resource if you can estimate the cost per day for each of the activities (see Chapter 4, “[The CPM Procedure](#),” for details about resource allocation and types of resources). This example illustrates such a method for monitoring costs and shows how you can compute some of the standard cost performance measures used in project management.

The following three measures can be used to determine if a project is running on schedule and within budget (see Moder, Phillips, and Davis 1983, for a detailed discussion on project cost control):

- *Actual cost of work performed (ACWP)* is the actual cost expended to perform the work accomplished in a given period of time.
- *Budgeted cost of work performed (BCWP)* is the budgeted cost of the work *completed* in a given period of time.
- *Budgeted cost of work scheduled (BCWS)* is the budgeted cost of the work *scheduled* to be accomplished in a given period of time (if a baseline schedule were followed).

Consider the survey example described earlier in this chapter. Suppose that it is possible to estimate the cost per day for each activity in the project. The following data set survcost contains the project data (activity, succ1–succ3, id, duration) and a variable named cost containing the cost per day in dollars. In order to compute the BCWS for the project, you need to establish a baseline schedule. Suppose the early start schedule computed by PROC CPM is chosen as the baseline schedule. The Resource data set costav1 establishes cost as a consumable resource, so that the CPM procedure can be used to accumulate costs (using the CUMUSAGE option).

The following program invokes PROC CPM with the RESOURCE statement and saves the Usage data set in survrout. The variable ecost in this Usage data set contains the cumulative expense incurred for the baseline schedule; this is the same as the budgeted cost of work scheduled (or BCWS) saved in the data set basecost.

```

data survcost;
  format id $20. activity $8. succ1-succ3 $8. ;
  input id & activity & duration succ1 & succ2 & succ3 & cost;
  datalines;
Plan Survey      plan sur   4 hire per  design q   .      300
Hire Personnel   hire per   5 trn per   .      .      350
Design Questionnaire  design q   3 trn per  select h  print q   100
Train Personnel   trn per   3 cond sur  .      .      500
Select Households  select h   3 cond sur  .      .      300
Print Questionnaire  print q   4 cond sur  .      .      250
Conduct Survey    cond sur   10 analyze .      .      200
Analyze Results   analyze   6 .      .      .      500
;

data holidata;
  format hol date7. ;
  hol = '4jul03'd;
  run;

```

```

data costav1;
  input per & date7. otype $ cost;
  format per date7. ;
  datalines;
    restype   2
1jul03  reslevel 12000
;

proc cpm date='1jul03'd interval=weekday
  data=survcost resin=costav1 holidata=holidata
  out=sched      resout=survrtout;
  activity     activity;
  successor   succ1-succ3;
  duration    duration;
  holiday     hol;
  id          id;
  resource    cost / period = per
                obstype = otype cumusage;
run;

data basecost (keep = _time_ bcws);
  set survrtout;
  bcws = ecost;
run;

```

Suppose that the project started as planned on July 1, 2003, but some of the activities took longer than planned and some of the cost estimates were found to be incorrect. The following data set, actual, contains updated information: the variables as and af contain the actual start and finish times of the activities that have been completed or are in progress. The variable actcost contains the revised cost per day for each activity. The following program combines this information with the existing project data and saves the result in the data set update, displayed in [Output 3.8.1](#). The Resource data set costav12 (also displayed in [Output 3.8.1](#)) defines cost and actcost as consumable resources.

```

data actual;
  format id $20. ;
  input id & as & date9. af & date9. actcost;
  format as af date7. ;
  datalines;
Plan Survey        1JUL03   8JUL03   275
Hire Personnel     9JUL03   15JUL03  350
Design Questionnaire 10JUL03  14JUL03  150
Train Personnel    16JUL03  17JUL03  800
Select Households  15JUL03  17JUL03  450
Print Questionnaire 15JUL03  18JUL03  250
Conduct Survey     21JUL03   .        200
;

data work.update;
  merge survcost actual;
run;

data costav12;
  input per & date7. otype $ cost actcost;

```

```

format per date7.;

data;
  restype 2      2
1jul03  reslevel 12000 12000
;

title 'Activity Data Set UPDATE';
proc print data=work.update;
run;

title 'Resource Data Set COSTAVL2';
proc print data=costavl2;
run;

```

### Output 3.8.1 Project Cost Control: Progress Update

#### Activity Data Set UPDATE

Obs id	activity	succ1	succ2	succ3	duration	cost	as	af	actcost	
1	Plan Survey	plan sur	hire per	design q	4	300	01JUL03	08JUL03	275	
2	Hire Personnel	hire per	trn per		5	350	09JUL03	15JUL03	350	
3	Design Questionnaire	design q	trn per	select h	print q	3	100	10JUL03	14JUL03	150
4	Train Personnel	trn per	cond sur			3	500	16JUL03	17JUL03	800
5	Select Households	select h	cond sur			3	300	15JUL03	17JUL03	450
6	Print Questionnaire	print q	cond sur			4	250	15JUL03	18JUL03	250
7	Conduct Survey	cond sur	analyze			10	200	21JUL03	.	200
8	Analyze Results	analyze				6	500	.	.	.

#### Resource Data Set COSTAVL2

Obs	per	otype	cost	actcost
1	.	restype	2	2
2	01JUL03	reslevel	12000	12000

Next, PROC CPM is used to revise the schedule by using the ACTUAL statement to specify the actual start and finish times and the RESOURCE statement to specify both the budgeted and the actual costs. The resulting schedule is saved in the data set updsched (displayed in Output 3.8.2) and the budgeted and the actual cumulative costs of the project (until the current date) are saved in the data set updtrout. These cumulative costs represent the budgeted cost of work performed (BCWP) and the actual cost of work performed (ACWP), respectively, and are saved in the data set updtrout. The two data sets basecost and updtrout are then merged to create a data set that contains the three measures: bcws, bcwp, and acwp. The resulting data set is displayed in Output 3.8.3.

```

proc cpm date='1jul03'd interval=weekday
  data=work.update    resin=costavl2
  out=updsched    resout=updtrout
  holodata=holodata;
activity activity;
successor succ1-succ3;
duration duration;
holiday hol;
id id;

```

```

resource    cost actcost / per      = per
            obstype = otype
            maxdate = '21jul03'd cumusage;
actual / a_start=as a_finish=af;
run;

title 'Updated Schedule: Data Set UPDSCHED';
proc print data=updsched;
run;

data updtcost (keep = _time_ bcwp acwp);
  set updtout;
  bcwp = ecost;
  acwp = eactcost;
run;

/* Create a combined data set to contain the BCWS, BCWP, ACWP */
/* per day and the cumulative values for these costs.          */
data costs;
  merge basecost updtcost;
run;

title 'BCWS, BCWP, and ACWP';
proc print data=costs;
run;

```

### Output 3.8.2 Project Cost Control: Updated Schedule

#### Updated Schedule: Data Set UPDSCHED

Obs	activity	succ1	succ2	succ3	duration	STATUS	A_DUR	id	cost	actcost
1	plan sur	hire per	design q		4	Completed	5	Plan Survey	300	275
2	hire per	trn per			5	Completed	5	Hire Personnel	350	350
3	design q	trn per	select h	print q	3	Completed	3	Design Questionnaire	100	150
4	trn per	cond sur			3	Completed	2	Train Personnel	500	800
5	select h	cond sur			3	Completed	3	Select Households	300	450
6	print q	cond sur			4	Completed	4	Print Questionnaire	250	250
7	cond sur	analyze			10	In Progress	.	Conduct Survey	200	200
8	analyze				6	Pending	.	Analyze Results	500	.

Obs	A_START	A_FINISH	S_START	S_FINISH	E_START	E_FINISH	L_START	L_FINISH
1	01JUL03	08JUL03	01JUL03	08JUL03	01JUL03	08JUL03	01JUL03	08JUL03
2	09JUL03	15JUL03	09JUL03	15JUL03	09JUL03	15JUL03	09JUL03	15JUL03
3	10JUL03	14JUL03	10JUL03	14JUL03	10JUL03	14JUL03	10JUL03	14JUL03
4	16JUL03	17JUL03	16JUL03	17JUL03	16JUL03	17JUL03	16JUL03	17JUL03
5	15JUL03	17JUL03	15JUL03	17JUL03	15JUL03	17JUL03	15JUL03	17JUL03
6	15JUL03	18JUL03	15JUL03	18JUL03	15JUL03	18JUL03	15JUL03	18JUL03
7	21JUL03	.	21JUL03	01AUG03	21JUL03	01AUG03	21JUL03	01AUG03
8	.	.	04AUG03	11AUG03	04AUG03	11AUG03	04AUG03	11AUG03

**Output 3.8.3** Project Cost Control: BCWS, BCWP, ACWP  
**BCWS, BCWP, and ACWP**

Obs	_TIME_	bcws	bcwp	acwp
1	01JUL03	0	0	0
2	02JUL03	300	300	275
3	03JUL03	600	600	550
4	07JUL03	900	900	825
5	08JUL03	1200	1200	1100
6	09JUL03	1650	1500	1375
7	10JUL03	2100	1850	1725
8	11JUL03	2550	2300	2225
9	14JUL03	3450	2750	2725
10	15JUL03	4350	3200	3225
11	16JUL03	5400	4100	4275
12	17JUL03	6150	5150	5775
13	18JUL03	6650	6200	7275
14	21JUL03	6850	6450	7525
15	22JUL03	7050	.	.
16	23JUL03	7250	.	.
17	24JUL03	7450	.	.
18	25JUL03	7650	.	.
19	28JUL03	7850	.	.
20	29JUL03	8050	.	.
21	30JUL03	8250	.	.
22	31JUL03	8450	.	.
23	01AUG03	8650	.	.
24	04AUG03	9150	.	.
25	05AUG03	9650	.	.
26	06AUG03	10150	.	.
27	07AUG03	10650	.	.
28	08AUG03	11150	.	.
29	11AUG03	11650	.	.

The data set **costs**, containing the required cost information, is then used as input to PROC GPLOT to produce a plot of the three cumulative cost measures. The plot is shown in Output 3.8.4.

**NOTE:** BCWS, BCWP, and ACWP are three of the cost measures used as part of *Earned Value Analysis*, which is an important component of the *Cost/Schedule Control Systems Criteria* (referred to as C/SCSC) that was established in 1967 by the Department of Defense (DOD) to standardize the reporting of cost and schedule performance on major contracts. Refer to Fleming (1988) for a detailed discussion of C/SCSC. Similar methods, such as the ones described in this example, can be used to calculate all the relevant measures for analyzing cost and schedule performance.

```
/* Plot the cumulative costs */
data costplot (keep=date dollars id);
  set costs;
  format date date7.;
  date = _time_;
  if bcws ^= . then do;
```

```

        dollars = BCWS; id = 1; output;
        end;
if bcwp ^= . then do;
        dollars = BCWP; id = 2; output;
        end;
if acwp ^= . then do;
        dollars = ACWP; id = 3; output;
        end;
run;

legend1 frame
value=(c=black j=l 'BCWS' 'BCWP' 'ACWP')
label=(c=black);


axis1 width=2
order=('1jul03'd to '1aug03'd by week)
length=60 pct
value=(c=black)
label=(c=black);

axis2 width=2
order=(0 to 12000 by 2000)
length = 55 pct
value=(c=black)
label=(c=black);

symbol1 i=join v=none c=green w=4 l=1;
symbol2 i=join v=none c=blue w=4 l=2;
symbol3 i=join v=none c=red w=4 l=3;
title c=black h=2.5 'Comparison of Costs';

proc gplot data=costplot;
plot dollars * date = id / legend=legend1
haxis=axis1
vaxis=axis2;
run;

```

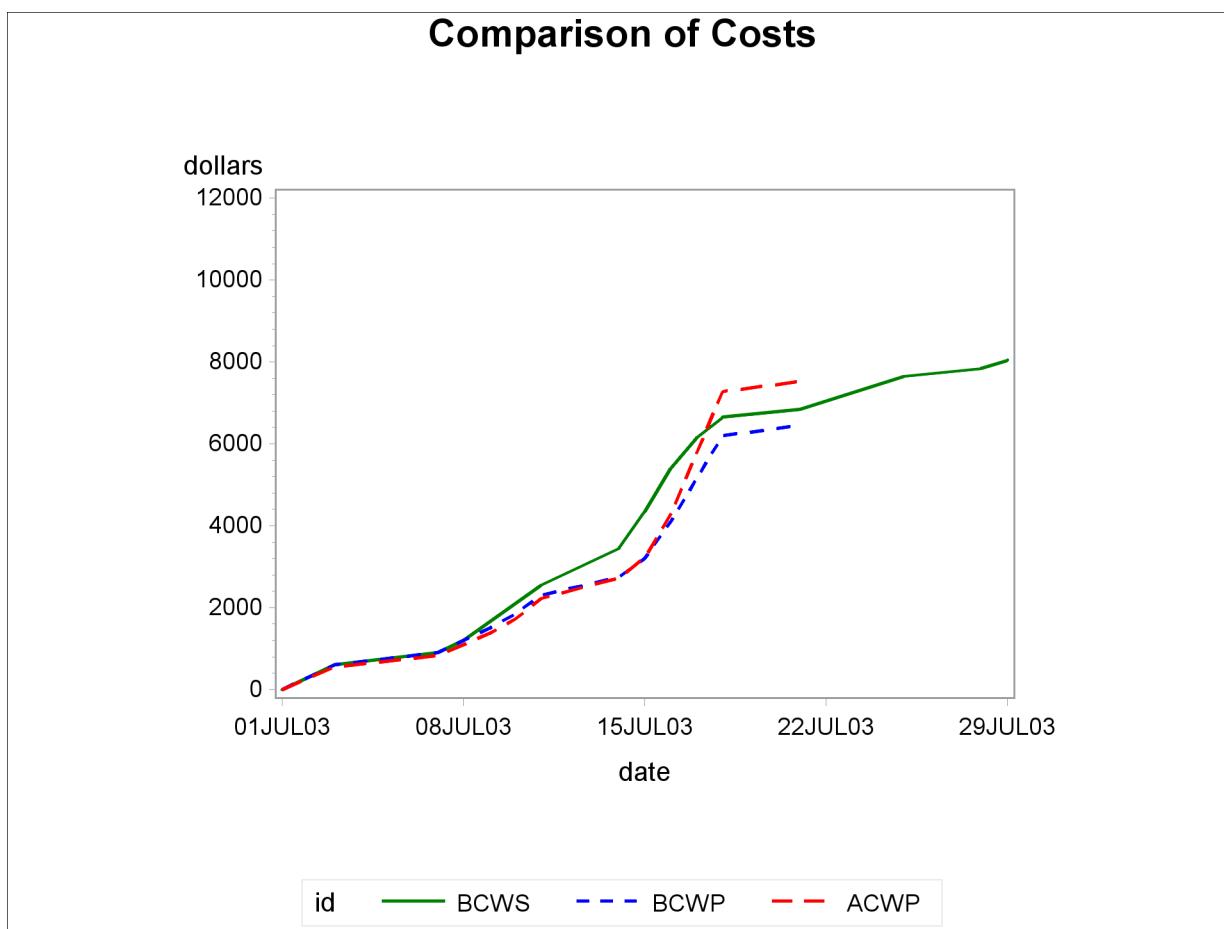**Output 3.8.4** Plot of BCWS, BCWP, and ACWP

### Example 3.9: Subcontracting Decisions

Making decisions about subcontracting forms an important part of several medium-to-large scale projects. For example, in the pharmaceutical industry, the analysis of clinical trials may be a part of the drug development project that could either be accomplished by the company's statistical group or be subcontracted to a statistical consulting firm. The decision may hinge upon how busy the local statistical group is with other projects that may delay the results of the analysis for the drug in question. Further, there may be more than one firm that is a likely candidate for performing the analysis. As a prerequisite for deciding whether to assign the *analysis* subproject to an external firm, you need to obtain a *bid* in the form of estimates of the cost and project duration from the competing firms as well as a corresponding estimate from the in-house team.

The cost corresponding to each possible subcontracting firm may be a combination of the actual costs (consulting fees and so on) and the tardiness of the project (tardiness being measured as the time difference between when the results are expected to be available and the target date for the availability of the results). The information required could be provided in terms of Gantt charts and cost analysis charts. Using this information, the project manager for the drug development project can use the principles of decision analysis to determine whether to do the analysis in-house or assign it to an outside consulting firm and to pick the firm to which the subcontract is to be assigned. Some of these ideas are illustrated in the following example.

**Output 3.9.1** Input Data Sets for Decision Problem

**Subcontracting Decision**  
**The Stage Data Set**

Obs	_STNAME_	_STTYPE_	_OUTCOM_	_REWARD_	_SUCCES_
1	Assignment D		In_House	.	Complete
2			Consult1	-20,000	Act_Finish
3			Consult2	-17,500	Act_Finish
4	Complete	C	On_Time	.	Cost
5			Delay	-10,000	Cost
6	Act_Finish	C	Early	.	
7			Late	.	
8			Delay2	-1,000	
9	Cost	C	High	.	
10			Low	.	

**Subcontracting Decision**  
**The Probability Data Set**

Obs	_GIVEN_	_EVENT_	_PROB_
1		High	0.50
2		Low	0.50
3		On_Time	0.60
4		Delay	0.40
5	Consult1	Early	0.60
6	Consult1	Late	0.35
7	Consult1	Delay2	0.05
8	Consult2	Early	0.50
9	Consult2	Late	0.40
10	Consult2	Delay2	0.10

**Subcontracting Decision**  
**The Payoffs Data Set**

Obs	_STATE1	_STATE2	_VALUE_
1	On_Time	High	-12,000
2	On_Time	Low	-9,500
3	Delay	High	-15,000
4	Delay	Low	-11,500
5	Early		3,500
6	Late		1,500
7	Delay2		0

The stages of the decision problem are identified by the STAGEIN= data set, stage, displayed in [Output 3.9.1](#). As a first step, the drug company needs to decide whether to perform the analysis in-house or to assign it to one of two consulting firms. If the in-house team is chosen, the resulting stage is a chance node, called ‘Complete,’ with two possible outcomes: ‘On-Time’ or ‘Delay’; if there is a delay, the resulting cost to the drug company is \$10,000. For each of these two outcomes, there is a second chance event corresponding to the cost of the analysis. For each of the two consulting firms, the outcome can be one of three possibilities: ‘Early,’ ‘Late,’ or ‘Delay2’; if there is a delay, the drug company imposes a delay penalty of \$9,000 on the firm, resulting in a net reward of -\$1,000 (penalty of \$9,000 minus the cost of \$10,000).

The PROBIN= data set, prob, identifies the various probabilities associated with the different possible outcomes at each of the chance events. The prob data set is also displayed in [Output 3.9.1](#).

The rewards (or payoffs) associated with each of the end stages are listed in the PAYOFFS= data set, payoff (also listed in [Output 3.9.1](#)). For example, for the in-house team, the high (low) cost associated with completing the analysis on time is \$12,000 (\$9,500), and so on.

The following program invokes PROC DTREE to solve the decision problem. The complete decision tree, displayed in [Output 3.9.2](#), represents the various stages and outcomes of the problem and identifies the optimal decision. In this example, the drug company should award the consulting contract to the second consulting firm as indicated by the dashed line for the corresponding branch of the tree.

See Chapter 7, “[The DTREE Procedure](#),” for details about the DTREE procedure.


```

title "Subcontracting Decision";
symbol1 f=marker v=P c=blue;
symbol2 f=marker v=U c=green;
symbol3 f=marker v=A c=red;

/* PROC DTREE statements */
proc dtree stagein=stage
    probin=prob
    payoffs=payoff
    nowarning
    ;
evaluate;
treeplot / graphics font='Cumberland AMT'
    compress ybetween=1 cell1
    lwidth=1 lwidthb=2 hsymbol=2
    symbolc=1 symbold=2 symbole=3
    lstyleb=1
    ;
quit;

```

### Output 3.9.2 Decision Analysis

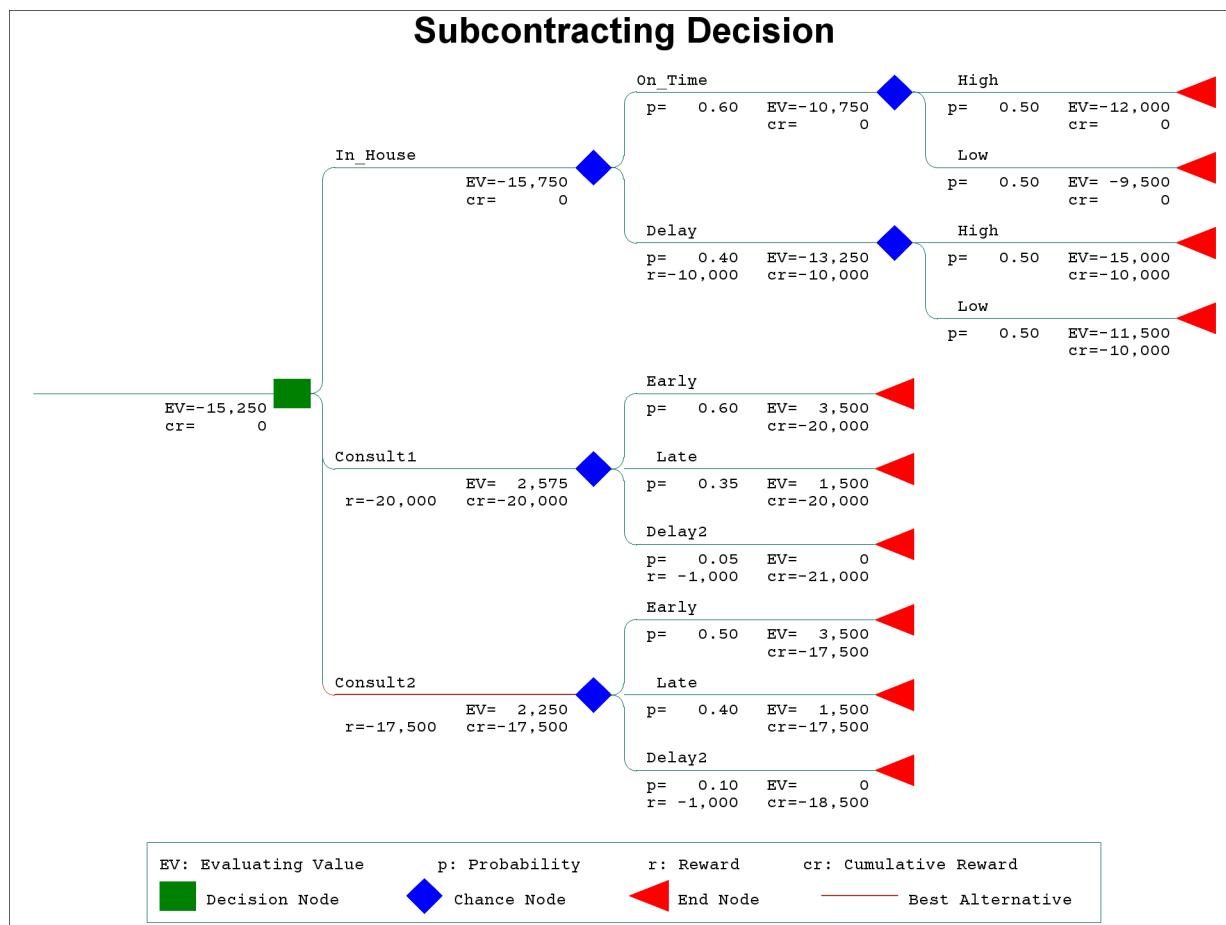

## Project Management Systems

As illustrated in the section “Data Flow” on page 10 and the section “Examples” on page 17, the procedures of SAS/OR software, when combined with the other parts of the SAS System, provide a rich environment for developing customized project management systems. Every company has its own set of requirements for how project data should be handled and for how costs should be accounted. The CPM, GANTT, NETDRAW, and PM procedures, together with the other reporting, summarizing, charting, and plotting procedures, are the basic building blocks that can be combined in several different ways to provide the exact structure that you need. The interactive PM procedure can be used as the primary editing interface for entering all activity information for your projects. Further, the application building tools in the SAS System can be used to cement the pieces together in a menu-driven application. You can create easy-to-use applications enabling the user to enter information continually and to obtain progress reports periodically.

---

## The Projman Application

The Projman application is a user-friendly graphical user interface for performing project management with the SAS System. Through the use of an interactive Gantt chart window provided by the **PM** procedure, you can easily create and manage multiple projects.

Projman is accessed by invoking the **projman** command in the SAS windowing environment or by selecting **Solutions ► Analysis ► Project Management** from the primary SAS menu. Projman enables you to define multiple projects, information about which are stored in a **project dictionary data set**. This project dictionary provides a convenient way to manage all the data sets associated with each project.

Projman also provides a variety of project reports. These reports include Gantt charts, network diagrams, calendars, and tabular listings as well as resource usage and cost reports. You can modify these reports to add your own personalized reports to the application.

For details about the Projman application, see Chapter 10, “The Projman Application.”

---

## Web-Based Scheduling Systems

The examples in this chapter describe several scenarios that illustrate the different ways in which the project management procedures can be used to define, manage, and monitor projects. As described in the previous sections, the SAS System can be used to create comprehensive Decision Support systems or project management systems, in particular, using the procedures described in this book. With the availability of SAS/IntrNet software, you can also create Web-based project management or scheduling systems where the browser is used to display schedules and resource usage information that is updated using the CPM procedure’s scheduling engine.

Examples of such Web-based applications are available at SAS Institute’s external Web site at the following url: <http://support.sas.com/sassamples/demos/supplychain/demos>. In particular, the “Enterprise-Wide Resource Management” (EWRM) demo uses several of the ideas described in this chapter and illustrated in the examples throughout this book to create an application that schedules the tasks required for the maintenance of aircraft engines at a hypothetical service facility.

**NOTE:** The EWRM Web demo is a client-server application driven from your desktop and running at SAS Institute in Cary, NC. You can access the demo from SAS Institute’s Supply Chain Web site ([http://support.sas.com/sassamples/demos/supplychain/demos/ewrm\\_index.html](http://support.sas.com/sassamples/demos/supplychain/demos/ewrm_index.html)). The graphs and reports in the demo have not been saved, but are calculated on demand; this means that they change dynamically as the data used to calculate them change. This demo requires Internet Explorer, version 5.0 or later.

---

## Microsoft Project Conversion Macros

%MSPTOSAS is a SAS macro that converts Microsoft Project® data to a form that is readable by the PM procedure. The macro generates the necessary SAS data sets, determines the values of the relevant options,

and invokes an instance of the PM procedure with the converted project data. %SASTOMSP is a SAS macro that converts data sets used by the PM and CPM procedures into a file that is readable by Microsoft Project. For details about the macros, see Chapter 6, “[The Microsoft Project Conversion Macros](#).”

---

## Earned Value Management Macros

*Earned value* refers to the amount of work that has been completed within a project to date. In earned value management (EVM), this earned value is compared to the original budget and schedule in order to measure project performance, estimate future costs, and predict the project completion date.

The earned value management macros are divided into two sets. The first set is used to analyze schedule and cost data and to derive earned value metrics. The second set is used to graphically represent the results from the first set. For details, see Chapter 11, “[The Earned Value Management Macros](#).”

---

## References

- Cohen, M. (1990). “Decision Analysis in Project Management.” *PM Network* 4:37–40.
- Fleming, Q. W. (1988). *Cost/Schedule Control Systems Criteria: The Management Guide to C/SCSC*. Chicago: Probus Publishing.
- Moder, J. J., Phillips, C. R., and Davis, E. W. (1983). *Project Management with CPM, PERT, and Precedence Diagramming*. New York: Van Nostrand Reinhold.
- SAS Institute Inc. (1993). *SAS/OR Software: Project Management Examples*. Cary, NC: SAS Institute Inc.
- Williams, G. A., and Boyd, W. L. (1990). “Decision Support Systems and Project Management.” *PM Network* 4:31–36.

# Chapter 4

## The CPM Procedure

### Contents

---

Overview: CPM Procedure . . . . .	55
Getting Started: CPM Procedure . . . . .	56
Syntax: CPM Procedure . . . . .	61
Functional Summary . . . . .	61
PROC CPM Statement . . . . .	65
ACTIVITY Statement . . . . .	70
ACTUAL Statement . . . . .	70
ALIGNDATE Statement . . . . .	73
ALIGNTYPE Statement . . . . .	73
BASELINE Statement . . . . .	74
CALID Statement . . . . .	75
DURATION Statement . . . . .	76
HEADNODE Statement . . . . .	76
HOLIDAY Statement . . . . .	77
ID Statement . . . . .	78
PROJECT Statement . . . . .	78
RESOURCE Statement . . . . .	80
SUCCESSOR Statement . . . . .	90
TAILNODE Statement . . . . .	91
Details: CPM Procedure . . . . .	92
Scheduling Subject to Precedence Constraints . . . . .	93
Using the INTERVAL= Option . . . . .	94
Nonstandard Precedence Relationships . . . . .	95
Time-Constrained Scheduling . . . . .	96
Finish Milestones . . . . .	98
OUT= Schedule Data Set . . . . .	99
Multiple Calendars . . . . .	101
Baseline and Target Schedules . . . . .	109
Progress Updating . . . . .	109
Resource-Driven Durations and Resource Calendars . . . . .	112
Resource Usage and Allocation . . . . .	113
RESOURCEOUT= Usage Data Set . . . . .	127
RESOURCESCHED= Resource Schedule Data Set . . . . .	131
Multiproject Scheduling . . . . .	131
Macro Variable _ORCPM_ . . . . .	134
Input Data Sets and Related Variables . . . . .	135

Missing Values in Input Data Sets . . . . .	137
FORMAT Specification . . . . .	139
Computer Resource Requirements . . . . .	139
Examples: CPM Procedure . . . . .	<b>140</b>
Example 4.1: Activity-on-Node Representation . . . . .	142
Example 4.2: Activity-on-Arc Representation . . . . .	146
Example 4.3: Meeting Project Deadlines . . . . .	149
Example 4.4: Displaying the Schedule on a Calendar . . . . .	151
Example 4.5: Precedence Gantt Chart . . . . .	154
Example 4.6: Changing Duration Units . . . . .	155
Example 4.7: Controlling the Project Calendar . . . . .	159
Example 4.8: Scheduling around Holidays . . . . .	161
Example 4.9: CALEDATA and WORKDATA Data Sets . . . . .	167
Example 4.10: Multiple Calendars . . . . .	172
Example 4.11: Nonstandard Relationships . . . . .	181
Example 4.12: Activity Time Constraints . . . . .	186
Example 4.13: Progress Update and Target Schedules . . . . .	188
Example 4.14: Summarizing Resource Utilization . . . . .	193
Example 4.15: Resource Allocation . . . . .	197
Example 4.16: Using Supplementary Resources . . . . .	207
Example 4.17: INFEASDIAGNOSTIC Option and Aggregate Resource Type . . . . .	211
Example 4.18: Variable Activity Delay . . . . .	217
Example 4.19: Activity Splitting . . . . .	225
Example 4.20: Alternate Resources . . . . .	230
Example 4.21: PERT Assumptions and Calculations . . . . .	238
Example 4.22: Scheduling Course - Teacher Combinations . . . . .	241
Example 4.23: Multiproject Scheduling . . . . .	245
Example 4.24: Resource-Driven Durations and Resource Calendars . . . . .	255
Example 4.25: Resource-Driven Durations and Alternate Resources . . . . .	267
Example 4.26: Multiple Alternate Resources . . . . .	273
Example 4.27: Auxiliary Resources and Alternate Resources . . . . .	275
Example 4.28: Use of the SETFINISHMILESTONE Option . . . . .	278
Example 4.29: Negative Resource Requirements . . . . .	286
Example 4.30: Auxiliary Resources and Negative Requirements . . . . .	289
Example 4.31: Resource-Driven Durations and Negative Requirements . . . . .	293
Statement and Option Cross-Reference Tables . . . . .	298
References . . . . .	<b>300</b>

---

---

## Overview: CPM Procedure

The CPM procedure can be used for planning, controlling, and monitoring a project. A typical project consists of several activities that may have precedence and time constraints. Some of these activities may already be in progress; some of them may follow different work schedules. All of the activities may compete for scarce resources. PROC CPM enables you to schedule activities subject to all of these constraints.

PROC CPM enables you to define calendars and specify holidays for the different activities so that you can schedule around holidays and vacation periods. Once a project has started, you can monitor it by specifying current information or progress data that is used by PROC CPM to compute an updated schedule. You can compare the new schedule with a baseline (or target) schedule.

For projects with scarce resources, you can determine resource-constrained schedules. PROC CPM enables you to select from a wide variety of options so that you can control the scheduling process. Thus, you may select to delay project completion time or use supplementary levels of resources, or alternate resources, if they are available.

All project information is contained in SAS data sets. The input data sets used by PROC CPM are as follows:

- The [Activity](#) data set contains all activity-related information such as activity name, precedence information, calendar used by the activity, progress information, baseline (or target schedule) information, resource requirements, time constraints, and any other information that you want to identify with each activity.
- The [Resource](#) data set specifies resource types, resource availabilities, resource priorities, and alternate resources.
- The [Workday](#) data set and the [Calendar](#) data set together enable you to specify any type of work pattern during a week and within each day of the week.
- The [Holiday](#) data set enables you to associate standard holidays and vacation periods with each calendar.

The output data sets are as follows:


- The [Schedule](#) data set contains the early, late, baseline, resource-constrained, and actual schedules and any other activity-related information that is calculated by PROC CPM.
- The [Resource Schedule](#) data set contains the schedules for each resource used by an activity.
- The [Usage](#) data set contains the resource usage for each of the resources used in the project.

See Chapter 5, “[The PM Procedure](#),” for an interactive procedure that enables you to use a Graphical User Interface to enter and edit project information.

## Getting Started: CPM Procedure

The basic steps necessary to schedule a project are illustrated using a simple example. Consider a software development project in which an applications developer has the software finished and ready for preliminary testing. In order to complete the project, several activities must take place. Certain activities cannot start until other activities have finished. For instance, the preliminary documentation must be written before it can be revised and edited and before the Quality Assurance department (QA) can test the software. Such constraints among the activities (namely, activity B can start after activity A has finished) are referred to as *precedence constraints*. Given the precedence constraints and estimated durations of the activities, you can use the *critical path method* to determine the shortest completion time for the project.

**Figure 4.1** Activity-On-Arc Network

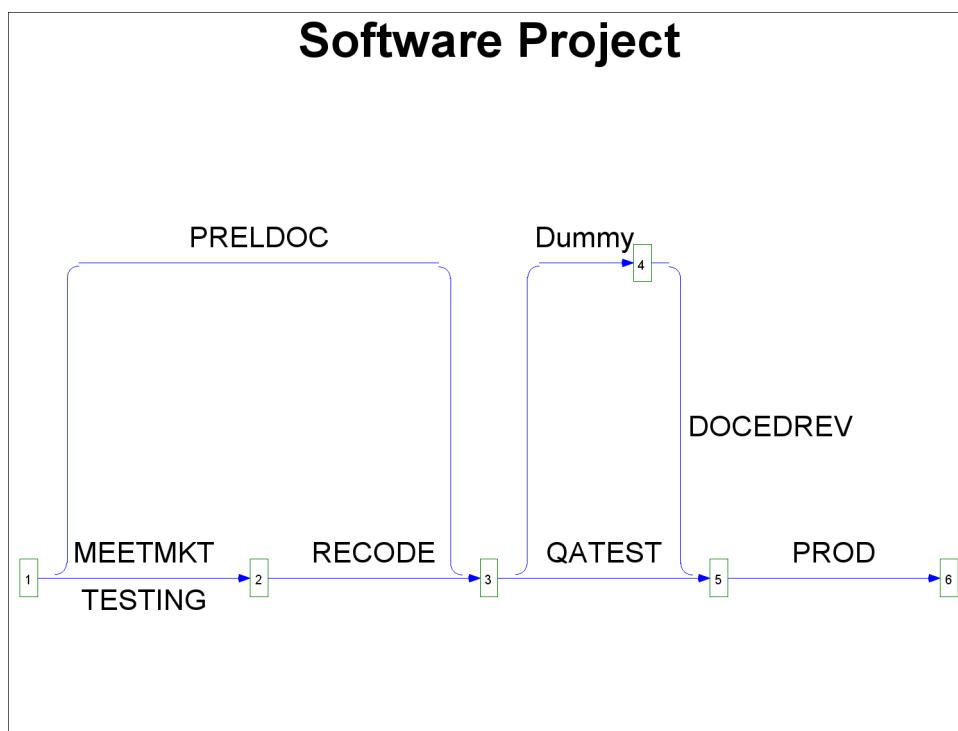

The first step in determining project completion time is to capture the relationships between the activities in a convenient representation. This is done by using a network diagram. Two types of network diagrams are popular for representing a project.

- Activity-On-Arc (AOA) or Activity-On-Edge (AOE) diagrams show the activities on the arcs or edges of the network. Figure 4.1 shows the AOA representation for the software project. This method of representing a project is known also as the arrow diagramming method (ADM). For projects represented in the AOA format, PROC CPM requires the use of the following statements:


```

PROC CPM options ;
  TAILNODE variable ;
  HEADNODE variable ;
  DURATION variable ;
  
```

- Activity-On-Node (AON) or Activity-On-Vertex (AOV) diagrams show the activities on nodes or vertices of the network. Figure 4.2 shows the AON representation of the project. This method is known also as the *precedence diagramming method* (PDM). The AON representation is more flexible because it enables you to specify nonstandard precedence relationships between the activities (for example, you can specify that activity B starts five days after the start of activity A). PROC CPM requires the use of the following statements to schedule projects that are represented using the AON format:

```
PROC CPM options ;
ACTIVITY variable ;
SUCCESSOR variables ;
DURATION variable ;
```

**Figure 4.2** Activity-On-Node Network

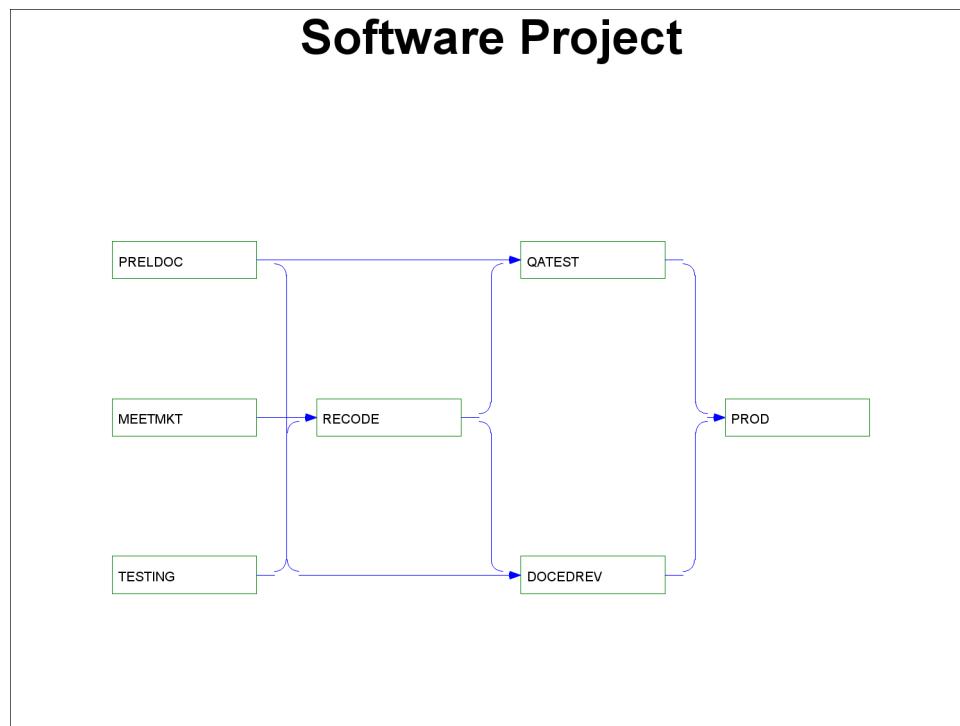

The AON representation of the network is used in the remainder of this section to illustrate some of the features of PROC CPM. The project data are input to PROC CPM using a SAS data set. The basic project information is conveyed to PROC CPM through the **ACTIVITY**, **SUCCESSOR**, and **DURATION** statements. Each observation of the Activity data set specifies an activity in the project, its duration, and its immediate successors. PROC CPM enables you to specify all of the immediate successors in the same observation, or you can have multiple observations for each activity, listing each successor in a separate observation. (Multiple variables in the **SUCCESSOR** statement are used here.) PROC CPM enables you to use long activity names. In this example, shorter names are used for the activities to facilitate data entry; a variable, Descrpt, is used to specify a longer description for each activity.

The procedure determines items such as the following:

- the minimum time in which the project can be completed
- the set of activities that is critical to the completion of the project in the minimum amount of time

No displayed output is produced. However, the results are saved in an output data set (the Schedule data set) that is shown in [Figure 4.3](#).

The code for the entire program is as follows.

```

data software;
  format Descript $20. Activity $8.
    Succesr1-Succesr2 $8. ;
  input Descript & Duration Activity $
    Succesr1 $ Succesr2 $ ;
  datalines;
Initial Testing      20  TESTING   RECODE     .
Prel. Documentation 15  PRELDOC  DOCEDREV  QATEST
Meet Marketing       1   MEETMKT  RECODE     .
Recoding             5   RECODE   DOCEDREV  QATEST
QA Test Approve     10  QATEST   PROD      .
Doc. Edit and Revise 10  DOCEDREV PROD      .
Production          1   PROD     .          .
;

proc cpm data=software
  out=introl
  interval=day
  date='01mar04'd;
  id descrpt;
  activity activity;
  duration duration;
  successor succesr1 succesr2;
run;

title 'Project Schedule';
proc print data=introl;
run;

```

**Figure 4.3** Software Project Plan**Project Schedule**

Obs	Activity		Succesr1	Succesr2	Duration	Descript
1	TESTING	RECODE		20	Initial Testing	
2	PRELDOC	DOCEDREV	QATEST	15	Prel. Documentation	
3	MEETMKT	RECODE		1	Meet Marketing	
4	RECODE	DOCEDREV	QATEST	5	Recoding	
5	QATEST	PROD		10	QA Test Approve	
6	DOCEDREV	PROD		10	Doc. Edit and Revise	
7	PROD			1	Production	

Obs	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
1	01MAR04	20MAR04	01MAR04	20MAR04	0	0
2	01MAR04	15MAR04	11MAR04	25MAR04	10	10
3	01MAR04	01MAR04	20MAR04	20MAR04	19	19
4	21MAR04	25MAR04	21MAR04	25MAR04	0	0
5	26MAR04	04APR04	26MAR04	04APR04	0	0
6	26MAR04	04APR04	26MAR04	04APR04	0	0
7	05APR04	05APR04	05APR04	05APR04	0	0

In addition to the variables specified in the ACTIVITY, SUCCESSOR, DURATION, and ID statements, the output data set contains the following new variables.

**E\_START**

specifies the earliest time an activity can begin, subject to any time constraints and the completion time of the preceding activity.

**E\_FINISH**

specifies the earliest time an activity can be finished, assuming it starts at E\_START.

**L\_START**

specifies the latest time an activity can begin so that the project is not delayed.

**L\_FINISH**

specifies the latest time an activity can be finished without delaying the project.

**T\_FLOAT**

specifies the amount of flexibility in the starting of a specific activity without delaying the project:

$$T\_FLOAT = L\_START - E\_START = L\_FINISH - E\_FINISH$$

**F\_FLOAT**

specifies the difference between the early finish time of the activity and the early start time of the activity's immediate successors.

In Figure 4.3 the majority of the tasks have a total float value of 0. These events are *critical*; that is, any delay in these activities will cause the project to be delayed. Some of the activities have slack present, which means that they can be delayed by that amount without affecting the project completion date. For example, the activity MEETMKT has a slack period of 19 days because there are 19 days between 01MAR04 and 20MAR04.

The INTERVAL= option in the PROC CPM statement enables you to specify the durations of the activities in one of several possible units including days, weeks, months, hours, and minutes. In addition, you can schedule activities around weekends and holidays. (To skip weekends, you specify INTERVAL=WEEKDAY.) You can also select different patterns of work during a day or a week (for example, holidays on Friday and Saturday) and different sets of holidays for the different activities in the project. A *calendar* consists of a set of work schedules for a typical week and a set of holidays. PROC CPM enables you to define any number of calendars and associate different activities with different calendars.

In the previous example, you saw that you could schedule your project by selecting a project start date. You can also specify a project finish date if you have a deadline to be met and you need to determine the latest start times for the different activities in the project. You can also set constraints on start or finish dates for specific activities within a given project. For example, testing the software may have to be delayed until the testing group finishes another project that has a higher priority. PROC CPM can schedule the project subject to such restrictions through the use of the **ALIGNDATE** and **ALIGNTYPE** statements. See Example 4.12 for more information about the use of the **ALIGNDATE** and **ALIGNTYPE** statements.

For a project that is already in progress, you can incorporate the *actual* schedule of the activities (some activities may already be completed while others may still be in progress) to obtain a progress update. You can save the original schedule as a *baseline* schedule and use it to compare against the current schedule to determine if any of the activities have taken longer than anticipated.

Quite often the resources needed to perform the activities in a project are available only in limited quantities and may cause certain activities to be postponed due to unavailability of the required resources. You can use PROC CPM to schedule the activities in a project subject to resource constraints. A wide range of options enables you to control the scheduling process. For example, you can specify resource or activity priorities, set constraints on the maximum amount of delay that can be tolerated for a given activity, enable activities to be preempted, specify alternate resources that can be used instead of scarce resources, or indicate secondary levels of resources that can be used when the primary levels are insufficient.

When an activity requires multiple resources, it is possible that each resource may follow a different calendar and each may require varying amounts of work. PROC CPM enables you to define resource-driven durations for the activities. You can also specify calendars for the resources. In either of these situations it is possible that each resource used by an activity may have its own individual schedule. PROC CPM enables you to save the resource schedules for the different activities in a Resource Schedule data set, the RESOURCESCHED= data set.

In addition to obtaining a resource-constrained schedule in an output data set, you can save the resource utilization summary in another output data set, the RESOURCEOUT= data set. Several options enable you to control the amount of information saved in this data set.

The CPM procedure enables you to define activities in a multiproject environment with multiple levels of nesting. You can specify a PROJECT variable that identifies the name or number of the project to which each activity belongs.

All the options available with the CPM procedure are discussed in detail in the following sections. Several examples illustrate most of the features.

---

## Syntax: CPM Procedure

The following statements are used in PROC CPM:

```
PROC CPM options ;
  ACTIVITY variable ;
  ACTUAL / actual options ;
  ALIGNDATE variable ;
  ALIGNTYPE variable ;
  BASELINE / baseline options ;
  CALID variable ;
  DURATION / duration options ;
  HEADNODE variable ;
  HOLIDAY variable / holiday options ;
  ID variables ;
  PROJECT variable / project options ;
  RESOURCE variables / resource options ;
  SUCCESSOR variables / lag options ;
  TAILNODE variable ;
```

---

## Functional Summary

Table 4.1 outlines the options available for the CPM procedure, classified by function.

**Table 4.1** Functional Summary

Description	Statement	Option
<b>Activity Splitting Specifications</b>		
Splits in-progress activities at TIMENOW	ACTUAL	TIMENOWSPLT
Specifies the maximum number of segments variable	RESOURCE	MAXNSEGMENT=
Specifies the minimum segment duration variable	RESOURCE	MINSEGMDUR=
Enables splitting	RESOURCE	SPLITFLAG
<b>Baseline or Target Schedule Specifications</b>		
Specifies the baseline finish date variable	BASELINE	B_FINISH=
Specifies the baseline start date variable	BASELINE	B_START=
Specifies the schedule to compare with baseline	BASELINE	COMPARE=
Specifies the schedule to use as baseline	BASELINE	SET=
Specifies the schedule to update baseline	BASELINE	UPDATE=
<b>Calendar Specifications</b>		
Specifies the calendar variable	CALID	
Specifies the holiday variable	HOLIDAY	
Specifies the holiday duration variable	HOLIDAY	HOLIDUR=
Specifies the holiday finish variable	HOLIDAY	HOLIFIN=

**Table 4.1** *continued*

Description	Statement	Option
<b>Data Set Specifications</b>		
Specifies the Calendar input data set	PROC CPM	CALEDATA=
Specifies the Activity input data set	PROC CPM	DATA=
Specifies the Holiday input data set	PROC CPM	HOLIDATA=
Specifies the Schedule Output data set	PROC CPM	OUT=
Specifies the Resource Availability input data set	PROC CPM	RESOURCEIN=
Specifies the Resource Schedule output data set	PROC CPM	RESOURCESCHED=
Specifies the Resource Usage output data set	PROC CPM	RESOURCEOUT=
Specifies the Workday input data set	PROC CPM	WORKDATA=
<b>Duration Control Specifications</b>		
Specifies the workday length	PROC CPM	DAYLENGTH=
Specifies the workday start	PROC CPM	DAYSTART=
Specifies the duration unit	PROC CPM	INTERVAL=
Specifies the duration multiplier	PROC CPM	INTPER=
Converts milestones into finish milestones	PROC CPM	SETFINISHMILESTONE
Specifies the duration variable	DURATION	
Specifies the finish variable	DURATION	FINISH=
Overrides specified duration	DURATION	OVERRIDEDUR
Specifies the start variable	DURATION	START=
Specifies the work variable	RESOURCE	WORK=
<b>Lag Specifications</b>		
Specifies the name of the lag duration calendar	SUCCESSOR	ALAGCAL=
Specifies the lag variables	SUCCESSOR	LAG=
Specifies the number of the lag duration calendar	SUCCESSOR	NLAGCAL=
<b>Miscellaneous Options</b>		
Suppresses warning messages	PROC CPM	SUPPRESSOBSWARN
Fixes L_FINISH for finish tasks to E_FINISH	PROC CPM	FIXFINISH
<b>Network Specifications</b>		
Specifies the AON format activity variable	ACTIVITY	
Specifies the AOA format headnode variable	HEADNODE	
Specifies the project variable	PROJECT	
Specifies the AON format successor variables	SUCCESSOR	
Specifies the AOA format tailnode variable	TAILNODE	
<b>Multiproject Specifications</b>		
Specifies the project variable	PROJECT	
Aggregates parent resources	PROJECT	AGGREGATEPARENTRES
Ignores parent resources	PROJECT	IGNOREPARENTRES
Computes separate critical paths	PROJECT	SEPCRIT
Uses specified project duration	PROJECT	USEPROJDUR

**Table 4.1** *continued*

Description	Statement	Option
Computes WBS Code	PROJECT	WBSCODE
<b>OUT= Data Set Options</b>		
Includes percent complete variable	ACTUAL	ESTIMATEPCTC
Adds an observation for missing activities	PROC CPM	ADDACT
Specifies single observation per activity	PROC CPM	COLLAPSE
Copies relevant variables to Schedule data set	PROC CPM	XFERVARS
Specifies the variables to be copied to Schedule data set	ID	
Includes descending sort variables	PROJECT	DESCENDING
Includes all sort order variables	PROJECT	ORDERALL
Includes early start sort order variable	PROJECT	ESORDER
Includes late start sort order variable	PROJECT	LSORDER
Includes resource start order variable	PROJECT	SSORDER
Includes WBS Code	PROJECT	WBSCODE
Includes information about resource delays	RESOURCE	DELAYANALYSIS
Includes early start schedule	RESOURCE	E_START
Includes free float	RESOURCE	F_FLOAT
Sets unscheduled S_START and S_FINISH	RESOURCE	FILLUNSCHED
Includes late start schedule	RESOURCE	L_START
Excludes early start schedule	RESOURCE	NOE_START
Excludes free float	RESOURCE	NOF_FLOAT
Excludes late start schedule	RESOURCE	NOL_START
Excludes resource variables	RESOURCE	NORESOURCEVARS
Excludes total float	RESOURCE	NOT_FLOAT
Includes resource variables	RESOURCE	RESOURCEVARS
Includes total float	RESOURCE	T_FLOAT
Sets unscheduled S_START and S_FINISH to missing	RESOURCE	UNSCHEDMISS
Updates unscheduled S_START, S_FINISH	RESOURCE	UPDTUNSCHED
<b>Problem Size Options</b>		
Specifies the number of precedence constraints	PROC CPM	NADJ=
Specifies the number of activities	PROC CPM	NACTS=
Specifies the number of distinct node or activity names	PROC CPM	NNODES=
Specifies the number of resource requirements	PROC CPM	NRESREQ=
Disables use of the Utility data set	PROC CPM	NOUTIL
<b>Progress Updating Options</b>		
Specifies the actual finish variable	ACTUAL	A_FINISH=
Specifies the actual start variable	ACTUAL	A_START=
Assumes automatic completion	ACTUAL	AUTOUPDT
Enables actual time to fall in a non-work period	ACTUAL	FIXASTART
Does not assume automatic completion	ACTUAL	NOAUTOUPDT
Specifies the percentage complete variable	ACTUAL	PCTCOMP=
Specifies the remaining duration variable	ACTUAL	REMENDUR=

**Table 4.1** *continued*

Description	Statement	Option
Specifies that progress updating should override resource scheduling (Experimental)	RESOURCE	SETFINISH=
Shows float for all activities	ACTUAL	SHOWFLOAT
Specifies the current date	ACTUAL	TIMENOW=
<b>Resource Variable Specifications</b>		
Specifies the resource variables	RESOURCE	
Specifies the observation type variable	RESOURCE	OBSTYPE=
Specifies the resource availability date/time variable	RESOURCE	PERIOD=
Specifies the alternate resource variable	RESOURCE	RESID=
Specifies the work variable	RESOURCE	WORK=
<b>Resource Allocation Control Options</b>		
Specifies the delay variable	RESOURCE	ACTDELAY=
Specifies the activity priority variable	RESOURCE	ACTIVITYPRTY=
Uses alternate resources before supplementary levels	RESOURCE	ALTBESTRESUP
Waits until L_START + DELAY	RESOURCE	AWAITDELAY
Specifies the delay	RESOURCE	DELAY=
Schedules even if there are insufficient resources	RESOURCE	INFEASDIAGNOSTIC
Specifies independent allocation	RESOURCE	INDEPENDENTALLOC
Enables milestones to consume resources	RESOURCE	MILESTONERESOURCE
Prevents milestones from consuming resources	RESOURCE	MILESTONENORESOURCE
Uses multiple alternates for a single resource	RESOURCE	MULTIPLEALTERNATES
Specifies the resource calendar intersect	RESOURCE	RESCALINTERSECT
Specifies the scheduling priority rule	RESOURCE	SCHEDRULE=
Specifies the secondary scheduling priority rule	RESOURCE	SCHEDRULE2=
Specifies the stop date for resource constrained scheduling	RESOURCE	STOPDATE=
<b>RESOURCEOUT= Data Set Options</b>		
Includes all types of resource usage	RESOURCE	ALL
Appends observations for total usage	RESOURCE	APPEND
Specifies the name of the calendar for _TIME_ increment	RESOURCE	AROUTCAL=
Includes availability profile for each resource	RESOURCE	AVPROFILE
Specifies the cumulative usage for consumable resources	RESOURCE	CUMUSAGE
Includes early start profile for each resource	RESOURCE	ESPROFILE
Excludes unscheduled activities in profile	RESOURCE	EXCLUNSCHED
Includes unscheduled activities in profile	RESOURCE	INCLUNSCHED
Records total usage of resource	RESOURCE	TOTUSAGE
Includes late start profile for each resource	RESOURCE	LSPROFILE
Specifies the maximum value of _TIME_	RESOURCE	MAXDATE=
Specifies the maximum number of observations	RESOURCE	MAXOBS=
Specifies the minimum value of _TIME_	RESOURCE	MINDATE=
Specifies the numeric calendar for _TIME_	RESOURCE	NROUTCAL=

**Table 4.1** *continued*

Description	Statement	Option
Includes resource constrained profile	RESOURCE	RCPROFILE
Specifies the unit of difference between consecutive _TIME_ values	RESOURCE	ROUTINTERVAL=
Specifies the difference between consecutive _TIME_ values	RESOURCE	ROUTINTPER=
Uses a continuous calendar for _TIME_	RESOURCE	ROUTNOBREAK
<b>RESOURCESCHED= Data Set Options</b>		
Adds activity or resource calendar	RESOURCE	ADDCAL
Includes WBS code	PROJECT	RSCHEWDWS
Includes order variables	PROJECT	RSCHEDORDER
Specifies the ID variables	RESOURCE	RSCHEID=
<b>Time Constraint Specifications</b>		
Specifies the alignment date variable	ALIGNDATE	
Specifies the alignment type variable	ALIGNTYPE	
Specifies the project start date	PROC CPM	DATE=
Specifies the project finish date	PROC CPM	FBDATE=
Finishes before DATE= value	PROC CPM	FINISHBEFORE

---

## PROC CPM Statement

**PROC CPM** *options* ;

The following options can appear in the PROC CPM statement.

### **ADDACT**

### **ADDALLACT**

### **EXPAND**

indicates that an observation is to be added to the Schedule output data set (and the Resource Schedule output data set) for each activity that appears as a value of the variables specified in the SUCCESSOR or PROJECT statements without appearing as a value of the variable specified in the ACTIVITY statement. If the PROJECT statement is used, and the activities do not have a single common parent, an observation is also added to the Schedule data set containing information for a single common parent defined by the procedure.

### **CALEDATA=SAS-data-set**

### **CALENDAR=SAS-data-set**

identifies a SAS data set that specifies the work pattern during a standard week for each of the calendars that are to be used in the project. Each observation of this data set (also referred to as the **Calendar** data set) contains the name or the number of the calendar being defined in that observation, the names of the shifts or work patterns used each day, and, optionally, a standard workday length in hours. For

details about the structure of this data set, see the section “[Multiple Calendars](#)” on page 101. The work shifts referred to in the Calendar data set are defined in the Workday data set. The calendars defined in the Calendar data set can be identified with different activities in the project.

### **COLLAPSE**

creates only one observation per activity in the output data set when the input data set for a network in AON format contains multiple observations for the same activity. This option is allowed only if the network is in AON format.

Often, the input data set may have more than one observation per activity (especially if the activity has several successors). If you are interested only in the schedule information about the activity, there is no need for multiple observations in the output data set for this activity. Use the COLLAPSE option in this case.

### **DATA=SAS-data-set**

names the SAS data set that contains the network specification and activity information. If the DATA= option is omitted, the most recently created SAS data set is used. This data set (also referred to in this chapter as the **Activity** data set) contains all of the information that is associated with each activity in the network.

### **DATE=date**

specifies the SAS date, time, or datetime that is to be used as an alignment date for the project. If neither the FINISHBEFORE option nor any other alignment options are specified, then the CPM procedure schedules the project to start on *date*. If *date* is a SAS time value, the value of the INTERVAL= parameter should be HOUR, MINUTE, or SECOND; if it is a SAS date value, *interval* should be DAY, WEEKDAY, WORKDAY, WEEK, MONTH, QTR, or YEAR; and if it is a SAS datetime value, *interval* should be DTWRKDAY, DTDAY, DTHOUR, DTMINUTE, DTSECOND, DTWEEK, DTMONT, DTQTR, or DTYEAR.

### **DAYLENGTH=daylength**

specifies the length of the workday. On each day, work is scheduled starting at the beginning of the day as specified in the DAYSTART= option and ending *daylength* hours later. The DAYLENGTH= value should be a SAS time value. The default value of *daylength* is 24 if the INTERVAL= option is specified as DTDAY, DTHOUR, DTMINUTE, or DTSECOND, and the default value of *daylength* is 8 if the INTERVAL= option is specified as WORKDAY or DTWRKDAY. If INTERVAL=DAY or WEEKDAY and the value of *daylength* is less than 24, then the schedule produced is in SAS datetime values. For other values of the INTERVAL= option, the DAYLENGTH= option is ignored.

### **DAYSTART=daystart**

specifies the start of the workday. The DAYSTART= value should be a SAS time value. This parameter should be specified only when *interval* is one of the following: DTDAY, WORKDAY, DTWRKDAY, DTHOUR, DTMINUTE, or DTSECOND; in other words, this parameter should be specified only if the schedule produced by the CPM procedure is in SAS datetime values. The default value of *daystart* is 9 a.m. if INTERVAL is WORKDAY; otherwise, the value of *daystart* is equal to the time part of the SAS datetime value specified for the DATE= option.

### **FBDATE=fbdate**

specifies a finish-before date that can be specified in addition to the DATE= option. If the FBDATE= option is not given but the FINISHBEFORE option is specified, then *fbdate* = *date*. Otherwise, *fbdate* is equal to the project completion date. If *fbdate* is given in addition to the DATE= and FINISHBEFORE

options, then the minimum of the two dates is used as the required project completion date. See the section “[Scheduling Subject to Precedence Constraints](#)” on page 93 for details about how the procedure uses the *date* and *fbdate* to compute the early and late start schedules.

#### **FINISHBEFORE**

specifies that the project be scheduled to complete before the date given in the DATE= option.

#### **FIXFINISH**

specifies that all **finish** tasks are to be constrained by their respective early finish times. In other words, the late finish times of all finish tasks do not float to the project completion time.

#### **HOLIDATA=SAS-data-set**

#### **HOLIDAY=SAS-data-set**

identifies a SAS data set that specifies holidays. These holidays can be associated with specific calendars that are also identified in the HOLIDATA= data set (also referred to as the **Holiday** data set). The HOLIDATA= option must be used with a **HOLIDAY** statement that specifies the variable in the SAS data set that contains the start time of holidays. Optionally, the data set can include a variable that specifies the length of each holiday or a variable that identifies the finish time of each holiday (if the holidays are longer than one day). For projects involving multiple calendars, this data set can also include the variable specified by the **CALID** statement that identifies the calendar to be associated with each holiday. See the section “[Multiple Calendars](#)” on page 101 for further information regarding holidays and multiple calendars.

#### **INTERVAL=interval**

requests that each unit of duration be measured in *interval* units. Possible values for *interval* are DAY, WEEK, WEEKDAY, WORKDAY, MONTH, QTR, YEAR, HOUR, MINUTE, SECOND, DTDAY, DTWRKDAY, DTWEEK, DTMONT, DTQTR, DTYEAR, DTHOUR, DTMINUTE, and DTSECOND. The default value is based on the format of the DATE= parameter. See the section “[Using the INTERVAL= Option](#)” on page 94 for further information regarding this option.

#### **INTPER=period**

requests that each unit of duration be equivalent to *period* units of duration. The default value is 1.

#### **NACTS=nacts**

specifies the number of activities for which memory is allocated in core by the procedure. If the number of activities exceeds *nacts*, the procedure uses a utility data set for storing the activity array. The default value for *nacts* is set to *nobs*, if the network is specified in AOA format, and to *nobs*×(*nsucc*+1), if the network is specified in AON format, where *nobs* is the number of observations in the Activity data set and *nsucc* is the number of variables specified in the SUCCESSOR statement.

#### **NADJ=nadj**

specifies the number of precedence constraints (adjacencies) in the project network. If the number of adjacencies exceeds *nadj*, the procedure uses a utility data set for storing the adjacency array. The default value of *nadj* is set to *nacts* if the network is in AON format, and it is set to *nacts*×2 if the network is in AOA format.

#### **NNODES=nnodes**

specifies the size of the symbolic table used to look up the activity names (node names) for the network specification in AON (AOA) format. If the number of distinct names exceeds *nnodes*, the procedure uses a utility data set for storing the tree used for the table lookup. The default value for *nnodes* is

set to  $nobs \times 2$  if the network is specified in AOA format and to  $nobs \times (nsucc + 1)$  if the network is specified in AON format, where  $nobs$  is the number of observations in the Activity data set and  $nsucc$  is the number of variables specified in the SUCCESSOR statement.

#### **NOUTIL**

specifies that the procedure should not use utility data sets for memory management. By default, the procedure resorts to the use of utility data sets and swaps between core memory and utility data sets as necessary if the number of activities or precedence constraints or resource requirements in the input data sets is larger than the number of each such entity for which memory is initially allocated in core. Specifying this option causes the procedure to increase the memory allocation instead of using a utility data set; if the problem is too large to fit in core memory, PROC CPM will stop with an error message.

#### **NRESREQ=nres**

specifies the number of distinct resource requirements corresponding to all activities and resources in the project. The default value of  $nres$  is set to  $nobs \times nresvar \times 0.25$ , where  $nobs$  is the number of observations in the Activity data set, and  $nresvar$  is the number of RESOURCE variables in the Activity data set.

#### **OUT=SAS-data-set**

specifies a name for the output data set that contains the schedule determined by PROC CPM. This data set (also referred to as the **Schedule** data set) contains all of the variables that were specified in the Activity data set to define the project. Every observation in the Activity data set has a corresponding observation in this output data set. If PROC CPM is used to determine a schedule that is not subject to any resource constraints, then this output data set contains the early and late start schedules; otherwise, it also contains the resource-constrained schedule. See the section “[OUT= Schedule Data Set](#)” on page 99 for information about the names of the new variables in the data set. If the OUT= option is omitted, the SAS system creates a data set and names it according to the DATA*n* naming convention.

#### **RESOURCEIN=SAS-data-set**

#### **RESIN=SAS-data-set**

#### **RIN=SAS-data-set**

#### **RESLEVEL=SAS-data-set**

names the SAS data set that contains the levels available for the different resources used by the activities in the project. This data set also contains information about the type of resource (replenishable or consumable), the calendar associated with each resource, the priority for each resource, and lists, for each resource, all the alternate resources that can be used as a substitute. In addition, this data set indicates whether or not the resource rate affects the duration. The specification of the RESIN= data set (also referred to as the **Resource** data set) indicates to PROC CPM that the schedule of the project is to be determined subject to resource constraints. For further information about the format of this data set, see the section “[RESOURCEIN= Input Data Set](#)” on page 114.

If this option is specified, you must also use the RESOURCE statement to identify the variable names for the resources to be used for resource-constrained scheduling. In addition, you must specify the name of the variable in this data set (using the PERIOD= option in the RESOURCE statement) that contains the dates from which the resource availabilities in each observation are valid. Furthermore, the data set must be sorted in order of increasing values of this period variable.

**RESOURCEOUT=SAS-data-set****RESOUT=SAS-data-set****ROUT=SAS-data-set****RESUSAGE=SAS-data-set**

names the SAS data set in which you can save resource usage profiles for each of the resources specified in the **RESOURCE** statement. This data set is also referred to as the **Usage** data set. In the Usage data set, you can save the resource usage by time period for the early start, late start, and resource-constrained schedules, and the surplus level of resources remaining after resource allocation is performed.

By default, it provides the usage profiles for the early and late start schedules if resource allocation is not performed. If resource allocation is performed, this data set also provides usage profiles for the resource-constrained schedule and a profile of the level of remaining resources.

You can control the types of profiles to be saved by using the ESPROFILE (early start usage), LSPROFILE (late start usage), RCPROFILE (resource-constrained usage), or AVPROFILE (resource availability after resource allocation) options in the **RESOURCE** statement. You can specify any combination of these four options. You can also specify the ALL option to indicate that all four options (ESPROFILE, LSPROFILE, RCPROFILE, AVPROFILE) are to be in effect. For details about variable names and the interpretation of the values in this data set, see the section “[“RESOURCEOUT= Usage Data Set” on page 127](#)” on page 127.

**RESOURCESCHED=SAS-data-set****RESSCHED=SAS-data-set****RSCHEDULE=SAS-data-set****RSCHED=SAS-data-set**

names the SAS data set in which you can save the schedules for each resource used by any activity. This option is valid whenever the **RESOURCE** statement is used to specify any resource requirements. The resulting data set is especially useful when resource-driven durations or resource calendars cause the resources used by an activity to have different schedules.

### **SETFINISHMILESTONE**

specifies that milestones (zero duration activities) should have the same start and finish times as the finish time of their predecessor. In other words, this option enables milestones that mark the *end* of the preceding activity to coincide with its finish time. By default, if a milestone M is a successor to an activity that finishes at the end of the day (say 15Mar2004), the start and finish times for the milestone are specified as the beginning of the next day (16Mar2004). This corresponds to the definition of start times in the CPM procedure: *all* start times indicate the *beginning* of the date specified. For zero duration activities, the finish time is defined to be the same as the start time. The **SETFINISHMILESTONE** option specifies that the start and finish times for the milestone M should be specified as 15Mar2004, with the interpretation that the milestone’s schedule corresponds to the *end* of the day. There may be exceptions to this definition if there are special alignment constraints on the milestone. For details, see the section “[“Finish Milestones” on page 98](#)” on page 98.

**SUPPRESSOBSWARN**

turns off the display of warnings and notes for every observation with invalid or missing specifications.

**WORKDATA=SAS-data-set****WORKDAY=SAS-data-set**

identifies a SAS data set that defines the work pattern during a standard working day. Each numeric variable in this data set (also referred to as the **Workday** data set) is assumed to denote a unique shift pattern during one working day. The variables must be formatted as SAS time values and the observations are assumed to specify, alternately, the times when consecutive shifts start and end. See the section “[Multiple Calendars](#)” on page 101 for a description of this data set.

**XFERVARS**

indicates that all relevant variables are to be copied from the Activity data set to the Schedule data set. This includes all variables used in the **ACTUAL** statement, the **ALIGNDATE** and **ALIGNTYPE** statements, the **SUCCESSOR** statement, and the **RESOURCE** statement.

## **ACTIVITY Statement**

**ACTIVITY** *variable* ;

**ACT** *variable* ;

The ACTIVITY statement is required when data are input in an AON format; this statement identifies the variable that contains the names of the nodes in the network. The activity associated with each node has a duration equal to the value of the DURATION variable. The ACTIVITY variable can be character or numeric because it is treated symbolically. Each node in the network must be uniquely defined.

The ACTIVITY statement is also supported in the Activity-on-Arc format. The ACTIVITY variable is used to uniquely identify the activity specified between two nodes of the network. In the AOA format, if the ACTIVITY statement is not specified, each observation in the Activity data set is treated as a new activity.

## **ACTUAL Statement**

**ACTUAL** / *actual options* ;

The ACTUAL statement identifies variables in the Activity data set that contain progress information about the activities in the project. For a project that is already in progress, you can describe the actual status of any activity by specifying the activity’s actual start, actual finish, remaining duration, or percent of work completed. At least one of the four variables (A\_START, A\_FINISH, REMDUR, PCTCOMP) needs to be specified in the ACTUAL statement. These variables are referred to as *progress variables*. The TIMENOW= option in this statement represents the value of the current time (referred to as TIMENOW), and it is used in conjunction with the values of the progress variables to check for consistency and to determine default values if necessary.

You can also specify options in the ACTUAL statement that control the updating of the project schedule. Using the ACTUAL statement causes four new variables (A\_START, A\_FINISH, A\_DUR, and STATUS) to be added to the Schedule data set; these variables are defined in the section “[OUT= Schedule Data Set](#)” on page 99. See the section “[Progress Updating](#)” on page 109 for more information.

The following options can be specified in the ACTUAL statement after a slash (/).

**A\_FINISH=variable**

**AF=variable**

identifies a variable in the Activity data set that specifies the actual finish times of activities that are already completed. The actual finish time of an activity must be less than TIMENOW.

**A\_START=variable**

**AS=variable**

identifies a variable in the Activity data set that specifies the actual start times of activities that are in progress or that are already completed. The actual start time of an activity must be less than TIMENOW.

**AUTOUPDT**

requests that PROC CPM should assume automatic completion (or start) of activities that are predecessors to activities already completed (or in progress). For example, if activity B is a successor of activity A, and B has an actual start time (or actual finish time or both) specified, while A has missing values for both actual start and actual finish times, then the AUTOUPDT option causes PROC CPM to assume that A must have already finished. PROC CPM then assigns activity A an actual start time and an actual finish time consistent with the precedence constraints. The AUTOUPDT option is the default.

**ESTIMATEPCTC**

**ESTPCTC**

**ESTPCTCOMP**

**ESTPROG**

indicates that a variable named PCT\_COMP is to be added to the Schedule output data set (and the Resource Schedule output data set) that contains the percent completion time for each activity (for each resource used by each activity) in the project. This value is 0 for activities that have not yet started and 100 for completed activities; for activities in progress, this value is computed using the actual start time, the value of TIMENOW, and the revised duration of the activity.

**FIXASTART**

specifies that the actual start time of an activity should not be overwritten if it is specified to be on a non-work day. By default, none of the start or finish times of an activity can occur during a non-work period corresponding to the activity's calendar. If the actual start time is specified on a non-work day, it is moved to the nearest work day. The FIXASTART option specifies that the actual start and finish times be left unchanged even if they coincide with a non-working time. Thus, if the actual start time is specified to be sometime on Sunday, it is left unchanged even if Sunday is a non-working day in the activity's calendar.

**NOAUTOUPDT**

requests that PROC CPM should not assume automatic completion of activities. (The NOAUTOUPDT option is the reverse of the AUTOUPDT option.) In other words, only those activities that have nonmissing actual start or nonmissing actual finish times or both (either specified as values for the A\_START and A\_FINISH variables or computed on the basis of the REMDUR or PCTCOMP variables and TIMENOW) are assumed to have started; all other activities have an implicit start time that is greater than or equal to TIMENOW. This option requires you to enter the progress information for all the activities that have started or are complete; an activity is assumed to be *pending* until one of the progress variables indicates that it has started.

**PCTCOMP=variable****PCTCOMPLETE=variable****PCOMP=variable**

identifies a variable in the Activity data set that specifies the percentage of the work that has been completed for the current activity. The values for this variable must be between 0 and 100. A value of 0 for this variable means that the current activity has not yet started. A value of 100 means that the activity is already complete. Once again, the value of the TIMENOW= option is used as a reference point to resolve the values specified for the PCTCOMP variable. See the section “[Progress Updating](#)” on page 109 for more information.

**REMDUR=variable****RDURATION=variable****RDUR=variable**

identifies a variable in the Activity data set that specifies the remaining duration of activities that are in progress. The values of this variable must be nonnegative: a value of 0 for this variable means that the activity in that observation is completed, while a value greater than 0 means that the activity is not yet complete (the remaining duration is used to revise the estimate of the original duration). The value of the TIMENOW parameter is used to determine an actual start time or an actual finish time or both for activities based on the value of the remaining duration. See the section “[Progress Updating](#)” on page 109 for further information.

**SHOWFLOAT**

This option in the [ACTUAL](#) statement indicates that PROC CPM should allow activities that are completed or in progress to have nonzero float. By default, all activities that are completed or in progress have the late start schedule set to be equal to the early start schedule and thus have both total float and free float equal to 0. If the SHOWFLOAT option is specified, the late start schedule is computed for in-progress and completed activities using the precedence and time constraints during the backward pass.

**TIMENOW=timenow****CURRDATE=timenow**

specifies the SAS date, time, or datetime value that is used as a reference point to resolve the values of the remaining duration and percent completion times when the [ACTUAL](#) statement is used. It can be thought of as the instant at the *beginning of the specified date*, when a *snapshot* of the project is taken; the actual start times or finish times or both are specified for all activities that have started or have been completed by the *end of the previous day*. If an ACTUAL statement is used without specification of the TIMENOW= option, the default value is set to be the time period following the maximum of all the actual start and finish times that have been specified; if there are no actual start or finish times, then TIMENOW is set to be equal to the current date. See the section “[Progress Updating](#)” on page 109 for further information regarding the TIMENOW= option and the [ACTUAL](#) statement.

**TIMENOWSPLT**

indicates that activities that are in progress at TIMENOW can be split at TIMENOW if they cause resource infeasibilities. During resource allocation, any activities with values of E\_START less than TIMENOW are scheduled even if there are not enough resources (a warning message is printed to the log if this is the case). This is true even for activities that are in progress. The TIMENOWSPLT option permits an activity to be split into two segments at TIMENOW, allowing the second segment of the activity to be scheduled later when resource levels permit. See the section “[Activity Splitting](#)” on

page 122 for information regarding activity segments. Activities with an alignment type of MS or MF are not allowed to be split; also, activities without resource requirements will not be split.

## ALIGNDATE Statement

**ALIGNDATE** *variable* ;

**DATE** *variable* ;

**ADATE** *variable* ;

The ALIGNDATE statement identifies the variable in the Activity data set that specifies the dates to be used to constrain each activity to start or finish on a particular date. The ALIGNDATE statement is used in conjunction with the ALIGNTYPE statement, which specifies the type of alignment. A missing value for the variables specified in the ALIGNDATE statement indicates that the particular activity has no restriction imposed on it.

PROC CPM requires that if the ALIGNDATE statement is used, then all start activities (activities with no predecessors) have nonmissing values for the ALIGNDATE variable. If any start activity has a missing ALIGNDATE value, it is assumed to start on the date specified in the PROC CPM statement (if such a date is given) or, if no date is given, on the earliest specified start date of all start activities. If none of the start activities has a start date specified and a project start date is not specified in the PROC CPM statement, the procedure stops execution and returns an error message. See the section “[Time-Constrained Scheduling](#)” on page 96 for information about how the variables specified in the ALIGNDATE and ALIGNTYPE statements affect the schedule of the project.

## ALIGNTYPE Statement

**ALIGNTYPE** *variable* ;

**ALIGN** *variable* ;

**ATYPE** *variable* ;

The ALIGNTYPE statement is used to specify whether the date value in the ALIGNDATE statement is the earliest start date, the latest finish date, and so forth, for the activity in the observation. The values allowed for the variable specified in the ALIGNTYPE statement are specified in [Table 4.2](#).

**Table 4.2** Valid Values for the ALIGNTYPE Variable

Value	Type of Alignment
SEQ	Start equal to
SGE	Start greater than or equal to
SLE	Start less than or equal to
FEQ	Finish equal to
FGE	Finish greater than or equal to
FLE	Finish less than or equal to
MS	Mandatory start equal to
MF	Mandatory finish equal to

If an **ALIGNDATE** statement is specified without an **ALIGNTYPE** statement, all of the activities are assumed to have an aligntype of SGE. If an activity has a nonmissing value for the **ALIGNDATE** variable and a missing value for the **ALIGNTYPE** variable, then the aligntype is assumed to be SGE. See the section “[Time-Constrained Scheduling](#)” on page 96 for information about how the **ALIGNDATE** and **ALIGNTYPE** variables affect project scheduling.

## **BASELINE Statement**

**BASELINE** / *options* ;

The **BASELINE** statement enables you to save a specific schedule as a *baseline* or *target* schedule and compare another schedule, such as an updated schedule or resource constrained schedule, against it. The schedule that is to be saved as a baseline can be specified either by explicitly identifying two numeric variables in the input data set as the **B\_START** and **B\_FINISH** variables, or by indicating the particular schedule (EARLY, LATE, ACTUAL, or RESOURCE constrained schedule) that is to be used to set the **B\_START** and **B\_FINISH** variables. The second method of setting the schedule is useful when you want to set the baseline schedule on the basis of the *current invocation* of PROC CPM.

Note that the **BASELINE** statement needs to be specified in order for the baseline start and finish times to be copied to the Schedule data set. Just including the **B\_START** and **B\_FINISH** variables in the Activity data set does not initiate baseline processing.

The following options can be specified in the **BASELINE** statement after a slash (/).

**B\_FINISH=variable**

**BF=variable**

specifies the numeric-valued variable in the Activity data set that sets **B\_FINISH**.

**B\_START=variable**

**BS=variable**

specifies the numeric-valued variable in the Activity data set that sets **B\_START**.

**COMPARE=schedule**

compares a specific schedule (EARLY, LATE, RESOURCE or ACTUAL) in the Activity data set with the baseline schedule. The **COMPARE** option is valid only if the input data set already has a **B\_START** and a **B\_FINISH** variable or if the **SET=** option is also specified. In other words, the **COMPARE** option is valid only if there is a baseline schedule to compare with. The comparison is specified in two variables in the Schedule data set, **S\_VAR** and **F\_VAR**, which have the following definition:

```
S_VAR = Compare Start - B_START;
F_VAR = Compare Finish - B_FINISH;
```

where **Compare Start** and **Compare Finish** refer to the start and finish times corresponding to the schedule that is used as a comparison.

The values of the variables **S\_VAR** and **F\_VAR** are calculated in units of the **INTERVAL=** parameter, taking into account the calendar defined for the activity.

**SET=schedule**

specifies which of the four schedules (EARLY, LATE, RESOURCE, or ACTUAL) to set the baseline schedule equal to. The SET= option causes the addition of two new variables in the Schedule data set; these are the B\_START and B\_FINISH variables. The procedure sets B\_START and B\_FINISH equal to the start and finish times corresponding to the EARLY, LATE, ACTUAL, or RESOURCE schedules. If the Activity data set already has a B\_START and B\_FINISH variable, it is overwritten by the SET= option and a warning is displayed. The value RESOURCE is valid only if resource-constrained scheduling is being performed, and the value ACTUAL is valid only if the [ACTUAL](#) statement is present.

**NOTE:** The values ACTUAL, RESOURCE, and so on cause the B\_START and B\_FINISH values to be set to the *computed* values of A\_START, S\_START, . . . , and so on. They cannot be used to set the B\_START and B\_FINISH values to be equal to, say, A\_START and A\_FINISH or S\_START and S\_FINISH, if these variables are present in the Activity data set; to do that you must use B\_START=A\_START, B\_FINISH=A\_FINISH, and so on.

**UPDATE=schedule**

specifies the name of the schedule (EARLY, LATE, ACTUAL, or RESOURCE) that can be used to *update* the B\_START and B\_FINISH variables. This sets B\_START and B\_FINISH on the basis of the specified schedules *only* when the values of the baseline variables are missing in the Activity data set. The UPDATE option is valid only if the Activity data set already has B\_START and B\_FINISH. Note that if both the UPDATE= and SET= options are specified, the SET= specification is used.

## CALID Statement

**CALID** *variable* ;

The CALID statement specifies the name of a SAS variable that is used in the Activity, Holiday, and Calendar data sets to identify the calendar to which each observation refers. This variable can be either numeric or character depending on whether the different calendars are identified by unique numbers or names. If this variable is not found in any of the three data sets, PROC CPM looks for a default variable named \_CAL\_ in each data set (a warning message is then printed to the log). In the Activity data set, this variable specifies the calendar used by the activity in the given observation. Each calendar in the project is defined using the Workday, Calendar, and Holiday data sets. Each observation of the Calendar data set defines a standard work week through the shift patterns as defined by the Workday data set and a standard day length; these values are associated with the calendar identified by the value of the calendar variable in that observation. Likewise, each observation of the Holiday data set defines a holiday for the calendar identified by the value of the calendar variable.

If there is no calendar variable in the Activity data set, all activities are assumed to follow the default calendar. If there is no calendar variable in the Holiday data set, all of the holidays specified are assumed to occur in all the calendars. If there is no calendar variable in the Calendar data set, the first observation is assumed to define the default work week (which is also followed by any calendar that might be defined in the Holiday data set), and all subsequent observations are ignored. See the section “[Multiple Calendars](#)” on page 101 for further information.

---

## DURATION Statement

**DURATION** *variable / options* ;

**DUR** *variable* ;

The DURATION statement identifies the variable in the Activity data set that contains the length of time necessary to complete the activity. If the network is input in AOA format, then the variable identifies the duration of the activity denoted by the arc joining the TAILNODE and the HEADNODE. If the network is input in AON format, then the variable identifies the duration of the activity specified in the **ACTIVITY** statement. The variable specified must be numeric. The DURATION statement must be specified. The values of the DURATION variable are assumed to be in *interval* units, where *interval* is the value of the INTERVAL= option.

If you want the procedure to compute the durations of the activities based on specified start and finish times, you can specify the start and finish times in the Activity data set, identified by the variables specified in the START= and FINISH= options. By default, the computed duration is used only if the value of the DURATION variable is missing for that activity. The duration is computed in units of the INTERVAL= parameter, taking into account the calendar defined for the activity.

In addition to specifying a fixed duration for an activity, you can specify the amount of work required (in units of the INTERVAL parameter) from each resource for a given activity. The **WORK** variable enables you to specify resource-driven durations for an activity; these (possibly different) durations are used to calculate the length of time required for the activity to be completed.

The following options can be specified in the DURATION statement after a slash (/).

**FINISH=***variable*

specifies a variable in the Activity data set that is to be used in conjunction with the START variable to determine the activity's duration.

**START=***variable*

specifies a variable in the Activity data set that is to be used in conjunction with the FINISH variable to determine the activity's duration.

**OVERRIDEDUR**

specifies that if the **START=** and **FINISH=** values are not missing, the duration computed from these values is to be used in place of the duration specified for the activity. In other words, the computed duration is used in place of the duration specified for the activity.

---

## HEADNODE Statement

**HEADNODE** *variable* ;

**HEAD** *variable* ;

**TO** *variable* ;

The HEADNODE statement is required when data are input in AOA format. This statement specifies the variable in the Activity data set that contains the name of the node on the head of an arrow in the project

network. This node is identified with the event that signals the end of an activity on that arc. The variable specified can be either a numeric or character variable because the procedure treats this variable symbolically. Each node must be uniquely defined.

## HOLIDAY Statement

**HOLIDAY** *variable / options* ;

**HOLIDAYS** *variable / options* ;

The HOLIDAY statement specifies the names of variables used to describe non-workdays in the [Holiday](#) data set. PROC CPM accounts for holidays only when the INTERVAL= option has one of the following values: DAY, WORKDAY, WEEKDAY, DTDAY, DTWRKDAY, DTHOUR, DTMINUTE, or DTSECOND. The HOLIDAY statement must be used with the HOLIDATA= option in the PROC CPM statement. Recall that the HOLIDATA= option identifies the SAS data set that contains a list of the holidays and non-workdays around which you schedule your project. Holidays are defined by specifying the start of the holiday (the HOLIDAY variable) and either the length of the holiday (the HOLIDUR variable) or the finish time of the holiday (the HOLIFIN variable). The HOLIDAY variable is mandatory with the HOLIDAY statement; the HOLIDUR and HOLIFIN variables are optional.

The HOLIDAY and HOLIFIN variables must be formatted as SAS date or datetime variables. If no format is associated with a HOLIDAY variable, it is assumed to be formatted as a SAS date value. If the schedule of the project is computed as datetime values (which is the case if INTERVAL is DTDAY, WORKDAY, and so on), the holiday variables are interpreted as follows:

- If the HOLIDAY variable is formatted as a date value, then the holiday is assumed to start at the value of the DAYSTART= option on the day specified in the observation and to end *d* units of *interval* later (where *d* is the value of the HOLIDUR variable and *interval* is the value of the INTERVAL= option).
- If the HOLIDAY variable is formatted as a datetime value, then the holiday is assumed to start at the date and time specified and to end *d* units of *interval* later.

The HOLIDUR and HOLIFIN variables are specified using the following options in the HOLIDAY statement:

**HOLIDUR=***variable*

**HDURATION=***variable*

identifies a variable in the [Holiday](#) data set that specifies the duration of the holiday. The INTERVAL= option specified on the PROC CPM statement is used to interpret the value of the holiday duration variables. Thus, if the duration of a holiday is specified as 2 and the value of the INTERVAL= option is WEEKDAY, the length of the holiday is interpreted as two weekdays.

**HOLIFIN=***variable*

**HOLIEND=***variable*

identifies a variable in the [Holiday](#) data set that specifies the finish time of the holiday defined in that observation. If a particular observation contains both the duration as well as the finish time of the holiday, only the finish time is used; the duration is ignored.

## ID Statement

**ID** *variables* ;

The ID statement identifies variables not specified in the **TAILNODE**, **HEADNODE**, **ACTIVITY**, **SUCCESSOR**, or **DURATION** statements that are to be included in the Schedule data set. This statement is useful for carrying any relevant information about each activity from the Activity data set to the Schedule data set.

## PROJECT Statement

**PROJECT** *variable / options* ;

**PARENT** *variables / options* ;

The PROJECT statement specifies the variable in the Activity data set that identifies the project to which an activity belongs. This variable must be of the same type and length as the variable defined in the ACTIVITY statement. A project can also be treated as an activity with precedence and time constraints. In other words, any value of the PROJECT variable can appear as a value of the ACTIVITY variable, and it can have specifications for the DURATION, ALIGNDATE, ALIGNTYPE, ACTUAL, RESOURCE, and SUCCESSOR variables. However, some of the interpretations of these variables for a project (or supertask) may be different from the corresponding interpretation for an activity at the lowest level. See the section “[Multiproject Scheduling](#)” on page 131 for an explanation.

The following options can be specified in the PROJECT statement after a slash (/).

**AGGREGATEPARENTRES**

**AGGREGATEP\_RES**

**AGGREGPR**

indicates that the resource requirements for all supertasks are to be used only for aggregation purposes and not for resource-constrained scheduling.

**DESCENDING**

**DESC**

indicates that, in addition to the ascending sort variables (ES\_ASC, LS\_ASC, and SS\_ASC) that are requested by the ESORDER, LSORDER, and SSORDER options, the corresponding descending sort variables (ES\_DESC, LS\_DESC, and SS\_DESC, respectively) are also to be added to the Schedule output data set.

**ESORDER**

**ESO**

indicates that a variable named ES\_ASC is to be added to the Schedule output data set; this variable can be used to order the activities in such a way that the activities within each subproject are in increasing order of the early start time. This order is not necessarily the same as the one that would be obtained by sorting all the activities in the Schedule data set by E\_START.

**IGNOREPARENTRES****IGNOREP\_RES****IGNOREPR**

indicates that the resource requirements for all supertasks are to be ignored.

**LSORDER****LSO**

indicates that a variable named LS\_ASC is to be added to the Schedule output data set; this variable can be used to order the activities in such a way that the activities within each subproject are in increasing order of the late start time.

**ORDERALL****ALL**

is equivalent to specifying the ESORDER and LSORDER options (and the SSORDER option when resource constrained scheduling is performed).

**RSCHEDORDER****RSCHDORD****RSORDER**

indicates that the order variables that are included in the Schedule output data set are also to be included in the Resource Schedule output data set.

**RSCHEDWBS****RSCHDWBS****RSWBS**

indicates that the WBS code is also to be included in the Resource Schedule data set.

**SEPCRIT**

computes individual critical paths for each project. By default, the master project's early finish time is treated as the starting point for the calculation of the backward pass (which calculates the late start schedule). The late finish time for each subproject is then determined during the backward pass on the basis of the precedence constraints. If a time constraint is placed on the finish time of a subproject (using the ALIGNDATE and ALIGNTYPE variables), the late finish time of the subproject is further constrained by this value.

The SEPCRIT option, on the other hand, requires the late finish time of each subproject to be less than or equal to the early finish time of the subproject. Thus, if you have a set of independent, parallel projects, the SEPCRIT option enables you to compute separate critical paths for each of the subprojects.

**SSORDER****SSO**

indicates that a variable named SS\_ASC is to be added to the Schedule output data set; this variable can be used to order the activities in such a way that the activities within each subproject are in increasing order of the resource-constrained start time.

**USEPROJDUR****USEPROJDURSPEC****USESPECDUR**

uses the specified subproject duration to compute the maximum allowed late finish for each subproject. This is similar to the SEPCRIT option, except that the *specified project duration* is used to set an upper bound on each subproject's late finish time instead of the *project span* as computed from the span of all the subtasks of the project. In other words, if E\_START and E\_FINISH are the early start and finish times of the subproject under consideration, and the subproject duration is PROJ\_DUR, where

$$\text{PROJ\_DUR} = \text{E\_FINISH} - \text{E\_START}$$

then the SEPCRIT option sets

$$\text{L\_FINISH} \leq \text{E\_START} + \text{PROJ\_DUR}$$

while the USEPROJDUR option sets

$$\text{L\_FINISH} \leq \text{E\_START} + \text{DUR}$$

where DUR is the duration specified for the subproject in the Activity data set.

**WBSCODE****WBS****ADDWBS**

indicates that the CPM procedure is to compute a WBS code for the activities in the project using the project hierarchy structure specified. This code is computed for each activity and stored in the variable WBS\_CODE in the Schedule output data set.

## RESOURCE Statement

**RESOURCE** *variables / resource options* ;

**RES** *variables / resource options* ;

The RESOURCE statement identifies the variables in the Activity data set that contain the levels of the various resources required by the different activities. This statement is necessary if the procedure is required to summarize resource utilization for various resources.

This statement is also required when the activities in the network use limited resources and a schedule is to be determined subject to resource constraints in addition to precedence constraints. The levels of the various resources available are obtained from the RESOURCEIN= data set (the Resource data set.) This data set need not contain all of the variables listed in the RESOURCE statement. If any resource variable specified in the RESOURCE statement is not also found in the Resource data set, it is assumed to be available in unlimited quantity and is not used in determining the constrained schedule.

The following options are available with the RESOURCE statement to help control scheduling the activities subject to resource constraints. Some control the scheduling heuristics, some control the amount of information to be output to the RESOURCEOUT= data set (the Usage data set), and so on.

**ACTDELAY=variable**

specifies the name of a variable in the Activity data set that specifies a value for the maximum amount of delay allowed for each activity. The values of this variable should be greater than or equal to 0. If a value is missing, the value of the DELAY= option is used instead.

**ACTIVITYPRTY=variable****ACTPRTY=variable**

identifies the variable in the Activity data set that contains the priority of each activity. This option is required if resource-constrained scheduling is to be performed and the scheduling rule specified is ACTPRTY. If the value of the SCEDRULE= option is specified as the keyword ACTPRTY, then all activities waiting for resources are ordered by increasing values of the ACTPRTY= variable. Missing values of the activity priority variable are treated as +INFINITY. See the section “[Scheduling Method](#)” on page 119 for a description of the various scheduling rules used during resource constrained scheduling.

**ADDCAL**

requests that a variable, \_CAL\_, be added to the Resource Schedule data set that identifies the resource calendar for each resource used by each activity. For observations that summarize the activity’s schedule, this variable identifies the activity’s calendar.

**ALL**

is equivalent to specifying the ESPROFILE and LSPROFILE options when an unconstrained schedule is obtained and is equivalent to specifying all four options, AVPROFILE (AVP), ESPROFILE (ESP), LSPROFILE (LSP), and RCPROFILE (RCP), when a resource-constrained schedule is obtained. If none of these four options are specified and a Usage data set is specified, by default the ALL option is assumed to be in effect.

**ALTBEFORESUP**

indicates that all alternate resources are to be checked first before using supplementary resources. By default, if supplementary levels of resources are available, the procedure uses supplementary levels first and uses alternate resources only if the supplementary levels are not sufficient.

**APPEND****APPENDINTXRATE****APPENDRATEXINT****APPENDUSAGE**

indicates that the Usage data set is to contain two sets of observations: the first set indicates the *rate* of usage for each resource at the beginning of the current time period, and the second set contains the *total* usage of each resource for the current time period. In other words, the Usage data set appends observations indicating the total usage of each resource to the default set of observations. If the APPEND option is specified, the procedure adds a variable named OBS\_TYPE to the Usage data set. This variable contains the value ‘RES\_RATE’ for the observations that indicate rate of usage and the value ‘RES\_USED’ for the observations that indicate the total usage.

**AROUTCAL=calname**

specifies the name of the calendar to be used for incrementing the \_TIME\_ variable in the Usage data set.

**AVPROFILE****AVP****AVL**

creates one variable in the Usage data set corresponding to each variable in the RESOURCE statement. These new variables denote the amount of resources remaining after resource allocation. This option is ignored if resource allocation is not performed.

**AWAITDELAY**

forces PROC CPM to wait until L\_START+*delay*, where *delay* is the maximum delay allowed for the activity (which is the value of the ACTDELAY= variable or the DELAY= option), before an activity is scheduled using supplementary levels of resources. By default, even if an activity has a nonzero value specified for the ACTDELAY= variable (or the DELAY= option), it may be scheduled using supplementary resources before L\_START+*delay*. This happens if the procedure does not see any increase in the resource availability in the future. Thus, if it appears that the activity will require supplementary resources anyway, the procedure may schedule it before L\_START+*delay*. The AWAITDELAY option prohibits this behavior; it will not use supplementary resources to schedule an activity before L\_START+*delay*. This option can be used to force activities with insufficient resources to start at L\_START by setting DELAY=0.

**CUMUSAGE**

specifies that the Usage data set should indicate the cumulative usage of consumable resources. Note that by default, for consumable resources, each observation in the Usage data set contains the rate of usage for each resource at the start of the given time interval. See the section “[RESOURCEOUT= Usage Data Set](#)” on page 127 for a definition of the variables in the resource usage output data set. In some applications, it may be useful to obtain the cumulative usage of these resources. The CUMUSAGE option can be used to obtain the cumulative usage of consumable resources up to the time specified in the \_TIME\_ variable.

**DELAY=***delay*

specifies the maximum amount by which an activity can be delayed due to lack of resources. If E\_START of an activity is 1JUN04 and L\_START is 5JUN04 and *delay* is specified as 2, PROC CPM first tries to schedule the activity to start on June 1, 2004. If there are not enough resources to schedule the activity, the CPM procedure postpones the activity’s start time. However, it does not postpone the activity beyond June 7, 2004 (because *delay*=2 and L\_START=5JUN04).

If the activity cannot be scheduled even on 7JUN04, then PROC CPM tries to schedule it by using supplementary levels of resources, if available, or by using alternate resources, if possible. If resources are still not sufficient, the procedure stops with an error message. The default value of the DELAY= option is assumed to be +INFINITY.

**DELAYANALYSIS****SLIPINF**

causes the addition of three new variables to the Schedule data set. The variables are R\_DELAY, DELAY\_R and SUPPL\_R. The R\_DELAY variable indicates the number of units (in *interval* units) by which the activity’s schedule has slipped due to resource unavailability, and the DELAY\_R variable contains the name of the resource, the *delaying resource*, that has caused the slippage.

The R\_DELAY variable is calculated as follows: it is the difference between S\_START and the time when an activity first enters the list of activities that are available to be scheduled. (See the section

“Scheduling Method” on page 119 for a definition of this waiting list of activities.) R\_DELAY is not necessarily the same as S\_START – E\_START.

If several resources are insufficient, causing a delay in the activity, DELAY\_R is the name of the resource that *first* causes an activity to be postponed.

The variable SUPPL\_R contains the name of the *first* resource that is used above the primary level in order for an activity to be scheduled at S\_START.

### **ESPROFILE**

#### **ESP**

#### **ESS**

creates one variable in the Usage data set corresponding to each variable in the **RESOURCE** statement. Each new variable denotes the resource usage based on the early start schedule for the corresponding resource variable.

### **E\_START**

requests that the E\_START and E\_FINISH variables, namely the variables specifying the early start schedule, be included in the Schedule data set in addition to the S\_START and S\_FINISH variables. This option is the default and can be turned off using the NOE\_START option.

### **EXCLUNSCHED**

excludes the resource consumption corresponding to unscheduled activities from the daily resource usage reported for each time period in the Usage data set. The Usage data set contains a variable named *Resname* for each resource variable *resname*. For each observation in this data set, each such variable contains the total amount of resource (*rate of usage* for a consumable resource) used by all the activities that are active at the time period corresponding to that observation. By default, this calculation includes even activities that are still unscheduled when resource constrained scheduling is stopped either by the STOPDATE= option or due to resource infeasibilities. The EXCLUNSCHED option enables the exclusion of activities that are still unscheduled. The unscheduled activities are assumed to start as per the early start schedule (unless the UPDTUNSCHED option is specified).

### **FILLUNSCHED**

### **FILLMISSING**

fills in S\_START and S\_FINISH values for activities that are still unscheduled when resource constrained scheduling is stopped either by the STOPDATE= option or due to resource infeasibilities. By default, the Schedule data set contains missing values for S\_START and S\_FINISH corresponding to unscheduled activities. If the FILLUNSCHED option is on, the procedure uses the original E\_START and E\_FINISH times for these activities. If the UPDTUNSCHED option is also specified, the procedure uses *updated* values.

### **F\_FLOAT**

requests that the Schedule data set include the F\_FLOAT variable computed using the unconstrained early and late start schedules. If resource allocation is not performed, this variable is always included in the output data set.

### **INCLUNSCHED**

enables the inclusion of activities that are still unscheduled in the computation of daily (or cumulative) resource usage in the Usage data set when resource-constrained scheduling is stopped either by the STOPDATE= option or due to resource infeasibilities. This option is the default and can be turned off by the EXCLUNSCHED option.

**INDEPENDENTALLOC****INDEPALLOC**

enables each resource to be scheduled independently for each activity during resource-constrained scheduling. Consider the basic resource scheduling algorithm described in the section “[Scheduling Method](#)” on page 119. When all the precedence requirements of an activity are satisfied, the activity is inserted into the list of activities that are waiting for resources using the appropriate scheduling rule. An activity in this list is scheduled to start at a particular time only if *all* the resources required by it are available in sufficient quantity. Even if the resources are required by the activity for different lengths of time, or if the resources have different calendars, all resources must be available to start at that particular time (or at the beginning of the next work period for the resource’s calendar).

If you specify the INDEPENDENTALLOC option, however, each resource is scheduled independently of the others. This may cause an activity’s schedule to be extended if its resources cannot all start at the same time.

**INFEASDIAGNOSTIC****INFEASDIAG**

requests PROC CPM to continue scheduling even when resources are insufficient. When PROC CPM schedules the project subject to resource constraints, the scheduling process is stopped when the procedure cannot find sufficient resources for an activity before the activity’s latest possible start time (accounting for the DELAY= or ACTDELAY= options and using supplementary or alternate resources if necessary and if allowed). The INFEASDIAGNOSTIC option can be used to override this default action. (Sometimes, you may want to know the level of resources needed to schedule a project to completion even if resources are insufficient.) This option is equivalent to specifying infinite supplementary levels for all the resources under consideration; the DELAY= value is assumed to equal the default value of +INFINITY, unless otherwise specified.

**LSPROFILE****LSP****LSS**

creates one variable in the Usage data set corresponding to each variable in the RESOURCE statement. Each new variable denotes the resource usage based on the late start schedule for the corresponding resource variable.

**L\_START**

requests that the L\_START and L\_FINISH variables, namely the variables specifying the late start schedule, be included in the Schedule data set in addition to the S\_START and S\_FINISH variables. This option is the default and can be turned off using the NOL\_START option.

**MAXDATE=***maxdate*

specifies the maximum value of the \_TIME\_ variable in the Usage data set. The default value of *maxdate* is the maximum finish time for all of the schedules for which a usage profile was requested.

**MAXNSEGMENT=***variable***MAXNSEG=***variable*

specifies a variable in the Activity data set that indicates the maximum number of segments that the current activity can be split into. A missing value for this variable is set to a default value that depends on the duration of the activity and the value of the MINSEGMTDUR variable. A value of 1 indicates that the activity cannot be split. By default, PROC CPM assumes that any activity, once started, cannot

be stopped until it is completed (except for breaks due to holidays or weekends). Thus, even during resource-constrained scheduling, an activity is scheduled only if enough resources can be found for it throughout its *entire* duration. Sometimes, you may want to allow preemption of activities already in progress; thus, a more *critical* activity could cause another activity to be split into two or more segments.

However, you may not want a particular activity to be split into too many segments, or to be split too many times. The MAXNSEGMT= and MINSEGMDUR= options enable you to control the number of splits and the length of each segment.

#### **MAXOBS=*max***

specifies an upper limit on the number of observations that the Usage data set can contain. If the values specified for the ROUTINTERVAL= and ROUTINTPER= options are such that the data set will contain more than *max* observations, then PROC CPM does not create the output data set and stops with an error message.

The MAXOBS= option is useful as a check to ensure that a very large data set (with several thousands of observations) is not created due to a wrong specification of the ROUTINTERVAL= option. For example, if *interval* is DTYEAR and *routinterval* is DTHOUR and the project extends over 2 years, the number of observations would exceed 15,000. The default value of the MAXOBS= option is 1000.

#### **MILESTONERESOURCE**

specifies that milestone activities consume resources. If a nonzero requirement is specified for a milestone, the corresponding consumable resources are used at the scheduled time of that milestone.

#### **MILESTONENORESOURCE**

specifies that milestone activities do not consume resources. This implies that all resource requirements are ignored for milestone activities. This is the default behavior.

#### **MINDATE=*mindate***

specifies the minimum value of the \_TIME\_ variable in the Usage data set. The default value of *mindate* is the minimum start time for all of the schedules for which a usage profile is requested. Thus, the Usage data set has observations containing the resource usage and availability information from *mindate* through *maxdate*.

#### **MINSEGMDUR=*variable***

#### **MINSEGD=*variable***

specifies a variable in the Activity data set that indicates the minimum duration of any segment of the current activity. A missing value for this variable is set to a value equal to one fifth of the activity's duration.

#### **MULTIPLEALTERNATES**

#### **MULTALT**

indicates that multiple alternate resources can be used to substitute for a single resource. In other words, if one of the alternate resources is not sufficient to substitute for the primary resource, the procedure will use other alternates, as needed, to fulfill the resource requirement. For example, if an activity needs 1.5 programmers and the allowed alternates are JOHN and MARY, the procedure will use JOHN (at rate 1) and MARY (at rate 0.5) to allocate a total of 1.5 programmers. See the section “[Specifying Multiple Alternates](#)” on page 125 for details.

**NOE\_START**

requests that the E\_START and E\_FINISH variables, namely the variables specifying the early start schedule, be dropped from the Schedule data set. Note that the default is E\_START. Also, if resource allocation is not performed, the NOE\_START option is ignored.

**NOF\_FLOAT**

requests that the F\_FLOAT variable be dropped from the Schedule data set when resource-constrained scheduling is requested. This is the default behavior. To include the F\_FLOAT variable in addition to the resource-constrained schedule, use the F\_FLOAT option. If resource allocation is not performed, F\_FLOAT is always included in the Schedule data set.

**NOL\_START**

requests that the Schedule data set does not include the late start schedule, namely, the L\_START and L\_FINISH variables. Note that the default is L\_START. Also, if resource allocation is not performed, the NOL\_START option is ignored.

**NORESOURCEVARS****NORESVARSOUT****NORESVARS**

requests that the variables specified in the RESOURCE statement be dropped from the Schedule data set. By default, all of the resource variables specified on the **RESOURCE** statement are also included in the Schedule data set.

**NOT\_FLOAT**

requests that the T\_FLOAT variable be dropped from the Schedule data set when resource-constrained scheduling is requested. This is the default behavior. To include the T\_FLOAT variable in addition to the resource-constrained schedule, use the T\_FLOAT option. If resource allocation is not performed, T\_FLOAT is always included in the Schedule data set.

**NROUTCAL=calnum**

specifies the number of the calendar to be used for incrementing the \_TIME\_ variable in the Usage data set.

**OBSTYPE=variable**

specifies a character variable in the Resource data set that contains the type identifier for each observation. Valid values for this variable are RESLEVEL, RESTYPE, RESUSAGE, RESPRTY, SUPLEVEL, ALTRATE, ALTPRTY, RESRCDUR, CALENDAR, MULTALT, MINARATE, and AUXRES. If OBSTYPE= is not specified, then all observations in the data set are assumed to denote the levels of the resources, and all resources are assumed to be replenishable and constraining.

**PERIOD=variable****PER=variable**

identifies the variable in the RESOURCEN= data set that specifies the date from which a specified level of the resource is available for each observation with the OBSTYPE variable equal to 'RESLEVEL'. It is an error if the PERIOD= variable has a missing value for any observation specifying the levels of the resources or if the Resource data set is not sorted in increasing order of the PERIOD= variable.

**RCPROFILE****RCP****RCS**

creates one variable in the Usage data set corresponding to each variable in the **RESOURCE** statement. Each new variable denotes the resource usage based on the resource-constrained schedule for the corresponding resource variable. This option is ignored if resource allocation is not performed.

**RESCALINTERSECT****RESCALINT****RCI**

specifies that an activity can be scheduled only during periods that are common working times for all resource calendars (corresponding to the resources used by that activity) and the activity's calendar. This option is valid only if multiple calendars are in use and if calendars are associated with individual resources. Use this option with caution; if an activity uses resources that have mutually disjoint calendars, that activity can never be scheduled. For example, if one resource works a night shift while another resource works a day shift, the two calendars do not have any common working time.

Only primary resources are included in the intersection; any alternate or auxiliary resources are not included when determining the common working calendar for the activity.

If you do not specify the RESCALINTERSECT option, and resources have independent calendars, then the procedure schedules each resource using its own calendar. Thus, an activity can have one resource working on a five-day calendar, while another resource is working on a seven-day calendar.

**RESID=variable**

specifies a variable in the RESOURCEIN= data set that indicates the name of the resource variable for which *alternate resource information* or *auxiliary resource information* is being specified in that observation.

Observations that indicate alternate resources are identified by the values 'ALTRATE' and 'ALTPRTY' for the OBSTYPE variable. These values indicate whether the observation specifies a *rate of substitution* or a *priority for substitution*; the value of the RESID variable in such an observation indicates the particular resource for which alternate resource information is specified in that observation. The specification of the RESID= option triggers the use of alternate resources. See the section "[Specifying Alternate Resources](#)" on page 123 for further information.

Observations indicating auxiliary resources are identified by the value 'AUXRES' for the OBSTYPE variable. Such observations specify the name of the primary resource as the value of the RESID variable and the rate of auxiliary resources needed for every unit of the primary resource as values of the other resource variables. See the section "[Auxiliary Resources](#)" on page 127 for further information.

**RESOURCEVARS****RESVARSOOUT**

requests that the variables specified in the **RESOURCE** statement be included in the Schedule data set. These include the RESOURCE variables identifying the resource requirements, the activity priority variable, the activity delay variable, and any variables specifying activity splitting information. This option is the default and can be turned off by the NORESVARSOOUT option.

**ROUTINTERVAL=routinterval****STEPINT=routinterval**

specifies the units to be used to determine the time interval between two successive values of the *\_TIME\_* variable in the Usage data set. It can be used in conjunction with the ROUTINTPER= option to control the amount of information to be included in the data set. Valid values for *routinterval* are DAY, WORKDAY, WEEK, MONTH, WEEKDAY, QTR, YEAR, DTDAY, DTWRKDAY, DTWEEK, DTMONTH, DTQTR, DTYEAR, DTSECOND, DTMINUTE, DTHOUR, SECOND, MINUTE, or HOUR. The value of this parameter must be chosen carefully; a massive amount of data could be generated by a bad choice. If this parameter is not specified, a default value is chosen depending on the format of the schedule variables.

**ROUTINTPER=routintper****STEPSIZE=routintper****STEP=routintper**

specifies the number of *routinterval* units between successive observations in the Usage data set where *routinterval* is the value of the ROUTINTERVAL= option. For example, if *routinterval* is MONTH and *routintper* is 2, the time interval between each pair of observations in the Usage data set is two months. The default value of *routintper* is 1. If *routinterval* is blank (''), then *routintper* can be used to specify the exact numeric interval between two successive values of the *\_TIME\_* variable in the Usage data set. *routintper* is only allowed to have integer values when *routinterval* is specified as one of the following: WEEK, MONTH, QTR, YEAR, DTWEEK, DTMONTH, DTQTR, or DTYEAR.

**ROUTNOBREAK****ROUTCONT**

specifies that the *\_TIME\_* variable is to be incremented using a calendar with no breaks or holidays. Thus, the Usage data set contains one observation per unit *routinterval* from *mindate* to *maxdate*, without any breaks for holidays or weekends. By default, the *\_TIME\_* variable is incremented using the default calendar; thus, if the default calendar follows a five-day work week, the Usage data set skips weekends.

**RSCHEDID=(variables)****RSID=(variables)**

identifies variables not specified in the TAILNODE, HEADNODE, or ACTIVITY statements that are to be included in the Resource Schedule data set. This option is useful for carrying any relevant information about each activity from the Activity data set to the Resource Schedule data set.

**SCHEDRULE=schedrule****RULE=schedrule**

specifies the rule to be used to order the list of activities whose predecessor activities have been completed while scheduling activities subject to resource constraints. Valid values for *schedrule* are LST, LFT, SHORTDUR, ACTPRTY, RESPRTY, and DELAYLST. (See the section “[Scheduling Rules](#)” on page 120 for more information.) The default value of SCHEDRULE is LST. If an invalid specification is given for the SCHEDRULE= option, the default value is used, and a warning message is displayed in the log.

**SCHEDRULE2=schedrule2****RULE2=schedule2**

specifies the rule to be used to break ties caused by the SCHEDRULE= option. Valid values for *schedrule2* are LST, LFT, SHORTDUR, ACTPRTY, RESPRTY, and DELAYLST. ACTPRTY and RESPRTY cannot be specified at the same time for the two scheduling rules; in other words, if *schedrule* is ACTPRTY, *schedrule2* cannot be RESPRTY and vice versa.

**SETFINISH=MAX | EARLY (Experimental)**

controls the computation of resource-constrained finish times for activities that are in progress. A value of EARLY sets the resource-constrained finish time to the early finish time as derived from the progress updating variables A\_START, A\_FINISH, REMDUR, and PCTCOMP. Specifying the default value of MAX sets the resource-constrained finish time to the maximum of the early finish time and the finish times for all resources for the given activity. Use of the EARLY value for this option could leave work unfulfilled because of the priority given to the progress updating information.

**SPLITFLAG**

indicates that activities are allowed to be split into segments during resource allocation. This option can be used instead of specifying either the MAXNSEGMENT= or the MINSEGMDUR= variable; PROC CPM assumes that the activity can be split into no more than five segments.

**STOPDATE=stdate**

specifies the cutoff date for resource-constrained scheduling. When such a date is specified, S\_START and S\_FINISH are set to missing beyond the cutoff date. Options are available to set these missing values to the original E\_START and E\_FINISH times (FILLUNSCHED) or to updated values based on the scheduled activities (UPDTUNSCHED).

**T\_FLOAT**

requests that the Schedule data set include the T\_FLOAT variable computed using the unconstrained early and late start schedules. Note that if resource allocation is not performed, this variable is always included in the Schedule data set.

**TOTUSAGE****INTXRATE****INTUSAGE****RATEXINT**

specifies that the Usage data set is to indicate the *total* usage of the resource for the current time period. The current time period is the time interval from the time specified in the \_TIME\_ variable for the current observation to the time specified in the \_TIME\_ variable for the next observation. The total usage is computed taking into account the relevant activity and resource calendars. Note that, by default, the observations in the Usage data set specify the *rate* of usage for each resource at the beginning of the current time period. The TOTUSAGE option specifies the *product* of the rate and the time interval between two successive observations. To get both the *rate* and the *product*, use the APPEND option.

**UNSCHEDEMISS**

sets the S\_START and S\_FINISH values to missing for activities that are still unscheduled when resource constrained scheduling is stopped either by the STOPDATE= option or due to resource infeasibilities. This is the default and can be turned off by specifying the FILLUNSCHED option.

**UPDTUNSCHED**

causes the procedure to use the S\_START and S\_FINISH times of *scheduled* activities to update the *projected* start and finish times for the activities that are still unscheduled when resource constrained scheduling is stopped either by the STOPDATE= option or due to resource infeasibilities. These updated dates are used as the S\_START and S\_FINISH times.

**WORK=variable**

identifies a variable in the Activity data set that specifies the total amount of work required by one unit of a resource. This work is represented in units of the INTERVAL parameter. The procedure uses the rate specified for the resource variable to compute the duration of the activity for that resource. Thus, if the value of the WORK variable is 10, and the value of the resource variable R1 is 2, then the activity requires 5 *interval* units for the resource R1. For details, see the section “[Resource-Driven Durations and Resource Calendars](#)” on page 112.

## SUCCESSOR Statement

**SUCCESSOR** *variables / lag options* ;

**SUCC** *variables / lag options* ;

The SUCCESSOR statement is required when data are input in an AON format. This statement specifies the variables that contain the names of the immediate successor nodes (activities) to the ACTIVITY node. These variables must be of the same type and length as those defined in the [ACTIVITY](#) statement.

If the project does not have any precedence relationships, it is not necessary to use the SUCCESSOR statement. Thus, you can specify only the ACTIVITY statement without an accompanying SUCCESSOR statement.

If the precedence constraints among the activities have some nonstandard relationships, you can specify these using the LAG options. The following is a list of LAG options.

**ALAGCAL=calname**

specifies the name of the calendar to be used for all lags. The default value for this option is the DEFAULT calendar.

**LAG=variables**

specifies the variables in the Activity data set used to identify the lag relationship (lag type, duration, and calendar) between the activity and its successor. The LAG variables must be character variables. You can specify as many LAG variables as there are SUCCESSOR variables; each SUCCESSOR variable is matched with the corresponding LAG variable. You must specify the LAG variables enclosed in parentheses. In a given observation, the *i*th LAG variable specifies the type of relation between the current activity (as specified by the ACTIVITY variable) and the activity specified by the *i*th SUCCESSOR variable. If there are more LAG variables than SUCCESSOR variables, the extra LAG variables are ignored; conversely, if there are fewer LAG variables, the extra SUCCESSOR variables are all assumed to indicate successors with a *standard* (finish-to-start) relationship.

In addition to the type of relation, you can also specify a lag duration and a lag calendar in the same variable. The relation\_lag\_calendar information is expected to be specified as

*keyword* \_ *duration* \_ *calendar*

where *keyword* is one of ‘’, FS, SS, SF, or FF, *duration* is a number specifying the duration of the lag (in *interval* units), and *calendar* is either a calendar name or number identifying the calendar followed by the lag duration. A missing value for the *keyword* is assumed to mean the same as FS, which is the standard relation of *finish-to-start*. The other three values, SS, SF, and FF, denote relations of the type *start-to-start*, *start-to-finish*, and *finish-to-finish*, respectively. If there are no LAG variables, all relationships are assumed to be of the type *finish-to-start* with no lag duration. Table 4.3 contains some examples of lag specifications.

**Table 4.3** Lag Specifications

Activity	Successor	LAG	Interpretation
A	B	SS_3	Start to start lag of 3 units
A	B	_5.5	Finish to start lag of 5.5 units
A	B	FF_4	Finish to finish lag of 4 units
A	B	_SS	Invalid and ignored (with warning)
A		SS_3	Ignored
A	B	SS_3_1	Start to start lag of 3 units w.r.t. calendar 1

**NLAGCAL=calnum**

specifies the number of the calendar to be used for all lags. The default value for this option is the DEFAULT calendar.

## TAILNODE Statement

**TAILNODE** *variable* ;

**TAIL** *variable* ;

**FROM** *variable* ;

The TAILNODE statement is required when data are input in AOA (arrow notation) format. It specifies the variable that contains the name of each node on the tail of an arc in the project network. This node is identified with the event that signals the *start* of the activity on that arc. The variable specified can be either a numeric or character variable since the procedure treats this variable symbolically. Each node must be uniquely defined.

## Details: CPM Procedure

This section provides a detailed outline of the use of the CPM procedure. The material is organized in subsections that describe different aspects of the procedure. They have been placed in increasing order of functionality. The first section describes how to use PROC CPM to schedule a project subject only to precedence constraints. The next two sections describe some of the features that enable you to control the units of duration and specify nonstandard precedence constraints. In the section “[Time-Constrained Scheduling](#)” on page 96, the statements needed to place time constraints on the activities are introduced. the section “[Finish Milestones](#)” on page 98 describes some options controlling the treatment of milestones.

The section “[OUT= Schedule Data Set](#)” on page 99 describes the format of the schedule output data set (the Schedule data set). The section “[Multiple Calendars](#)” on page 101 deals with calendar specifications for the different activities.

The section “[Baseline and Target Schedules](#)” on page 109 describes how you can save specific schedules as baseline or target schedules. The section “[Progress Updating](#)” on page 109 describes how to incorporate the actual start and finish times for a project that is already in progress. The section “[Resource-Driven Durations and Resource Calendars](#)” on page 112 describes how the WORK variable can be used to specify resource-driven durations and the effect of resource calendars on the activity schedules.

Next, the section “[Resource Usage and Allocation](#)” on page 113 pertains to resource usage and resource-constrained scheduling and describes how to specify information about the resources and the resource requirements for the activities. The scheduling algorithm is also described in this section and some advanced features such as alternate resources, auxiliary resources, negative resource requirements, and so on, are discussed under separate subsections.

The section “[RESOURCEOUT= Usage Data Set](#)” on page 127 describes the format of the resource usage output data set (the Usage data set) and explains how to interpret the variables in it.

When resource-driven durations are specified or resource calendars are in effect, each resource used by an activity may have a different schedule. In this case, the Resource Schedule data set, described in the section “[RESOURCESCHED= Resource Schedule Data Set](#)” on page 131, contains the individual resource schedules for each activity.

The section “[Multiproject Scheduling](#)” on page 131 describes how you can use PROC CPM when there are multiple projects that have been combined together in a multiproject structure.

PROC CPM also defines a macro variable that is described in the section “[Macro Variable \\_ORCPM\\_](#)” on page 134.

Table 4.9 in the section “[Input Data Sets and Related Variables](#)” on page 135 lists all the variables used by the CPM procedure and the data sets that contain them. Table 4.10 in the section “[Missing Values in Input Data Sets](#)” on page 137 lists all of the variables in the different input data sets and describes how PROC CPM treats missing values corresponding to each of them. Finally, the section “[FORMAT Specification](#)” on page 139 underlines the importance of associating the correct FORMAT specification with all the date-type variables, and the section “[Computer Resource Requirements](#)” on page 139 indicates the storage and time requirements of the CPM procedure.

---

## Scheduling Subject to Precedence Constraints

The basic function of the CPM procedure is to determine a schedule of the activities in a project subject to precedence constraints among them. The minimum amount of information that is required for a successful invocation of PROC CPM is the network information specified either in AON or AOA formats and the duration of each activity in the network. The INTERVAL= option specifies the units of duration, and the DATE= option specifies a start date for the project. If a start date is not specified for the project, the schedule is computed as unformatted numerical values with a project start date of 0. The DATE= option can be a SAS date, time, or datetime value (or a number) and can be used to specify a start date for the project. In addition to the start date of the project, you can specify a desired *finish date* for the project using the FBDATE= option.

PROC CPM computes the early start schedule as well as the late start schedule for the project. The project start date is used as the starting point for the calculation of the early start schedule, while the project completion date is used in the computation of the late start schedule. The early start time (E\_START) for all *start* activities (those activities with no predecessors) in the project is set to be equal to the value of the DATE parameter (if the FINISHBEFORE option is not specified). The early finish time (E\_FINISH) for each start activity is computed as E\_START + *dur*, where *dur* is the activity's duration (as specified in the Activity data set). For each of the other activities in the network, the early start time is computed as the maximum of the early finish time of all its immediate predecessors.

The project finish time is computed as the maximum of the early finish time of all the activities in the network. The late finish time (L\_FINISH) for all the *finish* activities (those activities with no successors) in the project is set to be equal to the project finish time. The late start time (L\_START) is computed as L\_FINISH - *dur*. For each of the other activities in the network, the late finish time is computed as the minimum of the late start time of all its immediate successors. If the FIXFINISH option is specified, the late finish time for each finish activity is set to be equal to its early finish time. In other words, the finish activities are not allowed to float to the end of the project.

Once the early and late start schedules have been computed, the procedure computes the free and total float times for each activity. Free float (F\_FLOAT) is defined as the maximum delay that can be allowed in an activity without delaying a successor activity. Total float (T\_FLOAT) is calculated as the difference between the activity's late finish time and early finish time; it indicates the amount of time by which an activity can be delayed without delaying the entire project. The values of both the float variables are calculated in units of the INTERVAL parameter.

An activity that has zero T\_FLOAT is said to be *critical*. As a result of the forward and backward pass computations just described, there is at least one path in the project network that contains only critical activities. This path is called the *critical path*. The duration of the project is equal to the length of the critical path.

If the FBDATE= option is also specified, the project finish time is set equal to the value of the FBDATE= option. The backward pass computation is initiated by setting the late finish time for all the finish activities in the project to be equal to *fbdate*. If the project finish time, as computed from the forward pass calculations, is different from *fbdate*, the longest path in the network may no longer have 0 total float. In such a situation, the critical path is defined to be the path in the network with the least total float. Activities with negative T\_FLOAT are referred to as *supercritical* activities.

**NOTE:** An important requirement for a project network is that it should be *acyclic* (cycles are not allowed).

A network is said to contain a *cycle* (or *loop*) if the precedence relationships starting from an activity loops back to the same activity. The forward and backward pass computations cannot be performed for a cyclic network. If the project network has a cycle, the CPM procedure stops processing after identifying the cycle.

## Using the INTERVAL= Option

The INTERVAL= option enables you to define the units of the DURATION variable; that is, you can indicate whether the durations are specified as hours, minutes, days, or in terms of workdays, and so on. In addition to specifying the units, the INTERVAL= option also indicates whether the schedule is to be output as SAS time, date, or datetime values, or as unformatted numeric values.

The prefix *DT* in the value of the INTERVAL= option (as in DTDAY, DTWEEK, and so on) indicates to PROC CPM that the schedule is output as SAS datetime values, and the DATE= option is expected to be a SAS datetime value. Thus, use DTYEAR, DTMONTH, DTQTR, or DTWEEK instead of the corresponding YEAR, MONTH, QTR, or WEEK if the DATE= option is specified as a SAS datetime value.

The start and finish times for the different schedules computed by PROC CPM denote the first and last *day* of work, respectively, when the values are formatted as SAS *date* values. If the times are SAS *time* or *datetime* values, they denote the first and last *second* of work, respectively.

If the INTERVAL= option is specified as WORKDAY, the procedure schedules work on weekdays and nonholidays starting at 9 a.m. and ending at 5 p.m. If you use INTERVAL=DTWRKDAY, the procedure also schedules work only on weekdays and nonholidays. In this case, however, the procedure expects the DATE= option to be a SAS datetime value, and the procedure interprets the start of the workday from the time portion of that option. To change the length of the workday, use the DAYLENGTH= option in conjunction with INTERVAL=DTWRKDAY.

The procedure sets the default value of the INTERVAL= option on the basis of the units of the DATE= option. Table 4.4 lists various valid combinations of the INTERVAL= option and the type of the DATE= option (number, SAS time, date or datetime value) and the resulting interpretation of the duration units and the format type of the schedule variables (numbers, SAS time, date or datetime format) output to the Schedule data set. For each DATE type value, the first INTERVAL value is the default. Thus, if the DATE= option is a SAS date value, the default value of the INTERVAL= option is DAY, and so on.

For the first five specifications of the INTERVAL= option in the last part of Table 4.4 (DTDAY , . . . , DTHOUR), the day starts at *daystart* and is *daylength* hours long.

The procedure may change the INTERVAL= specification and the units of the schedule variables to be compatible with the format specification of the ALIGNDATE variable, or the A\_START or A\_FINISH variables in the Activity data set, or the PERIOD variable in the Resource data set. For example, if *interval* is specified as DAY, but the ALIGNDATE variable contains SAS datetime values, the schedule is computed in SAS datetime values. Similarly, if *interval* is specified as DAY or WEEKDAY, but some of the durations are fractional, the schedule is computed as SAS datetime values.

**Table 4.4** INTERVAL= and DATE= Parameters and Units of Duration

<b>DATE Type</b>	<b>INTERVAL</b>	<b>Units of Duration</b>	<b>Format of Schedule Variables</b>
Number		Period	Unformatted
SAS time	HOUR	Hour	SAS time
	MINUTE	Minute	SAS time
	SECOND	Second	SAS time
	DAY	Day	SAS date
SAS date	WEEKDAY	Day (5-day week)	SAS date
	WORKDAY	Day (5-day week: 9-5 day)	SAS datetime
	WEEK	Week	SAS date
	MONTH	Month	SAS date
SAS datetime	QTR	Quarter	SAS date
	YEAR	Year	SAS date
	DTDAY	Day (7-day week)	SAS datetime
	DTWRKDAY	Day (5-day week)	SAS datetime
	DTSECOND	Second	SAS datetime
	DTMINUTE	Minute	SAS datetime
	DTHOUR	Hour	SAS datetime
	DTWEEK	Week	SAS datetime
	DTMONTH	Month	SAS datetime
	DTQTR	Quarter	SAS datetime
	DTYEAR	Year	SAS datetime

## Nonstandard Precedence Relationships

A *standard* precedence constraint between two activities (for example, activity A and an immediate successor B) implies that the second activity is ready to start as soon as the first activity has finished. Such a relationship is called a *finish-to-start* relationship with zero lag. Often, you want to specify other types of relationships between activities. For example:

- Activity B can start five days after activity A has started: start-to-start lag of five days.
- Activity B can start three days after activity A has finished: finish-to-start lag of three days.

The AON representation of the network enables you to specify such relationships between activities: use the LAG= option in the **SUCCESSOR** statement. This enables you to use variables in the Activity data set that specify the type of relationship between two activities and the time lag between the two events involved; you can also specify the calendar to be used in measuring the lag duration. See the section “**SUCCESSOR Statement**” on page 90 for information about the specification. **Example 4.11**, “Nonstandard Relationships,” in the section “Examples” illustrates a nonstandard precedence relationship.

This section briefly discusses how the computation of the early and late start schedules, described in the section “[Scheduling Subject to Precedence Constraints](#)” on page 93, changes in the presence of nonstandard relationships.

For each (predecessor, successor) pair of activities, the procedure saves the lag type, lag duration, and lag calendar information. Suppose that the predecessor is A, the immediate successor is B, the durations of the two activities are  $durA$  and  $durB$ , respectively, and the activity’s early start and finish times are  $pes$  and  $pef$ , respectively. Suppose further that the lag type is  $lt$ , lag duration is  $ld$ , and lag calendar is  $lc$ . Recall that the basic forward and backward passes described in the section “[Scheduling Subject to Precedence Constraints](#)” on page 93 assume that all the precedence constraints are standard of the type finish-to-start with zero lag. Thus, in terms of the notation just defined, the early start time of an activity is computed as the maximum of  $pef$  for all the preceding activities. However, in the presence of nonstandard relationships, the predecessor’s value used to compute an activity’s early start time depends on the lag type and lag value. [Table 4.5](#) lists the predecessor’s value that is used to determine the successor’s early start time.

**Table 4.5** Effect of Lag Duration and Calendar on Early Start Schedule

Lag Type	Definition	Value Used to Compute Successor’s E_START
FS	Finish-to-start	$pef + ld$
SS	Start-to-start	$pes + ld$
SF	Start-to-finish	$pes + ld - durB$
FF	Finish-to-finish	$pef + ld - durB$

The addition of the lag durations ( $ld$ ) is in units following the lag calendar  $lc$ ; the subtraction of  $durB$  is in units of the activity B’s calendar. The backward pass to determine the late start schedule is modified in a similar way to include lag durations and calendars.

---

## Time-Constrained Scheduling

You can use the DATE= and FBDATE= options in the PROC CPM statement (or the DATE= option in conjunction with the FINISHBEFORE option) to impose start and finish dates on the project as a whole. Often, you want to impose start or finish constraints on individual activities within the project. The [ALIGNDATE](#) and [ALIGNTYPE](#) statements enable you to do so. For each activity in the project, you can specify a particular date (as the value of the ALIGNDATE variable) and whether you want the activity to start on or finish before that date (by specifying one of several *alignment types* as the value of the ALIGNTYPE variable). PROC CPM uses all these dates in the computation of the early and late start schedules.

The following explanation best illustrates the restrictions imposed on the start or finish times of an activity by the different types of alignment allowed. Let  $d$  denote the value of the ALIGNDATE variable for a particular activity and let  $dur$  be the activity’s duration. If  $minsdate$  and  $maxfdate$  are used to denote the earliest allowed start date and the latest allowed finish date, respectively, for the activity, then [Table 4.6](#) illustrates the values of  $minsdate$  and  $maxfdate$  as a function of the value of the ALIGNTYPE variable.

Once the  $minsdate$  and  $maxfdate$  dates have been calculated for all of the activities in the project, the values of  $minsdate$  are used in the computation of the *early start* schedule and the values of  $maxfdate$  are used in the computation of the *late start* schedule.

**Table 4.6** Determining Alignment Date Values with the ALIGNTYPE Statement

Keywords	Alignment Type	<i>minsdate</i>	<i>maxfdate</i>
SEQ	Start equal	$d$	$d + dur$
SGE	Start greater than or equal	$d$	$+infinity$
SLE	Start less than or equal	$-infinity$	$d + dur$
FEQ	Finish equal	$d - dur$	$d$
FGE	Finish greater than or equal	$d - dur$	$+infinity$
FLE	Finish less than or equal	$-infinity$	$d$
MS	Mandatory start	$d$	$d + dur$
MF	Mandatory finish	$d - dur$	$d$

For the first six alignment types in **Table 4.6**, the value of *minsdate* specifies a lower bound on the early start time and the value of *maxfdate* specifies an upper bound on the late finish time of the activity. The early start time (E\_START) of an activity is computed as the maximum of its *minsdate* and the early finish times (E\_FINISH) of all its predecessors ( $E\_FINISH = E\_START + dur$ ). If nonstandard relationships are present in the project, the predecessor's value that is used depends on the type of the lag and the lag duration; **Table 4.5** in the previous section lists the values used as a function of the lag type. If a target completion date is not specified (using the FBDATE or FINISHBEFORE options), the project completion time is determined as the maximum value of E\_FINISH over all of the activities in the project. The late finish time (L\_FINISH) for each of the finish activities (those with no successors) is computed as the minimum of its *maxfdate* and the project completion date; late start time (L\_START) is computed as  $L\_FINISH - dur$ . The late finish time (L\_FINISH) for each of the other activities in the network is computed as the minimum of its *maxfdate* and the times of all its successors.

It is important to remember that the precedence constraints of the network are always respected (for these first six alignment types). Thus, it is possible that an activity that has an alignment constraint of the type SEQ, constraining it to start on a particular date, say  $d$ , may not start on the specified date  $d$  due to its predecessors not being finished before  $d$ . During resource-constrained scheduling, a further slippage in the start date could occur due to insufficient resources. In other words, *the precedence constraints and resource constraints have priority over the time constraints* (as imposed by the ALIGNDATE and ALIGNTYPE statements) in the determination of the schedule of the activities in the network.

The last two alignment types, MS and MF, however, specify *mandatory dates* for the start and finish times of the activities for both the early and late start schedules. These alignment types can be used to schedule activities to start or finish on a given date disregarding precedence and resource constraints. Thus, an activity with the ALIGNTYPE variable's value equal to MS and the ALIGNDATE variable's value equal to  $d$  is scheduled to start on  $d$  (for the early, late, and resource-constrained schedules) irrespective of whether or not its predecessors are finished or whether or not there are enough resources.

It is possible for the L\_START time of an activity to be less than its E\_START time if there are constraints on the start times of certain activities in the network (or constraints on the finish times of some successor activities) that make the target completion date infeasible. In such cases, some of the activities in the network have negative values for T\_FLOAT, indicating that these activities are supercritical. See [Example 4.12](#), “Activity Time Constraints,” for a demonstration of this situation.

## Finish Milestones

By default, the start and finish times for the different schedules computed by PROC CPM denote the first and last *day* of work, respectively, when the values are formatted as SAS *date* values. All start times are assumed to denote the beginning of the day and all finish times are assumed to correspond to the end of the day. If the times are SAS *time* or *datetime* values, they denote the first and last *second* of work, respectively. However, for zero duration activities, *both* the start and the finish times correspond to the beginning of the date (or second) specified.

Thus, according to the preceding definitions, the CPM procedure assumes that all milestones are scheduled at the *beginning* of the day indicated by their start times. In other words, the milestones can be regarded as *start* milestones since they correspond to the *beginning* of the time period indicated by their scheduled times.

However, in some situations, you may want to treat the milestones as *finish* milestones.

Consider the following example:

Activity ‘A’ has a 2-day duration and is followed by a milestone (zero duration) activity, ‘B’. Suppose that activity ‘A’ starts on March 15, 2004. The default calculations by the CPM procedure will produce the following schedule for the two activities:

OBS	Activity	Duration	E_START	E_FINISH
1	A	2	15MAR2004	16MAR2004
2	B	0	17Mar2004	17MAR2004

The start and finish times of the milestone activity, ‘B’, are interpreted as the beginning of March 17, 2004. In some situations, you may want the milestones to start and finish on the same day as their predecessors. For instance, in this example, you may want the start and finish time of activity ‘B’ to be set to March 16, 2004, with the interpretation that the time corresponds to the *end* of the day. Such milestones will be referred to as *finish milestones*.

The SETFINISHMILESTONE option in the PROC CPM statement indicates that a milestone that is linked to its predecessor by a *Finish-to-Start* or a *Finish-to-Finish* precedence constraint should be treated as a *finish milestone*. In other words, such a milestone should have the start and finish time set to the *end* of the day that the predecessor activity finishes. There are some exceptions to this rule:

- There is an alignment constraint on activity ‘B’ that requires the milestone to start on a later day than the date dictated by the precedence constraint.
- Activity ‘B’ has an actual start or finish time specified that is inconsistent with the predecessor’s finish date.

The alignment constraint that affects the early schedule of the project may not have any impact on the late schedule. Thus, a milestone may be treated as a finish milestone for the late schedule even if it is not a finish milestone according to the early schedule. See [Example 4.28](#) for an illustration of this situation. In addition, while computing the resource-constrained schedule, a start milestone (according to the early schedule) may in fact turn out to be a finish milestone according to the resource-constrained schedule.

Since the same milestone could be treated as either a start or a finish milestone depending on the presence or absence of an alignment constraint, or depending on the type of the schedule (early, late, resource-constrained,

or actual), the CPM procedure adds extra variables to the Schedule data set corresponding to each type of schedule. These variables, EFINMILE, LFINMILE, SFINMILE, and AFINMILE, indicate for each milestone activity in the project whether the corresponding schedule times (early, late, resource-constrained, or actual) are to be interpreted as finish milestone times. These variables have a value of ‘1’ if the milestone is treated as a finish milestone for the corresponding schedule; otherwise, the value is missing. In addition to providing an unambiguous interpretation for the schedule times of the milestones, these variables are useful in plotting the schedules correctly using the Gantt procedure. (See [Example 4.28](#)).

## OUT= Schedule Data Set

The Schedule data set always contains the variables in the Activity data set that are listed in the **TAILNODE**, **HEADNODE**, **ACTIVITY**, **SUCCESSOR**, **DURATION**, and **ID** statements. If the **INTPER=** option is specified in the PROC CPM statement, then the values of the **DURATION** variable in the Schedule data set are obtained by multiplying the corresponding values in the Activity data set by *intper*. Thus, the values in the Schedule data set are the durations used by PROC CPM to compute the schedule. If the procedure is used without specifying a **RESOURCEIN=** data set and only the unconstrained schedule is obtained, then the Schedule data set contains six new variables named **E\_START**, **L\_START**, **E\_FINISH**, **L\_FINISH**, **T\_FLOAT**, and **F\_FLOAT**.

If a resource-constrained schedule is obtained, however, the Schedule data set contains two new variables named **S\_START** and **S\_FINISH**; the **T\_FLOAT** and **F\_FLOAT** variables are omitted. You can request the omission of the **E\_START** and **E\_FINISH** variables by specifying **NOE\_START** and the omission of the **L\_START** and **L\_FINISH** variables by specifying **NOL\_START** in the **RESOURCE** statement. The variables listed in the **RESOURCE** statement are also included in the Schedule data set; to omit them, use the **NORESOURCEVARS** option in the **RESOURCE** statement. If the **DELAYANALYSIS** option is specified, the Schedule data set also includes the variables **R\_DELAY**, **DELAY\_R** and **SUPPL\_R**.

If resource-driven durations or resource calendars are in effect, the start and finish times shown in the Schedule data set are computed as the minimum of the start times for all resources for that activity and the maximum of the finish times for all resources for that activity, respectively. For details see the section “[Resource-Driven Durations and Resource Calendars](#)” on page 112.

If an **ACTUAL** statement is specified, the Schedule data set also contains the four variables **A\_START**, **A\_FINISH**, **A\_DUR**, and **STATUS**.

The format of the schedule variables in this data set (namely, **A\_START**, **A\_FINISH**, **E\_START**, **E\_FINISH**, **L\_START**, and so on) is consistent with the format of the **DATE=** specification and the **INTERVAL=** option in the PROC CPM statement.

### Definitions of Variables in the OUT= Data Set

Each observation in the Schedule data set is associated with an activity. The variables in the data set have the following meanings.

#### **A\_DUR**

specifies the actual duration of the activity. This variable is included in the Schedule data set only if the **ACTUAL** statement is used. The value for this variable is missing unless the activity is completed and may be different from the duration of the activity as specified by the **DURATION** variable. It is based on the values of the progress variables. See the section “[Progress Updating](#)” on page 109 for further details.

**A\_FINISH**

specifies the actual finish time of the activity, either as specified in the Activity data set or as computed by PROC CPM on the basis of the progress variables specified. This variable is included in the Schedule data set only if the **ACTUAL** statement is used.

**A\_START**

specifies the actual start time of the activity, either as specified in the Activity data set or as computed by PROC CPM on the basis of the progress variables specified. This variable is included in the Schedule data set only if the **ACTUAL** statement is used.

**E\_FINISH**

specifies the completion time if the activity is started at the early start time.

**E\_START**

specifies the earliest time the activity can be started. This is the maximum of the *maximum* early finish time of all predecessor activities and any lower bound placed on the start time of this activity by the alignment constraints.

**F\_FLOAT**

specifies the free float time, which is the difference between the early finish time of the activity and the minimum early start time of the activity's immediate successors. Consequently, it is the maximum delay that can be tolerated in the activity without affecting the scheduling of a successor activity. The values of this variable are calculated in units of the INTERVAL= parameter.

**L\_FINISH**

specifies the latest completion time of the activity. This is the minimum of the *minimum* late start time of all successor activities and any upper bound placed on the finish time of the activity by the alignment constraints.

**L\_START**

specifies the latest time the activity can be started. This is computed from the activity's latest finish time.

**S\_FINISH**

specifies the resource-constrained finish time of the activity. If resources are insufficient and the procedure cannot schedule the activity, the value is set to missing, unless the FILLUNSCHED option is specified.

**S\_START**

specifies the resource-constrained start time of the activity. If resources are insufficient and the procedure cannot schedule the activity, the value is set to missing, unless the FILLUNSCHED option is specified.

**STATUS**

specifies the current status of the activity. This is a character valued variable. Possible values for the status of an activity are *Completed*, *In Progress*, *Infeasible* or *Pending*; the meanings are self-evident. If the project is scheduled subject to resource constraints, activities that are *Pending* are classified as *Pending* or *Infeasible* depending on whether or not PROC CPM is able to determine a resource-constrained schedule for the activity.

### T\_FLOAT

specifies the total float time, which is the difference between the activity late finish time and early finish time. Consequently, it is the maximum delay that can be tolerated in performing the activity and still complete the project on schedule. An activity is said to be on the critical path if T\_FLOAT=0. The values of this variable are calculated in units of the INTERVAL= parameter.

If activity splitting is allowed during resource-constrained scheduling, the Schedule data set may contain more than one observation corresponding to each observation in the Activity data set. It will also contain the variable SEGMENT\_NO, which is explained in the section “[Activity Splitting](#)” on page 122.

If the PROJECT statement is used, some additional variables are added to the output data set. See the section “[Schedule Data Set](#)” on page 134 for details.

## Multiple Calendars

Work pertaining to a given activity is assumed to be done according to a particular *calendar*. A calendar is defined here in terms of a work pattern for each day and a work week structure for each week. In addition, each calendar may have holidays during a given year.

You can associate calendars with Activities (using the CALID variable in the [Activity](#) data set) or Resources (using observations with the keyword ‘CALENDAR’ for the OBSTYPE variable in the Resource data set).

PROC CPM enables you to define very general calendars using the WORKDATA, CALEDDATA, and HOLIDATA data sets and options in the PROC CPM statement. Recall that these data sets are referred to as the Workday, Calendar, and Holiday data sets, respectively. The Workday data set specifies distinct shift patterns during a day. The Calendar data set specifies a typical work week for any given calendar; for each day of a typical week, it specifies the shift pattern that is followed. The Holiday data set specifies a list of holidays and the calendars that they refer to; holidays are defined either by specifying the start of the holiday and its duration in *interval* units, or by specifying the start and end of the holiday period. The Activity data set (the DATA= input data set) then specifies the calendar that is used by each activity in the project through the CALID variable (or a default variable \_CAL\_). Each of the three data sets used to define calendars is described in greater detail later in this section.

Each new value for the CALID variable in either the Calendar data set or the Holiday data set defines a new calendar. If a calendar value appears in the Calendar data set and not in the Holiday data set, it is assumed to have the same holidays as the default calendar (the default calendar is defined later in this section). If a calendar value appears in the Holiday data set and not in the Calendar data set, it is assumed to have the same work pattern structures (for each week and within each day) as the default calendar. In the Activity data set, valid values for the CALID variable are those that are defined in either the Calendar data set or the Holiday data set.

### Cautions

The Holiday, Calendar, and Workday data sets and the processing of holidays and different calendars are supported only when *interval* is DAY, WEEKDAY, DTDAY, WORKDAY, DTWRKDAY, DTHOUR, DTMINUTE, or DTSECOND. PROC CPM uses default specifications whenever some information required to define a calendar is missing or invalid. The defaults have been chosen to provide consistency among different types of specifications and to correct for errors in input, while maintaining compatibility with

earlier versions of PROC CPM. You get a wide range of control over the calendar specifications, from letting PROC CPM define a single calendar entirely from defaults, to defining several calendars of your choice with precisely defined work patterns for each day of the week and for each week. If the Calendar, Workday, and Holiday data sets are used along with multiple calendar specifications, it is important to remember how all of the data sets and the various options interact to form the work patterns for the different calendars.

## Default Calendar

The default calendar is a special calendar that is defined by PROC CPM; its definition and uses are explained in this subsection.

If there is no CALID variable and no Calendar and Workday data sets, the default calendar is defined by *interval* and the DAYSTART= and DAYLENGTH= options in the PROC CPM statement. If *interval* is DAY, DT DAY, DT HOUR, DT MINUTE or DT SECOND, work is done on all seven days of the week; otherwise, Saturday and Sunday are considered to be non-working days. Further, if the schedule is computed as SAS datetime values, the length of the working day is determined by *daystart* and *daylength*. All of the holidays specified in the Holiday data set refer to this default calendar, and all of the activities in the project follow it. Thus, if there is no CALID variable, the default calendar is the only calendar that is used for all of the activities in the project.

If there is a CALID variable that identifies distinct calendars, you can use an observation in the Calendar data set to define the work week structure for the default calendar. Use the value ‘0’ (if CALID is a numeric variable) or the value ‘DEFAULT’ (if CALID is a character variable) to identify the default calendar. In the absence of such an observation, the default calendar is defined by *interval*, *daystart*, and *daylength*, as described earlier. The default calendar is used to substitute default work patterns for missing values in the Calendar data set or to set default work week structures for newly defined calendars in the Holiday data set.

## WORKDATA Data Set

All numeric variables in the Workday data set are assumed to denote unique shift patterns during one working day. For each variable the observations specify, alternately, the times when consecutive shifts start and end. Suppose S1, S2, and S3 are numeric variables formatted as TIME6. Consider the following Workday data:

S1	S2	S3
7:00	.	7:00 (start)
11:00	08:00	11:00 (end)
12:00	.	.
16:00	.	(start)
	.	(end)

The variables S1, S2, and S3 define three different work patterns. A missing value in the first observation is assumed to be 0 (or 12:00 midnight); a missing value in any other observation is assumed to denote 24:00 and ends the definition of the shift. Thus, the workdays defined are:

- S1 defines a workday starting at 7:00 a.m. and continuing until 4:00 p.m. with an hour off for lunch from 11:00 a.m. until 12:00 noon.

- S2 defines a workday from midnight to 8:00 a.m.
- S3 defines a workday from 7:00 a.m. to 11:00 a.m.

The last two values for the variables S2 and S3 (both values are ‘24:00’, by default) are ignored. This data set can be used to define all of the unique shift patterns that occur in any of the calendars in the project. These shift patterns are tied to the different calendars in which they occur using the Calendar data set.

## CALEDATA Data Set

The Calendar data set defines specific calendars using the names of the shift variables in the Workday data set. You can use the variable specified in the CALID statement or a variable named \_CAL\_ to identify the calendar name or number. Character variables named \_SUN\_, \_MON\_, \_TUE\_, \_WED\_, \_THU\_, \_FRI\_, and \_SAT\_ are used to indicate the work pattern that is followed on each day of the week. Valid values for these variables are ‘HOLIDAY’, ‘WORKDAY’ or, any shift variable name defined in the Workday data set.

**NOTE:** A missing value for any of these variables is assumed to denote that the work pattern for the corresponding day is the same as for the default calendar.

When *interval* is specified as DTDAY, WORKDAY, or DTWRKDAY, it is necessary to know the length of a *standard* working day in order to be able to compute the schedules consistently. For example, a given calendar may have an eight-hour day on Monday, Tuesday, and Wednesday and a seven-hour day on Thursday and Friday. If a given activity following that calendar has a duration of four days, does it mean that its duration is equal to  $8 \times 4 = 32$  hours or  $7 \times 4 = 28$  hours? To avoid ambiguity, a numeric variable named D\_LENGTH can be specified in the Calendar data set to define the length of a standard working day for the specified calendar. If this variable is not found in the Calendar data set, all calendars for the project are assumed to have a standard daylength as defined by the default calendar.

For example, consider the following Calendar data:

<u>CAL</u>	<u>SUN</u>	<u>MON</u>	<u>TUE</u>	<u>FRI</u>	<u>SAT</u>	<u>D_LENGTH</u>
1	HOLIDAY	S1	S1	S2	S3	8:00
2	HOLIDAY	.	.	.	HOLIDAY	.
3	.	.	.	.	.	.

These three observations define three calendars: ‘1’, ‘2’, and ‘3’. The values ‘S1’, ‘S2’, and ‘S3’ refer to the shift variables defined in the section “**WORKDATA Data Set**” on page 102. Activities in the project can follow either of these three calendars or the default calendar.

Suppose *daystart* has been specified as 9:00 a.m. and *daylength* is eight hours. Further, suppose that *interval* is DTDAY. Using these parameter specifications, PROC CPM defines the default calendar and calendars 1, 2 and 3 using the Calendar data set just defined:

- The default calendar (not specified explicitly in the Calendar data set) is defined using *interval*, *daystart*, and *daylength*. It follows a seven-day week with each day being an eight-hour day (from 9:00 a.m. to 5:00 p.m.). Recall that the default calendar is defined to have seven or five working days depending on whether *interval* is DTDAY or WORKDAY, respectively.

- Calendar ‘1’ (defined in observation 1) has a holiday on Sunday; on Monday and Tuesday work is done from 7:00 a.m. to 11:00 a.m. and then from 12:00 noon to 4:00 p.m.; work on Friday is done from 12:00 (midnight) to 8:00 a.m.; work on Saturday is done from 7:00 a.m. to 11:00 a.m.; on other days work is done from 9:00 a.m. to 5:00 p.m., as defined by the default calendar. The value of D\_LENGTH specifies the number of hours in a standard work day; when durations of activities are specified in terms of number of workdays, then the value of D\_LENGTH is used as a multiplier to convert workdays to the appropriate number of hours.
- Calendar ‘2’ (defined in observation 2) has holidays on Saturday and Sunday, and on the remaining days, it follows the standard working day as defined by the default calendar.
- Calendar ‘3’ (defined in observation 3) follows the same definition as the default calendar.

**NOTE:** If there are multiple observations in the Calendar data set identifying the same calendar, all except the first occurrence are ignored. The value ‘0’ (if CALID is a numeric variable) or the value ‘DEFAULT’ (if CALID is a character variable) refers to the default calendar. A missing value for the CALID variable is also assumed to refer to the default calendar. The Calendar data set can be used to define the default calendar also.

## HOLIDATA Data Set

The HOLIDATA data set (referred to as the Holiday data set) defines holidays for the different calendars that may be used in the project. Holidays are specified by using the **HOLIDAY** statement. See the **HOLIDAY** statement earlier in this chapter for a description of the syntax. This data set must contain a variable (the HOLIDAY variable) whose values specify the start of each holiday. Optionally, the data set may also contain a variable (the HOLIDUR variable) used to specify the length of each holiday or another variable (the HOLIFIN variable) specifying the finish time of each holiday. The variable specified by the **CALID** statement (or a variable named **\_CAL\_**) can be used in this data set to identify the calendar to which each holiday refers. A missing value for the HOLIDAY variable in an observation causes that observation to be ignored. If both the HOLIDUR and the HOLIFIN variables have missing values in a given observation, the holiday is assumed to start at the date and time specified for the HOLIDAY variable and last one unit of *interval* where the INTERVAL= option has been specified as *interval*. If a given observation has valid values for both the HOLIDUR and HOLIFIN variables, only the HOLIFIN variable is used so that the holiday is assumed to start and end as specified by the HOLIDAY and HOLIFIN variables, respectively. A missing value for the CALID variable causes the holiday to be included in all of the calendars, including the default.

The HOLIDUR variable is a natural way of expressing vacation times as *n workdays*, and the HOLIFIN variable is more useful for defining standard holiday periods, such as the CHRISTMAS holiday from 24DEC03 to 26DEC03 (both days inclusive). The HOLIDUR variable is assumed to be in units of *interval* and the procedure uses the particular work pattern structure for the given calendar to compute the length (finish time) of the holiday.

For example, consider the following Holiday data:

HOLISTA	HOLIDUR	HOLIFIN	<u>CAL</u>
24DEC03	.	26DEC03	.
01JAN04	1	.	1
19JAN04	.	.	2
29JAN04	3	.	2
29JAN04	3	.	3

Suppose calendars ‘1’, ‘2’, and ‘3’ and the default calendar have been defined as described earlier in the description of the Calendar and Workday data sets. Recall that in this example INTERVAL=DTDAY, DAYSTART=‘09:00’T, and DAYLENGTH=‘08:00’T. Because the schedule is computed as SAS datetime values (since INTERVAL=DTDAY), the holiday values (specified here as SAS date values) are converted to SAS datetime values. The first observation in the Holiday data set has a missing value for CAL and, hence, the holiday in this observation pertains to all the calendars. As defined by the Holiday data, the holiday lists for the different calendars (not including breaks due to shift definitions) are as shown in [Table 4.7](#).

Even though both calendars ‘2’ and ‘3’ have the same specifications for HOLISTA and HOLIDUR, the actual holiday periods are different for the two calendars. For calendar ‘2’, the three days starting from Thursday, January 29, imply that the holidays are on Thursday, Friday, and Monday (because Saturday and Sunday are already holidays). For calendar ‘3’ (all seven days are working days), the holidays are on Thursday, Friday, and Saturday.

**Table 4.7** Holiday Definitions

Calendar	Holiday Start	Holiday End
0	24DEC03:09:00	26DEC03:16:59:59
1	24DEC03:09:00	26DEC03:07:59:59
	01JAN04:00:00	01JAN04:07:59:59
2	24DEC03:09:00	26DEC03:16:59:59
	19JAN04:09:00	19JAN04:16:59:59
	29JAN04:09:00	02FEB04:16:59:59
3	24DEC03:09:00	26DEC03:16:59:59
	29JAN04:09:00	31JAN04:16:59:59

You can use the GANTT procedure to visualize the breaks and holidays for the different calendar. [Figure 4.4](#) shows all the breaks and holidays for the period between Christmas and New Year. Holidays and breaks are denoted by \*. Likewise, [Figure 4.5](#) shows the vacation periods in January for calendars ‘2’ and ‘3’.

**Figure 4.4** Christmas and New Year Holidays for Multiple Calendars

### Christmas and New Year Holidays

	DEC 22	DEC 22	DEC 23	DEC 23	DEC 24	DEC 24
<u>_cal_</u>	00:00	12:00	00:00	12:00	00:00	12:00
	-+-----+-----+-----+-----+-----+-----+					
0	*****-----*****-----*****-----*****					
1	*****-----*-----*****-----*-----*****					
2	*****-----*****-----*****-----*****					
3	*****-----*****-----*****-----*****					
	-+-----+-----+-----+-----+-----+-----+					

### Christmas and New Year Holidays

DEC 24	DEC 25	DEC 25	DEC 26	DEC 26	DEC 27	DEC 27
12:00	00:00	12:00	00:00	12:00	00:00	12:00
	-+-----+-----+-----+-----+-----+-----+					
	*****-----*****-----*****-----*****-----					
	*****-----*****-----*****-----*****-----**					
	*****-----*****-----*****-----*****-----					
	*****-----*****-----*****-----*****-----					
	-+-----+-----+-----+-----+-----+-----+					

**Figure 4.4** *continued*

**Christmas and New Year Holidays**

DEC 27	DEC 28	DEC 28	DEC 29	DEC 29	DEC 30	DEC 30
12:00	00:00	12:00	00:00	12:00	00:00	12:00
<pre> -+-----+-----+-----+-----+-----+-----+-----+   -----*****-----  -----*****-----  -----*****-----    *****-----*****-----*****-----*****-----*     *****-----*****-----*****-----*****-----*     *****-----*****-----*****-----*****-----*     -----*****-----  -----*****-----  -----*****-----  -+-----+-----+-----+-----+-----+-----+-----+ </pre>						

**Christmas and New Year Holidays**

DEC 30	DEC 31	DEC 31	JAN 01	JAN 01	JAN 02	JAN 02
12:00	00:00	12:00	00:00	12:00	00:00	12:00
<pre> -+-----+-----+-----+-----+-----+-----+-----+   -----*****-----  -----*****-----  -----*****-----    -----*****-----  -----*****-----  -----*****-----****    -----*****-----  -----*****-----  -----*****-----*     -----*****-----  -----*****-----  -----*****-----*     -----*****-----  -----*****-----  -----*****-----*   -+-----+-----+-----+-----+-----+-----+-----+ </pre>						

**Figure 4.5** Vacation Time for Calendars 2 and 3**Vacation Times for Calendars 2 and 3**

JAN	JAN	JAN	JAN	JAN	JAN	JAN
18	18	19	19	20	20	21
<u>_cal_</u>	00:00	12:00	00:00	12:00	00:00	12:00

**Vacation Times for Calendars 2 and 3**

| JAN   |
|-------|-------|-------|-------|-------|-------|-------|-------|
| 21    | 21    | 22    | 22    | 23    | 23    | 24    | 24    |
| 00:00 | 12:00 | 00:00 | 12:00 | 00:00 | 12:00 | 00:00 | 12:00 |
|       |       |       |       |       |       |       |       |

**Vacation Times for Calendars 2 and 3**

| JAN   |
|-------|-------|-------|-------|-------|-------|-------|-------|
| 24    | 25    | 25    | 26    | 26    | 27    | 27    | 28    |
| 12:00 | 00:00 | 12:00 | 00:00 | 12:00 | 00:00 | 12:00 | 00:00 |
|       |       |       |       |       |       |       |       |

**Figure 4.5** *continued***Vacation Times for Calendars 2 and 3**

JAN 28 00:00	JAN 28 12:00	JAN 29 00:00	JAN 29 12:00	JAN 30 00:00	JAN 30 12:00	JAN 31 00:00	JAN 31 12:00
--------------------	--------------------	--------------------	--------------------	--------------------	--------------------	--------------------	--------------------

-+-----+-----+-----+-----+-----+-----+-----+

|\*\*\*\*\*|-----|\*\*\*\*\*|-----|\*\*\*\*\*|-----|\*\*\*\*\*|-----|

|\*\*\*\*\*|-----|\*\*\*\*\*|-----|\*\*\*\*\*|-----|\*\*\*\*\*|-----|

-+-----+-----+-----+-----+-----+-----+-----+

**Vacation Times for Calendars 2 and 3**

JAN 31 12:00	FEB 01 00:00	FEB 01 12:00	FEB 02 00:00	FEB 02 12:00	FEB 03 00:00	FEB 03 12:00	FEB 04 00:00
--------------------	--------------------	--------------------	--------------------	--------------------	--------------------	--------------------	--------------------

-+-----+-----+-----+-----+-----+-----+-----+

|\*\*\*\*\*|-----|\*\*\*\*\*|-----|\*\*\*\*\*|-----|\*\*\*\*\*|-----|

|\*\*\*\*\*|-----|\*\*\*\*\*|-----|\*\*\*\*\*|-----|\*\*\*\*\*|-----|

-+-----+-----+-----+-----+-----+-----+-----+

**Baseline and Target Schedules**

An important aspect of project management is to examine the effects of changing some of the parameters of the project on project completion time. For example, you may want to examine different scenarios by changing the durations of some of the activities, or increasing or decreasing the resource levels. To see the effect of these changes, you need to compare the schedules corresponding to the changes. The **BASELINE** statement enables you to save a particular schedule as a target schedule and then compare a new schedule against that. See the section “**BASELINE Statement**” on page 74 for a description of the syntax.

**Progress Updating**

Once a project has been defined with all of its activities and their relationships, the durations, the resources needed, and so on, it is often useful to monitor its progress periodically. During resource-constrained

scheduling, it is useful to schedule only activities that have not yet started, taking into consideration the activities that have already been completed or scheduled and the resources that have already been used by them or allotted for them. The **ACTUAL** statement is used in PROC CPM to convey information about the current status of a project. As information about the activities becomes available, it can be incorporated into the schedule of the project through the specification of the actual start or finish times or both, the duration that is still remaining for the activity, or the percentage of work that has been completed on an activity. The specification of the progress variables and the options in the **ACTUAL** statement have been described earlier in this chapter. This section describes how the options work together and how some default values are determined.

The following options are discussed in this section:

- the TIMENOW= option
- the AUTOUPDT and NOAUTOUPDT options
- the TIMENOWSPLT option
- the progress variables (A\_START, A\_FINISH, REMDUR, and PCTCOMP)

The TIMENOW= option is specified in the **ACTUAL** statement. The value of the TIMENOW= option (often referred to simply as TIMENOW) is used as a reference point to resolve the values of the remaining duration and percent completion times. All actual start and finish times specified are checked to ensure that they are less than TIMENOW. If there is some inconsistency, a warning message is printed to the log.

If the **ACTUAL** statement is used, at least one of the four progress variables must be specified. PROC CPM uses the nonmissing values for the progress variables in any given observation to determine the information that is to be used for the activity. It is possible that there are some inconsistencies in the specification of the values relating to the progress information. For example, an activity may have valid values for both the A\_START and the A\_FINISH variables and also have the value of the PCTCOMP variable less than 100. PROC CPM looks at the values in a specific order, resolving inconsistencies in a reasonable manner. Further, PROC CPM determines revised estimates of the durations of the activities on the basis of the actual information.

Suppose that for a given activity, *as* is the actual start, *af* is the actual finish, *remdur* is the remaining duration, *pctc* is the percent complete, and *dur* is the duration of the activity as specified by the values of the corresponding variables in the Activity data set. (If a particular variable is not specified, assume that the corresponding value is missing.)

The *elapsed duration* of an activity in progress is the time lapse between its actual start and TIMENOW; the *revised duration* of the activity is the *updated duration* of the activity that is used to calculate the projected finish time for activities in progress and the *actual duration* for activities that are completed. The *revised duration* is used by PROC CPM to compute the updated schedule as described later in this section. In the discussion that follows, *as*, *af*, *remdur*, and *pctc* refer to the *actual start time*, *actual finish time*, *remaining duration*, and *percent completed*, respectively, for the activity in the Activity data set, while A\_START, A\_FINISH, and A\_DUR refer to the values calculated by PROC CPM for the corresponding new variables added to the Schedule data set.

The following is a list of some of the conventions used by PROC CPM in calculating the *revised duration*:

- If both *as* and *af* are specified, the *revised duration* is computed as the time, excluding non-working periods, between *as* and *af*; in the Schedule data set, the variable A\_DUR is also set to this value; A\_START is set to *as* and A\_FINISH to *af*.
- If *as* is specified without *af*, PROC CPM uses *remdur* to compute the *revised duration* as the sum of the elapsed duration and the remaining duration.
- If *as* is specified and both *af* and *remdur* are missing, the *revised duration* is computed on the basis of the elapsed duration and *pctc*.
- If *as* is specified and *af*, *remdur* and *pctc* are not specified, the duration is not revised. If the time lapse between *as* and TIMENOW is greater than or equal to the duration of the activity, it is assumed to have finished at the appropriate time (*as* + *dur*) and the Schedule data set has the appropriate values for A\_START, A\_FINISH, and A\_DUR.
- If *as* is missing and *af* is valid, PROC CPM determines *as* on the basis of *af* and the specified duration (*remdur* and *pctc*, if specified, are ignored.)
- If *as* and *af* are both missing, the *revised duration* is determined on the basis of *remdur* and *pctc*. If the activity has started (if *pctc* > 0 or *remdur* < *dur*), *as* is set appropriately, and if it has also finished (which is the case if *pctc* = 100 or *remdur* = 0), *af* is also set.

Using the preceding rules, PROC CPM attempts to determine actual start and finish times for as many activities as possible using the information given for each activity. The next question is: What about activities that have missing values for the actual start and finish times? Suppose a given activity has a valid value for A\_START and is currently in progress. It seems logical for successors of this activity to have missing values for A\_START. But how about predecessors of the activity? If they have missing values for A\_START and A\_FINISH, does it mean that there was an error in the input of the actual dates or an error in the precedence constraints? The AUTOUPDT and NOAUTOUPDT options enable you to control the answer to this question. AUTOUPDT instructs CPM to automatically fill in appropriate A\_START and A\_FINISH values for all activities that precede activities which have already started. NOAUTOUPDT implies that only those activities that have explicit progress information confirming their status are assumed to be in progress or completed; all other activities are assumed to have an implicit start date that is greater than or equal to TIMENOW. In other words, NOAUTOUPDT assumes that the precedence constraints may be overridden by the actual data. The default option is AUTOUPDT.

The scheduling algorithm treats the actual start and finish times as follows:

- If A\_START is not missing, the E\_START time is set equal to A\_START during the forward pass, and the E\_FINISH time is set equal to E\_START + the *revised duration*.
- If A\_START is missing, the E\_START time is computed as before.
- If A\_FINISH or A\_START is not missing, the L\_FINISH time is set equal to A\_FINISH during the backward pass, and the L\_START time is computed on the basis of L\_FINISH and the *revised duration*.

This rule causes the late start schedule to be the same as the early start schedule for completed or in-progress activities. Thus, T\_FLOAT and F\_FLOAT are 0 for such activities. Use the SHOWFLOAT option if you want to allow nonzero float for in-progress or completed activities. In this case, the late start schedule is computed as before, using the precedence constraints, so that you can determine the degree of lateness for the activities that have already been completed or are in progress.

- If E\_START is less than TIMENOW for an activity (and thus it is also the same as A\_START), the activity is scheduled during resource allocation even if there are not enough resources (a warning message is printed to the log if this is the case). Thus, resource-constrained scheduling is done only for the period starting from TIMENOW.

**NOTE:** The resources required by activities that are completed or in progress are accounted for and the corresponding changes are made to the resource availability profile before starting the constrained scheduling process at TIMENOW.

- If resource-constrained scheduling is being performed, the TIMENOWSPLT option can be used. This option affects those activities that are currently in progress that cause resource infeasibilities. The TIMENOWSPLT option causes such activities to be split at TIMENOW into segments; the first segment is assumed to be complete before TIMENOW, and the second segment is delayed until sufficient resources are available.

The Schedule data set contains the actual start times (A\_START) for all activities that are in progress or completed and the actual finish times (A\_FINISH) and the actual duration times (A\_DUR) for all activities that are completed. Some of these values may have been derived from the percent completion or remaining duration times in the Activity data set or may have been implicitly determined through the AUTOUPDT option. Also included in the Schedule data set is a variable named STATUS describing the status of each activity. The possible values are *Completed*, *In Progress*, *Infeasible*, and *Pending*; the interpretations are self-evident.

If the ESTPCTC option is specified, the Schedule data set also contains a variable named PCT\_COMP that contains the percent completion time for each activity in the project.

## Resource-Driven Durations and Resource Calendars

The DURATION variable enables you to specify a fixed duration for an activity. The CPM procedure then assumes that all the resources for that activity are required throughout the duration of that activity; further, the activity is assumed to follow the work pattern specified by the activity's calendar. Suppose that there are multiple resources required by an activity, each following a different calendar and each requiring varying amounts of work. For example, a programming task may require 50 hours of a programmer's time and 20 hours of a tester's time. Further, the programmer may work full time on the tasks, while the tester, due to other commitments, may work only half time on the same activity. The scheduling could be further complicated if the tester and the programmer followed different calendars. Situations of this type can be modeled using resource-driven durations and resource calendars.

The WORK variable in the Activity data set specifies the *total* amount of work required by one unit of a resource. Unlike the DURATION variable, which represents a fixed duration for an activity for all its resources, the WORK variable *drives* the duration for each resource required by the activity using the resource rate specified. You can specify different amounts of work for different resources by using different observations to specify rates and total work for the different resources. Consider the following data from an Activity data set:

ACT	WORK	PGMR	TESTER
1	50	1	.
1	20	.	.5
2	15	1	1

PGMR and TESTER are resource variables specifying the rate at which the respective resource is required (used) for the particular activity; WORK specifies the total number of hours (assuming that the INTERVAL parameter has been specified as HOUR) of work required by each resource that has a rate specified in that observation. Thus, Activity ‘1’ requires 50 hours of the resource PGMR and 20 hours of the resource TESTER, while activity ‘2’ requires 15 hours of each of the two resources. Using the rates for the resources specified in the preceding data, the procedure determines the resource durations for activity 1 to be 50 hours for PGMR and 40 hours for TESTER. Likewise, the resource durations for both resources are 15 hours for activity 2.

In the forward and backward pass calculations, the procedure computes the schedules for each resource and sets the activity’s start (finish) time to be the minimum (maximum) of the start (finish) times for all the resources.

Some activities may have a fixed duration for some resources and a resource-driven duration for other resources. For such activities, use the DURATION variable to specify the fixed duration and the WORK variable to specify the total amount of work required for the activity. If a particular observation has values specified for both the WORK and DURATION variables, use the resource type information in the Resource data set (described in the section “[RESOURCEIN= Input Data Set](#)” on page 114) to determine if the resource *drives* the duration of the activity.

Recall that the CALID variable in the Activity data set specifies the calendar that is used by each activity in the project. In addition, you can also associate calendars with the resources in the project. Resource calendars are specified in the Resource data set. However, the CALID variable must be numeric for you to associate calendars with resources; in other words, the calendars must be identified by numbers and not names.

## Resource Usage and Allocation

Often the activities in a project use several resources. If you assume that these resources are available in unlimited quantities, then the only restrictions on the start and finish times of the activities in the project are those imposed by precedence constraints and dates specified for alignment of the activities. In most practical situations, however, there are limitations on the availability of resources; as a result, neither the early start schedule nor the late start schedule (nor any intermediate schedule for that matter) may be feasible. In such cases, the project manager is faced with the task of scheduling the activities in the project subject to constraints on resource availability in addition to the precedence constraints and constraints on the start and finish times of certain activities in the project. This problem is known as *resource allocation*.

You can use PROC CPM to schedule the activities in a project subject to resource constraints. To perform resource allocation, you must specify the resource requirements for each activity in the project and also specify the amount of resources available on each day under consideration. The resource requirements are given in the Activity data set, with the variable names identified to PROC CPM through the **RESOURCE** statement. The levels of resources available on different dates, as well as other information regarding the resources, such as the type of resource, the priority of the resource, and so forth, are obtained from the **RESOURCEIN=** data set.

Specifying resource requirements is described in detail in the section “[Specifying Resource Requirements](#)” on page 118, and the description of the format of the Resource data set is given in the section “[RESOURCEIN= Input Data Set](#)” on page 114, which follows. The section “[Scheduling Method](#)” on page 119 describes how you can use the **SCHEDRULE=** and **DELAY=** options (and other options) in conjunction with certain special observations in the Resource data set to control the process of resource allocation to suit your needs.

Subsequent sections describe the different scheduling rules, supplementary resources, activity splitting, progress updating, and alternate resources.

### **RESOURCEIN= Input Data Set**

The RESOURCEIN= data set (referred to as the Resource data set) contains all of the necessary information about the resources that are to be used by PROC CPM to schedule the project. Typically, the Resource data set contains the resource variables (numeric), a type identifier variable (character) that identifies the type of information in each observation, a period variable (numeric and usually a SAS time, date, or datetime variable), and a RESID variable that is used to specify *alternate resources* and *auxiliary resources*.

The value of the type identifier variable in each observation tells CPM how to interpret that observation. Valid values for this variable are RESLEVEL, RESTYPE, RESUSAGE, RESPRTY, SUPLEVEL, ALTPRTY, ALTRATE, RESRCDUR, CALENDAR, MULTALT, MINARATE, and AUXRES.

**Table 4.8** Type Identifier Variables

Type Identifier Keywords	Description	Values
'RESLEVEL'	Contains levels available for each resource from the time specified in the period variable.	Missing values are not allowed. For consumable resources, the observation indicates the total availability and for replenishable resources, the new level.
'RESTYPE'	Specifies the nature of the resources, i.e., if they are consumable, replenishable, replenishable aggregate or consumable aggregate resources.	1 = Replenishable 2 = Consumable 3 = Replenishable Aggregate 4 = Consumable Aggregate
'RESUSAGE'	Indicates a profile of usage for a consumable resource	0 = Resource used continuously at specified rate 1 = Resource required at the beginning of activity 2 = Resource used at the end of activity A missing value is treated as 0.
'RESPRTY'	Specifies that PROC CPM should sort the activities in the waiting list in the order of increasing values of the <i>resource priority</i> for the most important resource used by each activity.	Low values indicate high priority.
'SUPLEVEL'	Specifies the amount of extra resource available for use throughout the duration of the project.	
'RESRCDUR'	Specifies the effect of the resource on the activity's duration.	0 = Resource uses a fixed duration 1 = Driving resource 2 = Spanning resource
'CALENDAR'	Specifies the calendar that is followed by each resource. If no calendar is specified for a given resource, the relevant activity's calendar is used instead.	Requires the calendar variable in the Activity and other data sets to be numeric.

'MULTALT'	Indicates which resources can have multiple alternate resources.	0 = Multiple alternates not allowed 1 = Multiple alternates allowed
'MINARATE'	Indicates the minimum rate of substitution for each resource, whenever multiple alternates are used.	
'ALTRATE'	Specifies the rate of substitution of alternate resources when a resource has more than one substitute. Resource data set must have a RESID variable.	Lower value indicates higher priority. Missing values imply that the particular resource cannot be substituted.
'ALTPRTY'	Specifies the prioritization of the alternate resources when a resource has more than one substitution. Resource data set must have a RESID variable.	Lower values indicate higher priority.
'AUXRES'	Specifies the auxiliary resources that are needed for each primary resource. RESID variable specifies the name of the primary resource.	Value for each auxiliary resource indicates the rate at which it is required whenever the primary resource is used.

If the value of the type identifier variable in a particular observation is 'RESLEVEL', then that observation contains the levels available for each resource from the time specified in the period variable. Missing values are not allowed for the period variable in an observation containing the levels of the resources. For consumable resources, the observation indicates the *total availability* and *not the increase in the availability*. Likewise, for replenishable resources, the observation indicates the *new level* and *not the change in the level* of the resource.

Each resource can be classified as either consumable or replenishable. A consumable resource is one that is used up by the job (such as bricks or money), while a replenishable resource becomes available again once a job using it is over (such as manpower or machinery). If the value of the type identifier variable is 'RESTYPE', then that observation identifies the nature (consumable or replenishable) of the resource. The observation contains a value 1 for a replenishable resource and a value 2 for a consumable one. A missing value in this observation is treated as 1. In fact, if there is no observation in the Resource data set with the type identifier variable equal to 'RESTYPE', then all resources are assumed to be replenishable.

Sometimes, it may be useful to include resources in the project that are to be used only for aggregation purposes. You can indicate that a given resource is to be used for aggregation, and not for resource allocation, by specifying the values 3 or 4, depending on whether the resource is replenishable or consumable. In other words, use 3 for replenishable aggregate resources and 4 for consumable aggregate resources.

Consumable resources are assumed to be used continuously throughout the duration of the activity at the rate specified in the Activity data set (as described in the section "Specifying Resource Requirements" on page 118). For example, when you specify a rate of 100 per day for bricks, the CPM procedure assumes that the activity consumes bricks at the constant rate of 100 per day. Sometimes, you may wish to allocate all of the resource at the beginning or end of an activity. For example, you may pay an *advance* at the start of a contracted activity while the *full payment* is made when the activity is completed. You can indicate such a profile of usage for a consumable resource using the keyword 'RESUSAGE' for the value of the type identifier variable. Valid values for the resource variables in such an observation are 0, 1, and 2. A value

0 indicates that the resource is used continuously at the specified rate throughout the activity's duration, a value 1 indicates that the resource is required at the beginning of the activity, and a value 2 specifies that the resource is used at the end of the activity. A missing value in this observation is treated as 0.

One of the scheduling rules that can be specified using the SCEDRULE= option is RESPRTY, which requires ordering the resources according to some priority (details are given in the section “[Scheduling Rules](#)” on page 120). If this option is used, there must be an observation in the Resource data set with the type identifier variable taking the value ‘RESPRTY’. This observation specifies the ordering of the resources.

If the type identifier variable is given as ‘SUPLEVEL’, the observation denotes the amount of extra resource that is available for use throughout the duration of the project. This extra resource is used only if the activity cannot be scheduled without delaying it beyond its late start time. See the section “[Secondary Levels of Resources](#)” on page 121 for details about the use of supplementary levels of resources in conjunction with the DELAY= and ACTDELAY= options.

If the type identifier variable is specified as ‘ALTRATE’, ‘ALTPRTY’, or ‘AUXRES’, the Resource data set must also have a RESID variable that is used to identify the name of a resource for which the current observation lists the possible alternate resources or the required auxiliary resources. See the section “[Specifying Alternate Resources](#)” on page 123 and the section “[Auxiliary Resources](#)” on page 127 for details.

If the value of the type identifier variable is ‘RESRCDUR’, that observation specifies the effect of the resource on an activity's duration. Valid values for the resource variables in such an observation are 0, 1, and 2. A value 0 indicates that the resource uses a fixed duration (specified by the DURATION variable); in other words, the activity's duration is not affected by changing the rate of the resource. A value 1 indicates that the WORK variable for an activity specifies the total amount of work required by the resource that is used to calculate the time required by the resource to complete its work on that activity; such a resource is referred to as a *driving* resource. The value 2 indicates a third type of resource; such a resource (referred to as a *spanning* resource) is required throughout the activity's duration, no matter which resource is working on it. For example, an activity might require 10 percent of a “supervisor,” or the use of a particular room, throughout its duration. For such an activity, the duration used for the spanning resource is computed after determining the span of the activity for all the other resources.

If the value of the type identifier variable is ‘CALENDAR’, that observation specifies the calendar that is followed by each resource. If no calendar is specified for a given resource, the relevant activity's calendar is used instead. This use of the calendar requires that the calendar variable in the Activity and other data sets be numeric.

If the value of the type identifier variable is ‘MULTALT’, that observation indicates which resources can have multiple alternate resources. The value 1 for a resource variable in the observation indicates that multiple alternates are allowed for that resource, and a value 0 indicates that multiple alternates are not allowed. See the section “[Specifying Multiple Alternates](#)” on page 125 for details.

If the value of the type identifier variable is ‘MINARATE’, that observation indicates the minimum rate of substitution for each resource, whenever multiple alternates are used. The ‘MINARATE’ values specified in this observation are used only if the **MULTIPLEALTERNATES** option is specified or if the Resource data set has an observation with the type identifier value of ‘MULTALT’.

The period variable must have nonmissing values for observations specifying the levels of the resources (that is, with type identifier equal to ‘RESLEVEL’). However, the period variable does not have any meaning when the type identifier variable has any value other than ‘RESLEVEL’; if the period variable has nonmissing

values in these observations, it is ignored. The Resource data set must be sorted in order of *increasing* values of the period variable.

Multiple observations are allowed for each type of observation. If there is a conflict in the values specified, only the first nonmissing value is honored; for example, if there are two observations of the type 'RESTYPE' and a resource variable has value 1 in the first and 2 in the second of these observations, the resource type is assumed to be 1 (replenishable). On the other hand, if the value is missing in the first observation but set to 2 in the second, the resource type is assumed to be 2 (consumable).

A resource is available at the specified level from the time given in the first observation with a nonmissing value for the resource. Its level changes (to the new value) whenever a new observation is encountered with a nonmissing value, and the date of change is the date specified in this observation.

The following examples illustrate the details about the Resource data set. Consider the following Resource data:

OBS	OBSTYPE	DATE	WORKERS	BRICKS	PAYMENT	ADVANCE
1	RESTYPE	.	1	2	2	2
2	RESUSAGE	.	.	0	2	1
3	RESPRTY	.	10	10	10	10
4	SUPLEVEL	.	1	.	.	.
5	RESLEVEL	1JUL04	.	1000	2000	500
6	RESLEVEL	5JUL04	4	.	.	.
7	RESLEVEL	9JUL04	.	1500	.	.

There are four resources in these data, WORKERS, BRICKS, PAYMENT, and ADVANCE. The variable OBSTYPE is the type identifier, and the variable DATE is the period variable. The first observation (because OBSTYPE has value 'RESTYPE') indicates that WORKERS is a replenishable resource while the other three resources are consumable. The second observation indicates the usage profile for the consumable resources: the resource BRICKS is used continuously throughout the duration of an activity, while the resource PAYMENT is required at the end of the activity and the resource ADVANCE is needed at the start of the activity. The third observation indicates that all the resources have equal priority. In the fourth observation, a value '1' under WORKERS indicates that a supplementary level of 1 worker is available if necessary, while no reserve is available for the resources BRICKS, PAYMENT, and ADVANCE.

The next three observations indicate the resource availability profile. The resource WORKERS is unavailable until July 5, 2004, when the level jumps from 0 to 4 and remains at that level through the end of the project. The resource BRICKS is available from July 1, 2004, at level 1000, while the resource levels for PAYMENT, and ADVANCE are 2000 and 500, respectively. On July 9, an additional 500 bricks are made available to increase the total availability to 1500. Missing values in observations 5 and 6 indicate that there is no change in the availability for the respective resources.

As another example, suppose that you want to treat BRICKS as an aggregate resource (one that is not to be included in resource allocation). Then consider the following data from a Resource data set:

OBSTYPE	BRICKS	PAINTER	SUPERV
RESTYPE	4	1	1
RESRCDUR	0	1	2
CALENDAR	1	0	0

The first observation indicates that the resource BRICKS is consumable and is to be used only for aggregation while the other two resources are replenishable and are to be treated as constrained resources during resource allocation.

The second observation, with the keyword ‘RESRCDUR’, specifies the effect of the resource on an activity’s duration. The value ‘0’ for the resource BRICKS implies that this resource does not affect the duration of an activity. On the other hand, the value ‘1’ identifies the resource PAINTER as a driving resource; this means that by increasing the number of painters, an activity’s duration can be decreased. The procedure uses this information about the nature of the resource only if a particular observation in the Activity data set has valid values for both the WORK and DURATION variables. Otherwise, if you specify a value only for the WORK variable, the procedure assumes that the resource specifications in that observation drive the activity’s duration. Likewise, if you specify a value only for the DURATION variable, the procedure assumes that the resources specified in that observation require a fixed duration.

In the Resource data set specifications, the second observation also identifies the resource SUPERV to be of the spanning type. In other words, such a resource is required by an activity whenever any of the other resources are working on the same activity. Thus, if you add more painters to an activity, thereby reducing its duration, the supervisor (a spanning resource) will be needed for a shorter time.

The third observation indicates the calendar to be used in calculating the activity’s start and finish times for the particular resource. If you do not specify a calendar, the procedure uses the activity’s calendar.

## Specifying Resource Requirements

To perform resource allocation or to summarize the resource utilization, you must specify the amount of resources required by each activity. In this section, the format for this specification is described. The amount required by each activity for each of the resources listed in the RESOURCE statement is specified in the Activity data set. The requirements for each activity are assumed to be constant throughout the activity’s duration. A missing value for a resource variable in the Activity data set indicates that the particular resource is not required for the activity in that observation.

The interpretation of the specification depends on whether or not the resource is replenishable. Suppose that the value for a given resource variable in a particular observation is ‘x’. If the resource is *replenishable*, it indicates that x units of the resource are required throughout the duration of the activity specified in that observation. On the other hand, if the resource is *consumable*, it indicates that the specified resource is consumed at the rate of x units per unit *interval*, where *interval* is the value specified in the INTERVAL= option in the PROC CPM statement. For example, consider the following specification:

OBS	ACTIVITY	DUR	WORKERS	BRICKS
1	A	5	.	100
2	B	4	2	.

Here, ACTIVITY denotes the activity under consideration, DUR is the duration in days (assuming that INTERVAL=DAY), and the resource variables are WORKERS and BRICKS. A missing value for WORKERS in observation 1 indicates that activity ‘A’ does not need the resource WORKERS, while the same is true for the resource BRICKS and activity ‘B’. You can assume that the resource WORKERS has been identified as replenishable, and the resource BRICKS has been identified as consumable in a Resource data set. Thus, a value ‘100’ for the consumable resource BRICKS indicates that 100 bricks per day are required for each of the 5 days of the duration of activity ‘A’, and a value ‘2’ for the replenishable resource WORKERS indicates that 2 workers are required throughout the duration (4 days) of activity ‘B’. Recall that consumable resources can

be further identified as having a special usage profile, indicating that the requirement is only at the beginning or end of an activity. See the section “[Variable Usage Profile for Consumable Resources](#)” on page 130 for details.

## Negative Resource Requirements

The CPM procedure enables you to specify negative resource requirements. A negative requirement indicates that a resource is *produced* instead of *consumed*. Typically, this interpretation is valid only for consumable resources. For example, a brick-making machine may produce bricks at the rate of 1000 units per hour which are then available for consumption by other tasks in the project. To indicate that a resource is produced (and not consumed) by an activity, specify the rate of usage for the resource as a negative number. For example, to indicate that a machine produces boxed cards at the rate of 5000 boxes per day, set the value of the resource, NUMBOXES, to -5000.

## Scheduling Method

PROC CPM uses the serial-parallel (serial in time and parallel in activities) method of scheduling. In this section, the basic scheduling algorithm is described. (Modifications to the algorithm if an [ACTUAL](#) statement is used, if activity splitting is allowed, or if alternate resources are specified, are described later.) The basic algorithm proceeds through the following steps:

1. An initial tentative schedule describing the early and late start and finish times is determined without taking any resource constraints into account. This schedule does, however, reflect any restrictions placed on the start and finish times by the use of the [ALIGNDATE](#) and [ALIGNTYPE](#) statements. As much as possible, PROC CPM tries to schedule each activity to start at its E\_START time (*e\_start*, as calculated in this step). Set *time*=min(*e\_start*), where the minimum is taken over all the activities in the network.
2. All of the activities whose *e\_start* values coincide with *time* are arranged in a waiting list that is sorted according to the rule specified in the [SCEDRULE=](#) option. (See the section “[Scheduling Rules](#)” on page 120 for details about the valid values of this option.) The [SCEDRULE2=](#) option can be used to break ties. PROC CPM tries to schedule the activities in the same order as on this list. For each activity the procedure checks to see if the required amount of each resource will be available throughout the activity’s duration; if enough resources are available, the activity is scheduled to start at *time*. Otherwise, the resource availability profile is examined to see if there is likely to be an increase in resources in the future. If none is perceived until *l\_start + delay*, the procedure tries to schedule the activity to start at *time* using supplementary levels of the resources (if there is an observation in the Resource data set specifying supplementary levels of resources); otherwise, it is postponed. (Note that if the [AWAITDELAY](#) option is specified, and there are not enough resources at *time*, the activity is not scheduled at *time* using supplementary resources). If *time* is equal to or greater than the value of *l\_start + delay*, and the activity cannot be scheduled (even using supplementary resources), PROC CPM stops with an error message, giving a partial schedule. You can also specify a cut-off date (using the [STOPDATE=](#) option) when resource constrained scheduling is to stop.

Once an activity that uses a supplementary level of a replenishable resource is over, the supplementary level that was used is returned to the reservoir and is not used again until needed. For consumable resources, if supplementary levels were used on a particular date, PROC CPM attempts to bring the reservoir back to the original level at the earliest possible time. In other words, the next time the primary availability of the resource increases, the reservoir is first used to replenish the supplementary

level of the resource. (See Example 4.16, “Using Supplementary Resources”). Adjustment is made to the resource availability profile to account for any activity that is scheduled to start at *time*.

3. All of the activities in the waiting list that were unable to be scheduled in Step 2 are postponed and are tentatively scheduled to start at the time when the next change takes place in the resource availability profile (that is, their *e\_start* is set to the next change date in the availability of resources). *time* is advanced to the minimum *e\_start* time of all unscheduled activities.

Steps 1, 2, and 3 are repeated until all activities are scheduled or the procedure stops with an error message.

Some important points to keep in mind are:

- Holidays and other non-working times are automatically accounted for in the process of resource allocation. Do not specify zero availabilities for the resources on holidays; PROC CPM accounts for holidays and weekends during resource allocation just as in the unrestricted case.
- It is assumed that the activities cannot be interrupted once they are started, unless one of the splitting options is used. See the section “[Activity Splitting](#)” on page 122 for details.

## Scheduling Rules

The SCHEDRULE= option specifies the criterion to use for determining the order in which activities are to be considered while scheduling them subject to resource constraints. As described in the section “[Scheduling Method](#)” on page 119, at a given time specified by *time*, all activities whose tentative *e\_start* coincides with *time* are arranged in a list ordered according to the scheduling rule, *schedrule*. The SCHEDRULE2= option can be used to break ties caused by the SCHEDRULE= option; valid values for *schedrule2* are the same as for *schedrule*. However, if *schedrule* is ACTPRTY, then *schedrule2* cannot be RESPRTY, and vice versa.

The following is a list of the six valid values of *schedrule*, along with a brief description of their respective effects.

### ACTPRTY

specifies that PROC CPM should sort the activities in the waiting list in the order of increasing values of the variable specified in the ACTIVITYPRTY= option in the [RESOURCE](#) statement. This variable specifies a user-assigned priority to each activity in the project (low value of the variable indicates high priority).

**NOTE:** If SCHEDRULE is specified as ACTPRTY, the [RESOURCE](#) statement must contain the specification of the variable in the Activity data set that assigns priorities to the activities; if the variable name is not specified through the ACTIVITYPRTY= option, then CPM ignores the specification for the SCHEDRULE= option and uses the default scheduling rule, LST, instead.

### DELAYLST

specifies that the activities in the waiting list are sorted in the order of increasing L\_START + ACTDELAY, where ACTDELAY is the value of the ACTDELAY variable for that activity.

### LFT

specifies that the activities in the waiting list are sorted in the order of increasing L\_FINISH time.

**LST**

specifies that the activities in the waiting list are sorted in the order of increasing L\_START time. Thus, this option causes activities that are closer to being critical to be scheduled first. This is the default rule.

**RESPRTY**

specifies that PROC CPM should sort the activities in the waiting list in the order of increasing values of the *resource priority* for the most important resource used by each activity. In order for this scheduling rule to be valid, there must be an observation in the Resource data set identified by the value RESPRTY for the type identifier variable and specifying priorities for the resources. PROC CPM uses these priority values (once again, low values indicate high priority) to order the activities; then, the activities in the waiting list are ordered according to the highest priority resource used by them. In other words, the CPM procedure uses the resource priorities to assign priorities to the activities in the project; these activity priorities are then used to order the activities in the waiting list (in increasing order). If this option is specified, and there is no observation in the Resource data set specifying the resource priorities, PROC CPM ignores the specification for the SCHDRULE= option and uses the default scheduling rule, LST, instead.

**SHORTDUR**

specifies that the activities in the waiting list are sorted in the order of increasing durations. Thus, PROC CPM tries to schedule activities with shorter durations first.

## Secondary Levels of Resources

There are two factors that you can use to control the process of scheduling subject to resource constraints: *time* and *resources*. In some applications, time is the most important factor, and you may be willing to use extra resources in order to meet project deadlines; in other applications, you may be willing to delay the project completion by an arbitrary amount of time if insufficient resources warrant doing so. The DELAY= and ACTDELAY= options and the availability of supplementary resources enable you to select either method or a combination of the two approaches.

In the first case, where you do not want the project to be delayed, specify the availability of supplementary resources in the Resource data set and set DELAY=0. In the latter case, where extra resources are unavailable and you are willing to delay project completion time, set the DELAY= option to some very large number or leave it unspecified (in which case it is assumed to be +INFINITY). You can achieve a combination of both effects (using supplementary levels and setting a limit on the delay allowed) by specifying an intermediate value for the DELAY= option and including an observation in the Resource data set with supplementary levels.

You can also use the INFEASDIAGNOSTIC option which is equivalent to specifying infinite supplementary levels for all the resources under consideration. In this case, the DELAY= value is assumed to equal the default value of +INFINITY, unless it is specified otherwise. See [Example 4.17, “INFEASDIAGNOSTIC Option and Aggregate Resource Type,”](#) for an illustration.

The DELAY= option presupposes that all the activities can be subjected to the same amount of delay. In some situations, you may want to control the amount of delay for each activity on the basis of some criterion, say the amount of float present in the activity. The ACTDELAY= option enables you to specify a variable amount of delay for each activity.

## Resource-Driven Durations and Resource Allocation

If resource-driven durations or resource calendars are specified, the procedure computes the start and finish times for each resource separately for each activity. An activity is considered to be completed only when all the resources have completed their work on that activity. Thus, an activity's start (finish) time is computed as the minimum (maximum) of the start (finish) times for all the resources used by that activity.

During resource-constrained scheduling, an activity enters the list of activities waiting for resources when all its precedence constraints have been satisfied. As before, this list is ordered using the scheduling rule specified. At this point, a tentative start and finish time is computed for each of the resources required by the activity using the resource's duration and calendar. An attempt is made to schedule *all* of this activity's resources at these calculated times using the available resources. If the attempt is successful, the activity is scheduled to start at the given time with the appropriate resource schedule times, and the required resources are reduced from the resource availabilities. Otherwise, the procedure attempts to schedule the next activity in the list of activities waiting for resources. When all activities have been considered at the given time, the procedure continues to the next event and continues the allocation process. Note that, at a given point of time, the procedure schedules the activity only if all the required resources are available for that activity to start at that time (or at the nearest time per that resource's calendar), unless you specify the **INDEPENDENTALLOC** option.

The **INDEPENDENTALLOC** option enables each resource to be scheduled independently for the activity. Thus, when an activity enters the list of activities waiting for resources, each resource requirement is considered independently, and a particular resource can be scheduled for that activity even if none of the other resources are available. However, the spanning type of resources must always be available throughout the activity's duration. The activity is considered to be finished (and its successors can start) only after all the resources for that activity have been scheduled. This option is valid even if all activities have fixed durations and calendars are not associated with resources.

## Activity Splitting

As mentioned in the section “[Scheduling Method](#)” on page 119, PROC CPM assumes that activities cannot be preempted once they have started. Thus, an activity is scheduled only if it can be assured of enough resources throughout its entire duration. Sometimes, you may be able to make better use of the resources by allowing activities to be *split*. PROC CPM enables you to specify the maximum number of segments that an activity can be split into as well as the minimum duration of any segment of the activity. Suppose that for a given activity,  $d$  is its duration,  $maxn$  is the maximum number of segments allowed, and  $dmin$  is the minimum duration allowed for a segment. If one or the other of these values is not given, it is calculated appropriately based on the duration of the activity.

The scheduling algorithm described earlier is modified as follows:

- In Step 2, the procedure tries to schedule the entire activity (call it A) if it is critical. Otherwise, PROC CPM schedules, if possible, only the first part (say A1) of the activity (of length  $dmin$ ). The remainder of the activity (call it A2, of length  $d - dmin$ ) is added to the waiting list to be scheduled later. When it is A2's turn to be scheduled, it is again a candidate for splitting if the values of  $maxn$  and  $dmin$  allow it, and if it is not critical. This process is repeated until the entire activity has been scheduled.
- While ordering the activities in the waiting list, in case of a tie, the split segments of an activity are given priority over unsplit activities. Note that some scheduling rules could lead to more splitting than others.

- Activities that have an alignment type of MS or MF imposed on them by the ALIGNTYPE variable are not split.

Note that splitting may not always reduce project completion time; it is designed to make better use of resources. In particular, if there are gaps in resource availability, it allows activities to be split and scheduled around the gaps, thus using the resources more efficiently.

If activity splitting is allowed, a new variable is included in the Schedule data set called SEGMENT\_NO (*segment number*). If splitting does occur, the Schedule data set has more observations than the Activity data set. Activities that are not split are treated as before, except that the value of the variable SEGMENT\_NO is set to missing. For split activities, the number of observations output is one more than the number of disjoint segments created.

The first observation corresponding to such an activity has SEGMENT\_NO set to missing, and the S\_START and S\_FINISH times are set to be equal to the start and finish times, respectively, of the entire activity. That is, S\_START is equal to the scheduled start time of the first segment, and S\_FINISH is equal to the scheduled finish time of the last segment that the activity is split into. Following this observation, there are as many observations as the number of disjoint segments in the activity. All values for these additional observations are the same as the corresponding values for the first observation for this activity, except for the variables SEGMENT\_NO, S\_START, S\_FINISH, and the DURATION variable. SEGMENT\_NO is the index of the segment, S\_START and S\_FINISH are the resource-constrained start and finish times for this segment, and DURATION is the duration of this segment.

## Actual Dates and Resource Allocation

The resource-constrained scheduling algorithm uses the early start schedule as the base schedule to determine possible start times for activities in the project. If an **ACTUAL** statement is used in the invocation of PROC CPM, the early start schedule (as well as the late start schedule) reflects the progress information that is specified for activities in the project, and thus affects the resource constrained schedule also. Further, activities that are already completed or in progress are scheduled at their actual start without regard to resource constraints. If the resource usage profile for such activities indicates that the resources are insufficient, a warning is printed to the log, but the activities are not postponed beyond their actual start time. The Usage data set contains negative values for the availability of the insufficient resources. These extra amounts are assumed to have come from the supplementary levels of the resources (if such a reservoir existed); for details about supplementary resources, see the section “**Secondary Levels of Resources**” on page 121.

If activity splitting is allowed (through the specification of the MINSEGMTDUR or MAXNSEGMENT variable or the SPLITFLAG or TIMENOWSPLT option), activities that are currently in progress may be split at TIMENOW if resources are insufficient; then the second segment of the split activity is added to the list of activities that need to be scheduled subject to resource constraints. Starting from TIMENOW, all activities that are still unscheduled are treated as described in the section “**Scheduling Method**” on page 119.

## Specifying Alternate Resources

PROC CPM enables you to identify alternate resources that can be substituted for any given resource that is insufficient. Thus, for example, you can specify that if programmer John is unavailable for a given task, he can be substituted by programmer David or Robert. This information is passed to PROC CPM through the Resource data set.

As with other aspects of the Resource data set, each observation is identified by a keyword indicating the type of information in that observation. Two keywords, ALTRATE and ALTPRTY, enable you to specify

the rate of substitution and a prioritization of the alternate resources when a resource has more than one substitution (lower value indicates higher priority). Further, a new variable (identified to PROC CPM through the RESID= option) is used to identify the resource for which alternates are being specified in the current observation. Consider the following Resource data:

OBS	OBSTYPE	RES_NAME	RES_DATE	JOHN	DAVID	ROBERT
1	RESTYPE		.	1	1.0	1.0
2	ALTRATE	JOHN	.	1	0.5	0.5
3	ALTPRTY	JOHN	.	1	2.0	3.0
4	RESLEVEL		15JUL04	1	1.0	1.0

In these Resource data, the second observation indicates that John can be substituted by David or Robert; however, either David or Robert can accomplish John's tasks with half the effort. In other words, if an activity requires 1 unit of John, it can also be accomplished with 0.5 units of David. Also, the third observation, with OBSTYPE='ALTPRTY', indicates that if John is unavailable, PROC CPM should first try to use David and if he, too, is unavailable, then should use Robert. This set up enables a wide range of control for specifying alternate resources.

In other words, the mechanism for specifying alternate resources is as follows: for each resource, specify a list of possible alternatives along with a conversion rate and an order in which the alternatives are to be considered. In the Resource data set, add another variable (identified by the RESID= option) to specify the name of the resource variable for which alternatives are being specified (the variable RES\_NAME in the preceding example).

Let OBSTYPE='ALTRATE' for the observation that specifies the rate of conversion for each possible alternate resource (missing implies the particular resource cannot be substituted). For resources that *drive* an activity's duration, the specification of the alternate rate is used as a multiplier of the resource-driven duration. See the section “Resource-Driven Durations and Alternate Resources” on page 126 for details.

Let OBSTYPE='ALTPRTY' for the observation that specifies a prioritization for the resources.

All substitute resources must be of the same type (replenishable or consumable) as the primary resource. The specification of the RESID= option triggers the use of alternate resources. If alternate resources are used, the Schedule data set contains new variables that specify the actual resources that are used; the names of these variables are obtained by prefixing the resource names by 'U'. When activities are allowed to be split and alternate resources are allowed, different segments of the activity can use a different set of resources. If this is the case, the Schedule data set contains a different observation for every segment that uses a different set of resources, even if these segments are contiguous in time. Contiguous segments, even if they use different sets of resources, are not treated as true splits for the purpose of counting the number of splits allowed for the activity.

By default, multiple resources cannot be used to substitute for a single resource. To enable multiple alternates, use the **MULTIPLEALTERNATES** option or add an observation to the Resource data set identifying which resources allow multiple alternates. For details, see the section “Specifying Multiple Alternates” on page 125.

See Example 4.20 for an illustration of the use of alternate resources.

## Specifying Multiple Alternates

As described in the section “[Specifying Alternate Resources](#)” on page 123, you can use the Resource data set to specify alternate resources for any given resource. You can specify a rate of substitution and a priority for substitution. However, the CPM procedure will not use multiple alternate resources to substitute for a given resource. For example, suppose that an activity needs two programmers and the available programmers (alternate resources) are John and Mary. By default, the CPM procedure cannot assign both John and Mary to the activity to fulfill the resource requirement of two programmers.

However, this type of substitution is useful to effectively model group resources or skill pools. To enable substitution of multiple alternates for a single resource, use the **MULTIPLEALTERNATES** option in the **RESOURCE** statement. This option enables all resources that have alternate specifications (through observations of the type ALTRATE or ALTPRTY in the Resource data set) to use multiple alternates. See [Table 4.8](#) for details about type identifier variables.

You can refine this feature to selectively allow multiple substitution or set a minimum rate of substitution, by adding special observations to the Resource data set. As with other aspects of the Resource data set, the specifications related to multiple alternates are identified by observations with special keywords, MULTALT and MINARATE.

Let OBSTYPE=‘MULTALT’ for the observation that identifies which resources can have multiple alternates. Valid values for such an observation are ‘0’ and ‘1’: ‘0’ indicates that the resource cannot be substituted by multiple resources, and ‘1’ indicates that it can be substituted by multiple resources. If the Resource data set contains such an observation, the **MULTIPLEALTERNATES** option is ignored and the values specified in the observation are used to allow multiple substitutions for only selected resources. See [Table 4.8](#) for details about type identifier variables.

Let OBSTYPE=‘MINARATE’ for the observation that indicates the minimum rate of substitution for each resource. For example, you may not want a primary resource requirement of 1.5 programmers, to be satisfied by 5 different alternate programmers at a rate of 0.3 each. To ensure that the minimum rate of substitution is 0.5, specify the value for the resource variable, PROGRAMMER, as ‘0.5’ in the observation with OBSTYPE=‘MINARATE’. In other words, use this observation if you do not wish to split an activity’s resource requirement across several alternate resources with a very small rate of utilization per resource. See [Table 4.8](#) for details about type identifier variables. Consider the following Resource data:

OBS	OBSTYPE	RES_NAME	RES_DATE	JOHN	DAVID	ROBERT
1	<b>RESTYPE</b>		.	1	1	1
2	<b>ALTRATE</b>	JOHN	.	1	2	2
3	<b>MULTALT</b>	.	.	1	.	.
4	<b>MINARATE</b>	.	.	0.5	.	.
5	<b>RESLEVEL</b>		15JUL04	0	1.0	1.0

In these Resource data, observations 3 and 4 control the use of multiple alternates. They specify that a requirement for John can be substituted with multiple alternates. Further, if multiple alternates are used instead of John, do not allocate them in units less than 0.5. Observation 2 indicates that David and Robert require twice the effort to accomplish John’s tasks. Thus, if an activity requires 1 unit of John, and he is unavailable, the CPM procedure will require 2 units of David (or Robert) to substitute for John. However, only 1 unit each of David and Robert is available. If multiple alternates are *not* allowed, the resource allocation algorithm will fail. However, since the resource John *does* allow multiple substitution, the activity can be scheduled with 1 unit of David and 1 unit of Robert (each substituting for 1/2 of the requirement for John).

Allowing multiple alternates for a single resource raises an interesting question: When distributing the resource requirements across multiple alternatives, should the primary resource be included in the list of multiple alternates? For instance, in the preceding example, if the resource level for John is ‘0.5’ (in observation 5), should the activity use John at rate 0.5 and assign the remainder to one (or more) of the alternate resources? Or, should the primary resource be excluded from the list of possible alternates? You can select either behavior for the primary resource by specifying ‘1’ (for inclusion) or ‘0’ (for exclusion) in the observation with OBSTYPE=‘ALTRATE’ that corresponds to the primary resource (with RES\_NAME=‘JOHN’). Thus, in the preceding example, John can be one of the multiple alternates when substituting for himself. To exclude John from the list, set the value of the variable JOHN to ‘0’ in observation 2. You will also need to set the value of JOHN to ‘0’ in any observation with OBSTYPE=‘ALTPRTY’ and RES\_NAME=‘JOHN’.

## Resource-Driven Durations and Alternate Resources

the section “Specifying Alternate Resources” on page 123 describes the use of the RESID= option and the observations of type ‘ALTRATE’ and ‘ALTPRTY’ in the Resource data set to control the use of alternate resources during resource allocation. The behavior described in that section refers to the substitution of resources for resources that have a fixed duration. Alternate resources can also be specified for resources that drive an activity’s duration. However, the specification of the alternate rate is interpreted differently: it is used as a multiplier of the resource-driven duration.

For example, consider the following Resource data:

OBS	OBSTYPE	RES_NAME	RES_DATE	JOHN	DAVID	ROBERT
1	RESTYPE	.	.	1	1	1
2	RESRCDUR	.	.	1	1	1
3	ALTRATE	JOHN	.	1	2	2
4	ALTPRTY	JOHN	.	1	2	3
5	RESLEVEL	.	15JUL04	.	1.0	1.0

In these Resource data, the second observation indicates that all the resources are driving resources. The third observation indicates that John can be substituted by David or Robert; however, either David or Robert will require twice as long to accomplish John’s tasks for resource-driven activities. Thus, in contrast to the fixed-duration activities, the ALTRATE specification changes the *duration* of the alternate resource, not the *rate of use*.

For instance, consider the following activity with the specified values for the DURATION and WORK variables and the resource requirement for John:

OBS	ACTIVITY	DURATION	WORK	JOHN	DAVID	ROBERT
1	Act1	3	10	1	.	.

Activity ‘Act1’ requires 10 days of work from John, indicating that the resource-driven duration for Act1 is 10 days. However, from the preceding Resource data, John is not available, but can be substituted by David or Robert, who will require twice as long to accomplish the work. So, if Act1 is scheduled using either one of the alternate resources, its resource-driven duration will be 20 days.

## Auxiliary Resources

Sometimes, the use of a certain resource may require simultaneous use of other resources. For example, use of a crane will necessitate the use of a crane operator. In other words, if an activity needs the resource, CRANE, it will also need a corresponding resource, CRANEOP. Such requirements can be easily modeled by adding both CRANE and CRANEOP to the list of resources required by the activity.

However, when alternate resources are used, the problem becomes more complex. For example, suppose an activity requires a CRANE and there are two possible cranes that can be used, CRANE1 and CRANE2. You can specify CRANE1 and CRANE2 as the alternate resources for CRANE. Suppose further that each of the two cranes has a specific operator, CRANEOP1 and CRANEOP2, respectively. Specifying CRANEOP1 and CRANEOP2 separately as alternates for CRANEOP will not necessarily guarantee that CRANEOP1 (or CRANEOP2) is used as the alternate for CRANEOP in conjunction with the use of the corresponding CRANE1 (or CRANE2).

You can model such a situation by the use of Auxiliary resource specification: specify CRANEOP1 and CRANEOP2 as auxiliary resources for CRANE1 and CRANE2, respectively. Auxiliary resources are specified through the Resource data set, using observations identified by the keyword AUXRES for the value of the OBSTYPE variable. For an observation of this type, the RESID variable specifies the name of the primary resource. (This is similar to the specification of ALTRATE and ALTPRTY.) See [Table 4.8](#) for details about type identifier variables.

Once auxiliary resources are specified in the Resource data set, it is sufficient to specify only the primary resource requirements in the Activity data set. In this situation, for example, it is sufficient to require a CRANE for the activity in the Activity data set.

In the Resource data set, add a new observation type, ‘AUXRES’, which will specify the auxiliary resources that are needed for each primary resource. For an observation of this type, the RESID variable specifies the name of the primary resource. The value for each auxiliary resource indicates the rate at which it is required whenever the primary resource is used. You will also need to specify CRANE1 and CRANE2 as the alternate resources for CRANE in the Resource data set.

When scheduling the activity, PROC CPM will schedule CRANE1 (or CRANE2) as the alternate only if both CRANE1 and CRANEOP1 (or CRANE2 and CRANEOP2) are available.

For instance, the preceding example will have the following Resource data set:

OBSTYPE	RESID	PER	CRANE	CRANE1	CRANE2	CRANEOP1	CRANEOP2
<b>AUXRES</b>	<b>CRANE1</b>	.	.	.	.	<b>1</b>	.
<b>AUXRES</b>	<b>CRANE2</b>	.	.	.	.	.	<b>1</b>
<b>ALTRATE</b>	<b>CRANE</b>	.	.	<b>1</b>	<b>1</b>	.	.
<b>RESLEVEL</b>	.	<b>10JUL04</b>	.	<b>1</b>	<b>1</b>	<b>1</b>	<b>1</b>

---

## RESOURCEOUT= Usage Data Set

The RESOURCEOUT= data set (referred to as the Usage data set) contains information about the resource usage for the resources specified in the **RESOURCE** statement. The options ALL, AVPROFILE, ESPROFILE, LSPROFILE, and RCPPROFILE (each is discussed earlier in the section “[RESOURCE Statement](#)” on page 80) control the number of variables that are to be created in this data set. The ROUTINTERVAL= and ROUTINTPER= options control the number of observations that this data set is to contain. Of the options

controlling the number of variables, AVPROFILE and RCPPROFILE are allowed only if the procedure is used to obtain a resource-constrained schedule.

The Usage data set always contains a variable named `_TIME_` that specifies the date for which the resource usage or availability in the observation is valid. For each of the variables specified in the **RESOURCE** statement, one, two, three, or four new variables are created depending on how many of the four possible options (AVPROFILE, ESPROFILE, LSPROFILE, and RCPPROFILE) are in effect. If none of these four options is specified, the ALL option is assumed to be in effect. Recall that the ALL option is equivalent to specifying ESPROFILE and LSPROFILE when PROC CPM is used to obtain an unconstrained schedule, and it is equivalent to specifying all four options when PROC CPM is used to obtain a resource-constrained schedule.

The new variables are named according to the following convention:

- The prefix A is used for the variable describing the resource availability profile.
- The prefix E is used for the variable denoting the early start usage.
- The prefix L is used for the variable denoting the late start usage.
- The prefix R is used for the variable denoting the resource-constrained usage.

The suffix is the name of the resource variable if the name is less than the maximum possible variable length (which is dependent on the VALIDVARNAME option). If the length of the name is equal to this maximum length, the suffix is formed by deleting the character following the  $(n/2)$ th position. The user must ensure that this naming convention results in unique variable names in the Usage data set.

The ROUTINTERVAL=*routinterval* and ROUTINTPER=*routintper* options specify that two successive values of the `_TIME_` variable differ by *routintper* number of *routinterval* units, measured with respect to a specific calendar. If the *routinterval* is not specified, PROC CPM selects a default value depending on the format of the start and finish variables in the Schedule data set. The value of *routinterval* is indicated in a message written to the SAS log.

The MINDATE=*mindate* and MAXDATE=*maxdate* options specify the minimum and maximum values of the `_TIME_` variable, respectively. Thus, the Usage data set has observations containing the resource usage information from *mindate* to *maxdate* with the time interval between the values of the `_TIME_` variable in two successive observations being equal to *routintper* units of *routinterval*, measured with respect to a specific calendar. For example, if *routinterval* is MONTH and *routintper* is 3, then the time interval between successive observations in the Usage data set is three months.

The calendar used for incrementing the `_TIME_` variable is specified using the AROUTCAL= or NROUTCAL= options depending on whether the calendars for the project are specified using alphanumeric or numeric values, respectively. In the absence of either of these specifications, the default calendar is used. For example, if the default calendar follows a five-day work week and ROUTINTERVAL=DAY, the Usage data set will not contain observations corresponding to Saturdays and Sundays. You can also use the ROUTNOBREAK option to indicate that there should be no breaks in the `_TIME_` values due to breaks or holidays.

## Interpretation of Variables

The availability profile indicates the amount of resources available at the beginning of the time interval specified in the `_TIME_` variable, after accounting for the resources used through the previous time period.

By default, each observation in the Resource Usage data set indicates the *rate* of resource usage per unit *routinterval* at the start of the time interval specified in the `_TIME_` variable. Note that *replenishable resources* are assumed to be tied to an activity during any of the activity's breaks or holidays that fall in the course of the activity's duration. For *consumable resources*, you can use the CUMUSAGE option to obtain *cumulative usage* of the resource, instead of *daily rate of usage*. Often, it is more useful to obtain *cumulative usage* for consumable resources.

You can use the TOTUSAGE option on the RESOURCE statement to get the *total* resource usage for each resource within each time period. If you wish to obtain both the *rate* of usage and the *total* usage for each time period, use the APPEND option on the RESOURCE statement.

The following example illustrates the default interpretation of the new variables.

Suppose that for the data given earlier (see the section “[Specifying Resource Requirements](#)” on page 118), activities ‘A’ and ‘B’ have S\_START equal to 1JUL04 and 5JUL04, respectively. If the RESOURCE statement has the options AVPROFILE and RCPROFILE, the Usage data set has these five variables, `_TIME_`, RWORKERS, AWORKERS, RBRICKS, and ABRICKS. Suppose further that *routinterval* is DAY and *routintper* is 1. The Usage data set contains the following observations:

<code>_TIME_</code>	RWORKERS	AWORKERS	RBRICKS	ABRICKS
1JUL04	0	0	100	1000
2JUL04	0	0	100	900
3JUL04	0	0	100	800
4JUL04	0	0	100	700
5JUL04	2	2	100	600
6JUL04	2	2	0	500
7JUL04	2	2	0	500
8JUL04	2	2	0	500
9JUL04	0	4	0	1000

On each day of activity A’s duration, the resource BRICKS is consumed at the rate of 100 bricks per day. At the beginning of the first day (July 1, 2004), all 1000 bricks are still available. Each day the availability drops by 100 bricks, which is the rate of consumption. On July 5, activity ‘B’ is scheduled to start. On the four days starting with July 5, the value of RWORKERS is ‘2’, indicating that 2 workers are used on each of those days leaving an available supply of 2 workers (AWORKERS is equal to ‘2’ on all 4 days).

If ROUTINTPER is set to 2, and the CUMUSAGE option is used, then the observations would be as follows:

<code>_TIME_</code>	RWORKERS	AWORKERS	RBRICKS	ABRICKS
1JUL04	0	0	0	1000
3JUL04	0	0	200	800
5JUL04	2	2	400	600
7JUL04	2	2	500	500
9JUL04	0	4	500	1000

The value of RBRICKS indicates the *cumulative* usage of the resource BRICKS through the *beginning* of the date specified by the value of the variable `_TIME_` in each observation. That is why, for example, RBRICKS = 0 on 1JUL04 and not 200.

If the procedure uses supplementary levels of resources, then, on a day when supplementary levels of resources were used through the beginning of the day, the value for the availability profile for the relevant resources would be negative. The absolute magnitude of this value would denote the amount of supplementary resource that was used through the beginning of the day. For instance, if ABRICKS is ‘–100’ on 11JUL04, it would indicate that 100 bricks from the supplementary reservoir were used through the end of July 10, 2004. See [Example 4.16](#), “Using Supplementary Resources,” and [Example 4.17](#), “INFEASDIAGNOSTIC Option and Aggregate Resource Type.”

If, for the same data, ROUTINTPER is 2, and the APPEND option is specified, the Usage data set would contain two sets of observations, the first indicating the *rate of resource usage per day*, and the second set indicating the *product of the rate and the time interval between two successive observations*. The observations (five in each set) would be as follows:

<u>TIME</u>	<u>OBS_TYPE</u>	RWORKERS	RBRICKS
01JUL04	RES_RATE	0	100
03JUL04	RES_RATE	0	100
05JUL04	RES_RATE	2	100
07JUL04	RES_RATE	2	0
09JUL04	RES_RATE	0	0
01JUL04	RES_USED	0	200
03JUL04	RES_USED	0	200
05JUL04	RES_USED	4	100
07JUL04	RES_USED	4	0
09JUL04	RES_USED	0	0

### Variable Usage Profile for Consumable Resources

For consumable resources that have a variable usage profile (as indicated by the values 1 or 2 for observations of type RESUSAGE in the Resource data set), the values of the usage variables indicate the amount of the resource consumed by an activity at the beginning or end of the activity. For example, consider the resources PAYMENT and ADVANCE specified in the following Resource data set:

OBS	OBSTYPE	DATE	WORKERS	BRICKS	PAYMENT	ADVANCE
1	RESTYPE	.	1	2	2	2
2	RESUSAGE	.	.	.	2	1
3	RESLEVEL	1JUL2004	4	1000	2000	500

Suppose the activity ‘Task 1’, specified in the following observation, is scheduled to start on July 1, 2004:

OBS	ACTIVITY	DUR	WORKERS	BRICKS	PAYMENT	ADVANCE
1	Task 1	5	1	100	1000	200

For these data, the resource usage profile for the resources will be as indicated in the following output:

<u>TIME</u>	RWORKERS	RBRICKS	RPAYMENT	RADVANCE
1JUL04	1	100	0	200
2JUL04	1	100	0	0
3JUL04	1	100	0	0
4JUL04	1	100	0	0
5JUL04	1	100	0	0
6JUL04	0	0	1000	0

---

## RESOURCESCHED= Resource Schedule Data Set

The Resource Schedule data set (requested by the RESSCHED= option on the CPM statement) is very similar to the Schedule data set, and it contains the start and finish times for each resource used by each activity. The data set contains the variables listed in the ACTIVITY, TAILNODE, and HEADNODE statements and all the relevant schedule variables (E\_START, E\_FINISH, and so forth). For each activity in the project, this data set contains the schedule for the entire activity as well as the schedule for each resource used by the activity. The variable RESOURCE identifies the name of the resource to which the observation refers; the value of the RESOURCE variable is missing for observations that refer to the entire activity's schedule. The variable DUR\_TYPE indicates whether the resource is a driving resource or a spanning resource or whether it is of the fixed type.

A variable \_DUR\_ indicates the duration of the activity for the resource identified in that observation. This variable has missing values for resources that are of the spanning type. For resources that are of the driving type, the variable \_WORK\_ shows the total amount of work required by the resource for the activity in that observation. The variable R\_RATE shows the rate of usage of the resource for the relevant activity. For driving resources, the variable \_DUR\_ is computed as (WORK / R\_RATE).

If you specify an ACTUAL statement, the Resource Schedule data set also contains the STATUS variable indicating whether the resource has completed work on the activity, is in progress, or is still pending.

---

## Multiproject Scheduling

The CPM procedure enables you to define activities in a multiproject environment with multiple levels of nesting. You can specify a PROJECT variable that identifies the name or number of the project to which each activity belongs. The PROJECT variable must be of the same type and length as the ACTIVITY variable. Further, each project can be considered as an activity, enabling you to specify precedence constraints, alignment dates, or progress information for the different projects. Precedence constraints can be specified between two projects, between activities in the same or different projects, or between a project and activities in another project.

The PROJECT variable enables you to specify the name of the project to which each activity belongs. Each project can in turn be treated as an activity that belongs to a bigger project. Thus, the (PROJECT, ACTIVITY) pair of variables enables you to specify multiple levels of nesting using a hierarchical structure for the (task, supertask) relationship.

In the following discussion, the terms superproject, supertask, parent task, ancestor task, project, or subproject refer to a *composite* task (a task composed of other tasks). A lowest level task (one which has no subtasks under it) is referred to as a child task, descendent task, a *leaf* task, or a *regular* task.

You can assign most of the “activity attributes” to a supertask; however, some of the interpretations may be different. The significant differences are listed as follows.

### Activity Duration

Even though a supertask has a value specified for the DURATION variable, the finish time of the supertask may not necessarily be equal to the (start time + duration). The start and finish times of a

parent task (supertask) always encompass the span of all its subtasks. In other words, the start (finish) time of a supertask is the minimum start (maximum finish) time of all its subtasks.

The specified DURATION for a supertask is used only if the USEPROJDUR option is specified; this variable is used to compute an upper bound on the late finish time of the project. In other words, you can consider the duration of a supertask as a *desired* duration that puts a constraint on its finish time.

**NOTE:** You cannot specify resource-driven durations for supertasks.

### Precedence Constraints

You cannot specify a Start-to-Finish or Finish-to-Finish type of precedence constraint when the Successor task is a supertask. Such a constraint is ignored, and a warning is written to the log.

### Time Constraints

The CPM procedure supports all the customary time constraints for a supertask. However, since the supertask does not really have an inherent duration, some of the constraints may lead to unexpected results.

For example, a constraint of the type SLE (Start Less than or Equal to) on a leaf task uses the task's duration to impose a maximum late finish time for the task. However, for a supertask, the duration is determined by the span of all its subtasks, which may depend on the activities' calendars. The CPM procedure uses an estimate of the supertask's duration computed on the basis of the precedence constraints to determine the maximum finish time for the supertask using the date specified for the SLE constraint. Such a constraint may not translate to the correct upper bound on the supertask's finish time if the project has multiple calendars. The presence of multiple calendars could change the computed duration of the supertask depending on the starting date of the supertask. Thus, in general, it is better to specify SGE (Start Greater than or Equal to) or FLE (Finish Less than or Equal to) constraints on supertasks.

Note that alignment constraints of the type SGE or FLE percolate down the project hierarchy. For example, if there is an SGE specification on a supertask, then all the subtasks of this supertask must also start on or after the specified date.

Mandatory constraints (either of the type MS or MF) are used to set fixed start and finish times on the relevant task. Such constraints are checked for consistency between a parent task and all its descendants.

### Progress Information

You can enter progress information for supertasks in the same way as you do for leaf tasks. The procedure attempts to reconcile inconsistencies between the actual start and finish times of a parent and its children. However, it is sufficient (and less ambiguous) to enter progress information only about the tasks at the lowest level.

### Resource Requirements

You can specify resource requirements for supertasks in the same way as you do for regular tasks. However, the supertask is scheduled in conjunction with all its subtasks. In other words, a leaf task is scheduled only when *its resources and the resources for all its ancestors* are available in sufficient quantity. Thus, a supertask needs to have enough resources throughout the schedule of any of its subtasks; in fact, the supertask needs to have enough resources throughout its entire span. In other words, a supertask's resource requirements are treated as "spanning."

In addition to the above treatment of a supertask's resources, there are two other resource scheduling options available for handling the resource requirements of supertasks. You can use the AGGRE-

GATEPARENTRES option in the PROJECT statement to indicate that a supertask's resource requirements are to be used only for aggregation. In other words, resource allocation is performed taking into account the resource requirements of only the leaf tasks. Alternately, you can select to ignore any resource requirements specified for supertasks by specifying the IGNOREPARENTRES option. Note the difference between the AGGREGATEPARENTRES and IGNOREPARENTRES options. The first option includes the supertask's requirements while computing the aggregate resource usage, while the second option is equivalent to setting all parent resource requirements to 0.

### **Resource-Driven Durations**

Any WORK specification is ignored for a parent task. Resources required for a supertask cannot drive the duration of the task; a supertask's duration is driven by all its subtasks. Note that each leaf task can still be resource driven.

### **Schedule Computation**

The project hierarchy and all the precedence constraints (between leaf tasks, between supertasks, or between a supertask and a leaf task) are taken into consideration when the project schedule is computed. A task (parent or leaf) can be scheduled only when *its precedences and all its parent's precedences* are satisfied.

During the forward pass of the scheduling algorithm, all independent start tasks (leaf tasks or supertasks with no predecessors) are initialized to the project start date. Once a supertask's precedences (if any) are satisfied, all its subtasks whose precedences have been satisfied are added to the list of activities that can be scheduled. The early start times for the subtasks are initialized to the early start time of the supertask and are then updated, taking into account the precedence constraints and any alignment constraints on the activities.

Once all the subtasks are scheduled, a supertask's early start and finish times are set to the minimum early start and maximum early finish, respectively, of all its subtasks.

The late start schedule is computed using a backward pass through the project network, considering the activities in a reverse order from the forward pass. The late schedule is computed starting with the last activity (activities) in the project; the late finish time for each such activity is set to the master project's finish date. By default, the master project's finish date is the maximum of the early finish dates of all the activities in the master project (if a FINISHBEFORE date is specified with the FBDATE option, this date is used as the starting point for the backward calculations).

During the backward pass, the late finish time of a supertask is determined by the precedence constraints and any alignment specification on the supertask. You can specify a finish constraint on a supertask by using the ALIGNDATE and ALIGNTYPE variables, or by using the SEPCRIT or USEPROJDUR option.

If a finish constraint is specified using the ALIGNDATE and ALIGNTYPE specifications, the L\_FINISH for the supertask is initialized to this value. If the SEPCRIT option is specified, the supertask's late finish time is initialized to its early finish time. If the USEPROJDUR option is specified, the late finish time for the supertask is initialized using the early start time of the supertask and the specified supertask duration. The late finish time of the supertask could further be affected by the precedence constraints. Once a supertask's late finish has been determined, this value is treated as an upper bound on the late finish of all its subtasks.

As with the early start schedule, once all the subtasks have been scheduled, the late start and finish times for a supertask are set to the minimum late start and maximum late finish time, respectively, of all its subtasks.

## Schedule Data Set

If a PROJECT variable is specified, the Schedule data set contains the PROJECT variable as well as two new variables called PROJ\_DUR and PROJ\_LEV.

The PROJ\_DUR variable contains the project duration (computed as E\_FINISH - E\_START of the project) for each superproject in the master project. This variable has missing values for the leaf tasks. It is possible for (L\_FINISH - L\_START) to be different from the value of PROJ\_DUR. If a resource-constrained schedule is produced by PROC CPM, the project duration is computed using the resource constrained start and finish times of the superproject; in other words, in this case PROJ\_DUR = (S\_FINISH - S\_START).

The PROJ\_LEV variable specifies the depth of each activity from the root of the project hierarchy tree. The root of the tree has PROJ\_LEV = 0; If the project does not have a single root, a common root is defined by the CPM procedure.

The ADDACT option on the PROC CPM statement causes an observation to be added to the Schedule data set for this common root. This observation contains the project start and finish times and the project duration. The ADDACT option also adds an observation for any activity that may appear as a value of the SUCCESSOR or PROJECT variable without appearing as a value of the ACTIVITY variable.

In addition to the PROJ\_DUR and PROJ\_LEV variables, you can request that a WBS code be added to the output data set (using the option ADDWBS). You can also add variables, ES\_ASC, ES\_DESC, LS\_ASC, LS\_DESC, SS\_ASC, and SS\_DESC, that indicate a sorting order for activities in the output data set. For example, the variable ES\_ASC enables you to sort the output data set in such a way that the activities within each superproject are ordered according to increasing early start time.

## Macro Variable \_ORCPM\_

The CPM procedure defines a macro variable named \_ORCPM\_. This variable contains a character string that indicates the status of the procedure. It is set at procedure termination. The form of the \_ORCPM\_ character string is STATUS=, optionally followed by REASON=. The value for STATUS= is one of the following:

- SUCCESSFUL - indicates successful completion
- ERROR\_EXIT - indicates unsuccessful termination

If PROC CPM terminates unsuccessfully, REASON= will be followed by one of the values below:

- CYCLE - indicates that PROC CPM found a cycle in the project network; activity/successor (or tailnode/headnode for an AOA representation) and parent/child (see **PROJECT** statement) pairs define precedence relationships among the activities, which can be viewed as directed arcs in a graph
- RES\_INFEASIBLE - indicates that PROC CPM could not find a schedule that satisfies the resource requirements, given the specified resource levels; the **INFEASDIAGNOSTIC** option might be useful in this case
- BADDATA\_ERROR - points to problems with the input specification; an example would be neglecting to name an activity or duration variable

- MEMORY\_ERROR - occurs when memory is exhausted
- IO\_ERROR - triggered by problems with a data set
- SEMANTIC\_ERROR - indicates an incongruity in the user specification or input data
- SYNTAX\_ERROR - occurs when the user has specified an invalid value for a keyword, for instance
- CPM\_BUG - should not occur
- UNKNOWN\_ERROR - should not occur

This information can be used when PROC CPM is one step in a larger program that needs to determine whether the procedure terminated successfully or not. Because \_ORCPM\_ is a standard SAS macro variable, it can be used in the ways that all macro variables can be used.

## Input Data Sets and Related Variables

The CPM procedure uses activity, resource, and holiday data from several different data sets with key variable names being used to identify the appropriate information. [Table 4.9](#) lists all of the variables associated with each input data set and their interpretation by the CPM procedure. The variables are grouped according to the statement that they are identified in. Some variables use default names and are not required to be identified in any statement.

**Table 4.9** PROC CPM Input Data Sets and Associated Variables

Data Set	Statement	Variable Name	Interpretation
CALEDATA	CALID	CALID	Calendar corresponding to work pattern
	Default names	D_LENGTH _SUN_ ... _SAT_	Length of standard work day Work pattern on day of week, valid values: WORKDAY, HOLIDAY, or one of the numeric variables in the Workday data set
DATA	ACTIVITY	ACTIVITY	Activity in AON format
	ACTUAL	A_START A_FINISH REMDUR PCTCOMP	Actual start time of activity Actual finish time of activity Remaining duration Percentage of work completed
	ALIGNDATE	ALIGNDATE	Time constraint on activity

**Table 4.9** (continued)

Data Set	Statement	Variable Name	Interpretation
	ALIGNTYPE	ALIGNTYPE	Type of time constraint, valid values: SGE, SEQ, SLE, FGE, FEQ, FLE, MS, MF
BASELINE	B_START		Baseline start time of activity
	B_FINISH		Baseline finish time of activity
	CALID	CALID	Calendar followed by activity
DURATION	DURATION	DURATION	Duration of activity
	FINISH		Finish time of activity
	START		Start time of activity
	HEADNODE	HEADNODE	Head of arrow (arc) in AOA format
	ID	ID	Additional project information
	PROJECT	PROJECT	Project to which activity belongs
RESOURCE	ACTDELAY	ACTDELAY	Activity delay
	ACTPRTY	ACTPRTY	Activity priority
	MAXNSEGMT	MAXNSEGMT	Maximum number of segments
	MINSEGMTDUR	MINSEGMTDUR	Minimum duration of a segment
	RESOURCE	RESOURCE	Amount of resource required
SUCCESSOR	WORK		Amount of work required
	SUCCESSOR		Successor in AON format
	LAG		Nonstandard precedence relationship
	TAILNODE	TAILNODE	Tail of arrow (arc) in AOA format

**Table 4.9** (continued)

Data Set	Statement	Variable Name	Interpretation
HOLIDATA	CALID	CALID	Calendar to which holiday applies
	HOLIDAY	HOLIDAY	Start of holiday
		HOLIDUR	Duration of holiday
RESOURCEIN	RESOURCE	HOLIFIN	End of holiday
		OBSTYPE	Type of observation; valid values: RESLEVEL, RESTYPE, SUPLEVEL, RESPRTY, ALTRATE, ALTPRTY, RESUSAGE, AUXRES, MULTALT, MINARATE, CALENDAR
		PERIOD	Time from which resource is available
		RESID	Resource for which alternates are given
WORKDATA	Any numeric variable	RESOURCE	Resource type, priority, availability, alternate rate, alternate priority
			On-off pattern of work (shift definition)

---

## Missing Values in Input Data Sets

The following table summarizes the treatment of missing values for variables in the input data sets used by PROC CPM.

**Table 4.10** Treatment of Missing Values in the CPM Procedure

Data Set	Variable	Value Used / Assumption Made / Action Taken
CALEDATA	CALID	Default calendar (0 or DEFAULT)
	D_LENGTH	DAYLENGTH, if available. 8:00, if INTERVAL = WORKDAY, DTWRKDAY 24:00, otherwise
	_SUN_	Corresponding shift for default calendar
	...	
	_SAT_	
DATA	ACTIVITY	Input error: procedure stops with error message
	ACTDELAY	DELAY= specification
	ACTPRTY	Infinity (indicates lowest priority)

**Table 4.10** (continued)

Data Set	Variable	Value Used / Assumption Made / Action Taken
	ALIGNDATE	Project start date for start activity
	ALIGNTYPE	SGE: if ALIGNDATE is not missing
	A_FINISH	See the section “ <a href="#">Progress Updating</a> ” on page 109 for details
	A_START	See the section “ <a href="#">Progress Updating</a> ” on page 109 for details
	B_FINISH	Updated if UPDATE= option is on
	B_START	Updated if UPDATE= option is on
	CALID	Default calendar (0 or DEFAULT)
	DURATION	Input error: procedure stops with error message
	FINISH	Value ignored
	HEADNODE	Input error: procedure stops with error message
	ID	Missing
	LAG	FS_0: if corresponding successor Variable value is not missing
	MAXNSEGMT	Calculated from MINSEGMTDUR
	MINSEGMTDUR	0.2 * DURATION
	PCTCOMP	See the section “ <a href="#">Progress Updating</a> ” on page 109 for details
	PROJECT	Activity is at highest level
	REMDUR	See the section “ <a href="#">Progress Updating</a> ” on page 109 for details
	RESOURCE	0
	START	Value ignored
	SUCCESSOR	Value ignored
	TAILNODE	Input error: procedure stops with error message
	WORK	Resources use fixed duration
HOLIDATA	CALID	Holiday applies to all calendars defined
	HOLIDAY	Observation ignored
	HOLIDUR	Ignored if HOLIFIN is not missing; 1, otherwise
	HOLIFIN	Ignored if HOLIDUR is not missing; HOLIDAY + (1 unit of INTERVAL), otherwise
RESOURCEIN	OBSTYPE	RESLEVEL
	PERIOD	Input error if OBSTYPE is RESLEVEL, otherwise ignored
	RESID	Observation ignored
	RESOURCE	1.0, if OBSTYPE is RESTYPE infinity, if OBSTYPE is RESPRTY 0.0, if OBSTYPE is RESUSAGE 0.0, if OBSTYPE is SUPLEVEL 0.0, if OBSTYPE is RESLEVEL and this is the first observation of this type otherwise, equal to value in previous observation
WORKDATA	Any numeric variable	00:00, if first observation 24:00, otherwise

---

## FORMAT Specification

As can be seen from the description of all of the statements and options used by PROC CPM, the procedure handles SAS date, time, and datetime values in several ways: as time constraints on the activities, holidays specified as date or datetime values, periods of resource availabilities, actual start and finish times, and several other options that control the scheduling of the activities in time. The procedure tries to reconcile any differences that may exist in the format specifications for the different variables. For example, if holidays are formatted as SAS date values while alignment constraints are specified in terms of SAS datetime values, PROC CPM converts all of the holidays to SAS datetime values suitably. However, the procedure needs to know how the variables are to be interpreted (as SAS date, datetime, or time values) in order for this reconciliation to be correct. Thus, it is important that you always use a FORMAT statement explicitly for each SAS date, time, or datetime variable that is used in the invocation of PROC CPM.

---

## Computer Resource Requirements

There is no inherent limit on the size of the project that can be scheduled with the CPM procedure. The number of activities and precedences, as well as the number of resources are constrained only by the amount of memory available. Naturally, there needs to be a sufficient amount of core memory available in order to invoke and initialize the SAS system. As far as possible, the procedure attempts to store all the data in core memory.

However, if the problem is too large to fit in core memory, the procedure resorts to the use of utility data sets and swaps between core memory and utility data sets as necessary, unless the [NOUTIL](#) option is specified. The procedure uses the NACTS=, NADJ=, NNODES=, and NRESREQ= options to determine approximate problem size. If these options are not specified, the procedure estimates default values on the basis of the number of observations in the Activity data set. See the section “[Syntax: CPM Procedure](#)” on page 61 for default specifications.

The storage requirement for the data area required by the procedure is proportional to the number of activities and precedence constraints in the project and depends on the number of resources required by each activity. The time required depends heavily on the number of resources that are constrained and on how tightly constrained they are.

## Examples: CPM Procedure

This section contains examples that illustrate several features of the CPM procedure. Most of the available options are used in at least one example. Two tables, [Table 4.13](#) and [Table 4.14](#), at the end of this section list all the examples in this chapter and the options and statements in the CPM procedure that are illustrated by each example.

A simple project concerning the manufacture of a widget is used in most of the examples in this section. [Example 4.22](#) deals with a nonstandard application of PROC CPM and illustrates the richness of the modeling environment that is available with the SAS System. The last few examples use different projects to illustrate multiproject scheduling and resource-driven durations, resource calendars and negative resource requirements.

There are 14 activities in the widget manufacturing project. [Example 4.1](#) and [Example 4.2](#) illustrate a basic project network that is built upon by succeeding examples. The tasks in the project can be classified by the division or department that is responsible for them.

[Table 4.11](#) lists the detailed names (and corresponding abbreviations) of all the activities in the project and the department that is responsible for each one. As in any typical project, some of these activities must be completed before others. For example, the activity ‘Approve Plan’ must be done before any of the activities ‘Drawings’, ‘Study Market’, and ‘Write Specs’, can start. [Table 4.12](#) summarizes the relationships among the tasks and gives the duration in days to complete each task. This table shows the relationship among tasks by listing the immediate successors to each task.

**Table 4.11** Widget Manufacture: Activity List

Task	Department	Activity Description
Approve Plan	Planning	Finalize and Approve Plan
Drawings	Engineering	Prepare Drawings
Study Market	Marketing	Analyze Potential Markets
Write Specs	Engineering	Write Specifications
Prototype	Engineering	Build Prototype
Mkt. Strat.	Marketing	Develop Marketing Concept
Materials	Manufacturing	Procure Raw Materials
Facility	Manufacturing	Prepare Manufacturing Facility
Init. Prod.	Manufacturing	Initial Production Run
Evaluate	Testing	Evaluate Product In-House
Test Market	Testing	Mail Product to Sample Market
Changes	Engineering	Engineering Changes
Production	Manufacturing	Begin Full Scale Production
Marketing	Marketing	Begin Full Scale Marketing


**Table 4.12** Widget Manufacture: Precedence Information

Task	Dur	Successor	Successor	Successor
Approve Plan	10	Drawings	Study Market	Write Specs
Drawings	20	Prototype		
Study Market	10	Mkt. Strat.		
Write Specs	15	Prototype		
Prototype	30	Materials	Facility	
Mkt. Strat.	25	Test Market	Marketing	
Materials	60	Init. Prod.		
Facility	45	Init. Prod.		
Init. Prod.	30	Test Market	Marketing	Evaluate
Evaluate	40	Changes		
Test Market	30	Changes		
Changes	15	Production		
Production	0			
Marketing	0			

The relationship among the tasks can be represented by the network in [Output 4.1.1](#). The diagram was produced by the NETDRAW procedure. The code used is the same as in [Example 9.11](#) in Chapter 9, “[The NETDRAW Procedure](#),” although the colors may be different.

## Example 4.1: Activity-on-Node Representation

#### **Output 4.1.1** Network Showing Task Relationships in Activity-on-Node Format

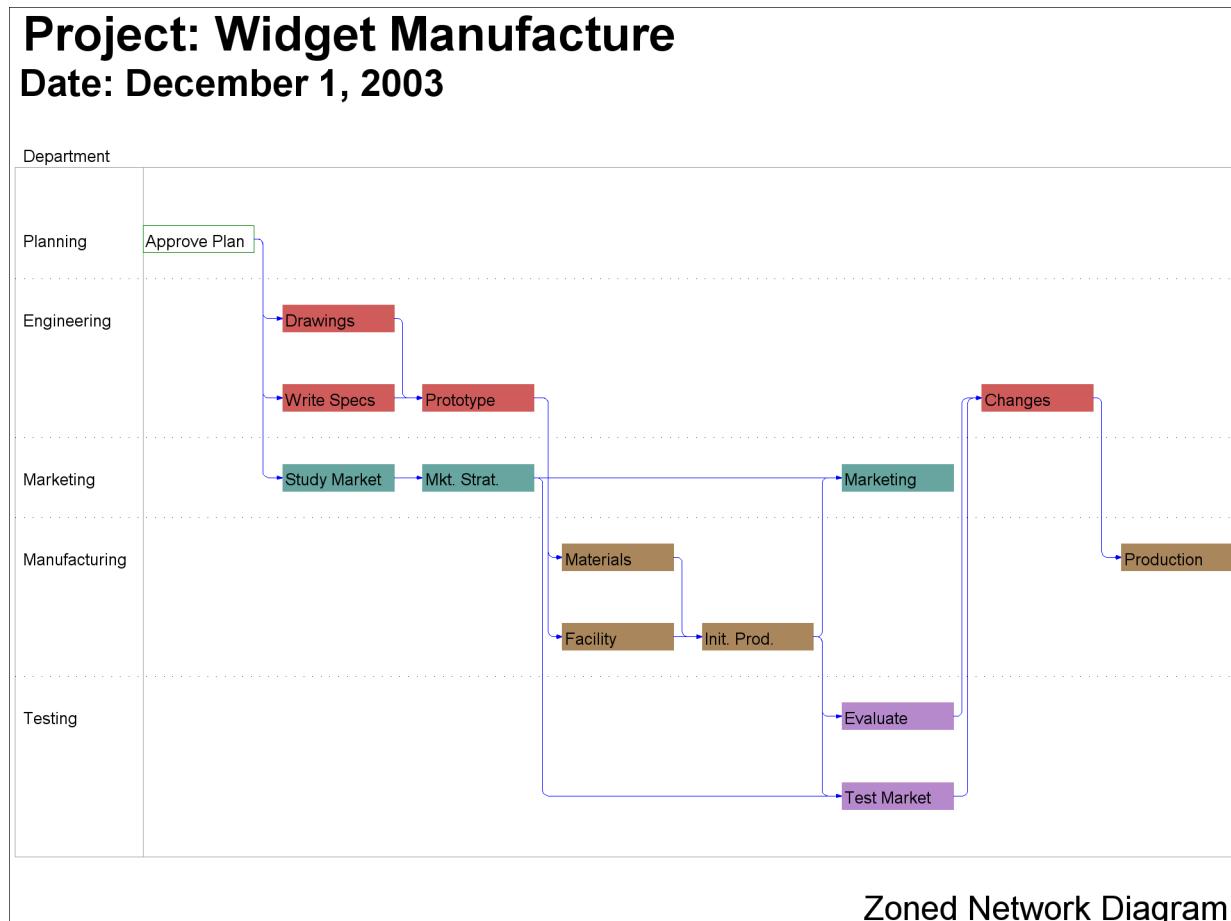

The following DATA step reads the project network in AON format into a SAS data set named WIDGET. The data set contains the minimum amount of information needed to invoke PROC CPM, namely, the ACTIVITY variable, one or more SUCCESSOR variables, and a DURATION variable. PROC CPM is invoked, and the Schedule data set is displayed using the PRINT procedure in [Output 4.1.2](#). The Schedule data set produced by PROC CPM contains the solution in canonical units, without reference to any calendar date or time. For instance, the early start time of the first activity in the project is the beginning of period 0 and the early finish time is the beginning of period 5.

```

/* Activity-on-Node representation of the project */
data widget;
format task $12. succ1-succ3 $12.;
input task & days succ1 & succ2 & succ3 & ;
datalines;
Approve Plan      5   Drawings        Study Market    Write Specs
Drawings          10  Prototype       .
Study Market     5   Mkt. Strat.    .
Write Specs       5   Prototype       .

```

```

Prototype      15 Materials       Facility      .
Mkt. Strat.   10 Test Market    Marketing     .
Materials      10 Init. Prod.    .
Facility       10 Init. Prod.    .
Init. Prod.    10 Test Market    Marketing     Evaluate
Evaluate       10 Changes        .
Test Market    15 Changes        .
Changes        5 Production    .
Production     0   .            .
Marketing      0   .            .

;

/* Invoke PROC CPM to schedule the project specifying the */
/* ACTIVITY, DURATION and SUCCESSOR variables           */
proc cpm;
  activity task;
  duration days;
  successor succ1 succ2 succ3;
run;

title 'Widget Manufacture: Activity-On-Node Format';
title2 'Critical Path';
proc print;
  run;

```

#### Output 4.1.2 Critical Path

### Widget Manufacture: Activity-On-Node Format Critical Path

Obs	task	succ1	succ2	succ3	days	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
1	Approve Plan	Drawings	Study Market	Write Specs	5	0	5	0	5	0	0
2	Drawings	Prototype			10	5	15	5	15	0	0
3	Study Market	Mkt. Strat.			5	5	10	35	40	30	0
4	Write Specs	Prototype			5	5	10	10	15	5	5
5	Prototype	Materials	Facility		15	15	30	15	30	0	0
6	Mkt. Strat.	Test Market	Marketing		10	10	20	40	50	30	30
7	Materials	Init. Prod.			10	30	40	30	40	0	0
8	Facility	Init. Prod.			10	30	40	30	40	0	0
9	Init. Prod.	Test Market	Marketing	Evaluate	10	40	50	40	50	0	0
10	Evaluate	Changes			10	50	60	55	65	5	5
11	Test Market	Changes			15	50	65	50	65	0	0
12	Changes	Production			5	65	70	65	70	0	0
13	Production				0	70	70	70	70	0	0
14	Marketing				0	50	50	70	70	20	20

Alternately, if you know that the project is to start on December 1, 2003, then you can determine the project schedule with reference to calendar dates by specifying the DATE= option in the PROC CPM statement. The default unit of duration is assumed to be DAY. The architecture of PROC CPM enables you to include

any number of additional variables that are relevant to the project. Here, for example, you may want to include more descriptive activity names and department information. The data set DETAILS contains more information about the project that is merged with the WIDGET data set to produce the WIDGETN data set. The ID statement is useful to carry information through to the data set. [Output 4.1.3](#) displays the resulting output data set.

```

data details;
  format task $12. dept $13. descrpt $30. ;
  input task & dept $ descrpt & ;
  label dept = "Department"
    descrpt = "Activity Description";
  datalines;
Approve Plan   Planning      Finalize and Approve Plan
Drawings       Engineering   Prepare Drawings
Study Market  Marketing     Analyze Potential Markets
Write Specs   Engineering   Write Specifications
Prototype     Engineering   Build Prototype
Mkt. Strat.   Marketing    Develop Marketing Concept
Materials     Manufacturing Procure Raw Materials
Facility      Manufacturing Prepare Manufacturing Facility
Init. Prod.   Manufacturing Initial Production Run
Evaluate      Testing       Evaluate Product In-House
Test Market   Testing       Mail Product to Sample Market
Changes       Engineering   Engineering Changes
Production   Manufacturing Begin Full Scale Production
Marketing    Marketing    Begin Full Scale Marketing
;

/* Combine project network data with additional details */
data widgetn;
  merge widget details;
  run;

/* Schedule using PROC CPM, identifying the variables */
/* that specify additional project information      */
/* and set project start date to be December 1, 2003 */
proc cpm data=widgetn date='1dec03'd;
  activity task;
  successor succ1 succ2 succ3;
  duration days;
  id dept descrpt;
  run;

```

```

proc sort;
  by e_start;
  run;

title2 'Project Schedule';
proc print;
  id descript;
  var dept e_: l_: t_float f_float;
  run;

```


#### Output 4.1.3 Critical Path: Activity-On-Node Format

### Widget Manufacture: Activity-On-Node Format Project Schedule

descript	dept	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
Finalize and Approve Plan	Planning	01DEC03	05DEC03	01DEC03	05DEC03	0	0
Prepare Drawings	Engineering	06DEC03	15DEC03	06DEC03	15DEC03	0	0
Analyze Potential Markets	Marketing	06DEC03	10DEC03	05JAN04	09JAN04	30	0
Write Specifications	Engineering	06DEC03	10DEC03	11DEC03	15DEC03	5	5
Develop Marketing Concept	Marketing	11DEC03	20DEC03	10JAN04	19JAN04	30	30
Build Prototype	Engineering	16DEC03	30DEC03	16DEC03	30DEC03	0	0
Procure Raw Materials	Manufacturing	31DEC03	09JAN04	31DEC03	09JAN04	0	0
Prepare Manufacturing Facility	Manufacturing	31DEC03	09JAN04	31DEC03	09JAN04	0	0
Initial Production Run	Manufacturing	10JAN04	19JAN04	10JAN04	19JAN04	0	0
Evaluate Product In-House	Testing	20JAN04	29JAN04	25JAN04	03FEB04	5	5
Mail Product to Sample Market	Testing	20JAN04	03FEB04	20JAN04	03FEB04	0	0
Begin Full Scale Marketing	Marketing	20JAN04	20JAN04	09FEB04	09FEB04	20	20
Engineering Changes	Engineering	04FEB04	08FEB04	04FEB04	08FEB04	0	0
Begin Full Scale Production	Manufacturing	09FEB04	09FEB04	09FEB04	09FEB04	0	0

## Example 4.2: Activity-on-Arc Representation

**Output 4.2.1** Network Showing Task Relationships in Activity-on-Arc Format

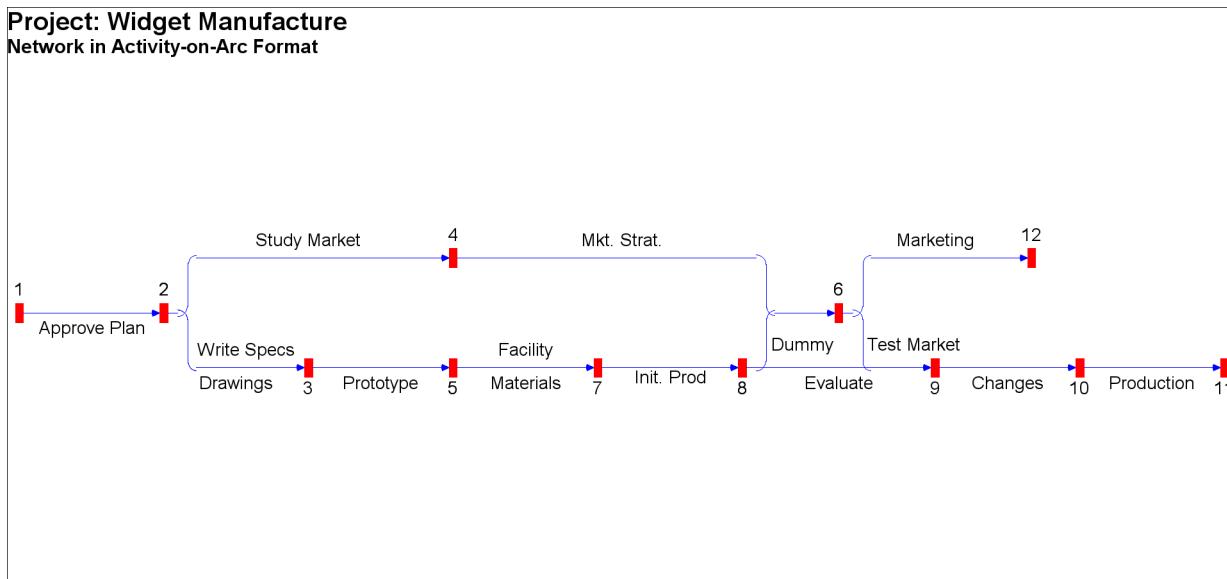

The problem discussed in [Example 4.1](#) can also be described in an AOA format. The network is illustrated in [Output 4.2.1](#). The network has an arc labeled ‘Dummy’, which is required to accurately capture all the precedence relationships. Dummy arcs are often needed when representing scheduling problems in AOA format.

The following DATA step saves the network description in a SAS data set, WIDGAOA. The data set contains the minimum amount of information required by PROC CPM for an activity network in AOA format, namely, the TAILNODE and HEADNODE variables, which indicate the direction of each arc in the network and the DURATION variable which gives the length of each task. In addition, the data set also contains a variable identifying the name of the task associated with each arc. This variable, task, can be identified to PROC CPM using the ACTIVITY statement. PROC CPM treats each observation in the data set as a new task, thus enabling you to specify multiple arcs between a pair of nodes. In this example, for instance, both the tasks ‘Drawings’ and ‘Write Specs’ connect the nodes 2 and 3; likewise, both the tasks ‘Materials’ and ‘Facility’ connect the nodes 5 and 7. If multiple arcs are not allowed, you would need more dummy arcs in this example. However, the dummy arc between nodes 8 and 6 is essential to the structure of the network and cannot be eliminated.

As in [Example 4.1](#), the data set DETAILS containing additional activity information, can be merged with the Activity data set and used as input to PROC CPM to determine the project schedule. For purposes of display (in Gantt charts, and so on) the dummy activity has been given a label, ‘Production Milestone’. [Output 4.2.2](#) displays the project schedule.

```
/* Activity-on-Arc representation of the project */
data widgaoa;
  format task $12. ;
  input task & days tail head;
  datalines;
```

```

Approve Plan      5   1   2
Drawings         10  2   3
Study Market     5   2   4
Write Specs      5   2   3
Prototype        15  3   5
Mkt. Strat.     10  4   6
Materials        10  5   7
Facility          10  5   7
Init. Prod.      10  7   8
Evaluate          10  8   9
Test Market      15  6   9
Changes           5   9  10
Production        0  10  11
Marketing          0   6  12
Dummyy            0   8   6
;

data details;
  format task $12. dept $13. descrpt $30.;
  input task & dept $ descrpt & ;
  label dept = "Department"
    descrpt = "Activity Description";
  datalines;
Approve Plan  Planning      Finalize and Approve Plan
Drawings       Engineering   Prepare Drawings
Study Market   Marketing    Analyze Potential Markets
Write Specs    Engineering   Write Specifications
Prototype      Engineering   Build Prototype
Mkt. Strat.    Marketing    Develop Marketing Concept
Materials      Manufacturing Procure Raw Materials
Facility        Manufacturing Prepare Manufacturing Facility
Init. Prod.     Manufacturing Initial Production Run
Evaluate        Testing      Evaluate Product In-House
Test Market    Testing      Mail Product to Sample Market
Changes         Engineering  Engineering Changes
Production      Manufacturing Begin Full Scale Production
Marketing       Marketing    Begin Full Scale Marketing
Dummyy          .           Production Milestone
;

data widgeta;
  merge widgaoa details;
  run;

/*
 * The project is scheduled using PROC CPM */
/*
 * The network information is conveyed using the TAILNODE */
/*
 * and HEADNODE statements. The ID statement is used to */
/*
 * transfer project information to the output data set */
proc cpm data=widgeta date='1dec03'd out=save;
  tailnode tail;
  headnode head;
  duration days;
  activity task;

```

```

id dept descrpt;
run;

proc sort;
by e_start;
run;

title 'Widget Manufacture: Activity-On-Arc Format';
title2 'Project Schedule';
proc print;
id descrpt;
var dept e_: l_: t_float f_float;
run;

```

**Output 4.2.2** Critical Path: Activity-on-Arc Format

**Widget Manufacture: Activity-On-Arc Format  
Project Schedule**

descrpt	dept	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
Finalize and Approve Plan	Planning	01DEC03	05DEC03	01DEC03	05DEC03	0	0
Prepare Drawings	Engineering	06DEC03	15DEC03	06DEC03	15DEC03	0	0
Analyze Potential Markets	Marketing	06DEC03	10DEC03	05JAN04	09JAN04	30	0
Write Specifications	Engineering	06DEC03	10DEC03	11DEC03	15DEC03	5	5
Develop Marketing Concept	Marketing	11DEC03	20DEC03	10JAN04	19JAN04	30	30
Build Prototype	Engineering	16DEC03	30DEC03	16DEC03	30DEC03	0	0
Procure Raw Materials	Manufacturing	31DEC03	09JAN04	31DEC03	09JAN04	0	0
Prepare Manufacturing Facility	Manufacturing	31DEC03	09JAN04	31DEC03	09JAN04	0	0
Initial Production Run	Manufacturing	10JAN04	19JAN04	10JAN04	19JAN04	0	0
Evaluate Product In-House	Testing	20JAN04	29JAN04	25JAN04	03FEB04	5	5
Mail Product to Sample Market	Testing	20JAN04	03FEB04	20JAN04	03FEB04	0	0
Begin Full Scale Marketing	Marketing	20JAN04	20JAN04	09FEB04	09FEB04	20	20
Production Milestone		20JAN04	20JAN04	20JAN04	20JAN04	0	0
Engineering Changes	Engineering	04FEB04	08FEB04	04FEB04	08FEB04	0	0
Begin Full Scale Production	Manufacturing	09FEB04	09FEB04	09FEB04	09FEB04	0	0

---

## Example 4.3: Meeting Project Deadlines

This example illustrates the use of the project finish date (using the FBDATE= option) to specify a deadline on the project. In the following program it is assumed that the project data are saved in the data set WIDGAOA. PROC CPM is first invoked with the FBDATE= option. [Output 4.3.1](#) shows the resulting schedule. The entire schedule is shifted in time (as compared to the schedule in [Output 4.2.2](#)) so that the end of the project is on March 1, 2004. The second part of the program specifies a project start date in addition to the project finish date using both the DATE= and FBDATE= options. The schedule displayed in [Output 4.3.2](#) shows that all of the activities have a larger float than before due to the imposition of a less stringent target date.

```

proc cpm data=widgaoa
  fbdays='1mar04'd interval=day;
  tailnode tail;
  headnode head;
  duration days;
  id task;
  run;

proc sort;
  by e_start;
  run;

title 'Meeting Project Deadlines';
title2 'Specification of Project Finish Date';
proc print;
  id task;
  var e_: l_: t_float f_float;
  run;

proc cpm data=widgaoa
  fbdays='1mar04'd
  date='1dec03'd interval=day;
  tailnode tail;
  headnode head;
  duration days;
  id task;
  run;

proc sort;
  by e_start;
  run;

title2 'Specifying Project Start and Completion Dates';
proc print;
  id task;
  var e_: l_: t_float f_float;
  run;

```

**Output 4.3.1** Meeting Project Deadlines: FBDATE= Option

**Meeting Project Deadlines**  
**Specification of Project Finish Date**

task	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
Approve Plan	22DEC03	26DEC03	22DEC03	26DEC03	0	0
Drawings	27DEC03	05JAN04	27DEC03	05JAN04	0	0
Study Market	27DEC03	31DEC03	26JAN04	30JAN04	30	0
Write Specs	27DEC03	31DEC03	01JAN04	05JAN04	5	5
Mkt. Strat.	01JAN04	10JAN04	31JAN04	09FEB04	30	30
Prototype	06JAN04	20JAN04	06JAN04	20JAN04	0	0
Materials	21JAN04	30JAN04	21JAN04	30JAN04	0	0
Facility	21JAN04	30JAN04	21JAN04	30JAN04	0	0
Init. Prod.	31JAN04	09FEB04	31JAN04	09FEB04	0	0
Evaluate	10FEB04	19FEB04	15FEB04	24FEB04	5	5
Test Market	10FEB04	24FEB04	10FEB04	24FEB04	0	0
Marketing	10FEB04	10FEB04	01MAR04	01MAR04	20	20
Dummy	10FEB04	10FEB04	10FEB04	10FEB04	0	0
Changes	25FEB04	29FEB04	25FEB04	29FEB04	0	0
Production	01MAR04	01MAR04	01MAR04	01MAR04	0	0

**Output 4.3.2** Meeting Project Deadlines: DATE= and FBDATE= Options

**Meeting Project Deadlines**  
**Specifying Project Start and Completion Dates**

task	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
Approve Plan	01DEC03	05DEC03	22DEC03	26DEC03	21	0
Drawings	06DEC03	15DEC03	27DEC03	05JAN04	21	0
Study Market	06DEC03	10DEC03	26JAN04	30JAN04	51	0
Write Specs	06DEC03	10DEC03	01JAN04	05JAN04	26	5
Mkt. Strat.	11DEC03	20DEC03	31JAN04	09FEB04	51	30
Prototype	16DEC03	30DEC03	06JAN04	20JAN04	21	0
Materials	31DEC03	09JAN04	21JAN04	30JAN04	21	0
Facility	31DEC03	09JAN04	21JAN04	30JAN04	21	0
Init. Prod.	10JAN04	19JAN04	31JAN04	09FEB04	21	0
Evaluate	20JAN04	29JAN04	15FEB04	24FEB04	26	5
Test Market	20JAN04	03FEB04	10FEB04	24FEB04	21	0
Marketing	20JAN04	20JAN04	01MAR04	01MAR04	41	41
Dummy	20JAN04	20JAN04	10FEB04	10FEB04	21	0
Changes	04FEB04	08FEB04	25FEB04	29FEB04	21	0
Production	09FEB04	09FEB04	01MAR04	01MAR04	21	21

---

## Example 4.4: Displaying the Schedule on a Calendar

This example shows how you can use the output from CPM to display calendars containing the critical path schedule and the early start schedule. The example uses the network described in [Example 4.2](#) and assumes that the data set SAVE contains the project schedule. The following program invokes PROC CALENDAR to produce two calendars; the first calendar in [Output 4.4.1](#) displays only the critical activities in the project, while the second calendar in [Output 4.4.1](#) displays all the activities in the project. In both invocations of PROC CALENDAR, a WHERE statement is used to display only the activities that are scheduled to finish in December.

```

proc cpm data=widgaoa out=save
  date='1dec03'd interval=day;
  tailnode tail;
  headnode head;
  duration days;
  id task;
  run;

proc sort data=save out=crit;
  where t_float=0;
  by e_start;
  run;

title 'Printing the Schedule on a Calendar';
title2 'Critical Activities in December';

/* print the critical act. calendar */
options nodate pageno=1 pagesize=50;

proc calendar schedule
  data=crit;
  id e_start;
  where e_finish <= '31dec03'd;
  var task;
  dur days;
  run;

/* sort data for early start calendar */
proc sort data=save;
  by e_start;

/* print the early start calendar */
title2 'Early Start Schedule for December';
options nodate pageno=1 pagesize=50;
proc calendar schedule data=save;
  id e_start;
  where e_finish <= '31dec03'd;
  var task;
  dur days;
  run;

```

## **Output 4.4.1 Project Calendar: All Activities**

### **Printing the Schedule on a Calendar Critical Activities in December**

**Output 4.4.1 continued****Printing the Schedule on a Calendar  
Early Start Schedule for December**

December 2003						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1	2	3	4	5	6
						+Write Sp>
						+Study Ma>
			Approve Plan			+Drawings>
7	8	9	10	11	12	13
						<=====Write Specs=====+
						<=====Study Market=====+  +Mkt. Strat.=====
						<=====Drawings=====+
14	15	16	17	18	19	20
						<=====Mkt. Strat.=====+
						<=====Drawings=====+  +Prototype=====+
21	22	23	24	25	26	27
						<=====Prototype=====+
28	29	30	31			
						<=====Prototype=====+

---

## Example 4.5: Precedence Gantt Chart

This example produces a Gantt chart of the schedule obtained from PROC CPM. The example uses the network described in [Example 4.2](#) (AOA format) and assumes that the data set `SAVE` contains the schedule produced by PROC CPM and sorted by the variable `E_START`. The Gantt chart produced shows the early and late start schedules as well as the precedence relationships between the activities. The precedence information is conveyed to PROC GANTT through the `TAILNODE=` and `HEADNODE=` options.

```

data details;
  input task $ 1-12 dept $ 15-27 descrpt $ 30-59;
  label dept = "Department"
    descrpt = "Activity Description";
  datalines;
Dev. Concept Planning      Finalize and Approve Plan
Drawings       Engineering   Prepare Drawings
Study Market  Marketing     Analyze Potential Markets
Write Specs   Engineering   Write Specifications
Prototype     Engineering   Build Prototype
Mkt. Strat.   Marketing    Develop Marketing Concept
Materials     Manufacturing Procure Raw Materials
Facility      Manufacturing Prepare Manufacturing Facility
Init. Prod.   Manufacturing Initial Production Run
Evaluate      Testing       Evaluate Product In-House
Test Market   Testing       Test Product in Sample Market
Changes       Engineering   Engineering Changes
Production   Manufacturing Begin Full Scale Production
Marketing    Marketing     Begin Full Scale Marketing
Dummy        Marketing     Production Milestone
;

data widgeta;
  merge widgaoa details;
  run;


* specify the device on which you want the chart printed;
options vpos=50 hpos=80 border;

title 'Precedence Gantt Chart';
title2 'Early and Late Start Schedule';

proc gantt graphics data=save;
  chart / compress tailnode=tail headnode=head
    height=2 nojobnum skip=2
    cprec=cyan cmile=magenta
    caxis=black
    dur=days increment=7 nolegend;
  id descrpt;
  run;

```

### Output 4.5.1 Gantt Chart of Project

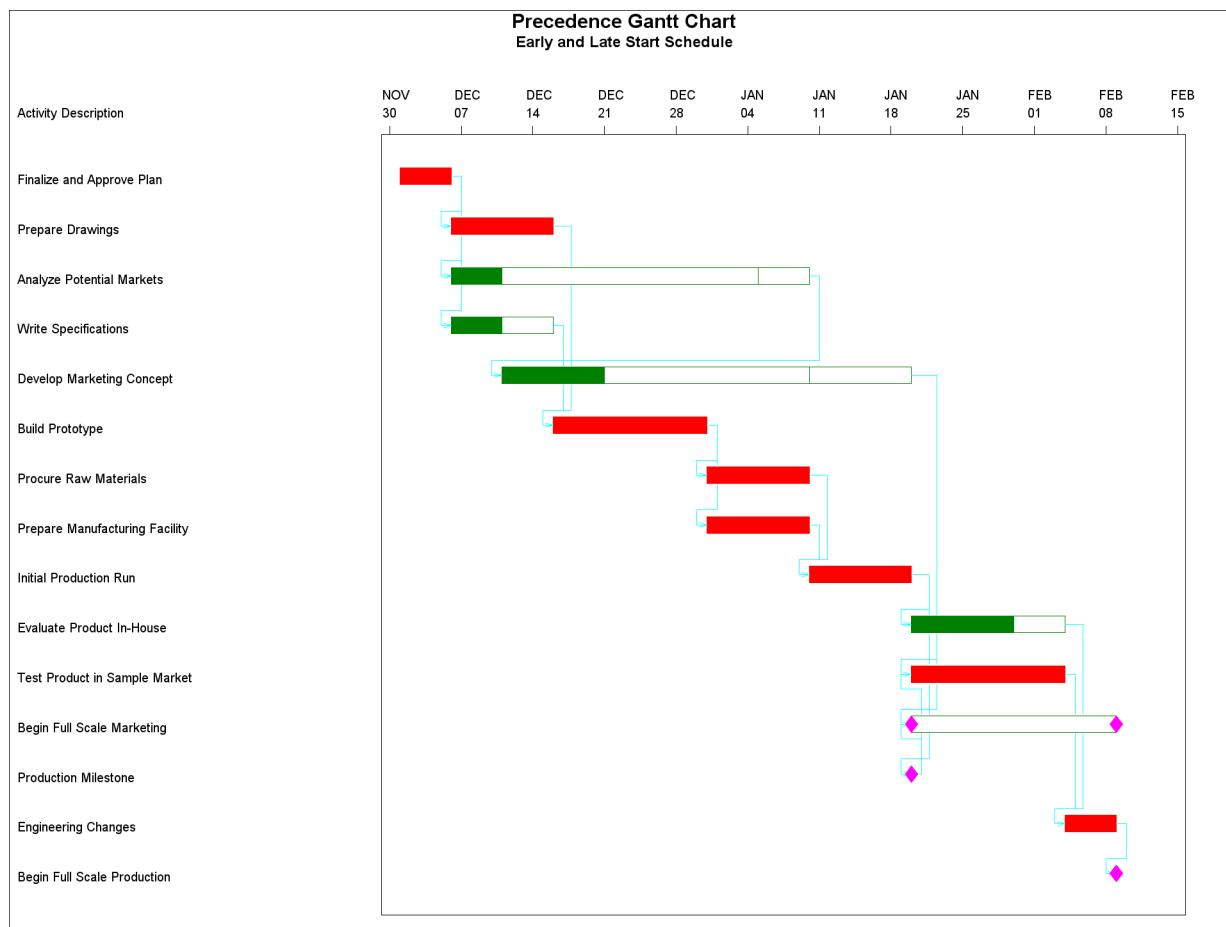

## Example 4.6: Changing Duration Units

This example illustrates the use of the INTERVAL= option to identify the units of duration to PROC CPM. In the previous examples, it was assumed that work can be done on the activities all seven days of the week without any break. Suppose now that you want to schedule the activities only on weekdays. To do so, specify INTERVAL=WEEKDAY in the PROC CPM statement. Output 4.6.1 displays the schedule produced by PROC CPM. Note that, with a shorter work week, the project finishes on March 8, 2004, instead of on February 9, 2004.

```

proc cpm data=widget out=save
    date='1dec03'd interval=weekday;
activity task;
succ    succ1 succ2 succ3;
duration days;
run;

title 'Changing Duration Units';
title2 'INTERVAL=WEEKDAY';
proc print;

```

```
id task;
var e_: l_: t_float f_float;
run;
```

**Output 4.6.1** Changing Duration Units: INTERVAL=WEEKDAY

**Changing Duration Units**  
**INTERVAL=WEEKDAY**

task	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
Approve Plan	01DEC03	05DEC03	01DEC03	05DEC03	0	0
Drawings	08DEC03	19DEC03	08DEC03	19DEC03	0	0
Study Market	08DEC03	12DEC03	19JAN04	23JAN04	30	0
Write Specs	08DEC03	12DEC03	15DEC03	19DEC03	5	5
Prototype	22DEC03	09JAN04	22DEC03	09JAN04	0	0
Mkt. Strat.	15DEC03	26DEC03	26JAN04	06FEB04	30	30
Materials	12JAN04	23JAN04	12JAN04	23JAN04	0	0
Facility	12JAN04	23JAN04	12JAN04	23JAN04	0	0
Init. Prod.	26JAN04	06FEB04	26JAN04	06FEB04	0	0
Evaluate	09FEB04	20FEB04	16FEB04	27FEB04	5	5
Test Market	09FEB04	27FEB04	09FEB04	27FEB04	0	0
Changes	01MAR04	05MAR04	01MAR04	05MAR04	0	0
Production	08MAR04	08MAR04	08MAR04	08MAR04	0	0
Marketing	09FEB04	09FEB04	08MAR04	08MAR04	20	20

To display the weekday schedule on a calendar, use the WEEKDAY option in the PROC CALENDAR statement. The following code sorts the Schedule data set by the E\_START variable and produces a calendar shown in [Output 4.6.2](#), which displays the schedule of activities for the month of December.

```
proc sort;
  by e_start;
  run;

/* truncate schedule: print only for december */
data december;
  set save;
  e_finish = min('31dec03'd, e_finish);
  if e_start <= '31dec03'd;
  run;

title3 'Calendar of Schedule';
options nodate pageno=1 ps=50;
proc calendar data=december schedule weekdays;
  id e_start;
  finish e_finish;
  var task;
  run;
```

**Output 4.6.2** Changing Duration Units: WEEKDAY Calendar for December

**Changing Duration Units**  
**INTERVAL=WEEKDAY**  
**Calendar of Schedule**

December 2003					
Monday	Tuesday	Wednesday	Thursday	Friday	
1	2	3	4	5	
+=====Approve Plan=====+					
8	9	10	11	12	
+=====Write Specs=====+					
+=====Study Market=====+					
+=====Drawings=====>					
15	16	17	18	19	
+=====Mkt. Strat.=====>					
<=====Drawings=====+					
22	23	24	25	26	
+=====Prototype=====>					
<=====Mkt. Strat.=====+					
29	30	31			
<=====Prototype=====+					

The durations of the activities in the project are multiples of 5. Thus, if work is done only on weekdays, all activities in the project last 0, 1, 2, or 3 weeks. The INTERVAL= option can also be used to set the units of duration to hours, minutes, seconds, years, months, quarters, or weeks. In this example, the data set WIDGWK is created from WIDGET to set the durations in weeks. PROC CPM is then invoked with INTERVAL=WEEK, and the resulting schedule is displayed in **Output 4.6.3**. Note that the float values are also expressed in units of weeks.

```

data widgwk;
  set widget;
  weeks = days / 5;
  run;

proc cpm data=widgwk date='1dec03'd interval=week;
  activity task;
  successor succ1 succ2 succ3;
  duration weeks;
  id task;
  run;

title2 'INTERVAL=WEEK';
proc print;
  id task;
  var e_: l_: t_float f_float;
  run;

```

#### Output 4.6.3 Changing Duration Units: INTERVAL=WEEK

### Changing Duration Units INTERVAL=WEEK

task	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
Approve Plan	01DEC03	07DEC03	01DEC03	07DEC03	0	0
Drawings	08DEC03	21DEC03	08DEC03	21DEC03	0	0
Study Market	08DEC03	14DEC03	19JAN04	25JAN04	6	0
Write Specs	08DEC03	14DEC03	15DEC03	21DEC03	1	1
Prototype	22DEC03	11JAN04	22DEC03	11JAN04	0	0
Mkt. Strat.	15DEC03	28DEC03	26JAN04	08FEB04	6	6
Materials	12JAN04	25JAN04	12JAN04	25JAN04	0	0
Facility	12JAN04	25JAN04	12JAN04	25JAN04	0	0
Init. Prod.	26JAN04	08FEB04	26JAN04	08FEB04	0	0
Evaluate	09FEB04	22FEB04	16FEB04	29FEB04	1	1
Test Market	09FEB04	29FEB04	09FEB04	29FEB04	0	0
Changes	01MAR04	07MAR04	01MAR04	07MAR04	0	0
Production	08MAR04	08MAR04	08MAR04	08MAR04	0	0
Marketing	09FEB04	09FEB04	08MAR04	08MAR04	4	4

---

## Example 4.7: Controlling the Project Calendar

This example illustrates the use of the INTERVAL=, DAYSTART=, and DAYLENGTH= options to control the project calendar. In Example 4.1 through Example 4.5, none of these three options is specified; hence the durations are assumed to be days (INTERVAL=DAY), and work is scheduled on all seven days of the week. In Example 4.6, the specification of INTERVAL=WEEKDAY causes the schedule to skip weekends. The present example shows further ways of controlling the project calendar. For example, you may want to control the work pattern during a standard week or the start and length of the workday.

Suppose you want to schedule the project specified in Example 4.1 but you want to schedule only on weekdays from 9 a.m. to 5 p.m. To schedule the project, use the INTERVAL=WORKDAY option rather than the default INTERVAL=DAY. Then, one unit of duration is interpreted as eight hours of work. To schedule the manufacturing project to start on December 1, with an eight-hour workday and a five-day work week, you can invoke PROC CPM with the following statements. Output 4.7.1 displays the resulting schedule; the start and finish times are expressed in SAS datetime values.

```
title 'Controlling the Project Calendar';
title2 'Scheduling on Workdays';
proc cpm data=widget date='1dec03'd interval=workday;
activity task;
succ    succ1 succ2 succ3;
duration days;
run;

title3 'Day Starts at 9 a.m.';
proc print;
id task;
var e_: l_: t_float f_float;
run;
```

**Output 4.7.1** Controlling the Project Calendar: INTERVAL=WORKDAY

**Controlling the Project Calendar**  
**Scheduling on Workdays**  
**Day Starts at 9 a.m.**

task	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
Approve Plan	01DEC03:09:00:00	05DEC03:16:59:59	01DEC03:09:00:00	05DEC03:16:59:59	0	0
Drawings	08DEC03:09:00:00	19DEC03:16:59:59	08DEC03:09:00:00	19DEC03:16:59:59	0	0
Study Market	08DEC03:09:00:00	12DEC03:16:59:59	19JAN04:09:00:00	23JAN04:16:59:59	30	0
Write Specs	08DEC03:09:00:00	12DEC03:16:59:59	15DEC03:09:00:00	19DEC03:16:59:59	5	5
Prototype	22DEC03:09:00:00	09JAN04:16:59:59	22DEC03:09:00:00	09JAN04:16:59:59	0	0
Mkt. Strat.	15DEC03:09:00:00	26DEC03:16:59:59	26JAN04:09:00:00	06FEB04:16:59:59	30	30
Materials	12JAN04:09:00:00	23JAN04:16:59:59	12JAN04:09:00:00	23JAN04:16:59:59	0	0
Facility	12JAN04:09:00:00	23JAN04:16:59:59	12JAN04:09:00:00	23JAN04:16:59:59	0	0
Init. Prod.	26JAN04:09:00:00	06FEB04:16:59:59	26JAN04:09:00:00	06FEB04:16:59:59	0	0
Evaluate	09FEB04:09:00:00	20FEB04:16:59:59	16FEB04:09:00:00	27FEB04:16:59:59	5	5
Test Market	09FEB04:09:00:00	27FEB04:16:59:59	09FEB04:09:00:00	27FEB04:16:59:59	0	0
Changes	01MAR04:09:00:00	05MAR04:16:59:59	01MAR04:09:00:00	05MAR04:16:59:59	0	0
Production	08MAR04:09:00:00	08MAR04:09:00:00	08MAR04:09:00:00	08MAR04:09:00:00	0	0
Marketing	09FEB04:09:00:00	09FEB04:09:00:00	08MAR04:09:00:00	08MAR04:09:00:00	20	20

If you want to change the length of the workday, use the DAYLENGTH= option in the PROC CPM statement. For example, if you want an eight-and-a-half hour workday instead of the default eight-hour workday, you should include DAYLENGTH='08:30't in the PROC CPM statement. In addition, you might also want to change the start of the workday. The workday starts at 9 a.m., by default. To change the default, use the DAYSTART= option. The following program schedules the project to start at 7 a.m. on December 1. The project is scheduled on eight-and-a-half hour workdays each starting at 7 a.m. Output 4.7.2 displays the resulting schedule produced by PROC CPM.

```
proc cpm data=widget date='1dec03'd interval=workday
           daylength='08:30't daystart='07:00't;
   activity task;
   succ    succ1 succ2 succ3;
   duration days;
   run;

title3 'Day Starts at 7 a.m. and is 8.5 Hours Long';
proc print;
   id task;
   var e_: l_: t_float f_float;
   run;
```

#### **Output 4.7.2** Controlling the Project Calendar: DAYSTART and DAYLENGTH

**Controlling the Project Calendar  
Scheduling on Workdays  
Day Starts at 7 a.m. and is 8.5 Hours Long**

task	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
Approve Plan	01DEC03:07:00:00	05DEC03:15:29:59	01DEC03:07:00:00	05DEC03:15:29:59	0	0
Drawings	08DEC03:07:00:00	19DEC03:15:29:59	08DEC03:07:00:00	19DEC03:15:29:59	0	0
Study Market	08DEC03:07:00:00	12DEC03:15:29:59	19JAN04:07:00:00	23JAN04:15:29:59	30	0
Write Specs	08DEC03:07:00:00	12DEC03:15:29:59	15DEC03:07:00:00	19DEC03:15:29:59	5	5
Prototype	22DEC03:07:00:00	09JAN04:15:29:59	22DEC03:07:00:00	09JAN04:15:29:59	0	0
Mkt. Strat.	15DEC03:07:00:00	26DEC03:15:29:59	26JAN04:07:00:00	06FEB04:15:29:59	30	30
Materials	12JAN04:07:00:00	23JAN04:15:29:59	12JAN04:07:00:00	23JAN04:15:29:59	0	0
Facility	12JAN04:07:00:00	23JAN04:15:29:59	12JAN04:07:00:00	23JAN04:15:29:59	0	0
Init. Prod.	26JAN04:07:00:00	06FEB04:15:29:59	26JAN04:07:00:00	06FEB04:15:29:59	0	0
Evaluate	09FEB04:07:00:00	20FEB04:15:29:59	16FEB04:07:00:00	27FEB04:15:29:59	5	5
Test Market	09FEB04:07:00:00	27FEB04:15:29:59	09FEB04:07:00:00	27FEB04:15:29:59	0	0
Changes	01MAR04:07:00:00	05MAR04:15:29:59	01MAR04:07:00:00	05MAR04:15:29:59	0	0
Production	08MAR04:07:00:00	08MAR04:07:00:00	08MAR04:07:00:00	08MAR04:07:00:00	0	0
Marketing	09FEB04:07:00:00	09FEB04:07:00:00	08MAR04:07:00:00	08MAR04:07:00:00	20	20

An alternate way of specifying the start of each working day is to set the INTERVAL= option to DTWRKDAY and specify a SAS datetime value for the project start date. Using INTERVAL=DTWRKDAY tells CPM that the DATE= option is a SAS datetime value and that the time given is the start of the workday. For the present example, you could have used DATE='1dec03:07:00'dt in conjunction with the specification INTERVAL=DTWRKDAY and DAYLENGTH='08:30't.

---

## Example 4.8: Scheduling around Holidays

This example shows how you can schedule around holidays with PROC CPM. First, save a list of holidays in a SAS data set as SAS date variables. The length of the holidays is assumed to be measured in units specified by the INTERVAL= option. By default, all holidays are assumed to be one unit long. You can control the length of each holiday by specifying either the finish time for each holiday or the length of each holiday in the same observation as the holiday specification.

### Output 4.8.1 Scheduling around Holidays: HOLIDAYS Data Set

#### Scheduling Around Holidays Data Set HOLIDAYS

Obs	holiday	holifin	holidur
1	24DEC03	26DEC03	4
2	01JAN04	.	.

For example, the data set HOLIDAYS, displayed in Output 4.8.1 specifies two holidays, one for Christmas and the other for New Year's Day. The variable holiday specifies the start of each holiday. The variable holifin specifies the end of the Christmas holiday as 26Dec03. Alternately, the variable holidur can be used to interpret the Christmas holiday as lasting four interval units starting from the 24th of December. If the variable holidur is used, the actual days when work is not done depends on the INTERVAL= option and on the underlying calendar used. This form of specifying holidays or breaks is useful for indicating vacations for specific employees. The second observation in the data set defines the New Year's holiday as just one day long because both the variables holifin and holidur variables have missing values.

To invoke PROC CPM to schedule around holidays, use the HOLIDATA= option in the PROC CPM statement (see the following program) to identify the data set, and list the names of the variables in the data set in a HOLIDAY statement. The holiday start and finish are identified by specifying the HOLIDAY and HOLIFIN variables. Output 4.8.2 displays the schedule obtained.

```

proc cpm data=widget holidata=holidays
    out=saveh date='1dec03'd ;
activity task;
succ    succ1 succ2 succ3;
duration days;
holiday  holiday / holifin=(holifin);
run;

proc sort data=saveh;
by e_start;
run;
pattern1 c=green v=s;      /* duration of a non-critical activity */
pattern2 c=green v=e;      /* slack time for a noncrit. activity */
pattern3 c=red   v=s;      /* duration of a critical activity */
pattern4 c=magenta v=e;   /* slack time for a supercrit. activity */
pattern5 c=magenta v=s;   /* duration of a supercrit. activity */
pattern6 c=cyan  v=s;     /* actual duration of an activity */
pattern7 c=black v=e;     /* break due to a holiday */

goptions vpos=50 hpos=80 border;

```


```

title 'Scheduling Around Holidays';
title2 'Project Schedule';

proc gantt graphics data=saveh holidata=holidays;
  chart / compress
    height=1.7 nojobnum skip=2
    dur=days increment=7
    holiday=(holiday) holifin=(holifin);

  id task;
  run;

```

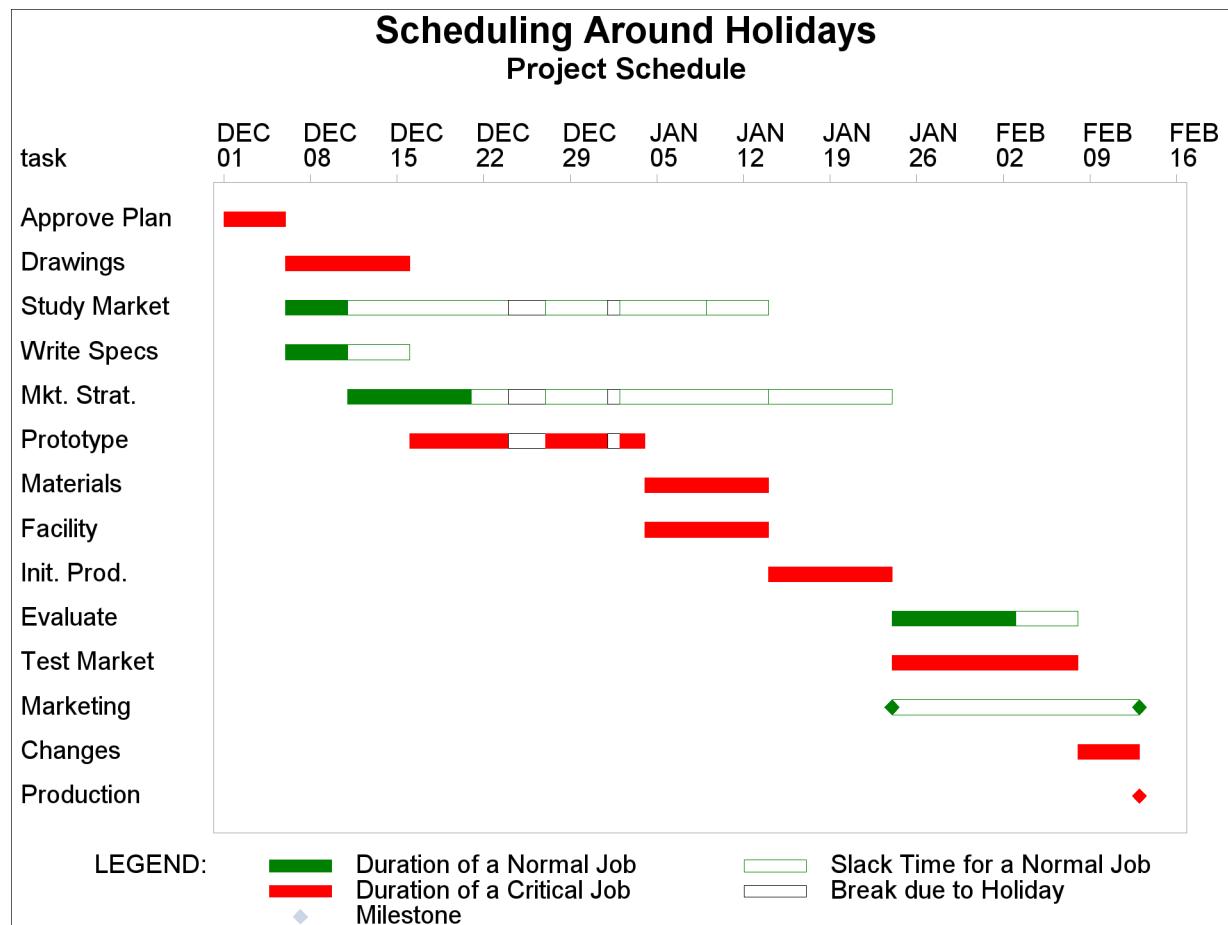**Output 4.8.2** Scheduling around Holidays: Project Schedule

The next two invocations illustrate the use of the HOLIDUR= option and the effect of the INTERVAL= option on the duration of the holidays. Recall that the holiday duration is also assumed to be in *interval* units where *interval* is the value specified for the INTERVAL= option. Suppose that a holiday period for the entire project starts on December 24, 2003, with duration specified as 4. First the project is scheduled with INTERVAL=DAY so that the holidays are on December 24, 25, 26, and 27, 2003. [Output 4.8.3](#) displays the resulting schedule. The project completion is delayed by one day due to the extra holiday on December 27, 2003.

```


proc cpm data=widget holidata=holidays
    out=saveh1 date='1dec03'd
    interval=day;
activity task;
succ    succ1 succ2 succ3;
duration days;
holiday  holiday / holidur=(holidur);
run;

title2 'Variable Length Holidays : INTERVAL=DAY';
proc sort data=saveh1;
by e_start;
run;

proc gantt graphics data=saveh1 holidata=holidays;
chart / compress
height=1.7 skip=2
nojobnum
dur=days increment=7
holiday=(holiday) holidur=(holidur) interval=day;

id task;
run;

```

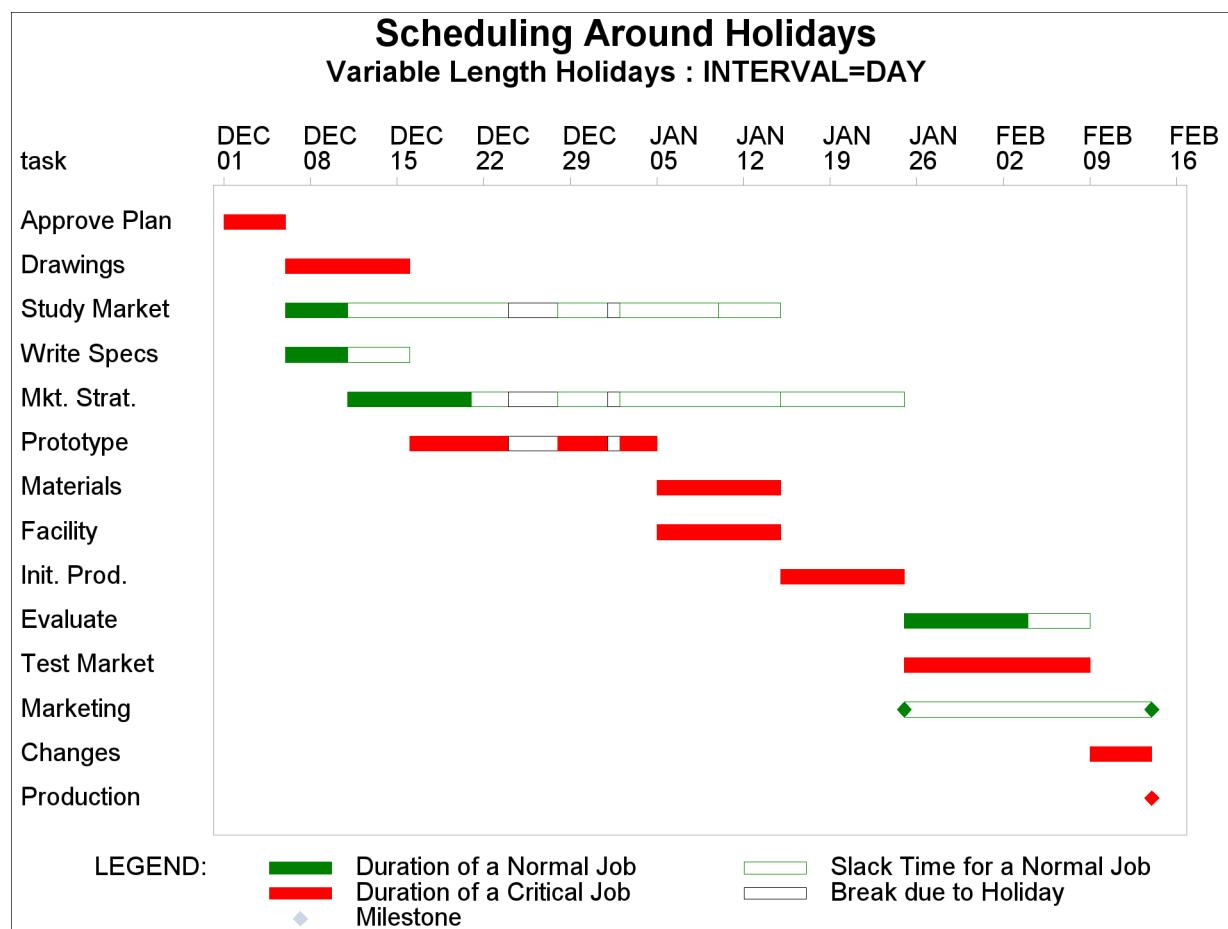**Output 4.8.3** Scheduling around Holidays: INTERVAL=DAY

Next, suppose that work on the project is to be scheduled only on weekdays. The INTERVAL= option is set to WEEKDAY. Then, the value ‘4’ specified for the variable holidur is interpreted as 4 weekdays. Thus, the holidays are on December 24, 25, 26, and 29, 2003, because December 27 and 28 (Saturday and Sunday) are non-working days anyway. (Note that if holifin had been used, the holiday would have ended on December 26, 2003.) The following statements schedule the project to start on December 1, 2003 with INTERVAL=WEEKDAY. Output 4.8.4 displays the resulting schedule. Note the further delay in project completion time.

```

proc cpm data=widget holidata=holidays
    out=saveh2 date='1dec03'd
    interval=weekday;
activity task;
succ    succ1 succ2 succ3;
duration days;
holiday holiday / holidur=(holidur);
run;

proc sort data=saveh2;
by e_start;
run;

```


```

title2 'Variable Length Holidays : INTERVAL=WEEKDAY';
proc gantt graphics data=saveh2 holidata=holidays;
  chart / compress
    height=1.8 skip=2
    nojobnum
    dur=days increment=7
    holiday=(holiday)
    holidur=(holidur)
    interval=weekday;

  id task;
run;

```

**Output 4.8.4** Scheduling around Holidays: INTERVAL=WEEKDAY

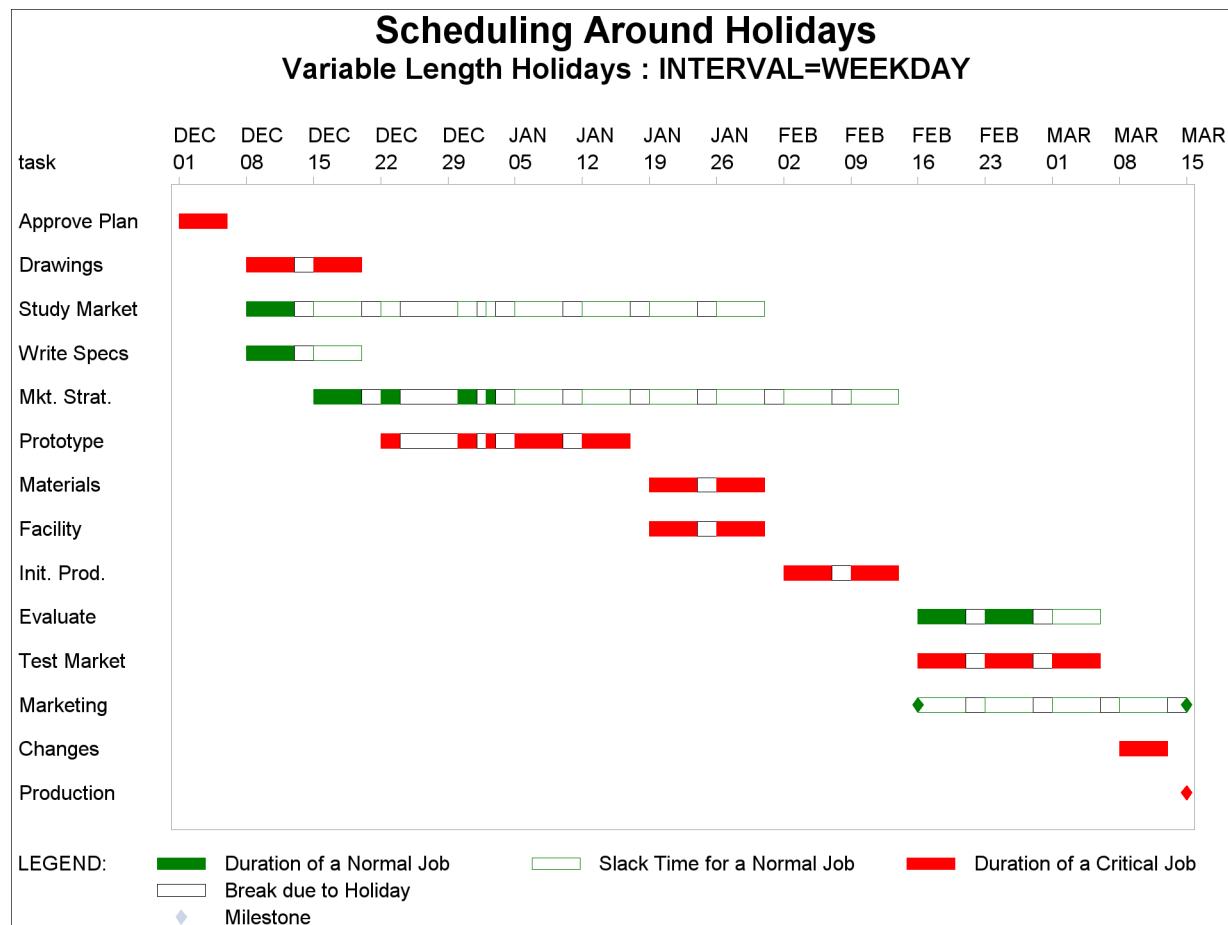

Finally, the same project is scheduled to start on December 1, 2003 with INTERVAL=WORKDAY. Output 4.8.5 displays the resulting Schedule data set. This time the holiday period starts at 5:00 p.m. on December 23, 2003, and ends at 9:00 a.m. on December 30, 2003.


```

proc cpm data=widget holidata=holidays
  out=saveh3 date='1dec03'd
  interval=workday;
  activity task;
  succ    succ1 succ2 succ3;
  duration days;
  holiday  holiday / holidur=(holidur);
  run;

proc sort data=saveh3;
  by e_start;
  run;

title2 'Variable Length Holidays : INTERVAL=WORKDAY';
proc gantt graphics data=saveh3 holidata=holidays;
  chart / compress
    height=1.8 nojobnum skip=2
    dur=days increment=7
    holiday=(holiday) holidur=(holidur) interval=workday;
  id task;
  run;

```

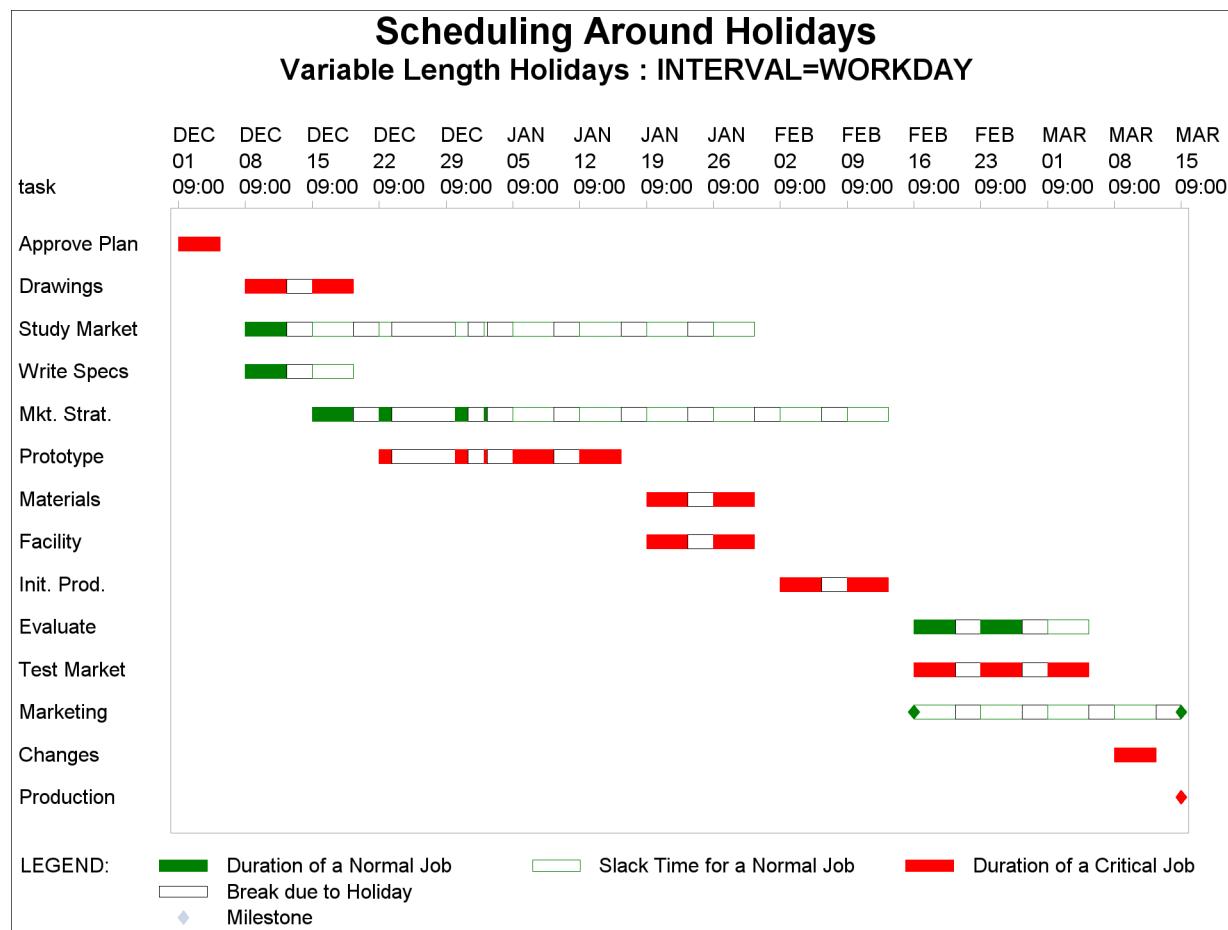**Output 4.8.5** Scheduling around Holidays: INTERVAL=WORKDAY**Example 4.9: CALEDATA and WORKDATA Data Sets**

This example shows how you can schedule the job over a nonstandard day and a nonstandard week. In the first part of the example, the calendar followed is a six-day week with an eight-and-a-half hour workday starting at 7 a.m. The project data are the same as were used in [Example 4.8](#), but some of the durations have been changed to include some fractional values. [Output 4.9.1](#) shows the project data set.

**Output 4.9.1** Data Set WIDGET9: Scheduling on the Six-Day Week

**Scheduling on the 6-Day Week**  
**Data Set WIDGET9**

Obs	task	days	succ1	succ2	succ3
1	Approve Plan	5.5	Drawings	Study Market	Write Specs
2	Drawings	10.0	Prototype		
3	Study Market	5.0	Mkt. Strat.		
4	Write Specs	4.5	Prototype		
5	Prototype	15.0	Materials	Facility	
6	Mkt. Strat.	10.0	Test Market	Marketing	
7	Materials	10.0	Init. Prod.		
8	Facility	10.0	Init. Prod.		
9	Init. Prod.	10.0	Test Market	Marketing	Evaluate
10	Evaluate	10.0	Changes		
11	Test Market	15.0	Changes		
12	Changes	5.0	Production		
13	Production	0.0			
14	Marketing	0.0			

The same Holiday data set is used. To indicate that work is to be done on all days of the week except Sunday, use INTERVAL=DTDAY and define a Calendar data set with a single variable \_SUN\_, and a single observation identifying Sunday as a holiday. The DATA step creating CALENDAR and the invocation of PROC CPM is shown in the following code. [Output 4.9.2](#) displays the resulting schedule.

```
/* Set up a 6-day work week, with Sundays off */
data calendar;
  _sun_='holiday';
  run;

title 'Scheduling on the 6-Day Week';
proc cpm data=widget9 holidata=holidays
  out=savec date='1dec03:07:00'dt
  interval=dtday daylength='08:30't
  calendar=calendar;
activity task;
succ    succ1 succ2 succ3;
duration days;
holiday  holiday / holifin=(holifin);
run;
```

**Output 4.9.2** Scheduling on the Six-Day Week

**Scheduling on the 6-Day Week  
Project Schedule**

Obs	task	days	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
1	Approve Plan	5.5	01DEC03:07:00:00	06DEC03:11:14:59	01DEC03:07:00:00	06DEC03:11:14:59	0.0	0.0
2	Drawings	10.0	06DEC03:11:15:00	18DEC03:11:14:59	06DEC03:11:15:00	18DEC03:11:14:59	0.0	0.0
3	Study Market	5.0	06DEC03:11:15:00	12DEC03:11:14:59	15JAN04:11:15:00	21JAN04:11:14:59	30.0	0.0
4	Write Specs	4.5	06DEC03:11:15:00	11DEC03:15:29:59	13DEC03:07:00:00	18DEC03:11:14:59	5.5	5.5
5	Prototype	15.0	18DEC03:11:15:00	09JAN04:11:14:59	18DEC03:11:15:00	09JAN04:11:14:59	0.0	0.0
6	Mkt. Strat.	10.0	12DEC03:11:15:00	27DEC03:11:14:59	21JAN04:11:15:00	02FEB04:11:14:59	30.0	30.0
7	Materials	10.0	09JAN04:11:15:00	21JAN04:11:14:59	09JAN04:11:15:00	21JAN04:11:14:59	0.0	0.0
8	Facility	10.0	09JAN04:11:15:00	21JAN04:11:14:59	09JAN04:11:15:00	21JAN04:11:14:59	0.0	0.0
9	Init. Prod.	10.0	21JAN04:11:15:00	02FEB04:11:14:59	21JAN04:11:15:00	02FEB04:11:14:59	0.0	0.0
10	Evaluate	10.0	02FEB04:11:15:00	13FEB04:11:14:59	07FEB04:11:15:00	19FEB04:11:14:59	5.0	5.0
11	Test Market	15.0	02FEB04:11:15:00	19FEB04:11:14:59	02FEB04:11:15:00	19FEB04:11:14:59	0.0	0.0
12	Changes	5.0	19FEB04:11:15:00	25FEB04:11:14:59	19FEB04:11:15:00	25FEB04:11:14:59	0.0	0.0
13	Production	0.0	25FEB04:11:15:00	25FEB04:11:15:00	25FEB04:11:15:00	25FEB04:11:15:00	0.0	0.0
14	Marketing	0.0	02FEB04:11:15:00	02FEB04:11:15:00	25FEB04:11:15:00	25FEB04:11:15:00	20.0	20.0

Suppose now that you want to schedule work on a five-and-a-half day week (five full working days starting on Monday and half a working day on Saturday). A full work day is from 8 a.m. to 4 p.m. [Output 4.9.3](#) shows the data set WORKDAT, which is used to define the work pattern for a full day (in the shift variable fullday and a half-day (in the shift variable halfday). [Output 4.9.4](#) displays the Calendar data set, CALDAT, which specifies the appropriate work pattern for each day of the week. The schedule produced by invoking the following program is displayed in [Output 4.9.5](#).

**Output 4.9.3** Workday Data Set

**Scheduling on a Five-and-a-Half-Day Week  
Workdays Data Set**

Obs	fullday	halfday
1	8:00	8:00
2	16:00	12:00

**Output 4.9.4** Calendar Data Set

**Scheduling on a Five-and-a-Half-Day Week  
Calendar Data Set**

Obs	_sun_	_mon_	_tue_	_wed_	_thu_	_fri_	_sat_	d_length
1	holiday	fullday	fullday	fullday	fullday	halfday		8:00

```

proc cpm data=widget9 holidata=holidays
          out=savecw date='1dec03'd
          interval=day
          workday=workdat calendar=caldat;
activity task;
succ    succ1 succ2 succ3;
duration days;
holiday holiday / holifin=(holifin);
run;

```

**Output 4.9.5** Scheduling on a Five-and-a-Half Day Week

**Scheduling on a Five-and-a-Half-Day Week  
Project Schedule**

Obs	task	days	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
1	Approve Plan	5.5	01DEC03:08:00:00	06DEC03:11:59:59	01DEC03:08:00:00	06DEC03:11:59:59	0.0	0.0
2	Drawings	10.0	08DEC03:08:00:00	19DEC03:11:59:59	08DEC03:08:00:00	19DEC03:11:59:59	0.0	0.0
3	Study Market	5.0	08DEC03:08:00:00	12DEC03:15:59:59	20JAN04:08:00:00	26JAN04:11:59:59	30.0	0.0
4	Write Specs	4.5	08DEC03:08:00:00	12DEC03:11:59:59	15DEC03:08:00:00	19DEC03:11:59:59	5.5	5.5
5	Prototype	15.0	19DEC03:12:00:00	13JAN04:11:59:59	19DEC03:12:00:00	13JAN04:11:59:59	0.0	0.0
6	Mkt. Strat.	10.0	13DEC03:08:00:00	30DEC03:11:59:59	26JAN04:12:00:00	06FEB04:15:59:59	30.0	30.0
7	Materials	10.0	13JAN04:12:00:00	26JAN04:11:59:59	13JAN04:12:00:00	26JAN04:11:59:59	0.0	0.0
8	Facility	10.0	13JAN04:12:00:00	26JAN04:11:59:59	13JAN04:12:00:00	26JAN04:11:59:59	0.0	0.0
9	Init. Prod.	10.0	26JAN04:12:00:00	06FEB04:15:59:59	26JAN04:12:00:00	06FEB04:15:59:59	0.0	0.0
10	Evaluate	10.0	07FEB04:08:00:00	19FEB04:15:59:59	13FEB04:12:00:00	26FEB04:11:59:59	5.0	5.0
11	Test Market	15.0	07FEB04:08:00:00	26FEB04:11:59:59	07FEB04:08:00:00	26FEB04:11:59:59	0.0	0.0
12	Changes	5.0	26FEB04:12:00:00	03MAR04:15:59:59	26FEB04:12:00:00	03MAR04:15:59:59	0.0	0.0
13	Production	0.0	04MAR04:08:00:00	04MAR04:08:00:00	04MAR04:08:00:00	04MAR04:08:00:00	0.0	0.0
14	Marketing	0.0	07FEB04:08:00:00	07FEB04:08:00:00	04MAR04:08:00:00	04MAR04:08:00:00	20.0	20.0

Note that, in this case, it was not necessary to specify the DAYLENGTH=, DAYSTART=, or INTERVAL= option in the PROC CPM statement. The default value of INTERVAL=DAY is assumed, and the CALDAT and WORKDAT data sets define the workday and work week completely. The length of a standard working day is also included in the Calendar data set, completing all the necessary specifications.

To visualize the breaks in the work schedule created by these specifications, you can use the following simple data set with a dummy activity ‘Schedule Breaks’ to produce a Gantt chart, shown in [Output 4.9.6](#). The period illustrated on the chart is from December 19, 2003 to December 27, 2003. The breaks are denoted by \*.

```

/* To visualize the breaks, use following "dummy" data set
   to plot a schedule bar showing holidays and breaks */
data temp;
e_start='19dec03:08:00'dt;
e_finish='27dec03:23:59:59'dt;
task='Schedule Breaks';
label task='Project Calendar';
format e_start e_finish datetime16.;
run;

```

```

title2 'Holidays and Breaks in the Project Calendar';
proc gantt data=temp lineprinter
    calendar=caldat holidata=holidays
    workday=workdat;
chart / interval=dtday mininterval=dthour skip=0
    holiday=(holiday) holifin=(holifin) markbreak
    nojobnum nolegend increment=8 holichar='*';
id task;
run;

```

#### **Output 4.9.6 Gantt Chart Showing Breaks and Holidays**

#### **Scheduling on a Five-and-a-Half-Day Week Holidays and Breaks in the Project Calendar**

	DEC	DEC	DEC	DEC	DEC	DEC
Project	19	19	20	20	20	21
Calendar	08:00	16:00	00:00	08:00	16:00	00:00
-----+-----+-----+-----+-----+						
Schedule Breaks	<-----*****----- -----*****-----					
	-----+-----+-----+-----+-----+					

#### **Scheduling on a Five-and-a-Half-Day Week Holidays and Breaks in the Project Calendar**

DEC	DEC	DEC	DEC	DEC	DEC	DEC	DEC
21	21	21	22	22	22	23	23
00:00	08:00	16:00	00:00	08:00	16:00	00:00	08:00
-----+-----+-----+-----+-----+							
*****----- -----*****-----							
-----+-----+-----+-----+-----+							

#### **Scheduling on a Five-and-a-Half-Day Week Holidays and Breaks in the Project Calendar**

DEC	DEC	DEC	DEC	DEC	DEC	DEC	DEC
23	23	24	24	24	25	25	25
08:00	16:00	00:00	08:00	16:00	00:00	08:00	16:00
-----+-----+-----+-----+-----+							
-----*****----- -----*****-----							
-----+-----+-----+-----+-----+							

#### **Scheduling on a Five-and-a-Half-Day Week Holidays and Breaks in the Project Calendar**

DEC	DEC	DEC	DEC	DEC	DEC	DEC	DEC
25	26	26	26	27	27	27	28
16:00	00:00	08:00	16:00	00:00	08:00	16:00	00:00
-----+-----+-----+-----+-----+							
*****----- -----*****-----							
-----+-----+-----+-----+-----+							

---

## Example 4.10: Multiple Calendars

This example illustrates the use of multiple calendars within a project. Different scenarios are presented to show the use of different calendars and how project schedules are affected. Output 4.10.1 shows the data set WORKDATA, which defines several shift patterns. These shift patterns are appropriately associated with three different calendars in the data set CALENDAR, also shown in the same output. The three calendars are defined as follows:

- The DEFAULT calendar has five eight-hour days (Monday through Friday) and holidays on Saturday and Sunday.
- The calendar OVT\_CAL specifies an overtime calendar that has 10-hour work days on Monday through Friday and a half day on Saturday and a holiday on Sunday.
- The calendar PROD\_CAL follows a more complicated work pattern: Sunday is a holiday; on Monday work is done from 8 a.m. through midnight with a two hour break from 6 p.m. to 8 p.m.; on Tuesday through Friday work is done round the clock with two 2-hour breaks from 6 a.m. to 8 a.m. and 6 p.m. to 8 p.m.; on Saturday the work shifts are from midnight to 6 a.m. and again from 8 a.m. to 6 p.m. In other words, work is done continuously from 8 a.m. on Monday morning to 6 p.m. on Saturday with two hour breaks every day at 6 a.m. and 6 p.m.

**Output 4.10.1** Workday and Calendar Data Sets

### Multiple Calendars Workdays Data Set

Obs	fullday	halfday	ovtday	s1	s2	s3
1	8:00	8:00	8:00	.	8:00	.
2	16:00	12:00	18:00	6:00	18:00	6:00
3	.	.	.	8:00	20:00	8:00
4	.	.	.	18:00	.	18:00
5	.	.	.	20:00	.	.
6	.	.	.	.	.	.

### Multiple Calendars CALENDAR Data Set

Obs	cal	_sun_	_mon_	_tue_	_wed_	_thu_	_fri_	_sat_
1	DEFAULT	holiday	fullday	fullday	fullday	fullday	fullday	holiday
2	OVT_CAL	holiday	ovtday	ovtday	ovtday	ovtday	ovtday	halfday
3	PROD_CAL	holiday	s2	s1	s1	s1	s1	s3

The same set of holidays is used as in Example 4.9, except that in this case the holiday for New Year's is defined by specifying both the start and finish time for the holiday instead of defaulting to a one-day long holiday. When multiple calendars are involved, it is often less confusing to define holidays by specifying both a start and a finish time for the holiday instead of the start time and duration. Output 4.10.2 displays the Holiday data set.

### Output 4.10.2 Holiday Data Set

#### Multiple Calendars Holidays Data Set


Obs	holiday	holifin	holidur
1	24DEC03	26DEC03	4
2	01JAN04	01JAN04	.

The data set HOLIDAYS does not include any variable identifying the calendars with which to associate the holidays. By default, the procedure associates the two holiday periods with all the calendars.





An easy way to visualize all the breaks and holidays for each calendar is to use a Gantt chart, plotting a bar for each calendar from the start of the project to January 4, 2004, with all the holiday and work shift specifications. The following program produces Output 4.10.3. Holidays and breaks are marked with a solid fill pattern.

```
goptions hpos=160 vpos=25;
title h=2 'Multiple Calendars';
title2 h=1.4 'Breaks and Holidays for the Different Calendars';
proc gantt data=cals graphics
    calendar=calendar holidata=holidays
    workday=workdata;
chart / interval=dtday mininterval=dthour skip=2
    holiday=(holiday) holifin=(holifin)
    markbreak daylength='08:00't calid=cal
    ref='1dec03:00:00'dt to '4jan04:08:00'dt by dtday
    nolegend nojobnum increment=16
    hpages=6;
id cal;
run;
```


### Output 4.10.3 Gantt Chart Showing Breaks and Holidays for Multiple Calendars

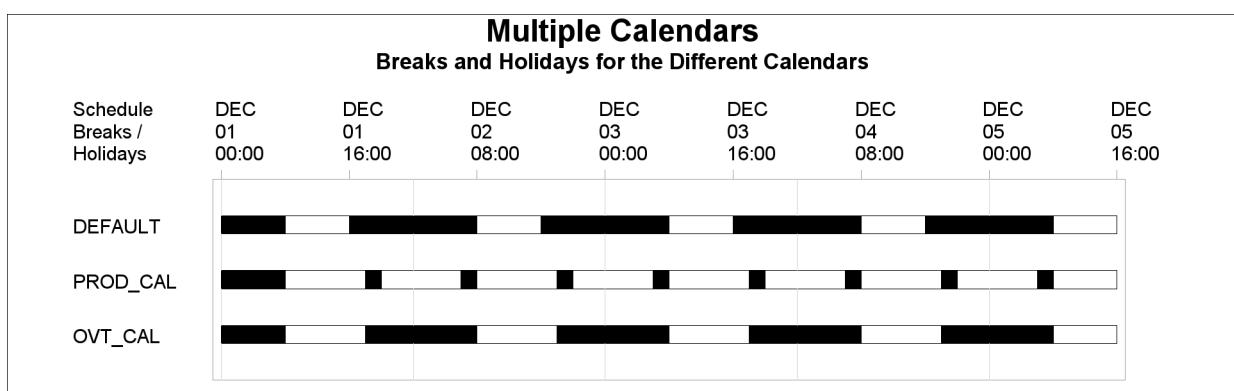

### **Output 4.10.3** *continued*

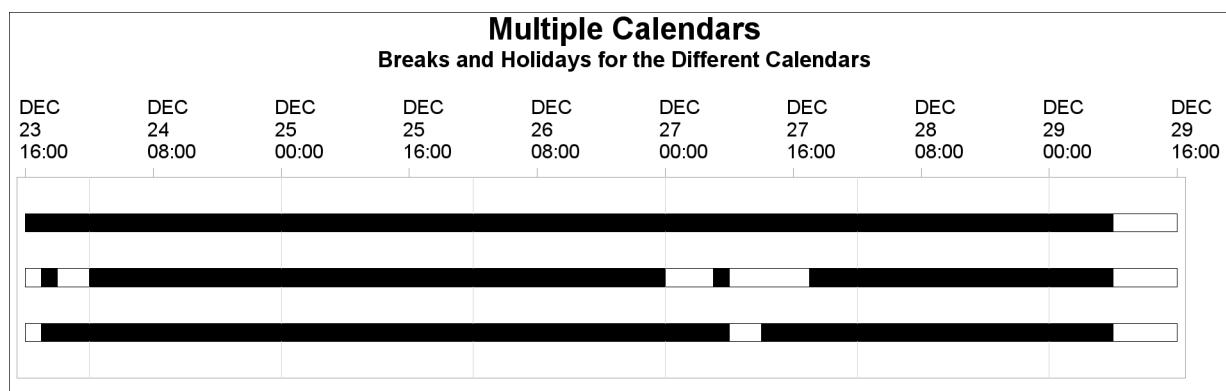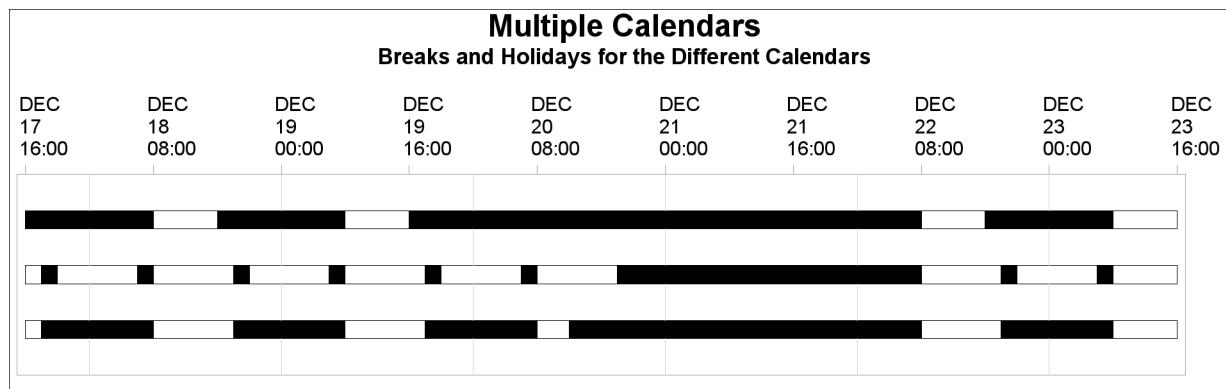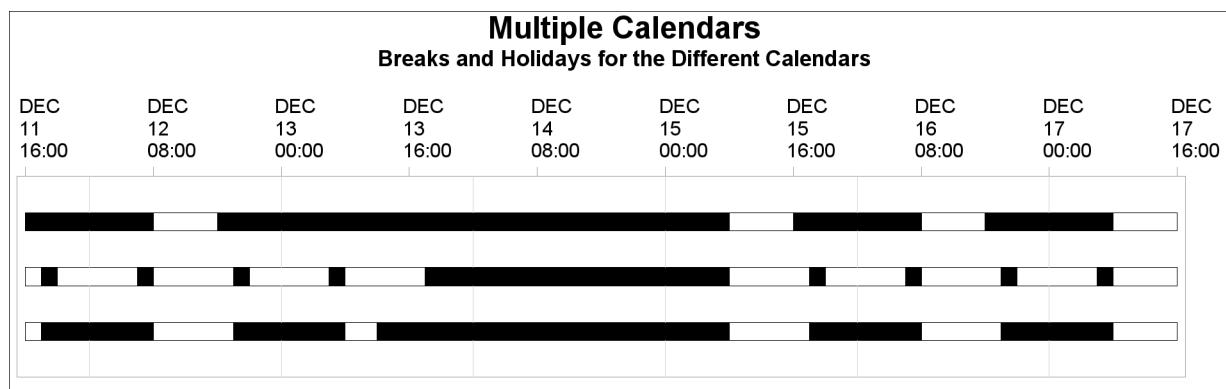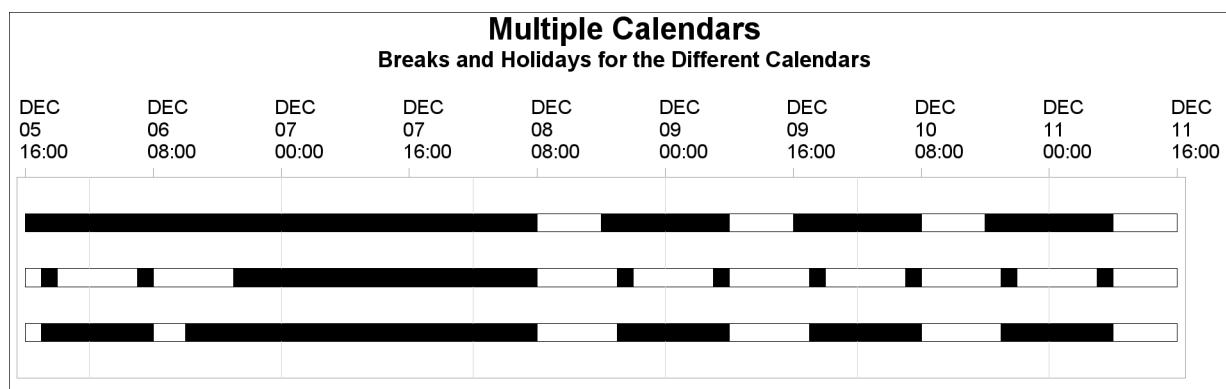

## **Output 4.10.3** *continued*

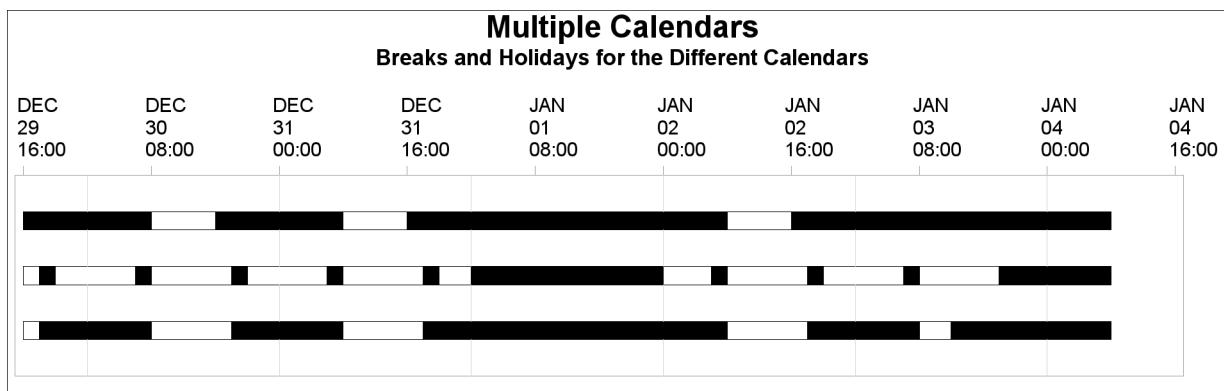

The Activity data set used in [Example 4.9](#) is modified by adding a variable called cal, which sets the calendar to be ‘PROD\_CAL’ for the activity ‘Production’, and ‘OVT\_CAL’ for the activity ‘Prototype’, and the DEFAULT calendar for the other activities. Thus, in both the Activity data set and the Calendar data set, the calendar information is conveyed through a CALID variable, cal.

PROC CPM is first invoked without reference to the CALID variable. Thus, the procedure recognizes only the first observation in the Calendar data set (a warning is printed to the log to this effect), and only the default calendar is used for all activities in the project. The daylength parameter is interpreted as the length of a standard work day; all the durations are assumed to be in units of this standard work day. Output 4.10.4 displays the schedule obtained. The project is scheduled to finish on March 12, 2004, at 12 noon.

```

data widgcal;
  set widget9;
  if task = 'Production' then      cal = 'PROD_CAL';
  else if task = 'Prototype' then   cal = 'OVT_CAL';
  else                           cal = 'DEFAULT';

run;

proc cpm date='01dec03'd data=widgcal out=scheddef
  holidata=holidays daylength='08:00't
  workday=workdata
  calendar=calendar;
  holiday holiday / holifin = holifin;
  activity task;
  duration days;
  successor succ1 succ2 succ3;
run;

title2 'Project Schedule: Default calendar';
proc print heading=h;
  var task days e_start e_finish l_start l_finish
    t_float f_float;
run;

```

**Output 4.10.4** Schedule Using Default Calendar

**Multiple Calendars**  
**Project Schedule: Default calendar**

Obs	task	days	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
1	Approve Plan	5.5	01DEC03:08:00:00	08DEC03:11:59:59	01DEC03:08:00:00	08DEC03:11:59:59	0.0	0.0
2	Drawings	10.0	08DEC03:12:00:00	22DEC03:11:59:59	08DEC03:12:00:00	22DEC03:11:59:59	0.0	0.0
3	Study Market	5.0	08DEC03:12:00:00	15DEC03:11:59:59	23JAN04:12:00:00	30JAN04:11:59:59	30.0	0.0
4	Write Specs	4.5	08DEC03:12:00:00	12DEC03:15:59:59	16DEC03:08:00:00	22DEC03:11:59:59	5.5	5.5
5	Prototype	15.0	22DEC03:12:00:00	16JAN04:11:59:59	22DEC03:12:00:00	16JAN04:11:59:59	0.0	0.0
6	Mkt. Strat.	10.0	15DEC03:12:00:00	02JAN04:11:59:59	30JAN04:12:00:00	13FEB04:11:59:59	30.0	30.0
7	Materials	10.0	16JAN04:12:00:00	30JAN04:11:59:59	16JAN04:12:00:00	30JAN04:11:59:59	0.0	0.0
8	Facility	10.0	16JAN04:12:00:00	30JAN04:11:59:59	16JAN04:12:00:00	30JAN04:11:59:59	0.0	0.0
9	Init. Prod.	10.0	30JAN04:12:00:00	13FEB04:11:59:59	30JAN04:12:00:00	13FEB04:11:59:59	0.0	0.0
10	Evaluate	10.0	13FEB04:12:00:00	27FEB04:11:59:59	20FEB04:12:00:00	05MAR04:11:59:59	5.0	5.0
11	Test Market	15.0	13FEB04:12:00:00	05MAR04:11:59:59	13FEB04:12:00:00	05MAR04:11:59:59	0.0	0.0
12	Changes	5.0	05MAR04:12:00:00	12MAR04:11:59:59	05MAR04:12:00:00	12MAR04:11:59:59	0.0	0.0
13	Production	0.0	12MAR04:12:00:00	12MAR04:12:00:00	12MAR04:12:00:00	12MAR04:12:00:00	0.0	0.0
14	Marketing	0.0	13FEB04:12:00:00	13FEB04:12:00:00	12MAR04:12:00:00	12MAR04:12:00:00	20.0	20.0

Next PROC CPM is invoked with the CALID statement identifying the variable CAL in the Activity and Calendar data sets. Recall that the two activities, ‘Production’ and ‘Prototype’, do not follow the default calendar. The schedule displayed in [Output 4.10.5](#) shows that, due to longer working hours for these two activities in the project, the scheduled finish date is now March 8, at 10:00 a.m.

```

proc cpm date='01dec03'd data=widgcal out=schedmc
    holidata=holidays daylength='08:00't
    workday=workdata
    calendar=calendar;
    holiday holiday / holifin = holifin;
    activity task;
    duration days;
    successor succ1 succ2 succ3;
    calid cal;
    run;
title2 'Project Schedule: Three Calendars';
proc print;
    var task days cal e_: l_: t_float f_float;
    run;

```

**Output 4.10.5** Schedule Using Three Calendars

**Multiple Calendars**  
**Project Schedule: Three Calendars**

Obs	task	days	cal	E_START	E_FINISH	L_START
1	Approve Plan	5.5	DEFAULT	01DEC03:08:00:00	08DEC03:11:59:59	01DEC03:08:00:00
2	Drawings	10.0	DEFAULT	08DEC03:12:00:00	22DEC03:11:59:59	08DEC03:12:00:00
3	Study Market	5.0	DEFAULT	08DEC03:12:00:00	15DEC03:11:59:59	19JAN04:10:00:00
4	Write Specs	4.5	DEFAULT	08DEC03:12:00:00	12DEC03:15:59:59	16DEC03:08:00:00
5	Prototype	15.0	OVT_CAL	22DEC03:12:00:00	12JAN04:09:59:59	22DEC03:12:00:00
6	Mkt. Strat.	10.0	DEFAULT	15DEC03:12:00:00	02JAN04:11:59:59	26JAN04:10:00:00
7	Materials	10.0	DEFAULT	12JAN04:10:00:00	26JAN04:09:59:59	12JAN04:10:00:00
8	Facility	10.0	DEFAULT	12JAN04:10:00:00	26JAN04:09:59:59	12JAN04:10:00:00
9	Init. Prod.	10.0	DEFAULT	26JAN04:10:00:00	09FEB04:09:59:59	26JAN04:10:00:00
10	Evaluate	10.0	DEFAULT	09FEB04:10:00:00	23FEB04:09:59:59	16FEB04:10:00:00
11	Test Market	15.0	DEFAULT	09FEB04:10:00:00	01MAR04:09:59:59	09FEB04:10:00:00
12	Changes	5.0	DEFAULT	01MAR04:10:00:00	08MAR04:09:59:59	01MAR04:10:00:00
13	Production	0.0	PROD_CAL	08MAR04:10:00:00	08MAR04:10:00:00	08MAR04:10:00:00
14	Marketing	0.0	DEFAULT	09FEB04:10:00:00	09FEB04:10:00:00	08MAR04:10:00:00

Obs	L_FINISH	T_FLOAT	F_FLOAT
1	08DEC03:11:59:59	0.00	0.00
2	22DEC03:11:59:59	0.00	0.00
3	26JAN04:09:59:59	25.75	0.00
4	22DEC03:11:59:59	5.50	5.50
5	12JAN04:09:59:59	0.00	0.00
6	09FEB04:09:59:59	25.75	25.75
7	26JAN04:09:59:59	0.00	0.00
8	26JAN04:09:59:59	0.00	0.00
9	09FEB04:09:59:59	0.00	0.00
10	01MAR04:09:59:59	5.00	5.00
11	01MAR04:09:59:59	0.00	0.00
12	08MAR04:09:59:59	0.00	0.00
13	08MAR04:10:00:00	0.00	0.00
14	08MAR04:10:00:00	20.00	20.00

Now suppose that the engineer in charge of writing specifications requests a seven-day vacation from December 8, 2003. How is the project completion time going to be affected? A new calendar, Eng\_cal, is defined that has the same work pattern as the default calendar, but it also contains an extra vacation period. **Output 4.10.6** displays the data sets HOLIDATA and CALEDATA, which contain information about the new calendar. The fourth observation in the data set CALEDATA has missing values for the variables \_sun\_, ..., \_sat\_, indicating that the calendar, Eng\_cal, follows the same work pattern as the default calendar.

**Output 4.10.6 HOLIDATA and CALEDATA Data Sets****Multiple Calendars  
Holidays Data Set**

Obs	holiday	holifin	holidur	cal
1	08DEC03	.	.	7 Eng_cal
2	24DEC03	26DEC03	.	.
3	01JAN04	01JAN04	.	.




**Multiple Calendars  
Calendar Data Set**

Obs	cal	_sun_	_mon_	_tue_	_wed_	_thu_	_fri_	_sat_
1	DEFAULT	holiday	fullday	fullday	fullday	fullday	fullday	holiday
2	OVT_CAL	holiday	ovtday	ovtday	ovtday	ovtday	ovtday	halfday
3	PROD_CAL	holiday	s2	s1	s1	s1	s1	s3
4	Eng_cal	.	.	.	.	.	.	.

Once again, in the following code, PROC GANTT is used to compare the new calendar with the default calendar, as shown in Output 4.10.7. Note that the breaks and holidays are marked with a solid fill pattern.

```
/* Create a data set to illustrate holidays with PROC GANTT */
data cals2;
  e_start='1dec03:00:00'dt;
  e_finish='18dec03:00:00'dt;
  label cal ='Schedule Breaks / Holidays';
  format e_start e_finish datetime16.;
  length cal $8.;
  cal='DEFAULT' ; output;
  cal='Eng_cal' ; output;
run;

title2 'Breaks and Holidays for Eng_cal and the DEFAULT Calendar';
proc gantt data=cals2 graphics
  calendar=caledata holidata=holidata
  workday=workdata;
chart / interval=dtday mininterval=dthour skip=2
  holiday=(holiday) holifin=(holifin) holidur=(holidur)
  markbreak daylength='08:00't calid=cal
  ref='1dec03:00:00'dt to '18dec03:00:00'dt by dtday
  nojobnum nolegend increment=16 hpages=3;
id cal;
run;
```

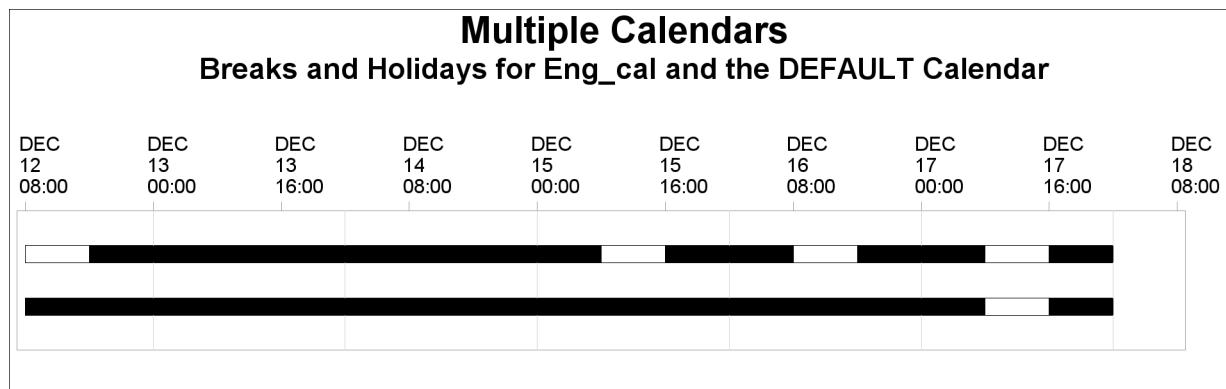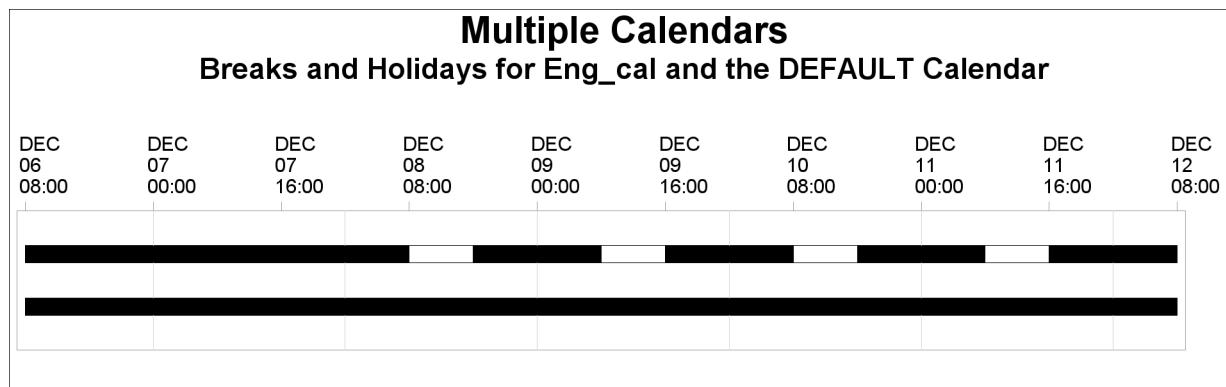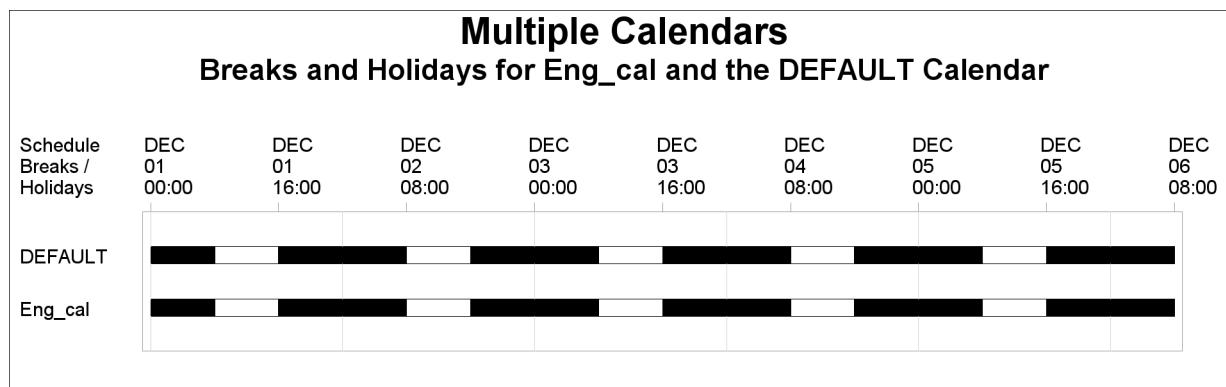**Output 4.10.7** Difference between Eng\_cal and DEFAULT Calendar

The Activity data set is modified to redefine the calendar for the task ‘Write Specs’. PROC CPM is invoked, and **Output 4.10.8** shows the new schedule obtained. Note the effect of the Engineer’s vacation on the project completion time. The project is now scheduled to finish at 10 a.m. on March 9, 2004; in effect, the delay is only one day, even though the planned vacation period is seven days. This is due to the fact that the activity ‘Write Specs’, which follows the new calendar, had some slack time present in its original schedule; however, this activity has now become critical.

```
data widgvac;
  set widgcal;
  if task = 'Write Specs' then cal = 'Eng_cal';
run;
```

```

proc cpm date='01dec03'd data=widgvac out=schedvac
      holidata=holidata daylength='08:00't
      workday=workdata
      calendar=calldata;
      holiday holiday / holifin = holifin holidur=holidur;
      activity task;
      duration days;
      successor succ1 succ2 succ3;
      calid cal;
      run;

title2 'Project Schedule: Four Calendars';
proc print;
  var task days cal e_: l_: t_float f_float;
run;

```

#### Output 4.10.8 Schedule Using Four Calendars

**Multiple Calendars**  
**Project Schedule: Four Calendars**

Obs	task	days	cal	E_START	E_FINISH	L_START
1	Approve Plan	5.5	DEFAULT	01DEC03:08:00:00	08DEC03:11:59:59	02DEC03:08:00:00
2	Drawings	10.0	DEFAULT	08DEC03:12:00:00	22DEC03:11:59:59	09DEC03:12:00:00
3	Study Market	5.0	DEFAULT	08DEC03:12:00:00	15DEC03:11:59:59	20JAN04:10:00:00
4	Write Specs	4.5	Eng_cal	17DEC03:08:00:00	23DEC03:11:59:59	17DEC03:08:00:00
5	Prototype	15.0	OVT_CAL	23DEC03:12:00:00	13JAN04:09:59:59	23DEC03:12:00:00
6	Mkt. Strat.	10.0	DEFAULT	15DEC03:12:00:00	02JAN04:11:59:59	27JAN04:10:00:00
7	Materials	10.0	DEFAULT	13JAN04:10:00:00	27JAN04:09:59:59	13JAN04:10:00:00
8	Facility	10.0	DEFAULT	13JAN04:10:00:00	27JAN04:09:59:59	13JAN04:10:00:00
9	Init. Prod.	10.0	DEFAULT	27JAN04:10:00:00	10FEB04:09:59:59	27JAN04:10:00:00
10	Evaluate	10.0	DEFAULT	10FEB04:10:00:00	24FEB04:09:59:59	17FEB04:10:00:00
11	Test Market	15.0	DEFAULT	10FEB04:10:00:00	02MAR04:09:59:59	10FEB04:10:00:00
12	Changes	5.0	DEFAULT	02MAR04:10:00:00	09MAR04:09:59:59	02MAR04:10:00:00
13	Production	0.0	PROD_CAL	09MAR04:10:00:00	09MAR04:10:00:00	09MAR04:10:00:00
14	Marketing	0.0	DEFAULT	10FEB04:10:00:00	10FEB04:10:00:00	09MAR04:10:00:00

Obs	L_FINISH	T_FLOAT	F_FLOAT
1	09DEC03:11:59:59	1.00	0.00
2	23DEC03:11:59:59	1.00	1.00
3	27JAN04:09:59:59	26.75	0.00
4	23DEC03:11:59:59	0.00	0.00
5	13JAN04:09:59:59	0.00	0.00
6	10FEB04:09:59:59	26.75	26.75
7	27JAN04:09:59:59	0.00	0.00
8	27JAN04:09:59:59	0.00	0.00
9	10FEB04:09:59:59	0.00	0.00
10	02MAR04:09:59:59	5.00	5.00
11	02MAR04:09:59:59	0.00	0.00
12	09MAR04:09:59:59	0.00	0.00
13	09MAR04:10:00:00	0.00	0.00
14	09MAR04:10:00:00	20.00	20.00

---

## Example 4.11: Nonstandard Relationships

This example shows the use of LAG variables to describe nonstandard relationships. Consider the project network in AON format. [Output 4.11.1](#) shows the data set WIDGLAG, which contains the required project information; here the data set contains only one successor variable, requiring multiple observations for activities that have more than one immediate successor. In addition, the data set contains two new variables, lagdur and lagdurl, which are used to convey nonstandard relationships that exist between some of the activities. In the first part of the example, lagdur specifies a lag type and lag duration between activities; in the second part, the variable lagdurl specifies a lag calendar in addition to the lag type and lag duration. When multiple successor variables are used, you can specify multiple lag variables and the lag values specified are matched one-for-one with the corresponding successor variables.

### **Output 4.11.1** Network Data

#### **Non-Standard Relationships Activity Data Set WIDGLAG**

<b>Obs</b>	<b>task</b>	<b>days</b>	<b>succ</b>	<b>lagdur</b>	<b>lagdurl</b>
1	Approve Plan	5	Drawings		
2	Approve Plan	5	Study Market		
3	Approve Plan	5	Write Specs		
4	Drawings	10	Prototype		
5	Study Market	5	Mkt. Strat.		
6	Write Specs	5	Prototype		
7	Prototype	15	Materials	ss_9	ss_9
8	Prototype	15	Facility	ss_9	ss_9
9	Mkt. Strat.	10	Test Market		
10	Mkt. Strat.	10	Marketing		
11	Materials	10	Init. Prod.		
12	Facility	10	Init. Prod.	fs_2	fs_2_SEVENDAY
13	Init. Prod.	10	Test Market		
14	Init. Prod.	10	Marketing		
15	Init. Prod.	10	Evaluate		
16	Evaluate	10	Changes		
17	Test Market	15	Changes		
18	Changes	5	Production		
19	Production	0			
20	Marketing	0			

Suppose that the project calendar follows a five-day work week. Recall from [Example 4.6](#) that the project finishes on March 8, 2004. The data set, WIDGLAG, specifies that there is a ‘ss\_9’ lag between the activities ‘Prototype’ and ‘Materials’, which means that you can start acquiring raw materials nine days after the start of the activity ‘Prototype’ instead of waiting until its finish time. Likewise, there is an ‘ss\_9’ lag between ‘Prototype’ and ‘Facility’. The ‘fs\_2’ lag between ‘Facility’ and ‘Init. Prod’ indicates that you should wait two days after the completion of the ‘Facility’ task before starting the initial production. To convey the lag information to PROC CPM, use the LAG= specification in the SUCCESSOR statement. The program and the resulting output ([Output 4.11.2](#)) follow.

```
proc cpm data=widglag date='1dec03'd  
        interval=weekday collapse out=lagsched;  
activity task;  
succ      succ / lag = (lagdur);  
duration days;  
run;
```

## **Output 4.11.2** Project Schedule: Default LAG Calendar

## Non-Standard Relationships

### Lag Type and Duration: Default LAG Calendar

task	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
Approve Plan	01DEC03	05DEC03	01DEC03	05DEC03	0	0
Drawings	08DEC03	19DEC03	08DEC03	19DEC03	0	0
Study Market	08DEC03	12DEC03	13JAN04	19JAN04	26	0
Write Specs	08DEC03	12DEC03	15DEC03	19DEC03	5	5
Prototype	22DEC03	09JAN04	22DEC03	09JAN04	0	0
Mkt. Strat.	15DEC03	26DEC03	20JAN04	02FEB04	26	26
Materials	02JAN04	15JAN04	06JAN04	19JAN04	2	2
Facility	02JAN04	15JAN04	02JAN04	15JAN04	0	0
Init. Prod.	20JAN04	02FEB04	20JAN04	02FEB04	0	0
Evaluate	03FEB04	16FEB04	10FEB04	23FEB04	5	5
Test Market	03FEB04	23FEB04	03FEB04	23FEB04	0	0
Changes	24FEB04	01MAR04	24FEB04	01MAR04	0	0
Production	02MAR04	02MAR04	02MAR04	02MAR04	0	0
Marketing	03FEB04	03FEB04	02MAR04	02MAR04	20	20

Due to the change in the type of precedence constraint (from the default ‘fs\_0’ to ‘ss\_9’), the project finishes earlier, on March 2, 2004, instead of on March 8, 2004 (compare with [Output 4.6.1](#)).

By default, all the lags are assumed to follow the default calendar for the project. In this case, the default project calendar has five workdays (since INTERVAL=WEEKDAY). Suppose now that the ‘fs\_2’ lag between ‘Facility’ and ‘Init. Prod.’ really indicates two calendar days and not two workdays. (Perhaps you want to allow two days for the paint to dry or the building to be ventilated.) The variable lagdrc in the WIDLAG data set indicates the calendar for this lag by specifying the lag to be ‘fs\_2\_sevenday’ where ‘sevenday’ is the name of the seven-day calendar defined in the Calendar data set, CALENDAR, displayed in [Output 4.11.3](#). PROC CPM is invoked with LAG=lagdrc and [Output 4.11.4](#) displays the resulting schedule. Note that the project now finishes on March 1, 2004.

### **Output 4.11.3 Calendar Data Set**

## **Non-Standard Relationships Calendar Data Set**

**Obs** \_cal\_      \_sun\_    \_mon\_    \_tue\_    \_wed\_    \_thu\_    \_fri\_    \_sat\_  
 1 SEVENDAY workday workday workday workday workday workday workday workday

```
proc cpm data=widglag date='1dec03'd calendar=calendar
    interval=weekday collapse out=lagsched;
activity task;
succ    succ / lag = (lagdurc);
duration days;
run;
```

**Output 4.11.4** Project Schedule: Lag Type, Duration, and Calendar

**Non-Standard Relationships**  
**Lag Type, Duration, and Calendar**

task	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
Approve Plan	01DEC03	05DEC03	02DEC03	08DEC03	1	0
Drawings	08DEC03	19DEC03	09DEC03	22DEC03	1	0
Study Market	08DEC03	12DEC03	12JAN04	16JAN04	25	0
Write Specs	08DEC03	12DEC03	16DEC03	22DEC03	6	5
Prototype	22DEC03	09JAN04	23DEC03	12JAN04	1	0
Mkt. Strat.	15DEC03	26DEC03	19JAN04	30JAN04	25	25
Materials	02JAN04	15JAN04	05JAN04	16JAN04	1	1
Facility	02JAN04	15JAN04	05JAN04	16JAN04	1	1
Init. Prod.	19JAN04	30JAN04	19JAN04	30JAN04	0	0
Evaluate	02FEB04	13FEB04	09FEB04	20FEB04	5	5
Test Market	02FEB04	20FEB04	02FEB04	20FEB04	0	0
Changes	23FEB04	27FEB04	23FEB04	27FEB04	0	0
Production	01MAR04	01MAR04	01MAR04	01MAR04	0	0
Marketing	02FEB04	02FEB04	01MAR04	01MAR04	20	20

In fact, you can specify an alternate calendar for *all* the lag durations by using the ALAGCAL= or NLAGCAL= option in the SUCCESSOR statement. The next invocation of the CPM procedure illustrates this feature by specifying ALAGCAL=SEVENDAY in the SUCCESSOR statement. Thus, all the lag durations now follow the seven-day calendar instead of the five-day calendar, which is the default calendar for this project. [Output 4.11.5](#) shows the resulting schedule. Now the project finishes on February 27, 2004. [Output 4.11.6](#) displays a precedence Gantt chart of the project. Note how the nonstandard precedence constraints are displayed.

```
proc cpm data=widglag date='1dec03'd calendar=calendar
    interval=weekday collapse out=lagsched;
activity task;
succ    succ / lag = (lagdur) alagcal=sevenday;
duration days;
run;

pattern1 c=green v=s;      /* duration of a non-critical activity */
pattern2 c=green v=e;      /* slack time for a noncrit. activity */
pattern3 c=red   v=s;      /* duration of a critical activity */

title  h=1.5  'Non-Standard Relationships';
title2 h=1 'Precedence Gantt Chart';
```

```

proc gantt graphics data=lagsched logic=widglag;
  chart / compress act=task succ=(succ) dur=days
         cprec=black cmile=blue
         caxis=black
         height=1.5 nojobnum
         dur=days increment=7 lag=(lagdur);
  id task;
run;

```

**Output 4.11.5** Project Schedule: LAG Calendar = SEVENDAY


**Non-Standard Relationships**  
**Lag Type and Duration: LAG Calendar = SEVENDAY**

task	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
Approve Plan	01DEC03	05DEC03	01DEC03	05DEC03	0	0
Drawings	08DEC03	19DEC03	08DEC03	19DEC03	0	0
Study Market	08DEC03	12DEC03	09JAN04	15JAN04	24	0
Write Specs	08DEC03	12DEC03	15DEC03	19DEC03	5	5
Prototype	22DEC03	09JAN04	22DEC03	09JAN04	0	0
Mkt. Strat.	15DEC03	26DEC03	16JAN04	29JAN04	24	24
Materials	31DEC03	13JAN04	02JAN04	15JAN04	2	2
Facility	31DEC03	13JAN04	31DEC03	13JAN04	0	0
Init. Prod.	16JAN04	29JAN04	16JAN04	29JAN04	0	0
Evaluate	30JAN04	12FEB04	06FEB04	19FEB04	5	5
Test Market	30JAN04	19FEB04	30JAN04	19FEB04	0	0
Changes	20FEB04	26FEB04	20FEB04	26FEB04	0	0
Production	27FEB04	27FEB04	27FEB04	27FEB04	0	0
Marketing	30JAN04	30JAN04	27FEB04	27FEB04	20	20

Output 4.11.6 Precedence Gantt Chart

## Non-Standard Relationships

Precedence Gantt Chart

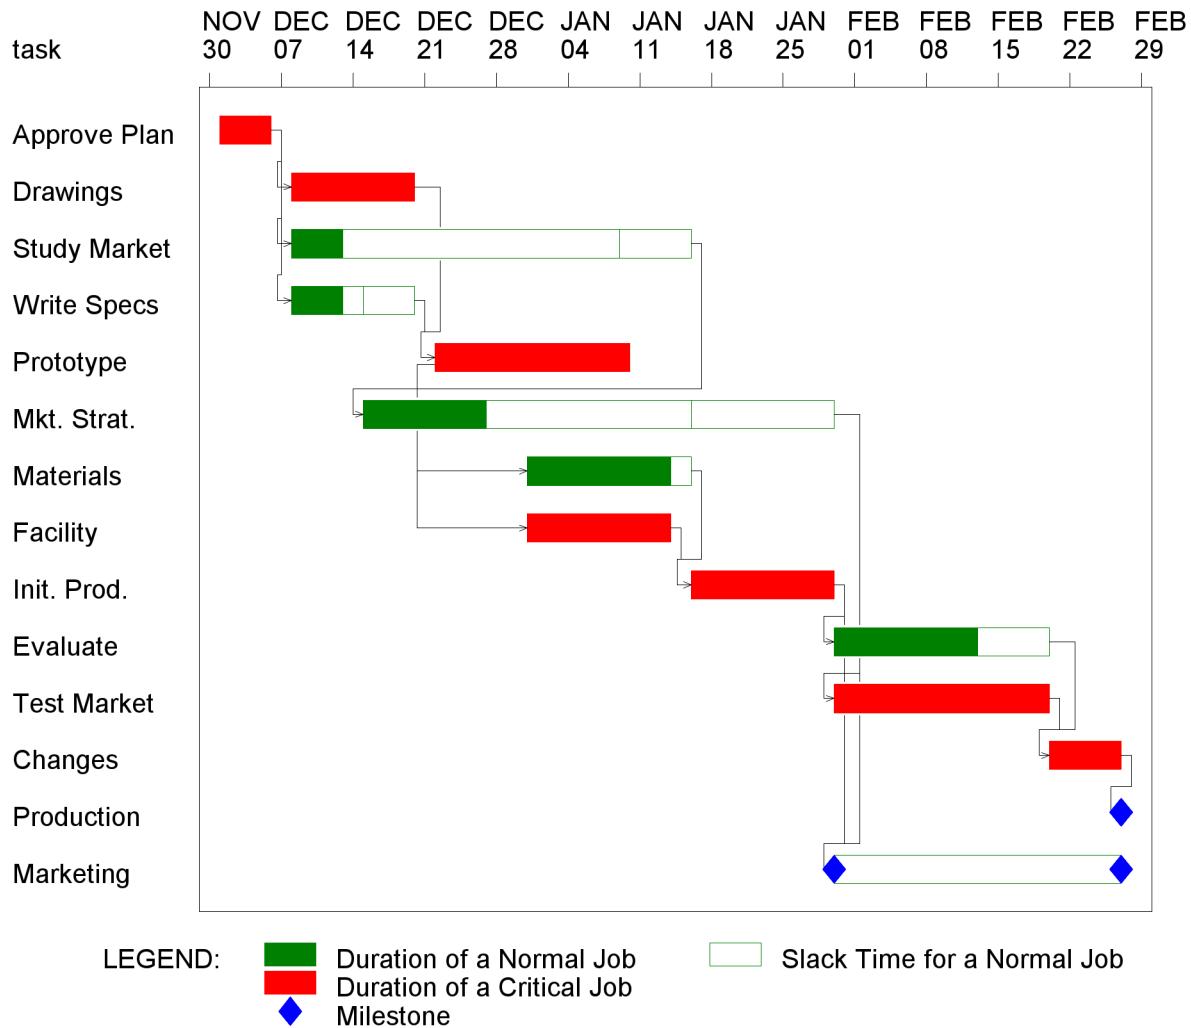

---

## Example 4.12: Activity Time Constraints

Often, in addition to a project start date or a project finish date, there may be other time constraints imposed selectively on the activities in the project. The **ALIGNDATE** and **ALIGNTYPE** statements enable you to add various types of time constraints on the activities. In this example, the data set WIDGET12 displayed in [Output 4.12.1](#) contains two variables, **adate** and **atype**, which enable you to specify these restrictions. For example, the activity ‘Drawings’ has an ‘feq’ (Finish Equals) constraint, requiring it to finish on the 15th of December. The activity ‘Test Market’ has a *mandatory* start date imposed on it.

### Output 4.12.1 Activity Data Set WIDGET12

#### Activity Time Constraints Activity data set

Obs	task	days	succ1	succ2	succ3	adate	atype
1	Approve Plan	5	Drawings	Study Market	Write Specs	.	.
2	Drawings	10	Prototype			15DEC03	feq
3	Study Market	5	Mkt. Strat.			.	.
4	Write Specs	5	Prototype			15DEC03	sge
5	Prototype	15	Materials	Facility		.	.
6	Mkt. Strat.	10	Test Market	Marketing		.	.
7	Materials	10	Init. Prod.			.	.
8	Facility	10	Init. Prod.			.	.
9	Init. Prod.	10	Test Market	Marketing	Evaluate	.	.
10	Evaluate	10	Changes			27FEB04	fle
11	Test Market	15	Changes			16FEB04	ms
12	Changes	5	Production			.	.
13	Production	0				.	.
14	Marketing	0				.	.

The following statements are needed to schedule the project subject to these restrictions. The option **XFERVARS** in the **PROC CPM** statement causes CPM to transfer all variables that were used in the analysis to the Schedule data set. [Output 4.12.2](#) shows the resulting schedule.

```
proc cpm data=widget12 date='1dec03'd
  xfervars interval=weekday;
activity task;
successor succ1 succ2 succ3;
duration days;
aligndate adate;
aligntype atype;
run;
```

```

title 'Activity Time Constraints';
title2 'Aligned Schedule';
proc print;
  id task;
  var adate atype e_: l_: t_float f_float;
run;

```

#### Output 4.12.2 Aligned Schedule

#### Activity Time Constraints Aligned Schedule

task	adate	atype	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
Approve Plan	.		01DEC03	05DEC03	25NOV03	01DEC03	-4	-4
Drawings	15DEC03	feq	08DEC03	19DEC03	02DEC03	15DEC03	-4	-4
Study Market	.		08DEC03	12DEC03	26JAN04	30JAN04	35	0
Write Specs	15DEC03	sge	15DEC03	19DEC03	22DEC03	26DEC03	5	0
Prototype	.		22DEC03	09JAN04	29DEC03	16JAN04	5	0
Mkt. Strat.	.		15DEC03	26DEC03	02FEB04	13FEB04	35	30
Materials	.		12JAN04	23JAN04	19JAN04	30JAN04	5	0
Facility	.		12JAN04	23JAN04	19JAN04	30JAN04	5	0
Init. Prod.	.		26JAN04	06FEB04	02FEB04	13FEB04	5	0
Evaluate	27FEB04	fle	09FEB04	20FEB04	16FEB04	27FEB04	5	5
Test Market	16FEB04	ms	16FEB04	05MAR04	16FEB04	05MAR04	0	0
Changes	.		08MAR04	12MAR04	08MAR04	12MAR04	0	0
Production	.		15MAR04	15MAR04	15MAR04	15MAR04	0	0
Marketing	.		09FEB04	09FEB04	15MAR04	15MAR04	25	25

Note that the MS and MF constraints are *mandatory* and override any precedence constraints; thus, both the late start and early start times for the activity ‘Test Market’ coincide with February 16, 2004. However, the other types of constraints are not mandatory; they are superseded by any constraints imposed by the precedence relationships. In other words, neither the early start nor the late start schedule violate precedence constraints. Thus, even though the activity ‘Drawings’ is required to finish on the 15th of December (by the ‘feq’ constraint), the early start schedule causes it to finish on the 19th of December because of its predecessor’s schedule. This type of inconsistency is indicated by the presence of negative floats for some of the activities alerting you to the fact that if some of these deadlines are to be met, these activities must start earlier than the early start schedule. Such activities are called *supercritical*.

---

## Example 4.13: Progress Update and Target Schedules

This example shows the use of the ACTUAL and BASELINE statements to track and compare a project's progress with the original planned schedule. Consider the data in [Example 4.1](#), for the network in AON format. Suppose that the project has started as scheduled on December 1, 2003, and that the current date is December 19, 2003. You may want to enter the actual dates for the activities that are already in progress or have been completed and use the CPM procedure to determine the schedule for activities that remain to be done. In addition to computing an updated schedule, you may want to check the progress of the project by comparing the current schedule with the planned schedule.

The BASELINE statement enables you to save a target schedule in the Schedule data set. In this example, suppose that you want to try to schedule the activities according to the project's early start schedule. As a first step, schedule the project with PROC CPM, and use the SET= option in the BASELINE statement to save the early start and finish times as the baseline start and finish times. The following program saves the baseline schedule (in the variables B\_START and B\_FINISH), and [Output 4.13.1](#) displays the resulting output data set.

```

data holidays;
  format holiday holifin date7.;
  input holiday & date7. holifin & date7. holidur;
  datalines;
24dec03 26dec03 4
01jan04 .
;

* store early schedule as the baseline schedule;

proc cpm data=widget holidata=holidays
  out=widgbase date='1dec03'd;
  activity task;
  succ    succ1 succ2 succ3;
  duration days;
  holiday holiday / holifin=(holifin);
  baseline / set=early;
run;

```

**Output 4.13.1** Target Schedule**Progress Update and Target Schedules**  
**Set Baseline Schedule**

Obs	task	succ1	succ2	succ3	days	E_START	E_FINISH
1	Approve Plan Drawings		Study Market	Write Specs	5	01DEC03	05DEC03
2	Drawings	Prototype			10	06DEC03	15DEC03
3	Study Market	Mkt. Strat.			5	06DEC03	10DEC03
4	Write Specs	Prototype			5	06DEC03	10DEC03
5	Prototype	Materials	Facility		15	16DEC03	03JAN04
6	Mkt. Strat.	Test Market	Marketing		10	11DEC03	20DEC03
7	Materials	Init. Prod.			10	04JAN04	13JAN04
8	Facility	Init. Prod.			10	04JAN04	13JAN04
9	Init. Prod.	Test Market	Marketing	Evaluate	10	14JAN04	23JAN04
10	Evaluate	Changes			10	24JAN04	02FEB04
11	Test Market	Changes			15	24JAN04	07FEB04
12	Changes	Production			5	08FEB04	12FEB04
13	Production				0	13FEB04	13FEB04
14	Marketing				0	24JAN04	24JAN04

Obs	L_START	L_FINISH	T_FLOAT	F_FLOAT	B_START	B_FINISH
1	01DEC03	05DEC03	0	0	01DEC03	05DEC03
2	06DEC03	15DEC03	0	0	06DEC03	15DEC03
3	09JAN04	13JAN04	30	0	06DEC03	10DEC03
4	11DEC03	15DEC03	5	5	06DEC03	10DEC03
5	16DEC03	03JAN04	0	0	16DEC03	03JAN04
6	14JAN04	23JAN04	30	30	11DEC03	20DEC03
7	04JAN04	13JAN04	0	0	04JAN04	13JAN04
8	04JAN04	13JAN04	0	0	04JAN04	13JAN04
9	14JAN04	23JAN04	0	0	14JAN04	23JAN04
10	29JAN04	07FEB04	5	5	24JAN04	02FEB04
11	24JAN04	07FEB04	0	0	24JAN04	07FEB04
12	08FEB04	12FEB04	0	0	08FEB04	12FEB04
13	13FEB04	13FEB04	0	0	13FEB04	13FEB04
14	13FEB04	13FEB04	20	20	24JAN04	24JAN04

As the project progresses, you have to account for the actual progress of the project and schedule the unfinished activities accordingly. You can do so by specifying actual start or actual finish times (or both) for activities that have already finished or are in progress. Progress information can also be specified using percent complete or remaining duration values. Assume that current information has been incorporated into the ACTUAL data set, shown in [Output 4.13.2](#). The variables sdate and fdate contain the actual start and finish times of the activities, and rdur specifies the number of days of work that are still remaining for the activity to be completed, and pctc specifies the percent of work that has been completed for that activity.

**Output 4.13.2 Progress Data Set ACTUAL**  
**Progress Update and Target Schedules**  
**Progress Data**

Obs	task	sdate	fdate	pctc	rdur
1	Approve Plan	01DEC2003	05DEC2003	.	.
2	Drawings	06DEC2003	16DEC2003	.	.
3	Study Market	05DEC2003	.	100	.
4	Write Specs	07DEC2003	12DEC2003	.	.
5	Prototype	.	.	.	.
6	Mkt. Strat.	10DEC2003	.	.	3
7	Materials	.	.	.	.
8	Facility	.	.	.	.
9	Init. Prod.	.	.	.	.
10	Evaluate	.	.	.	.
11	Test Market	.	.	.	.
12	Changes	.	.	.	.
13	Production	.	.	.	.
14	Marketing	.	.	.	.

The following statements invoke PROC CPM after merging the progress data with the Schedule data set. The NOAUTOUPTD option is specified so that only those activities that have explicit progress information are assumed to have started. The resulting Schedule data set contains the new variables A\_START, A\_FINISH, A\_DUR, and STATUS; this data set is displayed in [Output 4.13.3](#). The activity ‘Mkt. Strat.’, which has rdur=‘3’ in [Output 4.13.2](#), has an early finish time (December 21, 2003) that is three days after TIMENOW. The S\_VAR and F\_VAR variables show the amount of slippage in the start and finish times (predicted on the basis of the current schedule) as compared to the baseline schedule.

```
* merge the baseline information with progress update;
data widgact;
  merge actual widgbase;
  run;

proc cpm data=widgact holidata=holidays
  out=widgnupd date='1dec03'd;
  activity task;
  succ    succ1 succ2 succ3;
  duration days;
  holiday holiday / holifin=(holifin);
  baseline / compare=early;
  actual / a_start=sdate a_finish=fdate timenow='19dec03'd
           remdur=rdur pctcomp=pctc noautoupdt;
  run;
```

**Output 4.13.3** Comparison of Schedules: NOAUTOUPTD

**Progress Update and Target Schedules**  
**Updated Schedule vs. Target Schedule: NOAUTOUPTD**

Obs	task	succ1	succ2	succ3	days	STATUS	A_DUR	A_START	A_FINISH	E_START
1	Approve Plan	Drawings	Study Market	Write Specs	5	Completed	5	01DEC03	05DEC03	01DEC03
2	Drawings	Prototype			10	Completed	11	06DEC03	16DEC03	06DEC03
3	Study Market	Mkt. Strat.			5	Completed	5	05DEC03	09DEC03	05DEC03
4	Write Specs	Prototype			5	Completed	6	07DEC03	12DEC03	07DEC03
5	Prototype	Materials	Facility		15	Pending	.	.	.	19DEC03
6	Mkt. Strat.	Test Market	Marketing		10	In Progress	.	10DEC03	.	10DEC03
7	Materials	Init. Prod.			10	Pending	.	.	.	07JAN04
8	Facility	Init. Prod.			10	Pending	.	.	.	07JAN04
9	Init. Prod.	Test Market	Marketing	Evaluate	10	Pending	.	.	.	17JAN04
10	Evaluate	Changes			10	Pending	.	.	.	27JAN04
11	Test Market	Changes			15	Pending	.	.	.	27JAN04
12	Changes	Production			5	Pending	.	.	.	11FEB04
13	Production				0	Pending	.	.	.	16FEB04
14	Marketing				0	Pending	.	.	.	27JAN04

Obs	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT	B_START	B_FINISH	S_VAR	F_VAR
1	05DEC03	01DEC03	05DEC03	0	0	01DEC03	05DEC03	0	0
2	16DEC03	06DEC03	16DEC03	0	0	06DEC03	15DEC03	0	1
3	09DEC03	05DEC03	09DEC03	0	0	06DEC03	10DEC03	-1	-1
4	12DEC03	07DEC03	12DEC03	0	0	06DEC03	10DEC03	1	2
5	06JAN04	19DEC03	06JAN04	0	0	16DEC03	03JAN04	3	3
6	21DEC03	10DEC03	21DEC03	0	0	11DEC03	20DEC03	-1	1
7	16JAN04	07JAN04	16JAN04	0	0	04JAN04	13JAN04	3	3
8	16JAN04	07JAN04	16JAN04	0	0	04JAN04	13JAN04	3	3
9	26JAN04	17JAN04	26JAN04	0	0	14JAN04	23JAN04	3	3
10	05FEB04	01FEB04	10FEB04	5	5	24JAN04	02FEB04	3	3
11	10FEB04	27JAN04	10FEB04	0	0	24JAN04	07FEB04	3	3
12	15FEB04	11FEB04	15FEB04	0	0	08FEB04	12FEB04	3	3
13	16FEB04	16FEB04	16FEB04	0	0	13FEB04	13FEB04	3	3
14	27JAN04	16FEB04	16FEB04	20	20	24JAN04	24JAN04	3	3

In order for you to see the effect of the AUTOUPDT option, the same project information is used with the AUTOUPDT option in the ACTUAL statement. [Output 4.13.4](#) displays the resulting schedule. With the AUTOUPDT option (which is, in fact, the default option), PROC CPM uses the progress information and the precedence information to automatically fill in the actual start and finish information for activities that should have finished or started before TIMENOW. The activity ‘Prototype’ has no progress information in WIDGACT, but it is assumed to have an actual start date of December 17, 2003. This option is useful when there are several activities that take place according to the plan and only a few occur out of sequence; then it is sufficient to enter progress information only for the activities that did not follow the plan. The SHOWFLOAT option, also used in this invocation of PROC CPM, enables activities that are completed or in progress to have float; in other words, the late start schedule for activities in progress is not fixed by the progress information. Thus, the activity ‘Study Market’ has L\_START=‘08JAN04’ instead of ‘05DEC03’, as in the earlier invocation of PROC CPM (without the SHOWFLOAT option). The following invocation of PROC CPM produces [Output 4.13.4](#):

```

proc cpm data=widgact holidata=holidays
          out=widgupd date='1dec03'd;
activity task;
succ    succ1 succ2 succ3;
duration days;
holiday holiday / holifin=(holifin);
baseline / compare=early;
actual / as=sdate af=fdate timenow='19dec03'd
        remdur=rdur pctcomp=pctc
        autoupdt showfloat;
run;

```

#### Output 4.13.4 Comparison of Schedules: AUTOUPDT

### Progress Update and Target Schedules Updated Schedule vs. Target Schedule: AUTOUPDT

Obs	task	succ1	succ2	succ3	days	STATUS	A_DUR	A_START	A_FINISH	E_START
1	Approve Plan	Drawings	Study Market	Write Specs	5	Completed	5	01DEC03	05DEC03	01DEC03
2	Drawings	Prototype			10	Completed	11	06DEC03	16DEC03	06DEC03
3	Study Market	Mkt. Strat.			5	Completed	5	05DEC03	09DEC03	05DEC03
4	Write Specs	Prototype			5	Completed	6	07DEC03	12DEC03	07DEC03
5	Prototype	Materials	Facility		15	In Progress	.	17DEC03		17DEC03
6	Mkt. Strat.	Test Market	Marketing		10	In Progress	.	10DEC03		10DEC03
7	Materials	Init. Prod.			10	Pending	.	.		05JAN04
8	Facility	Init. Prod.			10	Pending	.	.		05JAN04
9	Init. Prod.	Test Market	Marketing	Evaluate	10	Pending	.	.		15JAN04
10	Evaluate	Changes			10	Pending	.	.		25JAN04
11	Test Market	Changes			15	Pending	.	.		25JAN04
12	Changes	Production			5	Pending	.	.		09FEB04
13	Production				0	Pending	.	.		14FEB04
14	Marketing				0	Pending	.	.		25JAN04

Obs	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT	B_START	B_FINISH	S_VAR	F_VAR
1	05DEC03	01DEC03	05DEC03	0	-1	01DEC03	05DEC03	0	0
2	16DEC03	06DEC03	16DEC03	0	0	06DEC03	15DEC03	0	1
3	09DEC03	08JAN04	12JAN04	30	0	06DEC03	10DEC03	-1	-1
4	12DEC03	11DEC03	16DEC03	4	4	06DEC03	10DEC03	1	2
5	04JAN04	17DEC03	04JAN04	0	0	16DEC03	03JAN04	1	1
6	21DEC03	13JAN04	24JAN04	30	30	11DEC03	20DEC03	-1	1
7	14JAN04	05JAN04	14JAN04	0	0	04JAN04	13JAN04	1	1
8	14JAN04	05JAN04	14JAN04	0	0	04JAN04	13JAN04	1	1
9	24JAN04	15JAN04	24JAN04	0	0	14JAN04	23JAN04	1	1
10	03FEB04	30JAN04	08FEB04	5	5	24JAN04	02FEB04	1	1
11	08FEB04	25JAN04	08FEB04	0	0	24JAN04	07FEB04	1	1
12	13FEB04	09FEB04	13FEB04	0	0	08FEB04	12FEB04	1	1
13	14FEB04	14FEB04	14FEB04	0	0	13FEB04	13FEB04	1	1
14	25JAN04	14FEB04	14FEB04	20	20	24JAN04	24JAN04	1	1

---

## Example 4.14: Summarizing Resource Utilization

This example shows how you can use the RESOURCE statement in conjunction with the RESOURCEOUT= option to summarize resource utilization. The example assumes that Engineer is a resource category and the project network (in AOA format) along with resource requirements for each activity is in a SAS data set, as displayed in [Output 4.14.1](#).

**Output 4.14.1** Resource Utilization: WIDGRES

**Summarizing Resource Utilization  
Activity Data Set**

Obs	task	days	tail	head	engineer
1	Approve Plan	5	1	2	2
2	Drawings	10	2	3	1
3	Study Market	5	2	4	1
4	Write Specs	5	2	3	2
5	Prototype	15	3	5	4
6	Mkt. Strat.	10	4	6	.
7	Materials	10	5	7	.
8	Facility	10	5	7	2
9	Init. Prod.	10	7	8	4
10	Evaluate	10	8	9	1
11	Test Market	15	6	9	.
12	Changes	5	9	10	2
13	Production	0	10	11	4
14	Marketing	0	6	12	.
15	Dummy	0	8	6	.

**Output 4.14.2** Resource Utilization: HOLDATA

**Summarizing Resource Utilization  
Holidays Data Set HOLDATA**

Obs	hol_name
1	25DEC03 Christmas
2	01JAN04 New Year

In the following program, PROC CPM is invoked with the RESOURCE statement identifying the resource for which usage information is required. The project is scheduled only on weekdays, and holiday information is included through the Holiday data set, HOLDATA, which identifies two holidays, one for Christmas and one for New Year's Day. [Output 4.14.2](#) shows the Holiday data set.

The program saves the resource usage information in a data set named ROUT, which is displayed in [Output 4.14.3](#). Two variables, Eengineer and Lengineer, denote the usage of the resource engineer corresponding to the early and late start schedules, respectively. Note the naming convention for the variables in the resource usage data set: A prefix (E for Early and L for Late) is followed by the name of the resource variable, engineer. Note also that the data set contains only observations corresponding to weekdays; by default, the \_TIME\_ variable in the resource usage output data set increases by one unit *interval* of the default calendar for every

observation. Further, the MAXDATE= option is used in the RESOURCE statement to get resource usage information only for the month of December.

```
proc cpm date='1dec03'd interval=weekday
         resourceout=rout data=widgres
         holidata=holdata;
   id task;
   tailnode tail;
   duration days;
   headnode head;
   resource engineer / maxdate='31dec03'd;
   holiday hol;
run;
```

#### Output 4.14.3 Resource Utilization: Resource Usage Data Set

#### Summarizing Resource Utilization Resource Usage

Obs	_TIME_	Engineer	Lengineer
1	01DEC03	2	2
2	02DEC03	2	2
3	03DEC03	2	2
4	04DEC03	2	2
5	05DEC03	2	2
6	08DEC03	4	1
7	09DEC03	4	1
8	10DEC03	4	1
9	11DEC03	4	1
10	12DEC03	4	1
11	15DEC03	1	3
12	16DEC03	1	3
13	17DEC03	1	3
14	18DEC03	1	3
15	19DEC03	1	3
16	22DEC03	4	4
17	23DEC03	4	4
18	24DEC03	4	4
19	26DEC03	4	4
20	29DEC03	4	4
21	30DEC03	4	4
22	31DEC03	4	4

This data set can be used as input for any type of resource utilization report. In this example, the resource usage for the month of December is presented in two ways: on a calendar and in a chart. The following program prints the calendar and bar chart:

```
/* format the Engineer variables */
proc format;
  picture efmt other='9 ESS Eng.';
  picture lfmt other='9 LSS Eng.';
```

```


proc calendar legend weekdays
  data=rout holidata=holodata;
  id _time_;
  var eengineer lengineer;
  format eengineer efmt. lengineer lfmt.;
  holiday hol;
  holiname name;

proc chart data=rout;
  hbar _time_/sumvar=eengineer discrete;
  hbar _time_/sumvar=lengineer discrete;
run;

```


#### Output 4.14.4 Calendar Showing Resource Usage


### Summarizing Resource Utilization Resource Usage

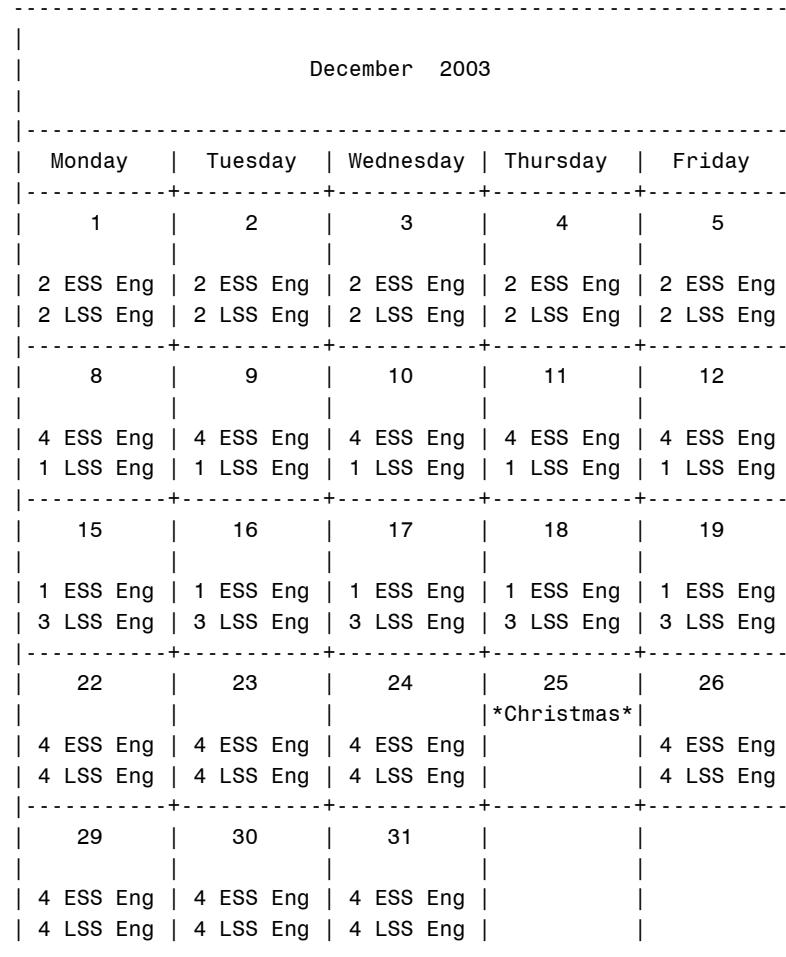

**Output 4.14.4** *continued*

Legend	
ESS Usage of engineer	
LSS Usage of engineer	

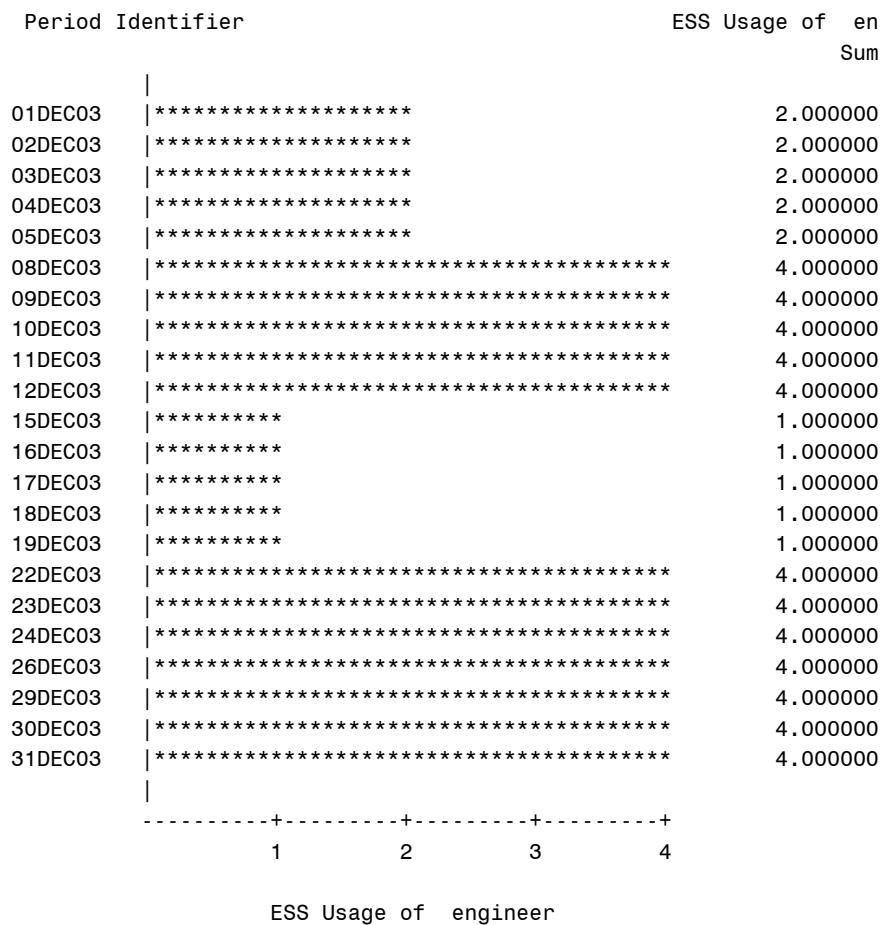**Output 4.14.5** Bar Chart for Early Start Usage**Summarizing Resource Utilization  
Resource Usage**

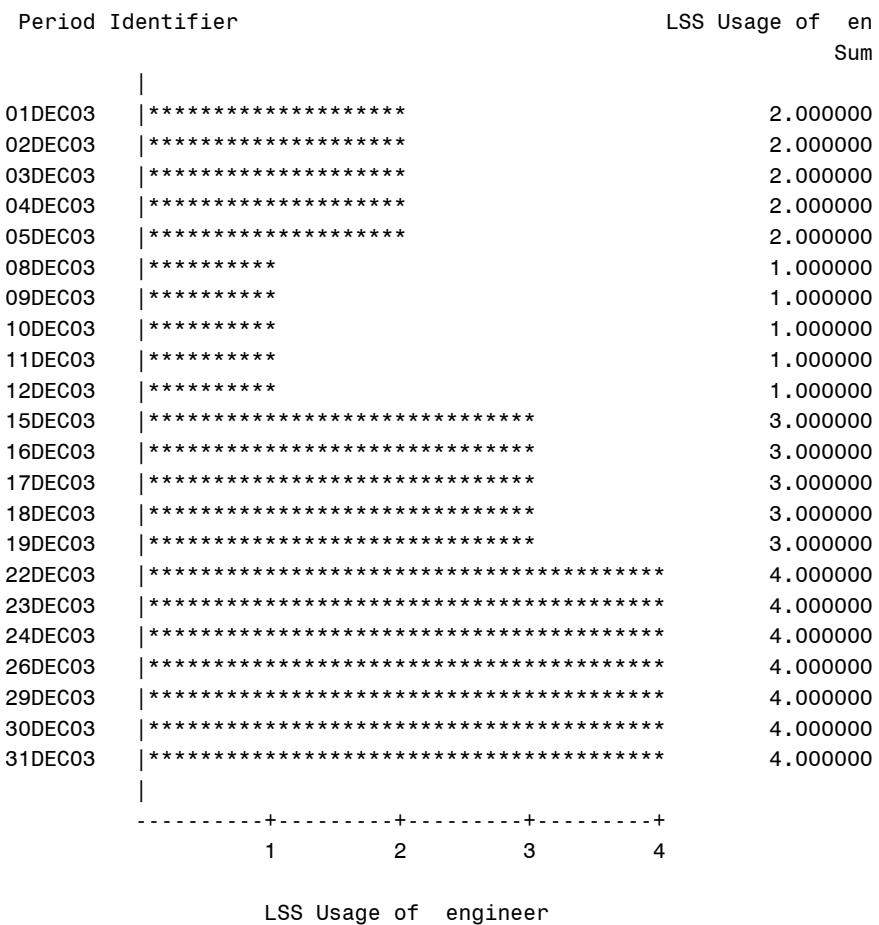**Output 4.14.6 Bar Chart for Late Start Usage****Summarizing Resource Utilization  
Resource Usage**

Charts such as those shown in Output 4.14.4 through Output 4.14.6 can be used to compare different schedules with respect to resource usage.

**Example 4.15: Resource Allocation**

In the previous example, a summary of the resource utilization is obtained. Suppose that you want to schedule the project subject to constraints on the availability of ENGINEERS. The activity data, as in Example 4.14, are assumed to be in a data set named WIDGRES. The resource variable, engineer, specifies the number of engineers needed per day for each activity in the project. In addition to the resource engineer, a consumable resource engcost is computed at a daily rate of 200 for each unit of resource engineer used per day. The following DATA step uses the Activity data set from Example 4.14 to create a new Activity data set that includes the resource engcost.

```
data widgres;
set widgres;
if engineer ^= . then engcost = engineer * 200;
run;
```

Now suppose that the availability of the resource engineer and the total outlay for engcost is saved in a data set named WIDGRIN, displayed in [Output 4.15.1](#).

#### **Output 4.15.1** Resource Availability Data Set

# **Resource Allocation Data Set WIDGRIN**

Obs	per	otype	engineer	engcost
1	.	restype	1	2
2	.	suplevel	1	.
3	01DEC03	reslevel	3	40000
4	26DEC03	reslevel	4	.

In the data set WIDGRIN, the first observation indicates that engineer is a replenishable resource, while engcost is a consumable resource. The second observation indicates that an extra engineer is available, if necessary. The remaining observations indicate the availability profile starting from December 1, 2003. PROC CPM is then used to schedule the project to start on December 1, 2003, subject to the availability as specified.

```
proc cpm date='01dec03'd interval=weekday  
        data=widgres holidata=holdata resin=widgrin  
        out=widgschd resout=widgrout;  
  
tailnode tail;  
duration days;  
headnode head;  
holiday hol;  
resource engineer engcost / period=per obstype=otype  
                           schedrule=shortdur  
                           delayanalysis;  
  
id task;  
run;
```

**Output 4.15.2** Resource Constrained Schedule: Rule = SHORTDUR

**Resource Allocation**  
**Resource Constrained Schedule: Rule = SHORTDUR**

Obs	tail	head	days	task	engineer	engcost	S_START	S_FINISH	E_START	E_FINISH
1	1	2	5	Approve Plan	2	400	01DEC03	05DEC03	01DEC03	05DEC03
2	2	3	10	Drawings	1	200	15DEC03	29DEC03	08DEC03	19DEC03
3	2	4	5	Study Market	1	200	08DEC03	12DEC03	08DEC03	12DEC03
4	2	3	5	Write Specs	2	400	08DEC03	12DEC03	08DEC03	12DEC03
5	3	5	15	Prototype	4	800	30DEC03	20JAN04	22DEC03	13JAN04
6	4	6	10	Mkt. Strat.	.	.	15DEC03	29DEC03	15DEC03	29DEC03
7	5	7	10	Materials	.	.	21JAN04	03FEB04	14JAN04	27JAN04
8	5	7	10	Facility	2	400	21JAN04	03FEB04	14JAN04	27JAN04
9	7	8	10	Init. Prod.	4	800	04FEB04	17FEB04	28JAN04	10FEB04
10	8	9	10	Evaluate	1	200	18FEB04	02MAR04	11FEB04	24FEB04
11	6	9	15	Test Market	.	.	18FEB04	09MAR04	11FEB04	02MAR04
12	9	10	5	Changes	2	400	10MAR04	16MAR04	03MAR04	09MAR04
13	10	11	0	Production	4	800	17MAR04	17MAR04	10MAR04	10MAR04
14	6	12	0	Marketing	.	.	18FEB04	18FEB04	11FEB04	11FEB04
15	8	6	0	Dummy	.	.	18FEB04	18FEB04	11FEB04	11FEB04

Obs	L_START	L_FINISH	R_DELAY	DELAY_R	SUPPL_R
1	01DEC03	05DEC03	0		
2	08DEC03	19DEC03	5	engineer	
3	21JAN04	27JAN04	0		
4	15DEC03	19DEC03	0		
5	22DEC03	13JAN04	0		
6	28JAN04	10FEB04	0		
7	14JAN04	27JAN04	0		
8	14JAN04	27JAN04	0		
9	28JAN04	10FEB04	0		
10	18FEB04	02MAR04	0		
11	11FEB04	02MAR04	0		
12	03MAR04	09MAR04	0		
13	10MAR04	10MAR04	0		
14	10MAR04	10MAR04	0		
15	11FEB04	11FEB04	0		

In the first invocation of PROC CPM, the scheduling rule used for ordering the activities to be scheduled at a given time is specified to be SHORTDUR. The data set WIDGSCHD, displayed in [Output 4.15.2](#), contains the resource constrained start and finish times in the variables S\_START and S\_FINISH. On December 8, three activities can be scheduled, all of which require the resource engineer. Using the scheduling rule specified, PROC CPM schedules the activities with the shortest durations first; thus, the activity ‘Drawings’ is delayed by five working days, until December 15, 2003.

The DELAYANALYSIS option in the RESOURCE statement helps analyze the cause of the delay by adding three new variables to the Schedule data set, R\_DELAY, DELAY\_R, and SUPPL\_R. In this example, the R\_DELAY and DELAY\_R variables indicate that there is a delay of five days in the activity ‘Drawings’ due to the resource engineer. Such information helps to pinpoint the source of resource insufficiency, if any.

Other activities that follow ‘Drawings’ also have S\_START>E\_START, but the slippage in these activities is not caused by resource insufficiency, it is due to their predecessors being delayed. The entire project is delayed by five working days due to resource constraints (the maximum value of S\_FINISH is 17MAR04, while the maximum value of E\_FINISH is 10MAR04).

In this invocation, the DELAY= option is not specified; therefore, the supplementary level of resource is not used, since the primary levels of resources are found to be sufficient to schedule the project by delaying some of the activities.

The data set WIDGROUT, displayed in [Output 4.15.3](#), contains variables Rengineer and Aengineer in addition to the variables Eengineer and Lengineer. The variable Rengineer denotes the usage of the resource engineer corresponding to the resource-constrained schedule, and Aengineer denotes the remaining level of the resource after resource allocation. For the consumable resource engcost, the variables Eengcost, Lengcost, and Rengcost indicate the rate of usage per unit *routinterval* (which defaults to INTERVAL=WEEKDAY, in this case) at the start of the time interval specified in the variable \_TIME\_. The variable Aengcost denotes the amount of money available at the beginning of the time specified in the \_TIME\_ variable.

**Output 4.15.3 Resource Usage: Rule = SHOR\_TDUR**

**Resource Allocation**  
**Usage Profiles for Constrained Schedule: Rule = SHOR\_TDUR**

	E	L	R	A	E	L	R	A
	e	e	e	e	n	n	n	n
	n	n	n	n	e	e	e	e
	g	g	g	g	n	n	n	n
	T	i	i	i	g	g	g	g
	I	n	n	n	c	c	c	c
O	M	e	e	e	o	o	o	o
b	E	e	e	e	s	s	s	s
s	_	r	r	r	t	t	t	t
1	01DEC03	2	2	2	1	400	400	400
2	02DEC03	2	2	2	1	400	400	400
3	03DEC03	2	2	2	1	400	400	400
4	04DEC03	2	2	2	1	400	400	400
5	05DEC03	2	2	2	1	400	400	400
6	08DEC03	4	1	3	0	800	200	600
7	09DEC03	4	1	3	0	800	200	600
8	10DEC03	4	1	3	0	800	200	600
9	11DEC03	4	1	3	0	800	200	600
10	12DEC03	4	1	3	0	800	200	600
11	15DEC03	1	3	1	2	200	600	200
12	16DEC03	1	3	1	2	200	600	200
13	17DEC03	1	3	1	2	200	600	200
14	18DEC03	1	3	1	2	200	600	200
15	19DEC03	1	3	1	2	200	600	200
16	22DEC03	4	4	1	2	800	800	200
17	23DEC03	4	4	1	2	800	800	200
18	24DEC03	4	4	1	2	800	800	200
19	26DEC03	4	4	1	3	800	800	200
20	29DEC03	4	4	1	3	800	800	200
21	30DEC03	4	4	4	0	800	800	800
22	31DEC03	4	4	4	0	800	800	800
23	02JAN04	4	4	4	0	800	800	800
24	05JAN04	4	4	4	0	800	800	800
25	06JAN04	4	4	4	0	800	800	800
26	07JAN04	4	4	4	0	800	800	800
27	08JAN04	4	4	4	0	800	800	800
28	09JAN04	4	4	4	0	800	800	800
29	12JAN04	4	4	4	0	800	800	800
30	13JAN04	4	4	4	0	800	800	800
31	14JAN04	2	2	4	0	400	400	800
32	15JAN04	2	2	4	0	400	400	800
33	16JAN04	2	2	4	0	400	400	800
34	19JAN04	2	2	4	0	400	400	800
35	20JAN04	2	2	4	0	400	400	800
36	21JAN04	2	3	2	2	400	600	400
37	22JAN04	2	3	2	2	400	600	400
38	23JAN04	2	3	2	2	400	600	400
39	26JAN04	2	3	2	2	400	600	400
40	27JAN04	2	3	2	2	400	600	400

**Output 4.15.3** *continued*

**Resource Allocation**  
**Usage Profiles for Constrained Schedule: Rule = SHORTDUR**

		E	L	R	A				
		e e e e	E	L	R	A			
		n n n n	e	e	e	e			
		g g g g	n	n	n	n			
		T	i i i i	g	g	g			
		I	n n n n	c	c	c			
O	M	e e e e	o	o	o	o			
b	E	e e e e	s	s	s	s			
s	_	r r r r	t	t	t	t			
<b>41</b>	28JAN04	4 4 2 2	800 800	400	19000				
<b>42</b>	29JAN04	4 4 2 2	800 800	400	18600				
<b>43</b>	30JAN04	4 4 2 2	800 800	400	18200				
<b>44</b>	02FEB04	4 4 2 2	800 800	400	17800				
<b>45</b>	03FEB04	4 4 2 2	800 800	400	17400				
<b>46</b>	04FEB04	4 4 4 0	800 800	800	17000				
<b>47</b>	05FEB04	4 4 4 0	800 800	800	16200				
<b>48</b>	06FEB04	4 4 4 0	800 800	800	15400				
<b>49</b>	09FEB04	4 4 4 0	800 800	800	14600				
<b>50</b>	10FEB04	4 4 4 0	800 800	800	13800				
<b>51</b>	11FEB04	1 0 4 0	200 0	800	13000				
<b>52</b>	12FEB04	1 0 4 0	200 0	800	12200				
<b>53</b>	13FEB04	1 0 4 0	200 0	800	11400				
<b>54</b>	16FEB04	1 0 4 0	200 0	800	10600				
<b>55</b>	17FEB04	1 0 4 0	200 0	800	9800				
<b>56</b>	18FEB04	1 1 1 3	200 200	200	9000				
<b>57</b>	19FEB04	1 1 1 3	200 200	200	8800				
<b>58</b>	20FEB04	1 1 1 3	200 200	200	8600				
<b>59</b>	23FEB04	1 1 1 3	200 200	200	8400				
<b>60</b>	24FEB04	1 1 1 3	200 200	200	8200				
<b>61</b>	25FEB04	0 1 1 3	0 200	200	8000				
<b>62</b>	26FEB04	0 1 1 3	0 200	200	7800				
<b>63</b>	27FEB04	0 1 1 3	0 200	200	7600				
<b>64</b>	01MAR04	0 1 1 3	0 200	200	7400				
<b>65</b>	02MAR04	0 1 1 3	0 200	200	7200				
<b>66</b>	03MAR04	2 2 0 4	400 400	0	7000				
<b>67</b>	04MAR04	2 2 0 4	400 400	0	7000				
<b>68</b>	05MAR04	2 2 0 4	400 400	0	7000				
<b>69</b>	08MAR04	2 2 0 4	400 400	0	7000				
<b>70</b>	09MAR04	2 2 0 4	400 400	0	7000				
<b>71</b>	10MAR04	0 0 2 2	0 0	400	7000				
<b>72</b>	11MAR04	0 0 2 2	0 0	400	6600				
<b>73</b>	12MAR04	0 0 2 2	0 0	400	6200				
<b>74</b>	15MAR04	0 0 2 2	0 0	400	5800				
<b>75</b>	16MAR04	0 0 2 2	0 0	400	5400				
<b>76</b>	17MAR04	0 0 0 4	0 0	0	5000				

The second invocation of PROC CPM uses a different scheduling rule (LST, which is the default scheduling rule). Ties are broken using the L\_START times for the activities. In this example, this rule results in a shorter project schedule. The schedule and the resource usage data sets are displayed in [Output 4.15.4](#) and [Output 4.15.5](#), respectively. Once again the variables DELAY\_R and R\_DELAY indicate that the resource engineer caused the activity ‘Study Market’ (‘Prototype’) to be delayed by five days (three days). However, the entire project is delayed only by three working days because the activity ‘Study Market’ is not a critical activity, and delaying it by five days did not affect the project completion time. Even with the resource delay of 5 days, this activity is scheduled earlier (S\_START=15DEC03) than its latest start time (L\_START=21JAN04).

```
proc cpm date='01dec03'd
    interval=weekday
    data=widgres
    resin=widgrin
    holidata=holdata
    out=widgsch2
    resout=widgrou2;
tailnode tail;
duration days;
headnode head;
holiday hol;
resource engineer engcost / period=per
    obstype=otype
    schedrule=lst
    delayanalysis;
id task;
run;
```

**Output 4.15.4** Resource Constrained Schedule: Rule = LST

**Resource Allocation**  
**Resource Constrained Schedule: Rule = LST**

Obs	tail	head	days	task	engineer	engcost	S_START	S_FINISH	E_START	E_FINISH
1	1	2	5	Approve Plan	2	400	01DEC03	05DEC03	01DEC03	05DEC03
2	2	3	10	Drawings	1	200	08DEC03	19DEC03	08DEC03	19DEC03
3	2	4	5	Study Market	1	200	15DEC03	19DEC03	08DEC03	12DEC03
4	2	3	5	Write Specs	2	400	08DEC03	12DEC03	08DEC03	12DEC03
5	3	5	15	Prototype	4	800	26DEC03	16JAN04	22DEC03	13JAN04
6	4	6	10	Mkt. Strat.	.	.	22DEC03	06JAN04	15DEC03	29DEC03
7	5	7	10	Materials	.	.	19JAN04	30JAN04	14JAN04	27JAN04
8	5	7	10	Facility	2	400	19JAN04	30JAN04	14JAN04	27JAN04
9	7	8	10	Init. Prod.	4	800	02FEB04	13FEB04	28JAN04	10FEB04
10	8	9	10	Evaluate	1	200	16FEB04	27FEB04	11FEB04	24FEB04
11	6	9	15	Test Market	.	.	16FEB04	05MAR04	11FEB04	02MAR04
12	9	10	5	Changes	2	400	08MAR04	12MAR04	03MAR04	09MAR04
13	10	11	0	Production	4	800	15MAR04	15MAR04	10MAR04	10MAR04
14	6	12	0	Marketing	.	.	16FEB04	16FEB04	11FEB04	11FEB04
15	8	6	0	Dummy	.	.	16FEB04	16FEB04	11FEB04	11FEB04

Obs	L_START	L_FINISH	R_DELAY	DELAY_R	SUPPL_R
1	01DEC03	05DEC03	0		
2	08DEC03	19DEC03	0		
3	21JAN04	27JAN04	5	engineer	
4	15DEC03	19DEC03	0		
5	22DEC03	13JAN04	3	engineer	
6	28JAN04	10FEB04	0		
7	14JAN04	27JAN04	0		
8	14JAN04	27JAN04	0		
9	28JAN04	10FEB04	0		
10	18FEB04	02MAR04	0		
11	11FEB04	02MAR04	0		
12	03MAR04	09MAR04	0		
13	10MAR04	10MAR04	0		
14	10MAR04	10MAR04	0		
15	11FEB04	11FEB04	0		

**Output 4.15.5** Resource Usage: Rule = LST

**Resource Allocation**  
**Usage Profiles for Constrained Schedule: Rule = LST**

	E	L	R	A					
	e e e e	E	L	R	A				
	n n n n	e	e	e	e				
	g g g g	n	n	n	n				
	T	i i i i	g	g	g				
	I	n n n n	c	c	c				
O	M	e e e e	o	o	o				
b	E	e e e s	s	s	s				
s	_	r r r r	t	t	t				
1	01DEC03	2 2 2 1	400 400 400	400 400 40000					
2	02DEC03	2 2 2 1	400 400 400	400 39600					
3	03DEC03	2 2 2 1	400 400 400	400 39200					
4	04DEC03	2 2 2 1	400 400 400	400 38800					
5	05DEC03	2 2 2 1	400 400 400	400 38400					
6	08DEC03	4 1 3 0	800 200 600	38000					
7	09DEC03	4 1 3 0	800 200 600	37400					
8	10DEC03	4 1 3 0	800 200 600	36800					
9	11DEC03	4 1 3 0	800 200 600	36200					
10	12DEC03	4 1 3 0	800 200 600	35600					
11	15DEC03	1 3 2 1	200 600 400	35000					
12	16DEC03	1 3 2 1	200 600 400	34600					
13	17DEC03	1 3 2 1	200 600 400	34200					
14	18DEC03	1 3 2 1	200 600 400	33800					
15	19DEC03	1 3 2 1	200 600 400	33400					
16	22DEC03	4 4 0 3	800 800 0	33000					
17	23DEC03	4 4 0 3	800 800 0	33000					
18	24DEC03	4 4 0 3	800 800 0	33000					
19	26DEC03	4 4 4 0	800 800 800	33000					
20	29DEC03	4 4 4 0	800 800 800	32200					
21	30DEC03	4 4 4 0	800 800 800	31400					
22	31DEC03	4 4 4 0	800 800 800	30600					
23	02JAN04	4 4 4 0	800 800 800	29800					
24	05JAN04	4 4 4 0	800 800 800	29000					
25	06JAN04	4 4 4 0	800 800 800	28200					
26	07JAN04	4 4 4 0	800 800 800	27400					
27	08JAN04	4 4 4 0	800 800 800	26600					
28	09JAN04	4 4 4 0	800 800 800	25800					
29	12JAN04	4 4 4 0	800 800 800	25000					
30	13JAN04	4 4 4 0	800 800 800	24200					
31	14JAN04	2 2 4 0	400 400 800	23400					
32	15JAN04	2 2 4 0	400 400 800	22600					
33	16JAN04	2 2 4 0	400 400 800	21800					
34	19JAN04	2 2 2 2	400 400 400	21000					
35	20JAN04	2 2 2 2	400 400 400	20600					
36	21JAN04	2 3 2 2	400 600 400	20200					
37	22JAN04	2 3 2 2	400 600 400	19800					
38	23JAN04	2 3 2 2	400 600 400	19400					
39	26JAN04	2 3 2 2	400 600 400	19000					
40	27JAN04	2 3 2 2	400 600 400	18600					

**Output 4.15.5 *continued***  
**Resource Allocation**  
**Usage Profiles for Constrained Schedule: Rule = LST**

		E	L	R	A			
		e e e e	E	L	R	A		
		n n n n	e	e	e	e		
		g g g g	n	n	n	n		
	T	i i i i	g	g	g	g		
O	I	n n n n	c	c	c	c		
b	M	e e e e	o	o	o	o		
s	E	e e e s	s	s	s	s		
	_	r r r r	t	t	t	t		
<b>41</b>	28JAN04	4 4 2 2	800 800	400	18200			
<b>42</b>	29JAN04	4 4 2 2	800 800	400	17800			
<b>43</b>	30JAN04	4 4 2 2	800 800	400	17400			
<b>44</b>	02FEB04	4 4 4 0	800 800	800	17000			
<b>45</b>	03FEB04	4 4 4 0	800 800	800	16200			
<b>46</b>	04FEB04	4 4 4 0	800 800	800	15400			
<b>47</b>	05FEB04	4 4 4 0	800 800	800	14600			
<b>48</b>	06FEB04	4 4 4 0	800 800	800	13800			
<b>49</b>	09FEB04	4 4 4 0	800 800	800	13000			
<b>50</b>	10FEB04	4 4 4 0	800 800	800	12200			
<b>51</b>	11FEB04	1 0 4 0	200 0	800	11400			
<b>52</b>	12FEB04	1 0 4 0	200 0	800	10600			
<b>53</b>	13FEB04	1 0 4 0	200 0	800	9800			
<b>54</b>	16FEB04	1 0 1 3	200 0	200 0	9000			
<b>55</b>	17FEB04	1 0 1 3	200 0	200 0	8800			
<b>56</b>	18FEB04	1 1 1 3	200 200	200 200	8600			
<b>57</b>	19FEB04	1 1 1 3	200 200	200 200	8400			
<b>58</b>	20FEB04	1 1 1 3	200 200	200 200	8200			
<b>59</b>	23FEB04	1 1 1 3	200 200	200 200	8000			
<b>60</b>	24FEB04	1 1 1 3	200 200	200 200	7800			
<b>61</b>	25FEB04	0 1 1 3	0 200	200 0	7600			
<b>62</b>	26FEB04	0 1 1 3	0 200	200 0	7400			
<b>63</b>	27FEB04	0 1 1 3	0 200	200 0	7200			
<b>64</b>	01MAR04	0 1 0 4	0 200	0 200	7000			
<b>65</b>	02MAR04	0 1 0 4	0 200	0 200	7000			
<b>66</b>	03MAR04	2 2 0 4	400 400	0 400	7000			
<b>67</b>	04MAR04	2 2 0 4	400 400	0 400	7000			
<b>68</b>	05MAR04	2 2 0 4	400 400	0 400	7000			
<b>69</b>	08MAR04	2 2 2 2	400 400	400 400	7000			
<b>70</b>	09MAR04	2 2 2 2	400 400	400 400	6600			
<b>71</b>	10MAR04	0 0 2 2	0 0	400 400	6200			
<b>72</b>	11MAR04	0 0 2 2	0 0	400 400	5800			
<b>73</b>	12MAR04	0 0 2 2	0 0	400 400	5400			
<b>74</b>	15MAR04	0 0 0 4	0 0	0 0	5000			

---

## Example 4.16: Using Supplementary Resources

In this example, the same project as in Example 4.15 is scheduled with a specification of DELAY=0. This indicates to PROC CPM that a supplementary level of resources is to be used if an activity cannot be scheduled to start on or before its latest start time (as computed in the unconstrained case). The schedule data and resource usage data are saved in the data sets WIDGO16 and WIDGRO16, respectively. They are displayed in Output 4.16.1 and Output 4.16.2, respectively.

```
title 'Using Supplementary Resources';
proc cpm date='01dec03'd interval=weekday
    data=widgres holdata=holdata resin=widgrin
    out=widgo16 resout=widgro16;
tailnode tail;
duration days;
headnode head;
holiday hol;
resource engineer engcost / period=per obstype=otype
    cumusage
    delay=0
    delayanalysis
    routnobreak;
id task;
run;
```

To analyze the results of the resource constrained scheduling, you must examine both output data sets, WIDGRO16 and WIDGO16. The negative values for Aengineer in observation numbers 22 through 25 of the Usage data set WIDGRO16 indicate the amount of supplementary resource that is needed on December 22, 23, 24, and 25, to complete the project without delaying any activity beyond its latest start time. Examination of the SUPPL\_R variable in the Schedule data set WIDGO16 indicates that the activity, ‘Prototype’, is scheduled to start on December 22 by using a supplementary level of the resource engineer.

The supplementary level is used only if the activity would otherwise get delayed beyond L\_START + DELAY. Thus, the activity ‘Study Market’ is delayed by five days (S\_START = ‘15DEC03’) and scheduled later than its early start time (E\_START = ‘08DEC03’), even though a supplementary level of the resource could have been used to start the activity earlier, because the activity’s L\_START time is equal to ‘21JAN04’ and DELAY = 0.

Further, note the use of the option CUMUSAGE in the RESOURCE statement, requesting that *cumulative* resource usage be saved in the Usage data set for consumable resources. Thus, for the consumable resource engcost, the procedure saves the *cumulative* resource usage in the variables Eengcost, Lengcost, and Rengcost, respectively. For instance, Eengcost in a given observation specifies the cumulative value of engcost for the early start schedule through the end of the previous day.

**Output 4.16.1** Resource-Constrained Schedule: Supplementary Resource

**Using Supplementary Resources**  
**Resource Constrained Schedule**

Obs	tail	head	days	task	engineer	engcost	S_START	S_FINISH	E_START	E_FINISH
1	1	2	5	Approve Plan	2	400	01DEC03	05DEC03	01DEC03	05DEC03
2	2	3	10	Drawings	1	200	08DEC03	19DEC03	08DEC03	19DEC03
3	2	4	5	Study Market	1	200	15DEC03	19DEC03	08DEC03	12DEC03
4	2	3	5	Write Specs	2	400	08DEC03	12DEC03	08DEC03	12DEC03
5	3	5	15	Prototype	4	800	22DEC03	13JAN04	22DEC03	13JAN04
6	4	6	10	Mkt. Strat.	.	.	22DEC03	06JAN04	15DEC03	29DEC03
7	5	7	10	Materials	.	.	14JAN04	27JAN04	14JAN04	27JAN04
8	5	7	10	Facility	2	400	14JAN04	27JAN04	14JAN04	27JAN04
9	7	8	10	Init. Prod.	4	800	28JAN04	10FEB04	28JAN04	10FEB04
10	8	9	10	Evaluate	1	200	11FEB04	24FEB04	11FEB04	24FEB04
11	6	9	15	Test Market	.	.	11FEB04	02MAR04	11FEB04	02MAR04
12	9	10	5	Changes	2	400	03MAR04	09MAR04	03MAR04	09MAR04
13	10	11	0	Production	4	800	10MAR04	10MAR04	10MAR04	10MAR04
14	6	12	0	Marketing	.	.	11FEB04	11FEB04	11FEB04	11FEB04
15	8	6	0	Dummy	.	.	11FEB04	11FEB04	11FEB04	11FEB04

Obs	L_START	L_FINISH	R_DELAY	DELAY_R	SUPPL_R
1	01DEC03	05DEC03	0		
2	08DEC03	19DEC03	0		
3	21JAN04	27JAN04	5	engineer	
4	15DEC03	19DEC03	0		
5	22DEC03	13JAN04	0		engineer
6	28JAN04	10FEB04	0		
7	14JAN04	27JAN04	0		
8	14JAN04	27JAN04	0		
9	28JAN04	10FEB04	0		
10	18FEB04	02MAR04	0		
11	11FEB04	02MAR04	0		
12	03MAR04	09MAR04	0		
13	10MAR04	10MAR04	0		
14	10MAR04	10MAR04	0		
15	11FEB04	11FEB04	0		

This example also illustrates the use of the ROUTNOBREAK option to produce a resource usage output data set that does not have any breaks for holidays. Thus, the output data set WIDGRO16 has observations corresponding to holidays and weekends, unlike the corresponding resource output data sets in Example 4.15. Note that for consumable resources with cumulative usage there is no accumulation of the resource on holidays; thus, the cumulative value of engcost at the beginning of the 7th and 8th of December equals the value for the beginning of the 6th of December. For the resource engineer, however, the resource is assumed to be tied to the activity in progress even across holidays or weekends that are spanned by the activity's duration. For example, both activities 'Drawings' and 'Write Specs' start on December 8, 2003, requiring one and two engineers, respectively. The 'Write Specs' activity finishes on the 12th, freeing up two engineers, whereas 'Drawings' finishes only on the 19th of December. Thus, the data set WIDGRO16 has Rengineer equal to '3' from 8DEC03 to 12DEC03 and then equal to '1' on the 13th and 14th of December. Another engineer is required by the activity 'Study Market' from December 15, 2003; thus, the total usage from 15DEC03 to 19DEC03 is '2'.

**Output 4.16.2** Resource Usage: Supplementary Resources

**Using Supplementary Resources**  
**Usage Profiles for Constrained Schedule**

		E	L	R	A				
		e e e e	E	L	R	A			
		n n n n	e	e	e	e			
		g g g g	n	n	n	n			
	T	i i i i	g	g	g	g			
	I	n n n n	c	c	c	c			
O	M	e e e e	o	o	o	o			
b	E	e e e e	s	s	s	s			
s	_	r r r r	t	t	t	t			
1	01DEC03	2 2 2 1	0	0	0	40000			
2	02DEC03	2 2 2 1	400	400	400	39600			
3	03DEC03	2 2 2 1	800	800	800	39200			
4	04DEC03	2 2 2 1	1200	1200	1200	38800			
5	05DEC03	2 2 2 1	1600	1600	1600	38400			
6	06DEC03	0 0 0 3	2000	2000	2000	38000			
7	07DEC03	0 0 0 3	2000	2000	2000	38000			
8	08DEC03	4 1 3 0	2000	2000	2000	38000			
9	09DEC03	4 1 3 0	2800	2200	2600	37400			
10	10DEC03	4 1 3 0	3600	2400	3200	36800			
11	11DEC03	4 1 3 0	4400	2600	3800	36200			
12	12DEC03	4 1 3 0	5200	2800	4400	35600			
13	13DEC03	1 1 1 2	6000	3000	5000	35000			
14	14DEC03	1 1 1 2	6000	3000	5000	35000			
15	15DEC03	1 3 2 1	6000	3000	5000	35000			
16	16DEC03	1 3 2 1	6200	3600	5400	34600			
17	17DEC03	1 3 2 1	6400	4200	5800	34200			
18	18DEC03	1 3 2 1	6600	4800	6200	33800			
19	19DEC03	1 3 2 1	6800	5400	6600	33400			
20	20DEC03	0 0 0 3	7000	6000	7000	33000			
21	21DEC03	0 0 0 3	7000	6000	7000	33000			
22	22DEC03	4 4 4 -1	7000	6000	7000	33000			
23	23DEC03	4 4 4 -1	7800	6800	7800	32200			
24	24DEC03	4 4 4 -1	8600	7600	8600	31400			
25	25DEC03	4 4 4 -1	9400	8400	9400	30600			
26	26DEC03	4 4 4 0	9400	8400	9400	30600			
27	27DEC03	4 4 4 0	10200	9200	10200	29800			
28	28DEC03	4 4 4 0	10200	9200	10200	29800			
29	29DEC03	4 4 4 0	10200	9200	10200	29800			
30	30DEC03	4 4 4 0	11000	10000	11000	29000			
31	31DEC03	4 4 4 0	11800	10800	11800	28200			
32	01JAN04	4 4 4 0	12600	11600	12600	27400			
33	02JAN04	4 4 4 0	12600	11600	12600	27400			
34	03JAN04	4 4 4 0	13400	12400	13400	26600			
35	04JAN04	4 4 4 0	13400	12400	13400	26600			
36	05JAN04	4 4 4 0	13400	12400	13400	26600			
37	06JAN04	4 4 4 0	14200	13200	14200	25800			
38	07JAN04	4 4 4 0	15000	14000	15000	25000			
39	08JAN04	4 4 4 0	15800	14800	15800	24200			
40	09JAN04	4 4 4 0	16600	15600	16600	23400			

**Output 4.16.2 *continued***  
**Using Supplementary Resources**  
**Usage Profiles for Constrained Schedule**

		E	L	R	A						
		e	e	e	e						
		n	n	n	n	e	e	e	e	e	
		g	g	g	g	n	n	n	n	n	
	T	i	i	i	i	g	g	g	g	g	
	I	n	n	n	n	c	c	c	c	c	
O	M	e	e	e	e	o	o	o	o	o	
b	E	e	e	e	s	s	s	s	s	s	
s	_	r	r	r	r	t	t	t	t	t	
<b>41</b>	10JAN04	4	4	4	0	17400	16400	17400	22600		
<b>42</b>	11JAN04	4	4	4	0	17400	16400	17400	22600		
<b>43</b>	12JAN04	4	4	4	0	17400	16400	17400	22600		
<b>44</b>	13JAN04	4	4	4	0	18200	17200	18200	21800		
<b>45</b>	14JAN04	2	2	2	2	19000	18000	19000	21000		
<b>46</b>	15JAN04	2	2	2	2	19400	18400	19400	20600		
<b>47</b>	16JAN04	2	2	2	2	19800	18800	19800	20200		
<b>48</b>	17JAN04	2	2	2	2	20200	19200	20200	19800		
<b>49</b>	18JAN04	2	2	2	2	20200	19200	20200	19800		
<b>50</b>	19JAN04	2	2	2	2	20200	19200	20200	19800		
<b>51</b>	20JAN04	2	2	2	2	20600	19600	20600	19400		
<b>52</b>	21JAN04	2	3	2	2	21000	20000	21000	19000		
<b>53</b>	22JAN04	2	3	2	2	21400	20600	21400	18600		
<b>54</b>	23JAN04	2	3	2	2	21800	21200	21800	18200		
<b>55</b>	24JAN04	2	3	2	2	22200	21800	22200	17800		
<b>56</b>	25JAN04	2	3	2	2	22200	21800	22200	17800		
<b>57</b>	26JAN04	2	3	2	2	22200	21800	22200	17800		
<b>58</b>	27JAN04	2	3	2	2	22600	22400	22600	17400		
<b>59</b>	28JAN04	4	4	4	0	23000	23000	23000	17000		
<b>60</b>	29JAN04	4	4	4	0	23800	23800	23800	16200		
<b>61</b>	30JAN04	4	4	4	0	24600	24600	24600	15400		
<b>62</b>	31JAN04	4	4	4	0	25400	25400	25400	14600		
<b>63</b>	01FEB04	4	4	4	0	25400	25400	25400	14600		
<b>64</b>	02FEB04	4	4	4	0	25400	25400	25400	14600		
<b>65</b>	03FEB04	4	4	4	0	26200	26200	26200	13800		
<b>66</b>	04FEB04	4	4	4	0	27000	27000	27000	13000		
<b>67</b>	05FEB04	4	4	4	0	27800	27800	27800	12200		
<b>68</b>	06FEB04	4	4	4	0	28600	28600	28600	11400		
<b>69</b>	07FEB04	4	4	4	0	29400	29400	29400	10600		
<b>70</b>	08FEB04	4	4	4	0	29400	29400	29400	10600		
<b>71</b>	09FEB04	4	4	4	0	29400	29400	29400	10600		
<b>72</b>	10FEB04	4	4	4	0	30200	30200	30200	9800		
<b>73</b>	11FEB04	1	0	1	3	31000	31000	31000	9000		
<b>74</b>	12FEB04	1	0	1	3	31200	31000	31200	8800		
<b>75</b>	13FEB04	1	0	1	3	31400	31000	31400	8600		
<b>76</b>	14FEB04	1	0	1	3	31600	31000	31600	8400		
<b>77</b>	15FEB04	1	0	1	3	31600	31000	31600	8400		
<b>78</b>	16FEB04	1	0	1	3	31600	31000	31600	8400		
<b>79</b>	17FEB04	1	0	1	3	31800	31000	31800	8200		
<b>80</b>	18FEB04	1	1	1	3	32000	31000	32000	8000		

**Output 4.16.2** *continued*

**Using Supplementary Resources  
Usage Profiles for Constrained Schedule**

		E	L	R	A	
		e e e e	E	L	R	A
		n n n n	e	e	e	e
		g g g g	n	n	n	n
	T	i i i i	g	g	g	g
	I	n n n n	c	c	c	c
O	M	e e e e	o	o	o	o
b	E	e e e e	s	s	s	s
s	_	r r r r	t	t	t	t
<b>81</b>	19FEB04	1 1 1	3	32200	31200	32200
<b>82</b>	20FEB04	1 1 1	3	32400	31400	32400
<b>83</b>	21FEB04	1 1 1	3	32600	31600	32600
<b>84</b>	22FEB04	1 1 1	3	32600	31600	32600
<b>85</b>	23FEB04	1 1 1	3	32600	31600	32600
<b>86</b>	24FEB04	1 1 1	3	32800	31800	32800
<b>87</b>	25FEB04	0 1 0	4	33000	32000	33000
<b>88</b>	26FEB04	0 1 0	4	33000	32200	33000
<b>89</b>	27FEB04	0 1 0	4	33000	32400	33000
<b>90</b>	28FEB04	0 1 0	4	33000	32600	33000
<b>91</b>	29FEB04	0 1 0	4	33000	32600	33000
<b>92</b>	01MAR04	0 1 0	4	33000	32600	33000
<b>93</b>	02MAR04	0 1 0	4	33000	32800	33000
<b>94</b>	03MAR04	2 2 2	2	33000	33000	33000
<b>95</b>	04MAR04	2 2 2	2	33400	33400	33400
<b>96</b>	05MAR04	2 2 2	2	33800	33800	33800
<b>97</b>	06MAR04	2 2 2	2	34200	34200	34200
<b>98</b>	07MAR04	2 2 2	2	34200	34200	34200
<b>99</b>	08MAR04	2 2 2	2	34200	34200	34200
<b>100</b>	09MAR04	2 2 2	2	34600	34600	34600
<b>101</b>	10MAR04	0 0 0	4	35000	35000	35000

---

### Example 4.17: INFEASDIAGNOSTIC Option and Aggregate Resource Type

The INFEASDIAGNOSTIC option instructs PROC CPM to continue scheduling even when resources are insufficient. When PROC CPM schedules subject to resource constraints, it stops the scheduling process when it cannot find sufficient resources (primary or supplementary) for an activity before the activity's latest possible start time (`L_START + DELAY`). In this case, you may want to determine which resources are needed to schedule all the activities and when the deficiencies occur. The INFEASDIAGNOSTIC option is equivalent to specifying infinite supplementary levels for all the resources under consideration; the `DELAY=` value is assumed to equal the default value of `+INFINITY`, unless it is specified otherwise.

The INFEASDIAGNOSTIC option is particularly useful when there are several resources involved and when project completion time is critical. You want things to be done on time, even if it means using supplementary resources or overtime resources; rather than trying to juggle activities around to try to fit available resource profiles, you want to determine the level of resources needed to accomplish tasks within a given time frame.

For the WIDGET manufacturing project, let us assume that there are four resources: a design engineer, a market analyst, a production engineer, and money. The resource requirements for the different activities are saved in a data set, WIDGR17, and displayed in [Output 4.17.1](#). Of these resources, suppose that the design engineer is the resource that is most crucial in terms of his availability; perhaps he is an outside contractor and you do not have control over his availability. You need to determine the project schedule subject to the constraints on the resource deseng. [Output 4.17.2](#) displays the RESOURCEIN= data set, RESIN17.

#### **Output 4.17.1 Data Set WIDGR17**

##### **Use of the INFEASDIAGNOSTIC Option Data Set WIDGR17**

Obs	task	days	tail	head	deseng	mktan	prodeng	money
1	Approve Plan	5	1	2	1	1	1	200
2	Drawings	10	2	3	1	.	1	100
3	Study Market	5	2	4	.	1	1	100
4	Write Specs	5	2	3	1	.	1	150
5	Prototype	15	3	5	1	.	1	300
6	Mkt. Strat.	10	4	6	.	1	.	150
7	Materials	10	5	7	.	.	.	300
8	Facility	10	5	7	.	.	1	500
9	Init. Prod.	10	7	8	.	.	.	250
10	Evaluate	10	8	9	1	.	.	150
11	Test Market	15	6	9	.	1	.	200
12	Changes	5	9	10	1	.	1	200
13	Production	0	10	11	1	.	1	600
14	Marketing	0	6	12	.	1	.	.
15	Dummy	0	8	6	.	.	.	.

#### **Output 4.17.2 Resourcein Data Set RESIN17**

##### **Use of the INFEASDIAGNOSTIC Option Data Set RESIN17**

Obs	per	otype	deseng	mktan	prodeng	money
1	.	restype	1	1	1	4
2	01DEC03	reslevel	1	.	1	.

In the first invocation of PROC CPM, the project is scheduled subject to resource constraints on the single resource variable deseng. [Output 4.17.3](#) displays the resulting Schedule data set WIDGO17S, which shows that the project is delayed by five days because of this resource. The project finish time has been delayed only by five days, even though R\_DELAY='10' for activity 'Write Specs'. This is due to the fact that there was a float of five days present in this activity.

```
proc cpm date='01dec03'd interval=weekday
           data=widgr17 holidata=holodata resin=resin17
           out=widgo17s;
tailnode tail;
duration days;
headnode head;
```

```

holiday hol;
resource deseng / period=per obstype=otype
               delayanalysis;
id task;
run;

```

**Output 4.17.3** Resource-Constrained Schedule: Single Resource

**Use of the INFEASDIAGNOSTIC Option  
Resource Constrained Schedule: Single Resource**

Obs	tail	head	days	task	deseng	S_START	S_FINISH	E_START	E_FINISH	L_START
1	1	2	5	Approve Plan	1	01DEC03	05DEC03	01DEC03	05DEC03	01DEC03
2	2	3	10	Drawings	1	08DEC03	19DEC03	08DEC03	19DEC03	08DEC03
3	2	4	5	Study Market	.	08DEC03	12DEC03	08DEC03	12DEC03	21JAN04
4	2	3	5	Write Specs	1	22DEC03	29DEC03	08DEC03	12DEC03	15DEC03
5	3	5	15	Prototype	1	30DEC03	20JAN04	22DEC03	13JAN04	22DEC03
6	4	6	10	Mkt. Strat.	.	15DEC03	29DEC03	15DEC03	29DEC03	28JAN04
7	5	7	10	Materials	.	21JAN04	03FEB04	14JAN04	27JAN04	14JAN04
8	5	7	10	Facility	.	21JAN04	03FEB04	14JAN04	27JAN04	14JAN04
9	7	8	10	Init. Prod.	.	04FEB04	17FEB04	28JAN04	10FEB04	28JAN04
10	8	9	10	Evaluate	1	18FEB04	02MAR04	11FEB04	24FEB04	18FEB04
11	6	9	15	Test Market	.	18FEB04	09MAR04	11FEB04	02MAR04	11FEB04
12	9	10	5	Changes	1	10MAR04	16MAR04	03MAR04	09MAR04	03MAR04
13	10	11	0	Production	1	17MAR04	17MAR04	10MAR04	10MAR04	10MAR04
14	6	12	0	Marketing	.	18FEB04	18FEB04	11FEB04	11FEB04	10MAR04
15	8	6	0	Dummy	.	18FEB04	18FEB04	11FEB04	11FEB04	11FEB04

Obs	L_FINISH	R_DELAY	DELAY_R	SUPPL_R
1	05DEC03	0		
2	19DEC03	0		
3	27JAN04	0		
4	19DEC03	10	deseng	
5	13JAN04	0		
6	10FEB04	0		
7	27JAN04	0		
8	27JAN04	0		
9	10FEB04	0		
10	02MAR04	0		
11	02MAR04	0		
12	09MAR04	0		
13	10MAR04	0		
14	10MAR04	0		
15	11FEB04	0		

Now suppose that you have one production engineer available, but you could obtain more if needed. You do not want to delay the project more than five days (the delay caused by deseng). The second invocation of PROC CPM sets a maximum delay of five days on the activities and specifies all four resources along with the INFEASDIAGNOSTIC option. The resource availability data set (printed in Output 4.17.2) has missing values for the resources mktan and money. Further, the resource money is defined to be a consumable aggregate resource (its value is '4' in the first observation). Thus, this resource is used by the CPM procedure

only for aggregation purposes and is not considered as a constraining resource during the scheduling process. The INFEASDIAGNOSTIC option enables CPM to assume an infinite supplementary level for all the constraining resources, and the procedure draws upon this infinite reserve, if necessary, to schedule the project with only five days of delay. In other words, PROC CPM assumes that there is an infinite supply of supplementary levels for all the relevant resources. Thus, if at any point in the scheduling process it finds that an activity does not have enough resources and it cannot be postponed any further, it schedules the activity ignoring the insufficiency of the resources.

```

proc cpm date='01dec03'd interval=weekday
         data=widgr17 holidata=holdata resin=resin17
         out=widgo17m resout=widgro17;
tailnode tail;
duration days;
headnode head;
holiday hol;
resource deseng prodeng mktan money / period=per obstype=otype
                                         delayanalysis
                                         delay=5
                                         infeasdiagnostic
                                         cumusage
                                         rcprofile avprofile;
id task;
run;

```

The Schedule data set WIDGO17M (for multiple resources) in [Output 4.17.4](#) shows the new resource-constrained schedule. With a maximum delay of five days the procedure schedules the activity ‘Study Market’ on January 21, 2004, using an extra production engineer as indicated by the SUPPL\_R variable. Note that the SUPPL\_R variable indicates the first resource in the resource list that was used beyond its primary level. Note also that it is possible to schedule the activities with only one production engineer, but the project would be delayed by more than five days.

The Usage data set, displayed in [Output 4.17.5](#), shows the amount of resources required on each day of the project. The data set contains usage and remaining resource information only for the resource-constrained schedule because PROC CPM was invoked with the RCPROFILE and AVPROFILE options in the RESOURCE statement. The availability profile contains only missing values for the resource money because it was used only for aggregation purposes. Further, since this resource is a consumable resource as per the RESOURCEIN= data set, and since the CUMUSAGE option is specified, the value for Rmoney in each observation indicates the cumulative amount of money that would be needed through the beginning of the date specified in that observation if the resource constrained schedule were followed.

For the other resources, the availability profile in the Usage data set contains negative values for all the resources that were insufficient on any given day. This feature is useful for diagnosing the level of insufficiency of any resource; you can determine the problem areas by examining the availability profile for the different resources. Thus, the negative values for the resource availability profile Aprodeng indicate that, in order for the project to be scheduled as desired, you need an extra production engineer between the 21st and 27th of January, 2004. The negative values for Amktan indicate the days when a market analyst is needed for the project.

**Output 4.17.4** Resource-Constrained Schedule: Multiple Resources

**Use of the INFEASDIAGNOSTIC Option**  
**Resource Constrained Schedule: Multiple Resources**

Obs	tail	head	days	task	deseng	prodeng	mktan	money	S_START	S_FINISH	E_START
1	1	2	5	Approve Plan	1	1	1	200	01DEC03	05DEC03	01DEC03
2	2	3	10	Drawings	1	1	.	100	08DEC03	19DEC03	08DEC03
3	2	4	5	Study Market	.	1	1	100	21JAN04	27JAN04	08DEC03
4	2	3	5	Write Specs	1	1	.	150	22DEC03	29DEC03	08DEC03
5	3	5	15	Prototype	1	1	.	300	30DEC03	20JAN04	22DEC03
6	4	6	10	Mkt. Strat.	.	.	1	150	28JAN04	10FEB04	15DEC03
7	5	7	10	Materials	.	.	.	300	21JAN04	03FEB04	14JAN04
8	5	7	10	Facility	.	1	.	500	21JAN04	03FEB04	14JAN04
9	7	8	10	Init. Prod.	.	.	.	250	04FEB04	17FEB04	28JAN04
10	8	9	10	Evaluate	1	.	.	150	18FEB04	02MAR04	11FEB04
11	6	9	15	Test Market	.	.	1	200	18FEB04	09MAR04	11FEB04
12	9	10	5	Changes	1	1	.	200	10MAR04	16MAR04	03MAR04
13	10	11	0	Production	1	1	.	600	17MAR04	17MAR04	10MAR04
14	6	12	0	Marketing	.	.	1	.	18FEB04	18FEB04	11FEB04
15	8	6	0	Dummy	.	.	.	.	18FEB04	18FEB04	11FEB04

Obs	E_FINISH	L_START	L_FINISH	R_DELAY	DELAY_R	SUPPL_R
1	05DEC03	01DEC03	05DEC03	0		mktan
2	19DEC03	08DEC03	19DEC03	0		
3	12DEC03	21JAN04	27JAN04	30	prodeng	prodeng
4	12DEC03	15DEC03	19DEC03	10	deseng	
5	13JAN04	22DEC03	13JAN04	0		
6	29DEC03	28JAN04	10FEB04	0		mktan
7	27JAN04	14JAN04	27JAN04	0		
8	27JAN04	14JAN04	27JAN04	0		
9	10FEB04	28JAN04	10FEB04	0		
10	24FEB04	18FEB04	02MAR04	0		
11	02MAR04	11FEB04	02MAR04	0		mktan
12	09MAR04	03MAR04	09MAR04	0		
13	10MAR04	10MAR04	10MAR04	0		
14	11FEB04	10MAR04	10MAR04	0		
15	11FEB04	11FEB04	11FEB04	0		

**Output 4.17.5 Resource Usage: Multiple Resources**

**Use of the INFEASDIAGNOSTIC Option**  
**Usage Profile: Multiple Resources**

Obs	_TIME_	Rdeseng	Adeseng	Rprodeng	Aprodeng	Rmktan	Amktan	Rmoney	Amoney
1	01DEC03	1	0	1	0	1	-1	0	.
2	02DEC03	1	0	1	0	1	-1	200	.
3	03DEC03	1	0	1	0	1	-1	400	.
4	04DEC03	1	0	1	0	1	-1	600	.
5	05DEC03	1	0	1	0	1	-1	800	.
6	08DEC03	1	0	1	0	0	0	1000	.
7	09DEC03	1	0	1	0	0	0	1100	.
8	10DEC03	1	0	1	0	0	0	1200	.
9	11DEC03	1	0	1	0	0	0	1300	.
10	12DEC03	1	0	1	0	0	0	1400	.
11	15DEC03	1	0	1	0	0	0	1500	.
12	16DEC03	1	0	1	0	0	0	1600	.
13	17DEC03	1	0	1	0	0	0	1700	.
14	18DEC03	1	0	1	0	0	0	1800	.
15	19DEC03	1	0	1	0	0	0	1900	.
16	22DEC03	1	0	1	0	0	0	2000	.
17	23DEC03	1	0	1	0	0	0	2150	.
18	24DEC03	1	0	1	0	0	0	2300	.
19	26DEC03	1	0	1	0	0	0	2450	.
20	29DEC03	1	0	1	0	0	0	2600	.
21	30DEC03	1	0	1	0	0	0	2750	.
22	31DEC03	1	0	1	0	0	0	3050	.
23	02JAN04	1	0	1	0	0	0	3350	.
24	05JAN04	1	0	1	0	0	0	3650	.
25	06JAN04	1	0	1	0	0	0	3950	.
26	07JAN04	1	0	1	0	0	0	4250	.
27	08JAN04	1	0	1	0	0	0	4550	.
28	09JAN04	1	0	1	0	0	0	4850	.
29	12JAN04	1	0	1	0	0	0	5150	.
30	13JAN04	1	0	1	0	0	0	5450	.
31	14JAN04	1	0	1	0	0	0	5750	.
32	15JAN04	1	0	1	0	0	0	6050	.
33	16JAN04	1	0	1	0	0	0	6350	.
34	19JAN04	1	0	1	0	0	0	6650	.
35	20JAN04	1	0	1	0	0	0	6950	.
36	21JAN04	0	1	2	-1	1	-1	7250	.
37	22JAN04	0	1	2	-1	1	-1	8150	.
38	23JAN04	0	1	2	-1	1	-1	9050	.
39	26JAN04	0	1	2	-1	1	-1	9950	.
40	27JAN04	0	1	2	-1	1	-1	10850	.
41	28JAN04	0	1	1	0	1	-1	11750	.
42	29JAN04	0	1	1	0	1	-1	12700	.
43	30JAN04	0	1	1	0	1	-1	13650	.
44	02FEB04	0	1	1	0	1	-1	14600	.
45	03FEB04	0	1	1	0	1	-1	15550	.
46	04FEB04	0	1	0	1	1	-1	16500	.

**Output 4.17.5** *continued*

**Use of the INFEASDIAGNOSTIC Option**  
**Usage Profile: Multiple Resources**

Obs	_TIME_	Rdeseng	Adeseng	Rprodeng	Aprodeng	Rmktn	Amktan	Rmoney	Amoney
47	05FEB04	0	1	0	1	1	-1	16900	.
48	06FEB04	0	1	0	1	1	-1	17300	.
49	09FEB04	0	1	0	1	1	-1	17700	.
50	10FEB04	0	1	0	1	1	-1	18100	.
51	11FEB04	0	1	0	1	0	0	18500	.
52	12FEB04	0	1	0	1	0	0	18750	.
53	13FEB04	0	1	0	1	0	0	19000	.
54	16FEB04	0	1	0	1	0	0	19250	.
55	17FEB04	0	1	0	1	0	0	19500	.
56	18FEB04	1	0	0	1	1	-1	19750	.
57	19FEB04	1	0	0	1	1	-1	20100	.
58	20FEB04	1	0	0	1	1	-1	20450	.
59	23FEB04	1	0	0	1	1	-1	20800	.
60	24FEB04	1	0	0	1	1	-1	21150	.
61	25FEB04	1	0	0	1	1	-1	21500	.
62	26FEB04	1	0	0	1	1	-1	21850	.
63	27FEB04	1	0	0	1	1	-1	22200	.
64	01MAR04	1	0	0	1	1	-1	22550	.
65	02MAR04	1	0	0	1	1	-1	22900	.
66	03MAR04	0	1	0	1	1	-1	23250	.
67	04MAR04	0	1	0	1	1	-1	23450	.
68	05MAR04	0	1	0	1	1	-1	23650	.
69	08MAR04	0	1	0	1	1	-1	23850	.
70	09MAR04	0	1	0	1	1	-1	24050	.
71	10MAR04	1	0	1	0	0	0	24250	.
72	11MAR04	1	0	1	0	0	0	24450	.
73	12MAR04	1	0	1	0	0	0	24650	.
74	15MAR04	1	0	1	0	0	0	24850	.
75	16MAR04	1	0	1	0	0	0	25050	.
76	17MAR04	0	1	0	1	0	0	25250	.

---

### Example 4.18: Variable Activity Delay

In Example 4.17, the DELAY= option is used to specify a maximum amount of delay that is allowed for all activities in the project. In some situations it may be reasonable to set the delay for each activity based on some characteristic pertaining to the activity. For example, consider the data in Example 4.17 with a slightly different scenario. Suppose that no delay is allowed in activities that require a production engineer. Data set WIDGR18, displayed in Output 4.18.1, is obtained from WIDGR17 using the following simple DATA step.

```
data widgr18;
  set widgr17;
  if prodeng ^= . then adelay = 0;
  else                  adelay = 5;
run;
```

```

title 'Variable Activity Delay';
title2 'Data Set WIDGR18';
proc print;
run;

```

**Output 4.18.1** Activity Data Set WIDGR18

**Variable Activity Delay  
Data Set WIDGR18**

Obs	task	days	tail	head	deseng	mktan	prodeng	money	adelay
1	Approve Plan	5	1	2	1	1	1	200	0
2	Drawings	10	2	3	1	.	1	100	0
3	Study Market	5	2	4	.	1	1	100	0
4	Write Specs	5	2	3	1	.	1	150	0
5	Prototype	15	3	5	1	.	1	300	0
6	Mkt. Strat.	10	4	6	.	1	.	150	5
7	Materials	10	5	7	.	.	.	300	5
8	Facility	10	5	7	.	.	1	500	0
9	Init. Prod.	10	7	8	.	.	.	250	5
10	Evaluate	10	8	9	1	.	.	150	5
11	Test Market	15	6	9	.	1	.	200	5
12	Changes	5	9	10	1	.	1	200	0
13	Production	0	10	11	1	.	1	600	0
14	Marketing	0	6	12	.	1	.	.	5
15	Dummy	0	8	6	.	.	.	.	5

PROC CPM is invoked with the ACTDELAY=ADELAY option in the RESOURCE statement. The INFEASDIAGNOSTIC option is also used to enable the procedure to schedule activities even if resources are insufficient. The output data sets are displayed in Output 4.18.2 and Output 4.18.3.

```

data resin17;
  input per & date7. otype $ 
    deseng mktan prodeng money;
  format per date7. ;
  datalines;
    restype 1 1 1 4
01dec03  reslevel 1 . 1 .
;

data holdata;
  format hol date7. name $9. ;
  input hol & date7. name & ;
  datalines;
25dec03  Christmas
01jan04  New Year
;

```

```
proc cpm date='01dec03'd
    interval=weekday
    data=widgr18
    holidata=holodata
    resin=resin17
    out=widgo18
    resout=widgro18;
tailnode tail;
duration days;
headnode head;
holiday hol;
resource deseng prodeng mktan money / period=per
    obstype=otype
    delayanalysis
    actdelay=adelay
    infeasdiagnostic
    rcs avl t_float
    cumusage;
id task;
run;
```

**Output 4.18.2** Resource-Constrained Schedule: Variable Activity Delay

**Variable Activity Delay**  
**Resource Constrained Schedule**

Obs	tail	head	days	task	adelay	deseng	prodeng	mktan	money	S_START	S_FINISH	E_START
1	1	2	5	Approve Plan	0	1	1	1	200	01DEC03	05DEC03	01DEC03
2	2	3	10	Drawings	0	1	1	.	100	08DEC03	19DEC03	08DEC03
3	2	4	5	Study Market	0	.	1	1	100	14JAN04	20JAN04	08DEC03
4	2	3	5	Write Specs	0	1	1	.	150	08DEC03	12DEC03	08DEC03
5	3	5	15	Prototype	0	1	1	.	300	22DEC03	13JAN04	22DEC03
6	4	6	10	Mkt. Strat.	5	.	.	1	150	21JAN04	03FEB04	15DEC03
7	5	7	10	Materials	5	.	.	.	300	14JAN04	27JAN04	14JAN04
8	5	7	10	Facility	0	.	1	.	500	14JAN04	27JAN04	14JAN04
9	7	8	10	Init. Prod.	5	.	.	.	250	28JAN04	10FEB04	28JAN04
10	8	9	10	Evaluate	5	1	.	.	150	11FEB04	24FEB04	11FEB04
11	6	9	15	Test Market	5	.	.	1	200	11FEB04	02MAR04	11FEB04
12	9	10	5	Changes	0	1	1	.	200	03MAR04	09MAR04	03MAR04
13	10	11	0	Production	0	1	1	.	600	10MAR04	10MAR04	10MAR04
14	6	12	0	Marketing	5	.	.	1	.	11FEB04	11FEB04	11FEB04
15	8	6	0	Dummy	5	.	.	.	.	11FEB04	11FEB04	11FEB04

Obs	E_FINISH	L_START	L_FINISH	T_FLOAT	R_DELAY	DELAY_R	SUPPL_R
1	05DEC03	01DEC03	05DEC03	0	0		mktan
2	19DEC03	08DEC03	19DEC03	0	0		
3	12DEC03	21JAN04	27JAN04	30	25	prodeng	prodeng
4	12DEC03	15DEC03	19DEC03	5	0		deseng
5	13JAN04	22DEC03	13JAN04	0	0		
6	29DEC03	28JAN04	10FEB04	30	0		mktan
7	27JAN04	14JAN04	27JAN04	0	0		
8	27JAN04	14JAN04	27JAN04	0	0		
9	10FEB04	28JAN04	10FEB04	0	0		
10	24FEB04	18FEB04	02MAR04	5	0		
11	02MAR04	11FEB04	02MAR04	0	0		mktan
12	09MAR04	03MAR04	09MAR04	0	0		
13	10MAR04	10MAR04	10MAR04	0	0		
14	11FEB04	10MAR04	10MAR04	20	0		
15	11FEB04	11FEB04	11FEB04	0	0		

**Output 4.18.3 Resource Usage****Variable Activity Delay  
Usage Profile**

<b>Obs</b>	<b>_TIME_</b>	<b>Rdeseng</b>	<b>Adeseng</b>	<b>Rprodeng</b>	<b>Aprodeng</b>	<b>Rmktan</b>	<b>Amktan</b>	<b>Rmoney</b>	<b>Amoney</b>
<b>1</b>	01DEC03	1	0	1	0	1	-1	0	.
<b>2</b>	02DEC03	1	0	1	0	1	-1	200	.
<b>3</b>	03DEC03	1	0	1	0	1	-1	400	.
<b>4</b>	04DEC03	1	0	1	0	1	-1	600	.
<b>5</b>	05DEC03	1	0	1	0	1	-1	800	.
<b>6</b>	08DEC03	2	-1	2	-1	0	0	1000	.
<b>7</b>	09DEC03	2	-1	2	-1	0	0	1250	.
<b>8</b>	10DEC03	2	-1	2	-1	0	0	1500	.
<b>9</b>	11DEC03	2	-1	2	-1	0	0	1750	.
<b>10</b>	12DEC03	2	-1	2	-1	0	0	2000	.
<b>11</b>	15DEC03	1	0	1	0	0	0	2250	.
<b>12</b>	16DEC03	1	0	1	0	0	0	2350	.
<b>13</b>	17DEC03	1	0	1	0	0	0	2450	.
<b>14</b>	18DEC03	1	0	1	0	0	0	2550	.
<b>15</b>	19DEC03	1	0	1	0	0	0	2650	.
<b>16</b>	22DEC03	1	0	1	0	0	0	2750	.
<b>17</b>	23DEC03	1	0	1	0	0	0	3050	.
<b>18</b>	24DEC03	1	0	1	0	0	0	3350	.
<b>19</b>	26DEC03	1	0	1	0	0	0	3650	.
<b>20</b>	29DEC03	1	0	1	0	0	0	3950	.
<b>21</b>	30DEC03	1	0	1	0	0	0	4250	.
<b>22</b>	31DEC03	1	0	1	0	0	0	4550	.
<b>23</b>	02JAN04	1	0	1	0	0	0	4850	.
<b>24</b>	05JAN04	1	0	1	0	0	0	5150	.
<b>25</b>	06JAN04	1	0	1	0	0	0	5450	.
<b>26</b>	07JAN04	1	0	1	0	0	0	5750	.
<b>27</b>	08JAN04	1	0	1	0	0	0	6050	.
<b>28</b>	09JAN04	1	0	1	0	0	0	6350	.
<b>29</b>	12JAN04	1	0	1	0	0	0	6650	.
<b>30</b>	13JAN04	1	0	1	0	0	0	6950	.
<b>31</b>	14JAN04	0	1	2	-1	1	-1	7250	.
<b>32</b>	15JAN04	0	1	2	-1	1	-1	8150	.
<b>33</b>	16JAN04	0	1	2	-1	1	-1	9050	.
<b>34</b>	19JAN04	0	1	2	-1	1	-1	9950	.
<b>35</b>	20JAN04	0	1	2	-1	1	-1	10850	.
<b>36</b>	21JAN04	0	1	1	0	1	-1	11750	.
<b>37</b>	22JAN04	0	1	1	0	1	-1	12700	.
<b>38</b>	23JAN04	0	1	1	0	1	-1	13650	.
<b>39</b>	26JAN04	0	1	1	0	1	-1	14600	.
<b>40</b>	27JAN04	0	1	1	0	1	-1	15550	.
<b>41</b>	28JAN04	0	1	0	1	1	-1	16500	.
<b>42</b>	29JAN04	0	1	0	1	1	-1	16900	.
<b>43</b>	30JAN04	0	1	0	1	1	-1	17300	.
<b>44</b>	02FEB04	0	1	0	1	1	-1	17700	.
<b>45</b>	03FEB04	0	1	0	1	1	-1	18100	.
<b>46</b>	04FEB04	0	1	0	1	0	0	18500	.

**Output 4.18.3** *continued***Variable Activity Delay  
Usage Profile**

<b>Obs</b>	<b>_TIME_</b>	<b>Rdeseng</b>	<b>Adeseng</b>	<b>Rprodeng</b>	<b>Aprodeng</b>	<b>Rmktn</b>	<b>Amktan</b>	<b>Rmoney</b>	<b>Amoney</b>
<b>47</b>	05FEB04	0	1	0	1	0	0	18750	.
<b>48</b>	06FEB04	0	1	0	1	0	0	19000	.
<b>49</b>	09FEB04	0	1	0	1	0	0	19250	.
<b>50</b>	10FEB04	0	1	0	1	0	0	19500	.
<b>51</b>	11FEB04	1	0	0	1	1	-1	19750	.
<b>52</b>	12FEB04	1	0	0	1	1	-1	20100	.
<b>53</b>	13FEB04	1	0	0	1	1	-1	20450	.
<b>54</b>	16FEB04	1	0	0	1	1	-1	20800	.
<b>55</b>	17FEB04	1	0	0	1	1	-1	21150	.
<b>56</b>	18FEB04	1	0	0	1	1	-1	21500	.
<b>57</b>	19FEB04	1	0	0	1	1	-1	21850	.
<b>58</b>	20FEB04	1	0	0	1	1	-1	22200	.
<b>59</b>	23FEB04	1	0	0	1	1	-1	22550	.
<b>60</b>	24FEB04	1	0	0	1	1	-1	22900	.
<b>61</b>	25FEB04	0	1	0	1	1	-1	23250	.
<b>62</b>	26FEB04	0	1	0	1	1	-1	23450	.
<b>63</b>	27FEB04	0	1	0	1	1	-1	23650	.
<b>64</b>	01MAR04	0	1	0	1	1	-1	23850	.
<b>65</b>	02MAR04	0	1	0	1	1	-1	24050	.
<b>66</b>	03MAR04	1	0	1	0	0	0	24250	.
<b>67</b>	04MAR04	1	0	1	0	0	0	24450	.
<b>68</b>	05MAR04	1	0	1	0	0	0	24650	.
<b>69</b>	08MAR04	1	0	1	0	0	0	24850	.
<b>70</b>	09MAR04	1	0	1	0	0	0	25050	.
<b>71</b>	10MAR04	0	1	0	1	0	0	25250	.

Note from the Schedule data set that the activity ‘Study Market’ is scheduled to start on January 14, 2004, even though  $(L\_START + adelay)=21JAN04$ . This is due to the fact that at every time interval, the scheduling algorithm looks ahead in time to detect any increase in the primary level of the resource; if the future resource profile indicates that the procedure will need to use supplementary levels anyway, the activity will not be forced to wait until  $(L\_START + DELAY)$ . (To force the activity to wait until its latest allowed start time, use the AWAITDELAY option). The DELAYANALYSIS variables indicate that a supplementary level of the resource prodeng is needed to schedule the activity on 14JAN03. The variable SUPPL\_R identifies only one supplementary resource that is needed for the activity. In fact, examination of the resource requirements for the activity and the RESOURCEOUT data set shows that an extra market analyst is also needed between the 14th and 20th of January to schedule this activity. Likewise, the activities ‘Write Specs’ and ‘Drawings’ require a design engineer and a production engineer; both these activities start on the 8th of December. The RESOURCEOUT data set indicates that an extra design engineer and an extra production engineer are needed from the 8th to the 12th of December.

The next invocation of PROC CPM illustrates the use of the ACTDELAY variable to force the resource-constrained schedule to coincide with the early start schedule. The following DATA step uses the Schedule data set WIDGO18 to set an activity delay variable (actdel) to be equal to  $-T\_FLOAT$ . PROC CPM is then invoked with the ACTDELAY variable equal to actdel and the INFEASDIAGNOSTIC option. This forces all activities to be scheduled on or before ( $L\_START + actdel$ ), which happens to be equal to  $E\_START$ ; thus all activities are scheduled to start at their early start time. The resulting Schedule data set is displayed in [Output 4.18.4](#). Though this is an extreme case, a similar technique could be used selectively to set the delay value for each activity (or some of the activities) to depend on the unconstrained schedule or the  $T\_FLOAT$  value. If both the  $DELAY=$  and  $ACTDELAY=$  options are specified, the  $DELAY=$  value is used to set the activity delay values for activities that have missing values for the ACTDELAY variable.

Note also that in this invocation of PROC CPM, the BASELINE statement is used to compare the early start schedule and the resource constrained schedule. The S\_VAR and F\_VAR variables are 0 for all the activities, as is to be expected (since all activities are forced to start as per the early start schedule).

```

data negdelay;
  set widgo18;
  actdel=-t_float;
  run;

proc cpm date='01dec03'd
  interval=weekday
  data=negdelay
  holodata=holodata
  resin=resin17
  out=widgo18n;
tailnode tail;
duration days;
headnode head;
holiday hol;
resource deseng prodeng mktan money / period=per
  obstype=otype
  delayanalysis
  actdelay=actdel
  infeasdiagnostic;
baseline / set=early compare=resource;
id task;
run;

```

**Output 4.18.4** Resource-Constrained Schedule: Activity Delay = - (T\_FLOAT)

**Variable Activity Delay**  
**Resource Constrained Schedule**  
**Activity Delay = - (T\_FLOAT)**

				p	S	S	E
				a d r	-	F	-
	t h d	t		c e o m m	S	I	S
O	a e a	a		t s d k o	T	N	T
b	i a y	s		d e e t n	A	I	A
s	l d s	k		e n n a e	R	S	R
				l g g n y	T	H	T
<b>1</b>	1 2 5	Approve Plan	0 1 1 1	200	01DEC03	05DEC03	01DEC03
<b>2</b>	2 3 10	Drawings	0 1 1 .	100	08DEC03	19DEC03	08DEC03
<b>3</b>	2 4 5	Study Market	-30 . 1	100	08DEC03	12DEC03	08DEC03
<b>4</b>	2 3 5	Write Specs	-5 1 1 .	150	08DEC03	12DEC03	08DEC03
<b>5</b>	3 5 15	Prototype	0 1 1 .	300	22DEC03	13JAN04	22DEC03
<b>6</b>	4 6 10	Mkt. Strat.	-30 . . 1	150	15DEC03	29DEC03	15DEC03
<b>7</b>	5 7 10	Materials	0 . . .	300	14JAN04	27JAN04	14JAN04
<b>8</b>	5 7 10	Facility	0 . 1 .	500	14JAN04	27JAN04	14JAN04
<b>9</b>	7 8 10	Init. Prod.	0 . . .	250	28JAN04	10FEB04	28JAN04
<b>10</b>	8 9 10	Evaluate	-5 1 . .	150	11FEB04	24FEB04	11FEB04
<b>11</b>	6 9 15	Test Market	0 . . 1	200	11FEB04	02MAR04	11FEB04
<b>12</b>	9 10 5	Changes	0 1 1 .	200	03MAR04	09MAR04	03MAR04
<b>13</b>	10 11 0	Production	0 1 1 .	600	10MAR04	10MAR04	10MAR04
<b>14</b>	6 12 0	Marketing	-20 . . 1 .	11FEB04	11FEB04	11FEB04	
<b>15</b>	8 6 0	Dummy	0 . . .	11FEB04	11FEB04	11FEB04	

	E	L	L	R D	S	B	B
	-	F	-	E	U	-	-
	I	S	I	D L	P	S	I S F
O	I	A	I	L Y	L	A	I V V
b	S	R	S	A -	-	R	S A A
s	H	T	H	Y R	R	T	H R R
<b>1</b>	05DEC03	01DEC03	05DEC03	0	mktan	01DEC03	05DEC03 0 0
<b>2</b>	19DEC03	08DEC03	19DEC03	0		08DEC03	19DEC03 0 0
<b>3</b>	12DEC03	21JAN04	27JAN04	0	prodeng	08DEC03	12DEC03 0 0
<b>4</b>	12DEC03	15DEC03	19DEC03	0	deseng	08DEC03	12DEC03 0 0
<b>5</b>	13JAN04	22DEC03	13JAN04	0		22DEC03	13JAN04 0 0
<b>6</b>	29DEC03	28JAN04	10FEB04	0	mktan	15DEC03	29DEC03 0 0
<b>7</b>	27JAN04	14JAN04	27JAN04	0		14JAN04	27JAN04 0 0
<b>8</b>	27JAN04	14JAN04	27JAN04	0		14JAN04	27JAN04 0 0
<b>9</b>	10FEB04	28JAN04	10FEB04	0		28JAN04	10FEB04 0 0
<b>10</b>	24FEB04	18FEB04	02MAR04	0		11FEB04	24FEB04 0 0
<b>11</b>	02MAR04	11FEB04	02MAR04	0	mktan	11FEB04	02MAR04 0 0
<b>12</b>	09MAR04	03MAR04	09MAR04	0		03MAR04	09MAR04 0 0
<b>13</b>	10MAR04	10MAR04	10MAR04	0		10MAR04	10MAR04 0 0
<b>14</b>	11FEB04	10MAR04	10MAR04	0		11FEB04	11FEB04 0 0
<b>15</b>	11FEB04	11FEB04	11FEB04	0		11FEB04	11FEB04 0 0

---

## Example 4.19: Activity Splitting

This example illustrates the use of activity splitting to help reduce project duration. By default, PROC CPM assumes that an activity cannot be interrupted once it is started (except for holidays and weekends). During resource-constrained scheduling, it is possible for a noncritical activity to be scheduled first, and at a later time a critical activity may be held waiting for a resource to be freed by this less critical activity. In such situations, you may want to allow noncritical activities to be preempted by critical ones. PROC CPM enables you to specify, selectively, the activities that can be split into segments, the minimum length of each segment, and the maximum number of segments per activity.

The data set WIDGR19, displayed in [Output 4.19.1](#), contains the widget network in AON format with two resources: prodman and hrdware. Suppose the production manager is required to oversee certain activities, as indicated by a ‘1’ in the prodman column. hrdware denotes some piece of equipment that is required by the activity ‘Drawings’ (perhaps a plotter to produce the engineering drawings). The variable minseg denotes the minimum length of the split segments for each activity. Missing values for this variable are set to default values (one-fifth of the activity’s duration). The Resource data set WIDGRIN, displayed in [Output 4.19.2](#), indicates that both resources are replenishable, there is one production manager available from December 1, and the hardware is unavailable on the 10th and 11th of December (perhaps it is scheduled for maintenance or has been reserved for some other project).

**Output 4.19.1** Activity Splitting: Activity Data Set

### Activity Splitting Project Data

Obs	task	days	succ	prodman	hrdware	minseg
1	Approve Plan	5	Drawings	1	.	.
2	Approve Plan	5	Study Market	1	.	.
3	Approve Plan	5	Write Specs	1	.	.
4	Drawings	10	Prototype	.	1	1
5	Study Market	5	Mkt. Strat.	.	.	.
6	Write Specs	5	Prototype	.	.	.
7	Prototype	15	Materials	1	.	.
8	Prototype	15	Facility	1	.	.
9	Mkt. Strat.	10	Test Market	1	.	1
10	Mkt. Strat.	10	Marketing	1	.	1
11	Materials	10	Init. Prod.	.	.	.
12	Facility	10	Init. Prod.	.	.	.
13	Init. Prod.	10	Test Market	1	.	.
14	Init. Prod.	10	Marketing	1	.	.
15	Init. Prod.	10	Evaluate	1	.	.
16	Evaluate	10	Changes	1	.	.
17	Test Market	15	Changes	.	.	.
18	Changes	5	Production	.	.	.
19	Production	0		1	.	.
20	Marketing	0		.	.	.

**Output 4.19.2** Activity Splitting: Resource Availability Data Set

**Activity Splitting  
Resource Availability Data Set**

Obs	per	otype	prodman	hardware
1	.	restype	1	1
2	01DEC03	reslevel	1	1
3	10DEC03	reslevel	.	0
4	12DEC03	reslevel	.	1

The project is first scheduled without allowing any of the activities to be split. The Schedule data set SCHED, displayed in [Output 4.19.3](#), indicates that the project has been delayed by one week (five working days, since maximum S\_FINISH = ‘17MAR04’ while maximum E\_FINISH = ‘10MAR04’). The activity ‘Drawings’ has been postponed to start after the equipment has been serviced (or used by the other project), and the activity ‘Prototype’ (which is actually a critical activity) cannot start on schedule because the production manager is tied up with the noncritical activity ‘Mkt. Strat.’.

```

proc cpm date='01dec03'd
  data=widgr19 resin=widgrin
  holidata=holodata
  out=sched resout=rout
  interval=weekday collapse;
activity task;
duration days;
successor succ;
holiday hol;
resource prodman hardware / period=per obstype=otype
  t_float f_float rcs avl;
run;

```

**Output 4.19.3 Project Schedule: Splitting Not Allowed**

**Activity Splitting**  
**Project Schedule: Splitting not Allowed**

Obs	task	succ	days	prodman	hrdware	S_START	S_FINISH	E_START	E_FINISH
1	Approve Plan	Drawings	5	1	.	01DEC03	05DEC03	01DEC03	05DEC03
2	Drawings	Prototype	10	.	1	12DEC03	26DEC03	08DEC03	19DEC03
3	Study Market	Mkt. Strat.	5	.	.	08DEC03	12DEC03	08DEC03	12DEC03
4	Write Specs	Prototype	5	.	.	08DEC03	12DEC03	08DEC03	12DEC03
5	Prototype	Materials	15	1	.	30DEC03	20JAN04	22DEC03	13JAN04
6	Mkt. Strat.	Test Market	10	1	.	15DEC03	29DEC03	15DEC03	29DEC03
7	Materials	Init. Prod.	10	.	.	21JAN04	03FEB04	14JAN04	27JAN04
8	Facility	Init. Prod.	10	.	.	21JAN04	03FEB04	14JAN04	27JAN04
9	Init. Prod.	Test Market	10	1	.	04FEB04	17FEB04	28JAN04	10FEB04
10	Evaluate	Changes	10	1	.	18FEB04	02MAR04	11FEB04	24FEB04
11	Test Market	Changes	15	.	.	18FEB04	09MAR04	11FEB04	02MAR04
12	Changes	Production	5	.	.	10MAR04	16MAR04	03MAR04	09MAR04
13	Production		0	1	.	17MAR04	17MAR04	10MAR04	10MAR04
14	Marketing		0	.	.	18FEB04	18FEB04	11FEB04	11FEB04

Obs	L_START	L_FINISH	T_FLOAT	F_FLOAT
1	01DEC03	05DEC03	0	0
2	08DEC03	19DEC03	0	0
3	21JAN04	27JAN04	30	0
4	15DEC03	19DEC03	5	5
5	22DEC03	13JAN04	0	0
6	28JAN04	10FEB04	30	30
7	14JAN04	27JAN04	0	0
8	14JAN04	27JAN04	0	0
9	28JAN04	10FEB04	0	0
10	18FEB04	02MAR04	5	5
11	11FEB04	02MAR04	0	0
12	03MAR04	09MAR04	0	0
13	10MAR04	10MAR04	0	0
14	10MAR04	10MAR04	20	20

In the second invocation of PROC CPM, the MINSEGMDUR= option is used in the RESOURCE statement to identify the variable minseg to the procedure. This enables the algorithm to split the ‘Drawings’ activity so that some of it is done before December 10, 2003, and the rest is scheduled to start on December 12, 2003. Likewise, the production manager is allocated to the activity ‘Mkt. Strat.’ on December 15, 2003. On the 24th of December the activity ‘Prototype’ demands the production manager, and since preemption is allowed, the earlier activity ‘Mkt. Strat.’, which is less critical than ‘Prototype’, is temporarily halted and is resumed on the 16th of January after the completion of ‘Prototype’ on the 15th of January. The Schedule data set, displayed in Output 4.19.4, contains separate observations for each segment of the split activities as indicated by the variable SEGMT\_NO. The project duration has been reduced by three working days, by allowing appropriate activities to be split.

```

proc cpm date='01dec03'd
  data=widgr19
  holidata=holodata resin=widgrin
  out=spltschd resout=spltrout
  interval=weekday collapse;
activity task;
duration days;
successor succ;
holiday hol;
resource prodman hardware / period=per obstype=otype
  minsegmdur=minseg
  rcs avl;
id task;
run;

```

**Output 4.19.4** Project Schedule: Splitting Allowed

**Activity Splitting**  
**Project Schedule: Splitting Allowed**

Obs	task	succ	SEGMT_NO	days	prodman	hrdware
1	Approve Plan	Drawings	.	5	1	.
2	Drawings	Prototype	.	10	.	1
3	Drawings	Prototype	1	2	.	1
4	Drawings	Prototype	2	8	.	1
5	Study Market	Mkt. Strat.	.	5	.	.
6	Write Specs	Prototype	.	5	.	.
7	Prototype	Materials	.	15	1	.
8	Mkt. Strat.	Test Market	.	10	1	.
9	Mkt. Strat.	Test Market	1	7	1	.
10	Mkt. Strat.	Test Market	2	3	1	.
11	Materials	Init. Prod.	.	10	.	.
12	Facility	Init. Prod.	.	10	.	.
13	Init. Prod.	Test Market	.	10	1	.
14	Evaluate	Changes	.	10	1	.
15	Test Market	Changes	.	15	.	.
16	Changes	Production	.	5	.	.
17	Production		.	0	1	.
18	Marketing		.	0	.	.
Obs	S_START	S_FINISH	E_START	E_FINISH	L_START	L_FINISH
1	01DEC03	05DEC03	01DEC03	05DEC03	01DEC03	05DEC03
2	08DEC03	23DEC03	08DEC03	19DEC03	08DEC03	19DEC03
3	08DEC03	09DEC03	08DEC03	19DEC03	08DEC03	19DEC03
4	12DEC03	23DEC03	08DEC03	19DEC03	08DEC03	19DEC03
5	08DEC03	12DEC03	08DEC03	12DEC03	21JAN04	27JAN04
6	08DEC03	12DEC03	08DEC03	12DEC03	15DEC03	19DEC03
7	24DEC03	15JAN04	22DEC03	13JAN04	22DEC03	13JAN04
8	15DEC03	20JAN04	15DEC03	29DEC03	28JAN04	10FEB04
9	15DEC03	23DEC03	15DEC03	29DEC03	28JAN04	10FEB04
10	16JAN04	20JAN04	15DEC03	29DEC03	28JAN04	10FEB04
11	16JAN04	29JAN04	14JAN04	27JAN04	14JAN04	27JAN04
12	16JAN04	29JAN04	14JAN04	27JAN04	14JAN04	27JAN04
13	30JAN04	12FEB04	28JAN04	10FEB04	28JAN04	10FEB04
14	13FEB04	26FEB04	11FEB04	24FEB04	18FEB04	02MAR04
15	13FEB04	04MAR04	11FEB04	02MAR04	11FEB04	02MAR04
16	05MAR04	11MAR04	03MAR04	09MAR04	03MAR04	09MAR04
17	12MAR04	12MAR04	10MAR04	10MAR04	10MAR04	10MAR04
18	13FEB04	13FEB04	11FEB04	11FEB04	10MAR04	10MAR04

---

## Example 4.20: Alternate Resources

Some projects may have two or more resource types that are interchangeable; if one resource is insufficient, the other one can be used in its place. To illustrate the use of alternate resources, consider the widget manufacturing example with the data in AON format as shown in [Output 4.20.1](#). As in [Example 4.17](#), suppose there are two types of engineers, a design engineer and a production engineer. In addition, there is a generic pool of engineers, denoted by the variable engpool. The resource requirements for each category are specified in the data set WIDGR20.

### **Output 4.20.1** Alternate Resources: Activity Data Set

#### **Scheduling with Alternate Resources Data Set WIDGR20**

Obs	task	days	succ	deseng	prodeng	engpool
1	Approve Plan	5	Drawings	1	1	.
2	Approve Plan	5	Study Market	1	1	.
3	Approve Plan	5	Write Specs	1	1	.
4	Drawings	10	Prototype	1	1	.
5	Study Market	5	Mkt. Strat.	.	1	.
6	Write Specs	5	Prototype	1	1	.
7	Prototype	15	Materials	1	1	1
8	Prototype	15	Facility	1	1	1
9	Mkt. Strat.	10	Test Market	.	.	.
10	Mkt. Strat.	10	Marketing	.	.	.
11	Materials	10	Init. Prod.	.	.	.
12	Facility	10	Init. Prod.	.	1	2
13	Init. Prod.	10	Test Market	.	.	2
14	Init. Prod.	10	Marketing	.	.	2
15	Init. Prod.	10	Evaluate	.	.	2
16	Evaluate	10	Changes	1	.	.
17	Test Market	15	Changes	.	.	.
18	Changes	5	Production	1	1	.
19	Production	0		.	.	.
20	Marketing	0		.	.	.

### **Output 4.20.2** Alternate Resources: RESOURCEIN Data Set

#### **Scheduling with Alternate Resources Data Set RESIN20**

Obs	per	otype	resid	deseng	prodeng	engpool
1	.	restype		1	1	1
2	.	altptry	deseng	.	1	2
3	.	altptry	prodeng	.	.	1
4	.	suplevel		1	1	.
5	01DEC03	reslevel		1	1	4

The resource availability data set RESIN20, displayed in [Output 4.20.2](#), identifies all three resources as replenishable resources and indicates a primary as well as a supplementary level of availability. A new variable resid in the data set is used to identify resources in observations 2 and 3 that can be substituted for deseng and prodeng, respectively. These observations have the value ‘altptry’ for the OBSTYPE variable and indicate a priority for the substitution. For example, observation number 2 indicates that if deseng is unavailable, the procedure can use prodeng, and if even that is insufficient, it can draw from the engineering resource pool engpool. To trigger the substitution of resources, use the RESID= option in the RESOURCE statement.

### **Output 4.20.3 Alternate Resources Not Used**

#### **Scheduling with Alternate Resources Alternate Resources not used**

Obs	task	succ	days	deseng	prodeng	engpool	S_START	S_FINISH
1	Approve Plan	Drawings	5	1	1	.	01DEC03	05DEC03
2	Drawings	Prototype	10	1	1	.	08DEC03	19DEC03
3	Study Market	Mkt. Strat.	5	.	1	.	04FEB04	10FEB04
4	Write Specs	Prototype	5	1	1	.	22DEC03	29DEC03
5	Prototype	Materials	15	1	1	1	30DEC03	20JAN04
6	Mkt. Strat.	Test Market	10	.	.	.	11FEB04	24FEB04
7	Materials	Init. Prod.	10	.	.	.	21JAN04	03FEB04
8	Facility	Init. Prod.	10	.	1	2	21JAN04	03FEB04
9	Init. Prod.	Test Market	10	.	.	2	04FEB04	17FEB04
10	Evaluate	Changes	10	1	.	.	18FEB04	02MAR04
11	Test Market	Changes	15	.	.	.	25FEB04	16MAR04
12	Changes	Production	5	1	1	.	17MAR04	23MAR04
13	Production		0	.	.	.	24MAR04	24MAR04
14	Marketing		0	.	.	.	25FEB04	25FEB04

Obs	E_START	E_FINISH	L_START	L_FINISH	R_DELAY	DELAY_R	SUPPL_R
1	01DEC03	05DEC03	01DEC03	05DEC03	0		
2	08DEC03	19DEC03	08DEC03	19DEC03	0		
3	08DEC03	12DEC03	21JAN04	27JAN04	40	prodeng	
4	08DEC03	12DEC03	15DEC03	19DEC03	10	deseng	
5	22DEC03	13JAN04	22DEC03	13JAN04	0		
6	15DEC03	29DEC03	28JAN04	10FEB04	0		
7	14JAN04	27JAN04	14JAN04	27JAN04	0		
8	14JAN04	27JAN04	14JAN04	27JAN04	0		
9	28JAN04	10FEB04	28JAN04	10FEB04	0		
10	11FEB04	24FEB04	18FEB04	02MAR04	0		
11	11FEB04	02MAR04	11FEB04	02MAR04	0		
12	03MAR04	09MAR04	03MAR04	09MAR04	0		
13	10MAR04	10MAR04	10MAR04	10MAR04	0		
14	11FEB04	11FEB04	10MAR04	10MAR04	0		

First, PROC CPM is invoked without reference to the RESID variable. The procedure ignores observations 2 and 3 in the RESOURCEIN data set (a message is written to the log), and the project is scheduled using the available resources; the supplementary level is not used because the project can be scheduled using only the primary resources by delaying it a few days. The project completion time is March 24, 2004 (see the schedule displayed in Output 4.20.3). The following program shows the invocation of PROC CPM.

```
proc cpm date='01dec03'd
    interval=weekday collapse
    data=widgr20 resin=resin20 holdata=holdata
    out=widgo20 resout=widgro20;
activity task;
duration days;
successor succ;
holiday hol;
resource deseng prodeng engpool / period=per
    obstype=otype
    delayanalysis
    rcs avl;
run;
```

Next, PROC CPM is invoked with the RESID= option, and the resulting Schedule data set is displayed in Output 4.20.4. The new schedule shows that the project completion time (10MAR04) has been reduced by two weeks as a result of using alternate resources.

**Output 4.20.4** Alternate Resources Used

**Scheduling with Alternate Resources**  
**Alternate Resources Reduce Project Completion Time**

Obs	task	succ	days	deseng	prodeng	engpool	Udeseng	Uprodeng	Uengpool	S_START
1	Approve Plan Drawings		5	1	1	.	1	1	.	01DEC03
2	Drawings	Prototype	10	1	1	.	1	1	.	08DEC03
3	Study Market	Mkt. Strat.	5	.	1	.	.	.	1	08DEC03
4	Write Specs	Prototype	5	1	1	.	.	.	2	08DEC03
5	Prototype	Materials	15	1	1	1	1	1	1	22DEC03
6	Mkt. Strat.	Test Market	10	.	.	.	.	.	.	15DEC03
7	Materials	Init. Prod.	10	.	.	.	.	.	.	14JAN04
8	Facility	Init. Prod.	10	.	1	2	.	1	2	14JAN04
9	Init. Prod.	Test Market	10	.	.	2	.	.	2	28JAN04
10	Evaluate	Changes	10	1	.	.	1	.	.	11FEB04
11	Test Market	Changes	15	.	.	.	.	.	.	11FEB04
12	Changes	Production	5	1	1	.	1	1	.	03MAR04
13	Production		0	.	.	.	.	.	.	10MAR04
14	Marketing		0	.	.	.	.	.	.	11FEB04

Obs	S_FINISH	E_START	E_FINISH	L_START	L_FINISH	R_DELAY	DELAY_R	SUPPL_R
1	05DEC03	01DEC03	05DEC03	01DEC03	05DEC03	0		
2	19DEC03	08DEC03	19DEC03	08DEC03	19DEC03	0		
3	12DEC03	08DEC03	12DEC03	21JAN04	27JAN04	0		
4	12DEC03	08DEC03	12DEC03	15DEC03	19DEC03	0		
5	13JAN04	22DEC03	13JAN04	22DEC03	13JAN04	0		
6	29DEC03	15DEC03	29DEC03	28JAN04	10FEB04	0		
7	27JAN04	14JAN04	27JAN04	14JAN04	27JAN04	0		
8	27JAN04	14JAN04	27JAN04	14JAN04	27JAN04	0		
9	10FEB04	28JAN04	10FEB04	28JAN04	10FEB04	0		
10	24FEB04	11FEB04	24FEB04	18FEB04	02MAR04	0		
11	02MAR04	11FEB04	02MAR04	11FEB04	02MAR04	0		
12	09MAR04	03MAR04	09MAR04	03MAR04	09MAR04	0		
13	10MAR04	10MAR04	10MAR04	10MAR04	10MAR04	0		
14	11FEB04	11FEB04	11FEB04	10MAR04	10MAR04	0		

When resource substitution is allowed, the procedure adds a new variable prefixed by a ‘U’ for each resource variable; this new variable specifies the actual resources *used* for each activity (as opposed to the resource *required*). The activity ‘Study Market’ requires one production engineer who is tied up with the activity ‘Drawings’ on the 8th of December. Since resource substitution is allowed, the procedure uses an engineer from engpool as indicated by a missing value for Uprodeng and a ‘1’ for Uengpool in the third observation. Likewise, the activity ‘Write Specs’ is scheduled by substituting one engineer from engpool for a design engineer and one for a production engineer to obtain Udeseng=‘.’, Uprodeng=‘.’, and Uengpool=2 in observation number 4. It is evident from the project finish date (S\_FINISH=L\_FINISH=‘10MAR04’) that resource substitution has enabled the project to be completed without any delay. In fact, the DELAYANALYSIS variables indicate that there is no delay in any of the activities (R\_DELAY=0 and DELAY\_R=‘ ’ for all activities). Note also that supplementary levels are not used (SUPPL\_R=‘ ’) for any of the resources (recall that use of supplementary levels is triggered by the specification of a finite value for DELAY).

The following program produced [Output 4.20.4](#):

```
proc cpm date='01dec03'd
    interval=weekday collapse
    data=widgr20 resin=resin20 holdata=holdata
    out=widgalt resout=widralt;
activity task;
duration days;
successor succ;
holiday hol;
resource deseng prodeng engpool / period=per
    obstype=otype
    delayanalysis
    resid=resid
    rcs avl;
run;
```

The next two invocations of PROC CPM illustrate the use of both supplementary as well as alternate resources. Note from the output data set, displayed in [Output 4.20.5](#), that once again the project is completed without any delay. Note also that the activity ‘Write Specs’ has used a supplementary resource whereas ‘Study Market’ has used an alternate resource. By default, when the DELAY= option is used, it forces the procedure to use supplementary resources before alternate resources. To invert this order so that alternate resources are used before supplementary resources, use the ALTBEFORESUP option in the RESOURCE statement, as illustrated in the second invocation of CPM in the following code. The resulting schedule is displayed in [Output 4.20.6](#); this schedule is, in fact, the same as the schedule displayed in [Output 4.20.4](#), obtained without the DELAY=0 and the ALTBEFORESUP options.

```
/* Invoke CPM with the DELAY=0 option */
proc cpm date='01dec03'd
    interval=weekday collapse
    data=widgr20 resin=resin20 holidata=holdata
    out=widgdsup resout=widrdsup;
activity task;
duration days;
successor succ;
holiday hol;
resource deseng prodeng engpool / period=per
    obstype=otype
    delayanalysis
    delay=0
    resid=resid
    rcs avl;
run;

/* Invoke CPM with the DELAY=0 and ALTBEBORESUP options */
proc cpm date='01dec03'd
    interval=weekday collapse
    data=widgr20 resin=resin20 holidata=holdata
    out=widgdsup resout=widrdsup;
activity task;
duration days;
successor succ;
holiday hol;
resource deseng prodeng engpool / period=per
    obstype=otype
    delayanalysis
    delay=0
    resid=resid altbeforesup
    rcs avl;
run;
```

**Output 4.20.5 Supplementary Resources Used Before Alternate Resources****Scheduling with Alternate Resources  
DELAY=0, Supplementary Resources Used instead of Alternate**

Obs	task	succ	days	deseng	prodeng	engpool	Udeseng	Uprodeng	Uengpool	S_START
1	Approve Plan Drawings		5	1	1	.	1	1	.	01DEC03
2	Drawings	Prototype	10	1	1	.	1	1	.	08DEC03
3	Study Market	Mkt. Strat.	5	.	1	.	.	.	1	08DEC03
4	Write Specs	Prototype	5	1	1	.	.	.	2	08DEC03
5	Prototype	Materials	15	1	1	1	1	1	1	22DEC03
6	Mkt. Strat.	Test Market	10	.	.	.	.	.	.	15DEC03
7	Materials	Init. Prod.	10	.	.	.	.	.	.	14JAN04
8	Facility	Init. Prod.	10	.	1	2	.	1	2	14JAN04
9	Init. Prod.	Test Market	10	.	.	2	.	.	2	28JAN04
10	Evaluate	Changes	10	1	.	.	1	.	.	11FEB04
11	Test Market	Changes	15	.	.	.	.	.	.	11FEB04
12	Changes	Production	5	1	1	.	1	1	.	03MAR04
13	Production		0	.	.	.	.	.	.	10MAR04
14	Marketing		0	.	.	.	.	.	.	11FEB04

Obs	S_FINISH	E_START	E_FINISH	L_START	L_FINISH	R_DELAY	DELAY_R	SUPPL_R
1	05DEC03	01DEC03	05DEC03	01DEC03	05DEC03	0		
2	19DEC03	08DEC03	19DEC03	08DEC03	19DEC03	0		
3	12DEC03	08DEC03	12DEC03	21JAN04	27JAN04	0		
4	12DEC03	08DEC03	12DEC03	15DEC03	19DEC03	0		
5	13JAN04	22DEC03	13JAN04	22DEC03	13JAN04	0		
6	29DEC03	15DEC03	29DEC03	28JAN04	10FEB04	0		
7	27JAN04	14JAN04	27JAN04	14JAN04	27JAN04	0		
8	27JAN04	14JAN04	27JAN04	14JAN04	27JAN04	0		
9	10FEB04	28JAN04	10FEB04	28JAN04	10FEB04	0		
10	24FEB04	11FEB04	24FEB04	18FEB04	02MAR04	0		
11	02MAR04	11FEB04	02MAR04	11FEB04	02MAR04	0		
12	09MAR04	03MAR04	09MAR04	03MAR04	09MAR04	0		
13	10MAR04	10MAR04	10MAR04	10MAR04	10MAR04	0		
14	11FEB04	11FEB04	11FEB04	10MAR04	10MAR04	0		

**Output 4.20.6** Alternate Resources Used Before Supplementary Resources

**Scheduling with Alternate Resources**  
**DELAY=0, Alternate Resources Used instead of Supplementary**

Obs	task	succ	days	deseng	prodeng	engpool	Udeseng	Uprodeng	Uengpool	S_START
1	Approve Plan	Drawings	5	1	1	.	1	1	.	01DEC03
2	Drawings	Prototype	10	1	1	.	1	1	.	08DEC03
3	Study Market	Mkt. Strat.	5	.	1	.	.	.	1	08DEC03
4	Write Specs	Prototype	5	1	1	.	.	.	2	08DEC03
5	Prototype	Materials	15	1	1	1	1	1	1	22DEC03
6	Mkt. Strat.	Test Market	10	.	.	.	.	.	.	15DEC03
7	Materials	Init. Prod.	10	.	.	.	.	.	.	14JAN04
8	Facility	Init. Prod.	10	.	1	2	.	1	2	14JAN04
9	Init. Prod.	Test Market	10	.	.	2	.	.	2	28JAN04
10	Evaluate	Changes	10	1	.	.	1	.	.	11FEB04
11	Test Market	Changes	15	.	.	.	.	.	.	11FEB04
12	Changes	Production	5	1	1	.	1	1	.	03MAR04
13	Production		0	.	.	.	.	.	.	10MAR04
14	Marketing		0	.	.	.	.	.	.	11FEB04

Obs	S_FINISH	E_START	E_FINISH	L_START	L_FINISH	R_DELAY	DELAY_R	SUPPL_R
1	05DEC03	01DEC03	05DEC03	01DEC03	05DEC03	0		
2	19DEC03	08DEC03	19DEC03	08DEC03	19DEC03	0		
3	12DEC03	08DEC03	12DEC03	21JAN04	27JAN04	0		
4	12DEC03	08DEC03	12DEC03	15DEC03	19DEC03	0		
5	13JAN04	22DEC03	13JAN04	22DEC03	13JAN04	0		
6	29DEC03	15DEC03	29DEC03	28JAN04	10FEB04	0		
7	27JAN04	14JAN04	27JAN04	14JAN04	27JAN04	0		
8	27JAN04	14JAN04	27JAN04	14JAN04	27JAN04	0		
9	10FEB04	28JAN04	10FEB04	28JAN04	10FEB04	0		
10	24FEB04	11FEB04	24FEB04	18FEB04	02MAR04	0		
11	02MAR04	11FEB04	02MAR04	11FEB04	02MAR04	0		
12	09MAR04	03MAR04	09MAR04	03MAR04	09MAR04	0		
13	10MAR04	10MAR04	10MAR04	10MAR04	10MAR04	0		
14	11FEB04	11FEB04	11FEB04	10MAR04	10MAR04	0		

---

## Example 4.21: PERT Assumptions and Calculations

This example illustrates the PERT statistical approach. Throughout this chapter, it has been assumed that the activity duration times are precise values determined uniquely. In practice, however, each activity is subject to a number of chance sources of variation and it is impossible to know, *a priori*, the duration of the activity. The PERT statistical approach is used to include uncertainty about durations in scheduling. For a detailed discussion about various assumptions, techniques, and cautions related to the PERT approach, refer to Moder, Phillips, and Davis (1983) and Elmaghraby (1977). A simple model is used here to illustrate how PROC CPM can incorporate some of these ideas. A more detailed example can be found in *SAS/OR Software: Project Management Examples*.

Consider the widget manufacturing example. To perform PERT analysis, you need to provide three estimates of activity duration: a pessimistic estimate (*tp*), an optimistic estimate (*to*), and a modal estimate (*tm*). These three estimates are used to obtain a weighted average that is assumed to be a reasonable estimate of the activity duration. The time estimates for the activities must be independent for the analysis to be considered valid. Furthermore, the distribution of activity duration times is purely hypothetical, as no statistical sampling is likely to be feasible on projects of a unique nature to be accomplished at some indeterminate time in the future. Often, the time estimates used are based on past experience with similar projects.

To derive the formula for the mean, you must assume some functional form for the unknown distribution. The well-known Beta distribution is commonly used, as it has the desirable properties of being contained inside a finite interval and can be symmetric or skewed, depending on the location of the mode relative to the optimistic and pessimistic estimates. A linear approximation of the exact formula for the mean of the beta distribution weights the three time estimates as follows:

$$(tp + (4*tm) + to) / 6$$

The following program saves the network (AOA format) from [Example 4.2](#) with three estimates of activity durations in a SAS data set. The DATA step also calculates the weighted average duration for each activity. Following the DATA step, PROC CPM is invoked to produce the schedule plotted on a Gantt chart in [Output 4.21.1](#). The E\_FINISH time for the final activity in the project contains the mean project completion time based on the duration estimates that are used.

```


title 'PERT Assumptions and Calculations';
/* Activity-on-Arc representation of the project
   with three duration estimates */
data widgpert;
  format task $12. ;
  input task & tail head tm tp to;
  dur = (tp + 4*tm + to) / 6;
  datalines;
Approve Plan      1    2    5    7    3
Drawings          2    3   10   11    6
Study Market     2    4    5    7    3
Write Specs       2    3    5    7    3
Prototype         3    5   15   12    9
Mkt. Strat.      4    6   10   11    9
Materials         5    7   10   12    8
Facility          5    7   10   11    9
Init. Prod.       7    8   10   12    8
Evaluate          8    9    9   13    8
Test Market       6    9   14   15   13
Changes           9   10    5    6    4
Production        10   11    0    0    0
Marketing         6   12    0    0    0
Dummy              8   6    0    0    0
;
;

proc cpm data=widgpert out=sched
  date='1dec03'd;
  tailnode tail;
  headnode head;
  duration dur;
  id task;
  run;

proc sort;
  by e_start;
  run;

```

Some words of caution are worth mentioning with regard to the traditional PERT approach. The estimate of the mean project duration obtained in this instance always underestimates the true value since the length of a critical path is a convex function of the activity durations. The original PERT model developed by Malcolm et al. (1959) provides a way to estimate the variance of the project duration as well as calculating the probabilities of meeting certain target dates and so forth. Their analysis relies on an implicit assumption that you may ignore all activities that are not on the critical path in the deterministic problem that is derived by setting the activity durations equal to the mean value of their distributions. It then applies the Central Limit Theorem to the duration of this critical path and interprets the result as pertaining to the project duration.

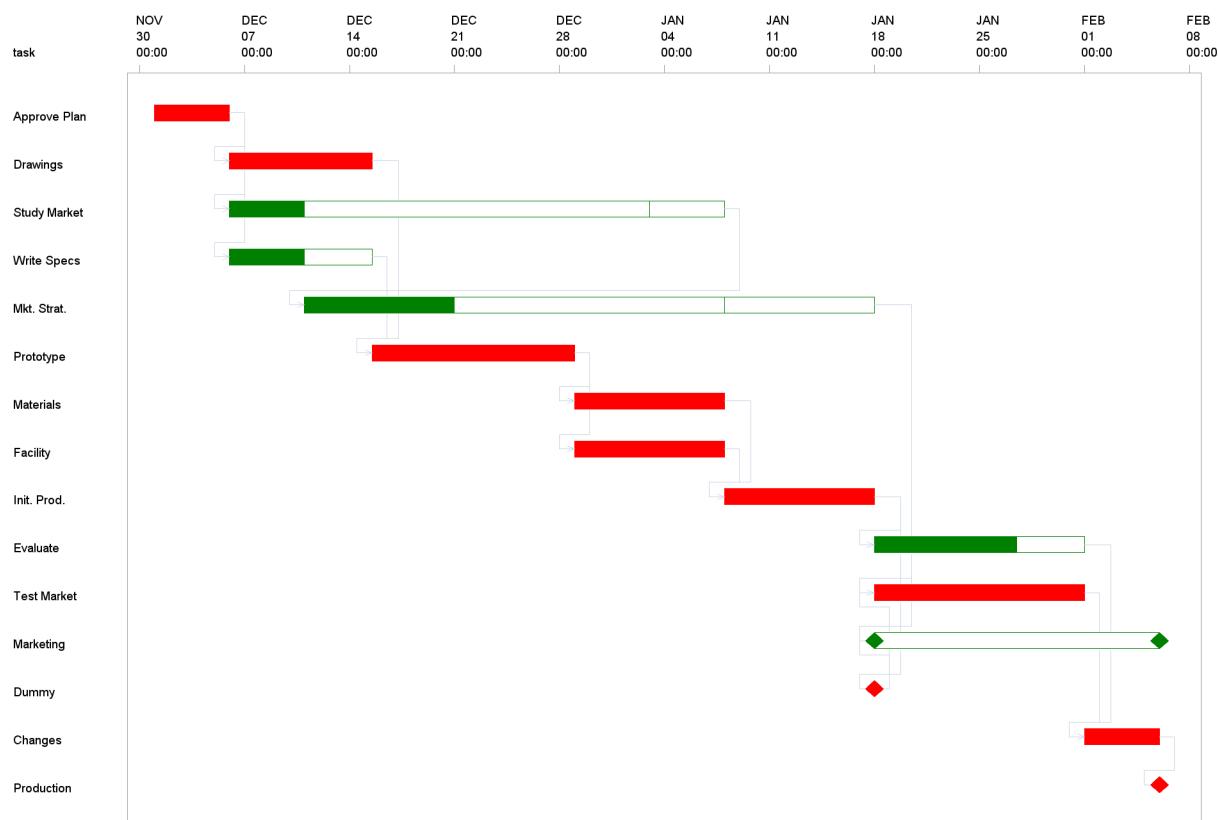**Output 4.21.1 PERT Statistical Estimates: Gantt Chart****PERT Assumptions and Calculations  
Project Schedule**

However, when the activity durations are random variables, each path of the project network is a likely candidate to be the critical path. Every outcome of the activity durations could result in a different longest path. Furthermore, there could be several dependent paths in the network in the sense that they share at least one common arc. Thus, in the most general case, the length of a longest path would be the maximum of a set of, possibly dependent, random variables. Evaluating or approximating the distribution of the longest path, even under very specific distributional assumptions on the activity durations is not a very easy problem. It is not surprising that this topic is the subject of much research.

In view of the inaccuracies that can stem from the original PERT assumptions, many people prefer to resort to the use of Monte Carlo Simulation. Van Slyke (1963) made the first attempt at straightforward simulation to analyze the distribution of the critical path. Refer to Elmaghraby (1977) for a detailed synopsis of the pitfalls of making traditional PERT assumptions and for an introduction to simulation techniques for activity networks.

---

## Example 4.22: Scheduling Course - Teacher Combinations

This example demonstrates the use of PROC CPM for a typical scheduling problem that may not necessarily fit into a conventional project management scenario. Such problems abound in practice and can usually be solved using a mathematical programming model. Here, the problem is modeled as a resource-allocation problem using PROC CPM, illustrating the richness of the modeling environment that is available with the SAS System. (Refer also to Kulkarni (1991) and *SAS/OR Software: Project Management Examples* for another example of course scheduling using PROC CPM.)

A committee for academically gifted children wishes to conduct some special classes on weekends. There are four subjects that are to be taught and a number of teachers available to teach them. Only certain course-teacher combinations are allowed. There is a constraint on the number of rooms that are available and some teachers may not be able to teach at certain times. Possible class times are one-hour periods between 9 a.m. and 12 noon on Saturdays and Sundays. The goal is to determine a feasible schedule of classes specifying the teacher that is to teach each class.

Suppose that there are four courses, c1, c2, c3, and c4, and three teachers, t1, t2, and t3. There are several ways of modeling this problem; one possible way is to form distinct classes for each possible course-teacher combination and treat each of these as a distinct activity that needs to be scheduled. For example, if course c1 can be taught by teachers t1, t2, and t3, define three activities, ‘c1t1’, ‘c1t2’, and ‘c1t3’. The resources for this problem are the courses, the teachers, and the number of rooms. In particular, the resources needed for a particular activity, say, ‘c1t3’, are c1 and t3.

The following constraints are imposed:

- Course 1 can be taught by Teachers 1, 2, and 3; Course 2 can be taught by Teachers 1 and 3; Course 3 can be taught by Teachers 1, 2, and 3; and Course 4 can be taught by Teachers 1 and 2.
- The total number of classes taught at any time cannot exceed NROOMS.
- Class ‘citj’ (if such a course-teacher combination is allowed) can be taught only at times when teacher tj is available.
- At any given time, a teacher can teach only one class.
- At any given time, only one class is to be taught for any given course.

The following program uses PROC CPM to schedule the classes. The schedule is obtained in terms of unformatted numeric values; the times 1, 2, 3, 4, 5, and 6 are interpreted as the six different time slots that are possible, namely, Saturday 9, 10, and 11 a.m. and Sunday 9, 10, and 11 a.m.

The data set CLASSES is the Activity data set, and it indicates the possible course-teacher combinations and identifies the specific room, teacher, and course as the resources required. For each activity, the duration is 1 unit. Note that, in this example, there are no precedence constraints between the activities; the resource availability dictates the schedule entirely. However, there may be situations (such as prerequisite courses) that impose precedence constraints.

The Resource data set, RESOURCE, specifies resource availabilities. The period variable, per, indicates the time period from which resources are available. Since only one class corresponding to a given course is to be taught at a given time, the availability for c1 – c4 is specified as ‘1’. Teacher 2 is available only on Sunday;

thus, specify the availability of t2 to be 1 from time period 4. The total number of rooms available at a given time is three. Thus, no more than three classes can be scheduled at a given time.

In the invocation of PROC CPM, the STOPDATE= option is used in the RESOURCE statement, thus restricting resource constrained scheduling to the first six time periods. Not all of the specified activities may be scheduled within the time available, in which case the unscheduled activities represent course-teacher combinations that are not feasible under the given conditions. The schedule obtained by PROC CPM is saved in a data set that is displayed, in [Output 4.22.1](#), after formatting the activity names and the schedule times appropriately. Note that, in this example, all the course-teacher combinations are scheduled within the two-day time period.

```

title 'Scheduling Course / Teacher Combinations';
data classes;
  input class $  succ $ dur  c1-c4  t1-t3  nrooms;
  datalines;
c1t1  .   1   1   .   .   .   1   .   .   .   1
c1t2  .   1   1   .   .   .   .   .   1   .   .   1
c1t3  .   1   1   .   .   .   .   .   .   1   1
c2t1  .   1   .   1   .   .   .   1   .   .   .   1
c2t3  .   1   .   .   1   .   .   .   .   .   1   1
c3t1  .   1   .   .   .   1   .   1   .   .   .   1
c3t2  .   1   .   .   .   1   .   .   1   .   .   1
c3t3  .   1   .   .   .   1   .   .   .   .   1   1
c4t1  .   1   .   .   .   .   1   1   .   .   .   1
c4t2  .   1   .   .   .   .   1   .   1   .   .   1
  ;
  data resource;
    input per c1-c4  t1-t3  nrooms;
    datalines;
1      1   1   1   1   1   .   1   .   3
4      .   .   .   .   .   .   1   .   .
  ;
proc cpm data=classes out=sched
  resin=resource;
  activity  class;
  duration  dur;
  successor  succ;
  resource  c1-c4 t1-t3 nrooms / period=per stopdate=6;
run;

proc format;
  value classtim
    1 = 'Saturday  9:00-10:00'
    2 = 'Saturday 10:00-11:00'
    3 = 'Saturday 11:00-12:00'
    4 = 'Sunday    9:00-10:00'
    5 = 'Sunday    10:00-11:00'
    6 = 'Sunday    11:00-12:00'
    7 = 'Not Scheduled'
  ;
  value $classt

```

```

c1t1 = 'Class 1, Teacher 1'
c1t2 = 'Class 1, Teacher 2'
c1t3 = 'Class 1, Teacher 3'
c2t1 = 'Class 2, Teacher 1'
c2t2 = 'Class 2, Teacher 2'
c2t3 = 'Class 2, Teacher 3'
c3t1 = 'Class 3, Teacher 1'
c3t2 = 'Class 3, Teacher 2'
c3t3 = 'Class 3, Teacher 3'
c4t1 = 'Class 4, Teacher 1'
c4t2 = 'Class 4, Teacher 2'
c4t3 = 'Class 4, Teacher 3'
;

data schedtim;
set sched;
format classtim classtim.;
format class $classt.;

if (s_start <= 6) then classtim = s_start;
else
      classtim = 7;
run;

title2 'Schedule of Classes';
proc print;
  id class;
  var classtim;
run;

```

#### Output 4.22.1 Class Schedule

### Scheduling Course / Teacher Combinations Schedule of Classes

class	classtim
Class 1, Teacher 1	Saturday 9:00-10:00
Class 1, Teacher 2	Sunday 9:00-10:00
Class 1, Teacher 3	Saturday 10:00-11:00
Class 2, Teacher 1	Saturday 10:00-11:00
Class 2, Teacher 3	Saturday 9:00-10:00
Class 3, Teacher 1	Saturday 11:00-12:00
Class 3, Teacher 2	Sunday 10:00-11:00
Class 3, Teacher 3	Sunday 9:00-10:00
Class 4, Teacher 1	Sunday 9:00-10:00
Class 4, Teacher 2	Sunday 11:00-12:00

There may be several other constraints that you want to impose on the courses scheduled. These can usually be modeled suitably by changing the resource availability profile. For example, suppose that you want to schedule more classes at 10 a.m. and fewer at other times. The following program creates a new Resource data set, RESOURC2, that changes the number of rooms available. Again, PROC CPM is invoked with the STOPDATE= option, and the resulting schedule is displayed in [Output 4.22.2](#). The schedule can also be displayed graphically using the NETDRAW procedure, as illustrated in a similar problem in [Example 9.16](#) in Chapter 9, “The NETDRAW Procedure.”

```

data resourc2;
  input per c1-c4  t1-t3  nrooms;
  datalines;
1      1   1   1   1   .   1   1
2      .   .   .   .   .   .   .   3
3      .   .   .   .   .   .   .   2
4      .   .   .   .   .   1   .   1
5      .   .   .   .   .   .   .   3
;

proc cpm data=classes out=sched2
  resin=resourc2;
  activity class;
  duration dur;
  successor succ;
  resource c1-c4 t1-t3 nrooms / period=per stopdate=6;
run;

data schedtim;
set sched2;
format classtim classtim.;
format class $classt.;
if (s_start <= 6) then classtim = s_start;
else                  classtim = 7;
run;

title2 'Alternate Schedule with Additional Constraints';
proc print;
  id class;
  var classtim;
run;

```

#### Output 4.22.2 Alternate Class Schedule

**Scheduling Course / Teacher Combinations  
Alternate Schedule with Additional Constraints**

class	classtim
Class 1, Teacher 1	Saturday 9:00-10:00
Class 1, Teacher 2	Sunday 9:00-10:00
Class 1, Teacher 3	Saturday 10:00-11:00
Class 2, Teacher 1	Saturday 10:00-11:00
Class 2, Teacher 3	Saturday 11:00-12:00
Class 3, Teacher 1	Saturday 11:00-12:00
Class 3, Teacher 2	Sunday 10:00-11:00
Class 3, Teacher 3	Sunday 11:00-12:00
Class 4, Teacher 1	Sunday 10:00-11:00
Class 4, Teacher 2	Sunday 11:00-12:00

---

## Example 4.23: Multiproject Scheduling

This example illustrates multiproject scheduling. Consider a Survey project that contains three phases, Plan, Prepare, and Implement, with each phase containing more than one activity. You can consider each phase of the project as a subproject within the master project, Survey. Each subproject in turn contains the lowest level activities, also referred to as the leaf tasks. The Activity data set, containing the task durations, project hierarchy, and the precedence constraints, is displayed in [Output 4.23.1](#).

The PROJECT and ACTIVITY variables together define the project hierarchy using the parent/child relationship. Thus, the subproject, ‘Plan’, contains the two leaf tasks, ‘plan sur’ and ‘design q’. Precedence constraints are specified between leaf tasks as well as between subprojects. For example, the subproject ‘Prepare’ is followed by the subproject ‘Implement’. Durations are specified for all the tasks in the project, except for the master project ‘Survey’.

In addition to the Activity data set, define a Holiday data set, also displayed in [Output 4.23.1](#).

### **Output 4.23.1 Survey Project**

#### **Survey Project Activity Data Set SURVEY**

<b>Obs id</b>	<b>activity</b>	<b>duration</b>	<b>succ1</b>	<b>succ2</b>	<b>succ3</b>	<b>project</b>
1	Plan Survey	plan sur	4	hire per	design q	Plan
2	Hire Personnel	hire per	5	trn per		Prepare
3	Design Questionnaire	design q	3	trn per	select h	Plan
4	Train Personnel	trn per	3			Prepare
5	Select Households	select h	3			Prepare
6	Print Questionnaire	print q	4			Prepare
7	Conduct Survey	cond sur	10	analyze		Implement
8	Analyze Results	analyze	6			Implement
9	Plan	Plan	6			Survey
10	Prepare	Prepare	8	Implement		Survey
11	Implement	Implement	18			Survey
12	Survey Project	Survey	.			

#### **Survey Project Holiday Data Set HOLIDA**

<b>Obs</b>	<b>hol</b>
1	09APR04

The following statements invoke PROC CPM with a PROJECT statement identifying the parent task for each subtask in the Survey project. The calendar followed is a weekday calendar with a holiday defined on April 9, 2004. The ORDERALL option on the PROJECT statement creates the ordering variables ES\_ASC and LS\_ASC in the Schedule data set, and the ADDWBS option creates a work breakdown structure code for the project. The Schedule data set is displayed in [Output 4.23.2](#), after being sorted by the variable ES\_ASC.

The PROJ\_DUR variable is missing for all the leaf tasks, and it contains the project duration for the supertasks. The project duration is computed as the span of all the subtasks of the supertask. The PROJ\_LEV variable specifies the level of the subtask within the tree defining the project hierarchy, starting with the level '0' for the master project (or the root), 'Survey'. The variable WBS\_CODE contains the Work Breakdown Structure code defined by the CPM procedure using the project hierarchy.

```

proc cpm data=survey date='29mar04'd out=survout1
           interval=weekday holidata=holidata;
  activity   activity;
  successor  succ1-succ3;
  duration   duration;
  id         id;
  holiday    hol;
  project    project / orderall addwbs;
  run;

proc sort;
  by es_asc;
  run;

title 'Conducting a Market Survey';
title2 'Early and Late Start Schedule';
proc print;
  run;

```

**Output 4.23.2 Survey Project Schedule****Conducting a Market Survey  
Early and Late Start Schedule**

	P	P	W	a		d		
p	R	R	B	c		u		
r	O	O	S	t		r		
o	J	J		i				
j	—	—	C	v	s	a		
O	D	L	O	i	s	u		
e	U	E	D	c	c	c		
b	c	t		c	c	o		
s	R	V	E	y	1	n		
t					2	3		
1	28	0	0	Survey		.		
2 Survey	7	1	0.0	Plan		6		
3 Plan	.	2	0.0.0	plan sur	hire per	design q	4	
4 Plan	.	2	0.0.1	design q	trn per	select h	print q	3
5 Survey	8	1	0.1	Prepare	Implement		8	
6 Prepare	.	2	0.1.0	hire per	trn per		5	
7 Prepare	.	2	0.1.2	select h			3	
8 Prepare	.	2	0.1.3	print q			4	
9 Prepare	.	2	0.1.1	trn per			3	
10 Survey	16	1	0.2	Implement			18	
11 Implement	.	2	0.2.0	cond sur	analyze		10	
12 Implement	.	2	0.2.1	analyze			6	

	E		L		T F	
	E	—F	L	—S	I	—F
	S	I	T	A	T	F
O	—	I	S	A	I	E
b	T	N	T	I	N	L
s	A	R	S	A	O	O
d	T	H	T	R	A	A
1 Survey Project	29MAR04	06MAY04	29MAR04	06MAY04	0	0
2 Plan	29MAR04	06APR04	29MAR04	07APR04	1	1
3 Plan Survey	29MAR04	01APR04	29MAR04	01APR04	0	2
4 Design Questionnaire	02APR04	06APR04	05APR04	07APR04	1	3
5 Prepare	02APR04	14APR04	02APR04	14APR04	0	4
6 Hire Personnel	02APR04	08APR04	02APR04	08APR04	0	5
7 Select Households	07APR04	12APR04	12APR04	14APR04	2	6
8 Print Questionnaire	07APR04	13APR04	08APR04	14APR04	1	7
9 Train Personnel	12APR04	14APR04	12APR04	14APR04	0	8
10 Implement	15APR04	06MAY04	15APR04	06MAY04	0	9
11 Conduct Survey	15APR04	28APR04	15APR04	28APR04	0	10
12 Analyze Results	29APR04	06MAY04	29APR04	06MAY04	0	11

Next, a Gantt chart of the master project schedule is produced with the subtasks of each project indented under the parent task. To produce the required indentation, prefix the Activity description (saved in the variable id) by a suitable number of blanks using a simple DATA step. The following program shows the DATA step and the invocation of the GANTT procedure; the resulting Gantt chart is plotted in [Output 4.23.3](#). Note the precedence constraints between the two supertasks ‘Prepare’ and ‘Implement’.


```

data gant;
length id $26.;
set survout1;
if proj_lev=1 then id="    "||id;
else if proj_lev=2 then id="          "||id;
run;

goptions hpos=80 vpos=43;
title c=black h=2 'Conducting a Market Survey';
title2 c=black h=1.5 'Project Schedule';

proc gantt graphics data=gant holidata=holidata;
chart / holiday=(hol)
      interval=weekday
      skip=2 height=1.8
      nojobnum
      compress noextra
      activity=activity succ=(succ1-succ3)
      cprec=cyan cmile=magenta
      caxis=black;
id   id;
run;

```

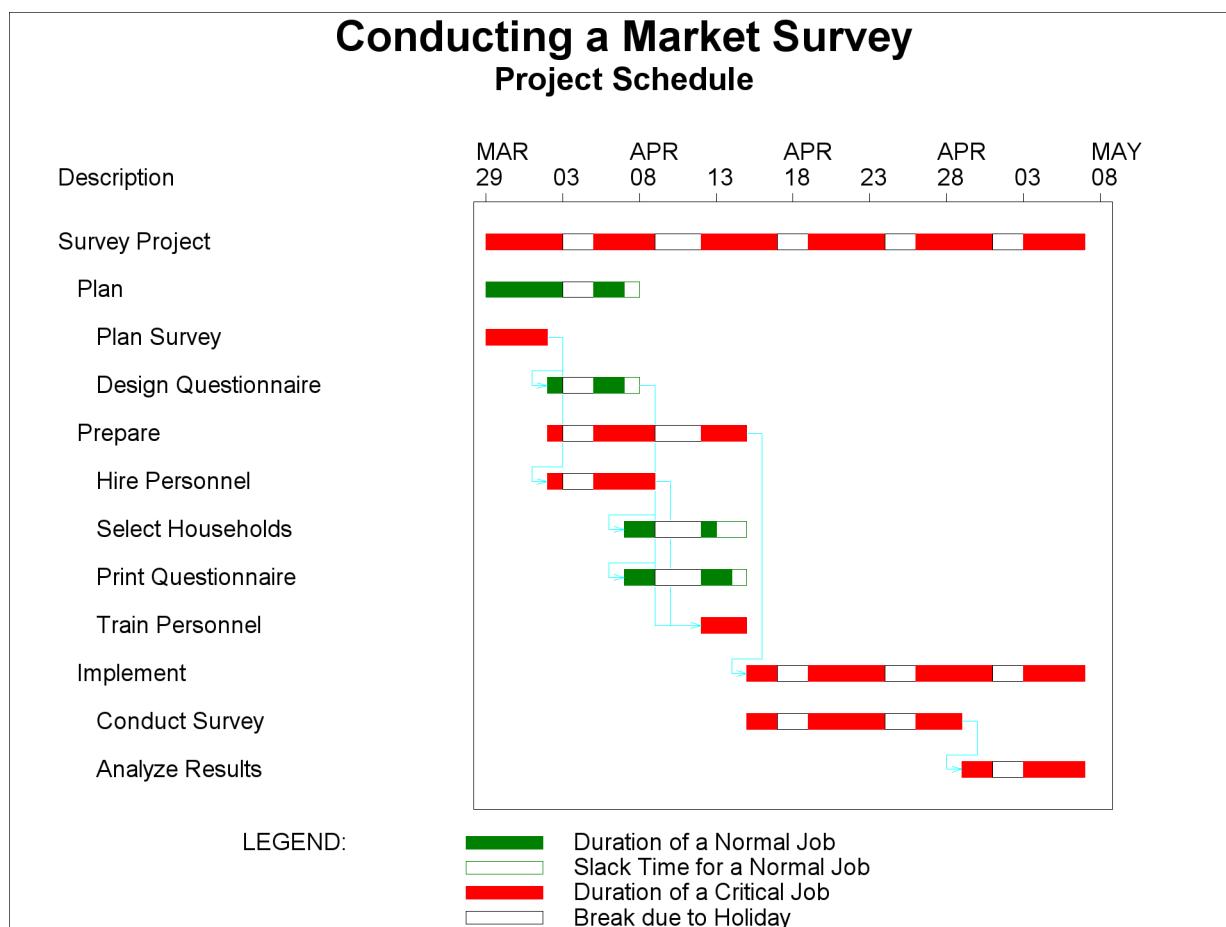**Output 4.23.3** Gantt Chart of Schedule

PROJ.LEV, WBS\_CODE, and other project-related variables can be used to display selected information about specific subprojects, summary information about subprojects at a given level of the hierarchy, and more. For example, the following statements display the summary schedule of the first level subtasks of the Survey project ([Output 4.23.4](#)).

```

title 'Market Survey';
title2 'Summary Schedule';
proc print data=survout1;
  where proj_lev=1;
  id activity;
  var proj_dur duration e_start--t_float;
run;

```

**Output 4.23.4 Survey Project Summary****Market Survey  
Summary Schedule**

activity	PROJ_DUR	duration	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT
Plan	7	6	29MAR04	06APR04	29MAR04	07APR04	1
Prepare	8	8	02APR04	14APR04	02APR04	14APR04	0
Implement	16	18	15APR04	06MAY04	15APR04	06MAY04	0

The variable WBS\_CODE in the Schedule data set (see [Output 4.23.2](#)) contains the Work Breakdown structure code defined by the CPM procedure. This code is defined to be ‘0.1’ for the subproject ‘Prepare’. Thus, the values of WBS\_CODE for all subtasks of this subproject are prefixed by ‘0.1’. To produce reports for the subproject ‘Prepare’, you can use a simple WHERE clause to subset the required observations from the Schedule data set, as shown in the following statements.

```
title 'Market Survey';
title2 'Sub-Project Schedule';
proc print data=survout1;
  where substr(WBS_CODE,1,3) = "0.1";
  id activity;
  var project--activity duration e_start--t_float;
run;
```

**Output 4.23.5 Subproject Schedule****Market Survey  
Sub-Project Schedule**

activity	project	PROJ_DUR	PROJ_LEV	WBS_CODE	activity	duration	E_START	E_FINISH
Prepare	Survey	8	1	0.1	Prepare	8	02APR04	14APR04
hire per	Prepare	.	2	0.1.0	hire per	5	02APR04	08APR04
select h	Prepare	.	2	0.1.2	select h	3	07APR04	12APR04
print q	Prepare	.	2	0.1.3	print q	4	07APR04	13APR04
trn per	Prepare	.	2	0.1.1	trn per	3	12APR04	14APR04

activity	L_START	L_FINISH	T_FLOAT
Prepare	02APR04	14APR04	0
hire per	02APR04	08APR04	0
select h	12APR04	14APR04	2
print q	08APR04	14APR04	1
trn per	12APR04	14APR04	0

In the first invocation of PROC CPM, the Survey project is scheduled with only a specification for the project start date. Continuing, this example shows how you can impose additional constraints on the master project or on the individual subprojects.

First, suppose that you impose a FINISHBEFORE constraint on the Survey project by specifying the FBDATE to be May 10, 2004. The following program schedules the project with a *project start and finish* specification. The resulting summary schedule for the subprojects is shown in [Output 4.23.6](#). The late finish time of the project is the 7th of May because there is a weekend on the 8th and 9th of May, 2004.

```
proc cpm data=survey date='29mar04'd out=survout2
    interval=weekday holidata=holidata
    fbdays='10may04'd; /* project finish date */
activity activity;
successor succ1-succ3;
duration duration;
id id;
holiday hol;
project project / orderall addwbs;
run;

title 'Market Survey';
title2 'Summary Schedule: FBDATE Option';
proc print data=survout2;
where proj_lev=1; /* First level subprojects */
id activity;
var proj_dur duration e_start--t_float;
run;
```

#### **Output 4.23.6 Summary Schedule: FBDATE Option**

#### **Market Survey Summary Schedule: FBDATE Option**

activity	PROJ_DUR	duration	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT
Plan	7	6	29MAR04	06APR04	30MAR04	08APR04	2
Prepare	8	8	02APR04	14APR04	05APR04	15APR04	1
Implement	16	18	15APR04	06MAY04	16APR04	07MAY04	1

The procedure computes the backward pass of the schedule starting from the *project finish date*. Thus, the critical path is computed in the context of the entire project. If you want to obtain individual critical paths for each subproject, use the SEPCRIT option on the PROJECT statement. You can see the effect of this option in [Output 4.23.7](#): all the subprojects have T\_FLOAT = '0'.

```
proc cpm data=survey date='29mar04'd out=survout3
    interval=weekday holidata=holidata fbdays='10may04'd;
activity activity;
successor succ1-succ3;
duration duration;
id id;
holiday hol;
project project / orderall addwbs sepcrit;
run;

title 'Market Survey';
```

```

title2 'Summary Schedule: FBDATE and SEPCRIT Options';
proc print data=survout3;
  where proj_lev=1;
  id activity;
  var proj_dur duration e_start--t_float;
run;

```

**Output 4.23.7** Summary Schedule: FBDATE and SEPCRIT Options

**Market Survey**  
**Summary Schedule: FBDATE and SEPCRIT Options**

activity	PROJ_DUR	duration	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT
Plan	7	6	29MAR04	06APR04	29MAR04	06APR04	0
Prepare	8	8	02APR04	14APR04	02APR04	14APR04	0
Implement	16	18	15APR04	06MAY04	15APR04	06MAY04	0

Now, suppose that, in addition to imposing a FINISHBEFORE constraint on the entire project, the project manager for each subproject specifies a desired duration for his or her subproject. In the present example, the variable duration has values ‘6’, ‘8’, and ‘18’ for the three subprojects. By default these values are not used in either the backward or forward pass, even though they may represent desired durations for the corresponding subprojects. You can specify the USEPROJDUR option on the PROJECT statement to indicate that the procedure should use these specified durations to determine the late finish schedule for each of the subprojects. In other words, if the USEPROJDUR option is specified, the late finish for each subproject is constrained to be less than or equal to

$$E\_START + \text{duration}$$

and this value is used during the backward pass.

The summary schedule resulting from the use of the USEPROJDUR option is shown in [Output 4.23.8](#). Note the difference in the schedules in [Output 4.23.7](#) and [Output 4.23.8](#). In [Output 4.23.7](#), the *computed project duration*, PROJ\_DUR, is used to set an upper bound on the late finish time of each subproject, while in [Output 4.23.8](#), the *specified project duration* is used for the same purpose. Here, only the summary schedules are displayed; the effect of the two options on the subtasks within each subproject can be seen by displaying the entire schedule in each case. A Gantt chart of the entire project is displayed in [Output 4.23.9](#).

```

proc cpm data=survout date='29mar04'd out=survout4
  interval=weekday holidata=holidata fbddate='10may04'd;
  activity activity;
  successor succ1-succ3;
  duration duration;
  id id;
  holiday hol;
  project project / orderall addwbs useprojdur;
run;

title 'Market Survey';
title2 'Summary Schedule: FBDATE and USEPROJDUR Options';

```

```

proc print data=survout4;
  where proj_lev=1;
  id activity;
  var proj_dur duration e_start--t_float;
run;

```

**Output 4.23.8** Summary Schedule: FBDATE and USEPROJDUR Options

**Market Survey**  
**Summary Schedule: FBDATE and USEPROJDUR Options**

activity	PROJ_DUR	duration	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT
Plan	7		6 29MAR04	06APR04	26MAR04	05APR04	-1
Prepare	8		8 02APR04	14APR04	02APR04	14APR04	0
Implement	16		18 15APR04	06MAY04	16APR04	07MAY04	1


```

data gant4;
  length id $26.;
  set survout4;
  if proj_lev=1 then id=" "||id;
  else if proj_lev=2 then id="      "||id;
run;

proc sort;
  by es_asc;
run;

goptions hpos=80 vpos=43;
title h=2 'Market Survey';
title2 h=1.5 'Project Schedule: FBDATE and USEPROJDUR Options';
proc gantt graphics data=gant4 holidata=holidata;
  chart / holiday=(hol)
        interval=weekday
        skip=2 scale=1.5 height=1.8
        nojobnum
        compress noeXtrange
        activity=activity succ=(succ1-succ3)
        cprec=cyan cmile=magenta
        caxis=black
        ;
  id id;
run;

```

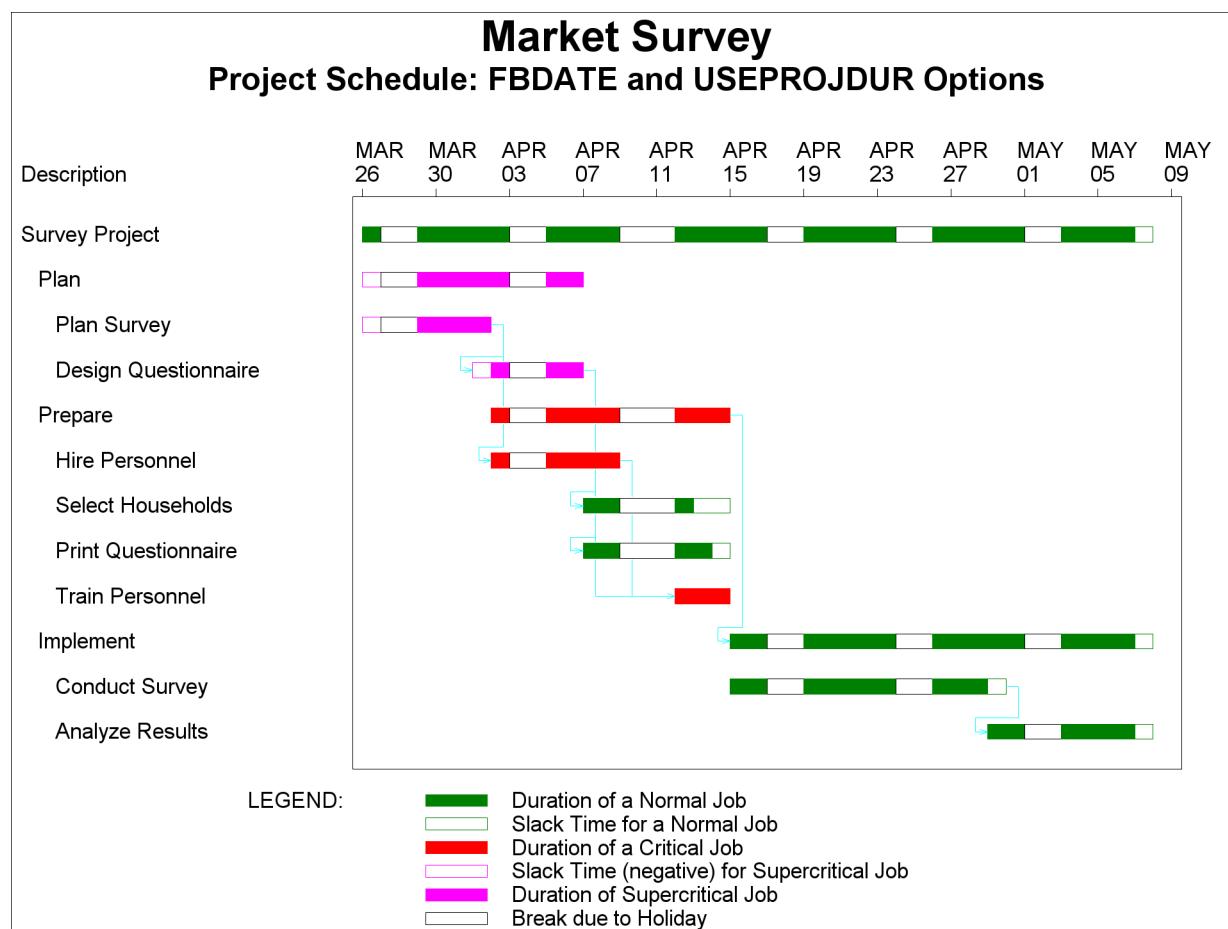**Output 4.23.9** Gantt Chart of Schedule

The project schedule is further affected by the presence of any alignment dates on the individual activities or subprojects. For example, if the implementation phase of the project has a deadline of May 5, 2004, you can specify an alignment date and type variable with the appropriate values for the subproject ‘Implement’, as follows, and invoke PROC CPM with the ALIGNDATE and ALIGNTYPE statements, to obtain the new schedule, displayed in Output 4.23.10.

```
data survey2;
  format aldate date7.;
  set survey;
  if activity="Implement" then do;
    altype="fle";
    aldate='5may04'd;
  end;
run;
```

```

proc cpm data=survey2 date='29mar04'd out=survout5
    interval=weekday holidata=holidata
    fbdate='10jun04'd;
activity activity;
successor succ1-succ3;
duration duration;
id id;
holiday hol;
project project / orderall addwbs sepcrit useprojdur;
aligntype altype;
aligndate aldate;
run;

title 'Market Survey';
title2 'USEPROJDUR option and Alignment date';
proc print;
where proj_lev=1;
id activity;
var proj_dur duration e_start--t_float;
run;

```

#### Output 4.23.10 USEPROJDUR option and Alignment Date

**Market Survey**  
**USEPROJDUR option and Alignment date**


activity	PROJ_DUR	duration	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT
Plan	7	6	29MAR04	06APR04	26MAR04	05APR04	-1
Prepare	8	8	02APR04	14APR04	01APR04	13APR04	-1
Implement	16	18	15APR04	06MAY04	14APR04	05MAY04	-1

## Example 4.24: Resource-Driven Durations and Resource Calendars

This example illustrates the effect of resource-driven durations and resource calendars on the schedule of a project involving multiple resources.

In projects that use manpower as a resource, the same activity may require different amounts of work from different people. Also, the work schedules and vacations may differ for each individual person. All of these factors may cause the schedules for the different resources used by the activity to differ from each other.

Consider a software project requiring two resources: a programmer and a tester. A network diagram displaying the activities and their precedence relationships is shown in [Output 4.24.1](#).

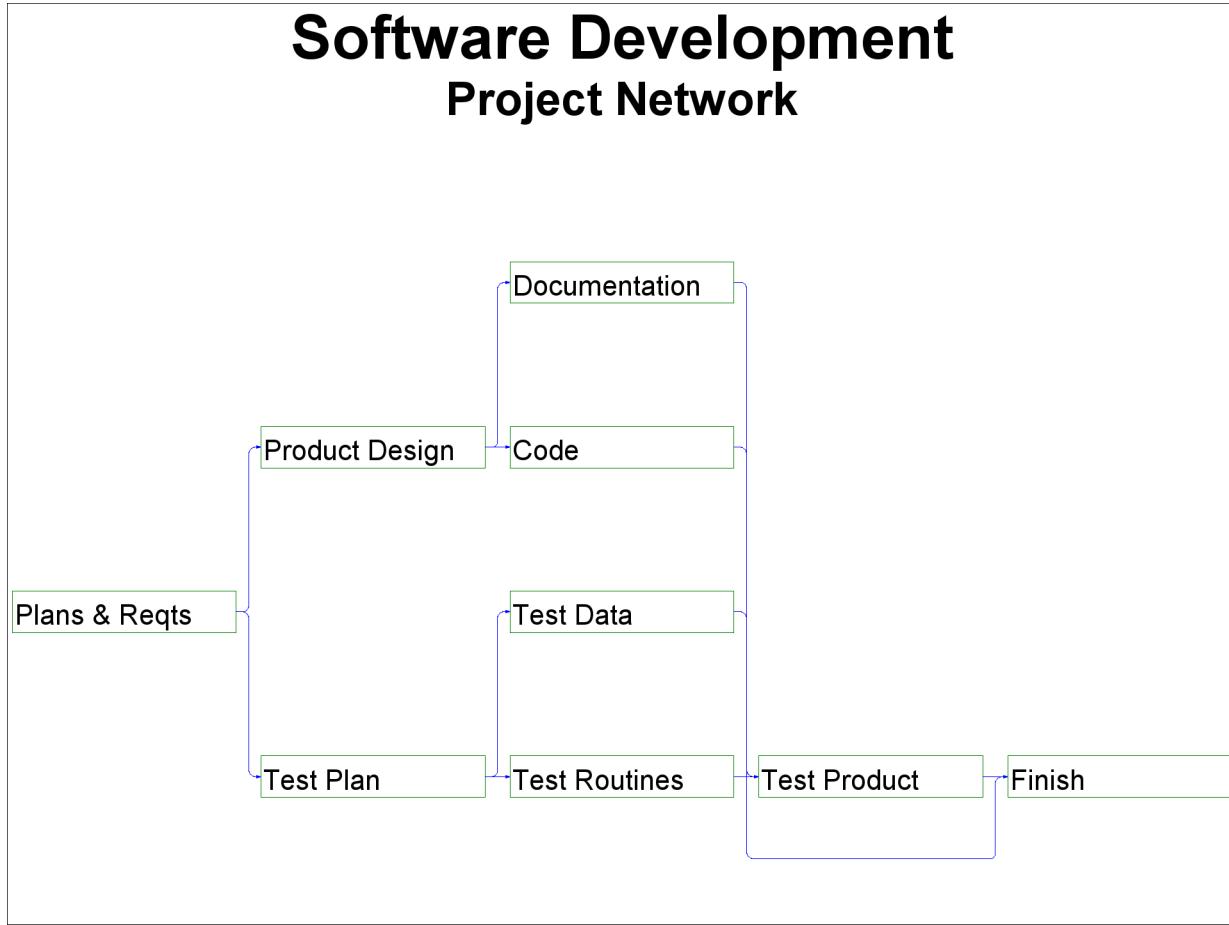**Output 4.24.1** Software Project Network

Some of the activities in this project have a fixed duration, requiring the same length of time from both resources; others require a different number of days from the programmer and the tester. Further, some activities require only a fraction of the resource; for example, ‘Documentation’ requires only 20 percent of the programmer’s time for a total of two man-days. The activities in the project, their durations (if fixed) in days, the total work required (if resource-driven) in days, the precedence constraints, and the resource requirements are displayed in [Output 4.24.2](#). There are two observations for some of the activities (‘Product Design’ and ‘Documentation’) which require different amounts of work from each resource.

**Output 4.24.2** Project Data**Software Development  
Activity Data Set SOFTWARE**

Activity	act	s1	s2	dur	mandays	Programmer	Tester
Plans & Reqs	1	2	3	2	.	1.0	1.0
Product Design	2	4	5	.	3	1.0	.
Product Design	2	.	.	.	1	.	1.0
Test Plan	3	6	7	3	.	.	1.0
Documentation	4	9	.	.	2	0.2	.
Documentation	4	.	.	.	1	.	0.5
Code	5	8	.	10	.	0.8	.
Test Data	6	8	.	5	.	.	0.5
Test Routines	7	8	.	5	.	.	0.5
Test Product	8	9	.	6	.	0.5	1.0
Finish	9	.	.	0	.	.	.

The following statements invoke PROC CPM with a WORK= specification on the RESOURCE statement, which identifies (in number of man-days, in this case) the amount of work required from each resource used by an activity. If the WORK variable has a missing value, the activity in that observation is assumed to have a fixed duration. The project is scheduled to start on April 12, 2004, and the activities are assumed to follow a five-day work week. Unlike fixed-duration scheduling, each resource used by an activity could have a different schedule; an activity is assumed to be finished only when all of its resources have finished working on it.

```
proc cpm data=software out=sftout resched=rsftout
    date='12apr04'd interval=weekday resout=rout;
    act act;
    succ s1 s2;
    dur dur;
    res Programmer Tester / work=mandays
        rschedid=Activity;
    id Activity;
run;
```

The individual resource schedules, as well as each activity's combined schedule, are saved in a Resource Schedule data set, RSFTOUT, requested by the RESSCHED= option on the CPM statement. This output data set (displayed in [Output 4.24.3](#)) is very similar to the Schedule data set and contains the activity variable and all the relevant schedule variables (E\_START, E\_FINISH, L\_START, and so forth).

**Output 4.24.3 Resource Schedule Data Set****Software Development  
Resource Schedule Data Set RSFTOUT**

A	R	D	m	E	E	L	L
c	E	U	a R	—	F	—	F
t	S	R	n —	S	I	S	I
i	O	—	d R	T	N	T	N
v	U	T	d a A	A	I	A	I
i	a	R	u y T	R	S	R	S
t	c	C	r s E	T	H	T	H
y	t	E					
<hr/>							
Plans & Reqts	1		2 . .	12APR04	13APR04	12APR04	13APR04
Plans & Reqts	1	Programmer	FIXED	2 . 1.0	12APR04	13APR04	12APR04
Plans & Reqts	1	Tester	FIXED	2 . 1.0	12APR04	13APR04	12APR04
Product Design	2		3 . .	14APR04	16APR04	14APR04	16APR04
Product Design	2	Programmer	RDRIVEN	3 3 1.0	14APR04	16APR04	14APR04
Product Design	2	Tester	RDRIVEN	1 1 1.0	14APR04	14APR04	16APR04
Test Plan	3		3 . .	14APR04	16APR04	21APR04	23APR04
Test Plan	3	Tester	FIXED	3 . 1.0	14APR04	16APR04	21APR04
Documentation	4		10 . .	19APR04	30APR04	27APR04	10MAY04
Documentation	4	Programmer	RDRIVEN	10 2 0.2	19APR04	30APR04	27APR04
Documentation	4	Tester	RDRIVEN	2 1 0.5	19APR04	20APR04	07MAY04
Code	5		10 . .	19APR04	30APR04	19APR04	30APR04
Code	5	Programmer	FIXED	10 . 0.8	19APR04	30APR04	19APR04
Test Data	6		5 . .	19APR04	23APR04	26APR04	30APR04
Test Data	6	Tester	FIXED	5 . 0.5	19APR04	23APR04	26APR04
Test Routines	7		5 . .	19APR04	23APR04	26APR04	30APR04
Test Routines	7	Tester	FIXED	5 . 0.5	19APR04	23APR04	26APR04
Test Product	8		6 . .	03MAY04	10MAY04	03MAY04	10MAY04
Test Product	8	Programmer	FIXED	6 . 0.5	03MAY04	10MAY04	03MAY04
Test Product	8	Tester	FIXED	6 . 1.0	03MAY04	10MAY04	03MAY04
Finish	9		0 . .	11MAY04	11MAY04	11MAY04	11MAY04

For each activity in the project, the Resource Schedule data set contains the schedule for the entire activity as well as the schedule for each resource used by the activity. The variable RESOURCE identifies the name of the resource to which the observation refers and has missing values for observations that refer to the entire activity's schedule. The value of the variable DUR\_TYPE indicates whether the resource drives the activity's duration ('RDRIVEN') or not ('FIXED').

The DURATION variable, dur, indicates the duration of the activity for the resource identified in that observation. For resources that are of the driving type, the WORK variable, mandays, shows the total amount of work (in units of the INTERVAL parameter) required by the resource for the activity in that observation. The variable R\_RATE shows the rate of usage of the resource for the relevant activity. For driving resources, the variable dur is computed as (mandays / R\_RATE). Thus, for the Activity, 'Documentation', the programmer requires 10 days to complete 2 man-days of work at a rate of 20 percent per day, while the tester works at a rate of 50 percent requiring 2 days to complete 1 man-day of work.

```


pattern1 c=green v=s;      /* duration of a non-critical activity */
pattern2 c=green v=e;      /* slack time for a noncrit. activity */
pattern3 c=red   v=s;      /* duration of a critical activity */
pattern4 c=magenta v=e;   /* slack time for a supercrit. activity */
pattern5 c=magenta v=s;   /* duration of a supercrit. activity */
pattern6 c=cyan  v=s;     /* actual duration of an activity */
pattern7 c=black  v=e;    /* break due to a holiday */
pattern8 c=blue   v=s;    /* resource schedule of activity */
pattern9 c=brown v=s;    /* baseline schedule of activity */

title h=2 'Software Development';
title2 h=1.5 'Project Schedule';

```

A Gantt chart of the schedules for each resource is plotted in Output 4.24.4.

**Output 4.24.4** Software Project Schedule

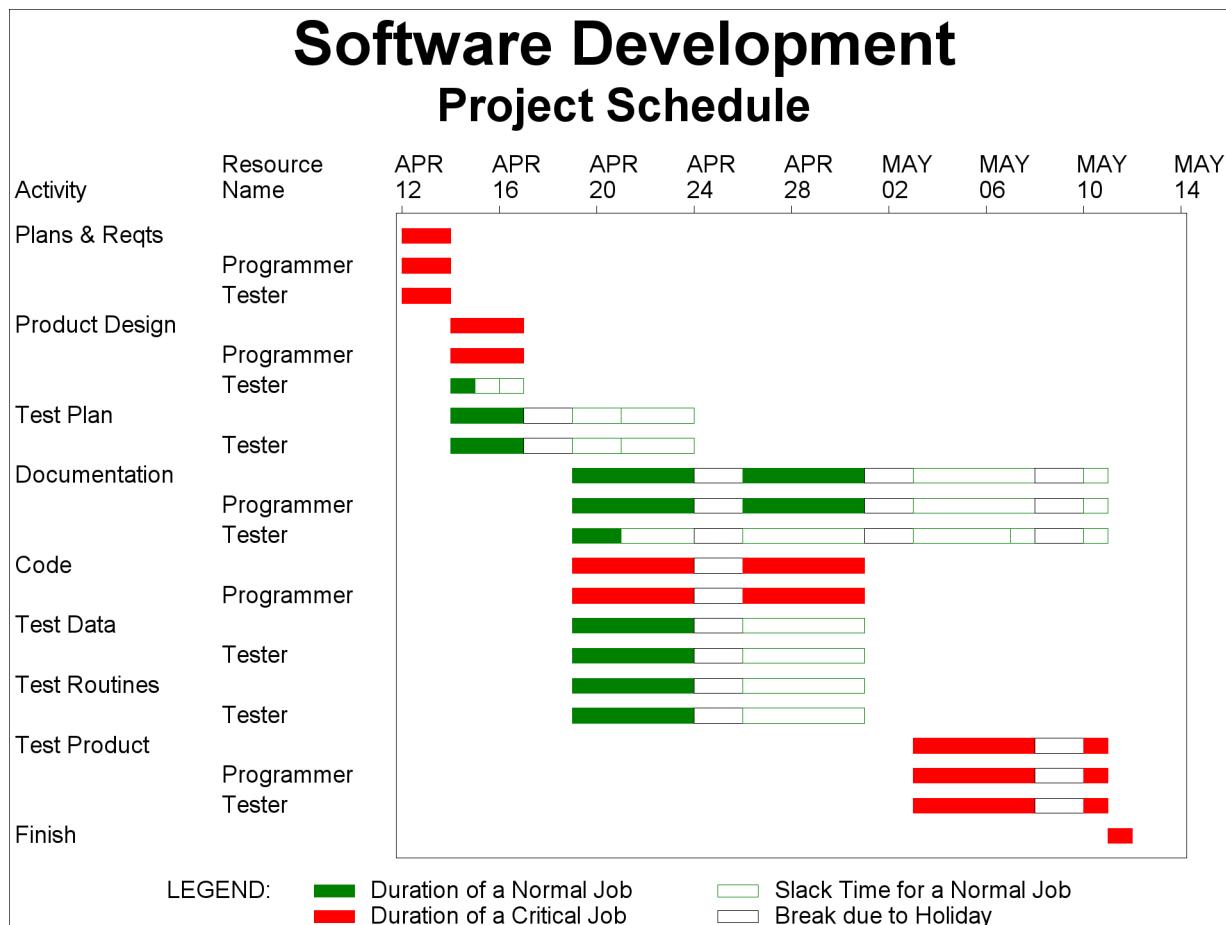

The daily utilization of the resources is also saved in a data set, ROUT, displayed in Output 4.24.5. The resource usage data set indicates that you need more than one tester on some days with both the early schedule (on the 14th, 19th, and 20th of April) and the late schedule (on the 7th and 10th of May).

#### Output 4.24.5 Resource Usage Data

##### Software Development Resource Usage Data Set ROUT

Obs	_TIME_	EProgrammer	LProgrammer	ETester	LTester
1	12APR04	1.0	1.0	1.0	1.0
2	13APR04	1.0	1.0	1.0	1.0
3	14APR04	1.0	1.0	2.0	0.0
4	15APR04	1.0	1.0	1.0	0.0
5	16APR04	1.0	1.0	1.0	1.0
6	19APR04	1.0	0.8	1.5	0.0
7	20APR04	1.0	0.8	1.5	0.0
8	21APR04	1.0	0.8	1.0	1.0
9	22APR04	1.0	0.8	1.0	1.0
10	23APR04	1.0	0.8	1.0	1.0
11	26APR04	1.0	0.8	0.0	1.0
12	27APR04	1.0	1.0	0.0	1.0
13	28APR04	1.0	1.0	0.0	1.0
14	29APR04	1.0	1.0	0.0	1.0
15	30APR04	1.0	1.0	0.0	1.0
16	03MAY04	0.5	0.7	1.0	1.0
17	04MAY04	0.5	0.7	1.0	1.0
18	05MAY04	0.5	0.7	1.0	1.0
19	06MAY04	0.5	0.7	1.0	1.0
20	07MAY04	0.5	0.7	1.0	1.5
21	10MAY04	0.5	0.7	1.0	1.5
22	11MAY04	0.0	0.0	0.0	0.0

Suppose now that you have only one tester and one programmer. You can determine a resource-constrained schedule using PROC CPM (as in the fixed duration case) by specifying a resource availability data set, **RESIN** ([Output 4.24.6](#)).

## **Output 4.24.6 Resource Availability Data**

## **Software Development Resource Availability Data Set**

Obs	per	otype	Programmer	Tester
1	12APR04	reslevel		1


The following statements invoke PROC CPM, and the resulting Resource Schedule data set is displayed in [Output 4.24.7](#). The ADDCAL option on the RESOURCE statement creates a variable in the Resource Schedule data set which identifies the activity or resource calendar. The project still finishes on May 11, but some of the activities ('Test Plan', 'Documentation', 'Test Data', and 'Test Routines') are delayed. The resource-constrained schedule is plotted on a Gantt chart in [Output 4.24.8](#); both resources follow the same weekday calendar.

**Output 4.24.7 Resource-Constrained Schedule: Common Calendar**

**Software Development**  
**Resource Constrained Schedule: Common Resource Calendar**

Activity	act	_CAL_	RESOURCE	DUR_TYPE	dur	mandays	R_RATE	S_START	S_FINISH
Plans & Reqts	1	0			2	.	.	12APR04	13APR04
Plans & Reqts	1	0	Programmer	FIXED	2	.	1.0	12APR04	13APR04
Plans & Reqts	1	0	Tester	FIXED	2	.	1.0	12APR04	13APR04
Product Design	2	0			3	.	.	14APR04	16APR04
Product Design	2	0	Programmer	RDRIVEN	3	3	1.0	14APR04	16APR04
Product Design	2	0	Tester	RDRIVEN	1	1	1.0	14APR04	14APR04
Test Plan	3	0			3	.	.	15APR04	19APR04
Test Plan	3	0	Tester	FIXED	3	.	1.0	15APR04	19APR04
Documentation	4	0			10	.	.	27APR04	10MAY04
Documentation	4	0	Programmer	RDRIVEN	10	2	0.2	27APR04	10MAY04
Documentation	4	0	Tester	RDRIVEN	2	1	0.5	27APR04	28APR04
Code	5	0			10	.	.	19APR04	30APR04
Code	5	0	Programmer	FIXED	10	.	0.8	19APR04	30APR04
Test Data	6	0			5	.	.	20APR04	26APR04
Test Data	6	0	Tester	FIXED	5	.	0.5	20APR04	26APR04
Test Routines	7	0			5	.	.	20APR04	26APR04
Test Routines	7	0	Tester	FIXED	5	.	0.5	20APR04	26APR04
Test Product	8	0			6	.	.	03MAY04	10MAY04
Test Product	8	0	Programmer	FIXED	6	.	0.5	03MAY04	10MAY04
Test Product	8	0	Tester	FIXED	6	.	1.0	03MAY04	10MAY04
Finish	9	0			0	.	.	11MAY04	11MAY04

Activity	E_START	E_FINISH	L_START	L_FINISH
Plans & Reqts	12APR04	13APR04	12APR04	13APR04
Plans & Reqts	12APR04	13APR04	12APR04	13APR04
Plans & Reqts	12APR04	13APR04	12APR04	13APR04
Product Design	14APR04	16APR04	14APR04	16APR04
Product Design	14APR04	16APR04	14APR04	16APR04
Product Design	14APR04	14APR04	16APR04	16APR04
Test Plan	14APR04	16APR04	21APR04	23APR04
Test Plan	14APR04	16APR04	21APR04	23APR04
Documentation	19APR04	30APR04	27APR04	10MAY04
Documentation	19APR04	30APR04	27APR04	10MAY04
Documentation	19APR04	20APR04	07MAY04	10MAY04
Code	19APR04	30APR04	19APR04	30APR04
Code	19APR04	30APR04	19APR04	30APR04
Test Data	19APR04	23APR04	26APR04	30APR04
Test Data	19APR04	23APR04	26APR04	30APR04
Test Routines	19APR04	23APR04	26APR04	30APR04
Test Routines	19APR04	23APR04	26APR04	30APR04
Test Product	03MAY04	10MAY04	03MAY04	10MAY04
Test Product	03MAY04	10MAY04	03MAY04	10MAY04
Test Product	03MAY04	10MAY04	03MAY04	10MAY04
Finish	11MAY04	11MAY04	11MAY04	11MAY04

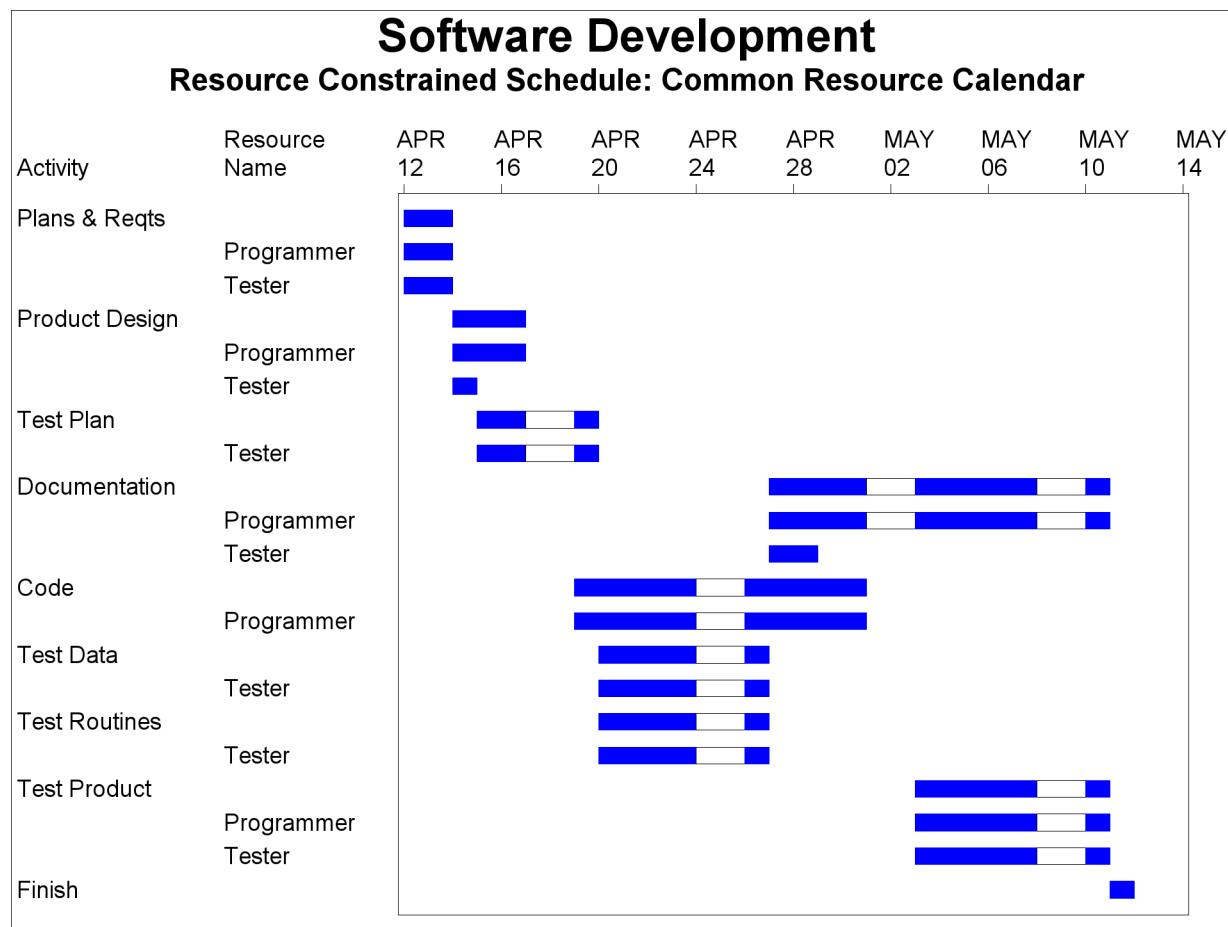**Output 4.24.8** Resource-Constrained Schedule

Now suppose that the tester switches to part-time employment, working only four days a week. Thus, the two resources have different calendars. To determine the effect this change has on the project schedule, define a calendar data set identifying calendar '1' as having a holiday on Friday (see [Output 4.24.9](#)). In a new resource availability data set (also displayed in [Output 4.24.9](#)), associate calendar '1' with the resource Tester and calendar '0' with the resource Programmer. '0' refers to the default calendar, which is the weekday calendar for this project (since INTERVAL = WEEKDAY).

**Output 4.24.9** Resource and Calendar Data

**Software Development  
Calendar Data Set CALENDAR**

Obs	_cal_	_fri_
1	1	holiday

**Resource Data Set RESIN2**


Obs	per	otype	Programmer	Tester
1	.	calendar	0	1
2	12APR04	reslevel	1	1

Next, invoke PROC CPM, as shown in the following statements, with the Activity, Resource, and Calendar data sets to obtain the revised schedule, plotted in [Output 4.24.10](#). The project is delayed by two days because of the TESTER's shorter work week, which is illustrated by the longer holiday breaks in the TESTER's schedule bars. The new resource constrained schedule is displayed in [Output 4.24.11](#).

```

proc cpm data=software resin=resin2
  caledata=calendar
  out=sftout2 rsched=rsftout2
  resout=rout2
  date='12apr04'd interval=weekday;
act act;
succ s1 s2;
dur dur;
res Programmer Tester / work=mandays addcal
  obstype=otype
  period=per
  rschedid=Activity;
id Activity;
run;

```

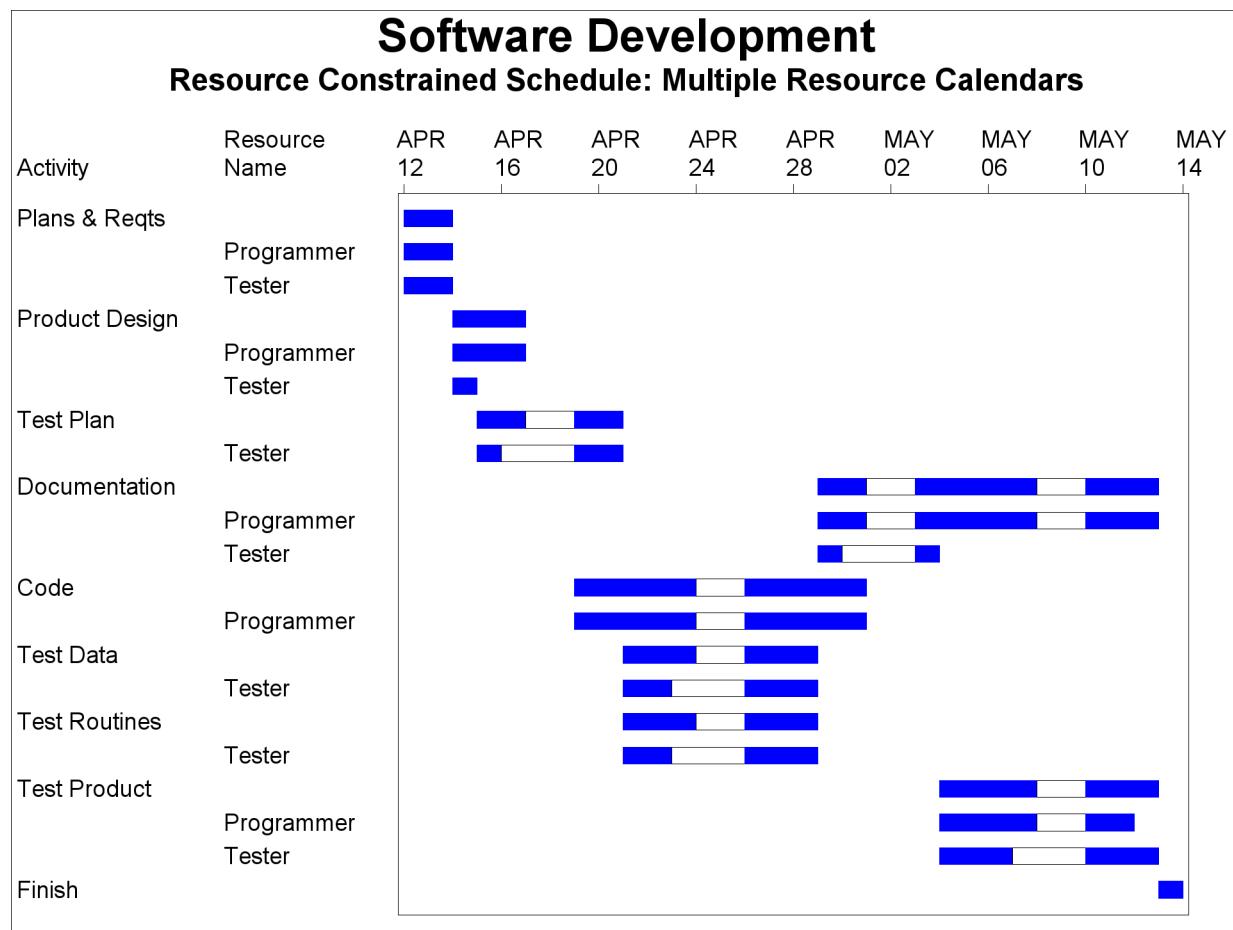**Output 4.24.10** Resource-Constrained Schedule

**Output 4.24.11 Resource-Constrained Schedule: Multiple Calendars**

**Software Development**  
**Resource Constrained Schedule: Multiple Resource Calendars**

Activity	act	_CAL_	RESOURCE	DUR_TYPE	dur	mandays	R_RATE	S_START	S_FINISH
Plans & Reqts	1	0			2	.	.	12APR04	13APR04
Plans & Reqts	1	0	Programmer	FIXED	2	.	1.0	12APR04	13APR04
Plans & Reqts	1	1	Tester	FIXED	2	.	1.0	12APR04	13APR04
Product Design	2	0			3	.	.	14APR04	16APR04
Product Design	2	0	Programmer	RDRIVEN	3	3	1.0	14APR04	16APR04
Product Design	2	1	Tester	RDRIVEN	1	1	1.0	14APR04	14APR04
Test Plan	3	0			3	.	.	15APR04	20APR04
Test Plan	3	1	Tester	FIXED	3	.	1.0	15APR04	20APR04
Documentation	4	0			10	.	.	29APR04	12MAY04
Documentation	4	0	Programmer	RDRIVEN	10	2	0.2	29APR04	12MAY04
Documentation	4	1	Tester	RDRIVEN	2	1	0.5	29APR04	03MAY04
Code	5	0			10	.	.	19APR04	30APR04
Code	5	0	Programmer	FIXED	10	.	0.8	19APR04	30APR04
Test Data	6	0			5	.	.	21APR04	28APR04
Test Data	6	1	Tester	FIXED	5	.	0.5	21APR04	28APR04
Test Routines	7	0			5	.	.	21APR04	28APR04
Test Routines	7	1	Tester	FIXED	5	.	0.5	21APR04	28APR04
Test Product	8	0			6	.	.	04MAY04	12MAY04
Test Product	8	0	Programmer	FIXED	6	.	0.5	04MAY04	11MAY04
Test Product	8	1	Tester	FIXED	6	.	1.0	04MAY04	12MAY04
Finish	9	0			0	.	.	13MAY04	13MAY04

Activity	E_START	E_FINISH	L_START	L_FINISH
Plans & Reqts	12APR04	13APR04	12APR04	13APR04
Plans & Reqts	12APR04	13APR04	12APR04	13APR04
Plans & Reqts	12APR04	13APR04	12APR04	13APR04
Product Design	14APR04	16APR04	14APR04	16APR04
Product Design	14APR04	16APR04	14APR04	16APR04
Product Design	14APR04	14APR04	15APR04	15APR04
Test Plan	14APR04	19APR04	19APR04	21APR04
Test Plan	14APR04	19APR04	19APR04	21APR04
Documentation	19APR04	30APR04	28APR04	11MAY04
Documentation	19APR04	30APR04	28APR04	11MAY04
Documentation	19APR04	20APR04	10MAY04	11MAY04
Code	19APR04	30APR04	19APR04	30APR04
Code	19APR04	30APR04	19APR04	30APR04
Test Data	20APR04	27APR04	22APR04	30APR04
Test Data	20APR04	27APR04	22APR04	29APR04
Test Routines	20APR04	27APR04	22APR04	30APR04
Test Routines	20APR04	27APR04	22APR04	29APR04
Test Product	03MAY04	11MAY04	03MAY04	11MAY04
Test Product	03MAY04	10MAY04	04MAY04	11MAY04
Test Product	03MAY04	11MAY04	03MAY04	11MAY04
Finish	12MAY04	12MAY04	12MAY04	12MAY04

---

## Example 4.25: Resource-Driven Durations and Alternate Resources

Consider the software project defined in Example 4.24 but now the project requires a single resource: a programmer. A network diagram displaying the activities and their precedence relationships is shown in [Output 4.24.1](#), as part of the same example.

Some of the activities in this project have a fixed duration, requiring a fixed length of time from a programmer. Other activities specify the amount of work required in terms of man-days; for these activities, the length of the task will depend on the number of programmers (or rate) that is assigned to the task. The activities in the project, their durations (if fixed) or the total work required (if resource-driven) in days, the precedence constraints, and the resource requirements are displayed in [Output 4.25.1](#).

Suppose that you have only one programmer assigned to the project. You can determine a resource-constrained schedule using PROC CPM by specifying a resource availability data set, `resin` (also in [Output 4.25.1](#)). The Resource data set indicates that the resource `Programmer` is a driving resource whenever the `WORK` variable has a valid value.

**Output 4.25.1** Project Data

### Software Development Activity Data Set SOFTWARE

Activity	act	s1	s2	dur	mandays	Programmer
Plans & Reqs	1	2	3	2	.	1
Product Design	2	4	5	.	3	1
Test Plan	3	6	7	3	.	.
Documentation	4	9	.	1	2	1
Code	5	8	.	1	10	1
Test Data	6	8	.	5	.	.
Test Routines	7	8	.	5	.	.
Test Product	8	9	.	6	.	1
Finish	9	.	.	0	.	.

### Software Development Resource Availability Data Set

Obs	per	otype	Programmer
1	.	resrcdur	1
2	12APR04	reslevel	1

The following statements invoke PROC CPM with a WORK= specification on the RESOURCE statement, which identifies (in number of man-days, in this case) the amount of work required from the resource Programmer for each activity. If the WORK variable has a missing value, the activity in that observation is assumed to have a fixed duration. The project is scheduled to start on April 12, 2004, and the activities are assumed to follow a five-day work week. The resulting schedule is displayed in [Output 4.25.2](#). For each activity in the project, the value of the variable DUR\_TYPE indicates whether the resource drives the activity's duration ('RDRIVEN') or not ('FIXED').

```

proc cpm data=software
    out=sftout1 resout=rout1
    rsched=rsftout1
    resin=resin
    date='12apr04'd interval=weekday;
act act;
succ s1 s2;
dur dur;
res Programmer / work=mandays
    obstype=otype
    period=per
    rschedid=Activity;
id Activity;
run;

title 'Software Development';
title2 'Resource Constrained Schedule: Single Programmer';
proc print data=rsftout1 heading=h;
id Activity;
run;

```

**Output 4.25.2 Resource Schedule****Software Development  
Resource Constrained Schedule: Single Programmer**

Activity	act	RESOURCE	DUR_TYPE	dur	mandays	R_RATE	S_START	S_FINISH
Plans & Reqs	1			2	.	1	12APR04	13APR04
Plans & Reqs	1	Programmer	FIXED	2	.	1	12APR04	13APR04
Product Design	2			3	.	1	14APR04	16APR04
Product Design	2	Programmer	RDRIVEN	3	3	1	14APR04	16APR04
Test Plan	3			3	.	1	14APR04	16APR04
Documentation	4			1	.	1	11MAY04	12MAY04
Documentation	4	Programmer	RDRIVEN	2	2	1	11MAY04	12MAY04
Code	5			1	.	1	19APR04	30APR04
Code	5	Programmer	RDRIVEN	10	10	1	19APR04	30APR04
Test Data	6			5	.	1	19APR04	23APR04
Test Routines	7			5	.	1	19APR04	23APR04
Test Product	8			6	.	1	03MAY04	10MAY04
Test Product	8	Programmer	FIXED	6	.	1	03MAY04	10MAY04
Finish	9			0	.	1	13MAY04	13MAY04


Activity	E_START	E_FINISH	L_START	L_FINISH
Plans & Reqs	12APR04	13APR04	12APR04	13APR04
Plans & Reqs	12APR04	13APR04	12APR04	13APR04
Product Design	14APR04	16APR04	14APR04	16APR04
Product Design	14APR04	16APR04	14APR04	16APR04
Test Plan	14APR04	16APR04	21APR04	23APR04
Documentation	19APR04	20APR04	07MAY04	10MAY04
Documentation	19APR04	20APR04	07MAY04	10MAY04
Code	19APR04	30APR04	19APR04	30APR04
Code	19APR04	30APR04	19APR04	30APR04
Test Data	19APR04	23APR04	26APR04	30APR04
Test Routines	19APR04	23APR04	26APR04	30APR04
Test Product	03MAY04	10MAY04	03MAY04	10MAY04
Test Product	03MAY04	10MAY04	03MAY04	10MAY04
Finish	11MAY04	11MAY04	11MAY04	11MAY04

The following statements invoke PROC GANTT to display a Gantt chart of the schedule in Output 4.25.3. The activity, ‘Documentation’, is delayed until May 11, 2004, because there is only one programmer available to the project.

```

title h=2.5 'Software Development';
title2 h=1.5 'Resource Constrained Schedule: Single Programmer';
proc gantt graphics data=sftout1;
  id Activity Programmer;
  chart / compress scale=3 increment=4 interval=weekday
    height=2.8 nojobnum nolegend between=5
    act=act succ=(s1 s2)
    cprec=cyan
    caxis=black
    ;
run;

```

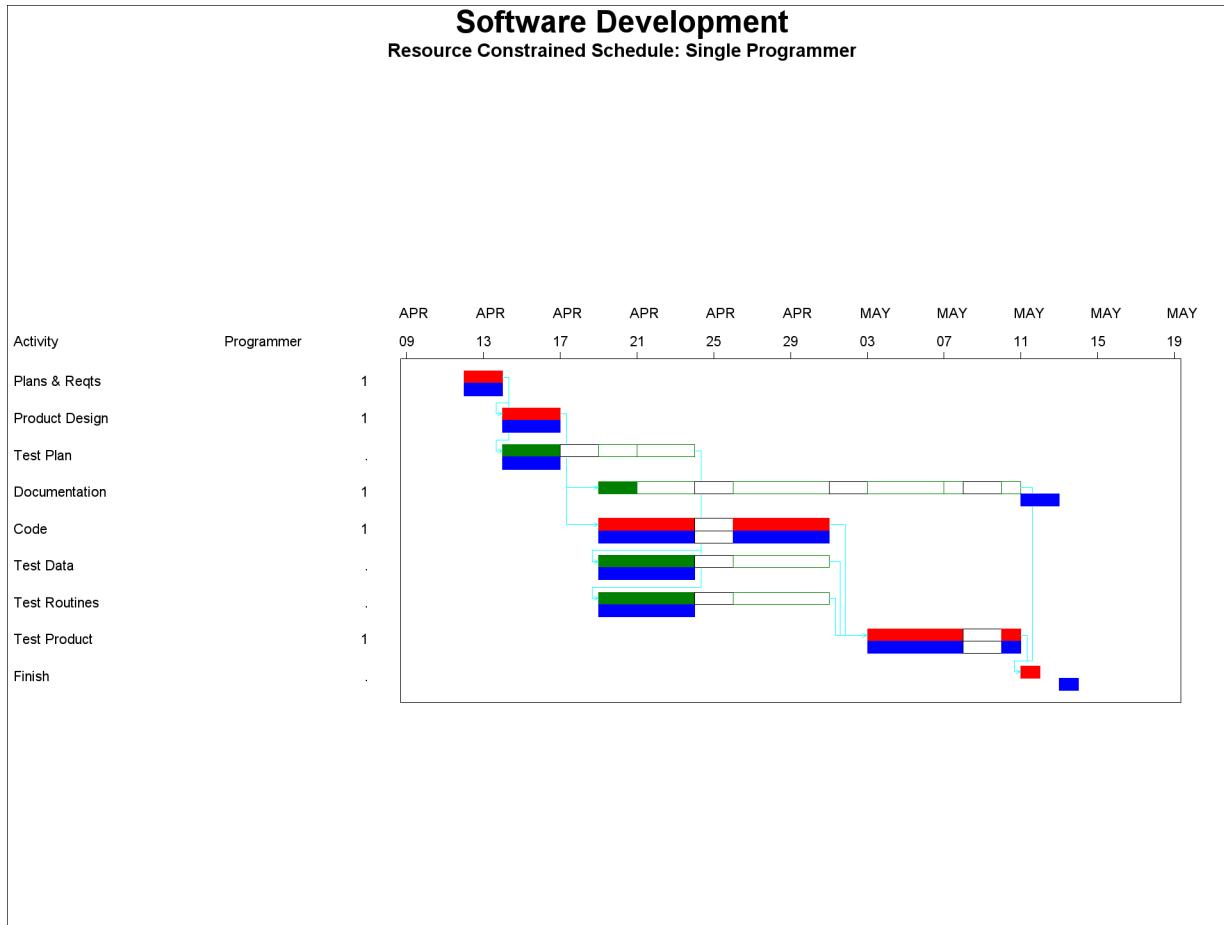**Output 4.25.3** Resource-Constrained Schedule: Single Programmer

Next, suppose that you have two programmers assigned to your project and you can use either one of them for a given task, depending on their availability. To model this scenario, specify Chris and John as alternate resources that can be substituted for the resource Programmer. The Resource data set, `resin2`, printed in [Output 4.25.4](#), indicates that Chris and John are alternates for Programmer. Specifying an availability of '0' for the resource Programmer ensures that the procedure will assign one of the two programmers, Chris or John, to each task.

The second observation in the data set `resin2` indicates two different rates of substitution for the alternate resources. A value less than 1 indicates that the alternate resource is more efficient than the primary resource, while a value greater than 1 indicates that the alternate resource is less efficient. For fixed-duration activities, the use of the alternate resource changes the *rate* of utilization of the resource, while for a resource-driven activity, it changes the *duration* of the resource. The data set `resin` specifies that John is twice as efficient as the primary resource Programmer while Chris takes one and a half times as long as the generic resource to accomplish a task.

**Output 4.25.4** Alternate Programmers**Resource Data Set RESIN2**

Obs	per	otype	resid	Programmer	Chris	John
1	.	resrcdur		1	1.0	1.0
2	.	altrate	Programmer	.	1.5	0.5
3	12APR04	reslevel		.	1.0	1.0

The following statements invoke PROC CPM with the new Resource data set and a modified Activity data set that includes the newly added resource variables, Chris and John. You can see the effects of the alternate resource specifications in the Resource Schedule data set, printed in [Output 4.25.5](#). The activity ‘Product Design’ that takes 3 days of time from a generic programmer actually takes 4.5 days because the programmer used is Chris, who is substituted at a rate of 1.5. On the other hand, the programmer John efficiently completes the task, ‘Documentation’, in only 1 day, instead of the planned 2 days for a generic programmer. Note also that the start and finish times are specified as SAS datetime values because the substitution of alternate resources results in some of the resource durations being fractional.

```

data software2;
  set software;
  Chris = .;
  John = .;
  run;

proc cpm data=software2 out=sftout2 rsched=rsftout2
  resin=resin2
  date='12apr04'd interval=weekday resout=rout2;
  act act;
  succ s1 s2;
  dur dur;
  res Programmer Chris John / work=mandays
    obstype=otype
    period=per
    resid=resid
    rschedid=Activity;
  id Activity;
  run;

```

### Output 4.25.5 Resource Schedule with Alternate Programmers

**Software Development**  
**Resource Constrained Schedule**  
**Alternate Resources at Varying Rates**

Activity	act	RESOURCE	DUR_TYPE	dur	mandays	R_RATE	S_START
<b>Plans &amp; Reqts</b>	1			2.0	.	.	12APR04:00:00:00
<b>Plans &amp; Reqts</b>	1	Programmer	FIXED	2.0	.	1.0	.
<b>Plans &amp; Reqts</b>	1	John	FIXED	2.0	.	0.5	12APR04:00:00:00
<b>Product Design</b>	2			3.0	.	.	14APR04:00:00:00
<b>Product Design</b>	2	Programmer	RDRIVEN	3.0	3.0	1.0	.
<b>Product Design</b>	2	Chris	RDRIVEN	4.5	4.5	1.0	14APR04:00:00:00
<b>Test Plan</b>	3			3.0	.	.	14APR04:00:00:00
<b>Documentation</b>	4			1.0	.	.	20APR04:12:00:00
<b>Documentation</b>	4	Programmer	RDRIVEN	2.0	2.0	1.0	.
<b>Documentation</b>	4	John	RDRIVEN	1.0	1.0	1.0	20APR04:12:00:00
<b>Code</b>	5			1.0	.	.	20APR04:12:00:00
<b>Code</b>	5	Programmer	RDRIVEN	10.0	10.0	1.0	.
<b>Code</b>	5	Chris	RDRIVEN	15.0	15.0	1.0	20APR04:12:00:00
<b>Test Data</b>	6			5.0	.	.	19APR04:00:00:00
<b>Test Routines</b>	7			5.0	.	.	19APR04:00:00:00
<b>Test Product</b>	8			6.0	.	.	11MAY04:12:00:00
<b>Test Product</b>	8	Programmer	FIXED	6.0	.	1.0	.
<b>Test Product</b>	8	John	FIXED	6.0	.	0.5	11MAY04:12:00:00
<b>Finish</b>	9			0.0	.	.	19MAY04:12:00:00

Activity	S_FINISH	E_START	E_FINISH
<b>Plans &amp; Reqts</b>	13APR04:23:59:59	12APR04:00:00:00	13APR04:23:59:59
<b>Plans &amp; Reqts</b>	.	12APR04:00:00:00	13APR04:23:59:59
<b>Plans &amp; Reqts</b>	13APR04:23:59:59	.	.
<b>Product Design</b>	20APR04:11:59:59	14APR04:00:00:00	16APR04:23:59:59
<b>Product Design</b>	.	14APR04:00:00:00	16APR04:23:59:59
<b>Product Design</b>	20APR04:11:59:59	.	.
<b>Test Plan</b>	16APR04:23:59:59	14APR04:00:00:00	16APR04:23:59:59
<b>Documentation</b>	21APR04:11:59:59	19APR04:00:00:00	20APR04:23:59:59
<b>Documentation</b>	.	19APR04:00:00:00	20APR04:23:59:59
<b>Documentation</b>	21APR04:11:59:59	.	.
<b>Code</b>	11MAY04:11:59:59	19APR04:00:00:00	30APR04:23:59:59
<b>Code</b>	.	19APR04:00:00:00	30APR04:23:59:59
<b>Code</b>	11MAY04:11:59:59	.	.
<b>Test Data</b>	23APR04:23:59:59	19APR04:00:00:00	23APR04:23:59:59
<b>Test Routines</b>	23APR04:23:59:59	19APR04:00:00:00	23APR04:23:59:59
<b>Test Product</b>	19MAY04:11:59:59	03MAY04:00:00:00	10MAY04:23:59:59
<b>Test Product</b>	.	03MAY04:00:00:00	10MAY04:23:59:59
<b>Test Product</b>	19MAY04:11:59:59	.	.
<b>Finish</b>	19MAY04:12:00:00	11MAY04:00:00:00	11MAY04:00:00:00

---

## Example 4.26: Multiple Alternate Resources

This example illustrates the use of the MULTIPLEALTERNATES option. The Activity data set printed in [Output 4.26.1](#) is a slightly modified version of the data set in [Example 4.25](#). The difference is in the resource requirement for the first activity in the project. The ‘Plans and Requirements’ task requires 2 programmers. By default, when alternate resources are used, the CPM procedures cannot use multiple alternate resources to substitute for any given resource. In this example, however, you would like the procedure to use both Chris and John for the first task. The Resource data set `resmult` is also printed in [Output 4.26.1](#), showing that both Chris and John are alternates that can be substituted at the same rate as the primary resource.

### Output 4.26.1 Multiple Alternates

**Software Development**  
**Use of Multiple Alternate Resources**  
**Activity Data Set**

Obs	Activity	dur	mandays	act	s1	s2	Programmer	Chris	John
1	Plans & Reqts	2	.	1	2	3	2	.	.
2	Product Design	.	3	2	4	5	1	.	.
3	Test Plan	3	.	3	6	7	.	.	.
4	Documentation	1	2	4	9	.	1	.	.
5	Code	1	10	5	8	.	1	.	.
6	Test Data	5	.	6	8	.	.	.	.
7	Test Routines	5	.	7	8	.	.	.	.
8	Test Product	6	.	8	9	.	1	.	.
9	Finish	0	.	9	.	.	.	.	.

**Software Development**  
**Use of Multiple Alternate Resources**  
**Resource Data Set**

Obs	per	otype	resid	Programmer	Chris	John
1	.	resrcdur		1	1	1
2	.	altrate	Programmer	.	1	1
3	12APR04	reslevel		.	1	1

To enable PROC CPM to use multiple alternates, use the MULTIPLEALTERNATES option, as shown in the following invocation:

```
proc cpm data=softmult out=sftmult rsched=rsftmult
    resin=resmult
    date='12apr04'd interval=weekday resout=routmult;
act act;
succ s1 s2;
dur dur;
res Programmer Chris John / work=mandays
    obstype=otype
    period=per resid=resid
    multiplealternates
    rschedid=Activity;
id Activity;
run;
```

The resulting schedule is printed in [Output 4.26.2](#). Note that both programmers are used for the activity ‘Plans and Reqs’.

**Output 4.26.2** Multiple Alternates: Resource Schedule Data Set

**Software Development**  
**Use of Multiple Alternate Resources**  
**Resource Constrained Schedule**

Activity	act	RESOURCE	DUR_TYPE	dur	mandays	R_RATE	S_START	S_FINISH
Plans & Reqts	1			2	.	.	12APR04	13APR04
Plans & Reqts	1	Programmer	FIXED	2	.	2	.	.
Plans & Reqts	1	John	FIXED	2	.	1	12APR04	13APR04
Plans & Reqts	1	Chris	FIXED	2	.	1	12APR04	13APR04
Product Design	2			3	.	.	14APR04	16APR04
Product Design	2	Programmer	RDRIVEN	3	3	1	.	.
Product Design	2	Chris	RDRIVEN	3	3	1	14APR04	16APR04
Test Plan	3			3	.	.	14APR04	16APR04
Documentation	4			1	.	.	19APR04	20APR04
Documentation	4	Programmer	RDRIVEN	2	2	1	.	.
Documentation	4	John	RDRIVEN	2	2	1	19APR04	20APR04
Code	5			1	.	.	19APR04	30APR04
Code	5	Programmer	RDRIVEN	10	10	1	.	.
Code	5	Chris	RDRIVEN	10	10	1	19APR04	30APR04
Test Data	6			5	.	.	19APR04	23APR04
Test Routines	7			5	.	.	19APR04	23APR04
Test Product	8			6	.	.	03MAY04	10MAY04
Test Product	8	Programmer	FIXED	6	.	1	.	.
Test Product	8	Chris	FIXED	6	.	1	03MAY04	10MAY04
Finish	9			0	.	.	11MAY04	11MAY04

Activity	E_START	E_FINISH	L_START	L_FINISH
Plans & Reqts	12APR04	13APR04	12APR04	13APR04
Plans & Reqts	12APR04	13APR04	12APR04	13APR04
Plans & Reqts	.	.	.	.
Plans & Reqts	.	.	.	.
Product Design	14APR04	16APR04	14APR04	16APR04
Product Design	14APR04	16APR04	14APR04	16APR04
Product Design	.	.	.	.
Test Plan	14APR04	16APR04	21APR04	23APR04
Documentation	19APR04	20APR04	07MAY04	10MAY04
Documentation	19APR04	20APR04	07MAY04	10MAY04
Documentation	.	.	.	.
Code	19APR04	30APR04	19APR04	30APR04
Code	19APR04	30APR04	19APR04	30APR04
Code	.	.	.	.
Test Data	19APR04	23APR04	26APR04	30APR04
Test Routines	19APR04	23APR04	26APR04	30APR04
Test Product	03MAY04	10MAY04	03MAY04	10MAY04
Test Product	03MAY04	10MAY04	03MAY04	10MAY04
Test Product	.	.	.	.
Finish	11MAY04	11MAY04	11MAY04	11MAY04

---

## Example 4.27: Auxiliary Resources and Alternate Resources

This example illustrates the use of Auxiliary resources. In the earlier examples, the use of alternate resources enabled the allocation of either John or Chris to the programming tasks. Now, suppose that each of the programmers has a different tester, and whenever a particular programmer is scheduled for a given task, his tester also needs to allocate some part of his or her time, say 50 percent, to the same task. To model such a scenario, specify Tester1 and Tester2 as auxiliary resources for Chris and John, respectively. The Activity and Resource data sets are printed in [Output 4.27.1](#). Unlike the earlier examples, all the activities are of fixed-duration.

```

data software;
  input Activity & $15. dur act s1 s2 Programmer;
datalines;
Plans & Reqts   2  1    2  3  1
Product Design  3  2    4  5  1
Test Plan        3  3    6  7  .
Documentation    3  4    9  .  1
Code             10 5   8  .  1
Test Data        5  6    8  .  .
Test Routines   5  7    8  .  .
Test Product    6  8    9  .  1
Finish           0  9    .  .  .
;

data softaux;
  set software;
  Chris = .;
  John = .;
  Tester1 = .;
  Tester2 = .;
run;

data resaux;
  input per date7. otype $ resid $ 18-27 Programmer Chris John
        Tester1 Tester2;
  format per date7.;
  datalines;
.      altrate Programmer  .  1  1  .  .
.      auxres  Chris       .  .  .  .5  .
.      auxres  John        .  .  .  .  .5
12apr04 reslevel .          .  1  1  1  1
;

```

**Output 4.27.1 Auxiliary Resources: Input Data Sets**

**Software Development**  
**Alternate and Auxiliary Resources**  
**Activity Data Set**

Obs	Activity	dur	act	s1	s2	Programmer	Chris	John	Tester1	Tester2
1	Plans & Reqts	2	1	2	3		1	.	.	.
2	Product Design	3	2	4	5		1	.	.	.
3	Test Plan	3	3	6	7		.	.	.	.
4	Documentation	3	4	9	.		1	.	.	.
5	Code	10	5	8	.		1	.	.	.
6	Test Data	5	6	8	.		.	.	.	.
7	Test Routines	5	7	8	.		.	.	.	.
8	Test Product	6	8	9	.		1	.	.	.
9	Finish	0	9	.	.		.	.	.	.

**Software Development**  
**Alternate and Auxiliary Resources**  
**Resource Data Set**

Obs	per	otype	resid	Programmer	Chris	John	Tester1	Tester2
1	.	altrate	Programmer	.	1	1	.	.
2	.	auxres	Chris	.	.	.	0.5	.
3	.	auxres	John	.	.	.	.	0.5
4	12APR04	reslevel		.	1	1	1.0	1.0

The following statements invoke PROC CPM with the appropriate data sets and resource variables. The resulting schedule is printed in [Output 4.27.2](#). Note the auxiliary resources that have been included in the schedule corresponding to each primary resource: Tester1 whenever Chris is used, and Tester2 whenever John is allocated.

```

proc cpm data=softaux out=sftaux rsched=rsftaux resin=resaux
    date='12apr04'd interval=weekday resout=raux;
    act act;
    succ s1 s2;
    dur dur;
    res Programmer Chris John Tester1 Tester2 /
        obstype=otype
        period=per resid=resid
        multalt rschedid=Activity;
    id Activity;
run;

```

**Output 4.27.2 Auxiliary Resources: Resource Schedule Data Set****Software Development: Alternate and Auxiliary Resources****Resource Schedule Data Set**

Activity	act	RESOURCE	DUR_TYPE	dur	_WORK_	R_RATE	S_START	S_FINISH
Plans & Reqts	1			2	.	.	12APR04	13APR04
Plans & Reqts	1	Programmer	FIXED	2	.	1.0	.	.
Plans & Reqts	1	Tester1	FIXED	2	.	0.5	12APR04	13APR04
Plans & Reqts	1	Chris	FIXED	2	.	1.0	12APR04	13APR04
Product Design	2			3	.	.	14APR04	16APR04
Product Design	2	Programmer	FIXED	3	.	1.0	.	.
Product Design	2	Tester1	FIXED	3	.	0.5	14APR04	16APR04
Product Design	2	Chris	FIXED	3	.	1.0	14APR04	16APR04
Test Plan	3			3	.	.	14APR04	16APR04
Documentation	4			3	.	.	19APR04	21APR04
Documentation	4	Programmer	FIXED	3	.	1.0	.	.
Documentation	4	Tester2	FIXED	3	.	0.5	19APR04	21APR04
Documentation	4	John	FIXED	3	.	1.0	19APR04	21APR04
Code	5			10	.	.	19APR04	30APR04
Code	5	Programmer	FIXED	10	.	1.0	.	.
Code	5	Tester1	FIXED	10	.	0.5	19APR04	30APR04
Code	5	Chris	FIXED	10	.	1.0	19APR04	30APR04
Test Data	6			5	.	.	19APR04	23APR04
Test Routines	7			5	.	.	19APR04	23APR04
Test Product	8			6	.	.	03MAY04	10MAY04
Test Product	8	Programmer	FIXED	6	.	1.0	.	.

Activity	E_START	E_FINISH	L_START	L_FINISH
Plans & Reqts	12APR04	13APR04	12APR04	13APR04
Plans & Reqts	12APR04	13APR04	12APR04	13APR04
Plans & Reqts	.	.	.	.
Plans & Reqts	.	.	.	.
Product Design	14APR04	16APR04	14APR04	16APR04
Product Design	14APR04	16APR04	14APR04	16APR04
Product Design	.	.	.	.
Product Design	.	.	.	.
Test Plan	14APR04	16APR04	21APR04	23APR04
Documentation	19APR04	21APR04	06MAY04	10MAY04
Documentation	19APR04	21APR04	06MAY04	10MAY04
Documentation	.	.	.	.
Documentation	.	.	.	.
Code	19APR04	30APR04	19APR04	30APR04
Code	19APR04	30APR04	19APR04	30APR04
Code	.	.	.	.
Code	.	.	.	.
Test Data	19APR04	23APR04	26APR04	30APR04
Test Routines	19APR04	23APR04	26APR04	30APR04
Test Product	03MAY04	10MAY04	03MAY04	10MAY04
Test Product	03MAY04	10MAY04	03MAY04	10MAY04

**Output 4.27.2** *continued***Software Development: Alternate and Auxiliary Resources****Resource Schedule Data Set**

Activity	act	RESOURCE	DUR_TYPE	dur	_WORK_	R_RATE	S_START	S_FINISH
Test Product	8	Tester1	FIXED	6	.	0.5	03MAY04	10MAY04
Test Product	8	Chris	FIXED	6	.	1.0	03MAY04	10MAY04
Finish	9			0	.	.	11MAY04	11MAY04

Activity	E_START	E_FINISH	L_START	L_FINISH				
Test Product	.	.	.	.				
Test Product	.	.	.	.				
Finish	11MAY04	11MAY04	11MAY04	11MAY04				

**Example 4.28: Use of the SETFINISHMILESTONE Option**

A simple activity network is used to illustrate the use of the SETFINISHMILESTONE option in a couple of different scenarios.

The following DATA step reads the project network in AON format into a SAS data set named tasks. The data set (printed in Output 4.28.1) contains an Activity variable (act), a Successor variable (succ), a Lag variable (lag), and a Duration variable (dur). There are several milestones linked to other activities through different types of precedence constraints. The data set also contains some alignment constraints as specified by the variables target and trgttype. The treatment of the milestones will vary depending on the presence or absence of the alignment constraints. The data set also contains two variables that indicate the expected early schedule dates for the milestones corresponding to two different invocations of PROC CPM: the variable notrgtmd corresponds to the non-aligned schedule and the variable miledate corresponds to an invocation with the ALIGNDATE statement (the values for these variables are explained later).

```

data tasks;
  format act $7. succ $7. lag $4. target date7.
    trgttype $3. miledate date7. notrgtmd date7. ;
  input act & succ & lag $ dur target & date7.
    trgttype $ miledate & date7. notrgtmd & date7. ;
  datalines;
Task 0  Mile 1  ss_0 1 26Jan04  SGE .
Mile 1  Task 2  . 0 . . 26Jan04 26Jan04
Task 2  . . 1 . . .
Task 3  Mile 4  . 1 . . .
Mile 4  . . 0 . . 26Jan04 26Jan04
Task 5  Mile 6  . 1 . . .
Mile 6  Mile 7  FS_1 0 . . 26Jan04 26Jan04
Mile 7  . . 0 . . 27Jan04 27Jan04
Task 8  Mile 9  SS_3 1 . .
Mile 9  Mile 10 . 0 . . 29Jan04 29Jan04
Mile 10 . . 0 . . 29Jan04 29Jan04
Task 11 Mile 12 . 2 . . .
Mile 12 Mile 13  FS_1 0 28Jan04  SGE 28Jan04 27Jan04
Mile 13 . . 0 . . 29Jan04 28Jan04
;

```

#### Output 4.28.1 Input Data Set

#### Schedule with option SETFINISHMILESTONE Input Data Set

Obs	act	succ	lag	target	trgttype	miledate	notrgtmd	dur
1	Task 0	Mile 1	ss_0	26JAN04	SGE	.	.	1
2	Mile 1	Task 2	.	.	.	26JAN04	26JAN04	0
3	Task 2	.	.	.	.	.	.	1
4	Task 3	Mile 4	.	.	.	.	.	1
5	Mile 4	.	.	.	26JAN04	26JAN04	0	
6	Task 5	Mile 6	.	.	.	.	.	1
7	Mile 6	Mile 7	FS_1	.	.	26JAN04	26JAN04	0
8	Mile 7	.	.	.	27JAN04	27JAN04	0	
9	Task 8	Mile 9	SS_3	.	.	.	.	1
10	Mile 9	Mile 10	.	.	29JAN04	29JAN04	0	
11	Mile 10	.	.	.	29JAN04	29JAN04	0	
12	Task 11	Mile 12	.	.	.	.	.	2
13	Mile 12	Mile 13	FS_1	28JAN04	SGE	28JAN04	27JAN04	0
14	Mile 13	.	.	.	29JAN04	28JAN04	0	

**Output 4.28.2 Default Schedule****Schedule with option SETFINISHMILESTONE  
Default Schedule**

			n	E	E	L	L	T	F	
O	a	u	d	I	t	A	I	A	I	
b	c	c	u	a	m	R	S	R	S	
s	t	c	r	g	d	T	H	T	H	
1	Task 0	Mile 1	1	ss_0	.	26JAN04	26JAN04	28JAN04	28JAN04	2 0
2	Mile 1	Task 2	0		26JAN04	26JAN04	26JAN04	28JAN04	28JAN04	2 0
3	Task 2		1		.	26JAN04	26JAN04	28JAN04	28JAN04	2 2
4	Task 3	Mile 4	1		.	26JAN04	26JAN04	28JAN04	28JAN04	2 0
5	Mile 4		0		26JAN04	27JAN04	27JAN04	29JAN04	29JAN04	2 2
6	Task 5	Mile 6	1		.	26JAN04	26JAN04	27JAN04	27JAN04	1 0
7	Mile 6	Mile 7	0	FS_1	26JAN04	27JAN04	27JAN04	28JAN04	28JAN04	1 0
8	Mile 7		0		27JAN04	28JAN04	28JAN04	29JAN04	29JAN04	1 1
9	Task 8	Mile 9	1	SS_3	.	26JAN04	26JAN04	26JAN04	26JAN04	0 0
10	Mile 9	Mile 10	0		29JAN04	29JAN04	29JAN04	29JAN04	29JAN04	0 0
11	Mile 10		0		29JAN04	29JAN04	29JAN04	29JAN04	29JAN04	0 0
12	Task 11	Mile 12	2		.	26JAN04	27JAN04	26JAN04	27JAN04	0 0
13	Mile 12	Mile 13	0	FS_1	27JAN04	28JAN04	28JAN04	28JAN04	28JAN04	0 0
14	Mile 13		0		28JAN04	29JAN04	29JAN04	29JAN04	29JAN04	0 0

First, the CPM procedure is invoked with the default treatment of milestones. The resulting schedule is printed in [Output 4.28.2](#). Note the dates for the milestones. Compare these dates with the values of the early finish dates of the immediate predecessors.

The default behavior of the CPM procedure defines the start times for milestones to be at the beginning of the day after the predecessor task (with a standard FS\_0 relationship) ends. Thus, for example, the activity, ‘Mile 4’ has E\_START=27JAN04 because its predecessor, ‘Task 3’, has E\_FINISH=26JAN04. The interpretation for these dates are that the early finish corresponds to the end of the day, while the early start of the milestone ‘Mile 4’ corresponds to the beginning of the day. However, in some situations you may want the milestone to be scheduled at the same time as the end of the predecessor activity. In other words, you may wish the early start time of the milestone ‘Mile 4’ to be displayed as 26JAN04, with the interpretation that this time actually denotes the end of the day, rather than the beginning. See the section “[Finish Milestones](#)” on page 98 for details about the treatment of milestones. In the current example, the variable notrgtmd contains the desired milestone schedule dates corresponding to this special treatment of milestones. To obtain these desired dates, you must use the SETFINISHMILESTONE option.

```

/* Schedule the project */
proc cpm data=tasks out=out0
    collapse interval=day
    date='26jan04'd;
activity act;
successor succ /lag=(lag);
duration dur;
id lag notrgtmd;
run;

title2 'Default Schedule';
proc print; run;

```

Next, the CPM procedure is invoked with the option SETFINISHMILESTONE and the resulting schedule is printed in [Output 4.28.3](#). Not all milestones are defined to denote the end of the displayed date; such milestones are referred to as finish milestone. The variables EFINMILE and LFINMILE indicate if the milestone is a finish milestone or not, corresponding to the early or late schedule, respectively. For example, the milestone ‘Mile 12’ has E\_FINISH = 27JAN04 and the value of EFINMILE is ‘1’, indicating that the activity finishes at the end of the day on January 27, 2004. The milestone ‘Mile 13’ (with a finish-to-start lag of 1 day) finishes at the end of the day on January 28, 2004. In fact, as the late finish schedule indicates, the value of L\_FINISH for ‘Mile 13’ (and the project finish time) is the end of the day on 28JAN04. Both the variables EFINMILE and LFINMILE have the same values for all the activities in this example.

```

proc cpm data=tasks out=out1
    collapse interval=day
    date='26jan04'd
    setfinishmilestone;
activity act;
successor succ /lag=(lag);
duration dur;
id lag notrgtmd;
run;

title 'Schedule with option SETFINISHMILESTONE';
title2 'No Target Dates';
proc print heading=v;
id act;
var succ lag dur notrgtmd e_start e_finish
    l_start l_finish efinmile lfinmile;
run;

```

**Output 4.28.3** Schedule with SETFINISHMILESTONE Option

**Schedule with option SETFINISHMILESTONE**  
**No Target Dates**

		n o t r s a c t	E -	L -	L F	E I	L N	E M	L M
		s u c g	g l a r	t d u m t d	A I R S A H	I N R S I T	A T R S I H	I N S L I E	I I L L I E
<b>Task 0</b>	Mile 1	ss_0	1	.	26JAN04	26JAN04	28JAN04	28JAN04	..
<b>Mile 1</b>	Task 2		0	26JAN04	26JAN04	26JAN04	28JAN04	28JAN04	..
<b>Task 2</b>			1	.	26JAN04	26JAN04	28JAN04	28JAN04	..
<b>Task 3</b>	Mile 4		1	.	26JAN04	26JAN04	28JAN04	28JAN04	..
<b>Mile 4</b>			0	26JAN04	26JAN04	26JAN04	28JAN04	28JAN04	1 1
<b>Task 5</b>	Mile 6		1	.	26JAN04	26JAN04	27JAN04	27JAN04	..
<b>Mile 6</b>	Mile 7	FS_1	0	26JAN04	26JAN04	26JAN04	27JAN04	27JAN04	1 1
<b>Mile 7</b>			0	27JAN04	27JAN04	27JAN04	28JAN04	28JAN04	1 1
<b>Task 8</b>	Mile 9	SS_3	1	.	26JAN04	26JAN04	26JAN04	26JAN04	..
<b>Mile 9</b>	Mile 10		0	29JAN04	29JAN04	29JAN04	29JAN04	29JAN04	..
<b>Mile 10</b>			0	29JAN04	29JAN04	29JAN04	29JAN04	29JAN04	..
<b>Task 11</b>	Mile 12		2	.	26JAN04	27JAN04	26JAN04	27JAN04	..
<b>Mile 12</b>	Mile 13	FS_1	0	27JAN04	27JAN04	27JAN04	27JAN04	27JAN04	1 1
<b>Mile 13</b>			0	28JAN04	28JAN04	28JAN04	28JAN04	28JAN04	1 1

The next invocation of CPM illustrates the effect of alignment constraints on the milestones. As explained in the section “Finish Milestones” on page 98, imposing an alignment constraint of type SGE on a milestone may change it from a finish milestone to a start milestone (default behavior) as far as the early schedule of the project is concerned. In the following program, the CPM procedure is invoked with the SETFINISHMILESTONE option and the ALIGNDATE and ALIGNTYPE statements. The resulting schedule is printed in [Output 4.28.4](#). The early schedule of the milestones should now correspond to the values in the variable miledate. Note also that the activities ‘Mile 12’ and ‘Mile 13’ are no longer finish milestones, as indicated by missing values for the variable EFINMILE. The ‘SGE’ alignment constraint with a target date of 28JAN04 moves the milestone ‘Mile 12’ to the beginning of January 28, 2004, instead of the end of January 27, 2004.

```
proc cpm data=tasks out=out2
  collapse
  interval=day
  date='26jan04'd
  setfinishmilestone;
  activity act;
  successor succ /lag=(lag);
  duration dur;
  aligndate target;
  aligntype trgtype;
  id target trgtype lag miledate;
run;
```

```

title 'Schedule with option SETFINISHMILESTONE';
title2 'Target Dates change Early Schedule for some Milestones';
proc print heading=v;
  id act;
  var succ lag target trgttype miledate e_start e_finish
      l_start l_finish efinmile lfinmile;
run;

```

#### Output 4.28.4 Effect of Alignment Constraints

### Schedule with option SETFINISHMILESTONE Target Dates change Early Schedule for some Milestones

		t	m	E		L	E L
		r	i	-	L	-	F F
	t	g	l	F		F	I I
	a	t	e	S	I	S	N N
	s	r	t	T	N	T	M M
a	u	l	g	A	I	A	I I I
c	c	a	e	P	R	S	L L
t	c	g	t	T	H	T	E E
<b>Task 0</b>	Mile 1	ss_0	26JAN04	SGE	. 26JAN04	26JAN04	28JAN04 28JAN04 . .
<b>Mile 1</b>	Task 2		.		26JAN04 26JAN04 26JAN04 28JAN04 28JAN04 . .		
<b>Task 2</b>			.		26JAN04 26JAN04 28JAN04 28JAN04 . .		
<b>Task 3</b>	Mile 4		.		26JAN04 26JAN04 28JAN04 28JAN04 . .		
<b>Mile 4</b>			.	26JAN04 26JAN04 26JAN04 28JAN04 28JAN04	1 1		
<b>Task 5</b>	Mile 6		.		26JAN04 26JAN04 27JAN04 27JAN04 . .		
<b>Mile 6</b>	Mile 7 FS_1		.	26JAN04 26JAN04 26JAN04 27JAN04 27JAN04	1 1		
<b>Mile 7</b>			.	27JAN04 27JAN04 27JAN04 28JAN04 28JAN04	1 1		
<b>Task 8</b>	Mile 9 SS_3		.		26JAN04 26JAN04 26JAN04 26JAN04 . .		
<b>Mile 9</b>	Mile 10		.	29JAN04 29JAN04 29JAN04 29JAN04 29JAN04	. .		
<b>Mile 10</b>			.	29JAN04 29JAN04 29JAN04 29JAN04 29JAN04	. .		
<b>Task 11</b>	Mile 12		.		26JAN04 27JAN04 26JAN04 27JAN04 . .		
<b>Mile 12</b>	Mile 13 FS_1 28JAN04 SGE	28JAN04	28JAN04 28JAN04 27JAN04 27JAN04 . 1				
<b>Mile 13</b>		.	29JAN04 29JAN04 29JAN04 28JAN04 28JAN04	. 1			

The interpretation of the start and finish times for a milestone depends on whether it is a start milestone or a finish milestone. By default, all milestones are start milestones and are assumed to be scheduled at the beginning of the date specified in the start or finish time variable. As such, PROC GANTT displays these milestones at the start of the corresponding days on the Gantt chart. However, if a milestone is a finish milestone then it may not be displayed correctly on the Gantt chart, depending on the scale of the display.

In this example, PROC GANTT is used to display the schedule produced in Output 4.28.4. Recall that the schedule is saved in the data set out2. First, PROC GANTT is invoked without any modifications to the schedule data set. The resulting Gantt chart is displayed in Output 4.28.5. The finish milestones (with values of EFINMILE = '1') are not plotted correctly. For example, 'Mile 6' is plotted at the *beginning* instead of the *end* of the schedule bar for the predecessor activity, 'Act 5'. To correct this problem, you can adjust the schedule variables for the finish milestones and plot the new values, as illustrated by the second invocation of PROC GANTT. The corrected Gantt chart is displayed in Output 4.28.6.

```


title h=1.5 'Schedule with option SETFINISHMILESTONE and ALIGNDATE';
title2 'Gantt Chart of Early Schedule without adjustment';
proc gantt data=out2(drop=l_:)];
  chart / compress act=act succ=succ lag=lag
    scale=7 height=1.7
    cprec=cyan cmile=magenta
    caxis=black
    dur=dur nojobnum nolegend;
  id act succ lag e_start efinmile;
run;


/* Save adjusted E_START and E_FINISH times for finish
milestones */
data temp;
set out2;
format estart efinish date7.;
estart = e_start;
efinish = e_finish;
if efinmile then do;
  estart=estart+1;
  efinish=efinish+1;
end;
run;

/* Plot the adjusted start and finish times for the
early schedule */
title h=1.5 'Schedule with option SETFINISHMILESTONE and ALIGNDATE';
title2 'Gantt Chart of Early Schedule after adjustment';
proc gantt data=temp(drop=l_:)];
  chart / compress act=act succ=succ lag=lag
    scale=7 height=1.7
    es=estart ef=efinish
    cprec=cyan cmile=magenta
    caxis=black
    dur=dur nojobnum nolegend;
  id act succ lag e_start efinmile;
run;

```

### Output 4.28.5 Gantt Chart of Unadjusted Schedule

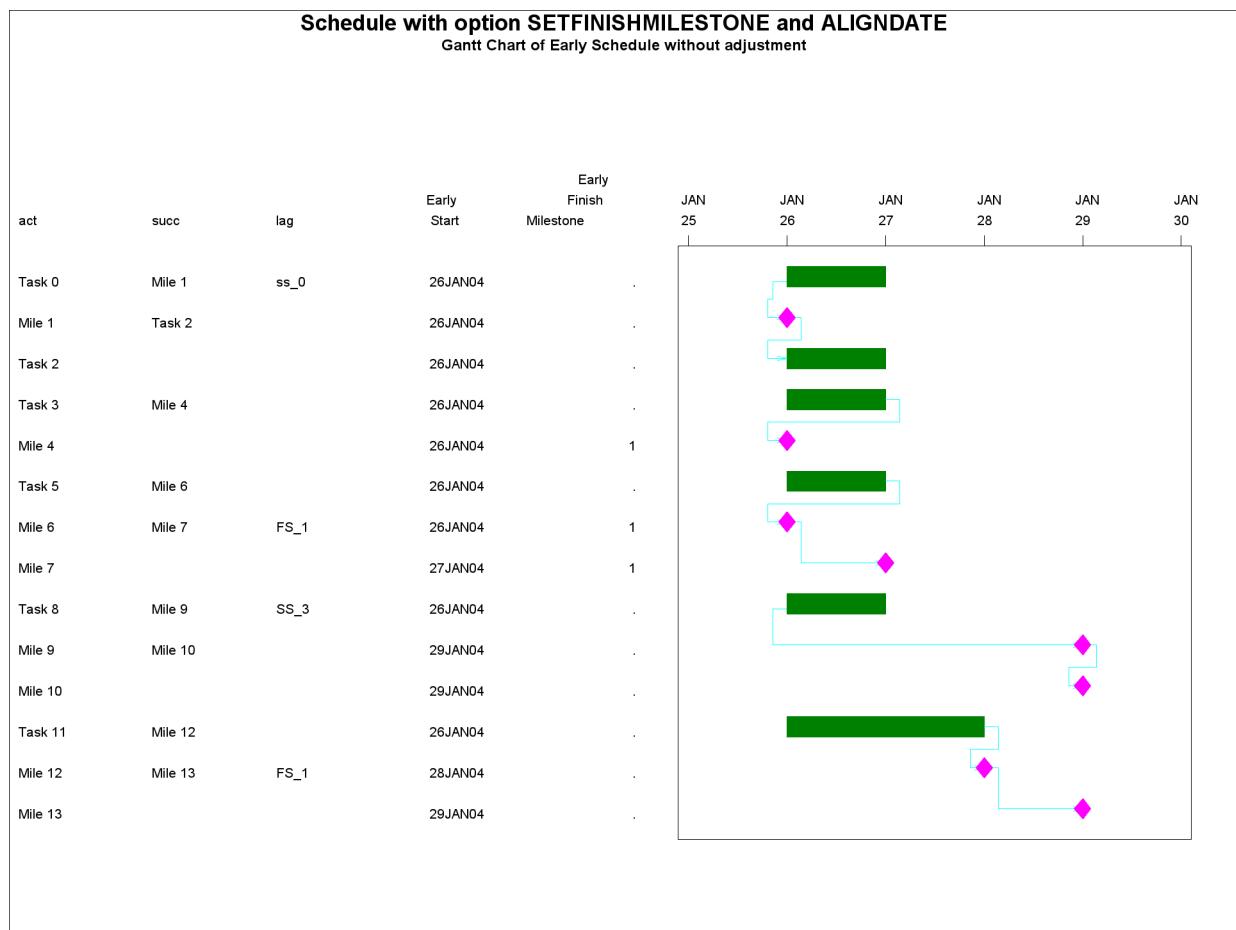

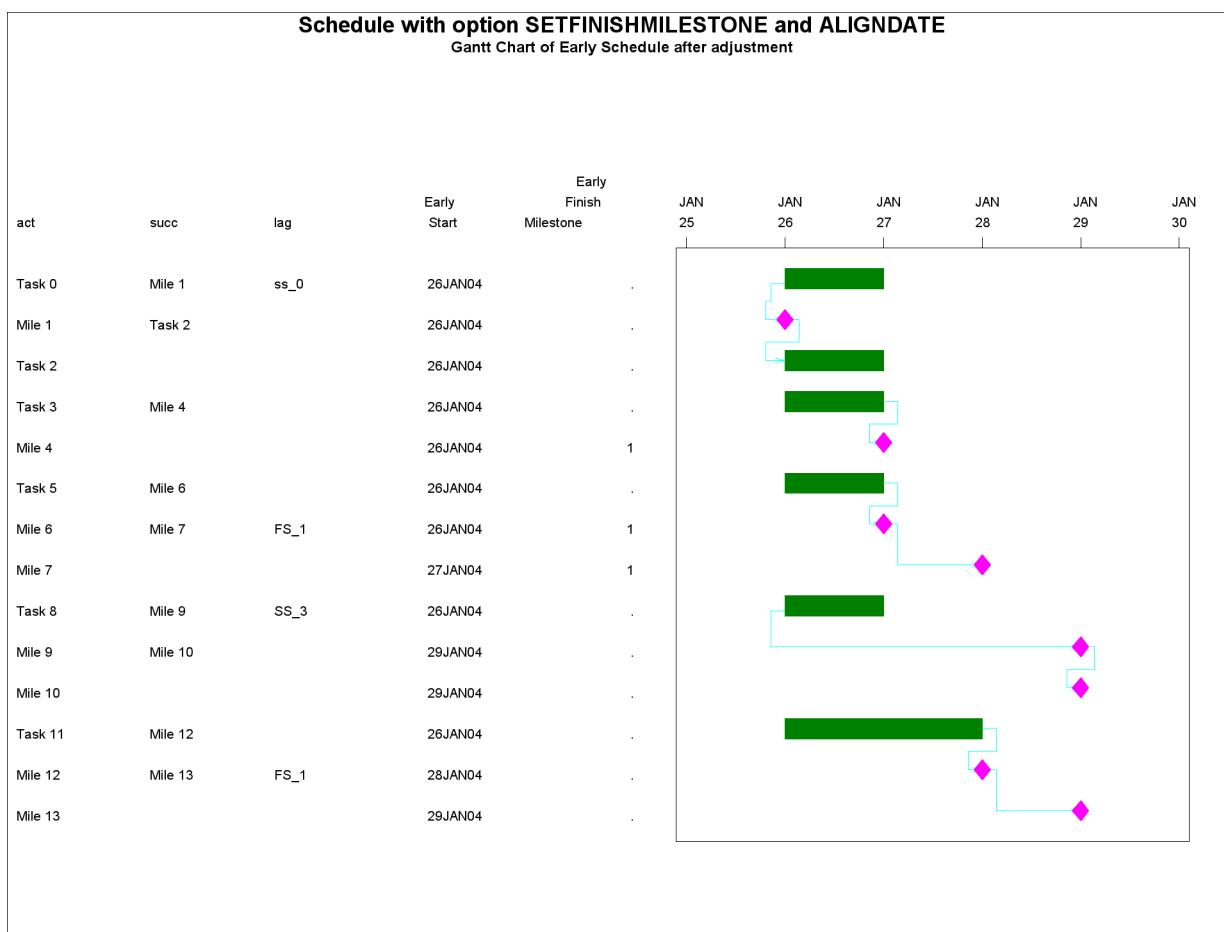**Output 4.28.6** Gantt Chart of Adjusted Schedule**Example 4.29: Negative Resource Requirements**

This example illustrates the use of negative resource requirements and the MILESTONERESOURCE option. Consider the production of boxed greeting cards that need to be shipped on trucks with a given capacity. Suppose there are three trucks with a capacity of 10,000 boxes of cards each. Suppose also that the boxes are produced at the rate of 5,000 boxes a day by the box-creating activity, ‘First Order’ with a duration of 6 days, and requiring the use of a machine, say resource Mach1. The activity data set OneOrder, displayed in [Output 4.29.1](#), represents the activities that are to be scheduled. The “Schedule Truck  $i$ ” task ( $i = 1, 2, 3$ ) is represented as a milestone to denote the point in time when the required number of boxes are available from the production line. The variable numboxes denotes the number of boxes that are produced by the machine, or delivered by the trucks. The Resource data set OneMachine, displayed in [Output 4.29.2](#), defines the resource numboxes as a consumable resource and the resources Mach1 and trucks as replenishable resources.

**Output 4.29.1** Activity Data Set**Negative Resource Requirements  
Activity Data Set OneOrder**

Obs	Activity	succ	Duration	Mach1	numboxes	trucks
1	First Order		6	1	-5000	.
2	Sched truck1	Delivery 1	0	.	10000	.
3	Sched truck2	Delivery 2	0	.	10000	.
4	Sched truck3	Delivery 3	0	.	10000	.
5	Delivery 1		2	.	.	1
6	Delivery 2		2	.	.	1
7	Delivery 3		2	.	.	1

**Output 4.29.2** Resource Data Set**Negative Resource Requirements  
Resource Data Set OneMachine**

Obs	per	obstype	Mach1	numboxes	trucks
1	.	restype	1	2	1
2	15AUG04	reslevel	1	.	1

The following statements invoke the CPM procedure to schedule the production of the boxed greeting cards. The option MILESTONERESOURCE indicates that milestones can consume resources. In this case, the milestones representing the scheduling of the trucks are scheduled only when 10,000 boxes of greeting cards are available. The resulting schedule is displayed in Output 4.29.3 using PROC GANTT, and the resource usage data set is displayed in Output 4.29.4.

```

proc cpm data=OneOrder resin=OneMachine
  out=OneSched rsched=OneRsch resout=OneRout
  date='15aug04'd;
  act      activity;
  succ     succ;
  duration duration;
  resource Mach1 numboxes trucks / period=per
    obstype=obstype
    milestonesource;
run;

proc sort data=OneSched;
  by s_start;
run;

title  h=2 'Negative Resource Requirements';
title2 h=1.5   'Truck Schedule';
proc gantt data=OneSched (drop=e_:_ l_:_);
  chart / act=activity succ=succ duration=duration
    cmile=red

```


```

cprec=blue height=1.8
nolegend nojobnum;
id activity duration;
run;

title2 'Resource Usage Data Set';
proc print data=OneRout;
id _time_;
run;

```

Output 4.29.3 Gantt Chart of Schedule

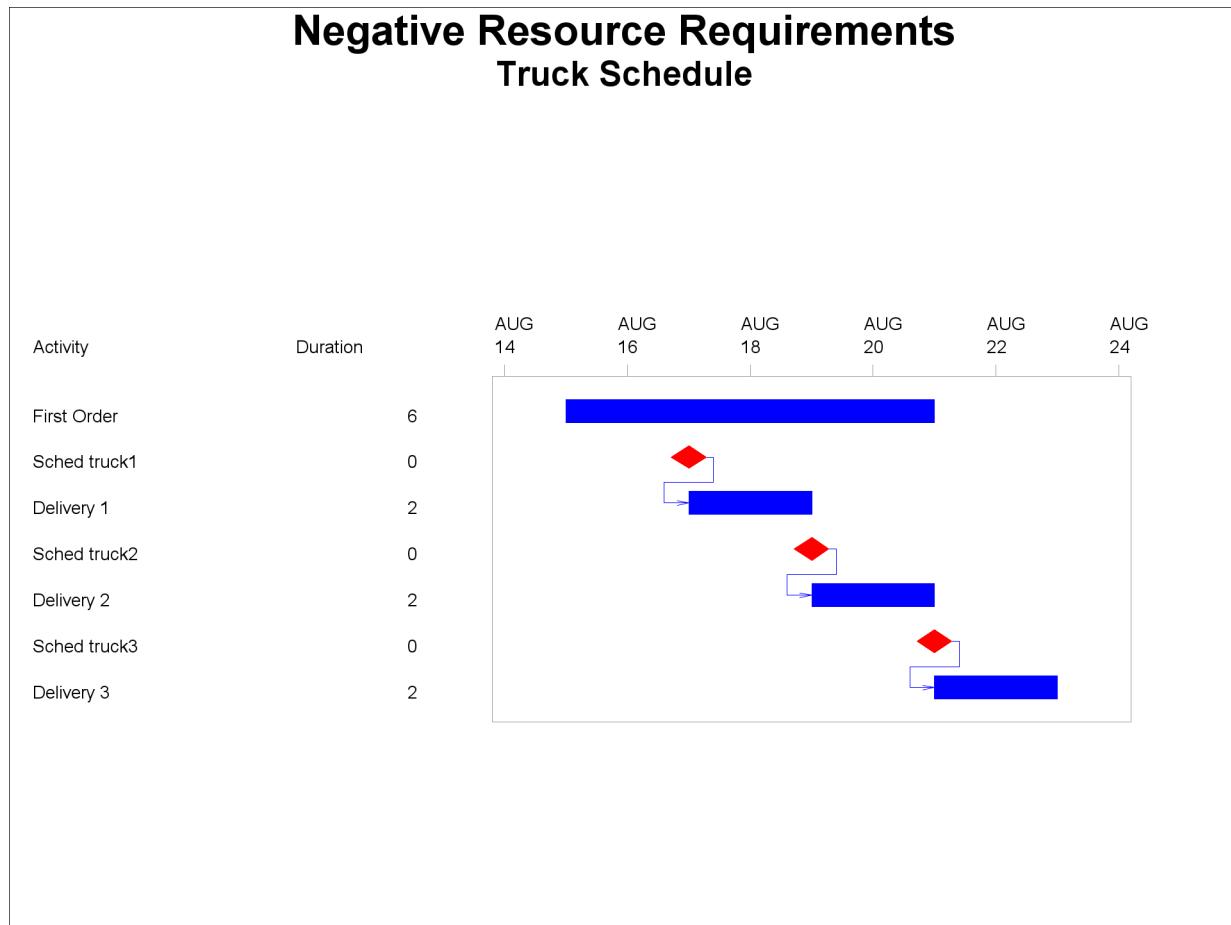

The resulting Gantt chart shows the schedule of the trucks, which is staggered according to the production rate of the machine that produces the cards. In other words, the trucks are scheduled at intervals of 2 days. The Resource Usage data set shows the production/consumption rate of the boxes for each day of the project.

#### Output 4.29.4 Resource Usage Data Set

##### Resource Usage Data Set

<u>_TIME_</u>	<u>EMach1</u>	<u>LMach1</u>	<u>RMach1</u>	<u>AMach1</u>	<u>Enumboxes</u>	<u>Lnumboxes</u>	<u>Rnumboxes</u>	<u>Anumboxes</u>
15AUG04	1	1	1	0	25000	-5000	-5000	0
16AUG04	1	1	1	0	-5000	-5000	-5000	5000
17AUG04	1	1	1	0	-5000	-5000	5000	10000
18AUG04	1	1	1	0	-5000	-5000	-5000	5000
19AUG04	1	1	1	0	-5000	25000	5000	10000
20AUG04	1	1	1	0	-5000	-5000	-5000	5000
21AUG04	0	0	0	1	0	0	10000	10000
22AUG04	0	0	0	1	0	0	0	0
23AUG04	0	0	0	1	0	0	0	0

<u>_TIME_</u>	<u>Etrucks</u>	<u>Ltrucks</u>	<u>Rtrucks</u>	<u>Atrucks</u>				
15AUG04	3	0	0	1				
16AUG04	3	0	0	1				
17AUG04	0	0	1	0				
18AUG04	0	0	1	0				
19AUG04	0	3	1	0				
20AUG04	0	3	1	0				
21AUG04	0	0	1	0				
22AUG04	0	0	1	0				
23AUG04	0	0	0	1				

---

## Example 4.30: Auxiliary Resources and Negative Requirements

This example extends the production scenario in the previous example to two separate orders of the greeting cards. Suppose also that the machine used in Example 4.29 is to be replaced by a faster machine that is scheduled to come on-line on August 24, 2004. This scheduling problem is modeled using alternate resources Mach1 and Mach2 for a primary resource Machine. Each of the alternate resources produces the auxiliary resource numboxes; the rate of production depends on which machine is used.

The Activity data set TwoOrders, displayed in Output 4.30.1, now contains additional activities corresponding to the second order of greeting cards. The resource requirement corresponding to the machine needed for the production is now represented in terms of the generic machine resource, Machine. The resource data set, TwoMachines, displayed in Output 4.30.2, specifies Mach1 and Mach2 as alternate resources for Machine and the resource numboxes as an auxiliary resource produced at the rate of 5,000 by Mach1 and 10,000 by Mach2. Observations 5 and 6 indicate that the first machine is available from August 15 and is then replaced by the second machine on August 24, 2004.

**Output 4.30.1 Activity Data Set****Auxiliary Resources  
Activity Data Set TwoOrder**

	A	D	n	-
c		u M	u	p
t		r a	m	t a
i		a c M M	b	r t
v		s t h a a	o	u t
O	i	u i i c c	x	c e
b	t	c o n h h	e	k r
s	y	c n e 1 2	s	s n
1	First Order	6 1 . . .	. . .	1
2	Sched truck1	Delivery 1 0 . . .	10000 .	1
3	Sched truck2	Delivery 2 0 . . .	10000 .	1
4	Sched truck3	Delivery 3 0 . . .	10000 .	1
5	Delivery 1	2 . . . .	. . .	1 1
6	Delivery 2	2 . . . .	. . .	1 1
7	Delivery 3	2 . . . .	. . .	1 1
8	Second Order	6 1 . . .	. . .	2
9	Sched truck4	Delivery 4 0 . . .	10000 .	2
10	Sched truck5	Delivery 5 0 . . .	10000 .	2
11	Sched truck6	Delivery 6 0 . . .	10000 .	2
12	Delivery 4	2 . . . .	. . .	1 2
13	Delivery 5	2 . . . .	. . .	1 2
14	Delivery 6	2 . . . .	. . .	1 2

**Output 4.30.2 Resource Data Set****Auxiliary Resources  
Resource Data Set TwoMachines**

Obs	per	obstype	resid	Machine	Mach1	Mach2	numboxes	trucks
1	.	restype		1	1	1	2	1
2	.	altrate	Machine	.	1	1	.	.
3	.	auxres	Mach1	.	.	.	-5000	.
4	.	auxres	Mach2	.	.	.	-10000	.
5	15AUG04	reslevel		.	1	.	.	3
6	24AUG04	reslevel		.	0	1	.	.

The following statements invoke the CPM procedure to schedule the production of the two orders of boxed greeting cards and display the schedule (in Output 4.30.3) using PROC GANTT. Note that PROC GANTT is invoked with the PATTERN= option indicating that the schedules should be drawn using the pattern statements corresponding to the variable \_pattern in the activity data set. In addition, the CTEXTCOLS= option indicates that the color of the text should match the color of the schedule bars.


```
proc cpm data=TwoOrders resin=TwoMachines
    out=TwoSched rsched=TwoRsched resout=TwoRout
    date='15aug04'd;
act      activity;
succ     succ;
duration duration;
resource Machine Mach1 Mach2 numboxes trucks / period=per
    obstype=obstype
    resid=resid
    milestonesresource;
id _pattern;
run;

proc sort data=TwoSched;
by s_start;
run;

pattern1 v=s c=red;
pattern2 v=s c=green;

title h=2 'Auxiliary Resources';
title2 h=1.5 'Truck Schedule: Fixed Activity Durations';
proc gantt data=TwoSched(drop=e_: 1:);
chart / act=activity succ=succ duration=duration
    nolegend nojobnum compress pattern=_pattern
    ctextcols=id cprec=blue scale=4 height=1.5;
id activity ;
run;

title2 'Resource Usage Data set: Fixed Activity Durations';
proc print data=TwoRout;
id _time_;
run;
```

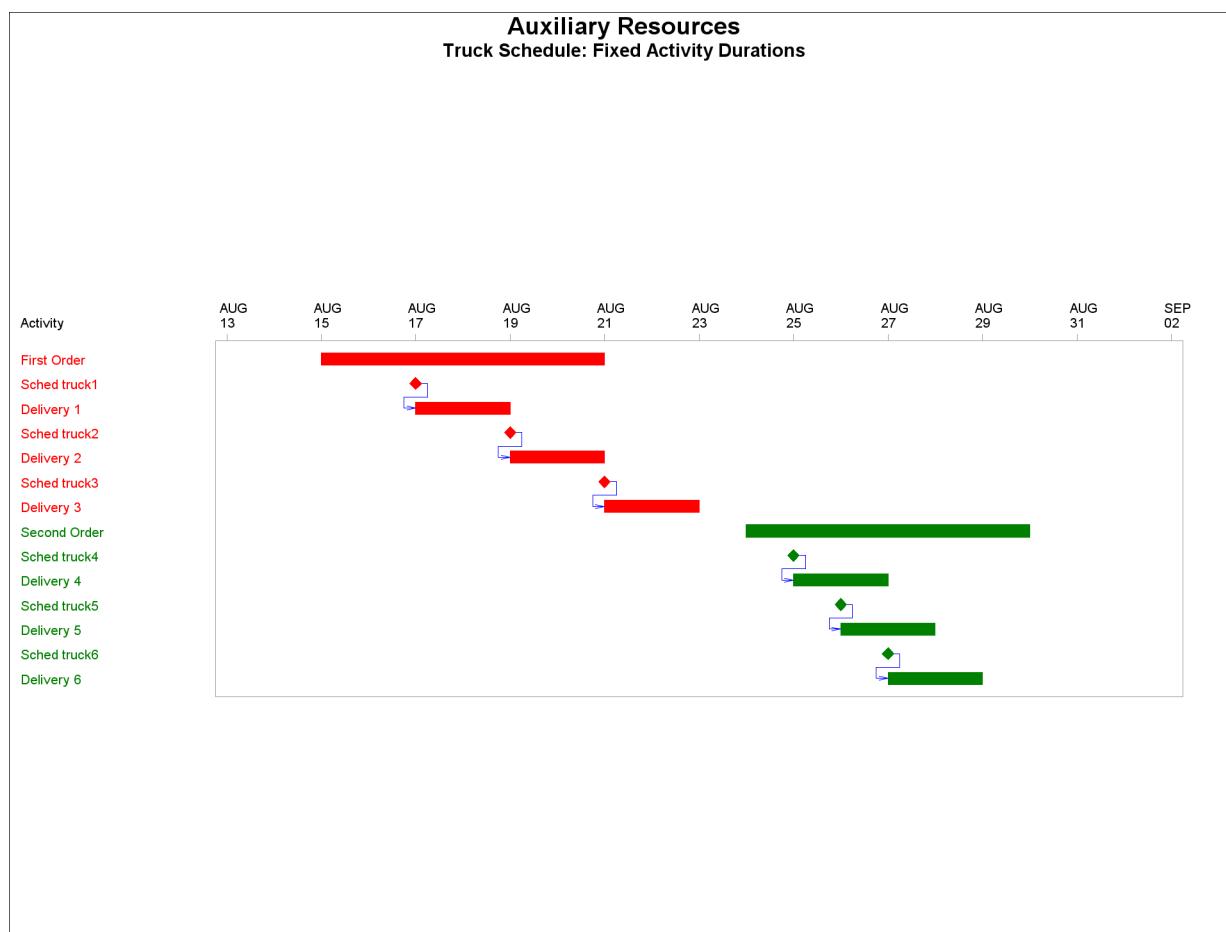**Output 4.30.3** Gantt Chart of Schedule

The Gantt chart shows that the trucks corresponding to the second order of greeting cards depart at a faster rate (every day) than the ones corresponding to the first order (every 2 days). The faster delivery is enabled by the use of the faster machine for the second order. Note also that the activity ‘Second Order’ continues for a total of 6 days, even though the order is filled within the first 3 days. This is due to the fact that the activity is defined to have a fixed duration. The resource usage data set, displayed in [Output 4.30.4](#) shows that 10,000 boxes are produced each day for 6 days, causing an inventory build up of 30,000 boxes at the end of the production schedule.

**Output 4.30.4** Resource Usage Data Set

**Auxiliary Resources**  
**Resource Usage Data set: Fixed Activity Durations**

_TIME_	EMachine	LMachine	RMachine	AMachine	EMach1	LMach1	RMach1	AMach1	EMach2	LMach2	RMach2
15AUG04	2	2	0	0	0	0	1	0	0	0	0
16AUG04	2	2	0	0	0	0	1	0	0	0	0
17AUG04	2	2	0	0	0	0	1	0	0	0	0
18AUG04	2	2	0	0	0	0	1	0	0	0	0
19AUG04	2	2	0	0	0	0	1	0	0	0	0
20AUG04	2	2	0	0	0	0	1	0	0	0	0
21AUG04	0	0	0	0	0	0	0	1	0	0	0
22AUG04	0	0	0	0	0	0	0	1	0	0	0
23AUG04	0	0	0	0	0	0	0	1	0	0	0
24AUG04	0	0	0	0	0	0	0	0	0	0	1
25AUG04	0	0	0	0	0	0	0	0	0	0	1
26AUG04	0	0	0	0	0	0	0	0	0	0	1
27AUG04	0	0	0	0	0	0	0	0	0	0	1
28AUG04	0	0	0	0	0	0	0	0	0	0	1
29AUG04	0	0	0	0	0	0	0	0	0	0	1
30AUG04	0	0	0	0	0	0	0	0	0	0	0

_TIME_	AMach2	Enumboxes	Lnumboxes	Rnumboxes	Anumboxes	Etrucks	Ltrucks	Rtrucks	Atrucks
15AUG04	0	60000	0	-5000	0	6	0	0	3
16AUG04	0	0	0	-5000	5000	6	0	0	3
17AUG04	0	0	0	5000	10000	0	0	1	2
18AUG04	0	0	0	-5000	5000	0	0	1	2
19AUG04	0	0	60000	5000	10000	0	6	1	2
20AUG04	0	0	0	-5000	5000	0	6	1	2
21AUG04	0	0	0	10000	10000	0	0	1	2
22AUG04	0	0	0	0	0	0	0	1	2
23AUG04	0	0	0	0	0	0	0	0	3
24AUG04	0	0	0	-10000	0	0	0	0	3
25AUG04	0	0	0	0	10000	0	0	1	2
26AUG04	0	0	0	0	10000	0	0	2	1
27AUG04	0	0	0	0	10000	0	0	2	1
28AUG04	0	0	0	-10000	10000	0	0	1	2
29AUG04	0	0	0	-10000	20000	0	0	0	3
30AUG04	1	0	0	0	30000	0	0	0	3

---

**Example 4.31: Resource-Driven Durations and Negative Requirements**

A more realistic model for the truck scheduling example can be built if the activities ‘First Order’ and ‘Second Order’ are defined to be resource driven. In other words, specify the total amount of work (6 days of work) that is needed from the activity at a pre-specified rate (of 5,000 boxes per day), and allow the choice of machine to dictate the duration of the activity. This modified model is illustrated by the activity data set, TwoOrdersRD, and resource data set, TwoMachinesRD, printed in [Output 4.31.1](#) and [Output 4.31.1](#), respectively. The two orders for greeting cards have a work specification of 6 days if the generic machine

Machine (which produces 5,000 boxes a day) is used. The resource data set has a new observation with value ‘resrcdur’ for the variable *obstype*. This observation specifies that the resources Machine, Mach1 and Mach2 drive the durations of activities that require them. The third observation in this data set specifies that the second machine is twice as fast as the first one, indicated by the fact that the alternate rate is 0.5. This implies that using the second machine will reduce the activity’s duration by 50 percent.

#### Output 4.31.1 Activity Data Set

##### Resource-Driven Durations Activity Data Set TwoOrdersRD

	A	D	n	
	c	u M	u	p
	t	r a	m	t a
	i	a c M M	b r t	
	v	s t w h a a	o u t	
O	i	u i o i c c	x c e	
b	t	c o r n h h	e k r	
s	y	c n k e 1 2	s s n	
<b>1</b>	First Order	1 6 1 . . .	. . . 1	
<b>2</b>	Sched truck1	Delivery 1 0 . . . .	10000 . 1	
<b>3</b>	Sched truck2	Delivery 2 0 . . . .	10000 . 1	
<b>4</b>	Sched truck3	Delivery 3 0 . . . .	10000 . 1	
<b>5</b>	Delivery 1	2 . . . . .	1 1	
<b>6</b>	Delivery 2	2 . . . . .	1 1	
<b>7</b>	Delivery 3	2 . . . . .	1 1	
<b>8</b>	Second Order	1 6 1 . . . .	. . . 2	
<b>9</b>	Sched truck4	Delivery 4 0 . . . .	10000 . 2	
<b>10</b>	Sched truck5	Delivery 5 0 . . . .	10000 . 2	
<b>11</b>	Sched truck6	Delivery 6 0 . . . .	10000 . 2	
<b>12</b>	Delivery 4	2 . . . . .	1 2	
<b>13</b>	Delivery 5	2 . . . . .	1 2	
<b>14</b>	Delivery 6	2 . . . . .	1 2	

#### Output 4.31.2 Resource Data Set

##### Resource-Driven Durations Resource Data Set TwoMachinesRD

Obs	per	obstype	resid	Machine	Mach1	Mach2	numboxes	trucks
<b>1</b>	.	resrcdur			1	1	1.0	.
<b>2</b>	.	restype			1	1	1.0	2 1
<b>3</b>	.	altrate	Machine		.	1	0.5	.
<b>4</b>	.	auxres	Mach1		.	.	-5000	.
<b>5</b>	.	auxres	Mach2		.	.	-10000	.
<b>6</b>	15AUG04	reslevel			.	1	.	3
<b>7</b>	24AUG04	reslevel			.	0	1.0	.

The following statements invoke PROC CPM with the additional specification of the WORK= option. Once again, the CPM procedure allocates one of the two machines for the production, depending on the availability. The Gantt chart is displayed in [Output 4.31.3](#) and the resource usage data set is printed in [Output 4.31.4](#). As before, the trucks for the first order depart every second day requiring a total of 6 days, while the second order is completed in 3 days. Also, using a resource-driven duration model allows the second activity to be completed in 3 days instead of 6 days, as in the previous example. The resource usage data set indicates that production is stopped as soon as the two orders are filled, avoiding excess inventory.

```

proc cpm data=TwoOrdersRD resin=TwoMachinesRD
  out=TwoSchedRD rsched=TwoRschedRD resout=TwoRoutRD
  date='15aug04'd;
  act      activity;
  succ     succ;
  duration duration;
  resource Machine Mach1 Mach2 numboxes trucks / period=per
    obstype=obstype
    resid=resid work=work
    milestonesresource;
  id _pattern;
  run;


proc sort data=TwoSchedRD;
  by s_start;
  run;

pattern1 v=s c=red;
pattern2 v=s c=green;

title h=2 'Resource-Driven Durations';
title2 h=1.5 'Truck Schedule';
proc gantt data=TwoSchedRD(drop=e_: 1:);
  chart / act=activity succ=succ duration=duration
    nolegend nojobnum compress pattern=_pattern
    ctextcols=id cprec=blue scale=4 height=1.4;
  id activity ;
  run;

title2 'Resource Usage Data Set';
proc print data=TwoRoutRD;
  id _time_;
  run;

```

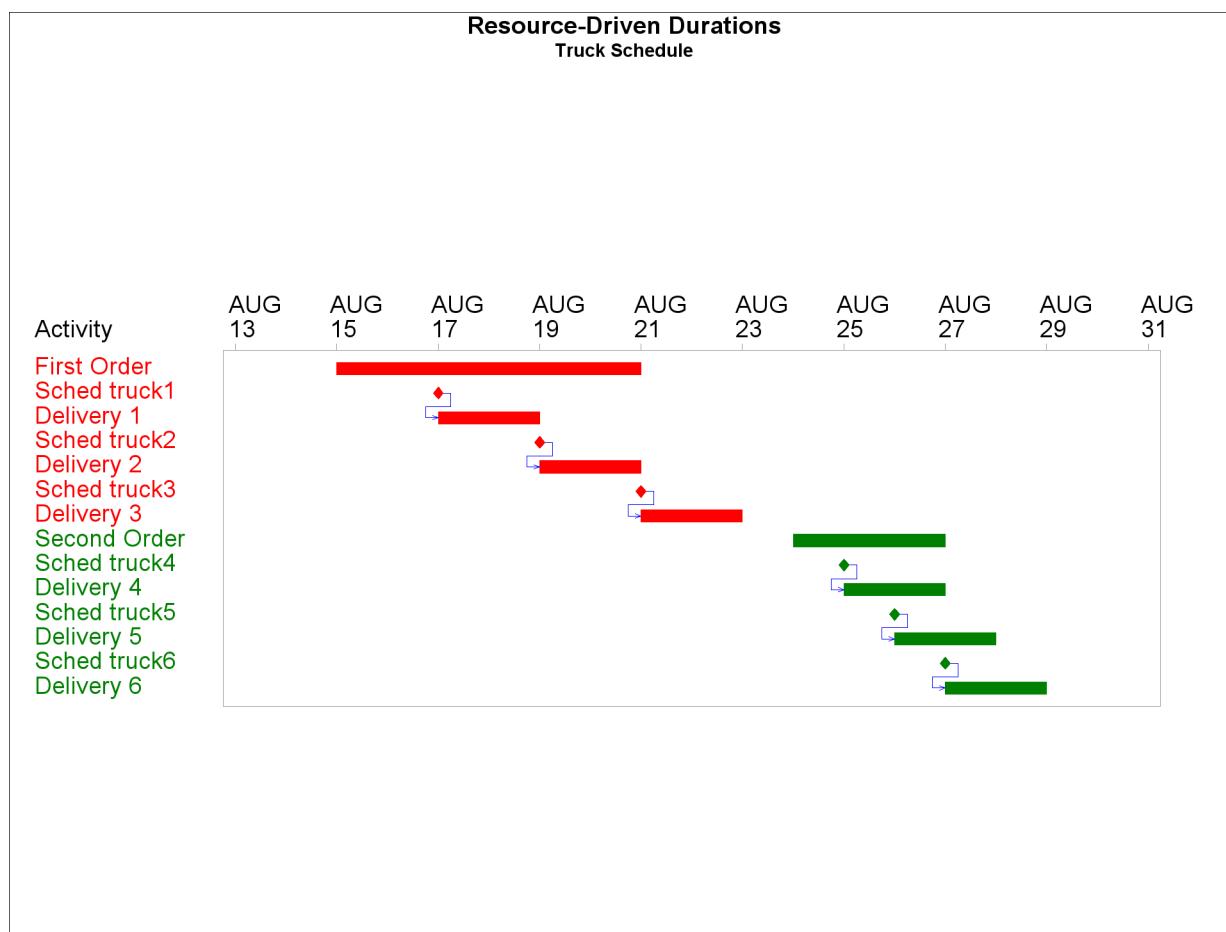**Output 4.31.3** Gantt Chart of Schedule

#### **Output 4.31.4** Resource Usage Data Set

## Resource-Driven Durations Resource Usage Data Set

## Statement and Option Cross-Reference Tables

The next two tables reference the statements and options in the CPM procedure that are illustrated by the examples in this section.

**Table 4.13** Statements and Options Specified in Examples 2.1–2.17

**Table 4.13** (continued)

REMDSUR=								X					
RESOURCEIN=									X	X	X	X	X
RESOURCEOUT=										X	X	X	X
ROUTNOBREAK											X		
SCHEDRULE=											X		
SET=												X	
SHOWFLOAT													X
TIMENOW=													X
WORKDATA=								X	X				
XFERVARS										X			

**Table 4.14** Statements and Options Specified in Examples 2.18–2.31

**Table 4.14** (continued)

ORDERALL	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
OUT=	X	X	X												
PERIOD=	X	X	X												
RCPROFILE	X	X	X												
RESID=			X												
RESOURCEIN=	X	X	X		X		X	X	X	X		X	X	X	X
RESOURCEOUT=	X	X	X				X	X	X	X		X	X	X	X
RESOURCESCHED=							X	X	X	X		X	X	X	X
ROUTNOBREAK															
RSCHEDID=							X	X	X	X					
SEPCRIT															
SET=	X														
SETFINISHMILESTONE							X					X			
STOPDATE=		X				X									
T_FLOAT							X								
USEPROJDUR								X	X	X					
WORK=															X

## References

- Davis, E. W. (1973). "Project Scheduling under Resource Constraints: Historical Review and Categorization of Procedures." *AIIE Transactions* 5:297–313.
- Elmaghraby, S. E. (1977). *Activity Networks: Project Planning and Control by Network Models*. New York: John Wiley & Sons.
- Horowitz, E., and Sahni, S. (1976). *Fundamentals of Data Structures*. Potomac, MD: Computer Science Press.
- Kulkarni, R. (1991). "Scheduling with the CPM Procedure." In *Proceedings of the Sixteenth Annual SAS Users Group International Conference*, 700–714. Cary, NC: SAS Institute Inc. <http://www.sascommunity.org/sugi/SUGI91/Sugi-91-118%20Kulkarni.pdf>.
- Malcolm, D. G., Roseboom, J. H., Clark, C. E., and Fazar, W. (1959). "Applications of a Technique for R and D Program Evaluation (PERT)." *Operations Research* 7:646–669.
- Minieka, E. (1978). *Optimization Algorithms for Networks and Graphs*. New York: Marcel Dekker.
- Moder, J. J., Phillips, C. R., and Davis, E. W. (1983). *Project Management with CPM, PERT, and Precedence Diagramming*. New York: Van Nostrand Reinhold.
- SAS Institute Inc. (1993). *SAS/OR Software: Project Management Examples*. Cary, NC: SAS Institute Inc.
- Van Slyke, R. M. (1963). "Monte Carlo Methods and the PERT Problem." *Operations Research* 11:839–860.
- Wiest, J. D. (1967). "A Heuristic Model for Scheduling Large Projects with Limited Resources." *Management Science* 13:359–377.

# Chapter 5

## The PM Procedure

### Contents

---

Overview: PM Procedure . . . . .	301
Getting Started: PM Procedure . . . . .	302
Syntax: PM Procedure . . . . .	304
PROC PM Statement . . . . .	304
Details: PM Procedure . . . . .	307
User Interface Features . . . . .	307
Project Hierarchy . . . . .	309
Table View . . . . .	310
Gantt View . . . . .	313
Creating and Editing Projects . . . . .	318
Setting Activity Filters . . . . .	322
Saving and Restoring Preferences . . . . .	323
Sorting Activities . . . . .	324
Setting the Project Font . . . . .	325
Renumbering the Activities . . . . .	325
Printing . . . . .	325
Macro Variable TIMENOW . . . . .	326
Summary of Differences . . . . .	327
Examples: PM Procedure . . . . .	328
Example 5.1: Defining a New Project . . . . .	329
Example 5.2: Adding Subtasks to a Project . . . . .	334
Example 5.3: Saving and Comparing Baseline Schedules . . . . .	336
Example 5.4: Effect of Calendars . . . . .	340
Example 5.5: Defining Resources . . . . .	343
Example 5.6: Editing Progress . . . . .	347

---

### Overview: PM Procedure

The PM procedure is an interactive procedure that can be used for planning, controlling, and monitoring a project. The syntax and the scheduling features of PROC PM are virtually the same as those of the CPM procedure. However, because the PM procedure is interactive, there are a few extra options that are available and a few other options that have a default behavior that is different from the CPM procedure. These differences are noted in the section “[Syntax: PM Procedure](#)” on page 304 and the section “[Summary of Differences](#)” on page 327. One major difference is that only the Activity-On-Node representation of the

project is supported in PROC PM. In other words, TAILNODE and HEADNODE statements from PROC CPM are not supported.

For a complete description of the syntax and the scheduling algorithm for the CPM procedure, see Chapter 4, “[The CPM Procedure](#).”

When PROC PM is invoked with the activity network representation, an interactive window is opened that displays a [Table View](#) of the project on the left and a [Gantt View](#) of the project on the right. You can add activities and edit the project data by using the Table View. You can also use the Gantt View to move activities, change the durations of the activities, and add precedence constraints between the activities. These features are described in the section “[Details: PM Procedure](#)” on page 307.

The PM procedure is designed to facilitate its inclusion in a Project Management application, such as [PROJMAN](#). Any changes that are made to the activity network or to the activity durations, resource requirements, alignment specifications, and other activity information need to be saved in the resulting Schedule output data set. Further, you should be able to use this output data set as input to a future invocation of PROC PM and continue to manage the project. Thus, there are some differences in the design of the Schedule data set (defined in Chapter 4, “[The CPM Procedure](#)”) to enable the integration of PROC PM into a Project Management application. The differences between the Schedule data sets in the two procedures are described in the section “[Schedule Data Set](#)” on page 327.

## Getting Started: PM Procedure

Consider the simple software development project described in the “Getting Started” section of Chapter 4, “[The CPM Procedure](#).” Recall that the Activity data set, SOFTWARE, contains the activity descriptions, durations, and precedence constraints. The following statements (identical to the PROC CPM invocation) initialize the project data and invoke the PM procedure.


```
data software;
  input Descrpt $char20.
    Duration 23-24
    Activity $ 27-34
    Succesr1 $ 37-44
    Succesr2 $ 47-54;
  datalines;
Initial Testing      20  TESTING   RECODE
Prel. Documentation 15  PRELDOC  DOCEDREV QATEST
Meet Marketing       1   MEETMKT  RECODE
Recoding             5   RECODE    DOCEDREV QATEST
QA Test Approve     10  QATEST   PROD
Doc. Edit and Revise 10  DOCEDREV PROD
Production          1   PROD
;
```

```
proc pm data=software  
        out=introl  
        interval=day  
        date='01mar04'd;  
  
id descprt;  
activity activity;  
duration duration;  
successor succesr1 succesr2;  
  
run;
```

When you invoke the PM procedure, the PM window appears (see Figure 5.1), consisting of the Table View and the Gantt View of the project. The activities are listed in the order in which they are defined in the Activity data set. The two views are separated by a dividing line that can be dragged to the left or right, controlling the size of the two views. Further, the two views scroll together in the vertical direction but can scroll independently in the horizontal direction.

The Table View contains several editable columns (in white) that can be used to edit the project data as well as add new activities to the project. Some of the columns (in gray), such as the Schedule times, are not editable. The Gantt View contains a Gantt chart of the project and displays the precedence relationships between the activities. You can use the Gantt View to add or delete precedence constraints between activities and to change the durations or alignment constraints of the activities by dragging the schedule bars. Details of the interface are described in the section “[Details: PM Procedure](#)” on page 307.

## **Figure 5.1** Software Development Project

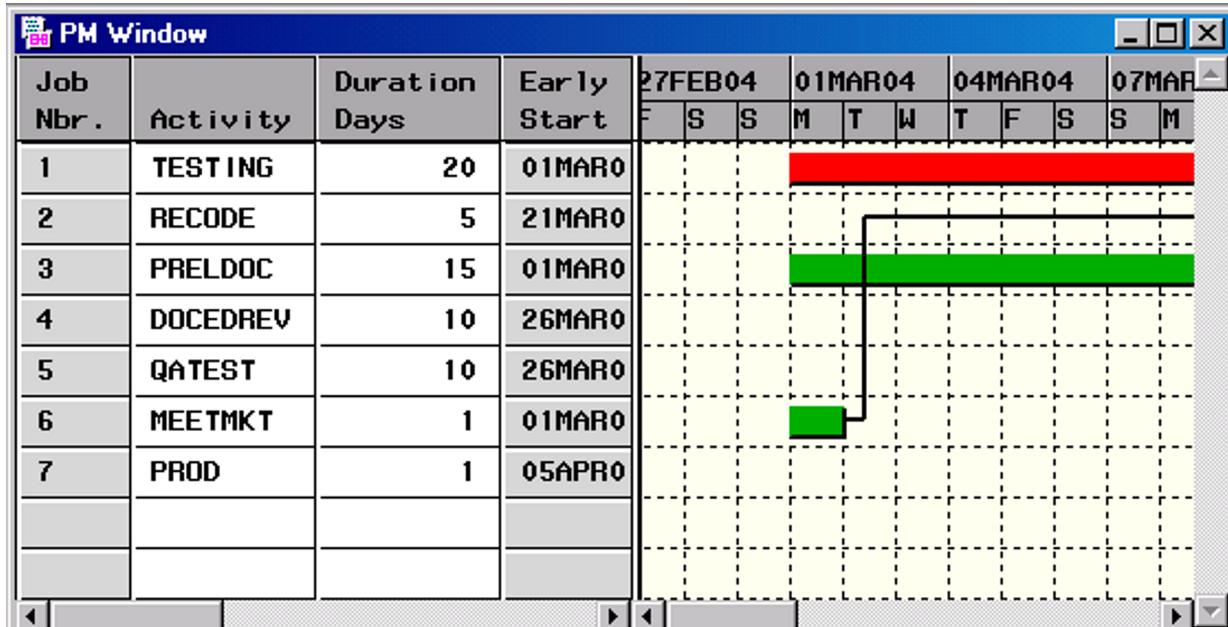

---

## Syntax: PM Procedure

The syntax for PROC PM is virtually identical to that for [PROC CPM](#). The main difference is that you replace the PROC CPM statement with the PROC PM statement.

The TAILNODE and HEADNODE statements from PROC CPM are not supported in PROC PM.

The form of the PROC PM statement is

**PROC PM** *options* ;

---

### PROC PM Statement

**PROC PM** *options* ;

All the options that are available in the PROC CPM statement can also be specified in the PROC PM statement. See Chapter 4, “[The CPM Procedure](#),” for details. However, there are a few additional options available with PROC PM, and some of the other PROC CPM options are not needed as they are the default behavior in PROC PM. See “[Summary of Differences](#)” on page 327 for more details about these differences.

### Options Specific to PROC PM

The following options can be specified on the PROC PM statement.

#### NODISPLAY

invokes the procedure in a noninteractive mode. The schedule for the project is still computed and the requested output data sets are created and saved. However, the PM window is not displayed. This option is useful for scheduling large projects that do not need to be updated interactively. Note that invoking PROC PM with the NODISPLAY option is similar to invoking PROC CPM; however, because the format of the Schedule output data set is different for the two procedures, you might see some differences in the order and content of the observations. See “[Schedule Data Set](#)” on page 327 for details.

#### PROJECT=SAS-data-set

identifies a SAS data set that can be used to save and restore preferences that control the project view. For example, preferences such as the font, column order, column widths, filters, and so forth, can be saved from one invocation to another. See “[PROJECT Data Set](#)” on page 323 for more details about this data set and the preferences that can be saved in it.

#### PROJECTNAME='string'

#### PROJNAME='string'

#### NAME='string'

specifies a descriptive string identifying the name of the project. This string is used to label the PM window.

**SUMMARYNAME='string'****SUMMARY='string'****PROJECTSUMMARY='string'**

specifies a descriptive string identifying the summary task. By default, when there is more than one root parent activity in a project, PROC PM creates a summary task named “Summary” (or “Project Summary” if the input format for the activity variable is 15 or greater). So, if there is already a child activity named “Summary” (or “Project Summary”) in the input data, the resulting schedule forms a cycle. The SUMMARYNAME= option enables you to override the default by specifying a different name for the summary task, thereby avoiding the previously described problem.

## Default Options for PROC PM Statement

The following options of PROC CPM are turned on by default in PROC PM.

**ADDACT****ADDALLACT****EXPAND**

indicates that an observation is to be added to the Schedule output data set (and the Resource Schedule output data set) for each activity that appears as a value of the variables specified in the SUCCESSOR or PROJECT statements without appearing as a value of the variable specified in the ACTIVITY statement. In other words, the Schedule output data set produced by PROC PM contains one observation for every activity that appears as a value of the ACTIVITY, SUCCESSOR, or PROJECT variables (as long as it has not been deleted in the current invocation of the procedure). It also contains an observation for every activity that is added to the project using the graphical user interface.

**XFERVARS**

indicates that all relevant variables are to be copied from the Activity data set to the Schedule data set. The procedure carries over to the output data set all the relevant variables from the input data set. Thus, the Schedule output data set contains all the project information that is necessary to schedule it.

## Default Options for ACTUAL Statement

**AUTOUPDT**

requests that the procedure assume automatic completion (or start) of activities that are predecessors to activities already completed (or in progress).

**ESTIMATEPCTC****ESTPCTC****ESTPCTCOMP****ESTPROG**

indicates that a variable named PCT\_COMP is to be added to the Schedule output data set (and the Resource Schedule output data set) that contains the percent completion time for each activity (for each resource used by each activity) in the project.

**SHOWFLOAT**

indicates that activities that are completed or in progress have nonzero float.

## **Default Options for PROJECT Statement**

**ADDWBS**

**WBSCODE**

**WBS**

indicates that the PM procedure is to compute a WBS code for the activities in the project using the project hierarchy structure specified. This code is computed for each activity and stored in the variable `WBS_CODE` in the Schedule output data set.

**DESCENDING**

**DESC**

indicates that, in addition to the ascending sort variables (`ES_ASC`, `LS_ASC`, and `SS_ASC`) that are requested by the `ESORDER`, `LSORDER`, and `SSORDER` options, the corresponding descending sort variables (`ES_DESC`, `LS_DESC`, and `SS_DESC`, respectively) are also to be added to the Schedule output data set.

**ESORDER**

**ESO**

indicates that a variable named `ES_ASC` is to be added to the Schedule output data set; this variable can be used to order the activities in such a way that the activities within each subproject are in increasing order of the early start time. Note that this order is not necessarily the same as the one that would be obtained by sorting all the activities in the Schedule data set by `E_START`.

**LSORDER**

**LSO**

indicates that a variable named `LS_ASC` is to be added to the Schedule output data set; this variable can be used to order the activities in such a way that the activities within each subproject are in increasing order of the late start time.

**ORDERALL**

**ALL**

is equivalent to specifying the `ESORDER` and `LSORDER` options (and the `SSORDER` option when resource constrained scheduling is performed).


**SSORDER**

**SSO**

indicates that a variable named `SS_ASC` is to be added to the Schedule output data set; this variable can be used to order the activities in such a way that the activities within each subproject are in increasing order of the resource-constrained start time.

## Details: PM Procedure

**Figure 5.2** LAN Selection Project

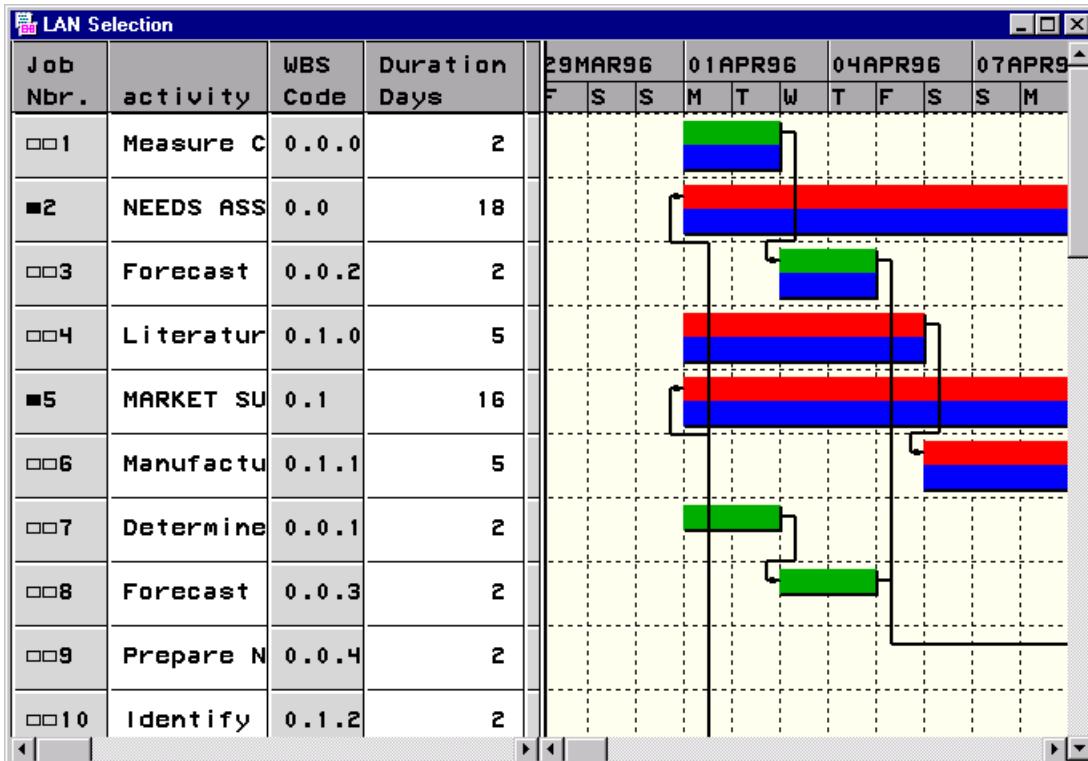

The PM window provides the standard editing and viewing functions of a typical project management tool. It can be displayed by invoking the PM procedure or using the Activities window in the PROJMAN application. See Chapter 10, “[The Projman Application](#),” for details. For an existing project, the PM window is populated with the activities in the project. For a new project, the PM window is empty. Figure 5.2 displays the PM window for one of the sample projects included with the PROJMAN application.

After you have finished editing the project, you can close the PM window to save the new project data in the Schedule output data set that was specified in the invocation of the PM procedure.


## User Interface Features

This section describes some of the typical features of the PM window’s graphical user interface. The PM window provides both a [Gantt View](#) and a [Table View](#) of the project. The size of each view can be changed by pointing to the dividing line between the two views until the pointer changes to a double arrow and then dragging it to the right or left.

Only part of the project may be visible in the PM window; horizontal and vertical scroll bars enable you to scroll the project data in both directions. Note that the Gantt and the Table Views are attached to each other so that they scroll together vertically. Each view can be scrolled horizontally, independently of the other.

The menu associated with the PM window provides access to several project management functions under the **Edit**, **View**, and **Project** menus. For example, the **Project** menu is shown in Figure 5.3. The commands available through the menus are described in detail in the appropriate sections.

**Figure 5.3** Project Menu




In addition to the drop-down menus, context-sensitive pop-up menus are available in the Table and Gantt Views, the time axis, along the arcs, and from select columns in the Table View. You open a pop-up menu by right-clicking on a particular object. For example, right-clicking on an arc in the Gantt View displays the arc pop-up menu shown in Figure 5.4.

**Figure 5.4** Arc Pop-up Menu



In some situations, the pop-up menu selection can lead to a dialog box that requires you to type a value in one or more of the fields in the box. For example, selecting **Edit Lag** from the arc pop-up menu leads to the dialog box displayed in Figure 5.5. (See “Create Nonstandard Precedence Relationships” on page 321 for a discussion of nonstandard precedence constraints.)

**Figure 5.5** Edit Lag Dialog Box

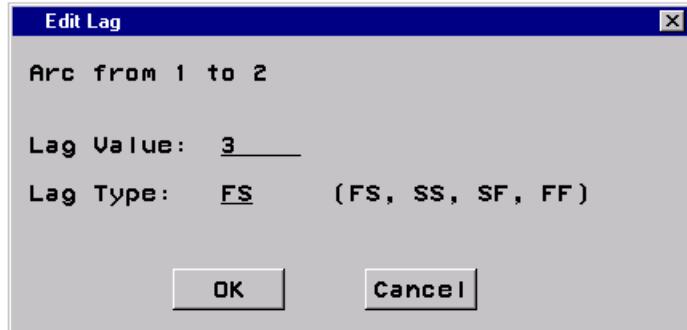


The **Table View** displays project data in a tabular format. Some of the columns are editable (white background) while other columns, which are computed by the procedure, are not editable (gray background). The **Gantt View** always displays the early start schedule of the project. In addition, it also displays the resource-constrained schedule (if resources are present), the actual schedule (if the project has started and is in progress), and the baseline schedule (if a baseline schedule is saved for the project). The display of all the schedule bars (except the Early Schedule bar) can be toggled on or off using the pop-up menu from the Gantt View.

Note that each row of the combined Table View and Gantt View represents one activity (also referred to as *task* in this chapter). Any change in data or movement of a row in one view is also reflected in the other.

In addition to the drop-down and pop-up menu actions, several drag-and-drop actions are available within the PM window. You can move the columns and rows of the Table View by selecting a row or column and dragging it to the desired position. You can also change the width of the columns by dragging the column dividers in the Table header region.

You can manipulate the durations of the tasks using the **Task Information** dialog box (see [Figure 5.6](#)) by right-clicking on the bar shown in the Gantt View or by changing the length of the Early Schedule bar in the Gantt View. You can also move the task in time by dragging the Early Schedule bar to a new position. This affects the Target Date for the associated task.

**Figure 5.6** Task Information Dialog Box

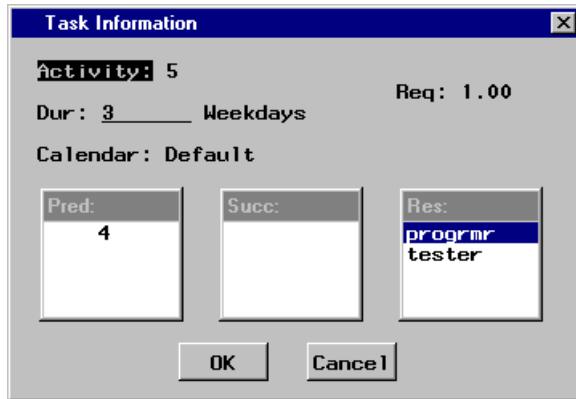

Any of the preceding actions may result in a change to the project schedule that is immediately reflected in the Table and Gantt Views. All editing abilities and the corresponding changes to the schedule are described in detail in the following sections.

## Project Hierarchy

The PM procedure displays a hierarchical project structure if it is invoked with the PROJECT statement. If the procedure is invoked without a PROJECT statement, the supertask and subtask relationship is not supported, and all the activities are considered to be at the same level, belonging to a single project. Note that, in the PROJMAN application, the PM procedure is always invoked with the PROJECT statement. See Chapter 10, “The Projman Application,” for details.

If the PROJECT statement is used, then a task’s level in the project hierarchy is indicated in the Table View by small square boxes to the left of the activity number in the Job Nbr. column. Empty boxes indicate that the activity does not have any subtasks (it is a *leaf* activity), while filled boxes indicate that the activity is a supertask. Further, a Project Summary task is included to represent the root task (or Summary Task) of the project. This task is positioned at the top of the list of activities, and its display can be toggled on or off by selecting **Display Summary Task** from the **View** menu (see [Figure 5.7](#)).

**Figure 5.7** View Menu

In the Gantt View, supertasks are indicated by vertical cones at the end of their corresponding schedule bars.

Note that the durations of the supertasks are determined by the overall duration of their subtasks. Thus, you cannot change the duration of a supertask.

If there is no PROJECT statement, all menu selections that correspond to the multi-project structure are unavailable for selection. For example, the **Display Summary Task** selection in Figure 5.7 will appear dimmed.


## Table View

The Table View displays information about a project in tabular form. It displays activities along with their descriptions, various activity schedules, resource requirements, calendars, and target dates. The hierarchical information about an activity is provided in the Job Nbr. column by a number of small square boxes to the left of the activity number. The number of square boxes corresponds to the level of the activity in the project hierarchy. Empty boxes indicate that the activity does not have any subtasks (it is a leaf activity), while filled boxes indicate that the activity is a supertask. Some columns in the Table View are editable while others are write-protected. The editable columns are lighter in color than the noneditable ones. In general, you can type into all columns that provide input to the project, while all other columns that contain output values from PROC PM are write-protected. For example, in Figure 5.2, the WBS Code column cannot be edited, while the activity and Duration columns can be edited.

In the Table View, you can add or delete activities, add subtasks, change the order of the columns or the activities, edit activity information, and so on. These tasks are described in the following sections.

### Add/Copy/Delete Tasks

Right-clicking any task in the Table View displays the pop-up menu shown in Figure 5.8. From this pop-up menu, you can Add/Copy/Delete the selected task. If you select the **Add Task** menu item, the new task is added immediately following the selected task. You can also add a subtask to the selected task by selecting the **Add Subtask** menu item. If you select the **Copy Task** menu item, a copy of the selected task is added to the bottom of the Table View. The new task has the same duration and calendar as the selected task. If the selected task is a supertask, all its subtasks (and any internal precedence constraints) are also copied.

**Figure 5.8** Table View Pop-up Menu


## Change Column Width

The width of a column in the Table View can be increased or decreased by dragging (with the left mouse button) the column dividers in the Table Header region of the Table View. When the pointer is positioned on the column divider, it changes to a double arrow. Dragging it to the right or left increases or decreases the width of the column.

## Change the Order of the Columns

The display order of columns in the Table View can be changed in several ways:

- Drag the column in the header row to the destination.
- Select **View** from the menu and then select **Move Columns to Left** (see [Figure 5.9](#)). Choosing any of the available options moves the corresponding columns to the leftmost portion of the Table View.

**Figure 5.9** Move Columns Menu

## Edit Durations

To change the duration of an activity, edit the Duration column in the Table View. Note that changing an activity's duration to 0 changes the activity into a [Milestone](#). Activity durations can also be [changed](#) in the Gantt View.

## Edit Alignment Constraints

Scroll to columns named Target Date and Target Type. Enter one of the values SGE, SLE, MS, MF, FGE, or FLE in the Target Type column. You can either type the values or select them from the pop-up menu displayed by right-clicking the Target Type column (see [Figure 5.10](#)). Enter the appropriate date in the Target

Date column. You can also view these columns by selecting **View ▶ Move Columns to Left ▶ Target Dates** from the menu (Figure 5.9). You can also change an activity's alignment constraints in the Gantt View.

**Figure 5.10** Target Type Pop-up Menu



## Edit Calendars

To change an activity's calendar, you can enter the calendar number in the Activity Calendar column or the calendar description in the Calendar Name column. The calendars that can be assigned to an activity are predefined in the Calendar data set. To see a list of the calendars, you can right-click in one of the calendar columns. This will pop up a list of calendars, from which you can select the activity's calendar. See Figure 5.11 for an example of a calendar pop-up menu with two calendars.

**Figure 5.11** Calendar Pop-up Menu



## Edit Resource Requirements

You can change the amount of resources required for an activity by editing the Resource columns in the Table View. Changing the resource requirement causes the project to be rescheduled using the new resource specifications. See “Edit Resource Requirements” on page 322 for more details.

## Edit Progress Information

You can edit the actual start, actual finish, percent complete, or remaining duration for an activity by editing one of the Progress Information columns in the Table View. Note that by changing one of these columns, all the other related progress columns might also be affected. For example, entering 100 in the Percent Complete column for an activity that is in progress updates the Remaining Duration column to 0, and the Actual Finish column is filled in appropriately. You can also modify the progress information of an activity in the Gantt View.

## Expand/Collapse Supertasks

Double-clicking on a supertask in the Table View toggles the expand/collapse switch. This action enables you to either view or hide all the subtasks of the supertask.

## Hide Tasks

An individual task can be hidden by right-clicking the task in the Table View and selecting **Hide** from the menu shown in [Figure 5.8](#). Tasks can also be hidden from view using several filters described in the section “[Setting Activity Filters](#)” on page 322.

## Move Tasks

Starting anywhere in the row corresponding to an activity you want to move, drag it to the destination.

## Gantt View

In the Gantt View, activity schedules are depicted by horizontal bars. There is one bar for each of the early, resource, actual, and baseline schedules. For the Early Schedule bar, critical activities are marked in different colors from the noncritical activities. Weekends are marked by shaded vertical rectangles running through the chart. Supertasks are differentiated from leaf activities by anchoring vertical cones at the ends of their Early Schedule bars.

The Gantt View is displayed with a rectangular grid that can be turned on or off by selecting **Grid** from the pop-up menu (see [Figure 5.12](#)) that is displayed by right-clicking anywhere outside of the schedule bars in the Gantt View.

**Figure 5.12** Gantt View Pop-up Menu




The pop-up menu in the Gantt View also enables you to toggle the display of the Actual, Resource, or Baseline Schedule bars. Note that these bars can be displayed in the Gantt View only if the project data contain the actual, resource-constrained, or baseline schedules, respectively.

In addition to displaying the activity schedules in an easy-to-view format, the Gantt View in the PM window can also be used to change the durations of the activities, add or delete precedence constraints, set activity alignment constraints, set progress information, and provide access to calendar, precedence, and resource information.

You can also change several of the display attributes of the Gantt View by using the **Time Axis** pop-up menu (see [Figure 5.13](#)) to set the scale of the axis, format the time axis labels, set the units of display, and so forth. All of these tasks are described in the following sections.


**Figure 5.13** Time Axis Pop-up Menu




## Change the Format of the Time Axis

The format of the major axis can be changed by right-clicking on the header row of the Gantt View and selecting **Format** for the major axis. For the minor axis, select **Format Minor**. Some example selections available for the formats are shown in [Figure 5.14](#) and [Figure 5.15](#). In addition to the formats explicitly listed for the major axis, you can specify any valid numeric format by selecting **Other** and filling in the appropriate fields in the dialog box that is opened as a result.

**Figure 5.14** Major Axis Format Pop-up Menu




**Figure 5.15** Minor Axis Format Pop-up Menu



## Change Increments

Increments in the Gantt View define the number of tick marks on the minor axis per tick mark on the major axis. They can be changed by right-clicking on the header area and selecting **Increment** from the pop-up menu. The available selections are shown in [Figure 5.16](#).


**Figure 5.16** Increment Pop-up Menu



## Change the Scale of the Time Axis

Move the pointer to a tick mark on the major axis in Gantt View. The pointer changes to a double arrow. Drag the tick mark horizontally to change the scale. You can also change the scale by using the **Scale** pop-up menu (see Figure 5.17) from the **Time Axis** pop-up menu.


**Figure 5.17** Scale Pop-up Menu



## Change Units

The Time Axis Units in the Gantt View can be changed by right-clicking on the header bar in the Gantt View and selecting **Units** (see Figure 5.18). The default value of the units used for display is based on the specification of the INTERVAL= parameter in the invocation of the PM procedure.

**Figure 5.18** Units Pop-up Menu



## Display/Hide Selected Schedules

A display/hide switch for a given schedule can be toggled by right-clicking in the main panel of the Gantt View and selecting the desired schedule (see Figure 5.19).

**Figure 5.19** Gantt View Pop-up Menu




## Display Task Information


You can display detailed information for an activity by right-clicking any of its schedule bars and selecting **Task Information** from the resulting pop-up menu (see Figure 5.20).

**Figure 5.20** Schedule Bar Pop-up Menu

The ensuing **Task Information** dialog box (see [Figure 5.21](#)) displays the job number, duration, duration units, a list of predecessor activities, and a list of successor activities, as well as applicable calendar and resource information for the selected activity. You can also edit the activity duration from the **Task Information** dialog box.

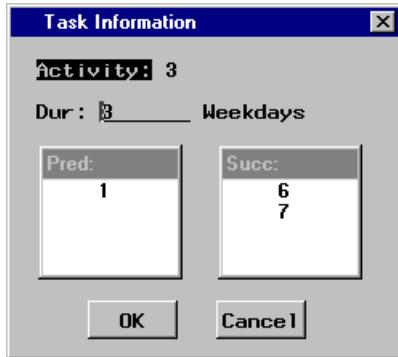**Figure 5.21** Task Information Dialog Box

If any calendars have been defined to the project, the activity calendar is also displayed. If the project utilizes any resources, there is a list box that lists the resources required by the activity (see [Figure 5.22](#)). Selecting a resource from this list box displays the quantity required by the activity in the **Req** field. Furthermore, if the selected resource drives the duration of the activity, then the appropriate work value is also displayed in the **Work** field.

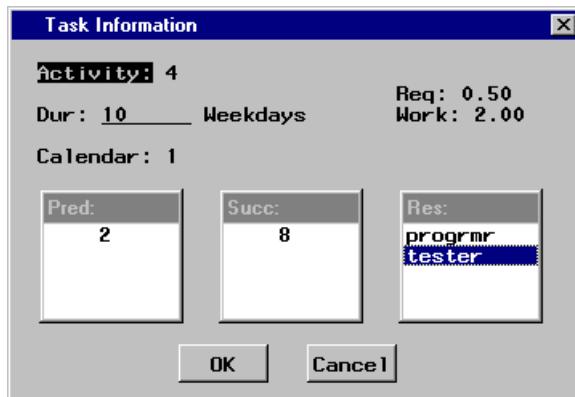**Figure 5.22** Task Information Dialog Box (Calendar and Resources)

### Modify Activity Alignment Constraints

An activity's Early Schedule bar can be moved using the left mouse button. When the pointer is positioned over the activity bar, it changes to a cross-hair type. You can then drag the bar horizontally to a new position. This sets an alignment constraint of type 'SGE' for the selected activity with the align date corresponding

to the one at the left edge of the bar's new position. Other types of alignment constraints can be entered by editing the Target Date and Target Type columns as described in “[Edit Alignment Constraints](#)” on page 311.

## Modify Durations


You can modify the duration of an activity in several ways. In the Gantt View, you can enter it directly by using the **Task Information** dialog box as described in “[Display Task Information](#)” on page 315, or change it indirectly by altering the width of the schedule bar. To change the duration of an activity, point to the right edge of the activity's Early Schedule bar, and drag to the left or the right depending on whether you want to decrease or increase the duration. You can also edit activity durations in the [Table View](#).

## Modify Precedence Information

You can add precedence constraints by depressing the left mouse button at either end of the predecessor activity bar and releasing it at either end of the successor activity bar. The type of constraint (FS, FF, SS, or SF) depends on which end of the bars the constraints are drawn from.


You can delete precedence constraints by right-clicking on the arc and selecting **Delete** (see [Figure 5.23](#)).

**Figure 5.23** Arc Pop-up Menu




You can modify the type of the precedence constraint or the lag value associated with the precedence constraint by right-clicking on the arc and selecting **Edit Lag**. The ensuing dialog box is shown in [Figure 5.24](#). Enter the value of the lag duration in the first field and the type of the lag in the second field. Valid values of lag are Finish-to-Start (FS), Start-to-Start (SS), Start-to-Finish (SF), and Finish-to-Finish (FF).

**Figure 5.24** Edit Lag Dialog Box

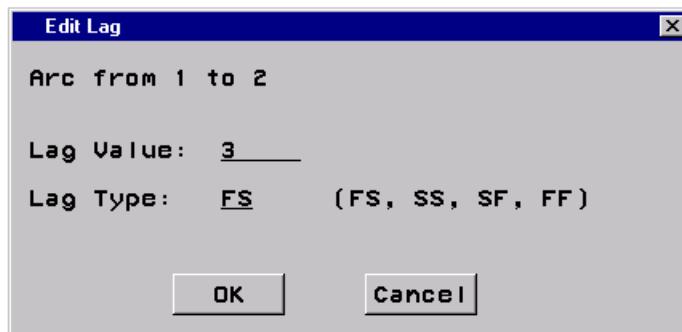

If calendars are defined in the project, the **Edit Lag** dialog box includes the lag calendar associated with the selected precedence constraint. You can change the lag calendar by selecting from the list of available calendars that is displayed within the **Edit Lag** dialog box shown in [Figure 5.25](#).

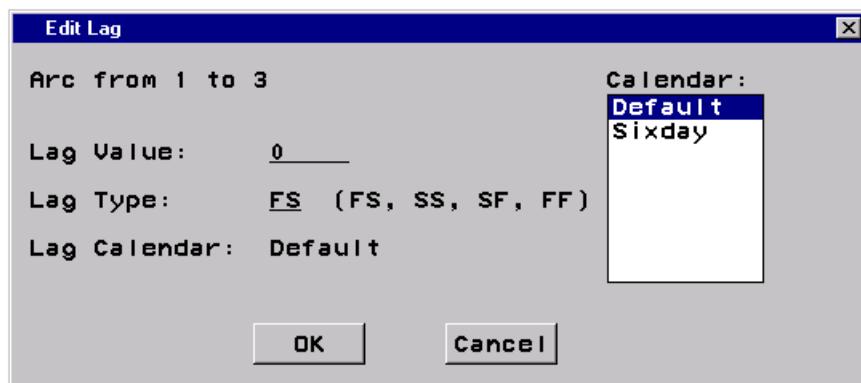**Figure 5.25** Edit Lag Dialog Box (Multiple Calendars)

## Modify Progress Information


To modify the Progress using the Gantt View, you must include the Actual Schedule in the view. You can drag the actual schedule bar for the activity to change the amount of progress on the activity; you can also move the activity's actual bar to change the Actual Start of the activity.

When the project contains progress information, a Timenow line is drawn in the Gantt View, indicating the TIMENOW date. You can move the Timenow line by dragging it. When you change the value of TIMENOW, the progress information changes for all the activities. A confirmation window requires you to confirm that you do want to change the progress information for all the activities. (See also “Macro Variable TIMENOW” on page 326.)

You can also edit the progress columns in the [Table View](#).

## Creating and Editing Projects

The PM window provides an easy-to-use interface to enter basic project information such as a list of activities, their durations, order of precedence, resource requirements, and so forth. You can also use the **Edit** menu (see [Figure 5.26](#)) to add or delete progress, baseline, and other information. These functions are described in the following sections.

**Figure 5.26** Edit Menu

## Add Activities

An activity (or task) can be added to the Project in the PM window by right-clicking in the Table View. If **Add Task** is selected from the pop-up menu, then an activity is added at the same level as the selected activity. Subtasks of an activity can be added by selecting **Add Subtask**. These actions are also available from the **Edit** menu (Figure 5.26) whenever an activity is selected in the Table View. Note that the selected activity is highlighted.

To add a new task at the topmost level of the project hierarchy, select **New Task** from the **Edit** menu.


## Add Precedence Constraints

To add precedence constraints in the Gantt view, point at the right edge of the predecessor activity until the pointer changes to a cross-hair and drag it vertically up or down to the left edge of the successor activity. By starting and dropping at different ends of the activity bar, you can create nonstandard precedence relationships between the activities. You can view the predecessor and successor tasks for an activity from the **Task Information** dialog box.

## Add Baseline Information

Baseline information is saved in a project so that the current status of a project can be measured against some base schedule. The baseline information can be set in several different ways; most of the actions relating to the Baseline schedule can be performed using the selections available from the **Edit** menu (see Figure 5.26).

- If the project data include a Baseline schedule, saved in the variables B\_START and B\_FINISH, the PM window displays the Baseline schedule when it is first invoked. This schedule can be replaced by selecting **Replace Baseline** from the **Edit** menu. This selection can be used to reset the Baseline schedule to a new schedule corresponding to one of the current schedules.
- If the project data do not include a Baseline schedule, the Baseline schedule can be set in the PM window by selecting **Set Baseline** from the **Edit** pull-down menu (see Example 5.3). This selection can be used to set the Baseline schedule to one of the current schedules (see Figure 5.27). Thus, selecting **Resource** from the **Set Baseline** menu sets the baseline schedule to the current resource-constrained schedule. By saving the current resource-constrained schedule, you can perform some what-if analysis by changing some of the resource requirements or other parameters of the project and comparing the resulting schedule with the saved baseline schedule.

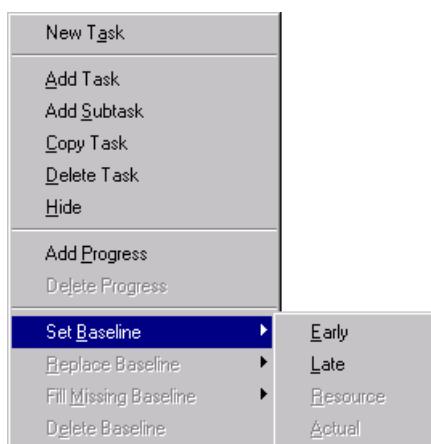**Figure 5.27** Set Baseline Pull-down Menu

- The individual Baseline values can also be edited in the Table View by changing the values in the Baseline Start and Baseline Finish columns.
- If new activities are added to the project, the Baseline values for the new tasks are missing. These can be set to correspond to the current schedule values by selecting **Fill Missing Baseline** from the **Edit** menu.
- If you want to delete the Baseline information from the project data, you can select **Delete Baseline** from the **Edit** menu.

## Add Progress Information

Progress information can be included by using the **ACTUAL** statement, which is similar to the one for PROC CPM. If the PM window is invoked without the ACTUAL statement, then progress information can be added to the Project from the **Edit** menu (Figure 5.26) by selecting **Add Progress**.

Progress information is updated by dragging the actual schedule bars horizontally (in a manner similar to the one for changing durations) in the Gantt View or by modifying the values in the Progress columns in the Table View. See “[Modify Progress Information](#)” on page 318 and “[Edit Progress Information](#)” on page 312.

For details about how the progress information is used to update the project schedule, see “[Progress Updating](#)” on page 109. See also [Example 5.6](#).

## Change Duration

The duration of an activity can be changed directly from the Duration column of the **Table View** or the **Task Information** dialog box of the **Gantt View**. It can also be changed indirectly by dragging the activity bar at the right edge in the **Gantt View**.

## Copy Activities

An activity (or task) can be copied in the PM window by right-clicking in the Table View. If **Copy Task** is selected from the pop-up menu, then a copy of the selected activity is added at the end of the activities listed in the Table View. The new task has the same duration and calendar as the selected task. If the selected task is a supertask, all its subtasks (and any internal precedence constraints) are also copied.

## Create Milestones

You can create milestones by adding an activity and assigning it zero duration.

## Create Nonstandard Precedence Relationships

A Finish-to-Start relationship between two activities is considered to be a standard precedence constraint. You can create it in Gantt view by dragging the precedence constraint from the right end of the predecessor activity bar to the left end of the successor activity bar. Nonstandard precedence constraints are created by starting and ending at different ends of the two activity bars. For example, a Start-to-Finish relationship is created by dragging from the left end of the predecessor activity bar to the right end of the successor activity bar.

In addition to specifying the type of the precedence constraint, you can also specify a lag or lead time between the two activities. This lag value can be edited from the Gantt View. See “[Modify Precedence Information](#)” on page 317 for more details.

## Create Subtasks

Subtasks can be created only if the PM procedure is invoked with the PROJECT statement or from the PROJMAN application. To create a subtask, right-click on the parent activity in the Table View. Then select **Add Subtask** from the background menu. The newly created subtask has one more little square box than the parent task in the Job Nbr. column in the Table View. The empty square boxes denote that it is a leaf activity (a task with no subtasks). The number of boxes denote a task’s level in the project hierarchy, starting with level 0 for the Project Summary task.

## Delete Activities

An activity can be deleted in the Table View by right-clicking anywhere in the task row and selecting **Delete Task**. If the selected task is a supertask, all its subtasks are also deleted. Note that, in this case, a confirmation dialog box confirms the **Delete Supertask** action.

## Delete Precedence Constraints

To delete a precedence constraint, right-click anywhere on the arc and select **Delete** from the pop-up menu. You can view the predecessor and successor tasks for an activity from the [task information window](#).

## Edit Activity Alignment Constraints

Activity alignment constraints can be added/modified as described in “[Edit Alignment Constraints](#)” on page 311 and “[Modify Activity Alignment Constraints](#)” on page 316, respectively.

## Edit Baseline Information

To edit the baseline schedule, scroll to the Baseline Start and Baseline Finish columns and type in the new values of the baseline start and finish times. Note that you cannot change the baseline values by moving the Baseline Schedule bars. See “[Add Baseline Information](#)” on page 319 for more details.

## Edit Calendar Specifications

Calendars are defined by the CALEDATA= option in the PROC PM statement. This option is similar to the corresponding option in PROC CPM. After calendars are defined in the Project, an activity's calendar can be changed or set in the Table View by editing the Activity Calendar or Calendar Name columns. You can either type the values or select them from the menu displayed by right-clicking in either of the Calendar columns. See “[Edit Calendars](#)” on page 312. You can also view the activity calendar from the task information window.

## Edit Resource Requirements


The resource requirement information for each activity is displayed and can be edited in the Table View. A column for a resource is created in the Table View when it is specified in the RESOURCE statement of the PROC PM invocation, or it is created by the Resource Manager of the PROJMAN application. For details about the RESOURCE statement, the Resource data set, and Resource Allocation, see Chapter 4, “[The CPM Procedure](#).“ Changing the resource requirement causes the project to be rescheduled to use the new resources. You can also view the resource requirements for an activity from the [task information window](#).

If alternate resources are used by the scheduling algorithm, an extra set of columns is added to the Table View. These columns (one for every resource in the project) display the resources that were actually used. These Usage columns for the resources cannot be edited.

## Setting Activity Filters


Activity filters can be set by using the project hierarchy or by selecting from a list of activity attributes, as described in this section.

**Figure 5.28** View Menu



Activities at different levels in the hierarchy can be viewed by selecting **View** from the menu (Figure 5.28) and selecting the appropriate level of the project hierarchy to filter out the higher level tasks. For example, selecting **Level 2 Tasks** displays only the tasks that are at Level 2 or lower. All activities can be viewed by selecting **Tasks at All Levels** from the **View** menu.

Activities can also be filtered using different criteria by selecting **View ▶ Filters** from the **View** menu (see Figure 5.29). The available filters are shown in Figure 5.29. By default, no filter is in effect (the selection is **None**); you can save the filter of your choice in the Preference data set (see “[Saving and Restoring Preferences](#)” on page 323).

**Figure 5.29** Filters Pull-down Menu

## Saving and Restoring Preferences

When the PM window is displayed for the first time for a given project, the order and width of the columns in the Table View, the font used for the display, the size of the window, the boundary between the Table and the Gantt Views, and several other attributes of the display are determined by the procedure. As you add activities and edit the Table View, you can change some of these attributes according to your preference. You can also select a different level of display or set some activity filters (see “Setting Activity Filters” on page 322).

### PROJECT Data Set

PROC PM enables you to save the attributes of the display in an indexed data set that is specified in the PROC PM statement by using the **PROJECT=** option. The following preferences can be saved from one invocation to another:

- text font
- time increment
- time units
- major time axis format
- minor time axis format
- schedule bars displayed (for example, Actual, Baseline, and so forth)
- chart grid
- chart scale
- table column widths
- table column order
- Table View-Gantt View dividing line
- activity filters

- activity level
- project summary
- window dimensions

The Project data set uses three variables to save the preference information:

- PROJATTR—contains a keyword identifying the project attribute. Each attribute has either a numeric value or a character value. The length of this variable is 8.
- PRATNVAL—used for numeric data corresponding to the attribute.
- PRATCVAL—used for character data corresponding to the attribute. The length of this variable is 200.

You can save and restore the preferences from the **Project** menu, which contains the **Preferences** submenu (Figure 5.30). Note that you have to explicitly save the project preferences using the **Save** selection from this menu. Closing the PM window saves only the activity data of the project; it does not automatically save the project preferences. When you restore preferences, the state used is the one that was last saved for the project in the specified preference data set.


**Figure 5.30** Preferences Menu



## Sorting Activities

Activities can be sorted by activity number, early start, late start, and resource start by selecting **Project ► Sort** from the **Project** pull-down menu (see Figure 5.31). Once the activities are sorted, the Schedule output data set contains the activities in the new sorted order. See “Renumbering the Activities” on page 325.

**Figure 5.31** Sort Menu



---

## Setting the Project Font

When the PM window is first displayed, the font used in all the text areas of the window is the same as the SAS font used in other windows. You can use the **Fonts** selection in the **Project** menu (Figure 5.32) to change the font used in the PM window. You can select the various fonts and their sizes from the font manager thus obtained. This font can also be saved (and restored) in the Project data set.

**Figure 5.32** Project Menu




---

## Renumbering the Activities

When the PM window is first displayed for the specified project, the activities are listed in the order in which they are defined in the Activity data set. The activity numbers displayed in the Job Nbr. column correspond to this same order. Even if the activities are rearranged, either by moving selected activities or by sorting, these numbers do not change. Likewise, no renumbering takes place automatically if activities are deleted from the project.

You can use the **Renumber** selection in the **Project** menu (Figure 5.32) to reassigned consecutive numbers to the activities, starting from the first activity displayed.

When you close the PM window, saving all the activity information to the Schedule data set, the activities are numbered according to the order in which they were displayed at the end of the editing session. In other words, the **Close** action implicitly invokes the **Renumber** command on the project activities. These activity numbers are, in fact, saved as the values of the ACTID variable (see “Schedule Data Set” on page 327).

---

## Printing

The PM window provides functionality to print the Gantt View, the Table View, or both, provided that a printer has been selected and the correct information has been set in the Printer Setup window. **Print Preview** can be used to view the information before printing, and the printed output can be saved to a file. All the printing functions are available from the **File** menu (Figure 5.33).


**Figure 5.33** File Menu

### Preview the Printed Output on the Screen

You can view the printed output on screen before actually printing it by selecting **Print Preview** from the **File** menu.

### Print Options

Select **Print Options** from the **File** menu. There are options for selecting time and activity axis range and scaling of the printed output. See Figure 5.34.

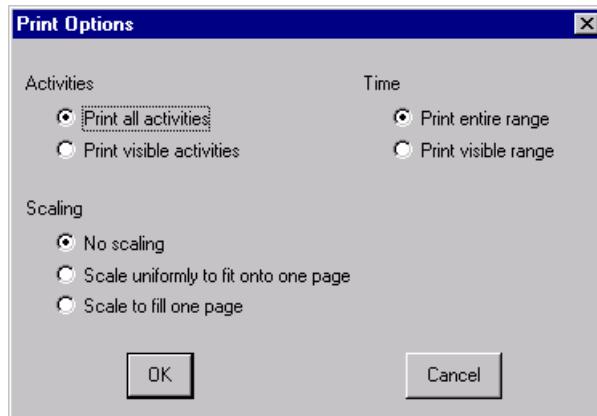**Figure 5.34** Print Options Dialog Box

### Save the Printed Output to a File

The printed output can be saved to a file by selecting **File** ► **Print** ► **Print to File**.

### Macro Variable TIMENOW

The PM window can be used to add and edit progress information to a project. When progress information is added, the Schedule data set contains all the progress variables; see “**Progress Updating**” on page 109.

However, all the values of the progress variables are reconciled and revised on the basis of the value of the **TIMENOW** parameter. Since the PM procedure enables you to move the **TIMENOW** line as well as

implicitly change the value of TIMENOW by updating the Actual Start or Finish times of the activities, the value of TIMENOW at the end of the editing session is an important parameter of the project. This value is saved in a macro variable called TIMENOW and can be used in subsequent editing sessions of the same project. See [Example 5.6](#) for an example of the use of the TIMENOW macro variable.

## Summary of Differences

The computation of the schedule, the resource-constrained scheduling algorithm, the resource usage information, and all other aspects of the scheduling engine for PROC PM are the same as the ones for PROC CPM. Refer to Chapter 4, “[The CPM Procedure](#),” for details. Some minor differences that pertain to the Schedule Data set and ALIGNTYPE statement are explained in the following sections.

### Schedule Data Set

The Schedule data set produced by PROC PM is very similar to the Schedule data set produced by PROC CPM. See “[OUT= Schedule Data Set](#)” on page 99.

However, unlike PROC CPM, the PM procedure is interactive in nature; it enables you to add activities, set precedence constraints, reorder the activities, and so on. Thus, the output data set produced by PROC PM is designed to capture the original project data as well as all the changes that are made to the project in the course of the interactive session.

There are several differences between the forms of the Schedule output data sets produced by the PM and CPM procedures:

- The PM procedure automatically includes all relevant variables that are needed to define the project. Thus, the ACTIVITY, SUCCESSOR, LAG, DURATION, ALIGNDATE, and ALIGNTYPE variables are included in the output data set by default. If the RESOURCE statement is used, all the resource variables are also included. Likewise, if actual progress is entered for the project during the course of the interactive session, all the progress-related variables are added to the output data set.
- The PM procedure contains three sets of observations, identified by three different values of a new variable, OBS\_TYPE. The first set of observations contains one observation for every activity in the project. The value of the OBS\_TYPE variable for these observations is 'SCHEDULE.' These observations contain all the activity information such as the duration, the start and finish times and the resource requirements. The second set of observations contains one observation for every precedence constraint in the project. The value of the OBS\_TYPE variable for these observations is 'LOGIC.' These observations contain all the precedence information such as the activity, successor, and lag information.

The third set of observations is present only if the project has resource-driven durations. The value of the OBS\_TYPE variable for these observations is 'WORK.' These observations specify the WORK value for each resource used by each activity in the project.

- The order of the activities in the Schedule data set produced by PROC PM corresponds to the order in which the activities appear in the Table View at the end of the interactive session. Likewise, when the procedure is first invoked, the order of the activities in the Table View corresponds to the order in which the activities are defined in the Activity input data set. If, during the course of the session, some

of the activities are reordered or deleted, or if some new activities are added, the Schedule output data set contains all the activities that are defined in the Table View at the end of the session.

- The PM procedure also assigns a numeric identifier for each activity. These values are assigned by PROC PM consecutively in the order of the activities in the Table View and are saved in a variable called ACTID (see “[Renumbering the Activities](#)” on page 325). In addition to the ACTID variable, the Schedule data set also contains a numeric variable called SUCCID, which contains the numeric identifier for the successor activities in the observations for which OBS\_TYPE='LOGIC.' If the PROJECT statement is used in the invocation of the PM procedure, a numeric variable called PNTID is added to the Schedule data set; this variable identifies the parent task for each activity.

**NOTE:** If the ACTIVITY variable in the Activity input data set is a character variable, the ACTID, SUCCID, and PNTID variables are added to the Schedule data set in addition to the ACTIVITY, SUCCESSOR, and PROJECT variables. On the other hand, if the ACTIVITY variable in the Activity input data set is numeric, the new ACTID, SUCCID, and PNTID variables replace the numeric ACTIVITY, SUCCESSOR, and PROJECT variables, respectively.

## ALIGNTYPE Statement

In PROC PM, if an ALIGNTYPE variable is specified but no ALIGNDATE variable is specified, then no error message is generated; PROC PM ignores the ALIGNTYPE variable and generates a schedule. However, in PROC CPM, this results in an error message with no schedule generated.

## RESOURCE Statement

In PROC CPM, the NORESOURCEVARS option in the RESOURCE statement requests that the variables specified in the RESOURCE statement be dropped from the Schedule data set. However in PROC PM, this has no effect.

## Examples: PM Procedure

This section illustrates some of the interactive features of PROC PM by using a few simple examples that lead you through different stages of entering and editing project data. A simple software development project is used in all the examples. The output data set from one example is used as input to the next example. Where necessary, additional data sets are created, or the input data set is modified using simple DATA step code.

You could also use PROJMAN to create the software project and then proceed to each succeeding example by using the application to define the calendars, resources, and so forth. The PROJMAN application automatically manages the required data sets.

---

## Example 5.1: Defining a New Project


In this example, a simple software development project is built from scratch, starting with an empty Activity data set. PROC PM is invoked with an Activity data set that has no observations and just a few variables that are required to start the procedure. In addition to the Activity data set, a Project data set is also defined that is used to save the display attributes of the PM window to be used between successive invocations of the procedure. The following program invokes PROC PM and opens a PM window that enables you to enter project data. The initial window is shown in [Output 5.1.1](#).

Note that the PROJNAME= option is used in the PROC PM statement. This value is used to label the PM window. Also specified in the PROC PM statement is the PROJECT= option that identifies the project attribute data set. The activities in the project follow a weekday calendar which is indicated to PROC PM by specifying the INTERVAL=WEEKDAY option. In the PM window, the weekends are shaded gray in the Gantt View.

```
/* Initialize the Activity data set */
data software;
  length activity $20.;
  input activity $ actid succid pntid duration;
  datalines;
;

data softattr;
  length projattr $8. pratcval $200.;
  input projattr pratnval pratcval;
  datalines;
;


proc pm data=software project=softattr
  date='1mar04'd interval=weekday
  projname='Software Project'
  out=softout1;
  act actid;
  succ succid;
  project pntid;
  duration duration;
  id activity;
run;
```

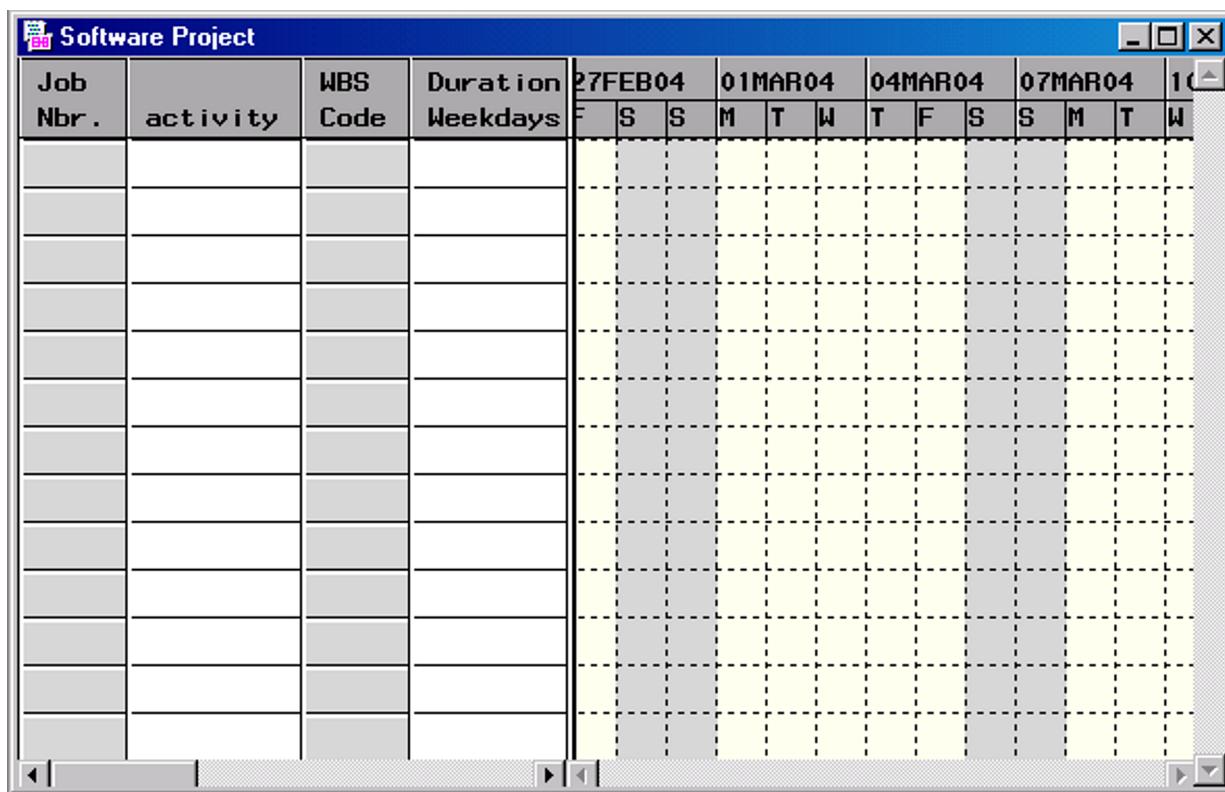**Output 5.1.1** Initial PM window

In the PM window, enter the following tasks with the corresponding durations in the Table View:

<b>Design</b>	5
<b>Develop</b>	10
<b>Document</b>	8
<b>Test</b>	8
<b>Ship</b>	0

As each task is entered, the Schedule columns in the Table View are updated with the early and late start times, and the Early Schedule bars appear in the Gantt View. Output 5.1.2 shows the PM window after the five tasks have been entered. To view the Schedule columns, you can scroll the Table View to the right or use the **View** menu ([Figure 5.7](#)) to move the Schedule columns to the left.

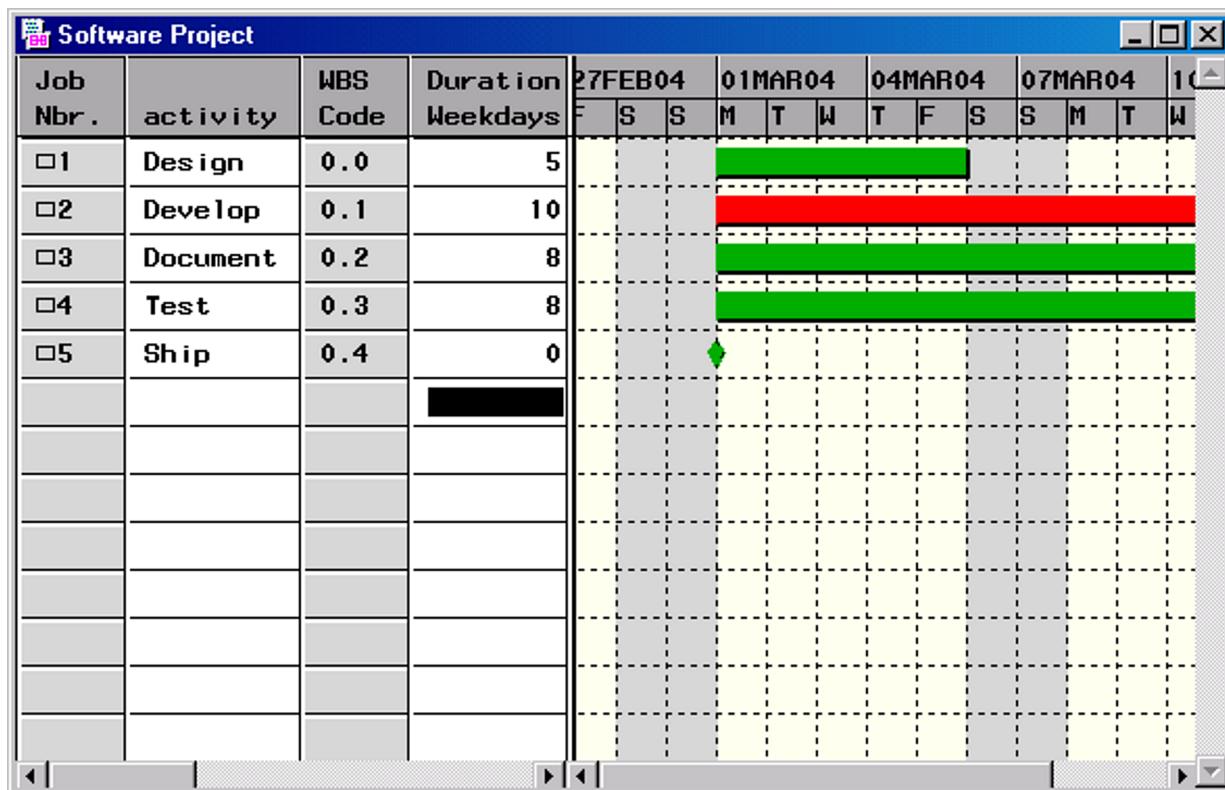**Output 5.1.2** List of Tasks in the Software Project

To enter precedence constraints between two activities, such as ‘Design’ and ‘Develop,’ draw an arc, using the left mouse button, from the end of the predecessor task to the beginning of the successor task. Use the Gantt View to enter the following precedence constraints:


```

Design --> Develop
Design --> Document
Develop --> Test
Test --> Ship

```

Output 5.1.3 shows the Software Project as the last precedence constraint is being drawn. Note that, in this view of the PM window, the Schedule columns have been moved to the left, the grid lines in the Gantt View have been turned off (using the menu in Figure 5.12), and the Gantt View has been scrolled to the right to bring the end of the schedule bar for ‘Test’ into view.


### **Output 5.1.3** Drawing Precedence Constraints

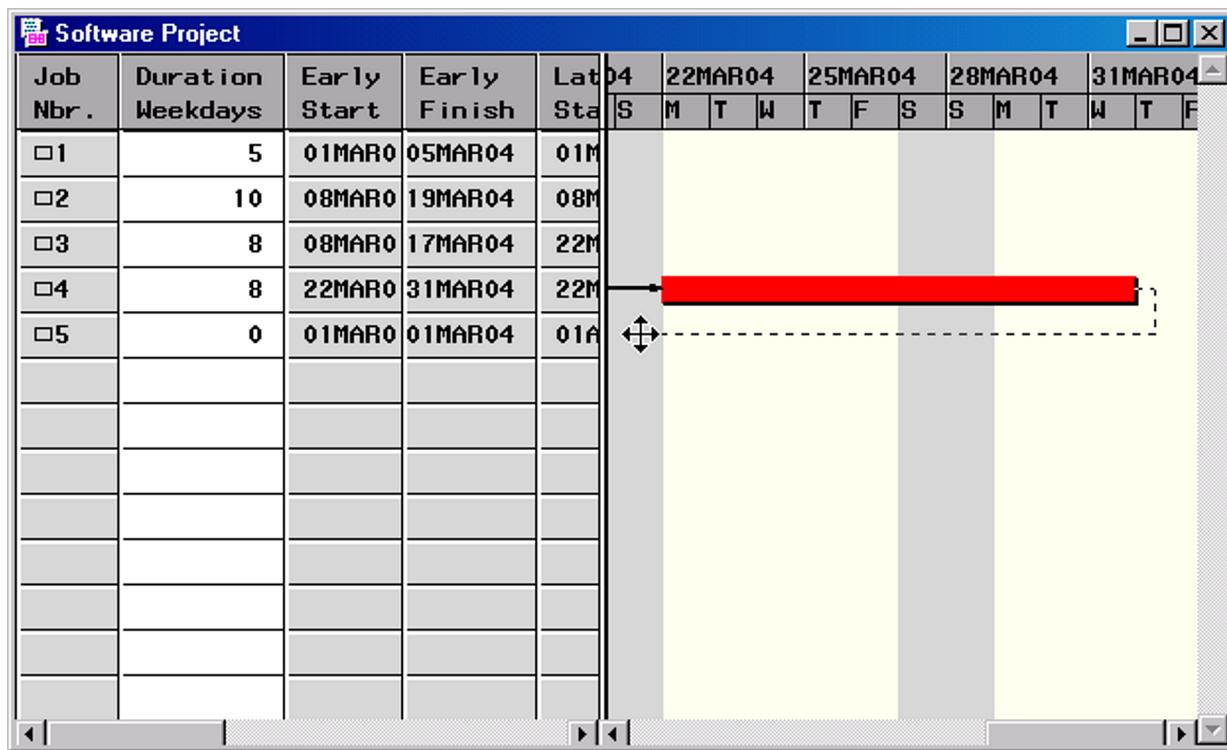

To check the overall project status, you can bring the Project Summary task into view by selecting **Display Summary Task** from the **View** menu ([Figure 5.7](#)). Note that the project duration is 23 days. The critical activities are shown in red while the noncritical ones are green. The Summary Task is indicated by vertical cones at the end of its schedule bar.

For the next few examples, the units used in the Gantt View are changed to “Weeks” by using the **Axis** pop-up menu shown in [Figure 5.13](#), the Summary Task is displayed at the top of the list of activities, and the Activity description columns are shown in the Table View. To save these window settings in the Project data set, select **Project ▶ Preferences ▶ Save from the Project** menu. The view of the project corresponding to these settings is shown in [Output 5.1.4](#). You can end the interactive editing session by closing the window. All the activity and precedence information is saved in the output data set, SOFTOUT1, displayed in [Output 5.1.5](#). Note the two sets of observations in this data set: the first contains all the schedule information for all the activities, and the second lists all the precedence relationships between activities.

## **Output 5.1.4 Project Schedule**

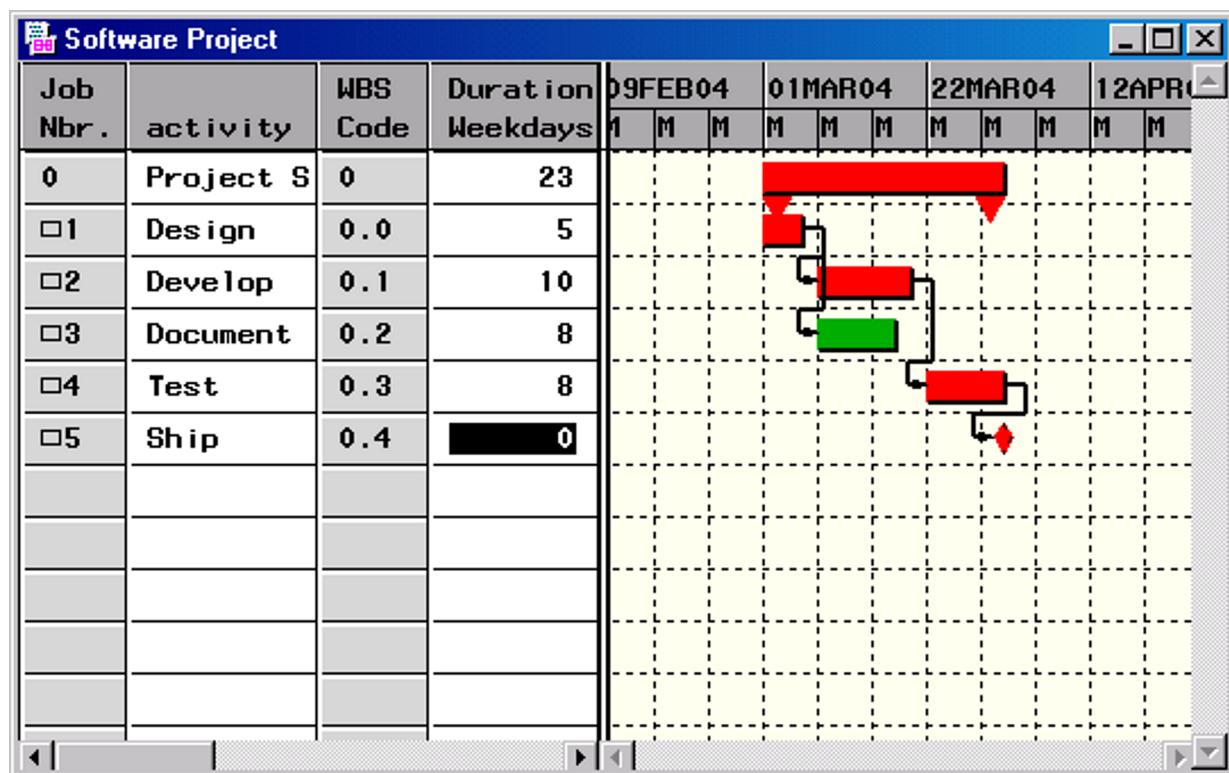

### Output 5.1.5 Schedule Data Set

#### Schedule Data Set

Obs	OBS_TYPE	PNTID	PROJ_DUR	PROJ_LEV	WBS_CODE	ACTID	SUCCID	duration
1	SCHEDULE	.	23	0 0		0	.	23
2	SCHEDULE	0	.	1 0.0		1	.	5
3	SCHEDULE	0	.	1 0.1		2	.	10
4	SCHEDULE	0	.	1 0.2		3	.	8
5	SCHEDULE	0	.	1 0.3		4	.	8
6	SCHEDULE	0	.	1 0.4		5	.	0
7	LOGIC	.	.	.		1	2	5
8	LOGIC	.	.	.		1	3	5
9	LOGIC	.	.	.		2	4	10
10	LOGIC	.	.	.		4	5	8

Obs	PARENT	activity	SUCCESSR	LAG	ALGNDATE	ALGNTYPE	E_START	E_FINISH
1		Project Summary					01MAR04	31MAR04
2	Project Summary	Design					01MAR04	05MAR04
3	Project Summary	Develop					08MAR04	19MAR04
4	Project Summary	Document					08MAR04	17MAR04
5	Project Summary	Test					22MAR04	31MAR04
6	Project Summary	Ship					01APR04	01APR04
7	Design	Develop					.	.
8	Design	Document					.	.
9	Develop	Test					.	.
10	Test	Ship					.	.

Obs	L_START	L_FINISH	T_FLOAT	F_FLOAT	ES_ASC	ES_DESC	LS_ASC	LS_DESC
1	01MAR04	31MAR04	0	0	0	0	0	0
2	01MAR04	05MAR04	0	0	1	5	1	5
3	08MAR04	19MAR04	0	0	2	4	2	4
4	22MAR04	31MAR04	10	10	3	3	3	3
5	22MAR04	31MAR04	0	0	4	2	4	2
6	01APR04	01APR04	0	0	5	1	5	1
7	.	.	.	.	.	.	.	.
8	.	.	.	.	.	.	.	.
9	.	.	.	.	.	.	.	.
10	.	.	.	.	.	.	.	.

---


### Example 5.2: Adding Subtasks to a Project

In this example, the output data set from Example 5.1 is used as input to PROC PM. The following statements bring up the saved view of the project as shown in Output 5.2.1. Note that this view is identical to the view saved in Output 5.1.4.

```
proc pm data=softout1 project=softattr
    date='1mar04'd interval=weekday
    projname='Software Project'
    out=softout1;
```

```
act actid;  
succ succid;  
project pntid;  
duration duration;  
id activity;  
run;
```

## **Output 5.2.1 Project Schedule**

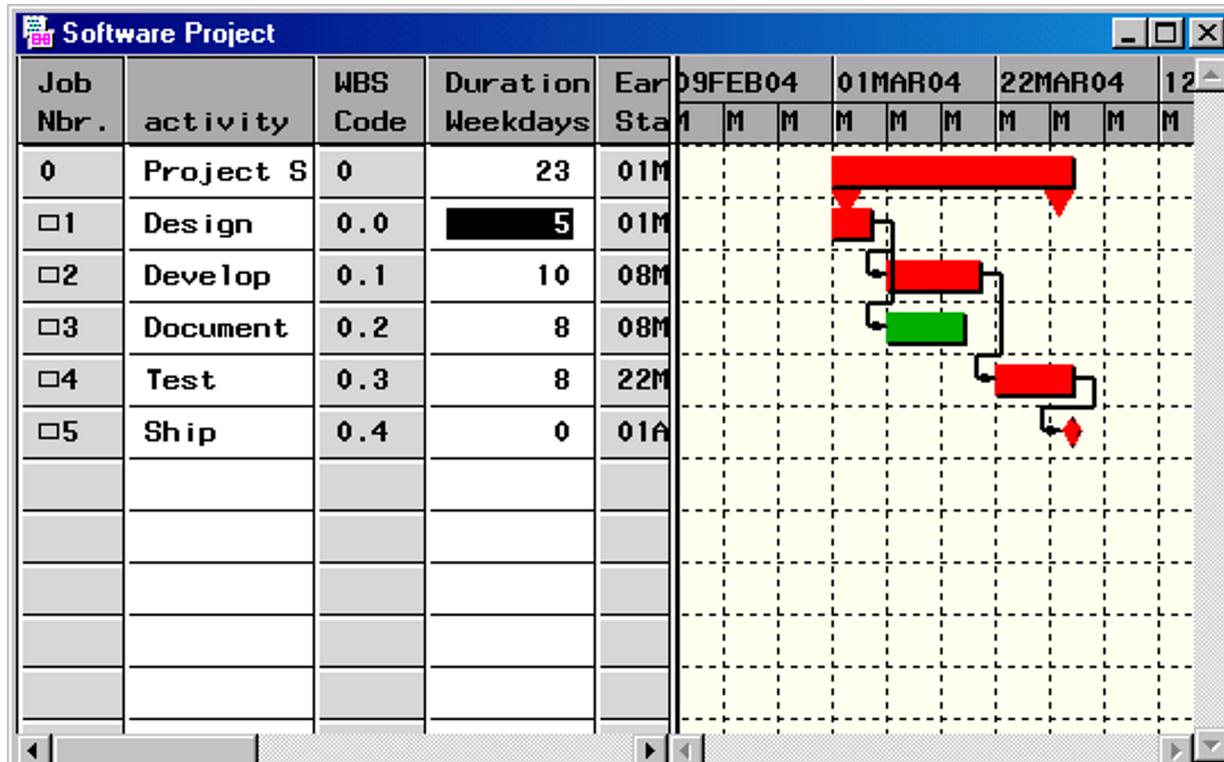

In the invocation of PROC PM, the output data set name is the same as the input data set. Thus, it is possible to make changes to the Activity data set using PROC PM and then save the results back to the original data set.

In the current view of the Software Project, you want to add some subtasks to the ‘Design’ and ‘Develop’ tasks. Suppose that these two tasks are broken into two subtasks each: one for ‘Module 1’ and the other for ‘Module 2.’ Further, you want to remove the precedence constraint between the ‘Design’ and ‘Develop’ phases and add constraints between the respective modules. You can accomplish these tasks by making the following editing changes in the PM window.

1. Use the Table View pop-up menu to add the following subtasks to ‘Design’:

**Module 1:** 5 days  
**Module 2:** 3 days


2. Add a link from ‘Module 1’ to ‘Module 2.’
  3. Use the Table View pop-up menu to add the following subtasks to ‘Develop’: 

**Module 1:** 6 days  
**Module 2:** 5 days

4. Add a link from ‘Module 1’ to ‘Module 2.’
5. Remove the link between the supertasks ‘Design’ and ‘Develop’ by clicking on the arc and selecting **Delete** from the pop-up menu.
6. Add a link from ‘Module 1’ under ‘Design’ to ‘Module 1’ under ‘Develop.’
7. Add a link from ‘Module 2’ under ‘Design’ to ‘Module 2’ under ‘Develop.’

The resulting project schedule is displayed in [Output 5.2.2](#) and saved in the data set SOFTOUT1. Note that the new project duration is 24 days.

**Output 5.2.2** Project Schedule

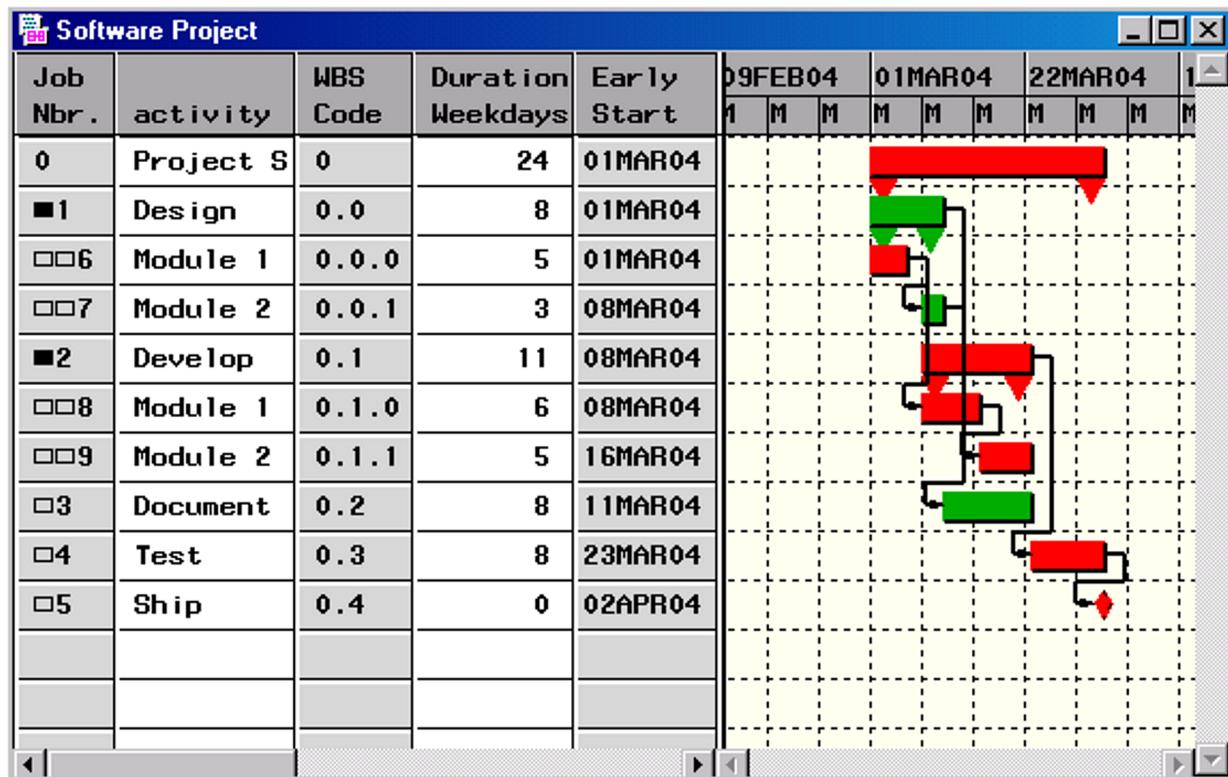

### Example 5.3: Saving and Comparing Baseline Schedules

This example shows you how to save a baseline schedule and use it for comparing new schedules. Recall that in [Example 5.2](#) the Schedule data are saved in the data set SOFTOUT1. Thus, the following invocation of PROC PM displays the Software project in its last saved state (as in [Output 5.2.2](#), but with the WBS codes filled in). At the end of the editing session, the schedule is saved in the data set SOFTOUT3.


```

proc pm data=softout1 project=softattr
  date='1mar04'd interval=weekday
  projname='Software Project'
  out=softout3;
  act actid;
  succ succid;
  project pntid;
  duration duration;
  id activity;
run;

```

Use the **Edit ► Set Baseline** pull-down menu (Figure 5.27) to save the current Early Schedule as a Baseline Schedule. The resulting display is shown in Output 5.3.1. Note that the Gantt View now shows the Baseline Schedule in addition to the Early Schedule. Also, the activities have been numbered to be sequential in the current view (see the section “Renumbering the Activities” on page 325).

#### Output 5.3.1 Using Baseline Schedules

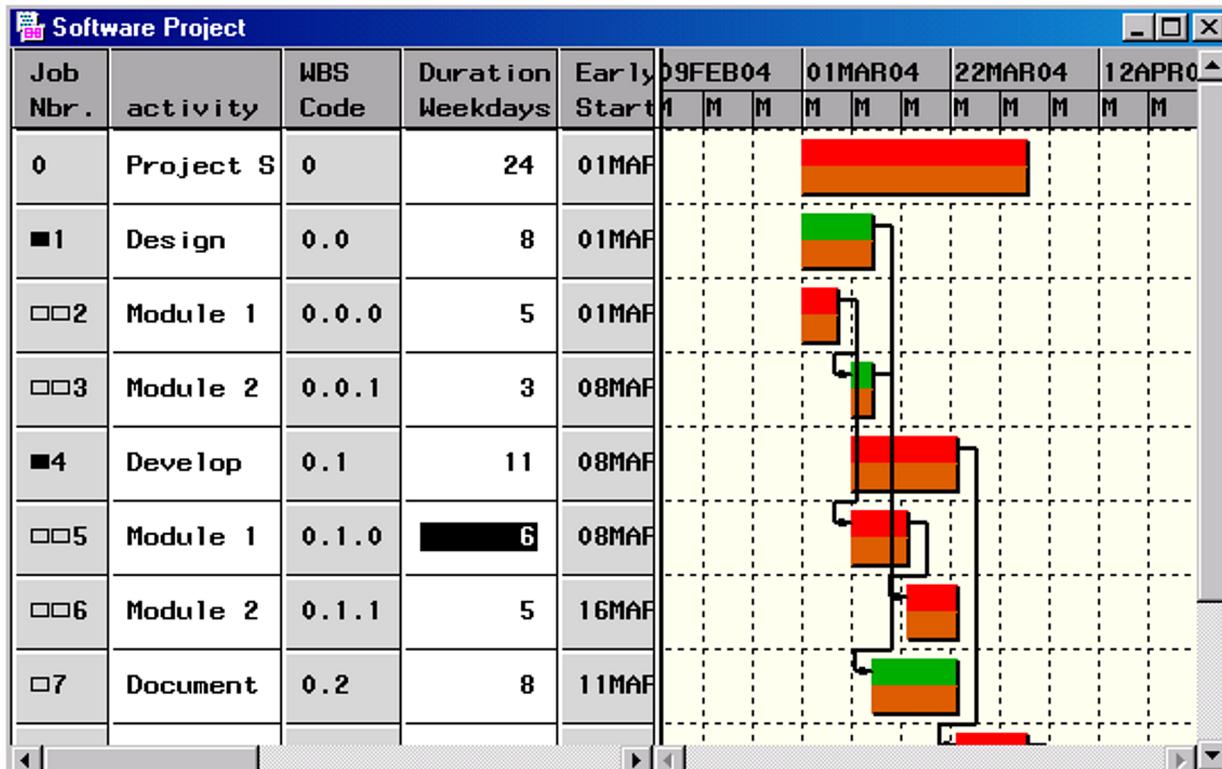


The baseline schedule is useful in determining the effect of changes to the project on the schedule. For example, suppose there is a directive from the director of your division that all the developers are required to attend a User Interface Standards Meeting before starting the development of Module 2. This meeting has been scheduled to start on March 15, 2004, and is expected to take 3 days. What is the effect of this directive on your project schedule?

To see the effect, you can make the following changes in the PM window:

1. Add a new task to the project by selecting **New Task** from the **Edit** pull-down menu.
2. To edit the newly entered task, you may need to scroll down.
3. Type in the name of the task: ‘UI Meeting.’ Set its duration to 3.
4. In the Gantt View, draw a link from this new task to Task 6 (‘Module 2’ under ‘Develop.’)
5. Also in the Gantt View, drag the task, ‘UI Meeting,’ to the tick mark corresponding to 15Mar04.

The resulting view is shown in [Output 5.3.2](#). Note that the view may differ depending on the display parameters of your device. It is easy to see that, due to the 3-day meeting that is mandated, there is a delay in the project schedule (the project duration is now 26 days).

**Output 5.3.2** Effect of UI Meeting on Schedule

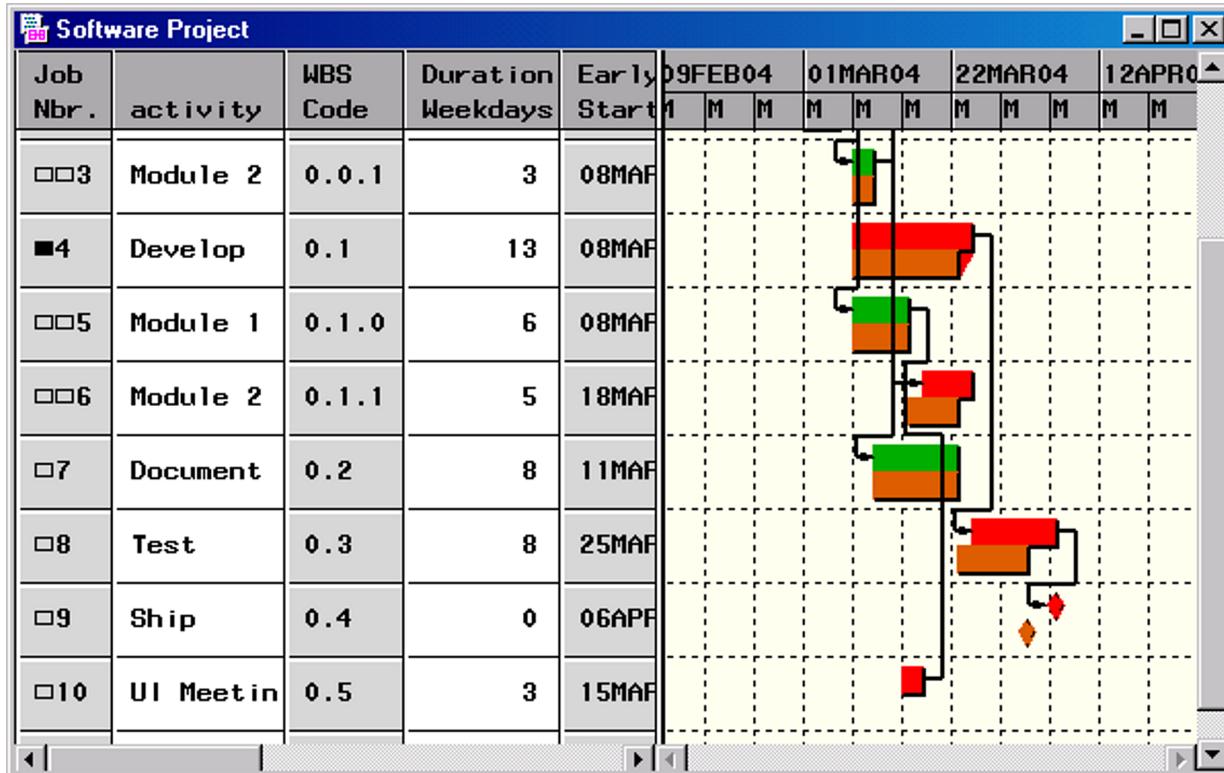

You can get a complete picture of the effect on the schedule by examining all the Schedule columns that are shown in the Table View. [Output 5.3.3](#) shows the Schedule columns, the Baseline columns, and the Target Date and Type columns in the Table View. To obtain this view, some of the columns have been moved and the Baseline Schedule bars (in the Gantt View) have been hidden from the display.

**Output 5.3.3** Table View Showing All Schedules

**Software Project**


Job Nbr.	activ	Dura Week	Early Start	Early Finish	Late Start	Late Finish	Baseline Start	Baseline Finish	Target Date	Targ Type	9
0	Projec	26	01MAR04	05APR04	03MAR04	05APR04	01MAR04	01APR04	.	.	
■1	Desig	8	01MAR04	10MAR04	03MAR04	17MAR04	01MAR04	10MAR04	.	.	
□□2	Modul	5	01MAR04	05MAR04	03MAR04	09MAR04	01MAR04	05MAR04	.	.	
□□3	Modul	3	08MAR04	10MAR04	15MAR04	17MAR04	08MAR04	10MAR04	.	.	
■4	Devel	13	08MAR04	24MAR04	10MAR04	24MAR04	08MAR04	22MAR04	.	.	
□□5	Modul	6	08MAR04	15MAR04	10MAR04	17MAR04	08MAR04	15MAR04	.	.	
□□6	Modul	5	18MAR04	24MAR04	18MAR04	24MAR04	16MAR04	22MAR04	.	.	
□7	Docum	8	11MAR04	22MAR04	25MAR04	05APR04	11MAR04	22MAR04	.	.	
□8	Test	8	25MAR04	05APR04	25MAR04	05APR04	23MAR04	01APR04	.	.	
□9	Ship	0	06APR04	06APR04	06APR04	06APR04	02APR04	02APR04	.	.	
□10	UI Me	3	15MAR04	17MAR04	15MAR04	17MAR04	.	.	15MAR04	SGE	

If the project delay resulting from the UI Meeting is of concern, you may want to schedule the meeting on an earlier date. Suppose the revised start date of the meeting is March 10, 2004. To see the effect of the change, you can do the following:

1. Revert to the saved project preferences so that both the Table and the Gantt Views are visible.
2. Use the **View** menu to move the Target Date column to the left in the Table View.
3. Scroll down, if necessary, to bring the task 'UI Meeting' into view.
4. Change the Target Date column for this task to '10Mar04.'

The resulting view is displayed in **Output 5.3.4**. Note that, as a result of this change, all the activities are back on schedule as the new schedule coincides with the saved baseline schedule. The last activity was defined after the baseline schedule had been saved in **Example 5.2**; hence, there is no baseline schedule bar for this activity. You can use the **Fill Missing Baseline** selection from the menu shown in **Figure 5.26** to set the baseline schedule for the 'UI Meeting' to be the current early schedule.

### **Output 5.3.4** Editing Target Date

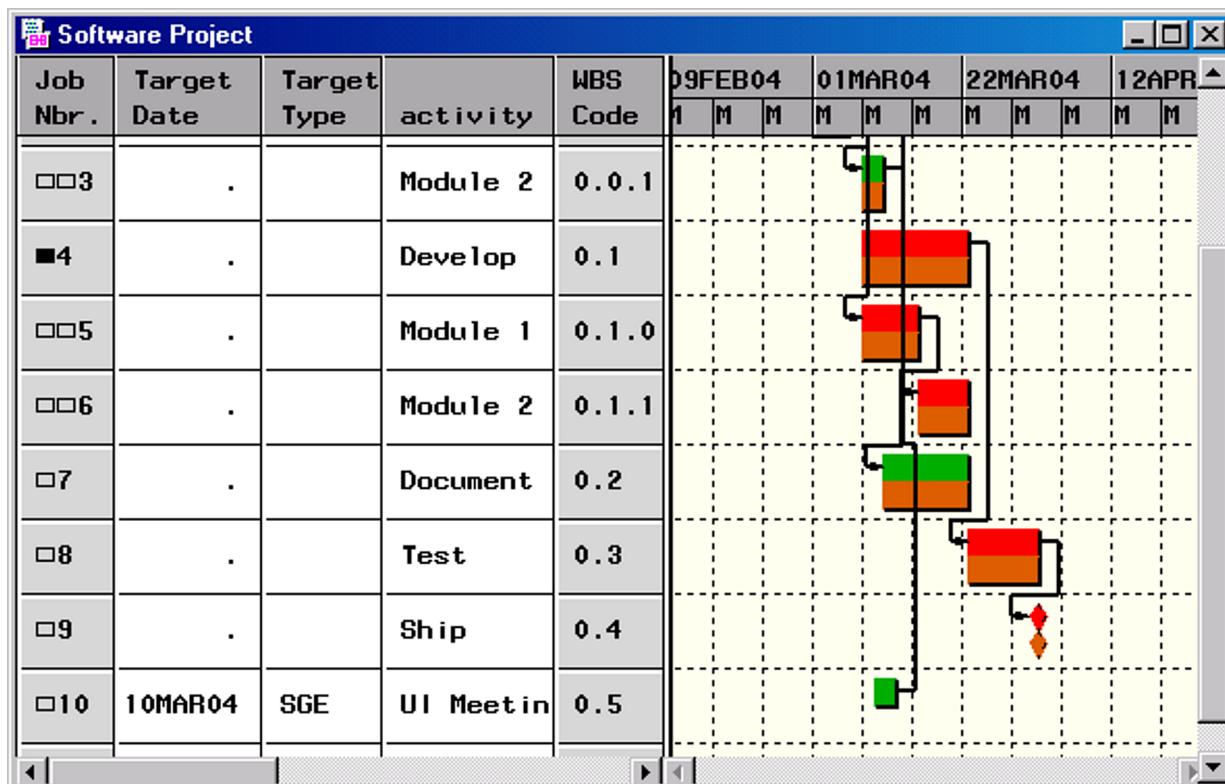

## Example 5.4: Effect of Calendars

Continuing with the project scenario in the preceding examples, you want to explore other ways of shortening the project duration. One possible alternative is to work overtime. As the project manager, you would like to see the effect on the schedule if you change the calendar for all the development tasks to a six-day calendar.

Calendars are defined using the [Calendar](#) data set, as in the CPM procedure. Alternately, if you are using the PROJMAN application, you can use the [Calendars window](#) to define a six-day calendar. This example defines a Calendar data set and invokes PROC PM as follows. Note that, in order to use calendars, the Activity data set needs to have a CALID variable, which is added in a simple DATA step.

```
* Define a Calendar data set identifying
* Saturday as a workday
;
data calendar;
  input calid calname $ _sat_ $;
 datalines;
1 Sixday WORKDAY
;
;

* Add the CALID variable to the Activity data set
* saved in the preceding example
;
data softout3;
  set softout3;
  calid=.;
run;
```


```

* Use softout3 as the Activity data set and specify ;
* the preceding calendar data set ;
proc pm data=softout3 project=softattr
  calendar=calendar
  date='1mar04'd interval=weekday
  projname='Software Project'
  out=softout4;
act actid;
succ succid;
project pntid;
duration duration;
id activity;
calid calid;
run;

```

When the PM procedure initializes the PM window, it attempts to restore all the display settings using the values in the Project data set, SOFTATTR. However, the new Activity data set has an extra variable, calid, which leads to two new columns in the Table View, one for the Activity Calendar (which displays the Calendar ID) and the other for the Calendar Name. These columns are added at the right end of the Table View and can be seen by scrolling to the right. The resulting view is displayed in [Output 5.4.1](#).

**Output 5.4.1** Calendar Columns

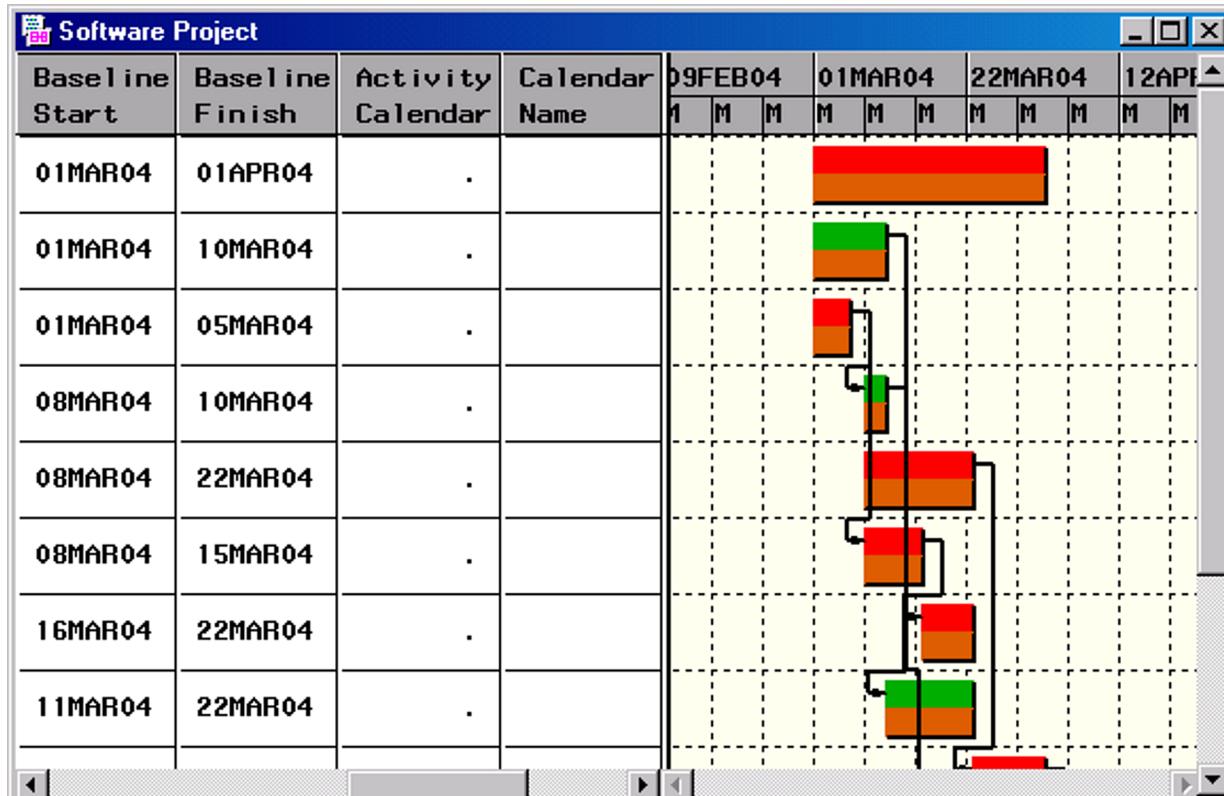


By default, all the activities are assumed to follow the standard five-day calendar. Now, you want to change the calendar for the supertask 'Develop' and all its subtasks to be the six-day calendar defined in the data set CALENDAR. Note that, in the calendar definition, it is sufficient to specify that Saturday is a working

day. All the other days of the week default to the default calendar's work pattern; see “Default Calendar” on page 102 in Chapter 4, “The CPM Procedure.”


To facilitate the editing of the calendar values and to see the effect on the project duration, reorder the columns (drag the columns in the Table Header) to display the activity, Activity Calendar, Calendar Name, and Duration columns in the Table View. You may need to move the dividing line between the Table and Gantt Views.

You can enter the Calendar values by typing the number 1 in the Activity Calendar column or the value 'Sixday' in the Calendar Name column. You can also use the Calendar pop-up menu in one of the calendar columns to select the desired calendar (see [Output 5.4.2](#)). Note that the project duration has reduced to 22 days as a result of the six-day calendar.

**Output 5.4.2** Effect of Six-Day Calendar

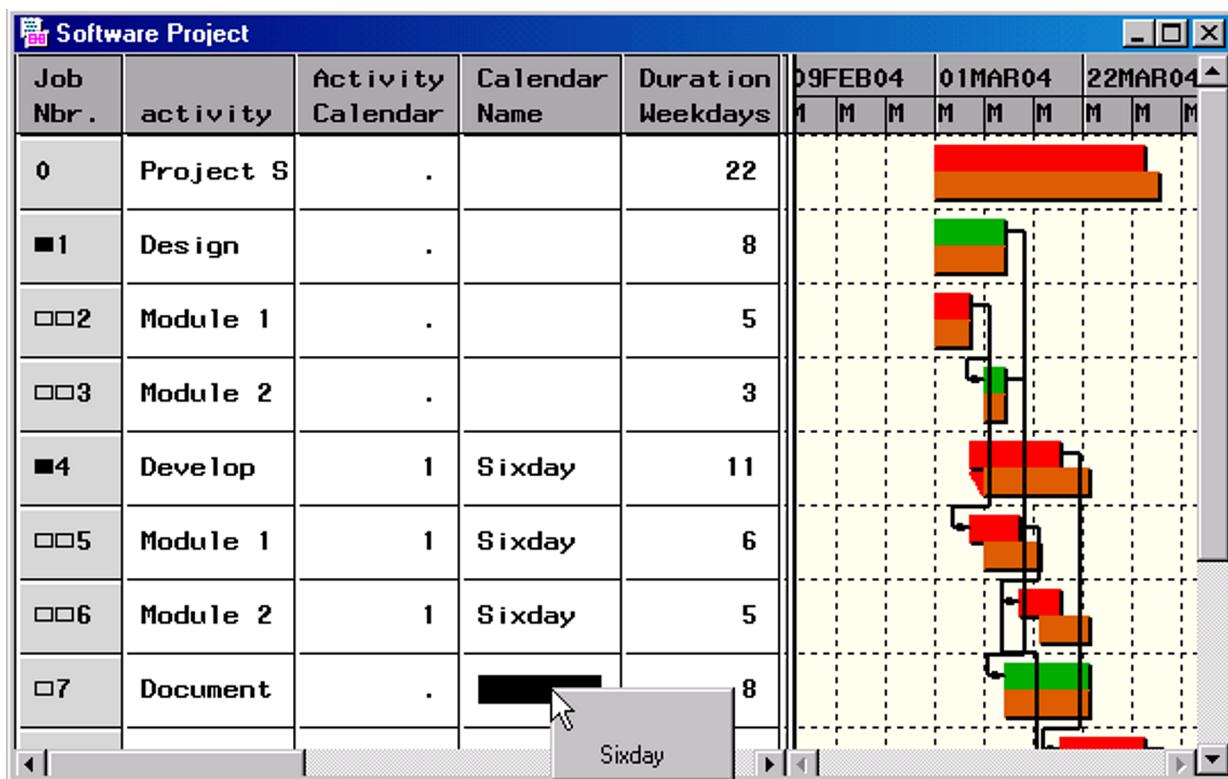

To see the effect on the individual activities, change the units to “Days” in the Gantt View and enlarge the Gantt View, as shown in [Output 5.4.3](#).

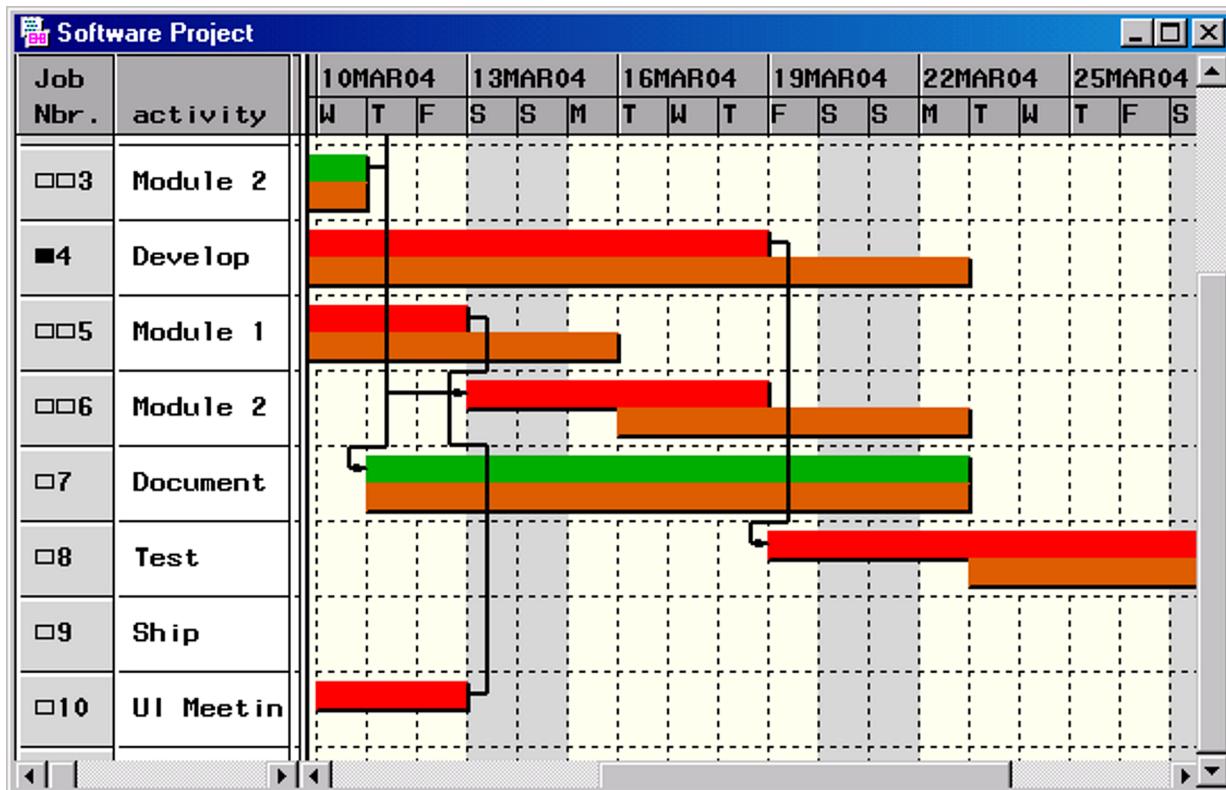**Output 5.4.3** Gantt View of Calendar Effect

## Example 5.5: Defining Resources

In all the preceding examples, it was assumed that you had enough resources to work on the different tasks. Unfortunately, as a project manager you need to schedule your project using the limited set of resources available to you. In this example, you will assign some project resources and schedule the project subject to resource constraints.

In order to assign resources to the tasks, you need to add resource variables to the Activity data set as well as define a resource availability (**Resource**) data set.

Suppose that the resources that you are interested in are Tester and Programmer. The following statements set up the project data needed to perform resource-constrained scheduling with PROC PM using the output data produced in [Example 5.4](#).

```
* Define a Resource data set specifying      ;
* 1 Tester and 1 Programmer as the          ;
* available resources                      ;
data resources;
  input _date_ date7. Tester  Programmer;
  datalines;
01jan04 1 1
;

* Add the resource variables Tester and      ;
* Programmer to the Activity data set       ;
```


```

* (the output data set saved in last example) ;
data softout4;
  set softout4;
  Tester=.;
  Programmer=.;
  run;

* Use softout4 as the Activity data set and      ;
* specify the preceding Resource data set.      ;
* Save the schedule in softout5.                 ;
proc pm data=softout4 project=softattr
  calendar=calendar
  resourcein=resources
  date='1mar04'd interval=weekday
  projname='Software Project'
  out=softout5;
act actid;
succ succid;
project pntid;
duration duration;
id activity;
calid calid;
resource Tester Programmer / per=_date_;
run;

```


Output 5.5.1 Adding Resources to the Project

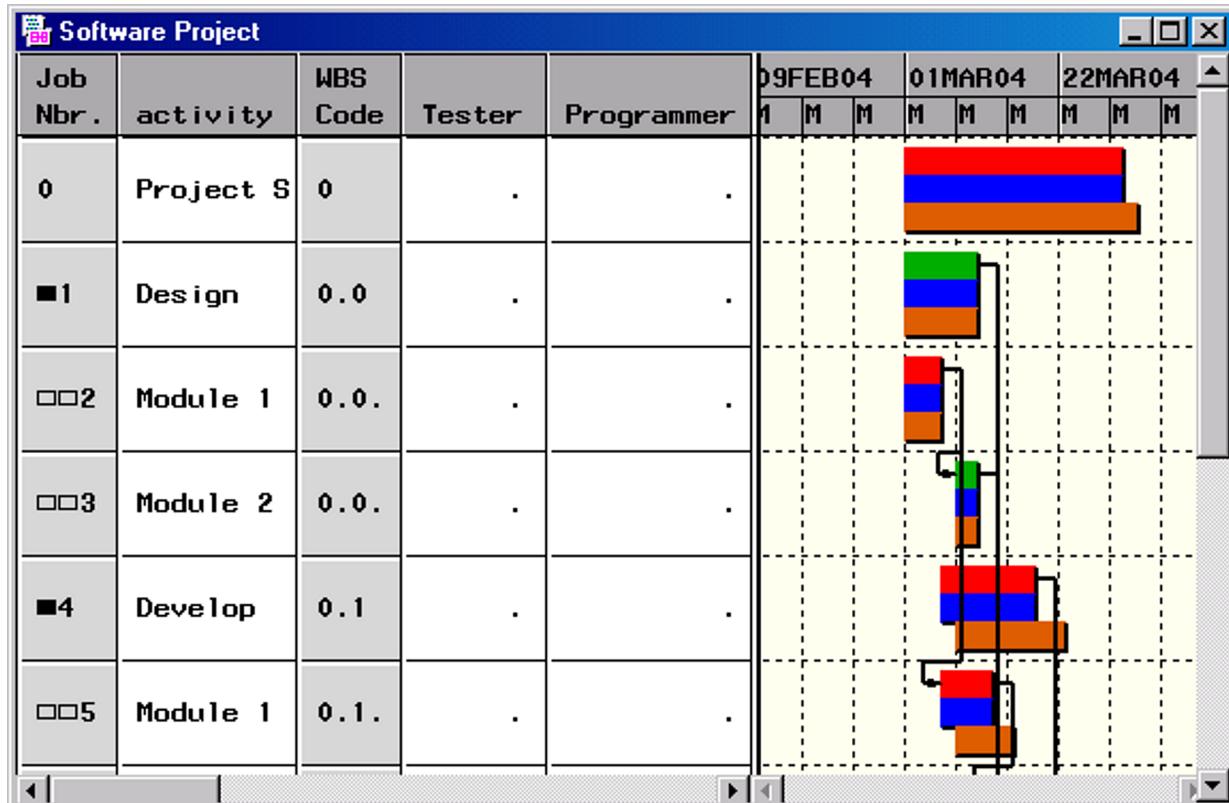

**Output 5.5.1** shows the Table and Gantt Views of the project after rearranging some of the columns and moving the dividing line to show the resource columns. The Resource Schedule bars are also brought into display by right-clicking on the background in the Gantt View and selecting **Resource Schedule**. The Resource Schedule bar is shown (in blue) between the Early Schedule bar and the Baseline Schedule bar. Note that the resource schedule coincides with the early schedule because no resource requirements have been specified for either of the two resources.

You can now use the Table View to enter the resource requirements for each task. Set the requirement for the resource Tester to '1' for the tasks 'Document' and 'Test,' and the requirement for the resource Programmer to '1' for the tasks numbered '2,' '3,' '5,' and '6.' The resulting schedule is displayed in [Output 5.5.2](#). In this view, the baseline schedule is not displayed. You can see that several of the tasks have been delayed, resulting in lengthening the project duration to 29 weekdays.

## **Output 5.5.2** Editing Resource Requirements

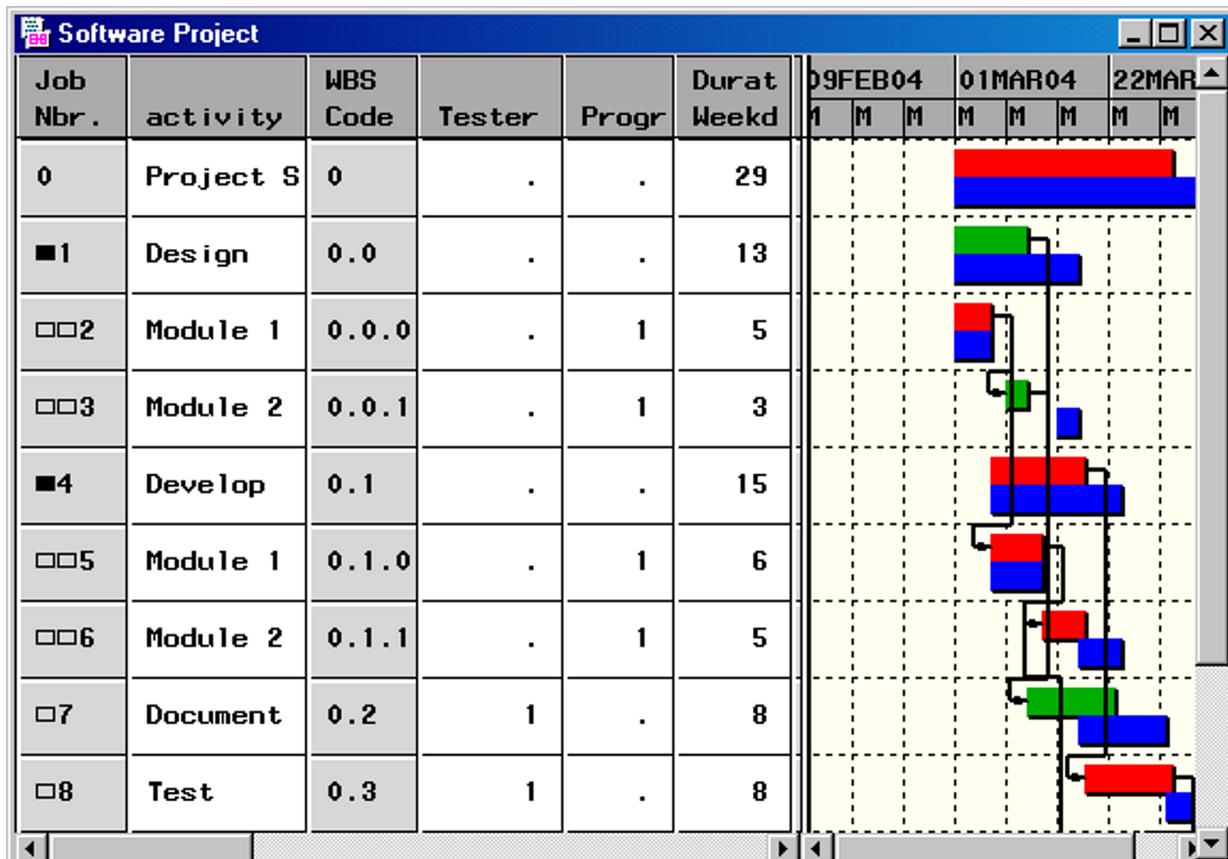

You can set the resource-constrained schedule as a baseline to do some “what-if” analysis. For example, suppose you would like to determine the effect of adding another programmer to the project. In order to change the resource availability, you need to save the current project, edit the Resource availability data set to add another programmer, and then reinvoke the PM procedure.

First, in the PM window displayed in [Output 5.5.2](#), do the following:


1. Display the Baseline Schedule bar again.
2. Use the **Replace Baseline** selection from the **Edit** menu to select the Resource Schedule as the new baseline schedule.
3. Save the project preferences.
4. Close the PM window.

Use the following statements to reinvoke PROC PM after defining a new resource availability:

```
* Change the resource availability for Programmer to 2 ;
data resources;
  input _date_ date7. Tester  Programmer;
  datalines;
01jan04  1  2
;

* Use softout4 as the Activity data set and specify ;
* the preceding Resource data set. ;
* Save the schedule in softout5. ;
proc pm data=softout4 project=softattr
  calendar=calendar
  resourcein=resources
  date='1mar04'd interval=weekday
  projname='Software Project'
  out=softout5;
act actid;
succ succid;
project pntid;
duration duration;
id activity;
calid calid;
resource Tester Programmer / per=_date_;
run;
```

Using the new resource availability, you reduced the project duration by five days. The resulting schedule is displayed in [Output 5.5.3](#), which also shows the baseline schedule corresponding to the earlier resource availability data set.

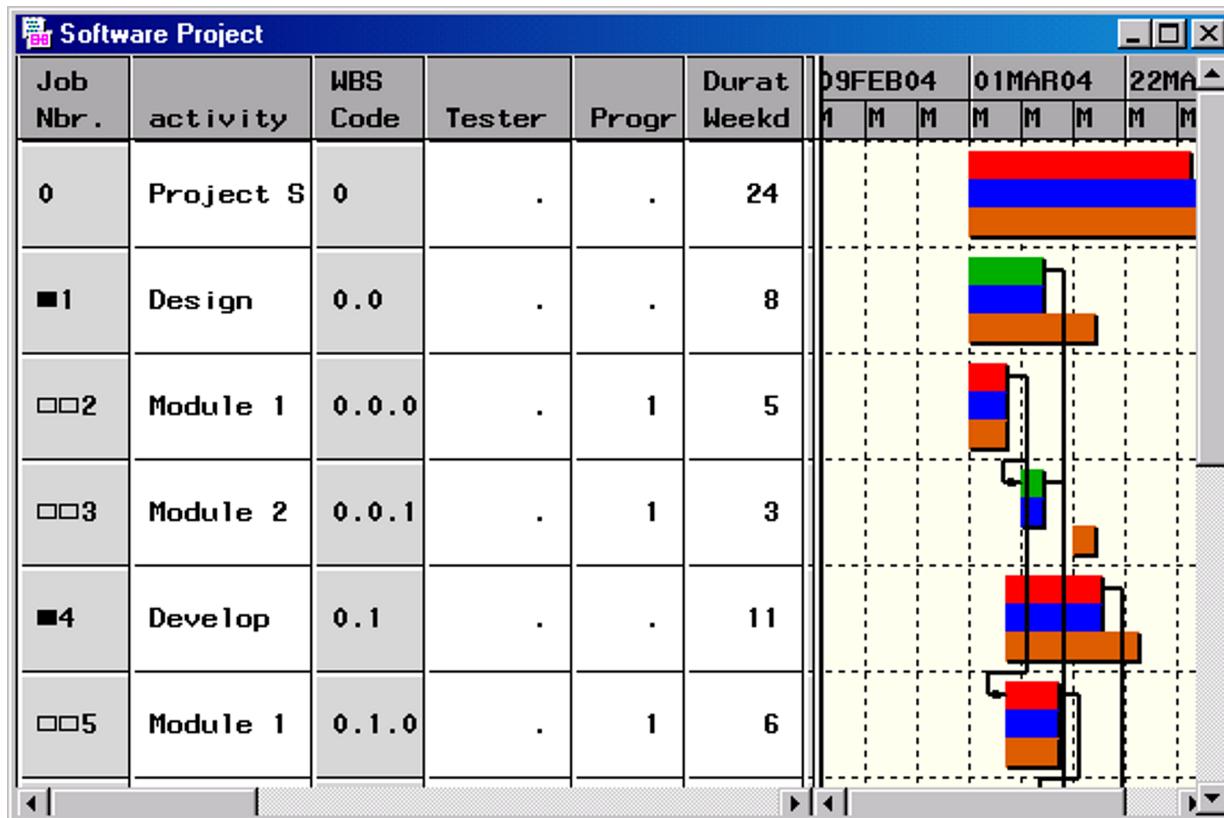**Output 5.5.3** Comparison of Two Resource Schedules

## Example 5.6: Editing Progress


Once a project plan has been established and the project is under way, a major part of a project manager's responsibility is to monitor the project as it progresses. This example uses the PM window to add progress information to the project and discusses some of the related editing functions.

In the final window of Example 5.5 (shown in Output 5.5.3), do the following:

1. Delete the baseline schedule using the **Edit** menu.
2. From the **Edit** menu, select **Add Progress**.

The resulting display is shown in Output 5.6.1. The Gantt View now shows the Actual Schedule bar between the Early Schedule bar and the Resource Schedule bar. It also displays a Timenow Line. Since no progress information has been entered, the Timenow Line is drawn at the beginning of the project and all the Actual Schedule bars show only a handle that can be used to drag progress for a particular task.


### Output 5.6.1 Adding Progress Information to Project

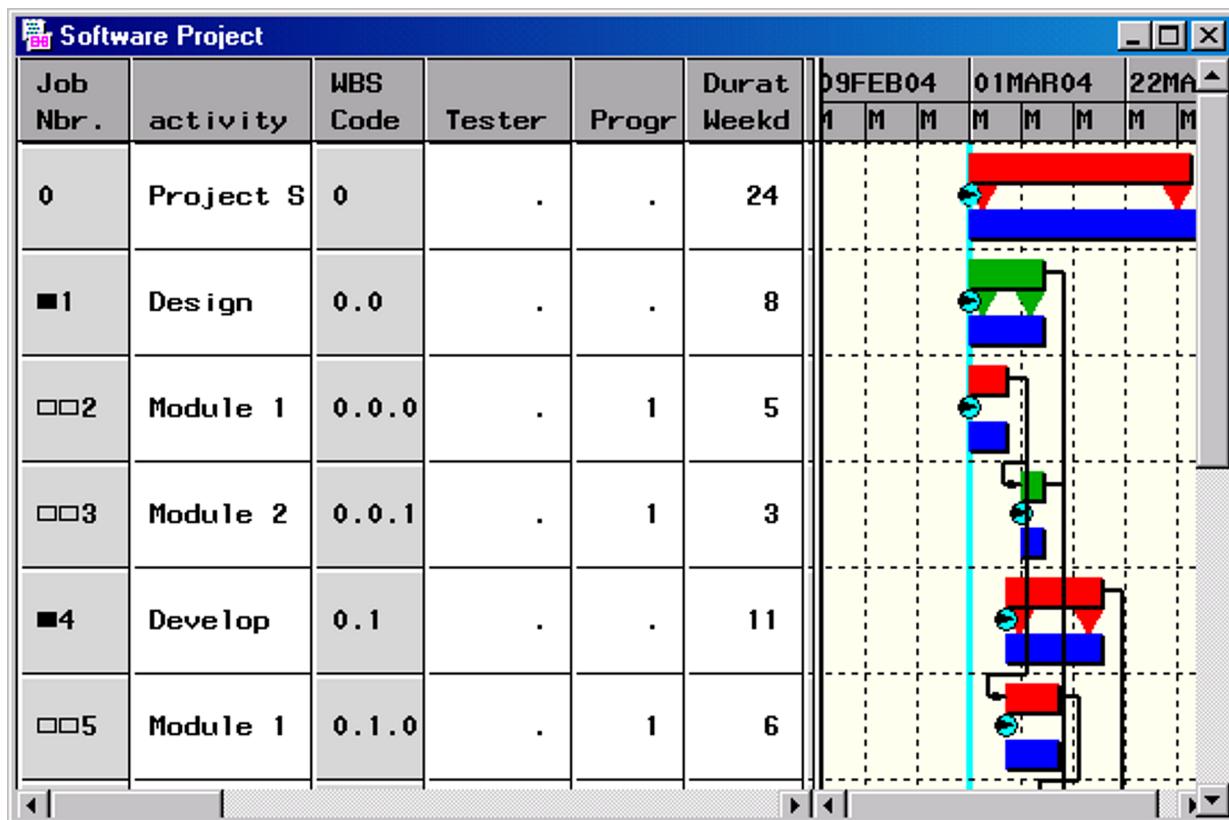

You can enter progress information in several ways:

- Drag the Timenow Line to update progress information for several tasks at once. The actual start and finish times (until the Timenow date) are set assuming that the tasks follow the resource-constrained schedule. (If there are no resource constraints, the tasks are assumed to follow the early schedule.)
- Use the handle on the Actual Schedule bar for a given task to drag the progress bar.
- Bring the Progress columns into view in the Table View and edit one of the Progress columns.

As an example, drag the Timenow Line to the tick mark corresponding to 15MAR04. The resulting window (after reordering and resizing some columns and scrolling the Gantt View) is shown in [Output 5.6.2](#).

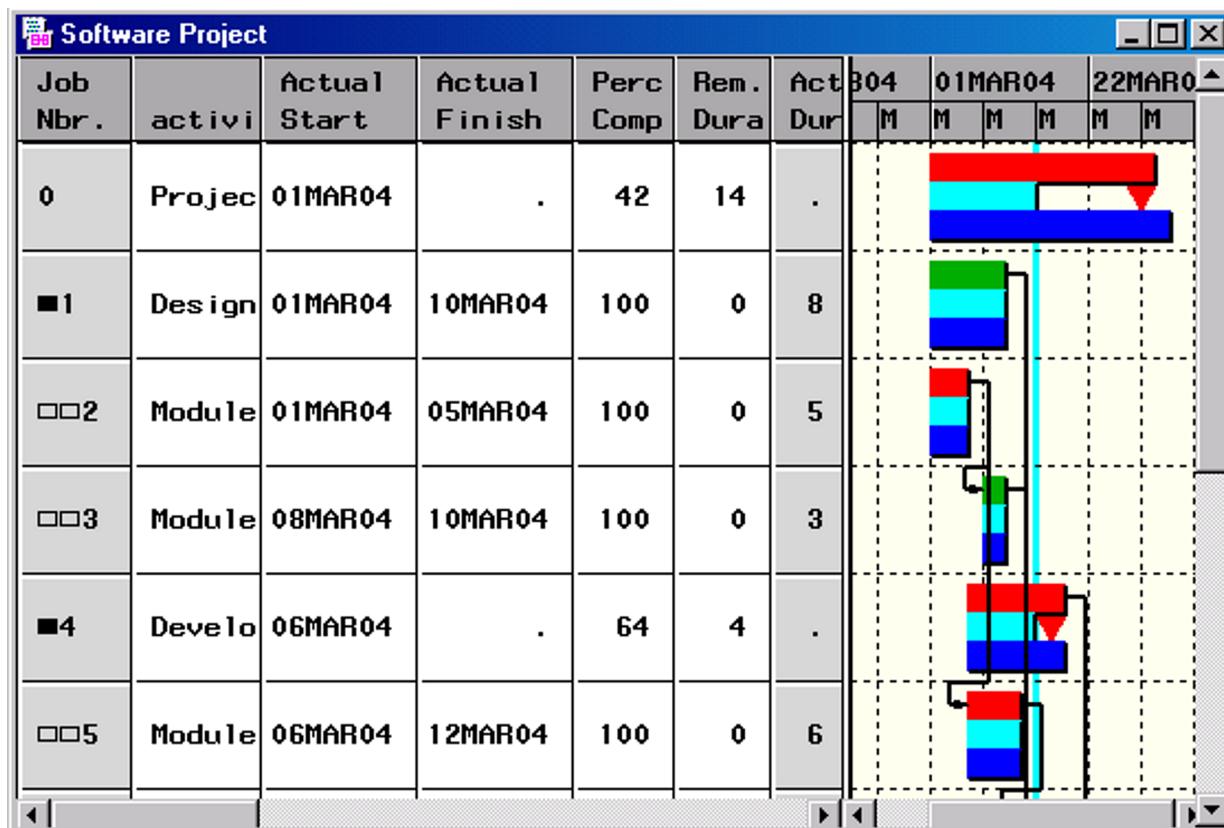**Output 5.6.2** Moving the Timenow Line

Note that some of the activities are completed while others are still in progress. If the project data are saved at this point, the Schedule data set will have all the Progress variables (A\_START, A\_FINISH, PCT\_COMP, and REM\_DUR). However, for the PM procedure to be able to recapture the exact state of the schedule as it was saved, it also needs to know the value of TIMENOW when the project data was last saved. This value ('15Mar04' for the current example) is saved as a macro variable named TIMENOW (see the section "Macro Variable TIMENOW" on page 326).

To see how the Actual information can be used from one invocation of PROC PM to the other, save the project as displayed in [Output 5.6.2](#) and then reinvoke PROC PM to continue editing the progress information. Note that if you are using the PROJMAN application, the value of TIMENOW is automatically saved by the application and used in subsequent editing of the project.

Recall from the last invocation of PROC PM that the data are saved in the data set SOFTOUT5. To use the saved progress information, invoke PROC PM as follows:

```
* Use softout5 as the Activity data set and specify ;
* the Resource data set defined in the last example. ;
* Save the schedule in softout6. ;
proc pm data=softout5 project=softattr
      calendar=calendar
      resourcein=resources
      date='1mar04'd interval=weekday
      projname='Software Project'
      out=softout6;
```

```


act actid;
succ succid;
project pntid;
duration duration;
id activity;
calid calid;
* Use the ACTUAL statement to specify the Progress variables ;
* and the value of TIMENOW saved from the previous invocation ;
actual / as=a_start af=a_finish
      remdur=rem_dur pctcomp=pct_comp
      timenow=&timenow;
resource Tester Programmer / per=_date_;
run;

```

The preceding program displays the PM window for the updated Software project. Now use the Table View to edit some of the Progress columns. To do so, you can either scroll to the Progress Columns or move these columns to the left in the Table View using the appropriate selection from the **View** menu (Figure 5.9).


Task number 6 ('Module 2' under 'Develop') has a Remaining Duration value of 4. Now, you may notice that you have misjudged the amount of work involved and that you need only one more day to finish the task. Enter 1 in the Remaining Duration column. This editing change immediately causes the Percent Complete column to update to 50, indicating that 50% of the work is completed. The resulting effect on the project schedule is shown in Output 5.6.3 (the window has been scrolled down so that the second half of the project is visible). Note that reducing the duration of the 'Module' task did not affect the project end date; the duration of the project is still 24 days. Studying the schedule of the 'Document' and 'Test' tasks, you notice that the delay to the project is caused by the fact that the resource-constrained schedule of the task 'Test' is delayed due to resource constraints.

**Output 5.6.3** Editing the Remaining Duration Column

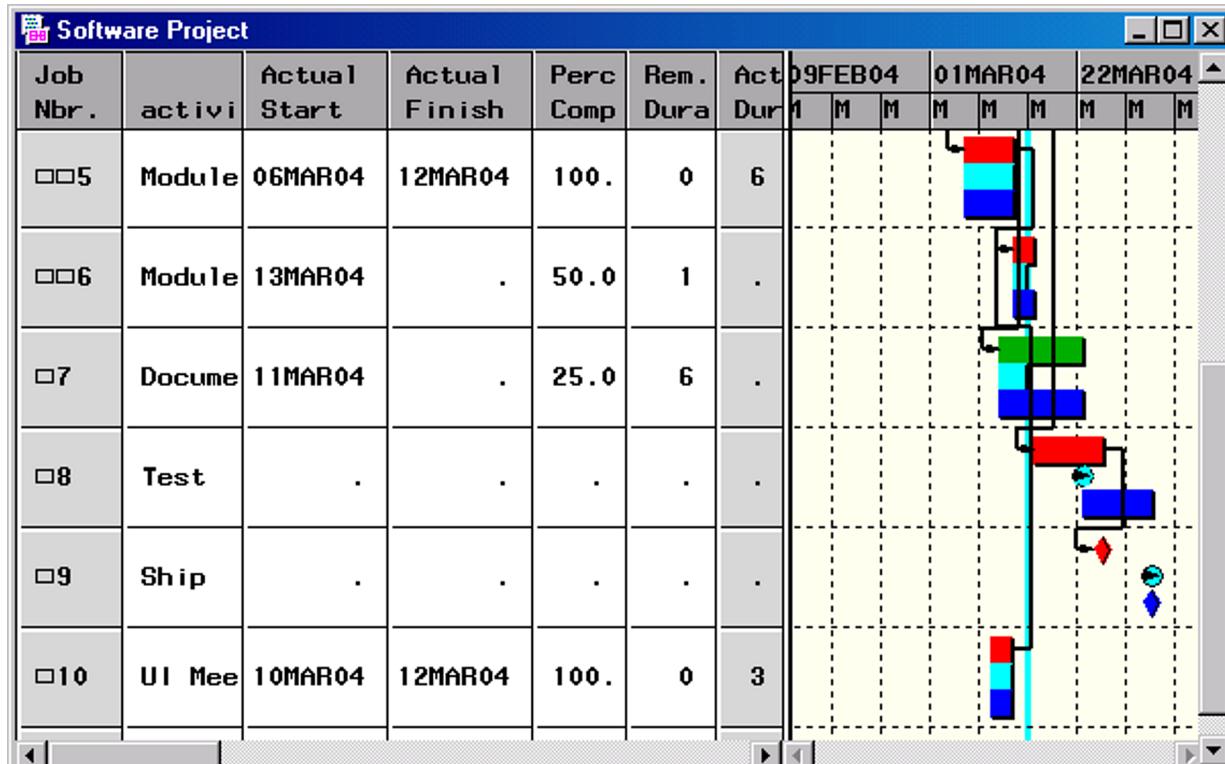

In addition to revising the progress information for ‘Module 2,’ you also realize that the ‘Document’ task is 50% complete as of the Timenow date. Edit the Percent Complete column in the Table View, changing the value from 25.0 to 50.0. Immediately, the Remaining Duration column changes to 2. The resulting window is shown in [Output 5.6.4](#). The project end date (for the resource-constrained schedule) is 28Mar04. Thus, the project duration is now reduced to 20 days.

**Output 5.6.4** Editing the Percent Complete Column

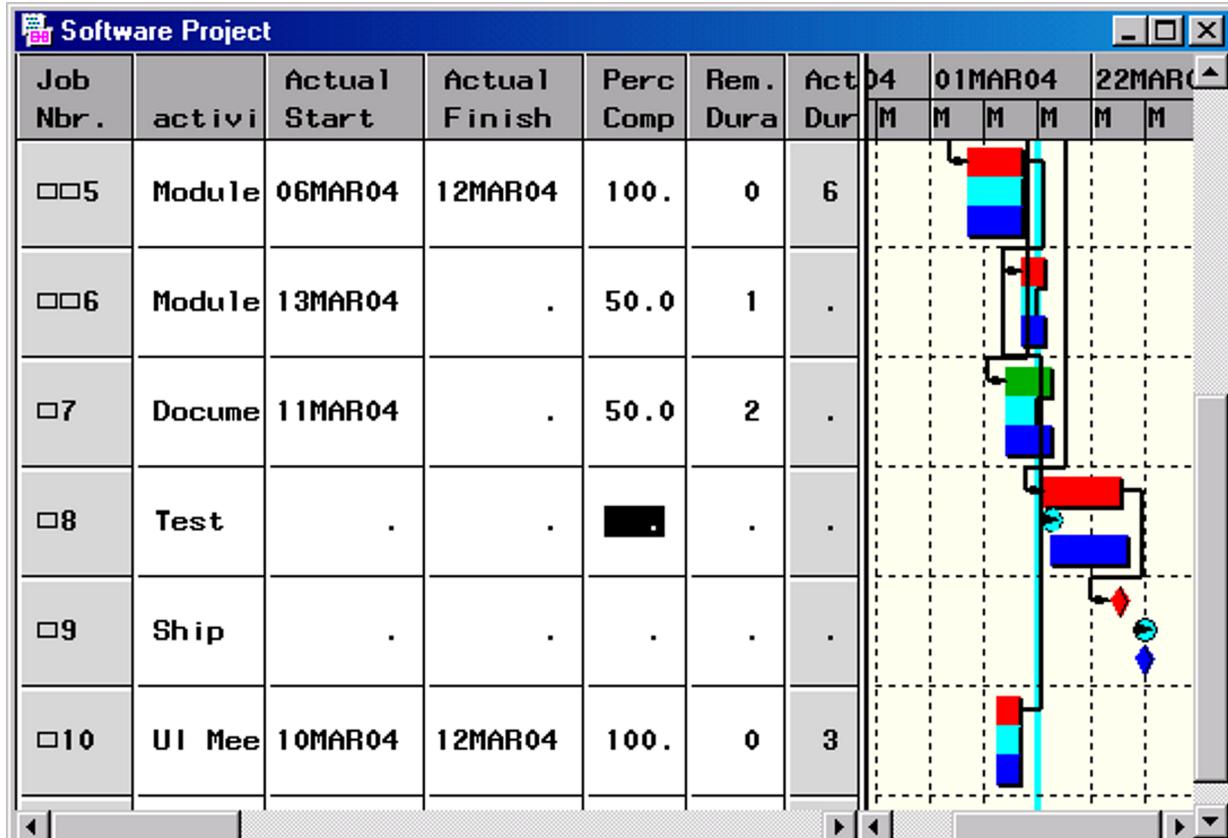



# Chapter 6

# The Microsoft Project Conversion Macros

## Contents

---

Overview: Microsoft Project Conversion Macros . . . . .	353
%MSPTOSAS . . . . .	354
%MSPTOSAS Macro Parameters . . . . .	354
%MSPTOSAS Macro Output . . . . .	355
%SASTOMSP . . . . .	359
%SASTOMSP Macro Parameters . . . . .	359
Default Values . . . . .	364
Examples: The Microsoft Project Conversion Macros . . . . .	364
Example 6.1: Simple %MSPTOSAS Conversion . . . . .	365
Example 6.2: Importing Activity Attributes . . . . .	366
Example 6.3: Importing Multiple Projects . . . . .	368
Example 6.4: Importing XML Files . . . . .	369
Example 6.5: Simple %SASTOMSP Conversion . . . . .	370
Example 6.6: Exporting Data Set and Variable Names . . . . .	372
Example 6.7: Exporting Calendars and Holidays . . . . .	373
Example 6.8: Exporting Resource-Constrained Schedules . . . . .	376
Example 6.9: Round Trip between a SAS Program and Microsoft Project . . . . .	378

---

## Overview: Microsoft Project Conversion Macros

The SAS macro %MSPTOSAS is available for converting Microsoft Project data to a form that is readable by the PM procedure. The %MSPTOSAS macro converts Microsoft Project 98, 2000, 2002, 2003, 2007, and 2010 data. The macro generates the necessary SAS data sets, determines the values of the relevant options, and enables you to invoke an instance of the PM procedure with the converted project data. Execution of this macro requires SAS/ACCESS<sup>®</sup> Interface to PC File Formats software.

The %SASTOMSP macro converts data sets used by the CPM and PM procedures into a form that is readable by Microsoft Project 2000, 2002, and 2003.

**NOTE:** Microsoft Project 98, 2000, 2002, 2003, 2007, and 2010 are registered trademarks of Microsoft Corporation.

## %MSPTOSAS

%MSPTOSAS is a SAS macro that converts Microsoft Project data saved in an MDB (Microsoft Access database) or XML format into data sets that are readable by the PM procedure. %MSPTOSAS requires specification of the location and name of either the MDB or the XML file (but not both), and it requires specification of the version of Microsoft Project that was used to create input. You can also include optional arguments to specify a location for storing SAS data sets, to control the mode of the PM procedure invocation, or to run the %MSPTOSAS macro on UNIX.

The %MSPTOSAS macro converts the hierarchical relationships, precedence relationships, time constraints, resource availabilities, resource requirements, project calendars, task calendars, resource calendars, holiday information, work-shift information, actual start and finish times, and baseline start and finish times. In addition, the task custom fields are extracted and stored in the Task\_Attributes data set.

---

### %MSPTOSAS Macro Parameters

```
%MSPTOSAS (LIBRARY=library, MAPFILE=mapfile,  
           MDBFILE=mdbfile, VERSION=version,  
           VIEWPM=indicator, XMLFILE=xmlfile,  
           DBMS=identifier, SERVER=pc-server-hostname,  
           PORT=port-number);
```

#### General Project Parameters

##### **LIBRARY=***library*

specifies the location of the directory for storing the SAS data sets and the file *callpm.sas*. This parameter can be either a SAS library reference or a path. A path can be specified with double quotes, single quotes, or no quotes. See the **MDBFILE=** parameter for an example. After a successful run of the %MSPTOSAS macro, the library reference ‘mspout’ is assigned to this path. The default value of the **LIBRARY=** parameter is **WORK**, which is the default libref that is generally assigned to your temporary SAS data library for the current session or job.

##### **MDBFILE=***mdbfile*

specifies the location and filename of the MDB file. This parameter can be either a SAS file reference or a filename. A filename can be specified with double quotes, single quotes, or no quotes. One of **MDBFILE=** or **XMLFILE=** is required, but they cannot both be specified.

##### **XMLFILE=***xmlfile*

specifies the location and filename of the XML file. This parameter can be either a SAS file reference or a filename. A filename can be specified with double quotes, single quotes, or no quotes. One of **MDBFILE=** or **XMLFILE=** is required, but they cannot both be specified.

##### **MAPFILE=***mapfile*

specifies the location and filename of the XML map file. The map file is a separate XML document that contains specific XML map syntax. The map file tells the XML engine how to interpret the XML markup in order to successfully import the XML document. This parameter can only be used when **XMLFILE=** is specified. The value of **MAPFILE=** can be either a SAS file reference or a filename. A

filename can be specified with double quotes, single quotes, or no quotes. If XMLFILE= is specified and MAPFILE= is not, a map file named mspxml.map will be created in the WORK directory and used as the XML map file. For more information related to the XML engine and XML map syntax, refer to SAS XML LIBNAME Engine User's Guide.

#### **VERSION=***version*

specifies the version of Microsoft Project used to create the MDB or XML file. The supported versions for MDB files are 98, 2000, 2002 and 2003. The supported versions for XML files are 2002, 2003, 2007, and 2010. This parameter is required; there is no default value. For example, to convert an MDB file from Microsoft Project 2003 format, you need to specify VERSION=2003.

#### **VIEWPM=***indicator*

controls the mode of the PM procedure invocation. The value VIEWPM=1 invokes the PM procedure in interactive mode, and the value VIEWPM=0 invokes the PM procedure in NODISPLAY mode. This parameter is optional; the default value is 1.

### **UNIX Parameters**

The following statements are available to establish a connection from SAS running on UNIX to a SAS PC Files Server. This enables you to run the %MSPTOSAS macro on UNIX. For more information, see *SAS/ACCESS Interface to PC Files: Reference*.

#### **DBMS=***identifier*

specifies the type of data to import. In this case, the value DBMS=accessscs must be specified.

#### **PORT=***port-number*

specifies the port or service name that the SAS PC Files Server is listening to on the PC. The default value is 8621.

#### **SERVER=***pc-server-hostname*

specifies the name of the computer on which you started the PC files server. This name is required by UNIX users to connect to this server machine and is reflected on the server control panel. This hostname can be specified as a simple computer name (e.g., wxp320), a fully qualified network name (e.g., wxp320.domain.com), or an IP address.

### **%MSPTOSAS Macro Output**

Once the file conversion is complete, the %MSPTOSAS macro uses the information from the MDB or XML file in a call to the PM procedure. The %MSPTOSAS conversion macro generates the following SAS data sets:

- Activity data set: Activity
- Calendar data set: Calendar
- Holiday data set: Holiday
- Workday data set: Workday

- Resource data set: Resource
- Schedule data set: Schedule
- Task attributes data set: Task\_Attributes
- Preferences data set: Prefs

In addition, the macro generates the SAS code that enables you to reinstate your project in current and future SAS sessions. The name of the file containing this SAS code is callpm.sas. The data sets and callpm.sas file are created in the location specified by the **LIBRARY=** parameter. For more information about data sets, variables, options, and statements related to the PM procedure, refer to Chapter 5, “The PM Procedure.”

The following statements are taken from a callpm.sas file:

```
Libname mspout "C:\MSPROJ";
PROC PM data = mspout.Activity project=mspout.Prefs
  caledata = mspout.Calendar
  workdata = mspout.Workday
  out=mspout.Schedule
  interval=dtday
  date="17DEC06:08:00:00"dt
  daylength=" 8:00"t
  suppressobswarn
  setfinishmilestone;
activity ACTID;
successor SUCCUID / LAG = LAG;
duration DURATION;
project PNTUID;
id ACTIVITY ACTUID;
run;
```

## Activity Data Set

Table 6.1 lists and describes the variables in the data set Activity. For more information about the activity data set in the PM procedure, see the section “Input Data Sets and Related Variables” on page 135 in Chapter 4, “The CPM Procedure.”

**Table 6.1** Variables in the Data Set Activity

Variable	Type	Description
_CAL_	Numeric	Activity calendar variable
A_START	Numeric	Actual start variable
A_FINISH	Numeric	Actual finish variable
ACTID	Numeric	Activity variable; has different values in the data set schedule
ACTIVITY	Character	Activity name variable; used as an ID variable in the PM procedure
ACTUID	Numeric	Variable uniquely identifying activities in the data sets Activity, Schedule, and Task_Attributes
ALGNDATE	Numeric	Alignment date variable

**Table 6.1** (continued)

Variable	Type	Description
ALGNTYPE	Character	Alignment type variable
ASSN_WORK	Numeric	Resource work variable
B_START	Numeric	Baseline start date variable
B_FINISH	Numeric	Baseline finish date variable
DURATION	Numeric	Duration variable
LAG	Character	Lag variable
PNTUID	Numeric	Parent variable
SUCCUID	Numeric	Successor variable
TASK_ID	Numeric	Position identifier of the current activity in the list of activities

## Calendar Data Set

The data set Calendar contains basic calendar data used by the PM and CPM procedures. If a task has "elapsed" duration in Microsoft Project, a special calendar is defined on 24-hour days and 7-day weeks, including holidays and other nonworking days. This calendar is associated with the tasks that have "elapsed" durations. For more information, see the section "[Multiple Calendars](#)" on page 101 in Chapter 4, "[The CPM Procedure](#)."

## Holiday Data Set

Table 6.2 lists and describes the variables in the data set Holiday. For more information, see the section "[Multiple Calendars](#)" on page 101 in Chapter 4, "[The CPM Procedure](#)."

**Table 6.2** Variables in the Data Set Holiday

Variable	Type	Description
_CAL_	Numeric	Holiday calendar variable
HFINISH	Numeric	Holiday finish variable
HOLIDUR	Numeric	Holiday duration variable
HSTART	Numeric	Holiday start variable

## Workday Data Set

Each variable in the data set WORKDAY defines a shift in the workday. For more information, see the section "[Multiple Calendars](#)" on page 101 in Chapter 4, "[The CPM Procedure](#)."

## Resource Availability Data Set

The data set Resource contains information about the resources required by the activities in the project. In addition to resource variables, the variables in Table 6.3 are included in the data set Resource. For more information, see the section "[Resource Usage and Allocation](#)" on page 113 in Chapter 4, "[The CPM Procedure](#)."

**Table 6.3** Variables in the Data Set Resource

Variable	Type	Description
AVAILDTE	Numeric	Resource availability date/time variable
OBSTYPE	Character	Observation type variable

## Schedule Data Set

The data set Schedule contains the schedule determined by the PM procedure. This data set is described in the section “Schedule Data Set” on page 327 in Chapter 5, “The PM Procedure.” In addition to the standard schedule variables, the Schedule data set created by the %MSPTOSAS macro contains the variables ACTUID and ACTIVITY. Since ACTUID and ACTIVITY are also present in the Activity and Task\_Attributes data sets, these variables enable you to identify activities and select a subset of the variables in these three data sets to create your report.

## Task Attributes Data Set

The data set Task\_Attributes stores task attribute variables. The variables in **Table 6.4** take their names from Microsoft Project custom fields. If you have renamed a custom field in Microsoft Project, then the name you specified for that field is used as the label for the corresponding SAS variable. A custom field can be converted only if it has at least nondefault values for at least one task or if the field has been renamed in Microsoft Project. The variables in the data set Task\_Attributes can have enterprise versions (e.g., Enterprise Cost1) and enterprise project versions (e.g., Enterprise Proj Cost1) if your project has enterprise fields defined with the Microsoft Enterprise Global Template and Enterprise Project Versions.

**Table 6.4** Variables in the Data Set Task\_Attributes

Variable	Type	Description
Cost1–10	Numeric	Custom cost fields in Microsoft Project
Date1–30	Numeric	Custom date fields in Microsoft Project
Duration1–10	Numeric	Custom duration fields in Microsoft Project
Finish1–10	Numeric	Custom finish date/time fields in Microsoft Project
Flag1–20	Character	Custom flag fields in Microsoft Project
Number1–20	Numeric	Custom number fields in Microsoft Project
Outlinecode1–10	Character	Custom outline code fields in Microsoft Project
Start1–10	Numeric	Custom start date/time fields in Microsoft Project
Text1–10	Character	Custom text fields in Microsoft Project

In addition to the variables in the preceding table, the data set Task\_Attributes converts the following variables from Microsoft Project: HYPERLINK, HYPERLINKADDRESS, HYPERLINKSUBADDRESS, NOTES, TASK\_COST, TASK\_WBS, TASK\_PCT\_COMP, TASK\_PCT\_WORK\_COMP, TASK\_PRIORITY, and TASK\_Rem\_DUR.

In the data set Task\_Attributes, the variable DURATION\_ELAPSED indicates whether the task duration is “elapsed” in Microsoft Project. When a task duration is elapsed, the special calendar n099999 is associated with this task in the Activity data set. See the section “Calendar Data Set” on page 357 for details.

Finally, the data set Task\_Attributes contains the ACTUID and ACTIVITY variables. These variables are also

contained in the data sets Activity and Schedule.

**NOTE:** For MDB files created in Microsoft Project 98, the only variables present in the data set Task\_Attributes are ACTUID, ACTIVITY, DURATION\_ELAPSED, TASK\_COST, TASK\_PCT\_COMP, TASK\_PCT\_WORK\_COMP, TASK\_PRIORITY, TASK\_Rem\_DUR, and TASK\_WBS.

### Project Preference Data Set

The data set Prefs is created by the PM procedure to save and restore preferences that control the project view. For more information, see the section “[Saving and Restoring Preferences](#)” on page 323 in Chapter 5, “The PM Procedure.”

## %SASTOMSP

%SASTOMSP is a SAS macro that converts data sets used by the PM and CPM procedures into a file that is readable by Microsoft Project 2000, 2002, and 2003.

**NOTE:** The MDB file created by the %SASTOMSP macro cannot be read directly by versions of Microsoft Project dated 2007 or later. This issue can be circumvented by opening the MDB file in Microsoft Project 2003, then saving the file in a format supported by versions of Microsoft Project dated 2007 or later (.mpp or .xml, for example).

The macro converts information that is common to both the CPM and PM procedures and Microsoft Project, including hierarchical relationships, precedence relationships, time constraints, resource availabilities, resource requirements, project calendars, resource calendars, task calendars, holiday information, and work-shift information. In addition, the early and late schedules, the actual schedule, the resource-constrained schedule, and the baseline schedule are also extracted and stored as start-finish fields.

### %SASTOMSP Macro Parameters

```
%SASTOMSP(PROJ_NAME=project_name, LIBRARY=library,
MDBFILE=mdbfile, ACTDS=SAS-data-set,
CALDS=SAS-data-set, HOLDS=SAS-data-set,
WORKDS=SAS-data-set, RESDS=SAS-data-set,
SCHEDULEDS=SAS-data-set, _INTERVAL=_interval,
_DATE=_date, _FBDATE=_fbdate,
_DAYSTART=_daystart, _DAYLENGTH=_daylength,
_CALID=variable, _ACTIVITY=variable,
_ID=variable, _DUR=variable,
_ALIGNDATE=variable, _ALIGNTYPE=variable,
_HEAD=variable, _TAIL=variable, _PROJECT=variable,
_SUCCESSOR=_successor, _LAG=_lag,
_HOLISTART=variable, _HOLIEND=variable,
_HOLIDUR=variable, _RESOURCE=_resource,
_RESOBSTYPE=variable, _RESPERIOD=variable,
DBMS=identifier, SERVER=pc-server-hostname,
PORT=port-number);
```

## General Project Parameters

### **LIBRARY=***library*

specifies the location of the input SAS data sets. This parameter can be either a SAS library reference or a path. A path can be specified with double quotes, single quotes, or no quotes. For example, in the following %SASTOMSP invocation, a path is specified with double quotes:

```
%sastomsp(library="C:\SASPROJ", mdbfile=C:\MSPROJ\filename.mdb);
```

The default value is ‘WORK’, which is the default libref generally assigned to your temporary SAS data library for the current session or job.

### **MDBFILE=***mdbfile*

specifies the output MDB file. This parameter can be either a SAS fileref or a filename. A filename can be specified with double quotes, single quotes, or no quotes.

If *mdbfile* does not have the file extension .mdb, the macro checks whether it is an assigned fileref. If *mdbfile* is a fileref, the macro creates an MDB file as specified by this fileref. If *mdbfile* is not a fileref, the resulting MDB file takes the value of *mdbfile* as the prefix and is created in the location specified by the **LIBRARY=** parameter.

If *mdbfile* is a fileref, the macro creates an MDB file as specified by this fileref. If you are running the %MSPTOSAS macro on UNIX, *mdbfile* has to be a filename.

If *mdbfile* is a filename without a path, then the %SASTOMSP macro uses the default path of the OUTFILE= option of PROC EXPORT. In many cases, this default path is ‘C:\Documents and Settings\username\’. See the PROC EXPORT documentation in *Base SAS Procedures Guide* for details.

This parameter is required; there is no default value.

### **PROJ\_NAME=***project\_name*

specifies the name of the project. The default value is ‘Project Imported from SAS’.

## Input Data Set Parameters

### **ACTDS=SAS-data-set**

specifies the name of the Activity data set used by the PM and CPM procedures. The default value is ACTIVITY. For more information, see the section “[Input Data Sets and Related Variables](#)” on page 135 in Chapter 4, “[The CPM Procedure](#).”

### **CALDS=SAS-data-set**

specifies the name of the Calendar data set used by the PM and CPM procedures. There is no default value. This parameter is required when the project uses special calendars. If the project uses the standard calendar defined by the INTERVAL=, DAYSTART=, and DAYLENGTH= parameters, then the CALDS= parameter is optional. For more information, see the section “[Multiple Calendars](#)” on page 101 in Chapter 4, “[The CPM Procedure](#).”

### **HOLDS=SAS-data-set**

specifies the name of the Holiday data set used by the PM and CPM procedures. There is no default value. This parameter is required only if the project uses holidays defined in a Holiday data set. For more information, see the section “[Multiple Calendars](#)” on page 101 in Chapter 4, “[The CPM Procedure](#).”

**RESDS=SAS-data-set**

specifies the name of the Resource data set used by the PM and CPM procedures. There is no default value. This parameter is required only if the project requires resource information defined in a Resource data set. For more information, see the section “[Resource Usage and Allocation](#)” on page 113 in Chapter 4, “[The CPM Procedure](#).”

**SCHEDULEDS=SAS-data-set**

specifies the name of the Schedule data set generated by the PM procedure, as described in [Chapter 5](#). You can alternatively specify a Schedule data set generated by the CPM procedure, as described in the section “[Schedule Data Set](#)” on page 327 in Chapter 5, “[The PM Procedure](#).“ The SCHEDULEDS= parameter has no default value. When this parameter is specified, the macro stores the SAS schedules in Microsoft Project date fields, as shown in [Table 6.5](#).

**Table 6.5** SAS Schedule Conversion

Schedule	SAS Variables	Microsoft Project Fields
Early schedule	E_START, E_FINISH	SAS_E_start, SAS_E_finish
Late schedule	L_START, L_FINISH	SAS_L_start, SAS_L_finish
Resource-constrained schedule	S_START, S_FINISH	SAS_R_start, SAS_R_finish
Actual schedule	A_START, A_FINISH	SAS_A_start, SAS_A_finish
Baseline schedule	B_START, B_FINISH	SAS_B_start, SAS_B_finish

In Microsoft Project, you can display these date fields by going to the **Insert** menu, selecting **Column**, and selecting the fields you want to display. You can also display the schedule in a Gantt chart. See [Example 6.8](#) for details.

**WORKDS=SAS-data-set**

specifies the name of the Workday data set used by the PM and CPM procedures. There is no default value. This parameter is required only when the specified calendar refers to special work shifts defined in a Workday data set. For more information, see the section “[Multiple Calendars](#)” on page 101 in Chapter 4, “[The CPM Procedure](#).“

**Variable and Option Parameters****\_ACTIVITY=variable**

specifies the name of the variable in the Activity data set that contains the names of the tasks. The default value is ACTIVITY.

**\_ALIGNDATE=variable**

identifies the variable in the Activity data set that specifies the date to be used to constrain an activity to start or finish on a particular date. This variable is optional, and it has no default value.

**\_ALIGNTYPE=variable**

identifies the variable in the Activity data set that specifies whether the date value specified in the ALIGNDATE= parameter is the earliest start date, the latest finish date, and so forth, for the activity in the observation. This variable is optional, and it has no default value.

**\_CALID=variable**

identifies the variable that is used in the Activity, Holiday, and Calendar data sets to identify the calendar to which each observation refers. When this parameter is not specified, the macro uses a default variable named \_CAL\_ in each of the three data sets.

**\_DATE=\_date**

specifies the SAS date, time, or datetime that is to be used as an alignment date for the project. The default value is the current value of the SAS system time.

**\_DAYLENGTH=\_daylength**

specifies the length of the workday. The default value is '8:00't, if \_INTERVAL is specified as 'WORKDAY' or 'DTWRKDAY'. Otherwise, the default value is '24:00't.

**\_DAYSTART=\_daystart**

specifies the start of the workday. The default value is '9:00't, if \_INTERVAL is specified as 'WORKDAY' or 'DTWRKDAY'. Otherwise, the default value is '0:00't.

**\_DUR=variable**

identifies the variable in the Activity data set that contains the durations of the tasks. The default value is 'DUR'.

**\_FBDATE=\_fbdate**

specifies the SAS date, time, or datetime that specifies a project deadline. When this parameter is specified, the project is scheduled according to this project finish time.

**\_HEAD=variable**

identifies the variable in the Activity data set that contains the name of the node on the head of an arc in the project network. This parameter is required when the project is in AOA (Activity-on-Arc) format.

**\_HOLIDUR=variable**

identifies the variable in the Holiday data set that specifies the duration of the holiday. This variable is used to calculate the finish time of a holiday. If the \_HOLIEND= parameter is specified, any value specified for the \_HOLIDUR= parameter is ignored. This variable is optional; it has no default value.

**\_HOLIEND=variable**

identifies the variable in the Holiday data set that specifies the finish time of each holiday. This variable is optional, and it has no default value.

**\_HOLISTART=variable**

identifies the variable in the Holiday data set that specifies the start time of each non-workday. This variable is optional, and it has no default value.

**\_ID=\_id**

defines a string that lists the ID variables, separated by a space. The format of the \_ID= parameter is *id1 id2 ... idn*, where *n* is the number of ID variables. When this parameter is specified, the macro passes ID variables to Microsoft Project. You can view them in Microsoft Project by inserting the columns 'text1' through 'textn'.

**\_INTERVAL=***interval*

specifies the interval units by which task durations are measured. Possible values are DAY, WEEK, WEEKDAYS, WORKDAY, MONTH, QTR, YEAR, HOUR, MINUTE, SECOND, DTDAY, DTWRKDAY, DTWEEK, DTMONT, DTQTR, DTYEAR, DTHOUR, DTMINUTE, and DTSECOND. The default value of \_INTERVAL= is DAY.

**\_LAG=***lag*

defines a string that lists the lag variables, separated by a space. The format of the \_LAG= parameter is *lag1 lag2 ... lagn*, where *n* is the number of lag variables.

**NOTE:** Microsoft Project does not enable predecessors of a summary task to have a finish-to-finish or start-to-finish dependency.

**NOTE:** Microsoft Project does not permit the use of lag calendars. The %SASTOMSP macro converts calendar information. The names (or IDs) of lag calendars assigned to activities are saved in a text field in Microsoft Project called “Lag Calendars in SAS.”

**\_PROJECT=***variable*

identifies the variable in the Activity data set that specifies the project to which an activity belongs. This parameter is required when tasks have hierarchical relationships.

**\_RESOBSTYPE=***variable*

identifies the character variable in the Resource data set that contains the type identifier for each observation. The \_RESOBSTYPE= parameter is required if the RESDS= parameter is specified.

**\_RESOURCE=***resource*

defines a string that lists the resource variables, separated by a space. The \_RESOURCE= parameter is required if the RESDS= parameter is specified. The format of the *resource* parameter is *res1 res2 ... resn*, where *n* is the number of resource variables.

**\_RESPERIOD=***variable*

identifies the variable in the Resource data set that specifies the date from which a specified level of the resource is available for each observation with the \_RESOBSTYPE= variable equal to ‘RESLEVEL.’

**\_SUCCESSOR=***successor*

defines a string that lists the successor variables in the Activity data set, separated by a space. The format of the \_SUCCESSOR= parameter is *succ1 succ2 ... succn*, where *n* is the number of successor variables. If this parameter is not specified, the macro identifies all variables in the Activity data set having names prefixed with ‘SUCC’ as successor variables.

**\_TAIL=***variable*

identifies the variable in the Activity data set that contains the name of the node on the tail of an arc in the project network. This parameter is required when the project is in AOA format.

## UNIX Parameters

The following statements are available to establish a connection from SAS running on UNIX to a SAS PC Files Server. This enables you to run the %SASTOMSP macro on UNIX. For more information, see *SAS/ACCESS Interface to PC Files: Reference*.

**DBMS=***identifier*

specifies the type of data to import. In this case, the value DBMS=accessscs must be specified.

**PORT=***port-number*

specifies the port or service name that the SAS PC Files Server is listening to on the PC. The default value is 8621.

**SERVER=***pc-server-hostname*

specifies the name of the computer on which you started the PC Files Server. This name is required by UNIX users to connect to this server machine and is reflected on the server control panel. This hostname can be specified as a simple computer name (e.g., wxp320), a fully qualified network name (e.g., wxp320.domain.com), or an IP address.

## Default Values

Table 6.6 summarizes the list of parameters that have default values.

**Table 6.6** Default Values

Parameter	Default Value
ACTDS	ACTIVITY
_ACTIVITY	ACTIVITY
_CALID	_CAL_
_DATE	SAS system date
_DAYLENGTH	'8:00't, when _INTERVAL is 'WORKDAY' or 'DTWRKDAY'; '24:00't, otherwise
_DAYSTART	'9:00't, when _INTERVAL is 'WORKDAY' or 'DTWRKDAY'; '0:00't, otherwise
_DUR	DUR
_INTERVAL	DAY
LIBRARY	'WORK' library
PROJ_NAME	'Project Imported from SAS'
_SUCCESSOR	List of all variables in Activity data set having names prefixed with 'SUCC'

## Examples: The Microsoft Project Conversion Macros

Since both the %MSPTOSAS and %SASTOMSP macros involve input and output activities, we assume for the sake of convenience that 'C:\MSPROJ\' is a valid path in the operating environment where the input or output files are located. You may need to replace the path appearing in the example programs before running them.


**NOTE:** Using Microsoft Access 2007 to open the provided Microsoft Project sample files might elicit the security warning 'Certain content in the database has been disabled'. The message can be safely ignored.

The aforementioned sample files are named mspas1.mdb, mspas2.mdb, mspas3.mdb, and mspas4.mdb.

## Example 6.1: Simple %MSPTOSAS Conversion

This example illustrates the use of the %MSPTOSAS macro. Consider the following project created in Microsoft Project 98, as shown in [Output 6.1.1](#).

**Output 6.1.1** Microsoft Project Window

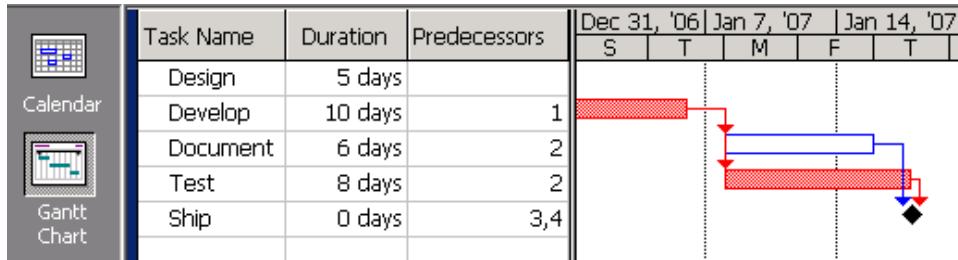

You can use the following call to the %MSPTOSAS macro to convert the MS Project file and view it in the PM window:


```
%msptosas (mdbfile=C:\MSPROJ\mspas1.mdb, version=98)
```

Alternatively, you can specify the MDB file by using a file reference, as in the following example:

```
filename mspref "C:\MSPROJ\mspas1.mdb";
%msptosas (mdbfile=mspref, version=98)
```

The PM window containing the preceding project is displayed in [Output 6.1.2](#).

**Output 6.1.2** PM Window

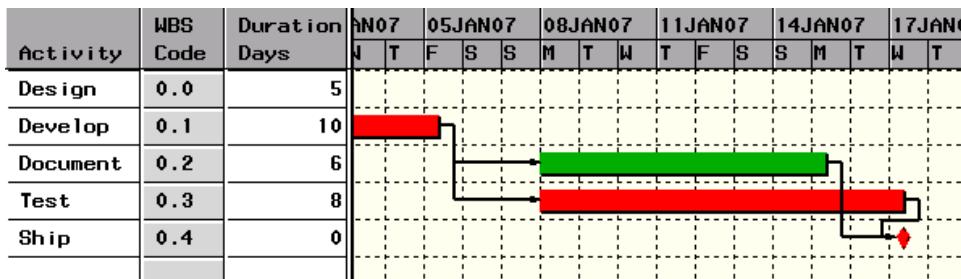

Because the LIBRARY= parameter is not specified, the default value ‘WORK’ is used. All eight data sets and the callpm.sas file are created in the ‘WORK’ library. The library reference ‘mspout’ is also assigned to this output library.

A partial view of the data set Activity generated during the conversion is shown in [Output 6.1.3](#).

### Output 6.1.3 Activity Data Set

ACTUID	SUCCUID	DURATIO	PNTUID	ACTIVITY	ALGNDAT	ALGNTYP	_CAL_
1000000	.	.	.	mspsas1	17DEC2006	SGE	1000001
1000001	.	5	1000000	Design	.	.	1000001
1000002	.	10	1000000	Develop	.	.	1000001
1000003	.	6	1000000	Document	.	.	1000001
1000004	.	8	1000000	Test	.	.	1000001
1000005	.	0	1000000	Ship	.	.	1000001
1000001	1000002	5	.	.	.	.	.
1000002	1000003	10	.	.	.	.	.
1000002	1000004	10	.	.	.	.	.
1000003	1000005	6	.	.	.	.	.
1000004	1000005	8	.	.	.	.	.

A partial view of the data set Schedule generated during the conversion is shown in Output 6.1.4.


### Output 6.1.4 Schedule Data Set

Observation Type	Activity Variable	ACTIVITY	DURATION	Successor Variable	WBS Code for the Activity	ACTUID	Early Start	Early Finish
SCHEDULE	0	mspsas1	23	.	0	1000000	18DEC06:08:00:00	17JAN07:16:59:59
SCHEDULE	1	Design	5	.	0.0	1000001	18DEC06:08:00:00	22DEC06:16:59:59
SCHEDULE	2	Develop	10	.	0.1	1000002	25DEC06:08:00:00	05JAN07:16:59:59
SCHEDULE	3	Document	6	.	0.2	1000003	08JAN07:08:00:00	15JAN07:16:59:59
SCHEDULE	4	Test	8	.	0.3	1000004	08JAN07:08:00:00	17JAN07:16:59:59
SCHEDULE	5	Ship	0	.	0.4	1000005	17JAN07:16:59:59	17JAN07:16:59:59
LOGIC	1	Design	5	2	.	.	.	.
LOGIC	2	Develop	10	3	.	.	.	.
LOGIC	2	Develop	10	4	.	.	.	.
LOGIC	3	Document	6	5	.	.	.	.
LOGIC	4	Test	8	5	.	.	.	.

Note that in the Activity and Schedule data sets, there can be more than one observation associated with one activity. Some observations contain information about predecessor-successor relationships (LOGIC observations); the other observations contain the remaining activity information.

## Example 6.2: Importing Activity Attributes

This example demonstrates the ability of the %MSPTOSAS macro to import Microsoft Project custom fields to a SAS data set. Consider the Microsoft Project window displayed in Output 6.2.1. The tasks and their precedence relationships are the same as in Example 6.1, but the version of the Microsoft Project is 2003 and there are two custom fields: “Flag1” and “Text1” (“Text1” is renamed as “Department Num.”)

**Output 6.2.1** Microsoft Project Window

To convert this project, use the following SAS macro call:

```
%msptosas (mdbfile=C:\MSPROJ\msspsas2.mdb, version=2003)
```

After the conversion, the PM window is the same as in [Output 6.1.2](#). However, in the resulting data set `Task_Attributes` there are two more variables: `Flag1` and `Text1` (`Text1` has the label “Department Num.”). Note that the three data sets `Task_Attributes`, `Activity`, and `Schedule` have two variables in common: `ACTUID` and `ACTIVITY`. `ACTUID` is numeric; `ACTIVITY` is character. Different activities can have identical `ACTIVITY` values, but each activity has a unique `ACTUID` value. Hence we recommend using `ACTUID` to identify the activities. For example, if you want to create a table consisting of the variables `ACTIVITY` and `DURATION` from the `Activity` data set, `E_START` and `E_FINISH` from the `Schedule` data set, and `Flag1` and `Text1` from the `Task_Attributes` data set, you can use the following SAS statements:

```
proc sql;
  create table merged as
    select a.ACTIVITY, a.DURATION,
      b.E_START, b.E_FINISH, c.Flag1, c.Text1
    from mspout.Activity a, mspout.Schedule b,
      mspout.Task_attributes c
    where a.ACTUID=b.ACTUID=c.ACTUID
      and a.ACTIVITY is not missing;
quit;
```

These statements merge variables from individual data sets. The variable `ACTUID` is used to identify activities; `a.ACTIVITY is not missing` is used to skip the logic observations.

The resulting data set `Merged` appears in [Output 6.2.2](#).

**Output 6.2.2** Merged Data Set

ACTIVITY	DURATION	Early Start	Early Finish	Flag1	Department Num.
mspsas2		18DEC06:08:00:00	17JAN07:16:59:59	NO	
Design	5	18DEC06:08:00:00	22DEC06:16:59:59	YES	R&D 5434
Develop	10	25DEC06:08:00:00	05JAN07:16:59:59	NO	R&D 5305
Document	6	08JAN07:08:00:00	15JAN07:16:59:59	YES	R&D 5313
Test	8	08JAN07:08:00:00	17JAN07:16:59:59	NO	R&D 5444
Ship	0	17JAN07:16:59:59	17JAN07:16:59:59	NO	R&D 5440

Note that a custom field is extracted and saved in the data set `Task_Attributes` only when the field has nondefault values for at least one task or when it has been renamed in Microsoft Project. If you are not sure whether or not `Flag1` is present in the data set `Task_attributes`, you can use the following SAS statements instead:


```
%macro merge;
/* Open the data set mspout.Task_attributes and
   return an identifier &dsid. */
%let dsid=%sysfunc(open(mspout.Task_attributes));
proc sql;
  create table merged as
  select a.ACTIVITY, a.DURATION,
    b.E_START, b.E_FINISH,
    %if %sysfunc(varnum(&dsid,Flag1)) %then %do;
      c.Flag1,
    %end;
    c.Text1
  from mspout.Activity a, mspout.Schedule b,
    mspout.Task_attributes c
  where a.ACTUID=b.ACTUID=c.ACTUID
    and a.ACTIVITY is not missing;
quit;
/* Close the data set opened with the identifier &dsid. */
%let rc = %sysfunc (close (&dsid));
%mend;

%merge;
```


### Example 6.3: Importing Multiple Projects

This example illustrates the ability of the %MSPTOSAS macro to convert multiple projects saved in one database file to a form readable by the PM procedure. Assume you have two projects, named “Software Project” and “Marketing Project,” in the Microsoft Access file mspsas3.mdb. The details of the projects are displayed in Output 6.3.1 and Output 6.3.2.

**Output 6.3.1** Marketing Project: Microsoft Project Window



**Output 6.3.2** Software Project: Microsoft Project Window




You can use the following call to the %MSPTOSAS macro to convert the projects and open them in the PM window:

```
%msptosas (mdbfile=C:\MSPROJ\mspsas3.mdb, version=2003)
```

The PM window containing the preceding projects is displayed in [Output 6.3.3](#).

**Output 6.3.3** PM Window

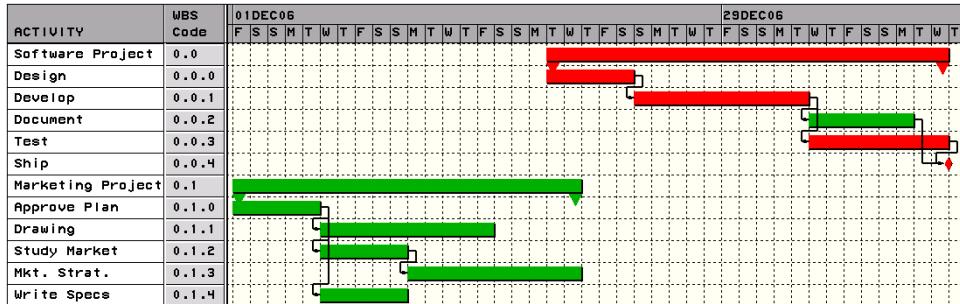

## Example 6.4: Importing XML Files


This example illustrates how to convert a Microsoft Project file that was saved in XML format to SAS data sets. Microsoft Project 2007 is initially used to save the project from [Example 6.2](#) in XML format.

You can use the following SAS macro call to convert this project:

```
%msptosas (xmlfile=C:\MSPROJ\mspsas2.xml, version=2007)
```

Since the MAPFILE= option is not specified, the map file *mspxml.map* is created and used. After the conversion, the PM window that shows the converted project is displayed, as shown in [Output 6.4.1](#). The display is the same as that shown in [Output 6.1.2](#). You can customize the display by following the same steps as in [Example 6.2](#). [Output 6.4.2](#) shows the merged data set.

**Output 6.4.1** PM Window

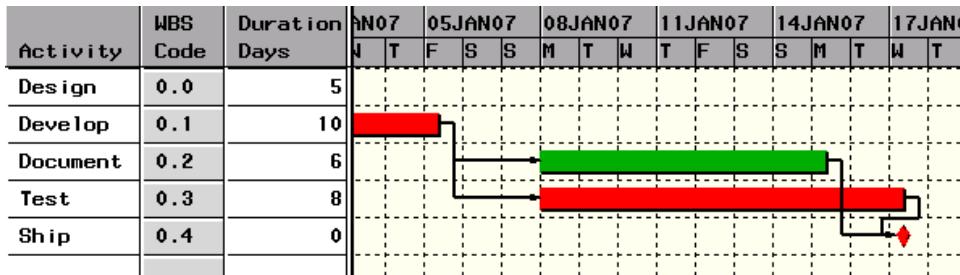

#### Output 6.4.2 Merged Data Set

ACTIVITY	DURATION	Early Start	Early Finish	Flag1	Department Num.
mspsas2	.	18DEC06:08:00:00	17JAN07:16:59:59	NO	
Design	5	18DEC06:08:00:00	22DEC06:16:59:59	YES	R&D 5434
Develop	10	25DEC06:08:00:00	05JAN07:16:59:59	NO	R&D 5305
Document	6	08JAN07:08:00:00	15JAN07:16:59:59	YES	R&D 5313
Test	8	08JAN07:08:00:00	17JAN07:16:59:59	NO	R&D 5444
Ship	0	17JAN07:16:59:59	17JAN07:16:59:59	NO	R&D 5440

#### Example 6.5: Simple %SASTOMSP Conversion

This example demonstrates how to convert a simple project from SAS to Microsoft Project. The data set Activity is created using the following SAS DATA step:


```
data activity;
  format activity succ1 $8.;
  input activity dur succ1;
  datalines;
Design      5 Develop
Develop    10 Document
Develop    10 Test
Document   6 Ship
Test        8 Ship
Ship        0 .
;
```

You can display this project in the PM procedure with the following SAS statements:

```
proc pm data=activity;
  act activity;
  succ succ1;
  duration dur;
run;
```

The resulting PM window is shown in Output 6.5.1. Note that the project starts at time 0, and there are no time units.

#### Output 6.5.1 PM Window




To convert the project specified by a SAS data set to an MDB file that is readable by Microsoft Project, you use the %SASTOMSP macro. You need to use the **MDBFILE=** parameter to specify the location and name of the MDB file to be created. For example, the following statement converts the project specified by the SAS data set Activity to the MDB file ‘C:\MSPROJ\sasmfsp1a.mdb’:

```
filename mspref "C:\MSPROJ\sasmsp1a.mdb";
%$astomsp(mdbfile=mspref);
```

Note that several parameters are omitted since the variable names in the data set **Activity** are identical to the corresponding default parameters of the conversion macro (see the section “[Default Values](#)” on page 364). **Output 6.5.2** shows the resulting project schedule as viewed in Microsoft Project.

## **Output 6.5.2** Microsoft Project Window



The schedule seen in [Output 6.5.1](#) (the PM window) is represented in terms of the time interval (days) while that in [Output 6.5.2](#) (the MS Project window) has dates. The PM procedure does not use dates if none are specified, so the project is scheduled to begin at time 0 and end at time 23. However, Microsoft Project schedules projects by using dates. Since no start date is specified, the conversion macro uses the current day as the default starting date.

To create a project schedule that is consistent across both the PM procedure and Microsoft Project, you need to add an additional option in both the PM invocation and the %SASTOMSP macro statement. In the PM invocation, you need to add the DATE= option to start the project on a given date. In the following example, the project is started on December 15, 2006:


```
proc pm data=activity date='15Dec06'd;
  act activity;
  succ succl;
  duration dur;
run;
```

For the call to %SASTOMSP, you specify this same starting date by using the DATE= parameter:


```
filename mspref "C:\MSPROJ\sasmfsp1b.mdb";
%astomsp(mdbfile=mspref, date='15Dec06'd);
```

The resulting windows are shown in [Output 6.5.3](#) and [Output 6.5.4](#).

### Output 6.5.3 PM Window



#### Output 6.5.4 Microsoft Project Window



#### Example 6.6: Exporting Data Set and Variable Names

In this example, the same project from [Example 6.5](#) is used. However, in this case, the data set names and variable names do not have the default variables, so they must be explicitly specified in the %SASTOMSP macro.


For example, suppose the data set containing the activity information is created as follows:

```
data software;
  format task $1. $8.;
  input task duration $1. $8.;
  datalines;
Design      5   Develop     .
Develop    10   Document   Test
Document    6   Ship       .
Test        8   Ship       .
Ship        0   .
;
```

This data set is identical to the data set Activity in [Example 6.5](#), except for a slightly different format. The following PM invocation results in the PM window shown in [Output 6.6.1](#):

```
proc pm data=software date='15Dec06'd;
  act task;
  succ s1 s2;
  duration duration;
run;
```

#### Output 6.6.1 PM Window



To convert the data to an MDB file, you need to specify several additional parameters in the %SASTOMSP macro call. First, you need to specify the name of the data set (Software in this case) using the ACTDS= parameter. In [Example 6.1](#), this parameter was not needed, because the default data set name Activity was used.

Similarly, you must specify the names of the activity, duration, and successor variables using the \_ACTIVITY=, \_DUR=, and \_SUCCESSOR= parameters, respectively.

The following call to the %SASTOMSP macro results in the Microsoft Project window as shown in Output 6.5.4:

```
filename mspref "C:\MSPROJ\sasmmp2.mdb";
%sastomsp (mdbfile=mspref,
            actds=software,
            _activity=task,
            _dur=duration,
            _successor=s1 s2,
            _date='15Dec06'd);
```

## Example 6.7: Exporting Calendars and Holidays

This example demonstrates the capability of the %SASTOMSP macro to handle multiple calendars within a project. Each activity is associated with one of four available calendars. Each calendar is customized to incorporate various workday shift patterns. In addition, there is a holiday data set that is also appropriately associated with a calendar. The four different calendars are defined as follows:

- The DEFAULT calendar has five eight-hour days (Monday through Friday) and holidays on Saturday and Sunday.
- The calendar OVT\_CAL specifies an overtime calendar that has 10-hour workdays on Monday through Friday, a half-day on Saturday, and a holiday on Sunday.
- The calendar PROD\_CAL follows a more complicated work pattern: Sunday is a holiday; on Monday work is done from 8 a.m. through midnight with a two hour break from 6 p.m. to 8 p.m.; on Tuesday through Friday work is done round the clock with two 2-hour breaks, one from 6 a.m. to 8 a.m. and the other from 6 p.m. to 8 p.m.; on Saturday the work shifts are from midnight to 6 a.m. and again from 8 a.m. to 6 p.m.
- The calendar ENG\_CAL is specified similar to the default calendar, but with an extra vacation period of 7 days beginning on December 8.

The following data set contains the activity information:

```
data actdat;
  format activities $12. s1-s3 $12. cal $8.;
  input activities & days s1 & s2 & s3 & cal &;
  datalines;
Approve Plan      5   Drawings        Study Market    Write Specs    DEFAULT
Drawings          10  Prototype       .              .              .
Study Market     5   Mkt. Strat.    .              .              .
Write Specs       5   Prototype       .              .              .
Prototype         15  Materials       Facility        .              .
Mkt. Strat.      10  Test Market    Marketing      .              .
Materials         10  Init. Prod.    .              .              .
Facility          10  Init. Prod.    .              .              .
Init. Prod.       10  Test Market    Marketing      Evaluate     .
Evaluate          10  Changes         .              .              .
Test Market       15  Changes         .              .              .
```

```

Changes      5  Production   .   .
Production    0  .   .   .
Marketing     0  .   .   .
;

```

The next three data sets specify the work shift patterns, calendars, and holidays, respectively:

```

data wrkdat;
  input fullday time8. halfday time8. ovtday time8.
    d1 time8. d2 time8. d3 time8.;
  format fullday halfday ovtday d1 d2 d3 time6.;
  datalines;
08:00 08:00 08:00 . 08:00 .
16:00 12:00 18:00 06:00 18:00 06:00
. . . 08:00 20:00 08:00
. . . 18:00 . 18:00
. . . 20:00 .
. . .
;

data caldat;
  input cal $ _sun_ $ _mon_ $ _tue_ $ _wed_ $ _thu_ $ _fri_ $ _sat_ $;
  datalines;
DEFAULT holiday fullday fullday fullday fullday fullday holiday
OVT_CAL holiday ovtday ovtday ovtday ovtday ovtday halfday
PROD_CAL holiday d2 d1 d1 d1 d1 d3
ENG_CAL .
;

data holdat;
  format holiday holifin date7.;
  input holiday & date7. holifin & date7. holidur cal $;
  datalines;
08Dec06 . 7 ENG_CAL
24Dec06 26Dec06 . .
01Jan07 01Jan07 . .
;
```


You can view the resulting project schedule in the PM window with the following call:

```

proc pm date='01Dec06'd data=actdat
  calendar=caldat holidata=holdat
  workday=wrkdat
  daylength='08:00't;
  activity activities;
  duration days;
  successor s1 s2 s3;
  calid cal;
  holiday holiday / holifin = holifin holidur=holidur;
run;
```

The resulting PM window is shown in [Output 6.7.1](#).

### Output 6.7.1 PM Window

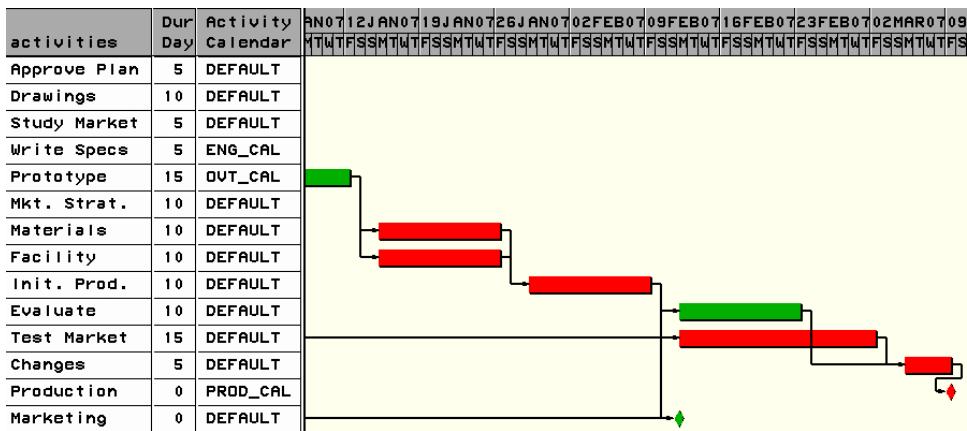


To convert the preceding data to an MDB file that includes the calendar and holiday information, you can use the following call to %SASTOMSP:

```
%sastomsp (mdbfile=mspref,
            actds=actdat, calds=caldat,
            holds=holdat, workds=wrkdat,
            _date='1Dec06'd,
            _daylength='08:00't,
            _activity=activities,
            _dur=days,
            _successor=s1 s2 s3,
            _calid=cal,
            _holistart=holiday, _holiend=holifin, _holidur=holidur)
```

The resulting MS Project Window is shown in Output 6.7.2. The schedule is the same as the one produced by the PM procedure.

### Output 6.7.2 MS Project Window

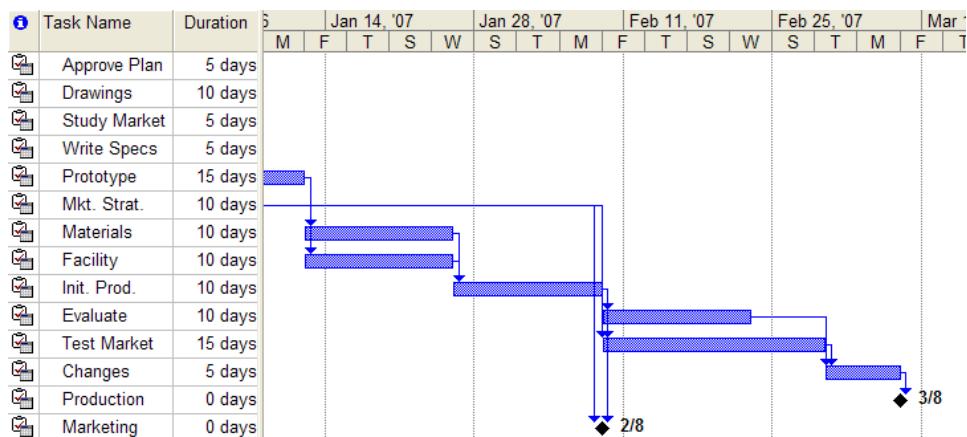

## Example 6.8: Exporting Resource-Constrained Schedules

In this example, a project is scheduled subject to resource constraints.

Before you continue, make sure that in your Microsoft Project software, “resource leveling” is properly set as follows so that the resource-constrained schedule is automatically displayed in the Gantt chart. From the Microsoft Project Tools menu, select **Level Resources** (**Resource Leveling** in Microsoft Project 2000). Then select **Automatic** for **Leveling calculations**. Clear **Level only within available slack** for **Resolving overallocations**. Then click on **OK**.

The following DATA steps specify the project in this example. Resource assignments are specified in the data set **Activity**, and the resource availabilities are defined in the data set **Resources**.

```
data activity;
  format task succ1 $8.;
  input task dur succ1 engineer writer tester;
  datalines;
Design 5 Develop 1 . 1
Develop 10 Document 1 . 1
Develop 10 Test 1 . 1
Document 6 Ship 1 1 .
Test 8 Ship 1 . 1
Ship 0 . . .
;


data resources;
  format obstype $8.;
  input obstype date: date7. engineer writer tester;
  datalines;
reslevel 15Dec06 . . 1
reslevel 18Dec06 1 . .
reslevel 30Dec06 . 1 .
;
```

The PM invocation is given in the following statements. The resource data set is specified with `resin=resources`; and the RESOURCE statement is also added to identify the applicable resources.

```
proc pm data=activity
  date='15Dec06'd
  resin=resources;
  act task;
  succ succ1;
  duration dur;
  resource engineer writer tester / period=date;
run;
```

The resulting PM window is shown in [Output 6.8.1](#). Notice that both the early schedule and the resource-constrained schedule are displayed in the Gantt chart.

### Output 6.8.1 PM Window

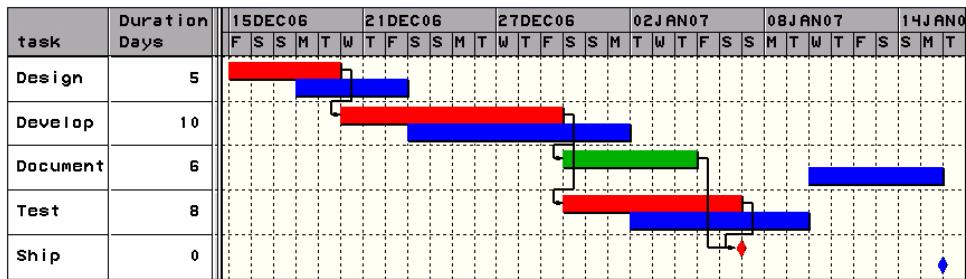


To convert the data to an MDB file that includes resource requirements, you use the following call to %SASTOMSP:

```
%sastomsp (mdbfile=mspref,
            resds=resources,
            _activity=task,
            _date='15Dec06'd,
            _resobstype=obstype,
            _resource=engineer writer tester,
            _resperiod=date);
```

The resulting MS Project window is shown in Output 6.8.2.

### Output 6.8.2 MS Project Window



In Output 6.8.2, Microsoft Project displays only the resource-constrained schedule. To get a comparison view as in the PM procedure, you can save the output schedule of the PM procedure and specify the SCHEDULEDS= parameter in the call to %SASTOMSP, as follows:

```
proc pm data=activity
  date='15Dec06'd
  resin=resources out=schedule;
  act task;
  succ succ1;
  duration dur;
  resource engineer writer tester / period=date;
run;


filename mspref "C:\MSPROJ\sasmsp4b.mdb";
%sastomsp (mdbfile=mspref,
            resds=resources,
            scheduleds=schedule,
            _activity=task,
            _date='15Dec06'd,
            _resobstype=obstype,
```

```
_resource=engineer writer tester,
_resperiod=date);
```

The PROC PM window is identical to the one shown in [Output 6.8.1](#), and the resulting Microsoft Project window is identical to the one shown in [Output 6.8.2](#). However, the schedule information computed by SAS has been exported to the MDB file and is available for display in Microsoft Project.

You can manually set Microsoft Project to display the schedules in the Gantt Chart. In Microsoft Project, from the **Format** menu, select **Bar Styles**. Then change the **Task** number in the column **Row** from 1 to 2. Click on **Insert Row**. Type a name for the new row (e.g., SAS Early Schedule). Under **From**, select **Start1 (SAS\_E\_start)**. Under **To**, select **Finish1 (SAS\_E\_finish)**. Click **OK**. The resulting window is shown in [Output 6.8.3](#). Now both the resource-constrained schedule and the early schedule are displayed in the Gantt chart.

**Output 6.8.3** MS Project Window

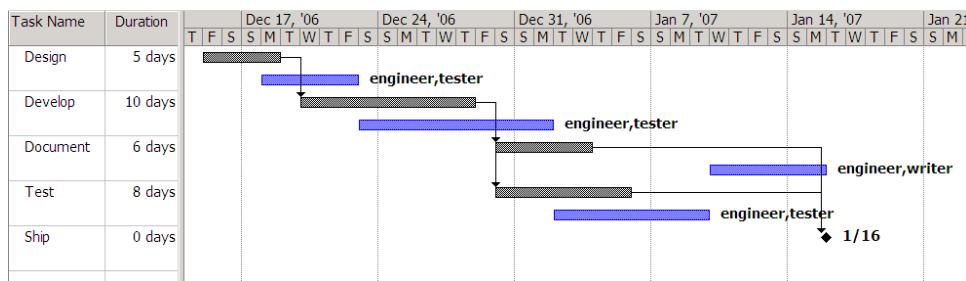


You can also display the SAS\_E\_start and the SAS\_E\_finish in columns by going to the **Insert** menu, selecting **Column**, and selecting the **Start1 (SAS\_E\_start)** and **Finish1 (SAS\_E\_finish)** fields.

## Example 6.9: Round Trip between a SAS Program and Microsoft Project

This example demonstrates how to convert a Microsoft Project (MSP) database file into SAS by using the %MSPTOSAS macro, and then to convert the file back to MSP by using the %SASTOMSP macro.

**Output 6.9.1** MS Project Window

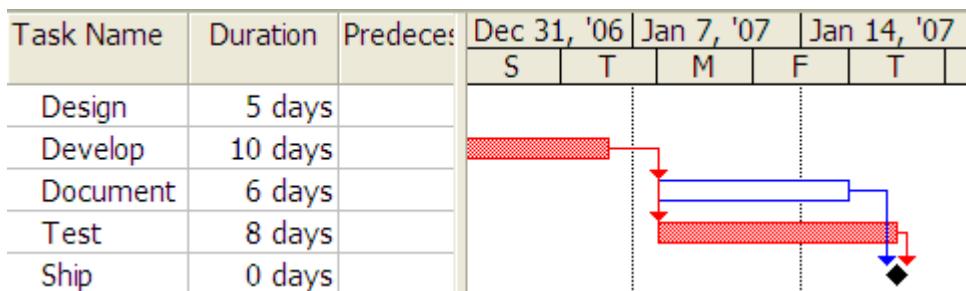

Suppose you want to convert the MSP project shown in [Output 6.9.1](#) into SAS software. You can convert the corresponding MDB file into a SAS data set by using the %MSPTOSAS macro, as follows:


```
%msptosas (mdbfile=C:\MSPROJ\mspsas4.mdb, library=C:\MSPROJ,
version=2003)
```

The %MSPTOSAS macro generates the data sets Activity, Calendar, Holiday, Workday, Resource, Schedule, Task\_Attributes, and Prefs, as well as the file callpm.sas. The following SAS statements can be found either in the callpm.sas file or in the SAS log:

```
libname mspout "C:\MSPROJ";
PROC PM data = mspout.activity project=mspout.prefs
  caledata = mspout.calendar
  workdata = mspout.workday
  out=mspout.schedule
  interval=dtday
  date="17DEC06:08:00:00"dt
  daylength=" 8:00"t
  suppressobswarn
  setfinishmilestone;
activity ACTID;
successor SUCCUID / LAG = LAG;
duration DURATION;
project PNTUID;
id ACTIVITY ACTUID;
RUN;
```

Output 6.9.2 shows the resulting PM window.

**Output 6.9.2** PM Window

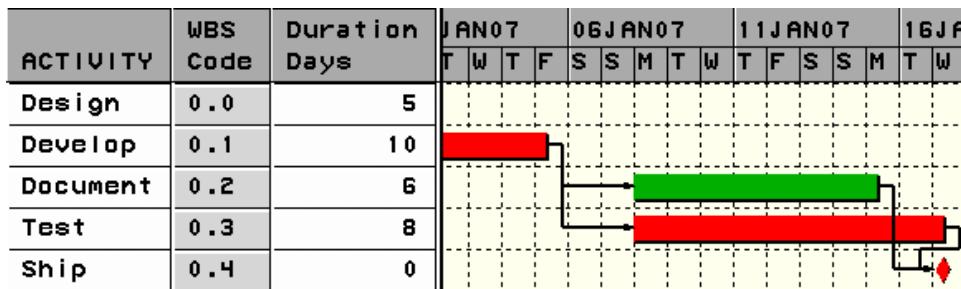

By taking the parameters from the preceding PM invocation, you can specify the values in the following %SASTOMSP call. The %SASTOMSP macro converts the project back into Microsoft Project format.

```
filename mspref "C:\MSPROJ\sasmmp5.mdb";
%sastomsp(library=C:\MSPROJ, mdbfile=mspref,
  actds=activity, calds=calendar, workds=workday,
  scheduleds=schedule, _interval=dtday,
  _date="17DEC06:08:00:00"dt, _daylength=" 8:00"t,
  _activity=ACTUID, _successor=SUCCUID,
  _lag=LAG, _dur=DURATION, _project=PNTUID,
  _id=ACTIVITY ACTUID)
```

In this example, after the project was converted to SAS code, the same project was converted back to Microsoft Project. The round trip between Microsoft Project and SAS software enables you to harness the power of SAS programming in scheduling, resource leveling, data processing, and more. Once your calculations are complete, you can return the results to Microsoft Project. Note that because SAS/OR Project Management and Microsoft Project use different strategies in calculating schedules, your project might show different start or finish times in SAS software and Microsoft Project. To compare the differences, you can display SAS schedules both in a table column view and in a Gantt chart, as described in Example 6.8.



# Chapter 7

## The DTREE Procedure

### Contents

---

Overview: DTREE Procedure . . . . .	382
Getting Started: DTREE Procedure . . . . .	383
Introductory Example . . . . .	383
Attitudes toward Risk . . . . .	388
Sensitivity Analysis and Value of Perfect Information . . . . .	389
Value of Perfect Control . . . . .	390
Oil Wildcatter's Problem with Sounding Test . . . . .	391
Syntax: DTREE Procedure . . . . .	395
Functional Summary . . . . .	396
PROC DTREE Statement . . . . .	399
EVALUATE Statement . . . . .	411
MODIFY Statement . . . . .	411
MOVE Statement . . . . .	412
QUIT Statement . . . . .	412
RECALL Statement . . . . .	412
RESET Statement . . . . .	412
SAVE Statement . . . . .	413
SUMMARY Statement . . . . .	413
TREEPLOT Statement . . . . .	413
VARIABLES Statement . . . . .	414
VPC Statement . . . . .	417
VPI Statement . . . . .	418
Details: DTREE Procedure . . . . .	418
Input Data Sets . . . . .	418
Missing Values . . . . .	421
Interactivity . . . . .	422
Options in Multiple Statements . . . . .	422
The Order of Stages . . . . .	422
Evaluation . . . . .	423
Displayed Output . . . . .	426
Displaying the Decision Tree . . . . .	427
Web-Enabled Decision Tree . . . . .	431
ODS Table Names . . . . .	432
ODS Style Templates . . . . .	432
Precision Errors . . . . .	434
Computer Resource Requirements . . . . .	435

Examples: DTREE Procedure . . . . .	435
Example 7.1: Oil Wildcatter's Problem with Insurance . . . . .	436
Example 7.2: Oil Wildcatter's Problem in Risk-Averse Setting . . . . .	441
Example 7.3: Contract Bidding Problem . . . . .	452
Example 7.4: Research and Development Decision Problem . . . . .	457
Example 7.5: Loan Grant Decision Problem . . . . .	461
Example 7.6: Petroleum Distributor's Decision Problem . . . . .	471
Statement and Option Cross-Reference Tables . . . . .	480
References . . . . .	482

---

## Overview: DTREE Procedure

The DTREE procedure in SAS/OR software is an interactive procedure for decision analysis. The procedure interprets a decision problem represented in SAS data sets, finds the optimal decisions, and plots on a line printer or a graphics device the decision tree showing the optimal decisions.

To use PROC DTREE you first construct a decision model to represent your problem. This model, called *a generic decision tree model*, is made up of *stages*.<sup>1</sup> Every stage has a *stage name*, which identifies the stage, as well as a *type*, which specifies the type of the stage. There are three types of stages: decision stages, chance stages, and end stages. In addition, every stage has possible *outcomes*.

A *decision stage* represents a particular decision you have to make. The outcomes of a decision stage are the possible *alternatives* (or *actions*) of the decision. A *chance stage* represents an *uncertain factor* in the decision problem (a statistician might call it a *random variable*; here it is called an *uncertainty*). The outcomes of a chance stage are *events*, one of which will occur according to a given probability distribution. An *end stage* terminates a particular *scenario* (a sequence of alternatives and events). It is not necessary to include an end stage in your model; the DTREE procedure adds an end stage to your model if one is needed.

Each outcome of a decision or chance stage also has several attributes, an *outcome name* to identify the outcome, a *reward* to give the instant reward of the outcome, and a *successor* to specify the name of the stage that comes next when this outcome is realized. For chance stages, a *probability* attribute is also needed. It gives the relative likelihood of this outcome. Every decision stage should have at least two alternatives, and every chance stage should have at least two events. Probabilities of events for a chance stage *must* sum to 1. End stages do not have any outcomes.

The structure of a decision model is given in the **STAGEIN=** data set. It contains the stage name, the type, and the attributes (except probability) of all outcomes for each stage in your model. You can specify each stage in one observation or across several observations. If a diagrammatic representation of a decision problem is all you want, you probably do not need any other data sets.

If you want to evaluate and analyze your decision problem, you need another SAS data set, called the **PROBIN=** data set. This data set describes the probabilities or conditional probabilities for every event in your model. Each observation in the data set contains a list of given conditions (list of outcomes), if there are any, and at least one combination of event and probability. Each event and probability combination identifies

---

<sup>1</sup>The stages are often referred to as *variables* in many decision analysis articles.

the probability that the event occurs given that all the outcomes specified in the list occur. If no conditions are given, then the probabilities are unconditional probabilities.

The third data set, called the **PAYOFFS=** data set, contains the value of each possible scenario. You can specify one or more scenarios and the associated values in one observation. If the **PAYOFFS=** data set is omitted, the DTREE procedure assumes that all values are zero and uses rewards for outcomes to evaluate the decision problem.

You can use PROC DTREE to display, evaluate, and analyze your decision problem. In the **PROC DTREE** statement, you specify input data sets and other options. A **VARIABLES** statement identifies the variables in the input data set that describe the model. This statement can be used only once and must appear immediately after the **PROC DTREE** statement. The **EVALUATE** statement evaluates the decision tree. You can display the optimal decisions by using the **SUMMARY** statement, or you can plot the complete tree with the **TREEPLOT** statement. Finally, you can also associate HTML pages with decision tree nodes and create Web-enabled decision tree diagrams.

It is also possible to interactively modify some attributes of your model with the **MODIFY** statement and to change the order of decisions by using the **MOVE** statement. Before making any changes to the model, you should save the current model with the **SAVE** statement so that you can call it back later by using the **RECALL** statement. Questions about the value of perfect information or the value of perfect control are answered using the **VPI** and **VPC** statements. Moreover, any options that can be specified in the **PROC DTREE** statement can be reset at any time with the **RESET** statement.

All statements can appear in any order and can be used as many times as desired with one exception. The **RECALL** statement must be preceded by at least one **SAVE** statement. In addition, only one model can be saved at any time; the **SAVE** statement overwrites the previously saved model. Finally, you can use the **QUIT** statement to stop processing and exit the procedure.

The DTREE procedure produces one output data set. The **IMAGEMAP=** data set contains the outline coordinates for the nodes in the decision tree that can be used to generate HTML MAP tags.

PROC DTREE uses the Output Delivery System (ODS), a SAS subsystem that provides capabilities for displaying and controlling the output from SAS procedures. ODS enables you to convert any of the output from PROC DTREE into a SAS data set. For further details, refer to the chapter on ODS in the *SAS/STAT User's Guide*.

## Getting Started: DTREE Procedure

### Introductory Example

A decision problem for an oil wildcatter illustrates the use of the DTREE procedure. The oil wildcatter must decide whether or not to drill at a given site before his option expires. He is uncertain about many things: the cost of drilling, the extent of the oil or gas deposits at the site, and so on. Based on the reports of his technical staff, the hole could be '**Dry**' with probability 0.5, '**Wet**' with probability 0.3, and '**Soaking**' with probability 0.2. His monetary payoffs are given in the following table.

**Table 7.1** Monetary Payoffs of Oil Wildcatter's Problem

	Drill	Not Drill
Dry	0	0
Wet	\$700,000	0
Soaking	\$1,200,000	0

The wildcatter also learned from the reports that the cost of drilling could be \$150,000 with probability 0.2, \$300,000 with probability 0.6, and \$500,000 with probability 0.2. He can gain further relevant information about the underlying geological structure of this site by conducting seismic soundings. A cost control procedure that can make the probabilities of the '**High**' cost outcomes smaller (and hence, the probabilities of the '**Low**' cost outcomes larger) is also available. However, such information and control are quite costly, about \$60,000 and \$120,000, respectively. The wildcatter must also decide whether or not to take the sounding test or the cost control program before he makes his final decision: to drill or not to drill.

The oil wildcatter feels that he should structure and analyze his basic problem first: whether or not to drill. He builds a model that contains one decision stage named '**Drill**' (with two outcomes, '**Drill**' and '**Not\_Drill**') and two chance stages named '**Cost**' and '**Oil\_Deposit**'. A representation of the model is saved in three SAS data sets. In particular, the **STAGEIN=** data set can be saved as follows:

```
/* -- create the STAGEIN= data set          -- */
data Dtoils1;
format _STNAME_ $12. _STTYPE_ $2. _OUTCOM_ $10.
      _SUCCES_ $12. ;
input _STNAME_ $ _STTYPE_ $ _OUTCOM_ $ _SUCCES_ $ ;
datalines;
Drill      D   Drill      Cost
.          .   Not_Drill  .
Cost       C   Low        Oil_Deposit
.          .   Fair        Oil_Deposit
.          .   High       Oil_Deposit
Oil_Deposit C   Dry        .
.          .   Wet        .
.          .   Soaking    .
;
```

The structure of the decision problem is given in the Dtoils1 data set. As you apply this data set, you should be aware of the following points:

- There is no reward variable in this data set; it is not necessary.
- The ordering of the chance stages '**Cost**' and '**Oil\_Deposit**' is arbitrary.
- Missing values for the **\_SUCCES\_** variable are treated as '**\_ENDST\_**' (the default name of the end stage) unless the associated outcome variable (**\_OUTCOM\_**) is also missing.

The following PROBIN= data set contains the probabilities of events:

```
/* -- create the PROBIN= data set          -- */
data Dtoilp1;
input _EVENT1 $ _PROB1
      _EVENT2 $ _PROB2
      _EVENT3 $ _PROB3 ;
datalines;
Low   0.2   Fair   0.6   High    0.2
Dry   0.5   Wet    0.3   Soaking 0.2
;
```

Notice that the sum of the probabilities of the events 'Low', 'Fair', and 'High' is 1.0. Similarly, the sum of the probabilities of the events 'Dry', 'Wet', and 'Soaking' is 1.0.

Finally, the following statements produce the PAYOFFS= data set that lists all possible scenarios and their associated payoffs.

```
/* -- create PAYOFFS= data set          -- */
data Dtoilul;
format _STATE1-_STATE3 $12. _VALUE_ dollar12.0;
input _STATE1 $ _STATE2 $ _STATE3 $ ;

/* determine the cost for this scenario */
if _STATE1='Low' then _COST_=150000;
else if _STATE1='Fair' then _COST_=300000;
else _COST_=500000;

/* determine the oil deposit and the          */
/* corresponding net payoff for this scenario */
if _STATE2='Dry' then _PAYOFF_=0;
else if _STATE2='Wet' then _PAYOFF_=700000;
else _PAYOFF_=1200000;

/* calculate the net return for this scenario */
if _STATE3='Not_Drill' then _VALUE_=0;
else _VALUE_= _PAYOFF_- _COST_;

/* drop unneeded variables */
drop _COST_ _PAYOFF_;

datalines;
Low      Dry      Not_Drill
Low      Dry      Drill
Low      Wet      Not_Drill
Low      Wet      Drill
Low      Soaking  Not_Drill
Low      Soaking  Drill
Fair     Dry      Not_Drill
Fair     Dry      Drill
Fair     Wet      Not_Drill
Fair     Wet      Drill
Fair     Soaking  Not_Drill
Fair     Soaking  Drill
```

```

High      Dry      Not_Drill
High      Dry      Drill
High      Wet      Not_Drill
High      Wet      Drill
High      Soaking  Not_Drill
High      Soaking  Drill
;

```

This data set can be displayed, as shown in Figure 7.1, with the following PROC PRINT statements:

```

/* -- print the payoff table          -- */
title "Oil Wildcatter's Problem";
title3 "The Payoffs";

proc print data=Dtoilul1;
run;

```

**Figure 7.1** Payoffs of the Oil Wildcatter's Problem

### Oil Wildcatter's Problem

#### The Payoffs

Obs	_STATE1	_STATE2	_STATE3	_VALUE_
1	Low	Dry	Not_Drill	\$0
2	Low	Dry	Drill	\$-150,000
3	Low	Wet	Not_Drill	\$0
4	Low	Wet	Drill	\$550,000
5	Low	Soaking	Not_Drill	\$0
6	Low	Soaking	Drill	\$1,050,000
7	Fair	Dry	Not_Drill	\$0
8	Fair	Dry	Drill	\$-300,000
9	Fair	Wet	Not_Drill	\$0
10	Fair	Wet	Drill	\$400,000
11	Fair	Soaking	Not_Drill	\$0
12	Fair	Soaking	Drill	\$900,000
13	High	Dry	Not_Drill	\$0
14	High	Dry	Drill	\$-500,000
15	High	Wet	Not_Drill	\$0
16	High	Wet	Drill	\$200,000
17	High	Soaking	Not_Drill	\$0
18	High	Soaking	Drill	\$700,000

The \$550,000 payoff associated with the scenario '**Low**', '**Wet**', and '**Drill**' is a net figure; it represents a return of \$700,000 for a wet hole less the \$150,000 cost for drilling. Similarly, the net return of the consequence associated with the scenario '**High**', '**Soaking**', and '**Drill**' is \$700,000, which is interpreted as a return of \$1,200,000 less the \$500,000 '**High**' cost.

Now the wildcatter can invoke PROC DTREE to evaluate his model and to find the optimal decision using the following statements:

```

/* -- PROC DTREE statements                                -- */
title "Oil Wildcatter's Problem";

proc dtree stagein=Dtoils1
  probin=Dtoilp1
  payoffs=Dtoilu1
  nowarning;

  evaluate / summary;

```

The following message, which notes the order of the stages, appears on the SAS log:

**NOTE: Present order of stages:**

**Drill (D), Cost (C), Oil\_Deposit (C), \_ENDST\_ (E) .**

**Figure 7.2** Optimal Decision Summary of the Oil Wildcatter's Problem

### Oil Wildcatter's Problem

#### The DTREE Procedure

#### Optimal Decision Summary

Order of Stages	
Stage	Type
Drill	Decision
Cost	Chance
Oil_Deposit	Chance
<u>_ENDST_</u>	End

#### Decision Parameters

**Decision Criterion:** Maximize Expected Value (MAXEV)

**Optimal Decision Yields:** \$140,000

#### Optimal Decision Policy

##### Up to Stage Drill

##### Alternatives


Outcomes	or	Cumulative Reward	Evaluating Value
Drill			\$140,000*
<u>Not_Drill</u>			\$0

The **SUMMARY** option in the **EVALUATE** statement produces the optimal decision summary shown in Figure 7.2.

The summary shows that the best action, in the sense of maximizing the expected payoff, is *to drill*. The expected payoff for this optimal decision is \$140,000, as shown on the summary.

Perhaps the best way to view the details of the results is to display the complete decision tree. The following statement draws the decision tree, as shown in Figure 7.3, in line-printer format:

```
/* plot decision tree diagram in line-printer mode */
OPTIONS LINESIZE=100;
treeplot/ lineprinter;
```

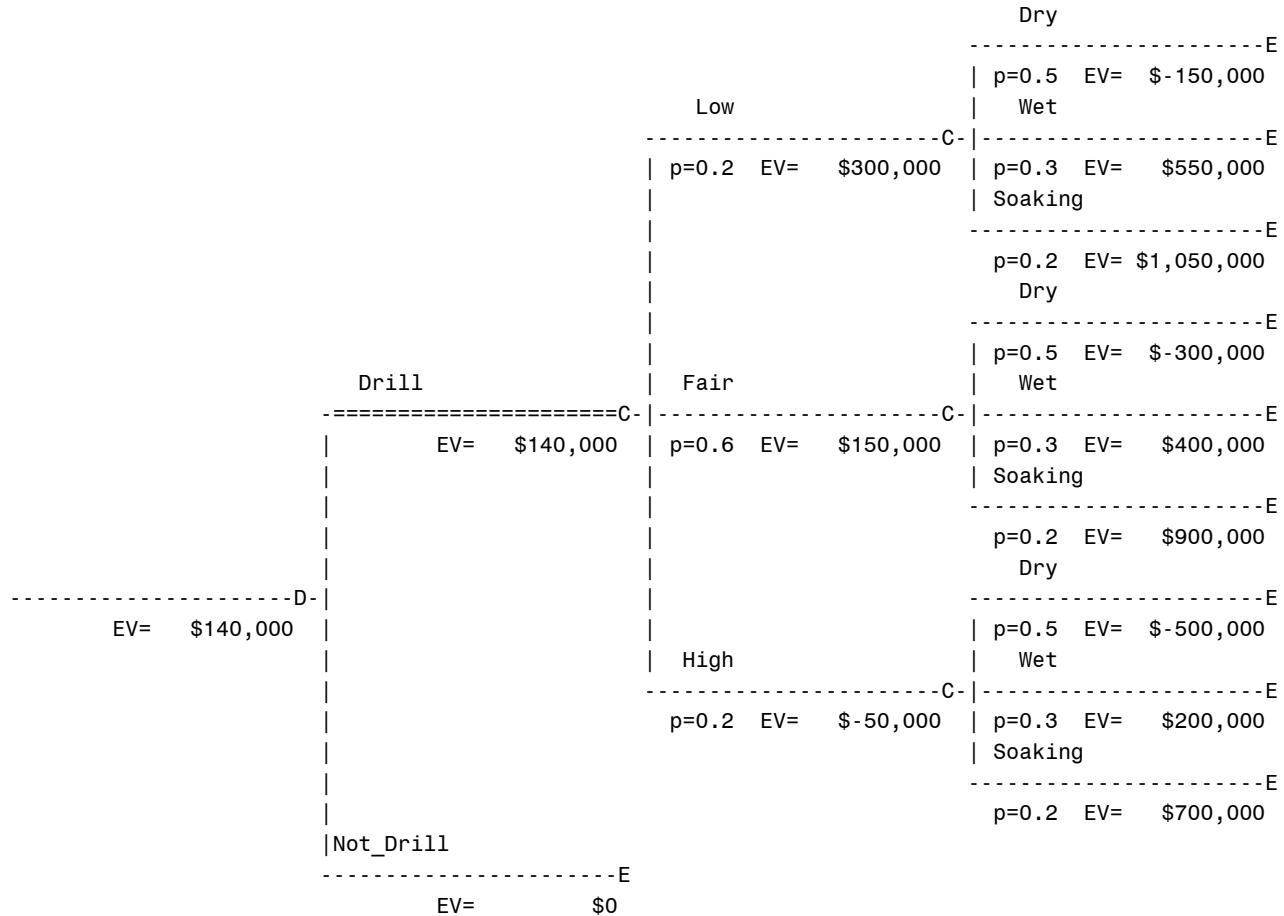**Figure 7.3** The Decision Tree**Oil Wildcatter's Problem****The DTREE Procedure****Line-printer Plot****Attitudes toward Risk**

Assume now that the oil wildcatter is constantly risk averse and has an exponential utility function with a *risk tolerance* (RT) of \$700,000. The risk tolerance is a measure of the decision maker's attitude to risk. See the section “Evaluation” on page 423 for descriptions of the utility function and risk tolerance.

The new optimal decision based on this utility function can be determined with the following statement:

```
evaluate / criterion=maxce rt=700000 summary;
```

The summary, shown in Figure 7.4, indicates that the venture of investing in the oil well is worth \$-13,580 to the wildcatter, and he should not drill the well.

**Figure 7.4** Summary of the Oil Wildcatter's Problem with RT = \$700,000

<b>Oil Wildcatter's Problem</b>	
<b>The DTREE Procedure</b>	
<b>Optimal Decision Summary</b>	
<b>Order of Stages</b>	
<b>Stage</b>	<b>Type</b>
Drill	Decision
Cost	Chance
Oil_Deposit	Chance
<u>_ENDST_</u>	End
<b>Decision Parameters</b>	
<b>Decision Criterion:</b> Maximize Certain Equivalent Value (MAXCE)	
<b>Risk Tolerance:</b> \$700,000	
<b>Optimal Decision Yields:</b> \$0	
<b>Optimal Decision Policy</b>	
<b>Up to Stage Drill</b>	
<b>Alternatives</b>	
or	
<b>Outcomes</b>	<b>Cumulative Reward</b>
	<b>Evaluating Value</b>
Drill	\$-13,580
Not_Drill	\$0*

## Sensitivity Analysis and Value of Perfect Information

The oil wildcatter learned that the optimal decision changed when his attitude toward risk changed. Since risk attitude is difficult to express quantitatively, the oil wildcatter wanted to learn more about the uncertainties in his problem. Before spending any money on information-gathering procedures, he would like to know the benefit of knowing, before the '**Drill**' or '**Not\_Drill**' decision, the amount of oil or the cost of drilling. The simplest approach is to calculate the value of perfect information for each uncertainty. This quantity gives an upper limit on the amount that could be spent profitably on information gathering. The expected value of information for the amount of oil is calculated by the following statement:

```
vpi Oil_Deposit;
```

The result of the previous statement is written to the SAS log as

```
NOTE: The currently optimal decision yields 140000.
```

```

NOTE: The new optimal decision yields 295000.
NOTE: The value of perfect information of stage Oil_Deposit
      yields 155000.

```

This means that the wildcatter could spend up to \$155,000 to determine the amount of oil in the deposit with certainty before losing money. There are several alternative ways to calculate the expected value of perfect information. For example, the following statement

```
vpi Cost;
```

is equivalent to

```

save;
move Cost before Drill;
evaluate;
recall;

```

The messages, which appear on the SAS log, show that if there is some way that the wildcatter knows what the cost to drill will be before his decision has to be made, it will yield an expected payoff of \$150,000. So, the expected value of perfect information about drilling cost is  $\$150,000 - \$140,000 = \$10,000$ .

```
NOTE: The current problem has been successfully saved.
```

```
NOTE: Present order of stages:
```

```
Cost(C), Drill(D), Oil_Deposit(C), _ENDST_(E).
```

```
NOTE: The currently optimal decision yields 150000.
```

```
NOTE: The original problem has been successfully recalled.
```

```
NOTE: Present order of stages:
```

```
Drill(D), Cost(C), Oil_Deposit(C), _ENDST_(E).
```

## Value of Perfect Control

The oil wildcatter may also want to know what the value of perfect control (VPC) is on the cost of drilling. That is, how much is he willing to pay for getting complete control on the drilling cost? This analysis can be performed with the following statement:

```
vpc Cost;
```

The result is written to the SAS log as

```

NOTE: The currently optimal decision yields 140000.
NOTE: The new optimal decision yields 300000.
NOTE: The value of perfect control of stage Cost
      yields 160000.

```

---

## Oil Wildcatter's Problem with Sounding Test

The wildcatter is impressed with the results of calculating the values of perfect information and perfect control. After comparing those values with the costs of the sounding test and the cost-controlling procedure, he prefers to spend \$60,000 on sounding test, which has a potential improvement of \$155,000. He is informed that the sounding will disclose whether the terrain below has no structure (which is bad), open structure (which is okay), or closed structure (which is really hopeful). The expert also provides him with the following table, which shows the conditional probabilities.

**Table 7.2** Conditional Probabilities of Oil Wildcatter's Problem

State	Seismic Outcomes		
	No Structure	Open Structure	Closed Structure
Dry	0.6	0.3	0.1
Wet	0.3	0.4	0.3
Soaking	0.1	0.4	0.5

To include this additional information into his basic problem, the wildcatter needs to add two stages to his model: a decision stage to represent the decision whether or not to take the sounding test, and one chance stage to represent the uncertain test result. The new STAGEIN= data set is

```
/* -- create the STAGEIN= data set                                -- */
data Dtools2;
format _STNAME_ $12. _STTYPE_ $2. _OUTCOM_ $14.
      _SUCCES_ $12. _REWARD_ dollar12.0;
input _STNAME_ & _STTYPE_ & _OUTCOM_ &
      _SUCCES_ & _REWARD_ dollar12.0;
datalines;
Drill      D   Drill           Cost
          .   Not_Drill        .
Cost       C   Low            Oil_Deposit
          .   Fair            Oil_Deposit
          .   High            Oil_Deposit
Oil_Deposit C   Dry            .
          .   Wet             .
          .   Soaking          .
Sounding    D   Noseismic      Drill
          .   Seismic          Structure   -$60,000
Structure   C   No_Struct     Drill
          .   Open_Struct     Drill
          .   Closed_Struct   Drill
;
```

Note that the cost for the seismic soundings is represented as negative reward (of the outcome Seismic) in this data set. The conditional probabilities for stage Structure are added to the PROBIN= data set as follows:

```

/* -- create PROBIN= data set                                -- */
data Dtoilp2;
  format _EVENT1 $10. _EVENT2 $12. _EVENT3 $14. ;
  input _GIVEN_ $ _EVENT1 $ _PROB1
        _EVENT2 $ _PROB2 _EVENT3 $ _PROB3;
  datalines;
.    Low      0.2 Fair      0.6 High      0.2
.    Dry      0.5 Wet       0.3 Soaking    0.2
Dry   No_Struct 0.6 Open_Struct 0.3 Closed_Struct 0.1
Wet   No_Struct 0.3 Open_Struct 0.4 Closed_Struct 0.3
Soaking No_Struct 0.1 Open_Struct 0.4 Closed_Struct 0.5
;

```

It is not necessary to make any change to the PAYOFFS= data set. To evaluate his new model, the wildcatter invokes PROC DTREE as follows:

```

/* -- PROC DTREE statements                                -- */
title "Oil Wildcatter's Problem";

proc dtree stagein=Dtoils2
  probin=Dtoilp2
  payoffs=Dtoilu1
  nowarning;

evaluate;

```

As before, the following messages are written to the SAS log:

```

NOTE: Present order of stages:
      Sounding(D), Structure(C), Drill(D), Cost(C),
      Oil_Deposit(C), _ENDST_(E).

NOTE: The currently optimal decision yields 140000.

```

The following **SUMMARY** statements produce the optimal decision summary as shown in Figure 7.5 and Figure 7.6:

```
summary / target=Sounding;
summary / target=Drill;
```

The optimal strategy for the oil-drilling problem is found to be the following:

- No soundings test should be taken, and always drill. This alternative has an expected payoff of \$140,000.
- If the soundings test is conducted, then drill unless the test shows the terrain below has no structure.
- The soundings test is worth  $\$180,100 - \$140,000 = \$40,100$  (this quantity is also called the *value of imperfect information* or the *value of sample information*), but it costs \$60,000; therefore, it should not be taken.

**Figure 7.5** Summary of the Oil Wildcatter's Problem for SOUNDING

### Oil Wildcatter's Problem

#### The DTREE Procedure

#### Optimal Decision Summary

Order of Stages	
Stage	Type
<b>Sounding</b>	Decision
<b>Structure</b>	Chance
<b>Drill</b>	Decision
<b>Cost</b>	Chance
<b>Oil_Deposit</b>	Chance
<b>_ENDST_</b>	End

#### Decision Parameters

**Decision Criterion:** Maximize Expected Value (MAXEV)

**Optimal Decision Yields:** \$140,000

#### Optimal Decision Policy

##### Up to Stage Sounding

Alternatives or Outcomes	Cumulative Reward	Evaluating Value
<b>NoSeismic</b>	\$0	\$140,000*
<b>Seismic</b>	\$-60,000	\$180,100

**Figure 7.6** Summary of the Oil Wildcatter's Problem for DRILL**Oil Wildcatter's Problem****The DTREE Procedure****Optimal Decision Summary**

Order of Stages	
Stage	Type
Sounding	Decision
Structure	Chance
Drill	Decision
Cost	Chance
Oil_Deposit	Chance
<u>ENDST_</u>	End

**Decision Parameters**

Decision Criterion: Maximize Expected Value (MAXEV)  
Optimal Decision Yields: \$140,000

**Optimal Decision Policy****Up to Stage Drill**

Alternatives or Outcomes		Cumulative Reward	Evaluating Value
Noseismic	Drill	\$0	\$140,000*
Noseismic	Not_Drill	\$0	\$0
Seismic	No_Struct	Drill	\$-60,000
Seismic	No_Struct	Not_Drill	\$-60,000
Seismic	Open_Struct	Drill	\$-60,000
Seismic	Open_Struct	Not_Drill	\$204,286*
Seismic	Closed_Struct	Drill	\$-60,000
Seismic	Closed_Struct	Not_Drill	\$452,500*
			\$0

Note that the value of sample information also can be obtained by using the following statements:

```
modify Seismic reward 0;
evaluate;
```

The following messages, which appear in the SAS log, show the expected payoff with soundings test is \$180,100. Recall that the expected value without test information is \$140,000. Again, following the previous calculation, the value of test information is \$180,100 - \$140,000 = \$40,100.

**NOTE: The reward of outcome Seismic has been changed to 0.**

**NOTE: The currently optimal decision yields 180100.**

Now, the wildcatter has the information to make his best decision.

---

## Syntax: DTREE Procedure

The following statements are available in PROC DTREE:

```
PROC DTREE options ;
  EVALUATE /options ;
  MODIFY specifications ;
  MOVE specifications ;
  QUIT ;
  RECALL ;
  RESET options ;
  SAVE ;
  SUMMARY /options ;
  TREEPLOT /options ;
  VARIABLES /options ;
  VPC specifications ;
  VPI specifications ;
```

The DTREE procedure begins with the **PROC DTREE** statement and terminates with the **QUIT** statement. The **VARIABLES** statement can be used only once, and if it is used, it must appear before any other statements. The **EVALUATE**, **MODIFY**, **MOVE**, **RECALL**, **RESET**, **SAVE**, **SUMMARY**, **TREEPLOT**, **VPC**, and **VPI** statements can be listed in any order and can be used as many times as desired with one exception: the **RECALL** statement must be preceded by at least one **SAVE** statement.

You can also submit any other valid SAS statements, for example, **OPTIONS**, **TITLE**, and **SAS/GPGRAPH** global statements. In particular, the **SAS/GPGRAPH** statements that can be used to enhance the DTREE procedure's output on graphics devices are listed in [Table 7.3](#). Note that the DTREE procedure is not supported with the ActiveX or Java series of devices on the **GOPTIONS** statement. Refer to *SAS/GPGRAPH Software: Reference* for more explanation of these statements.

**Table 7.3** Statements to Enhance Graphics Output

Statement	Function
FOOTNOTE	Produce footnotes that are displayed on the graphics output
GOPTIONS	Define default values for graphics options
NOTE	Produce text that is displayed on the graphics output
SYMBOL	Create symbol definitions
TITLE	Produce titles that are displayed on the graphics output

## Functional Summary

Table 7.4 outlines the options available for the DTREE procedure, classified by function.

**Table 7.4** Functional Summary

Description	Statement	Option
<b>Accuracy Control Options</b> Specifies the accuracy of numerical computation	DTREE, RESET	TOLERANCE=
<b>Data Set Specifications</b> Specifies the Annotate data set Specifies the Image map output data set Specifies the Payoffs data set Specifies the Probability data set Specifies the Stage data set	DTREE, RESET, TREEPLOT DTREE, RESET, TREEPLOT DTREE DTREE DTREE	ANNOTATE= IMAGEMAP= PAYOFFS= PROBIN= STAGEIN=
<b>Error Handling Options</b> Automatically rescales the probabilities of an uncertainty if they do not sum to 1 Specifies the error handling behavior Disables automatic rescaling of probabilities Disables warning messages Enables warning messages	DTREE, RESET DTREE, RESET DTREE, RESET DTREE, RESET DTREE, RESET	AUTOSCALE ERRHANDLE= NOSCALE NOWARNING WARNING
<b>Evaluation Control Options</b> Specifies the criterion used to determine the optimal decision Specifies the risk tolerance	DTREE, EVALUATE, RESET DTREE, EVALUATE, RESET	CRITERION= RT=
<b>Format Control Options</b> Specifies the maximum decimal width to format numerical values Specifies the maximum field width to format numerical values Specifies the maximum field width to format names	DTREE, EVALUATE, RESET, SUMMARY, TREEPLOT DTREE, EVALUATE, RESET, SUMMARY, TREEPLOT DTREE, EVALUATE, RESET, NWIDTH= SUMMARY, TREEPLOT	MAXPREC= MAXWIDTH= NWIDTH=
<b>Graphics Catalog Options</b> Specifies the description field for the catalog entry Specifies the name of the graphics catalog Specifies the name field for the catalog entry	DTREE, RESET, TREEPLOT DTREE, RESET, TREEPLOT DTREE, RESET, TREEPLOT	DESCRIPTION= GOUT= NAME=

**Table 7.4** *continued*

Description	Statement	Option
<b>Line-Printer Options</b> Specifies the characters for line-printer plot	DTREE, RESET, TREEPLOT	FORMCHAR=
<b>Link Appearance Options</b> Specifies the color of LOD <sup>1</sup> Specifies the color of all links except LOD <sup>1</sup> Defines the symbol for all links except LOD <sup>1</sup> and LCP <sup>2</sup> Defines the symbol for LOD <sup>1</sup> Defines the symbol for LCP <sup>2</sup> Specifies the line type of all links except LOD <sup>1</sup> and LCP <sup>2</sup> Specifies the line type of LOD <sup>1</sup> Specifies the line type of LCP <sup>2</sup> Specifies the line thickness of all links except LOD <sup>1</sup> Specifies the line thickness of LOD <sup>1</sup>	DTREE, RESET, TREEPLOT DTREE, RESET, TREEPLOT	CBEST= CLINK= LINKA= LINKB= LINKC= LSTYLE= LSTYLEB= LSTYLEC= LWIDTH= LWIDTHB=
<b>Node Appearance Options</b> Specifies the color of chance nodes Specifies the color of decision nodes Specifies the color of end nodes Specifies the height of symbols for all nodes Specifies the symbol definition for chance nodes Specifies the symbol definition for decision nodes Specifies the symbol definition for end nodes Specifies the symbol used for chance nodes Specifies the symbol used for decision nodes Specifies the symbol used for end nodes	DTREE, RESET, TREEPLOT DTREE, RESET, TREEPLOT	CSYMBOLC= CSYMBOLD= CSYMBOLE= HSYMBOL= SYMBOLC= SYMBOLD= SYMBOLE= VSYMBOLC= VSYMBOLD= VSYMBOLE=
<b>Output Control Options</b> Suppresses display of the optimal decision summary Displays the optimal decision summary	DTREE, EVALUATE, RESET DTREE, EVALUATE, RESET	NOSUMMARY SUMMARY

**Table 7.4** *continued*

Description	Statement	Option
Specifies the decision stage up to which the optimal decision summary is displayed	DTREE, EVALUATE, RESET, SUMMARY	TARGET=
<b>Plot Control Options</b>		
Draws diagram on one page in graphics mode	DTREE, RESET, TREEPLOT	COMPRESS
Displays information on the decision tree diagram	DTREE, RESET, TREEPLOT	DISPLAY=
Processes the Annotate data set	DTREE, RESET, TREEPLOT	DOANNOTATE
Invokes graphics version	DTREE, RESET, TREEPLOT	GRAPHICS
Displays labels	DTREE, RESET, TREEPLOT	LABEL
Displays legend	DTREE, RESET, TREEPLOT	LEGEND
Invokes line-printer version	DTREE, RESET, TREEPLOT	LINEPRINTER
Suppresses processing of the Annotate data set	DTREE, RESET, TREEPLOT	NOANNOTATE
Draws diagram across multiple pages	DTREE, RESET, TREEPLOT	NOCOMPRESS
Suppresses displaying label	DTREE, RESET, TREEPLOT	NOLABEL
Suppresses displaying legend	DTREE, RESET, TREEPLOT	NOLEGEND
Suppresses displaying page number	DTREE, RESET, TREEPLOT	NOPAGENUM
Uses rectangular corners for turns in the links	DTREE, RESET, TREEPLOT	NORC
Displays page number at upper right corner	DTREE, RESET, TREEPLOT	PAGENUM
Uses rounded corners for turns in the links	DTREE, RESET, TREEPLOT	RC
Specifies the vertical space between two end nodes	DTREE, RESET, TREEPLOT	YBETWEEN=
<b>Text Appearance Options</b>		
Specifies the text color	DTREE, RESET, TREEPLOT	CTEXT=
Specifies the text font	DTREE, RESET, TREEPLOT	FTEXT=
Specifies the text height	DTREE, RESET, TREEPLOT	HTEXT=
<b>Variables in PAYOFFS= Data Set</b>		
Specifies the action outcome names	VARIABLES	ACTION=
Specifies the state outcome names	VARIABLES	STATE=
Specifies the payoffs	VARIABLES	VALUE=
<b>Variables in PROBIN= Data Set</b>		
Specifies the event outcome names	VARIABLES	EVENT=
Specifies the given outcome names	VARIABLES	GIVEN=
Specifies the (conditional) probabilities	VARIABLES	PROB=

**Table 7.4** *continued*

Description	Statement	Option
<b>Variables in STAGEIN= Data Set</b>		
Specifies the outcome names	VARIABLES	OUTCOME=
Specifies the rewards	VARIABLES	REWARD=
Specifies the stage name	VARIABLES	STAGE=
Specifies the successor names	VARIABLES	SUCCESSOR=
Specifies the type of stage	VARIABLES	TYPE=
Specifies the web reference variable	VARIABLES	WEB=

<sup>1</sup>LOD denotes links that indicate optimal decisions.

<sup>2</sup>LCP denotes links that continue on subsequent pages.

## PROC DTREE Statement

**PROC DTREE** *options* ;

The options that can appear in the PROC DTREE statement are listed in the following section. The options specified in the PROC DTREE statement remain in effect for all statements until the end of processing or until they are changed by a **RESET** statement. These options are classified under appropriate headings: first, all options that are valid for all modes of the procedure are listed followed by the options classified according to the mode (line-printer or graphics) of invocation of the procedure.

### General Options

#### **AUTOSCALE | NOSCALE**

specifies whether the procedure should rescale the probabilities of events for a given chance stage if the total probability of this stage is not equal to 1. The default is NOSCALE.

#### **CRITERION=***i*

indicates the decision criterion to be used for determining the optimal decision and the certain equivalent for replacing uncertainties. The following table shows all valid values of *i* and their corresponding decision criteria and certain equivalents.

**Table 7.5** Values for the CRITERION= Option

<i>i</i>	Criterion	Certain Equivalent
MAXEV	Maximize	Expected value
MINEV	Minimize	Expected value
MAXMLV	Maximize	Value with largest probability
MINMLV	Minimize	Value with largest probability
MAXCE	Maximize	Certain equivalent value of expected utility
MINCE	Minimize	Certain equivalent value of expected utility

The default value is MAXEV. The last two criteria are used when your utility curve can be fit by an exponential function. See the section “Evaluation” on page 423 for more information on the exponential utility function.

#### **DISPLAY=(*information-list*)**

specifies information that should be displayed on each link of the decision tree diagram. **Table 7.6** lists the valid keywords and corresponding information.

**Table 7.6** Information on Decision Tree and Keywords

<b>Keyword</b>	<b>Information</b>
ALL	All information listed in this table
CR	Cumulative rewards of outcomes on the path that leads to the successor of the link
EV	Evaluating value that can be expected from the successor of the link
LINK	Outcome name represented by the link
P	Probability of the outcome represented by the link
R	Instant reward of the outcome represented by the link
STAGE	Stage name of the successor of the link

The default value is (LINK P EV R CR).

Note that the probability information displays on links that represent chance outcomes only. In addition, the **PROBIN=** option must be specified. The expected values display only if the decision tree has been evaluated. The reward information displays on a link only if the instant reward of the outcome represented by the link is nonzero. The cumulative rewards do not display if the cumulative rewards of links are all zero.

#### **ERRHANDLE=DRAIN | QUIT**

specifies whether the procedure should stop processing the current statement and wait for next statement or quit PROC DTREE when an error has been detected by the procedure. The default value is DRAIN.

#### **GRAPHICS**

creates plots for a graphics device. To specify this option, you need to have SAS/GRAF software licensed at your site. This is the default.

#### **LABEL | NOLABEL**

specifies whether the labels for information displayed on the decision tree diagram should be displayed. If the NOLABEL option is not specified, the procedure uses the following symbols to label all the information that is displayed on each link.

**Table 7.7** Labels and Their Corresponding Information

<b>Label</b>	<b>Information</b>
cr=	The cumulative rewards of outcomes on the path that lead to the successor of the link
EV=	The value that can be expected from the successor of the link
p=	The probability of the outcome represented by the link
r=	The instant reward of the outcome

The default is LABEL.

#### **LINEPRINTER**

##### **LP**

creates plots of line-printer quality. If you do not specify this option, graphics plots are produced.

#### **MAXPREC=d**

specifies the maximum decimal width (the precision) in which to format numerical values using *w.d* format. This option is used in displaying the decision tree diagrams and the summaries. The value for this option must be no greater than 9; the default value is 3.

#### **MAXWIDTH=mw**

specifies the maximum field width in which to format numerical values (probabilities, rewards, cumulative rewards and evaluating values) using *w.d* format. This option is used in displaying the decision tree diagrams and the summaries. The value for this option must be no greater than 16 and must be at least 5 plus the value of the **MAXPREC=** option. The default value is 10.

#### **NWIDTH=nw**

specifies the maximum field width in which to format outcome names when displaying the decision tree diagrams. The value for this option must be no greater than 40; the default value is 32.

#### **PAYOUTS=SAS-data-set**

names the SAS data set that contains the evaluating values (payoffs, losses, utilities, and so on) for each state and action combination. The use of **PAYOUTS=** is optional in the PROC DTREE statement. If the **PAYOUTS=** option is not used, PROC DTREE assumes that all evaluating values at the end nodes of the decision tree are 0.

#### **PROBIN=SAS-data-set**

names the SAS data set that contains the (conditional) probability specifications of outcomes. The **PROBIN=** SAS data set is required if the evaluation of the decision tree is desired.

#### **RT=r**

specifies the value of the risk tolerance. The **RT=** option is used only when **CRITERION=MAXCE** or **CRITERION=MINCE** is specified. If the **RT=** option is not specified, and **CRITERION=MAXCE** or **CRITERION=MINCE** is specified, PROC DTREE changes the value of the **CRITERION=** option to **MAXEV** or **MINEV** (which would mean straight-line utility function and imply infinite risk tolerance).

#### **STAGEIN=SAS-data-set**

names the SAS data set that contains the stage names, stage types, names of outcomes, and their rewards and successors for each stage. If the **STAGEIN=** option is not specified, PROC DTREE uses the most recently created SAS data set.

#### **SUMMARY | NOSUMMARY**

specifies whether an optimal decision summary should be displayed each time the decision tree is evaluated. The decision summary lists all paths through the tree that lead to the target stage as well as the cumulative rewards and the evaluating values of all alternatives for that path. The alternative with optimal evaluating value for each path is marked with an asterisk (\*). The default is **NOSUMMARY**.

**TARGET=stage**

specifies the decision stage up to which the optimal decision policy table is displayed. The TARGET= option is used only in conjunction with the **SUMMARY** option. The stage specified must be a decision stage. If the TARGET= option is not specified, the procedure displays an optimal decision policy table for each decision stage.

**TOLERANCE=d**

specifies either a positive number close to 0 or greater than 1. PROC DTREE treats all numbers within  $\epsilon$  of 0 as 0, where

$$\epsilon = \begin{cases} d & \text{if } d < 1 \\ d \times \epsilon & \text{otherwise} \end{cases}$$

and  $\epsilon$  is the *machine epsilon*. The default value is 1,000.

**WARNING | NOWARNING**

specifies whether the procedure should display a warning message when

- the payoff for an outcome is not assigned in the **PAYOFFS=** data set
- probabilities of events for a given chance stage have been automatically scaled by PROC DTREE because the total probability of the chance stage does not equal 1

The default is **WARNING**.

**YBETWEEN=ybetween <units>**

specifies the vertical distance between two successive end nodes. If the **GRAPHICS** option is specified, the valid values for the optional *units* are listed in [Table 7.8](#).

**Table 7.8** Valid Values for the Units of the YBETWEEN= Option

Unit	Description
CELL	Character cells
CM	Centimeters
INCH	Inches
PCT	Percentage of the graphics output area
SPACE	Height of the box surrounding the node, its predecessor link, and all text information

The value of the YBETWEEN= option must be greater than or equal to 0. Note that if the **COMPRESS** option is specified, the actual distance between two successive end nodes is scaled by PROC DTREE and may not be the same as the YBETWEEN= specification.

If the **LINEPRINTER** option is specified, the optional *units* value can be CELL or SPACE. The value of the YBETWEEN= option must be a nonnegative integer.

If you do not specify units, a unit specification is determined in the following order:

- the GUNIT= option in a GOPTIONS statement, if the GRAPHICS option is specified
- the default unit, CELL

The default value of YBETWEEN= option is 0.

## Graphics Options

The following options are specifically for the purpose of producing a high-resolution quality decision tree diagram.

**ANNOTATE=SAS-data-set**

**ANNO=SAS-data-set**

specifies an input data set that contains appropriate Annotate variables. The ANNOTATE= option enables you to add features (for example, customized legend) to plots produced on graphics devices.

For additional information, refer to the chapter on the annotate data set in *SAS/GRAF Software: Reference*.

**CBEST=color**

**CB=color**

specifies the color for all links in the decision tree diagram that represent optimal decisions. If you do not specify the CBEST= option, the color specification is determined in the following order:

- the CI= option in the  $j$ th generated SYMBOL definition, if the option **LINKB=j** is specified
- the ContrastColor attribute of the GraphData2 element of the current ODS style template (if the GSTYLE system option is active)
- the second color in the colors list

**CLINK=color**

**CL=color**

specifies the color for all links in the decision tree diagram except those that represent optimal decisions. If the CLINK= option is not specified, the color specification is determined in the following order:

- the CI= option in the  $i$ th generated SYMBOL definition, if the option **LINKA=i** is specified
- the ContrastColor attribute of the GraphData3 element of the current ODS style template (if the GSTYLE system option is active)
- the third color in the colors list

**COMPRESS | NOCOMPRESS**

**CP | NOCP**

specifies whether the decision tree diagram should be drawn on one physical page. If the COMPRESS option is specified, PROC DTREE determines the scale so that the diagram is compressed, if necessary, to fit on one physical page. Otherwise, the procedure draws the diagram across multiple pages if necessary. The default is NOCOMPRESS.

**CSYMBOLC=color**

**CC=color**

specifies the color of the symbol used to draw all chance nodes in the decision tree diagram. If the CSYMBOLC= option is not specified, the color specification is determined in the following order:

- the CV= option in the  $m$ th generated SYMBOL definition, if the option **SYMBOLC=m** is specified
- the CSYMBOL= option in a GOPTIONS statement

- the ContrastColor attribute of the GraphData1 element of the current ODS style template (if the GSTYLE system option is active)
- the fifth color in the colors list

**CSYMBOLD=***color*

**CD=***color*

specifies the color of the symbol used to draw all decision nodes in the decision tree diagram. If the CSYMBOLD= option is not specified, the color specification is determined in the following order:

- the CV= option in the *d*th generated SYMBOL definition, if the option **SYMBOLD=d** is specified
- the CSYMBOL= option in a GOPTIONS statement
- the ContrastColor attribute of the GraphData5 element of the current ODS style template (if the GSTYLE system option is active)
- the fourth color in the colors list

**CSYMBOLE=***color*

**CE=***color*

specifies the color of the symbol used to draw all end nodes in the decision tree diagram. If the CSYMBOLE= option is not specified, the color specification is determined in the following order:

- the CV= option in the *n*th generated SYMBOL definition, if the option **SYMBOLE=n** is specified
- the CSYMBOL= option in a GOPTIONS statement
- the ContrastColor attribute of the GraphData8 element of the current ODS style template (if the GSTYLE system option is active)
- the sixth color in the colors list

**CTEXT=***color*

**CT=***color*

specifies the color to be used for all text that appears on plots except on TITLE and FOOTNOTE lines. If the CTEXT= option is not specified, the color specification is determined in the following order:

- the CTEXT= option in a GOPTIONS statement
- the Color attribute of the GraphDataText element of the current ODS style template (if the GSTYLE system option is active)
- the first color in the colors list

**DESCRIPTION=**'*string*'

**DES=**'*string*'

specifies a descriptive string, up to 40 characters long, that appears in the description field of the master menu of PROC GREPLAY. If the DESCRIPTION= option is omitted, the description field contains a description assigned by PROC DTREE.

**DOANNOTATE | NOANNOTATE****DOANNO | NOANNO**

specifies whether the Annotate data set should be processed. If the NOANNOTATE option is specified, the procedure does not process the Annotate data set even though the **ANNOTATE=** option is specified. The default is DOANNOTATE.

**FTEXT=name****FONT=name**

specifies the font to be used for text on plots. If you do not use this option, the font specification is determined in the following order:

- the FTEXT= option in a GOPTIONS statement
- the Font attribute of the GraphDataText element of the current ODS style template (if the GSTYLE system option is active)
- the hardware font for your graphics output device

Refer to the chapter on SAS/GRAF fonts in *SAS/GRAF Software: Reference* for details about SAS/GRAF fonts.

**GOUT=SAS-catalog**

specifies the name of the graphics catalog used to save the output produced by PROC DTREE for later replay. For additional information, refer to the chapter on graphics output in *SAS/GRAF Software: Reference*.

**HSYMBOL=h****HS=h**

specifies that the height of symbols for all nodes in the decision tree diagram is *h* times the heights of symbols assigned by SAS/GRAF software. You can specify the heights of decision nodes, chance nodes, and end nodes by using the HEIGHT= options in the corresponding SYMBOL statements. For example, if you specify the options HSYMBOL=2 and SYMBOLD=1 in the PROC DTREE statement and defined SYMBOL1 as

```
symbol1 height=4 pct;
```

then all decision nodes in the decision tree diagram are sized at  $2 \times 4 = 8\%$  of the graphics output area. The default value is 1.

**HTEXT=h****HT=h**

specifies that the height for all text in plots (except that in TITLE and FOOTNOTE statements) be *h* times the height of the characters assigned by SAS/GRAF software. You can also specify character height by using the HTEXT= option in a GOPTIONS statement.

For example, if you specify the option HTEXT=0.6 in the PROC DTREE statement and also specified a GOPTIONS statement as follows

```
options htext=2 in;
```

then the size of all text is  $0.6 \times 2 = 1.2$  inches. For more explanation of the GOPTIONS statement, refer to the chapter on the GOPTIONS statement in *SAS/GRAF Software: Reference*. The default value is 1.

**IMAGEMAP=SAS-data-set**

names the SAS data set that receives a description of the areas of a graph and a link for each area. This information is for the construction of HTML image maps. You use a SAS DATA step to process the output file and generate your own HTML files. The graph areas correspond to the link information that comes from the **WEB=** variable in the **STAGEIN=** data set. This gives you complete control over the appearance and structure of your HTML pages.

**LEGEND | NOLEGEND****LG | NOLG**

specifies whether the default legend should be displayed. If the NOLEGEND is not specified, the procedure displays a legend at the end of each page of the decision tree diagram. The default is LEGEND.

**LINKA=*i***

If the LINKA=*i* option is specified, then PROC DTREE uses the color specified with the CI= option, the type specified with the LINE= option, and the thickness specified with the WIDTH= option in the *i*th generated SYMBOL definition to draw all links in the decision tree diagram, except those that indicate optimal decisions and those that are continued on subsequent pages. There is no default value for this option. The color, type, and thickness specifications may be overridden by the specifications of the **CLINK=**, **LSTYLE=**, and **LWIDTH=** options in the PROC DTREE statement.

Note that if you specify the LINKA=*i* option, PROC DTREE uses the specifications in the *i*th *generated SYMBOL definition* and not the specifications in the SYMBOL*i* statement. Refer to *SAS/GRAPH Software: Reference* for the details about creating, canceling, reviewing, and altering SYMBOL definitions.

**LINKB=*j***

If the LINKB=*j* option is specified, then PROC DTREE uses the color specified with the CI= option, the type specified with the LINE= option, and the thickness specified with the WIDTH= option in the *j*th generated SYMBOL definition to draw all links that represent optimal decisions. There is no default value for this option. The color, type, and thickness specifications may be overridden by the specifications of the **CBEST=**, **LSTYLEB=**, and **LWIDTHB=** options in the PROC DTREE statement.

Note that if you specify the LINKB=*j* option, PROC DTREE uses the specifications in the *j*th *generated SYMBOL definition* and not the specifications in the SYMBOL*j* statement. Refer to *SAS/GRAPH Software: Reference* for the details about creating, canceling, reviewing, and altering SYMBOL definitions.

**LINKC=*k***

If the LINKC=*k* option is specified, then PROC DTREE uses the type specified with the LINE= option in the *k*th generated SYMBOL definition to draw all links in the decision tree diagram that are continued on subsequent pages. There is no default value for this option. The color and thickness for links continued on another page indicate whether the link represents an optimal decision or not. The type specification may be overridden by the specification of the **LSTYLEC=** option in the PROC DTREE statement.

Note that if you specify the LINKC=*k* option, PROC DTREE uses the specifications in the *k*th *generated SYMBOL definition* and not the specifications in the SYMBOL*k* statement. Refer to *SAS/GRAPH Software: Reference* for the details about creating, canceling, reviewing, and altering SYMBOL definitions.

**LSTYLE=/****L=/*l***

specifies the line type (style) used for drawing all links in the decision tree diagram, except those that represent the optimal decisions and those that are continued on subsequent pages. Valid values for *l* are 1 through 46. If the LSTYLE= option is not specified, the type specification is determined in the following order:

- the LINE= option in the *i*th generated SYMBOL definition, if the option **LINKA=*i*** is specified
- the default value, 1 (solid line)

**LSTYLEB=/*l*2****LB=*l*2**

specifies the line type (style) used for drawing the links in the decision tree diagram that represent optimal decisions. Valid values for *l*2 are 1 through 46. If the LSTYLEB= option is not specified, the type specification is determined in the following order:

- the LINE= option in the *j*th generated SYMBOL definition, if the option **LINKB=*j*** is specified
- the default value, 1 (solid line)

**LSTYLEC=/*l*3****LC=*l*3**

specifies the line type (style) used for drawing the links in the decision tree diagram that are continued on the next subsequent pages. Valid values for *l*3 are 1 through 46.

If the LSTYLEC= option is not specified, the type specification is determined in the following order:

- the LINE= option in the *k*th generated SYMBOL definition, if the option **LINKC=*k*** is specified
- the default value, 2 (dot line)

**LWIDTH=*w*****LTHICK=*w***

specifies the line thickness (width) used to draw all links in the decision tree diagram except those that represent the optimal decisions.

If the LWIDTH= option is not specified, the thickness specification is determined in the following order:

- the WIDTH= option in the *i*th generated SYMBOL definition, if the option **LINKA=*i*** is specified
- the default value, 1

**LWIDTHB=*w*2****LTHICKB=*w*2**

specifies the line thickness (width) used to draw the links in the decision tree diagram that represent optimal decisions. If the LWIDTHB= option is not specified, the thickness specification is determined in the following order:

- the WIDTH= option in the *j*th generated SYMBOL definition, if the option **LINKB=*j*** is specified
- 2 times the thickness for links that represent regular outcomes

**NAME=**'string'

specifies a descriptive string, up to 8 characters long, that appears in the name field of the master menu of PROC GREPLAY. The default is 'DTREE'.

**PAGENUM | NOPAGENUM****PAGENUMBER | NOPAGENUMBER**

specifies whether the page numbers should be displayed in the top right corner of each page of a multipage decision tree diagram. If the NOPAGENUM is not specified, the pages are ordered from top to bottom, left to right.

The default is PAGENUM.

**RC | NORC**

specifies whether the links in the decision tree diagram should be drawn with rounded corners or with rectangular corners. The default is RC.

**SYMBOLC=*m*****SYMBC=*m***

If the SYMBOLC= option is specified, then PROC DTREE uses the color specified with the CV= option, the character specified with the VALUE= option, the font specified with the FONT= option, and the height specified with the HEIGHT= option in the *m*th generated SYMBOL definition to draw all chance nodes in the decision tree diagram. There is no default value for this option. The color and the symbol specifications may be overridden by the specification of the CSYMBOLC= and VSYMBOLC= options in the PROC DTREE statement. The height of the symbol can be changed by the HSYMBOL= option in the PROC DTREE statement.

Note that if you specify the SYMBOLC=*m* option, PROC DTREE uses the specifications in the *m*th generated SYMBOL definition and not the specifications in the SYMBOL*m* statement. Refer to *SAS/GRAFH Software: Reference* for the details about creating, canceling, reviewing, and altering SYMBOL definitions.

**SYMBOLD=*d*****SYMBD=*d***

If the SYMBOLD= option is specified, then PROC DTREE uses the color specified with the CV= option, the character specified with the VALUE= option, the font specified with the FONT= option, and the height specified with the HEIGHT= option in the *d*th generated SYMBOL definition to draw all decision nodes in the decision tree diagram. There is no default value for this option. The color and the symbol specifications may be overridden by the specification of the CSYMBOLD= and VSYMBOLD= options in the PROC DTREE statement. The height of the characters can be changed by the HSYMBOL= option in the PROC DTREE statement.

Note that if you specify the SYMBOLD=*d* option, PROC DTREE uses the specifications in the *d*th generated SYMBOL definition and not the specifications in the SYMBOL*d* statement. Refer to *SAS/GRAFH Software: Reference* for the details about creating, canceling, reviewing, and altering SYMBOL definitions.

**SYMBOLE=n****SYMBE=n**

If the SYMBOLE option is specified, then PROC DTREE uses the color specified with the CV= option, the character specified with the VALUE= option, the font specified with the FONT= option, and the height specified with the HEIGHT= option in the *n*th generated SYMBOL definition to draw all end nodes in the decision tree diagram. There is no default value for this option. The color and the symbol specifications may be overridden by the specification of the CSYMBOLE= and VSYMBOLE= options specified in the PROC DTREE statement. The height of the characters can be changed by the HSYMBOL= option in the PROC DTREE statement.

Note that if you specify the SYMBOLE=n option, PROC DTREE uses the specifications in the *n*th generated SYMBOL definition and not the specifications in the SYMBOL*n* statement. Refer to *SAS/GRAFH Software: Reference* for the details about creating, canceling, reviewing, and altering SYMBOL definitions.

**VSYMBOLC=symbolc-name****VC=symbolc-name**

specifies that the symbol *symbolc-name* from the special symbol table be used to draw all chance nodes in the decision tree diagram. If you do not specify this option, the symbol used is determined in the following order:

- the options VALUE= and FONT= specifications in the *m*th generated SYMBOL definition, if the option SYMBOLC=*m* is specified
- the symbol CIRCLE in the special symbol table

**VSYMBOLD=symbold-name****VD=symbold-name**

specifies that the symbol *symbold-name* from the special symbol table be used to draw all decision nodes in the decision tree diagram. If you do not specify this option, the symbol used is determined in the following order:

- the options VALUE= and FONT= specifications in the *d*th generated SYMBOL definition, if the option SYMBOLD=*d* is specified
- the symbol SQUARE in the special symbol table

**VSYMBOLE=symbole-name****VE=symbole-name**

specifies that the symbol *symbole-name* from the special symbol table be used to draw all end nodes in the decision tree diagram. If you do not specify this option, the symbol used is determined in the following order:

- the options VALUE= and FONT= specifications in the *n*th generated SYMBOL definition, if the option SYMBOLE=*n* is specified
- the symbol DOT in the special symbol table

## Line-Printer Options

The following options are specifically for the purpose of producing line-printer quality decision tree diagram.

### **FORMCHAR<(syni-list)>= 'formchar-string'**

defines characters to be used for features on line-printer plots. The *syni-list* is a list of numbers ranging from 1 to 13. The list identifies which features are controlled with the string characters. The *formchar-string* gives characters for features in *syni-list*. Any character or hexadecimal string can be used. By default, *syni-list* is omitted, and the FORMCHAR= option gives a string for all 13 features. The features associated with values of *syni* are listed in Table 7.9. Note that characters 4, 6, 7, 10, and 12 are not used in drawing a decision tree diagram.

**Table 7.9** Features Associated with the FORMCHAR= Option

Syni	Description of Character	Feature
1	Vertical bar	Vertical link
2	Horizontal bar	Horizontal link
3	Box character (upper left)	Vertical up to horizontal turn
5	Box character (upper right)	Horizontal and down vertical joint
8	Box character (middle right)	Horizontal to split joint
9	Box character (lower left)	Vertical down to horizontal turn
11	Box character (lower right)	Horizontal and up vertical joint
13	Horizontal thick	Horizontal link that represents optimal decision

As an example, the decision tree diagram in Figure 7.7 is produced by the following statement:


```

title "Decision Tree Showing the Effects of FORMCHAR";

data Dtoils4;
  format _STNAME_ $12. _STTYPE_ $2. _OUTCOM_ $10.
    _SUCCES_ $12.;
  input _STNAME_ $ _STTYPE_ $ _OUTCOM_ $ _SUCCES_ $;
  datalines;
Drill      D   Drill      Cost
.          .   Not_Drill  .
Cost       C   Low       Oil_Deposit
.          .   High      Oil_Deposit
Oil_Deposit C   Dry       .
.          .   Wet       .
;

proc dtree stagein=Dtoils4
  nowarning
  ;
  treeplot / formchar(1 2 3 5 8 9 11 13)='|/-/*<\+='
    lineprinter display=(LINK);
quit;

```

**Figure 7.7** Decision Tree Showing the Effects of FORMCHAR**Decision Tree Showing the Effects of FORMCHAR****The DTREE Procedure****Line-printer Plot**

By default, the form character list specified with the SAS system option FORMCHAR= is used; otherwise, the default is '|----|+|---+=+'. Refer to the chapter on the Calendar Procedure in the *SAS Procedures Guide* for more information.

## EVALUATE Statement

**EVALUATE** /*options* ;

The EVALUATE statement causes PROC DTREE to evaluate the decision tree and calculate the optimal decisions. If the **SUMMARY** option is specified a decision summary is displayed. Otherwise, the current optimal value is displayed on the SAS log.

The following **options**, which can appear in the PROC DTREE statement, can also be specified in the EVALUATE statement:

CRITERION= <i>i</i>	MAXPREC= <i>d</i>	MAXWIDTH= <i>mw</i>
NOSUMMARY	NWIDTH= <i>nw</i>	RT= <i>r</i>
SUMMARY	TARGET= <i>stage</i>	

The **MAXPREC=**, **MAXWIDTH=**, and **NWIDTH=**, options are valid only in conjunction with the **SUMMARY** option. The **RT=** option is valid only in conjunction with the **CRITERION=MAXCE** or **CRITERION=MINCE** specification. The options specified in this statement are only in effect for this statement.

## MODIFY Statement

**MODIFY** *outcome-name* **REWARD** *new-value* ;

**MODIFY** *stage-name* **TYPE** ;

The MODIFY statement is used to change either the type of a stage or the reward from an outcome. If **MODIFY** *outcome-name* **REWARD** *new-value* is given where the *outcome-name* is an outcome specified in the **STAGEIN=** data set, and *new-value* is a numeric value, then the reward of the outcome named *outcome-name* is changed to *new-value*.

If **MODIFY stage-name TYPE** is given where *stage-name* is a stage name specified in the **STAGEIN=** data set, then the type of the stage named *stage-name* is changed to '**DECISION**' if its current type is '**CHANCE**' and is changed to '**CHANCE**' if its current type is '**DECISION**'. You cannot change the type of an '**END**' stage. The change of the type of a stage from '**CHANCE**' to '**DECISION**' can help the decision-maker learn how much improvement can be expected if he or she could pick which of the future (or unknown) outcomes would occur. However, if you want to change the type of a stage from '**DECISION**' to '**CHANCE**', the procedure is not able to determine the probabilities for its outcomes unless you specify them in the **PROBIN=** data set.

## MOVE Statement

**MOVE stage1 (BEFORE / AFTER) stage2 ;**

The MOVE statement is used to change the order of the stages. After all data in input data sets have been read, PROC DTREE determines the order (from left to right) of all stages specified in the **STAGEIN=** data set and display the order in the SAS log. The ordering is determined based on the rule that if stage **A** is the successor of an outcome of stage **B**, then stage **A** should occur to the right of stage **B**. The MOVE statement can be used to change the order. If the keyword BEFORE is used, *stage1* becomes the new successor for all immediate predecessors of *stage2*, and *stage2* becomes the new successor for all outcomes of *stage1*. An outcome is said to be an *immediate predecessor* of a stage if the stage is the successor of that outcome. Similarly, if the keyword AFTER is used, the old leftmost (in previous order) successor of outcomes for *stage2* becomes the new successor for all outcomes of *stage1* and the new successor of all outcomes of *stage2* is *stage1*.

There are two limitations: the END stage cannot be moved, and no stage can be moved after the END stage. In practice, any stage after the END stage is useless.

## QUIT Statement

**QUIT ;**

The QUIT statement tells the DTREE procedure to terminate processing. This statement has no options.

## RECALL Statement

**RECALL ;**

This statement tells PROC DTREE to recall the decision model that was saved previously with a **SAVE** statement. The RECALL statement has no options.

## RESET Statement

**RESET options ;**

The RESET statement is used to change options after the procedure has started. All of the options that can be set in the **PROC DTREE** statement can also be reset with this statement, except for the **STAGEIN=**, the **PROBIN=**, and the **PAYOUTS=** data set options.

---

## SAVE Statement

**SAVE** ;

The SAVE statement saves the current model (attributes of stages and outcomes, the ordering of stages, and so on) to a scratch space from which you can call it back later. It is a good idea to save your decision model before you specify any MOVE or MODIFY statements. Then you can get back to your original model easily after a series of statements that change the decision model. The SAVE statement has no options.

---

## SUMMARY Statement

**SUMMARY** /*options* ;

Unlike the **SUMMARY** option on the PROC DTREE statement or the **EVALUATE** statement, which specifies that PROC DTREE display a decision summary when the decision tree is evaluated, the SUMMARY statement causes the procedure to display the summary immediately. If the decision tree has not been evaluated yet, or if it has been changed (by the MOVE, MODIFY, or RECALL statement) since last evaluated, the procedure evaluates or re-evaluates the decision tree before the summary is displayed.

The following options that can appear in the PROC DTREE statement can also be specified in this statement:

**MAXPREC**=*d*    **MAXWIDTH**=*mw*  
**NWIDTH**=*nw*    **TARGET**=*stage*

The options specified in this statement are in effect only for this statement.

---

## TREEPLOT Statement

**TREEPLOT** /*options* ;

The TREEPLOT statement plots the current decision tree (a diagram of the decision problem). Each path in the decision tree represents a possible scenario of the problem. In addition to the nodes and links on the decision tree, the information for each link that can be displayed on the diagram is listed in Table 7.10.

**Table 7.10** Information on Decision Tree Diagram

Information	Labeled by
Stage name for the successor of the link	NL <sup>3</sup>
Outcome name for the link	NL <sup>3</sup>
Probability of the outcome	p=
Value can be expected from the successor	EV=
Instant reward of the outcome	r=
Cumulative rewards of outcomes on the path that leads to the successor	cr=

<sup>3</sup>NL denotes that this information is not labeled.

If necessary, the outcome names and the stage names are displayed above the link, and other information (if there is any) is displayed below the link. The **DISPLAY=** option can be used to control which information should be included in the diagram. The **NOLABEL** can be used to suppress the displaying of the labels.

If the **LINEPRINTER** option is used, the decision nodes, chance nodes, and the end nodes are represented by the characters ‘D’, ‘C’, and ‘E’, respectively. The links are displayed using the specifications of the **FORMCHAR=** option. See the section “[PROC DTREE Statement](#)” on page 399 for more details. In graphics mode, the control of the appearances of nodes and links is more complex. See the section “[Displaying the Decision Tree](#)” on page 427 for more information.

The following options that can appear in the PROC DTREE statement can also be specified in the TREEPLOT statement:

<b>DISPLAY=(</b> <i>information-list</i> <b>)</b>	<b>GRAPHICS</b>	<b>LABEL</b>
<b>LINEPRINTER</b>	<b>MAXPREC=</b> <i>d</i>	<b>MAXWIDTH=</b> <i>mw</i>
<b>NOLABEL</b>	<b>NWIDTH=</b> <i>nw</i>	<b>YBETWEEN=</b> <i>ybetween</i> <units>

The following line-printer options that can appear in the PROC DTREE statement can also be specified in the TREEPLOT statement if the **LINEPRINTER** option is specified:

**FORMCHAR**<(*syni-list*)>=‘*formchar-string*’

Moreover, the following graphics options that can appear in the PROC DTREE statement can also be specified in the TREEPLOT statement if the **GRAPHICS** option is specified:

<b>ANNOTATE=SAS-data-set</b>	<b>CBEST=</b> <i>color</i>	<b>CLINK=</b> <i>color</i>
<b>COMPRESS</b>	<b>CSYMBOLC=</b> <i>color</i>	<b>CSYMBOLD=</b> <i>color</i>
<b>CSYMBOLE=</b> <i>color</i>	<b>CTEXT=</b> <i>color</i>	<b>DESCRIPTION=</b> ‘ <i>string</i> ’
<b>DOANNOTATE</b>	<b>FTEXT=</b> <i>name</i>	<b>GOUT=SAS-catalog</b>
<b>HSYMBOL=</b> <i>h</i>	<b>HTEXT=</b> <i>h</i>	<b>IMAGEMAP=SAS-data-set</b>
<b>LEGEND</b>	<b>LINKA=</b> <i>i</i>	<b>LINKB=</b> <i>j</i>
<b>LINKC=</b> <i>k</i>	<b>LSTYLE=</b> <i>l</i>	<b>LSTYLEB=</b> <i>l2</i>
<b>LSTYLEC=</b> <i>l3</i>	<b>LWIDTH=</b> <i>w2</i>	<b>LWIDTHB=</b> <i>w2</i>
<b>NAME=</b> ‘ <i>string</i> ’	<b>NOANNOTATE</b>	<b>NOCOMPRESS</b>
<b>NOLEGEND</b>	<b>NOPAGENUM</b>	<b>NORC</b>
<b>PAGENUM</b>	<b>RC</b>	<b>SYMBOLC=</b> <i>m</i>
<b>SYMBOLD=</b> <i>d</i>	<b>SYMBOLE=</b> <i>n</i>	<b>VSYMBOLC=</b> <i>symbolc-name</i>
<b>VSYMBOLD=</b> <i>symbold-name</i>	<b>VSYMBOLE=</b> <i>symbole-name</i>	

The options specified in this statement are in effect only for this statement, and they may override the options specified in the **PROC DTREE** statement.

## VARIABLES Statement

**VARIABLES** / *options* ;

The **VARIABLES** statement specifies the variable lists in the input data sets. This statement is optional but if it is used, it must appear immediately after the **PROC DTREE** statement. The options that can appear in the

VARIABLES statement are divided into groups according to the data set in which they occur. Table 7.11 lists all the variables or variable lists associated with each input data set and their types. It also lists the default variables if they are not specified in this statement.

**Table 7.11** Input Data Sets and Their Associated Variables

Data Set	Variable	Type <sup>4</sup>	Interpretation	Default
STAGEIN=	OUTCOME=	C/N	Outcome names	Variables with prefix _OUT
	REWARD=	N	Instant reward	Variables with prefix _REW
	STAGE=	C/N	Stage name	_STNAME_
	SUCCESSOR=	as STAGE=	Immediate successors	Variables with prefix _SUCC
	TYPE=	C/N	Stage type	_STTYPE_
	WEB=	C	HTML page for the stage	
PROBIN=	EVENT=	as OUTCOME=	Event names	Variables with prefix _EVEN
	GIVEN=	as OUTCOME=	Names of given outcomes	Variables with prefix _GIVE
	PROB=	N	Conditional probabilities	Variables with prefix _PROB
PAYOFFS=	ACTION=	as OUTCOME=	Action names of final decision	Variables with prefix _ACT
	STATE=	as OUTCOME=	Outcome names	Variables with prefix _STAT
	VALUE=	N	Values of the scenario	Variables with prefix _VALU

<sup>4</sup>‘C’ denotes character, ‘N’ denotes numeric, ‘C/N’ denotes character or numeric, and ‘as X’ denotes the same as variable X.

## Variables in STAGEIN= Data Set

The following options specify the variables or variable lists in the STAGEIN= input data set that identify the stage name, its type, its outcomes, and the reward; and the immediate successor of each outcome for each stage in the decision model:

### OUTCOME=(variables)

identifies all variables in the STAGEIN= data set that contain the outcome names of the stage specified by the STAGE= variable. If the OUTCOME= option is not specified, PROC DTREE looks for the default variable names that have the prefix \_OUT in the data set. It is necessary to have at least one OUTCOME= variable in the STAGEIN= data set. The OUTCOME= variables can be either all character or all numeric. You cannot mix character and numeric variables as outcomes.

### REWARD=(variables)

### COST=(variables)

identifies all variables in the STAGEIN= data set that contain the reward for each outcome specified by the OUTCOME= variables. If the REWARD= option is not specified, PROC DTREE looks for the default variable names that have the prefix \_REW in the data set. The number of REWARD= variables must be equal to the number of OUTCOME= variables in the data set. The REWARD= variables must have numeric values.

### STAGE=variable

specifies the variable in the STAGEIN= data set that names the stages in the decision model. If the STAGE= option is omitted, PROC DTREE looks for the default variable named \_STNAME\_ in the data set. The STAGE= variable must be specified if the data set does not contain a variable named \_STNAME\_. The STAGE= variable can be either character or numeric.

**SUCCESSOR=(variables)****SUCC=(variables)**

identifies all variables in the **STAGEIN=** data set that contain the names of immediate successors (another stage) of each outcome specified by the **OUTCOME=** variables. These variables must be of the same type and length as those defined in the **STAGE=** option. If the **SUCCESSOR=** option is not specified, PROC DTREE looks for the default variable names that have the prefix **\_SUCC** in the data set. The number of **SUCCESSOR=** variables must be equal to the number of **OUTCOME=** variables. The values of **SUCCESSOR=** variables must be stage names (values of **STAGE=** variables in the same data set).

**TYPE=variable**

identifies the variable in the **STAGEIN=** data set that contains the type identifier of the stage specified by the **STAGE=** variable. If the **TYPE=** option is omitted, PROC DTREE looks for the default variable named **\_STTYPE\_** in the data set. The **TYPE=** variable must be specified if the data set does not contain a variable named **\_STTYPE\_**. The **STAGE=** variable can be either character or numeric.

The following are valid values for the **TYPE=** variable.

		<b>Value</b>			<b>Description</b>
DECISION	or	D	or	1	Identifies the stage as a decision stage
CHANCE	or	C	or	2	Identifies the stage as an uncertain stage
END	or	E	or	3	Identifies the stage as an end stage

It is not necessary to specify an end stage in the **STAGEIN=** data set.

**WEB=variable****HTML=variable**

specifies the character variable in the **STAGEIN=** data set that identifies an HTML page for each stage. The procedure generates an HTML image map using this information for all the decision tree nodes corresponding to a stage.

## Variables in PROBIN= Data Set

The following options specify the variables or variable lists in the **PROBIN=** input data set that identify the given outcome names, the event (outcome) name, and the conditional probability for each outcome of a chance stage.

**EVENT=(variables)**

identifies all variables in the **PROBIN=** data set that contain the names of events (outcomes) that probabilities depend on the outcomes specified by the **GIVEN=** variables. If the **EVENT=** option is not specified, PROC DTREE looks for the default variable names that have the prefix **\_EVEN** in the data set. You must have at least one **EVENT=** variable in the **PROB=** data set. The values of **EVENT=** variables must be outcome names that are specified in the **STAGEIN=** data set.

**GIVEN=(variables)**

identifies all variables in the **PROBIN=** data set that contain the given condition (a list of outcome names) of a chance stage on which the probabilities of the outcome depend. If the **GIVEN=** option is not specified, PROC DTREE looks for the default variable names that have the prefix **\_GIVE** in the data set. It is not necessary to have **GIVEN=** variables in the data set but if there are any, their values must be outcome names that are specified in the **STAGEIN=** data set.

**PROB=(variables)**

identifies all variables in the **PROBIN=** data set that contain the values of the conditional probability of each event specified by the **EVENT=** variables, given that the outcomes specified by the **GIVEN=** variables have occurred. If the PROB= option is not specified, PROC DTREE looks for the default variable names that have the prefix \_PROB in the data set. The number of PROB= variables in the data set must be equal to the number of **EVENT=** variables. The PROB= variables must have numeric values between 0 and 1 inclusive.

**Variables in PAYOFFS= Data Set**

The following options specify the variables or variable lists in the **PAYOFFS=** input data set that identify the possible scenarios (a sequence of outcomes), the final outcome names, and the evaluating values (payoff) of combinations of scenarios and final outcomes.

**ACTION=(variables)**

identifies all variables in the **PAYOFFS=** data set that contain the name of the final outcome for each possible scenario. If the ACTION= option is not specified, PROC DTREE looks for the default variable names that have the prefix \_ACT in the data set. It is not necessary to have any ACTION= variables in the PAYOFFS= data set, but if there are any, their values must be outcome names specified in the **STAGEIN=** data set.

**STATE=(variables)**

identifies all variables in the **PAYOFFS=** data set that contain the names of outcomes that identify a possible scenario (a sequence of outcomes or a path in the decision tree), or the names of outcomes which combine with every outcome specified by the ACTION= variables to identify a possible scenario. If the STATE= option is not specified, PROC DTREE looks for the default variable names that have the prefix \_STAT in the data set. It is not necessary to have any STATE= variables in the PAYOFFS= data set, but if there are any, their values must be outcome names specified in the **STAGEIN=** data set.

**VALUE=(variables)****PAYOFFS=(variables)****UTILITY=(variables)****LOSS=(variables)**

identifies all variables in the **PAYOFFS=** data set that contain the evaluating values or payoffs for all possible scenarios identified by the outcomes specified by the **STATE=** variables and the outcomes specified by the associated ACTION= variables. If the VALUE= option is not specified, PROC DTREE looks for the default variable names that have the prefix \_VALU in the data set. The number of VALUE= variables must be equal to the number of ACTION= variables if there are any ACTION= variables. If there are no ACTION= variables in the data set, at least one **STATE=** variable must be in the data set, and the number of VALUE= variables must be exactly 1. The VALUE= variables must have numeric values.

**VPC Statement**

**VPC** *chance-stage-name* ;

The VPC statement causes PROC TREE to compute the value of perfect control (the value of controlling an uncertainty). The effect of perfect control is that you can pick the outcome of an uncertain stage. This value

gives an upper limit on the amount you should be willing to spend on any control procedure. Only the name of a chance stage can be used to calculate the value of perfect control. The procedure evaluates the decision tree, if it has not already done so, before computing this value.

## VPI Statement

**VPI** *chance-stage-name* ;

The VPI statement causes PROC DTREE to compute the value of perfect information. The value of perfect information is the benefit of resolving an uncertain stage before making a decision. This value is the upper limit on the improvement that can be expected for any information gathering effort. Only the name of a chance stage can be used to calculate the value of perfect information. The procedure evaluates the decision tree, if it has not already done so, before computing this value.

## Details: DTREE Procedure

### Input Data Sets

A decision problem is normally constructed in three steps:

1. A structuring of the problem in terms of decisions, uncertainties, and consequences.
2. Assessment of probabilities for the events.
3. Assessment of values (payoffs, losses, or preferences) for each consequence or scenario.

PROC DTREE represents these three steps in three SAS data sets. The **STAGEIN=** data set describes the structure of the problem. In this data set, you define all decisions and define all key uncertainties. This data set also contains the relative order of when decisions are made and uncertainties are resolved (planning horizon). The **PROBIN=** data set assigns probabilities for the uncertain events, and the **PAYOFFS=** data set contains the values (or utility measure) for each consequence or scenario. See the section “[Overview: DTREE Procedure](#)” on page 382 and the section “[Getting Started: DTREE Procedure](#)” on page 383 for a description of these three data sets.

PROC DTREE is designed to minimize the rules for describing a problem. For example, the **PROBIN=** data set is required only when the evaluation and analysis of a decision problem is necessary. Similarly, if the **PAYOFFS=** data set is not specified, the DTREE procedure assumes all payoff values are 0. The order of the observations is not important in any of the input data sets. Since a decision problem can be structured in many different ways and the data format is so flexible, all possible ways of describing a given decision problem cannot be shown here. However, some alternate ways of supplying the same problem are demonstrated. For example, the following statements show another way to input the oil wildcatter’s problem described in the section “[Introductory Example](#)” on page 383.

```

data Dtoils3;
  format _STNAME_ $12. _STTYPE_ $2. _OUTCOM_ $10.
    _REWARD_ dollar12.0 _SUCCES_ $12.;
  input _STNAME_ $12. _STTYPE_ $4. _OUTCOM_ $12.
    _REWARD_ dollar12.0 _SUCCES_ $12.;
  datalines;
Drill      D   Drill          .     Cost
.           .   Not_drill       .
Cost       C   Low            -$150,000 Oil_deposit
.           .   Fair             -$300,000 Oil_deposit
.           .   High            -$500,000 Oil_deposit
Oil_deposit C   Dry            .
.           .   Wet              $700,000 .
.           .   Soaking         $1,200,000 .
;

/* -- create PAYOFFS= data set                                -- */
data Dtoilp3;
  input _EVENT1 $ _PROB1 _EVENT2 $ _PROB2;
  datalines;
Low        0.2  Dry        0.5
Fair       0.6  Wet        0.3
High       0.2  Soaking    0.2
;

/* -- PROC DTREE statements                                    -- */
title "Oil Wildcatter's Problem";
proc dtree stagein=Dtoils3
  probin=Dtoilp3
  nowarning;
  evaluate / summary;

```

Note that the **STAGEIN=** data set describes the problem structure and the payoffs (using the **REWARD=** variable). Thus, the **PAYOFFS=** data set is no longer needed. Note also the changes made to the **PROBIN=** data set. The results, shown in [Figure 7.8](#), are the same as those shown in [Figure 7.2](#). However, the rewards and the payoffs are entirely different entities in decision tree models. Recall that the reward of an outcome means the *instant returns* when the *outcome* is realized. On the other hand, the payoffs are the *return* from each *scenario*. In the other words, the decision tree model described in the previous code and the model described in the section “[Introductory Example](#)” on page 383 are not equivalent, even though they have the same optimal decision.

**Figure 7.8** Optimal Decision Summary of the Oil Wildcatter's Problem

Oil Wildcatter's Problem		
The DTREE Procedure		
Optimal Decision Summary		
<hr/>		
<b>Order of Stages</b>		
<b>Stage</b>	<b>Type</b>	
Drill	Decision	
Cost	Chance	
Oil_deposit	Chance	
<u>ENDST_</u>	End	
<hr/>		
<b>Decision Parameters</b>		
<b>Decision Criterion:</b> Maximize Expected Value (MAXEV)		
<b>Optimal Decision Yields:</b> 140000		
<hr/>		
<b>Optimal Decision Policy</b>		
Up to Stage Drill		
<b>Alternatives</b>		
or		
<b>Outcomes</b>	<b>Cumulative Reward</b>	
	<b>Evaluating Value</b>	
Drill	\$0	140000*
Not_drill	\$0	0

You can try many alternative ways to specify your decision problem. Then you can choose the model that is most convenient and closest to your real problem. If PROC DTREE cannot interpret the input data, it writes a message to that effect to the SAS log unless the **NOWARNING** option is specified. However, there are mistakes that PROC DTREE cannot detect. These often occur after the model has been modified with either the **MOVE** statement or the **MODIFY** statement. After a **MOVE** statement is specified, it is a good idea to display the decision tree (using the **TREEPLOT** statement) and check the probabilities and value assessments to make sure they are reasonable.

For example, using the **REWARD=** variable in the **STAGEIN=** data set to input the payoff information as shown in the previous code may cause problems if you change the order of the stages. Suppose you move the stage '**Cost**' to the beginning of the tree, as was done in the section “**Sensitivity Analysis and Value of Perfect Information**” on page 389:

```
move Cost before Drill;
evaluate / summary;
```

The optimal decision yields \$140,000, as shown on the optimal decision summary in Figure 7.9.

**Figure 7.9** Optimal Decision Summary of the Oil Wildcatter's Problem**Oil Wildcatter's Problem****The DTREE Procedure****Optimal Decision Summary**

Order of Stages	
Stage	Type
Cost	Chance
Drill	Decision
Oil_deposit	Chance
<u>ENDST_</u>	End

Decision Parameters	
Decision Criterion: Maximize Expected Value (MAXEV)	
Optimal Decision Yields: 140000	

Optimal Decision Policy			
Up to Stage Drill			
Alternatives or Outcomes	Cumulative Reward	Evaluating Value	
Low Drill	\$-150,000	450000*	
Low Not_drill	\$-150,000	0	
Fair Drill	\$-300,000	450000*	
Fair Not_drill	\$-300,000	0	
High Drill	\$-500,000	450000*	
High Not_drill	\$-500,000	0	

Recall that when this was done in the section “Sensitivity Analysis and Value of Perfect Information” on page 389, the optimal decision yielded \$150,000. The reason for this discrepancy is that the cost of drilling, implemented as (negative) instant rewards here, is imposed on all scenarios including those that contain the outcome '**Not\_drill**'. This mistake can be observed easily from the **Cumulative Reward** column of the optimal decision summary shown [Figure 7.9](#).

Changing a decision stage to a chance stage is another example where using the **MODIFY** statement without care may cause problems. PROC DTREE cannot determine the probabilities of outcomes for this new chance stage unless they are included in the **PROBIN=** data set. In contrast to changing a chance stage to a decision stage (which yields insight on the value of gaining control of an uncertainty), changing a decision stage to a chance stage is not likely to yield any valuable insight even if the needed probability data are included in the **PROBIN=** data set, and it should be avoided.

---

## Missing Values

In the **STAGEIN=** data set, missing values are allowed only for the **STAGE=** and **TYPE=** variables when the information of a stage is specified in more than one observation. In this case, missing values for the **STAGE=** and **TYPE=** variables are not allowed for the first observation defining the stage. Missing values for the **OUTCOME=**, **GIVEN=**, **EVENT=**, **STATE=**, and **ACTION=** variables are ignored. Missing values for

the REWARD=, PROB=, and VALUE= variables are treated as 0. Missing values for the SUCCESSOR= variables are ignored if the value for the corresponding OUTCOME= variable is also missing.

## Interactivity

The DTREE procedure is interactive. You start the procedure with the PROC DTREE statement and terminate it with the QUIT statement. It is not necessary to have a VARIABLES statement, although if you do include one, it must appear immediately after the PROC DTREE statement. The other statements such as the EVALUATE, MODIFY, MOVE, RECALL, RESET, SAVE, SUMMARY, TREEPLOT, VPC, and VPI, as well as the FOOTNOTE, GOPTIONS, NOTE, SYMBOL, and TITLE statements of SAS/GRAF Software can be used in any order and as often as needed. One exception is that the RECALL statement has to be preceded by at least one SAVE statement.

When an error is detected during processing a statement other than the PROC DTREE statement and the QUIT statement, the procedure terminates if the option ERRHANDLE=QUIT is specified; otherwise it stops processing the current statement and waits for the next statement. In either case, an error message is written to the SAS log. If an error is detected in the PROC DTREE statement or the QUIT statement, the procedure terminates immediately with an error message.

## Options in Multiple Statements

Many options that can be specified in the PROC DTREE statement can also appear in other statements. The options specified in the PROC DTREE statement remain in effect for all statements until the end of processing or until they are changed by a RESET statement. In this sense, those options are *global* options. The options specified in other statements are in effect only for the statement in which they are specified; hence, they are *local* options. If an option is specified both in the PROC DTREE statement and in another statement, the local specification overrides the global specification.

For example, the following statements

```
reset criterion=maxev;
evaluate / criterion=maxce rt=700000;
summary;
```

imply that the decision problem is evaluated and the optimal decision is determined based on the criterion MAXCE with RT=700000. However, the optimal decision summary produced by the SUMMARY statement is based on the option CRITERION=MAXEV and not the MAXCE criterion. If you want an option to be set permanently, use the RESET statement.

## The Order of Stages

The order of stages is an important issue in structuring the decision problem. This sets the sequence of events or a time horizon and determines when a decision has to be made and when a chance stage has its uncertainty resolved. If a decision stage precedes another decision stage in the stages order, the decision to the right is made after the decision to the left. Moreover, the choice made in the first decision is remembered by the

decision maker when he or she makes the second decision. Any chance stages that occur to the left of a decision stage have their uncertainty resolved before the decision is made. In other words, the decision maker knows what actually happened when he or she makes the decision. However, the order of two chance stages is fairly arbitrary if there are no other decision stages between them. For example, you can change the order of stages '**Cost**' and '**Oil\_Deposit**' in the oil wildcatter's problem without affecting the results.

PROC DTREE determines the order (from left to right) of all stages specified in the **STAGEIN=** data set. The ordering is based on the rule that if stage **A** is the successor of an outcome of stage **B**, then stage **A** should occur to the right of (or after) stage **B**. With the **MOVE** statement, you can change this order. The **MOVE** statement is very useful in determining the value (benefit or penalty) of postponing or hurrying a decision. In particular, the *value of perfect information* about an uncertainty can be determined by moving the corresponding chance stage to the beginning. However, as mentioned in early sections, the results may be misleading if you use the **MOVE** statement without care. See the section “[Input Data Sets](#)” on page 418 for an example.

Suggestions for preventing misleading results are as follows:

- Using the **SAVE** statement, always save the original structure before making any changes.
- Use the **TREEPLOT** statement to display the complete decision tree and check all details after you change the order.

## Evaluation

The **EVALUATE** statement causes PROC DTREE to calculate the optimal decision. The evaluate process is done by successive use of two devices:

- Find a certain equivalent for the uncertain evaluating values at each chance node.
- Choose the best alternative at each decision node.

The *certain equivalent* of an uncertainty is the certain amount you would accept in exchange for the uncertain venture. In other words, it is a single number that characterizes an uncertainty described by a probability distribution. This value is subjective and can vary widely from person to person. There are two quantities, closely related to the certain equivalent, that are commonly used by decision-makers: the most likely value and the expected value. The *most likely value* of an uncertainty is the value with the largest probability. The *expected value* is the sum of all outcomes multiplied by their probabilities.

Perhaps the most popular way to find the certain equivalent for an uncertainty is the use of *utility function* or *utility curve*. *Utility* is a measurement of relative *preference* to the decision maker for particular outcomes. The utility function assigns a utility to payoff when it is in terms of continuous values such as money. The certain equivalent of an uncertainty (a random variable) is calculated by the following steps:

1. Use the utility function or the utility curve to find the utility values of the outcomes.
2. Calculate the expected utility of the uncertainty.

3. Determine the certain equivalent of the uncertainty as the value that corresponding utility value is the expected utility.

Refer to Raiffa (1970) for a complete discussion of the utility function.

A simple case that is commonly used is the straight line utility curve or the linear utility function. The linear utility function has the form

$$u(x) = a + bx$$

where  $x$  is the evaluating value, and  $a$  and  $b$  are parameters set by the choice of two points in the utility curve. For example, if the utility curve passes two points  $u(0) = 0$  and  $u(1000) = 1$ , then parameters  $a$  and  $b$  are set by  $a = 0$  and  $b = 1 / 1000$ . The certain equivalent of an uncertainty based on this function is the expected value.

Another special case that is commonly used is the exponential utility function, as

$$u(x) = a - b \times \exp(-x/r)$$

where, again,  $a$  and  $b$  can be set by the choice of two arbitrary points in the utility curve. For example, if your utility curve goes through points  $(0,0)$  and  $(1000,1)$ , then  $a$  and  $b$  are given by

$$a = b = 1/[1 - \exp(-1000/r)]$$

If an uncertain venture  $A$  has  $n$  events, event  $i$  having probability  $p_i$  and payoff  $x_i$ , and if the utility function is an exponential function as in the preceding example, then the certain equivalent of  $A$  is


$$\text{CE}(A) = -r \ln \left[ \sum_{i=1}^n p_i \exp(-x_i/r) \right]$$

and is independent of the choice of values for  $a$  and  $b$  (provided that  $b > 0$ ) (Raiffa 1970).


The parameter  $r$ , called the *risk tolerance*, describes the curvature of the utility function. Moreover, the quantity  $1/r$ , called *risk aversion coefficient* (Howard 1968) is a measure of risk aversion.

Experimental results show that within a reasonable range of values, many utility curves can be fit quite well by an exponential function.

If your utility function is an exponential function as in the preceding example, the risk tolerance can be estimated by the largest number  $R$  for which the following venture is still acceptable to you.

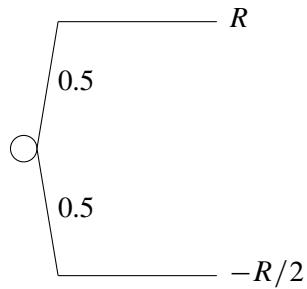

A similar way to approximate the risk tolerance is to find the largest value  $R$  for which the venture is acceptable (Howard 1988).

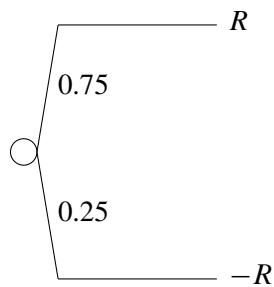

For corporate decision making, there are some rules of thumb for estimating the risk tolerance. Examples are to set risk tolerance about equal to one of the following:

- net income of the company
- one sixth of equity
- six percent of net sales

To reveal how well these rules perform in assessing corporate risk tolerance, Howard (1988) provided the following two tables: Table 7.12 shows the relationship between the risk tolerance and financial measures of four large oil and chemicals companies. There, the risk tolerances are obtained from the top executives of the companies. The net sales, net income, and equity are obtained from the annual reports of the four companies.

**Table 7.12** Relating Corporate Risk Tolerance to Financial Measures

Measure (\$ millions)	Company			
	A	B	C	D
Net Sales	2,300	3,307	16,000	31,000
Net Income	120	152	700	1,900
Equity	1,000	1,153	6,500	12,000
Risk Tolerance	150	200	1,000	2,000

Table 7.13 shows the ratio of risk tolerance to each of the other quantities.

**Table 7.13** Ratios of Corporate Risk Tolerance to Financial Measures

Measure	Company				Average
	A	B	C	D	
RT/Sales	0.0652	0.0605	0.0625	0.0645	0.0632
RT/Income	1.25	1.32	1.43	1.05	1.26
RT/Equity	0.150	0.174	0.154	0.167	0.161

Once the certain equivalents for all chance nodes are assessed, the choice process at each decision node is fairly simple; select the alternative yielding either the maximum or the minimum (depending on the problem) future certain equivalent value.\* You can use the **CRITERION=** option to control the way the certain equivalent is calculated for each chance node and the optimal alternative is chosen at each decision node. Possible values for the **CRITERION=** option are listed in Table 7.5. If you use an exponential utility function, the **RT=** option can be used to specify your risk tolerance. You also have control over how to present the solution. By default, PROC DTREE writes the value of the optimal decisions to the SAS log. In addition, with the **SUMMARY** option, you can ask PROC DTREE to display the optimal decision summary to the output.

## Displayed Output

The **SUMMARY** statement and the **SUMMARY** option in an **EVALUATE** statement cause PROC DTREE to display a optimal decision summary for the decision model. This output is organized into various tables, and they are discussed in order of appearance.

\*The future certain equivalent value is often referred to as the evaluating value in this documentation.

## Order of stages

The Order of stages table lists all stages, and their types, in order of appearance in the decision model. See the section “[The Order of Stages](#)” on page 422 for details.

For ODS purposes, the label of the Order of stages table is “Stages.”

## Decision Parameters

The Decision Parameters table describes the criterion used for determining the optimal decision and the certain equivalent for replacing uncertainties. If you specify the option **CRITERION=MAXCE** or **CRITERION=MINCE** in the **PROC DTREE** statement or in the **EVALUATE** statement, an additional row is added to the table listing the value of the risk tolerance. It also contains a row showing the value of the optimal decision yields. For additional information, see the section “[Evaluation](#)” on page 423.

For ODS purposes, the label of the Decision Parameters table is “Parameters.”

## Optimal Decision Policy

By default, PROC DTREE produces an Optimal Decision Policy table for each decision stage. You can use the **TARGET=** option to force PROC DTREE to produce only one table for a particular stage. The Alternatives or Outcomes columns list the events in the scenario that leads to the current stage. The Cumulative Reward column lists the rewards accumulated along the scenario to the events of the current target stage. The Evaluating Value column lists the values that can be expected from the events of the target stage. An asterisk (\*) is placed beside an evaluating value indicates the current event is the best alternative of the given scenario.

For ODS purposes, the label of the Optimal Decision Policy table is “Policy.”

## Displaying the Decision Tree

PROC DTREE draws the decision tree either in line-printer mode or in graphics mode. However, you need to have SAS/GRAF software licensed at your site to use graphics mode. In many cases, the procedure draws the decision tree across page boundaries. If the decision tree diagram is drawn on multiple pages, the procedure numbers each page of the diagram on the upper right corner of the page (unless the **NOPAGENUM** option is specified). The pages are numbered starting with the upper left corner of the entire diagram. Thus, if the decision tree diagram is broken into three horizontal and four vertical levels and you want to paste all the pieces together to form one picture, they should be arranged as shown in [Figure 7.10](#).

**Figure 7.10** Page Layout of the Decision Tree Diagram

1	5	9
2	6	10
3	7	11
4	8	12

The number of pages that are produced depends on the size of the tree and on the number of print positions that are available in the horizontal and vertical directions. **Table 7.14** lists all options you can use to control the number of pages.

**Table 7.14** Options That Control the Number of Pages

Option	Effect
DISPLAY=	Amounts of information displayed on the diagram
MAXPREC=	Maximum decimal width allowed (the precision) to format numerical values into $w.d$ format
MAXWIDTH=	Maximum field width allowed to format numerical values
NOLABEL	No labels are displayed on the diagram
NWIDTH=	Maximum field width allowed to format outcome names
YBETWEEN=	Vertical spaces between two successive end nodes

If the **GRAPHICS** option is used, the following options can be used to control the number of pages:

- The **COMPRESS** option draws the entire decision tree on one page.
- The **HSYMBOL=** option controls the height of all symbols.
- The **HTEXT=** option controls the height of text in the tree.
- The **HEIGHT=** option in a **SYMBOL** definition specifies the height of a symbol.
- The **HTEXT=** option in a **GOPTIONS** statement specifies the height of all text.
- The **HTITLE=** option in a **GOPTIONS** statement specifies the height of the first title line.

- The HPOS= and VPOS= options in a GOPTIONS statement change the number of rows and columns.

The font used for all text can also affect the number of pages needed. Some fonts take more space than others.

If the decision tree diagram is produced on a line printer, you can use the FORMCHAR= option to control the appearance of the links and the junctions of the diagram. When you specify the GRAPHICS option, several options are available to enhance the appearance of the decision tree diagram. These are described in the section “[Graphics Options](#)” on page 403. In addition, many other options are available in the GOPTIONS and SYMBOL statements for controlling the details of graphics output. See the relevant chapters in *SAS/GRAFH Software: Reference* for a detailed discussion of the GOPTIONS and SYMBOL statements. ODS graphical styles can be applied to the decision tree diagram; see the section “[ODS Style Templates](#)” on page 432 for more information.

[Table 7.15](#), [Table 7.16](#), and [Table 7.17](#) show the relationship among the options for controlling the appearance of texts, nodes, and links, respectively. The order that PROC DTREE uses in determining which option is in effect is also provided. The order assumes that the GSTYLE system option is in effect; if that is not the case, then the steps that refer to ODS style templates are ignored. Names with arguments indicate style elements and attributes of the current ODS style template. For example, “GraphDataText(‘Font’)” refers to the Font attribute of the GraphDataText element.

For ODS purposes, the label of the decision tree diagram drawn in line-printer quality is “Treeplot.”

**Table 7.15** Options That Control Text Appearance

Object	Specification	Search Order
Text	Font	<ol style="list-style-type: none"> <li>1. The <code>FTEXT=</code> option</li> <li>2. The <code>FTEXT=</code> option in a GOPTIONS statement</li> <li>3. <code>GraphDataText('Font')</code></li> <li>4. Hardware font</li> </ol>
	Color	<ol style="list-style-type: none"> <li>1. The <code>CTEXT=</code> option</li> <li>2. The <code>CTEXT=</code> option in a GOPTIONS statement</li> <li>3. <code>GraphDataText('ContrastColor')</code></li> <li>4. The first color in the colors list</li> </ol>
	Height	<ol style="list-style-type: none"> <li>1. The value of the <code>HTEXT=</code> option<sup>1</sup> times the value of the <code>HTEXT=</code> option<sup>2</sup> in a GOPTIONS statement</li> </ol>

<sup>1</sup>If this option is not specified, the default value 1 is used.

<sup>2</sup>The default value of this option is 1 unit.

**Table 7.16** Options That Control Node Appearance

Object	Specification	Search Order
Chance Nodes	Symbol	<ol style="list-style-type: none"> <li>1. The <code>VSYMBOLC=</code> option</li> <li>2. The <code>VALUE=</code> and <code>FONT=</code> options in the <i>m</i>th generated SYMBOL definition, if <code>SYMBOLC=m</code> is specified</li> <li>3. The default symbol, CIRCLE</li> </ol>
	Color	<ol style="list-style-type: none"> <li>1. The <code>CSYMBOLC=</code> option</li> <li>2. The <code>CV=</code> option in the <i>m</i>th generated SYMBOL definition, if <code>SYMBOLC=m</code> is specified</li> <li>3. The <code>CSYMBOL=</code> option in a GOPTIONS statement</li> </ol>

**Table 7.16** (continued)

Object	Specification	Search Order
		4. GraphData1('ContrastColor') 5. The fifth color in the colors list
Height		1. $h$ times the value of the HEIGHT= option in the $m$ th generated SYMBOL definition, if both HSYMBOL= $h$ and SYMBOLC= $m$ are specified 2. The HSYMBOL= option, if it is specified 3. The HEIGHT= option in the $m$ th generated symbol definition, if SYMBOLC= $m$ is specified 4. The default value, 1 cell
Decision Nodes	Symbol	1. The VSYMBOLD= option 2. The VALUE= and FONT= options in the $d$ th generated SYMBOL definition, if SYMBOLD= $d$ is specified 3. The default value, SQUARE
	Color	1. The CSYMBOLD= option 2. The CV= option in the $d$ th generated SYMBOL definition, if SYMBOLD= $d$ is specified 3. The CSYMBOL= option in a OPTIONS statement 4. GraphData5('ContrastColor') 5. The fourth color in the colors list
	Height	1. $h$ times the value of the HEIGHT= option in the $d$ th generated SYMBOL definition, if both HSYMBOL= $h$ and SYMBOLD= $d$ are specified 2. The HSYMBOL= option, if it is specified 3. The HEIGHT= option in the $d$ th generated symbol definition, if SYMBOLD= $d$ is specified 4. The default value, 1 cell
End Nodes	Symbol	1. The VSYMBOLE= option 2. The VALUE= and FONT= options in the $n$ th generated SYMBOL definition, if SYMBOLE= $n$ is specified 3. The default value, DOT
	Color	1. The CSYMBOLE= option 2. The CV= option in the $n$ th generated SYMBOL definition if the option SYMBOLE= $n$ is specified 3. The CSYMBOL= option in a OPTIONS statement 4. GraphData8('ContrastColor') 5. The sixth color in the colors list
	Height	1. $h$ times the value of the HEIGHT= option in the $n$ th generated SYMBOL definition, if both HSYMBOL= $h$ and SYMBOLE= $n$ are specified 2. The HSYMBOL= option, if it is specified 3. The HEIGHT= option in the $n$ th generated symbol definition, if SYMBOLE= $n$ is specified 4. The default value, 1 cell

**Table 7.17** Options That Control Link Appearance

Object	Specification	Search Order
Links for Regular Outcomes	Type	<ol style="list-style-type: none"> <li>1. The <b>LSTYLE</b>= option</li> <li>2. The LINE= option in the <i>i</i>th generated SYMBOL definition, if <b>LINKA</b>=<i>i</i> is specified</li> <li>3. The default value, 1 (solid line)</li> </ol>
	Color	<ol style="list-style-type: none"> <li>1. The <b>CLINK</b>= option</li> <li>2. The CI= option in the <i>i</i>th generated SYMBOL definition, if <b>LINKA</b>=<i>i</i> is specified</li> <li>3. GraphData3('ContrastColor')</li> <li>4. The third color in the colors list</li> </ol>
	Thickness	<ol style="list-style-type: none"> <li>1. The <b>LWIDTH</b>= option</li> <li>2. The WIDTH= option in the <i>i</i>th generated SYMBOL definition, if <b>LINKA</b>=<i>i</i> is specified</li> <li>3. The default value, 1</li> </ol>
Links for Optimal Decision	Type	<ol style="list-style-type: none"> <li>1. The <b>LSTYLEB</b>= option</li> <li>2. The LINE= option in the <i>j</i>th generated SYMBOL definition, if <b>LINKB</b>=<i>j</i> is specified</li> <li>3. The default value, 1 (solid line)</li> </ol>
	Color	<ol style="list-style-type: none"> <li>1. The <b>CBEST</b>= option</li> <li>2. The CI= option in the <i>j</i>th generated SYMBOL definition, if <b>LINKB</b>=<i>j</i> is specified</li> <li>3. GraphData2('ContrastColor')</li> <li>4. The second color in the colors list</li> </ol>
	Thickness	<ol style="list-style-type: none"> <li>1. The <b>LWIDTHB</b>= option</li> <li>2. The WIDTH= option in the <i>j</i>th generated SYMBOL definition, if <b>LINKB</b>=<i>j</i> is specified</li> <li>3. 2 times the thickness of links that represent regular outcomes</li> </ol>
Links That Fall across Pages	Type	<ol style="list-style-type: none"> <li>1. The <b>LSTYLEC</b>= option</li> <li>2. The LINE= option in the <i>k</i>th generated SYMBOL definition, if <b>LINKC</b>=<i>k</i> is specified</li> <li>3. The default value, 2 (dot line)</li> </ol>
	Color	1. Depends on whether or not it represents an optimal decision
	Thickness	1. Depends on whether or not it represents an optimal decision

---

## Web-Enabled Decision Tree

The **WEB**= variable in the **STAGEIN**= data set enables you to define an HTML reference for each stage. This HTML reference is currently associated with all the decision tree nodes that correspond to the stage. The **WEB**= variable is a character variable, and the values need to be of the form **HREF**=*htmlpage*.

In addition, you can also store the coordinate and link information defined by the **WEB**= option in a SAS data set by specifying the **IMAGEMAP**= option in the **PROC DTREE** statement or in the **TREEPLOT** statement. If you process this SAS data set by using a DATA step, you can generate customized HTML pages for your decision tree diagram.

---

## ODS Table Names

PROC DTREE assigns a name to each table that it creates. You can use these names to reference the table when you use the Output Delivery System (ODS) to select tables and create output data sets. These names are listed in Table 7.18. For more information about ODS, see the chapter on ODS in the *SAS/STAT User's Guide*.

**Table 7.18** ODS Tables Produced in PROC DTREE

ODS Table Name	Description	Statement / Option
Parameters	Decision parameters	<code>SUMMARY</code> or <code>EVALUATE / SUMMARY</code>
Policy	Optimal decision policy	<code>SUMMARY</code> or <code>EVALUATE / SUMMARY</code>
Stages	List of stages in order	<code>SUMMARY</code> or <code>EVALUATE / SUMMARY</code>
Treeplot	Line-printer plot of decision tree	<code>TREEPLOT / LINEPRINTER</code>

---

## ODS Style Templates

ODS style templates, or *styles*, control the overall look of your output. An ODS style template consists of a set of *style elements*. A style element is a collection of *style attributes* that apply to a particular feature or aspect of the output. You can specify a value for each attribute in a style. See Chapter 21, “Statistical Graphics Using ODS” (*SAS/STAT User's Guide*), for a thorough discussion of ODS Graphics.

To create your own style or to modify a style for use with ODS Graphics, you need to understand the relationships between style elements and graph features. This information is provided in the ODS Graphics documentation at <http://support.sas.com/documentation/onlinedoc/base/>. You create and modify style templates with the TEMPLATE procedure. For more information, see the section “TEMPLATE Procedure: Creating a Style Template” in the *SAS Output Delivery System: User's Guide*. Kuhfeld (2010) also offers detailed information and examples.

### PROC DTREE Style Template

A predefined ODS style template named DTREE is available for the DTREE procedure. You can use the template to maintain a consistent appearance in all graphical output produced by the procedure.

To change the current style, specify the `STYLE=` option in an ODS destination statement. The specified style is applied to all output for that destination until you change or close the destination or start a new SAS session. For example, the following statement specifies that ODS should apply the DTREE style template to all HTML output:

```
ods html style=dtree;
```

To disable the use of graphical styles, specify the SAS system option NOGSTYLE.


The parent style template for the DTREE style is the DEFAULT style. Table 7.19 lists the style elements (in bold) and corresponding attributes specified in the DTREE style. The table also indicates which, if any, PROC DTREE options or graphics options (in a GOPTIONS statement) can be used to override the value of a style attribute.

**Table 7.19** Style Elements and Attributes in the DTREE Style

Element/Attributes	Description	DTREE Option	GOPTION
<b>GraphColors</b>	Colors of various graph features		
gadata5	Decision nodes	CSYMBOLD=	COLORS=
gadata1	Chance nodes	CSYMBOLC=	COLORS=
gadata8	End nodes	CSYMOBLE=	COLORS=
gadata3	Regular links	LINK=	COLORS=
gadata2	Optimal links	CBEST=	COLORS=
gtextt	Title text		CTITLE=
gtext	Text		CTEXT=
<b>GraphFonts</b>	Fonts for various graph features		
GraphDataFont	Default	FTEXT=	
GraphLabelFont	Labels	FTEXT=	
GraphTitleFont	Title text	FTITLE=	
<b>GraphLabelText</b>	Attributes related to general text		
ContrastColor	GraphColors('gtext')	CTEXT=	CTEXT=
Font	GraphFonts('GraphDataFont')	FTEXT=	FTEXT=
<b>GraphTitleText</b>	Attributes related to title text		
Color	GraphColors('gtext')		CTITLE=
Font	GraphFonts('gtext')		FTITLE=
<b>GraphTitle1Text</b>	Attributes related to the first title text		
Color	GraphColors('gtext')		CTITLE=
Font	GraphFonts('gtext')		FTITLE=
<b>GraphLabelText</b>	Attributes related to label text		
Color	GraphColors('glabel')	CTEXT=	
Font	GraphFonts('GraphTitleFont')	FTEXT=	
<b>GraphDataDefault</b>	Default values		
Color	GraphColors('gdata')		COLORS=
<b>GraphBackground</b>	Attributes related to graph background		
Image	Dtree.jpg		CBACK=

Attributes that you do not override retain the values specified in the style template.

Figure 7.11 demonstrates features of the DTREE graphical style. The decision tree in the figure is the first output from Example 7.4.

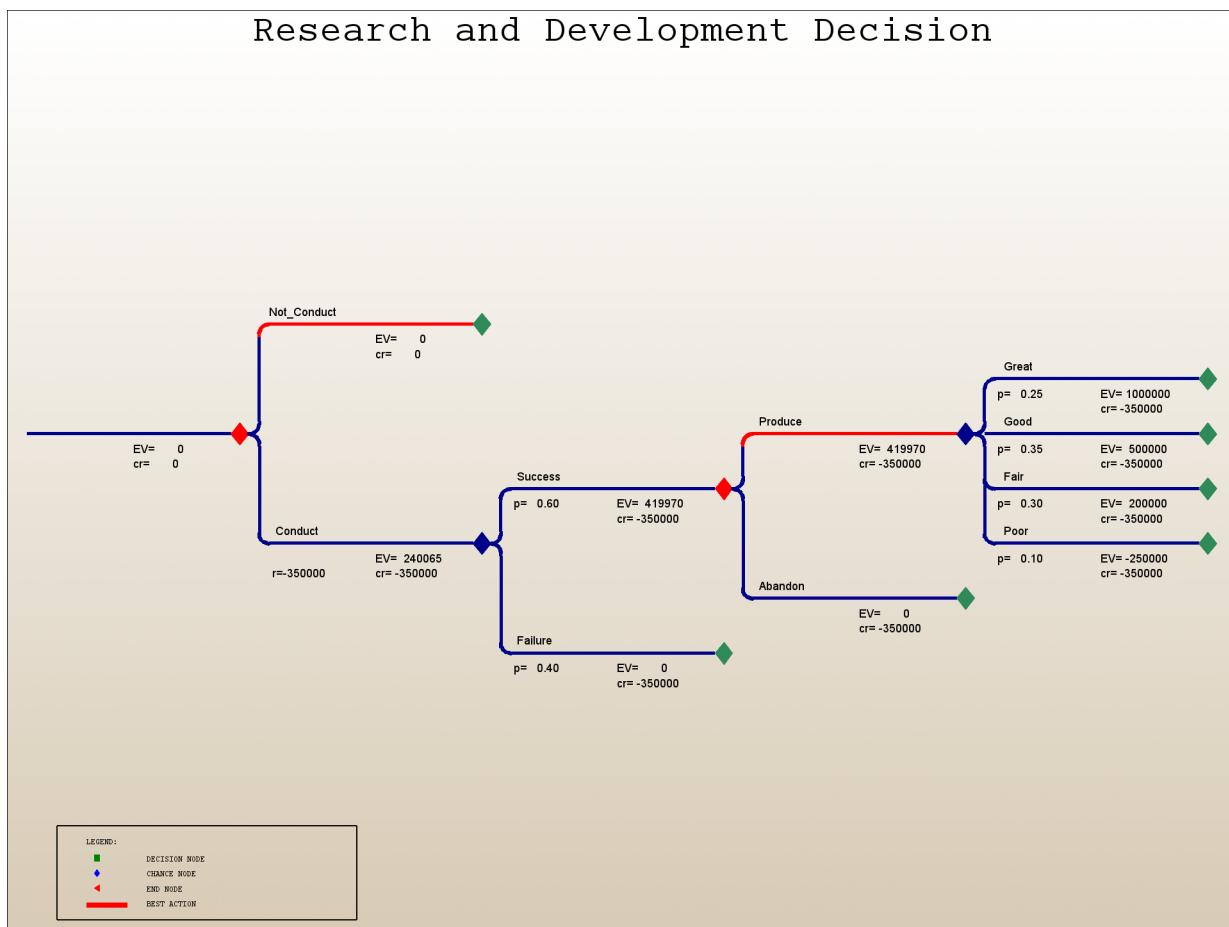**Figure 7.11** DTREE Style Template: Example

## Default Values

If the SAS system option GSTYLE is in effect (this is the default), then the default values of certain PROC DTREE options can depend on the current ODS style template. See the section “[Displaying the Decision Tree](#)” on page 427 for more information.

## Precision Errors

When PROC DTREE detects an error, it displays a message on the SAS log to call it to your attention. If the error is in a statement other than the **PROC DTREE** statement and the **QUIT** statement, and if the **ERRHANDLE=QUIT** option is not specified, the procedure ignores the erroneous statement and waits for you to enter another statement. This gives you a chance to correct the mistake you made and keep running. You can exit the procedure at any time by specifying the **QUIT** statement.

If the error is in an input data set, typically, you will have to edit the data set and then reinvoke PROC DTREE. In one case, however, you can use an option to correct the problem. You may receive an error message indicating that the sum of probabilities for a particular chance stage does not equal 1.0. If it is caused by roundoff errors in the summation, then you can reset the **TOLERANCE=** option to correct this error. For

example, suppose that your problem contains a chance stage that has three outcomes, 'Out1', 'Out2' and 'Out3', and each has probability 1/3. Suppose also that you input their probabilities in the PROBIN= data set as follows:

```
Out1      Out2      Out3      0.3333  0.3333  0.3333
```

Then, PROC DTREE detects the total probabilities for that stage as 0.9999, not equal to 1, and hence displays an error message. The following **RESET** statement fixes the error:

```
reset tolerance=0.00015;
```

Alternatively, you can specify the **AUTOSCALE** option to ask the procedure to rescale the probabilities whenever this situation occurs.

## Computer Resource Requirements

There is no inherent limit on the size of the decision tree model that can be evaluated and analyzed with the DTREE procedure. The numbers of stages and outcomes are constrained only by the amount of memory available. Naturally, there needs to be a sufficient amount of core memory available in order to invoke and initialize the SAS system. Furthermore, more memory is required to load the graphics sublibrary if the **GRAPHICS** option is specified. As far as possible, the procedure attempts to store all the data in core memory. However, if the problem is too large to fit in core memory, the procedure resorts to the use of utility data sets and swaps between core memory and utility data sets as necessary.

The storage requirement for the data area required by the procedure is proportional to the number of stages and outcomes as well as the number of nodes<sup>2</sup> in the decision tree model. The time required depends heavily on the number of nodes in the decision tree.

## Examples: DTREE Procedure

This section contains six examples that illustrate several features and applications of the DTREE procedure. The aim of this section is to show you how to use PROC DTREE to solve your decision problem and gain valuable insight into its structure.

**Example 7.1** and **Example 7.2** show two methods frequently used to spread the risk of a venture: buy insurance and enter a partnership. **Example 7.1** also illustrates the use of the VARIABLE statement to identify the variables in the input data sets. **Example 7.3** illustrates the use of the graphics options to produce a graphics quality decision tree diagram. **Example 7.4** illustrates the use of SYMBOL and GOPTIONS statements and the Annotate facility to control the appearance of the decision tree diagram. **Example 7.5** demonstrates an application of PROC DTREE for financial decision problems. It also illustrates a situation where redundant data are necessary to determine the value of information. In addition, it shows a case where the results from the **VPI** and **VPC** statements are misleading if they are used without care. **Example 7.6**

<sup>2</sup>The number of nodes depends on the number of stages and the number of outcomes for each stage.

shows an application in litigation, a sophisticated use of sensitivity analysis. It also shows you how to deal with the value of future money.

Finally, [Table 7.27](#) and [Table 7.28](#) list all the examples in this chapter, and the options and statements in the DTREE procedure that are illustrated by each example.

## Example 7.1: Oil Wildcatter's Problem with Insurance

Again consider the oil wildcatter's problem introduced in the section "Introductory Example" on page 383. Suppose that the wildcatter is concerned that the probability of a dry well may be as high as 0.5.

The wildcatter has learned that an insurance company is willing to offer him a policy that, with a premium of \$130,000, will redeem \$200,000 if the well is dry. He would like to include the alternative of buying insurance into his analysis. One way to do this is to include a stage for this decision in the model. The following DATA step reads this new decision problem into the **STAGEIN=** data set named Dtoils4. Notice the new stage named '**Insurance**', which represents the decision of whether or not to buy the insurance. Also notice that the cost of the insurance is represented as a negative reward of \$130,000.

```
/* -- create the STAGEIN= data set                                -- */
data Dtoils4;
format Stage $12. Stype $2. Outcome $14.
      Succ $12. Premium dollar12.0;
input Stage $12. Stype $4. Outcome $16. Succ $12.
      Premium dollar12.0;
datalines;
Drill      D   Drill           Insurance       .
.          .   Not_Drill        .
Insurance  D   Buy_Insurance   Cost         -$130,000
.          .   Do_Not_Buy     Cost
Cost       C   Low            Oil_Deposit  .
.          .   Fair           Oil_Deposit  .
.          .   High           Oil_Deposit  .
Oil_Deposit C   Dry           .
.          .   Wet            .
.          .   Soaking         .
;
```

Probabilities associated with the uncertain events are given in the **PROBIN=** data set named Dtoilp4. Except for the order of the variables in this data set, it is the same as the Dtoilp1 data set given in the section "Introductory Example" on page 383.

```
/* -- create the PROBIN= data set                                -- */
data Dtoilp4;
input (V1-V3) ($) P1-P3 ;
datalines;
Low        Fair        High        0.2      0.6      0.2
Dry        Wet         Soaking    0.5      0.3      0.2
;
```

The payoffs for this problem are now calculated to include the cost and value of the insurance. The following DATA step does this.

```

/* -- create PAYOFFS= data set                                -- */
data Dtoilu4;
input (Cost Deposit Drill Insuran) ($16.) ;
format Drill $9. Insuran $14. Payoff dollar12.0;

/* determine the cost for this scenario */
if      Cost='Low'  then Rcost=150000;
else if Cost='Fair' then Rcost=300000;
else               Rcost=500000;

/* determine the oil deposit and the corresponding */
/* net payoff for this scenario                  */
if      Deposit='Dry' then Return=0;
else if Deposit='Wet' then Return=700000;
else               Return=1200000;

/* calculate the net return for this scenario */
if      Drill='Not_Drill' then Payoff=0;
else               Payoff=Return-Rcost;

/* determine redeem received for this scenario */
if Insuran='Buy_Insurance' and Deposit='Dry' then
  Payoff=Payoff+200000;

/* drop unneeded variables */
drop Rcost Return;

datalines;
Low      Dry      Not_Drill   .
Low      Dry      Drill       Buy_Insurance
Low      Dry      Drill       Do_Not_Buy
Low      Wet      Not_Drill   .
Low      Wet      Drill       Buy_Insurance
Low      Wet      Drill       Do_Not_Buy
Low      Soaking  Not_Drill   .
Low      Soaking  Drill       Buy_Insurance
Low      Soaking  Drill       Do_Not_Buy
Fair     Dry      Not_Drill   .
Fair     Dry      Drill       Buy_Insurance
Fair     Dry      Drill       Do_Not_Buy
Fair     Wet      Not_Drill   .
Fair     Wet      Drill       Buy_Insurance
Fair     Wet      Drill       Do_Not_Buy
Fair     Soaking  Not_Drill   .
Fair     Soaking  Drill       Buy_Insurance
Fair     Soaking  Drill       Do_Not_Buy
High    Dry      Not_Drill   .
High    Dry      Drill       Buy_Insurance
High    Dry      Drill       Do_Not_Buy
High    Wet      Not_Drill   .
High    Wet      Drill       Buy_Insurance
High    Wet      Drill       Do_Not_Buy
High    Soaking  Not_Drill   .

```

High	Soaking	Drill	Buy_Insurance
High	Soaking	Drill	Do_Not_Buy
;			

The payoff table can be displayed with the following PROC PRINT statement:

```

/* -- print the payoff table           -- */
title "Oil Wildcatter's Problem";
title3 "The Payoffs";

proc print data=Dtoilu4;
run;

```

The table is shown in Output 7.1.1.

### Output 7.1.1 Payoffs of the Oil Wildcatter's Problem with an Insurance Option

#### Oil Wildcatter's Problem

#### The Payoffs

Obs	Cost	Deposit	Drill	Insuran	Payoff
1	Low	Dry	Not_Drill		\$0
2	Low	Dry	Drill	Buy_Insurance	\$50,000
3	Low	Dry	Drill	Do_Not_Buy	-\$150,000
4	Low	Wet	Not_Drill		\$0
5	Low	Wet	Drill	Buy_Insurance	\$550,000
6	Low	Wet	Drill	Do_Not_Buy	\$550,000
7	Low	Soaking	Not_Drill		\$0
8	Low	Soaking	Drill	Buy_Insurance	\$1,050,000
9	Low	Soaking	Drill	Do_Not_Buy	\$1,050,000
10	Fair	Dry	Not_Drill		\$0
11	Fair	Dry	Drill	Buy_Insurance	-\$100,000
12	Fair	Dry	Drill	Do_Not_Buy	-\$300,000
13	Fair	Wet	Not_Drill		\$0
14	Fair	Wet	Drill	Buy_Insurance	\$400,000
15	Fair	Wet	Drill	Do_Not_Buy	\$400,000
16	Fair	Soaking	Not_Drill		\$0
17	Fair	Soaking	Drill	Buy_Insurance	\$900,000
18	Fair	Soaking	Drill	Do_Not_Buy	\$900,000
19	High	Dry	Not_Drill		\$0
20	High	Dry	Drill	Buy_Insurance	-\$300,000
21	High	Dry	Drill	Do_Not_Buy	-\$500,000
22	High	Wet	Not_Drill		\$0
23	High	Wet	Drill	Buy_Insurance	\$200,000
24	High	Wet	Drill	Do_Not_Buy	\$200,000
25	High	Soaking	Not_Drill		\$0
26	High	Soaking	Drill	Buy_Insurance	\$700,000
27	High	Soaking	Drill	Do_Not_Buy	\$700,000

To find the optimal decision, call PROC DTREE with the following statements:

```

/* -- PROC DTREE statements                                -- */
title "Oil Wildcatter's Problem";

proc dtree stagein=Dtoils4
    probin=Dtoilp4
    payoffs=Dtoilu4
    nowarning
;

variables / stage=Stage type=Stype outcome=(Outcome)
    reward=(Premium) successor=(Succ)
    event=(V1 V2 V3) prob=(P1 P2 P3)
    state=(Cost Deposit Drill Insuran)
    payoff=(Payoff);

evaluate;
summary / target=Insurance;

```

The **VARIABLES** statement identifies the variables in the input data sets. The yield of the optimal decision is written to the SAS log as:

**NOTE: Present order of stages:**

Drill(D), Insurance(D), Cost(C), Oil\_Deposit(C),  
 $\_ENDST\_(E)$ .

**NOTE: The currently optimal decision yields 140000.**

The optimal decision summary produced by the SUMMARY statements are shown in [Output 7.1.2](#). The summary in [Output 7.1.2](#) shows that the insurance policy is worth  $\$240,000 - \$140,000 = \$100,000$ , but since it costs  $\$130,000$ , the wildcatter should reject such an insurance policy.

### Output 7.1.2 Summary of the Oil Wildcatter's Problem

#### Oil Wildcatter's Problem

##### The DTREE Procedure

##### Optimal Decision Summary

Order of Stages	
Stage	Type
Drill	Decision
Insurance	Decision
Cost	Chance
Oil_Deposit	Chance
$\_ENDST\_$	End

##### Decision Parameters

**Decision Criterion:** Maximize Expected Value (MAXEV)

**Optimal Decision Yields:** \$140,000

**Output 7.1.2** *continued*

Optimal Decision Policy			
Up to Stage Insurance			
Alternatives or Outcomes	Cumulative Reward	Evaluating Value	
Drill    Buy_Insurance	\$-130,000	\$240,000	
Drill    Do_Not_Buy	\$0	\$140,000*	

Now assume that the oil wildcatter is risk averse and has an exponential utility function with a risk tolerance of \$1,200,000. In order to evaluate his problem based on this decision criterion, the wildcatter reevaluates the problem with the following statements:

```
reset criterion=maxce rt=1200000;
summary / target=Insurance;
```

The output from PROC DTREE given in [Output 7.1.3](#) shows that the decision to purchase an insurance policy is favorable in the risk-averse environment. Note that an **EVALUATE** statement is not necessary before the **SUMMARY** statement. PROC DTREE evaluates the decision tree automatically when the decision criterion has been changed using the **RESET** statement.

**Output 7.1.3** Summary of the Oil Wildcatter's Problem with RT = 1,200,000**Oil Wildcatter's Problem****The DTREE Procedure****Optimal Decision Summary**

Order of Stages	
Stage	Type
Drill	Decision
Insurance	Decision
Cost	Chance
Oil_Deposit	Chance
<u>ENDST_</u>	End

**Decision Parameters**

**Decision Criterion:** Maximize Certain Equivalent Value (MAXCE)

**Risk Tolerance:** \$1,200,000

**Optimal Decision Yields:** \$45,728

**Optimal Decision Policy****Up to Stage Insurance**

Alternatives or Outcomes	Cumulative Reward	Evaluating Value	
Drill    Buy_Insurance	\$-130,000	\$175,728*	
Drill    Do_Not_Buy	\$0	\$44,499	

---

## Example 7.2: Oil Wildcatter's Problem in Risk-Averse Setting

Continuing with the oil wildcatter's problem, suppose that in addition to possibly buying insurance to spread the risk of the venture, the wildcatter is considering sharing the risk by selling a portion of this venture to other investors. Now, the decision he faces is whether to buy insurance or not and what percentage of the investment to divest. Again, assume that the wildcatter is risk averse with a risk tolerance of \$1,200,000. Notice that in the program that follows the 'Divestment' decision includes possibilities of no divestment to 100% divestment in 10% increments.

```
/* -- create the STAGEIN= data set                                -- */
data Dtoils4;
format _STNAME_ $12. _OUTCOM_ $15. _SUCCES_ $12. ;
input _STNAME_ $ _STTYPE_ $ _OUTCOM_ $
      _SUCCES_ $ ;
datalines;
Divestment    Decision      No_Divestment   Insurance
.             .             10%_Divestment  Insurance
.             .             20%_Divestment  Insurance
.             .             30%_Divestment  Insurance
.             .             40%_Divestment  Insurance
.             .             50%_Divestment  Insurance
.             .             60%_Divestment  Insurance
.             .             70%_Divestment  Insurance
.             .             80%_Divestment  Insurance
.             .             90%_Divestment  Insurance
.             .             100%_Divestment .
Insurance     Decision      Buy_Insurance   Cost
.             .             Do_Not_Buy     Cost
Cost          Chance       Low            Oil_Deposit
.             .             Fair           Oil_Deposit
.             .             High          Oil_Deposit
Oil_Deposit   Chance       Dry            .
.             .             Wet            .
.             .             Soaking        .
;
;
```

The probabilities associated with the uncertain events are given in the PROBIN= data set named Dtoilp4. Except for the order of the variables in this data set, it is the same as the Dtoilp1 data set used in the section “Introductory Example” on page 383.

```
/* -- create the PROBIN= data set                                -- */
data Dtoilp4;
input _EVENT1 $ _PROB1  _EVENT3 $ _PROB3 ;
datalines;
Low          0.2      Dry          0.5
Fair         0.6      Wet          0.3
High         0.2      Soaking      0.2
;

/* -- create the PAYOFFS= data set                                -- */
data Dtoilu4(drop=i j k l);
length _STATE1-_STATE4 $16. ;
```

```

format _VALUE_ dollar12.0;

/* define and initialize arrays */
array DIVEST{11} $16. _TEMPORARY_ ('No_Divestment',
                                    '10%_Divestment',
                                    '20%_Divestment',
                                    '30%_Divestment',
                                    '40%_Divestment',
                                    '50%_Divestment',
                                    '60%_Divestment',
                                    '70%_Divestment',
                                    '80%_Divestment',
                                    '90%_Divestment',
                                    '100%_Divestment' );
array INSUR{3} $16.      _TEMPORARY_ ('Do_Not_Buy',
                                         'Buy_Insurance',
                                         ' ' );
array COST{4} $        _TEMPORARY_ ('Low',
                                    'Fair',
                                    'High',
                                    ' ' );
array DEPOSIT{4} $     _TEMPORARY_ ('Dry',
                                    'Wet',
                                    'Soaking',
                                    ' ' );

do i=1 to 10;           /* loop for each divestment */
  _STATE1=DIVEST{i};

/*
 * determine the percentage of ownership retained
 * for this scenario
 */
PCT=1.0-((i-1)*0.1);

do j=1 to 2;           /* loop for insurance decision */
  _STATE2=INSUR{j};

/*
 * determine the premium need to pay for this
 * scenario
 */
if _STATE2='Buy_Insurance' then PREMIUM=130000;
else                           PREMIUM=0;

do k=1 to 3;           /* loop for each well cost */
  _STATE3=COST{k};

/* determine the cost for this scenario */
if      _STATE3='Low' then _COST_=150000;
else if _STATE3='Fair' then _COST_=300000;
else                           _COST_=500000;

do l=1 to 3; /* loop for each deposit type */

```

```

_STATE4=DEPOSIT{1};

/*
 * determine the oil deposit and the
 * corresponding net payoff for this scenario
 */
if      _STATE4='Dry' then _PAYOFF_=0;
else if _STATE4='Wet' then _PAYOFF_=700000;
else                      _PAYOFF_=1200000;

/* determine redeem received for this scenario */
if _STATE2='Buy_Insurance' and _STATE4='Dry' then
    REDEEM=200000;
else REDEEM=0;

/* calculate the net return for this scenario */
_VALUE_=(_PAYOFF_-_COST_-PREMIUM+REDEEM)*PCT;

/* drop unneeded variables */
drop _COST_ _PAYOFF_ PREMIUM REDEEM PCT;

/* output this record */
output;
end;
end;
end;
end;

/* output an observation for the scenario 100%_Divestment */
_STATE1=DIVEST{11};
_STATE2=INSUR{3};
_STATE3=COST{4};
_STATE4=DEPOSIT{4};
_VALUE_=0;
output;

run;

```

The Dtoilu4 data set for this problem, which contains 181 observations and 5 variables, is displayed in Output 7.2.1.

**Output 7.2.1** Payoffs of the Oil Wildcatter's Problem with Risk Sharing**Oil Wildcatter's Problem****The Payoffs**

<u>Obs</u>	<u>_STATE1</u>	<u>_STATE2</u>	<u>_STATE3</u>	<u>_STATE4</u>	<u>_VALUE_</u>
1	No_Divestment	Do_Not_Buy	Low	Dry	\$-150,000
2	No_Divestment	Do_Not_Buy	Low	Wet	\$550,000
3	No_Divestment	Do_Not_Buy	Low	Soaking	\$1,050,000
4	No_Divestment	Do_Not_Buy	Fair	Dry	\$-300,000
5	No_Divestment	Do_Not_Buy	Fair	Wet	\$400,000
6	No_Divestment	Do_Not_Buy	Fair	Soaking	\$900,000
7	No_Divestment	Do_Not_Buy	High	Dry	\$-500,000
8	No_Divestment	Do_Not_Buy	High	Wet	\$200,000
9	No_Divestment	Do_Not_Buy	High	Soaking	\$700,000
10	No_Divestment	Buy_Insurance	Low	Dry	\$-80,000
11	No_Divestment	Buy_Insurance	Low	Wet	\$420,000
12	No_Divestment	Buy_Insurance	Low	Soaking	\$920,000
13	No_Divestment	Buy_Insurance	Fair	Dry	\$-230,000
14	No_Divestment	Buy_Insurance	Fair	Wet	\$270,000
15	No_Divestment	Buy_Insurance	Fair	Soaking	\$770,000
16	No_Divestment	Buy_Insurance	High	Dry	\$-430,000
17	No_Divestment	Buy_Insurance	High	Wet	\$70,000
18	No_Divestment	Buy_Insurance	High	Soaking	\$570,000
19	10%_Divestment	Do_Not_Buy	Low	Dry	\$-135,000
20	10%_Divestment	Do_Not_Buy	Low	Wet	\$495,000
21	10%_Divestment	Do_Not_Buy	Low	Soaking	\$945,000
22	10%_Divestment	Do_Not_Buy	Fair	Dry	\$-270,000
23	10%_Divestment	Do_Not_Buy	Fair	Wet	\$360,000
24	10%_Divestment	Do_Not_Buy	Fair	Soaking	\$810,000
25	10%_Divestment	Do_Not_Buy	High	Dry	\$-450,000
26	10%_Divestment	Do_Not_Buy	High	Wet	\$180,000
27	10%_Divestment	Do_Not_Buy	High	Soaking	\$630,000
28	10%_Divestment	Buy_Insurance	Low	Dry	\$-72,000
29	10%_Divestment	Buy_Insurance	Low	Wet	\$378,000
30	10%_Divestment	Buy_Insurance	Low	Soaking	\$828,000
31	10%_Divestment	Buy_Insurance	Fair	Dry	\$-207,000
32	10%_Divestment	Buy_Insurance	Fair	Wet	\$243,000
33	10%_Divestment	Buy_Insurance	Fair	Soaking	\$693,000
34	10%_Divestment	Buy_Insurance	High	Dry	\$-387,000
35	10%_Divestment	Buy_Insurance	High	Wet	\$63,000
36	10%_Divestment	Buy_Insurance	High	Soaking	\$513,000
37	20%_Divestment	Do_Not_Buy	Low	Dry	\$-120,000
38	20%_Divestment	Do_Not_Buy	Low	Wet	\$440,000
39	20%_Divestment	Do_Not_Buy	Low	Soaking	\$840,000
40	20%_Divestment	Do_Not_Buy	Fair	Dry	\$-240,000
41	20%_Divestment	Do_Not_Buy	Fair	Wet	\$320,000
42	20%_Divestment	Do_Not_Buy	Fair	Soaking	\$720,000
43	20%_Divestment	Do_Not_Buy	High	Dry	\$-400,000
44	20%_Divestment	Do_Not_Buy	High	Wet	\$160,000
45	20%_Divestment	Do_Not_Buy	High	Soaking	\$560,000

**Output 7.2.1** *continued***Oil Wildcatter's Problem****The Payoffs**

<u>Obs</u>	<u>_STATE1</u>	<u>_STATE2</u>	<u>_STATE3</u>	<u>_STATE4</u>	<u>_VALUE_</u>
46	20%_Divestment	Buy_Insurance	Low	Dry	\$-64,000
47	20%_Divestment	Buy_Insurance	Low	Wet	\$336,000
48	20%_Divestment	Buy_Insurance	Low	Soaking	\$736,000
49	20%_Divestment	Buy_Insurance	Fair	Dry	\$-184,000
50	20%_Divestment	Buy_Insurance	Fair	Wet	\$216,000
51	20%_Divestment	Buy_Insurance	Fair	Soaking	\$616,000
52	20%_Divestment	Buy_Insurance	High	Dry	\$-344,000
53	20%_Divestment	Buy_Insurance	High	Wet	\$56,000
54	20%_Divestment	Buy_Insurance	High	Soaking	\$456,000
55	30%_Divestment	Do_Not_Buy	Low	Dry	\$-105,000
56	30%_Divestment	Do_Not_Buy	Low	Wet	\$385,000
57	30%_Divestment	Do_Not_Buy	Low	Soaking	\$735,000
58	30%_Divestment	Do_Not_Buy	Fair	Dry	\$-210,000
59	30%_Divestment	Do_Not_Buy	Fair	Wet	\$280,000
60	30%_Divestment	Do_Not_Buy	Fair	Soaking	\$630,000
61	30%_Divestment	Do_Not_Buy	High	Dry	\$-350,000
62	30%_Divestment	Do_Not_Buy	High	Wet	\$140,000
63	30%_Divestment	Do_Not_Buy	High	Soaking	\$490,000
64	30%_Divestment	Buy_Insurance	Low	Dry	\$-56,000
65	30%_Divestment	Buy_Insurance	Low	Wet	\$294,000
66	30%_Divestment	Buy_Insurance	Low	Soaking	\$644,000
67	30%_Divestment	Buy_Insurance	Fair	Dry	\$-161,000
68	30%_Divestment	Buy_Insurance	Fair	Wet	\$189,000
69	30%_Divestment	Buy_Insurance	Fair	Soaking	\$539,000
70	30%_Divestment	Buy_Insurance	High	Dry	\$-301,000
71	30%_Divestment	Buy_Insurance	High	Wet	\$49,000
72	30%_Divestment	Buy_Insurance	High	Soaking	\$399,000
73	40%_Divestment	Do_Not_Buy	Low	Dry	\$-90,000
74	40%_Divestment	Do_Not_Buy	Low	Wet	\$330,000
75	40%_Divestment	Do_Not_Buy	Low	Soaking	\$630,000
76	40%_Divestment	Do_Not_Buy	Fair	Dry	\$-180,000
77	40%_Divestment	Do_Not_Buy	Fair	Wet	\$240,000
78	40%_Divestment	Do_Not_Buy	Fair	Soaking	\$540,000
79	40%_Divestment	Do_Not_Buy	High	Dry	\$-300,000
80	40%_Divestment	Do_Not_Buy	High	Wet	\$120,000
81	40%_Divestment	Do_Not_Buy	High	Soaking	\$420,000
82	40%_Divestment	Buy_Insurance	Low	Dry	\$-48,000
83	40%_Divestment	Buy_Insurance	Low	Wet	\$252,000
84	40%_Divestment	Buy_Insurance	Low	Soaking	\$552,000
85	40%_Divestment	Buy_Insurance	Fair	Dry	\$-138,000
86	40%_Divestment	Buy_Insurance	Fair	Wet	\$162,000
87	40%_Divestment	Buy_Insurance	Fair	Soaking	\$462,000
88	40%_Divestment	Buy_Insurance	High	Dry	\$-258,000
89	40%_Divestment	Buy_Insurance	High	Wet	\$42,000
90	40%_Divestment	Buy_Insurance	High	Soaking	\$342,000

**Output 7.2.1** *continued***Oil Wildcatter's Problem****The Payoffs**

<u>Obs</u>	<u>_STATE1</u>	<u>_STATE2</u>	<u>_STATE3</u>	<u>_STATE4</u>	<u>_VALUE_</u>
91	50%_Divestment	Do_Not_Buy	Low	Dry	\$-75,000
92	50%_Divestment	Do_Not_Buy	Low	Wet	\$275,000
93	50%_Divestment	Do_Not_Buy	Low	Soaking	\$525,000
94	50%_Divestment	Do_Not_Buy	Fair	Dry	\$-150,000
95	50%_Divestment	Do_Not_Buy	Fair	Wet	\$200,000
96	50%_Divestment	Do_Not_Buy	Fair	Soaking	\$450,000
97	50%_Divestment	Do_Not_Buy	High	Dry	\$-250,000
98	50%_Divestment	Do_Not_Buy	High	Wet	\$100,000
99	50%_Divestment	Do_Not_Buy	High	Soaking	\$350,000
100	50%_Divestment	Buy_Insurance	Low	Dry	\$-40,000
101	50%_Divestment	Buy_Insurance	Low	Wet	\$210,000
102	50%_Divestment	Buy_Insurance	Low	Soaking	\$460,000
103	50%_Divestment	Buy_Insurance	Fair	Dry	\$-115,000
104	50%_Divestment	Buy_Insurance	Fair	Wet	\$135,000
105	50%_Divestment	Buy_Insurance	Fair	Soaking	\$385,000
106	50%_Divestment	Buy_Insurance	High	Dry	\$-215,000
107	50%_Divestment	Buy_Insurance	High	Wet	\$35,000
108	50%_Divestment	Buy_Insurance	High	Soaking	\$285,000
109	60%_Divestment	Do_Not_Buy	Low	Dry	\$-60,000
110	60%_Divestment	Do_Not_Buy	Low	Wet	\$220,000
111	60%_Divestment	Do_Not_Buy	Low	Soaking	\$420,000
112	60%_Divestment	Do_Not_Buy	Fair	Dry	\$-120,000
113	60%_Divestment	Do_Not_Buy	Fair	Wet	\$160,000
114	60%_Divestment	Do_Not_Buy	Fair	Soaking	\$360,000
115	60%_Divestment	Do_Not_Buy	High	Dry	\$-200,000
116	60%_Divestment	Do_Not_Buy	High	Wet	\$80,000
117	60%_Divestment	Do_Not_Buy	High	Soaking	\$280,000
118	60%_Divestment	Buy_Insurance	Low	Dry	\$-32,000
119	60%_Divestment	Buy_Insurance	Low	Wet	\$168,000
120	60%_Divestment	Buy_Insurance	Low	Soaking	\$368,000
121	60%_Divestment	Buy_Insurance	Fair	Dry	\$-92,000
122	60%_Divestment	Buy_Insurance	Fair	Wet	\$108,000
123	60%_Divestment	Buy_Insurance	Fair	Soaking	\$308,000
124	60%_Divestment	Buy_Insurance	High	Dry	\$-172,000
125	60%_Divestment	Buy_Insurance	High	Wet	\$28,000
126	60%_Divestment	Buy_Insurance	High	Soaking	\$228,000
127	70%_Divestment	Do_Not_Buy	Low	Dry	\$-45,000
128	70%_Divestment	Do_Not_Buy	Low	Wet	\$165,000
129	70%_Divestment	Do_Not_Buy	Low	Soaking	\$315,000
130	70%_Divestment	Do_Not_Buy	Fair	Dry	\$-90,000
131	70%_Divestment	Do_Not_Buy	Fair	Wet	\$120,000
132	70%_Divestment	Do_Not_Buy	Fair	Soaking	\$270,000
133	70%_Divestment	Do_Not_Buy	High	Dry	\$-150,000
134	70%_Divestment	Do_Not_Buy	High	Wet	\$60,000
135	70%_Divestment	Do_Not_Buy	High	Soaking	\$210,000

**Output 7.2.1** *continued***Oil Wildcatter's Problem****The Payoffs**

<u>Obs</u>	<u>_STATE1</u>	<u>_STATE2</u>	<u>_STATE3</u>	<u>_STATE4</u>	<u>_VALUE_</u>
136	70%_Divestment	Buy_Insurance	Low	Dry	\$-24,000
137	70%_Divestment	Buy_Insurance	Low	Wet	\$126,000
138	70%_Divestment	Buy_Insurance	Low	Soaking	\$276,000
139	70%_Divestment	Buy_Insurance	Fair	Dry	\$-69,000
140	70%_Divestment	Buy_Insurance	Fair	Wet	\$81,000
141	70%_Divestment	Buy_Insurance	Fair	Soaking	\$231,000
142	70%_Divestment	Buy_Insurance	High	Dry	\$-129,000
143	70%_Divestment	Buy_Insurance	High	Wet	\$21,000
144	70%_Divestment	Buy_Insurance	High	Soaking	\$171,000
145	80%_Divestment	Do_Not_Buy	Low	Dry	\$-30,000
146	80%_Divestment	Do_Not_Buy	Low	Wet	\$110,000
147	80%_Divestment	Do_Not_Buy	Low	Soaking	\$210,000
148	80%_Divestment	Do_Not_Buy	Fair	Dry	\$-60,000
149	80%_Divestment	Do_Not_Buy	Fair	Wet	\$80,000
150	80%_Divestment	Do_Not_Buy	Fair	Soaking	\$180,000
151	80%_Divestment	Do_Not_Buy	High	Dry	\$-100,000
152	80%_Divestment	Do_Not_Buy	High	Wet	\$40,000
153	80%_Divestment	Do_Not_Buy	High	Soaking	\$140,000
154	80%_Divestment	Buy_Insurance	Low	Dry	\$-16,000
155	80%_Divestment	Buy_Insurance	Low	Wet	\$84,000
156	80%_Divestment	Buy_Insurance	Low	Soaking	\$184,000
157	80%_Divestment	Buy_Insurance	Fair	Dry	\$-46,000
158	80%_Divestment	Buy_Insurance	Fair	Wet	\$54,000
159	80%_Divestment	Buy_Insurance	Fair	Soaking	\$154,000
160	80%_Divestment	Buy_Insurance	High	Dry	\$-86,000
161	80%_Divestment	Buy_Insurance	High	Wet	\$14,000
162	80%_Divestment	Buy_Insurance	High	Soaking	\$114,000
163	90%_Divestment	Do_Not_Buy	Low	Dry	\$-15,000
164	90%_Divestment	Do_Not_Buy	Low	Wet	\$55,000
165	90%_Divestment	Do_Not_Buy	Low	Soaking	\$105,000
166	90%_Divestment	Do_Not_Buy	Fair	Dry	\$-30,000
167	90%_Divestment	Do_Not_Buy	Fair	Wet	\$40,000
168	90%_Divestment	Do_Not_Buy	Fair	Soaking	\$90,000
169	90%_Divestment	Do_Not_Buy	High	Dry	\$-50,000
170	90%_Divestment	Do_Not_Buy	High	Wet	\$20,000
171	90%_Divestment	Do_Not_Buy	High	Soaking	\$70,000
172	90%_Divestment	Buy_Insurance	Low	Dry	\$-8,000
173	90%_Divestment	Buy_Insurance	Low	Wet	\$42,000
174	90%_Divestment	Buy_Insurance	Low	Soaking	\$92,000
175	90%_Divestment	Buy_Insurance	Fair	Dry	\$-23,000
176	90%_Divestment	Buy_Insurance	Fair	Wet	\$27,000
177	90%_Divestment	Buy_Insurance	Fair	Soaking	\$77,000
178	90%_Divestment	Buy_Insurance	High	Dry	\$-43,000
179	90%_Divestment	Buy_Insurance	High	Wet	\$7,000

**Output 7.2.1** *continued***Oil Wildcatter's Problem****The Payoffs**

<u>Obs</u>	<u>_STATE1</u>	<u>_STATE2</u>	<u>_STATE3</u>	<u>_STATE4</u>	<u>_VALUE_</u>
180	90%_Divestment	Buy_Insurance	High	Soaking	\$57,000
181	100%_Divestment				\$0

The optimal decisions for this problem can be identified by invoking PROC DTREE and using the **SUMMARY** statement as follows:

```
title "Oil Wildcatter's Problem";
proc dtree stagein=Dtoils4
    probin=Dtoilp4
    payoffs=Dtoilu4
    criterion=maxce rt=1200000
    nowarning;
evaluate;
summary / target=Divestment;
summary / target=Insurance;
quit;
```

The optimal decision summaries in [Output 7.2.2](#) and [Output 7.2.3](#) show the optimal strategy for the wildcatter.

- The wildcatter should sell 30% of his investment to other companies and reject the insurance policy offered to him.
- The insurance policy should be accepted only if the decision to not divest is made.
- If the decision to buy the insurance policy is made, then it is optimal to divest 10% of the venture.

**Output 7.2.2** Summary of the Oil Wildcatter's Problem for DIVESTMENT**Oil Wildcatter's Problem****The DTREE Procedure****Optimal Decision Summary**

Order of Stages	
Stage	Type
Divestment	Decision
Insurance	Decision
Cost	Chance
Oil_Deposit	Chance
<u>ENDST_</u>	End

**Decision Parameters**

**Decision Criterion:** Maximize Certain Equivalent Value (MAXCE)

**Risk Tolerance:** \$1,200,000

**Optimal Decision Yields:** \$50,104

**Output 7.2.2** *continued*

Optimal Decision Policy Up to Stage Divestment		
Alternatives or Outcomes	Cumulative Reward	Evaluating Value
No_Divestment	\$45,728	
10%_Divestment	\$48,021	
20%_Divestment	\$49,907	
30%_Divestment	\$50,104*	
40%_Divestment	\$48,558	
50%_Divestment	\$45,219	
60%_Divestment	\$40,036	
70%_Divestment	\$32,965	
80%_Divestment	\$23,961	
90%_Divestment	\$12,985	
100%_Divestment	\$0	

**Output 7.2.3** Summary of the Oil Wildcatter's Problem for INSURANCE**Oil Wildcatter's Problem****The DTREE Procedure****Optimal Decision Summary**

Order of Stages	
Stage	Type
Divestment	Decision
Insurance	Decision
Cost	Chance
Oil_Deposit	Chance
<u>ENDST_</u>	End

**Decision Parameters****Decision Criterion:** Maximize Certain Equivalent Value (MAXCE)**Risk Tolerance:** \$1,200,000**Optimal Decision Yields:** \$50,104

**Output 7.2.3** *continued*

Optimal Decision Policy Up to Stage Insurance		Cumulative Reward	Evaluating Value
Alternatives or Outcomes			
No_Divestment	Buy_Insurance	\$45,728*	
No_Divestment	Do_Not_Buy	\$44,499	
10%_Divestment	Buy_Insurance	\$46,552	
10%_Divestment	Do_Not_Buy	\$48,021*	
20%_Divestment	Buy_Insurance	\$46,257	
20%_Divestment	Do_Not_Buy	\$49,907*	
30%_Divestment	Buy_Insurance	\$44,812	
30%_Divestment	Do_Not_Buy	\$50,104*	
40%_Divestment	Buy_Insurance	\$42,186	
40%_Divestment	Do_Not_Buy	\$48,558*	
50%_Divestment	Buy_Insurance	\$38,350	
50%_Divestment	Do_Not_Buy	\$45,219*	
60%_Divestment	Buy_Insurance	\$33,273	
60%_Divestment	Do_Not_Buy	\$40,036*	
70%_Divestment	Buy_Insurance	\$26,927	
70%_Divestment	Do_Not_Buy	\$32,965*	
80%_Divestment	Buy_Insurance	\$19,284	
80%_Divestment	Do_Not_Buy	\$23,961*	
90%_Divestment	Buy_Insurance	\$10,317	
90%_Divestment	Do_Not_Buy	\$12,985*	

This information can be illustrated graphically using the GPLOT procedure. **Output 7.2.4**, produced by the PROC GPLOT statements shown in the following code, provides a clear picture of the effects of the divestment possibilities and the insurance options.

```
/*  create a data set for the return corresponds to each */
/*  divestment possibilities and the insurance options  */
data Data2g;
  input INSURE DIVEST VALUE;
  datalines;
    1      0   45728
    0      0   44499
    1     10   46552
    0     10   48021
    1     20   46257
    0     20   49907
    1     30   44812
    0     30   50104
    1     40   42186
    0     40   48558
    1     50   38350
    0     50   45219
    1     60   33273
    0     60   40036
    1     70   26927
    0     70   32965
```

```

1      80    19284
0      80    23961
1      90    10317
0      90    12985
1     100      0
0     100      0
;

/* -- define a format for INSURE variable          -- */
proc format;
  value sample 0='Do_Not_Buy' 1='Buy_Insurance';
run;

/* -- define title                                -- */
title h=3 "Oil Wildcatter's Problem";

/* define legend                                  -- */
legend1 frame cframe=white label=none
  cborder=black position=center ;

/* define symbol characteristics of the data points   */
/* and the interpolation line for returns vs divestment */
/* when INSURE=0                                     */
symbol1 c=cyan i=join v=dot l=1 h=1;

/* define symbol characteristics of the data points   */
/* and the interpolation line for returns vs divestment */
/* when INSURE=1                                     */
symbol2 c=green i=join v=square l=2 h=1;

/* -- define axis characteristics                  -- */
axis1 minor=none label=('Divestment (in percentage)');
axis2 minor=none label=(angle=90 rotate=0 'Certainty Equivalent');


/* set graphics options                           */
goptions htext=1.5;

/* plot VALUE vs DIVEST using INSURE as third variable */
proc gplot data=Data2g ;
  plot VALUE*DIVEST=INSURE / haxis=axis1
    vaxis=axis2
    legend=legend1
    name="dt2"
    frame
    cframe=white ;
  format INSURE SAMPLE.;
run;

quit;

```

Note that the data input into the Data2g data set is obtained from the optimal decision summary as in Output 7.2.3. The value 1 of the INSURE variable represents the alternative 'Buy\_Insurance' and the value 0 represents the alternative 'Do\_Not\_Buy'.

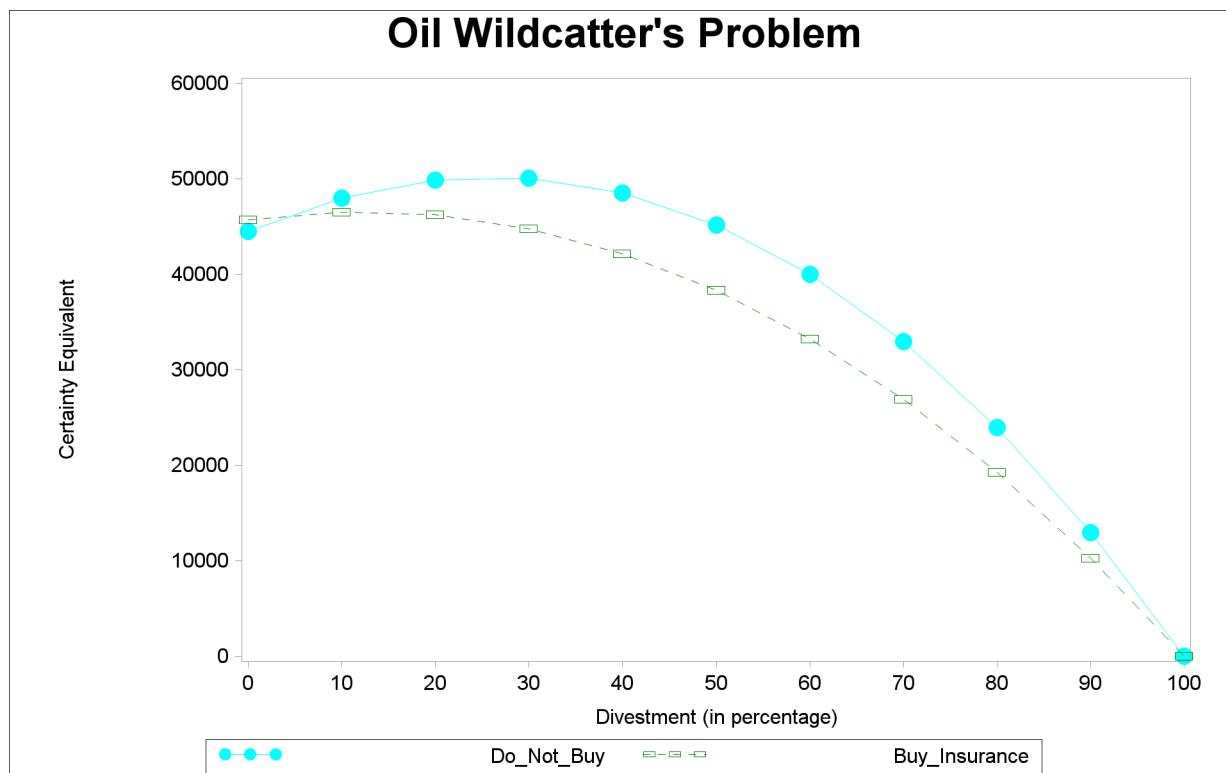**Output 7.2.4** Returns of the Oil Wildcatter's Problem**Example 7.3: Contract Bidding Problem**

This example illustrates the use of several of the graphics options for producing graphics quality decision tree diagrams.

The production manager of a manufacturing company is planning to bid on a project to manufacture a new type of machine. He has the choice of bidding low or high. The evaluation of the bid will more likely be favorable if the bidder has built a prototype of the machine and includes it with the bid. However, he is uncertain about the cost of building the prototype. His technical staff has provided him a probability distribution on the cost of the prototype.

**Table 7.20** Probability on the Cost of Building Prototype

Outcome	Cost	Probability
Expensive	\$4,500	0.4
Moderate	\$2,500	0.5
Inexpensive	\$1,000	0.1

There is also uncertainty in whether he will win the contract or not. He has estimated the probability distribution of winning the contract as shown in Table 7.21.

**Table 7.21** Probability of Winning the Contract

<b>Givens</b>	<b>Events</b>	
	Win the Contract	Lose the Contract
Build Prototype	High Bid	0.4
Build Prototype	Low Bid	0.8
No Prototype	High Bid	0.2
No Prototype	Low Bid	0.7

In addition, the payoffs of this bidding venture are affected by the cost of building the prototype. **Table 7.22** shows his payoffs. The first row of the table shows the payoff is 0 if he loses the contract, regardless of whether or not he builds the prototype and whether he bids low or high. The remainder of the entries in the table give the payoff under the various scenarios.

**Table 7.22** Payoffs of the Contract Bidding Decision

<b>States</b>		<b>Actions</b>	
Result	Cost	Bid low	Bid high
Lose the Contract		0	0
Win the Contract		\$35,000	\$75,000
Win the Contract	Expensive	\$25,000	\$65,000
Win the Contract	Moderate	\$35,000	\$75,000
Win the Contract	Inexpensive	\$45,000	\$85,000

The production manager must decide whether to build the prototype and how to bid. He uses PROC DTREE to help him to make these decisions. The structure of the model is stored in the **STAGEIN=** data set named Stage3. There are two decision stages, '**Choose**' and '**Bid**', and two chance stages, '**Cost\_Prototype**' and '**Contract**'. The '**Choose**' stage represents the decision whether or not to build a prototype. The chance stage '**Cost\_Prototype**' represents the uncertain cost for building a prototype. It can be '**Expensive**', which costs \$4,500, or '**Moderate**', which costs \$2,500, or '**Inexpensive**', which costs \$1,000. The '**Bid**' stage represents the decision whether to bid high or bid low. The last stage, '**Contract**', represents the result, either win the contract or lose the contract.

```
/* -- create the STAGEIN= data set                                */
data Stage3;
format _STNAME_ $14. _STTYPE_ $2. _OUTCOM_ $15.
      _SUCCES_ $14. _REWARD_ dollar8.0 ;
input _STNAME_ $16. _STTYPE_ $4. _OUTCOM_ $16.
      _SUCCES_ $16. _REWARD_ dollar8.0 ;
datalines;
Choose      D   Build_Prototype Cost_Prototype   .
.          .   No_Prototype   Bid           .
Cost_Prototype C   Expensive     Bid           -$4,500
.          .   Moderate      Bid           -$2,500
.          .   Inexpensive   Bid           -$1,000
Bid        D   High_Bid     Contract       .
.          .   Low_Bid      Contract       .
Contract    C   Win_Contract  .             .
.          .   Lose_Contract .             .
;
```

The **PROBIN=** data set, named Prob3, contains the probability information as in Table 7.20 and Table 7.21.

```
/* -- create the PROBIN= data set                                -- */
data Prob3;
format _GIVEN1_ $15. _GIVEN2_ $15. _EVENT_ $14. ;
input (_GIVEN1_ _GIVEN2_ _EVENT_) ($) _PROB_;
datalines;
. . Expensive      0.4
. . Moderate       0.5
. . Inexpensive    0.1
Build_Prototype High_Bid   Win_Contract 0.4
Build_Prototype High_Bid   Lose_Contract 0.6
Build_Prototype Low_Bid    Win_Contract 0.8
Build_Prototype Low_Bid    Lose_Contract 0.2
No_Prototype     High_Bid   Win_Contract 0.2
No_Prototype     High_Bid   Lose_Contract 0.8
No_Prototype     Low_Bid    Win_Contract 0.7
No_Prototype     Low_Bid    Lose_Contract 0.3
;
```

The **PAYOFFS=** data set named Payoff3 contains the payoff information as in Table 7.22. Notice that the payoff to outcome '**Lose\_Contract**' is not in the data set Payoff3. Since PROC DTREE assigns the default value 0 to all scenarios that are not in the **PAYOFFS=** data set, it is not necessary to include it.

```
/* -- create the PAYOFFS= data set                                -- */
data Payoff3;
format _STATE1_ _STATE2_ $12.;
input (_STATE1_ _STATE2_ _ACTION_) ($16.)
      _VALUE_ dollar8.0;
datalines;
Win_Contract . Low_Bid      $35,000
Win_Contract . High_Bid     $75,000
Win_Contract Expensive     Low_Bid      $25,000
Win_Contract Expensive     High_Bid     $65,000
Win_Contract Moderate      Low_Bid     $35,000
Win_Contract Moderate      High_Bid     $75,000
Win_Contract Inexpensive   Low_Bid     $45,000
Win_Contract Inexpensive   High_Bid    $85,000
;
```

The solution, as in Output 7.3.1, is displayed on a graphics device with the following code. Notice that the title is specified before invoking PROC DTREE. The **GRAPHICS** option is given on the **PROC DTREE** statement. Specifying the **COMPRESS** option in the **TREEPLOT** statement causes the decision tree diagram to be drawn completely on one page. The vertical distance between two successive end nodes is 1 character cell (**ybetween=1 cell**). All text, except that in the first title line, is drawn with the font specified by the **FTEXT=** option. The height for all nodes is the number of character cells specified by the **HSYMBOL=** option. The thickness for all links in the diagram, except those that represent optimal decisions, is specified by the **LWIDTH=** option. The thickness of the links that represent optimal decisions is specified by the **LWIDTHB=** option, and the type of those links is 3 (**lstyleb=3**), the dash line. Colors for the text, links and nodes to be used for nodes are not specified and hence defaults are used.


```

goptions ctext=black;
goptions hsize=10in htext=3.0;
/* -- define title                                -- */
title1 h=2 "Contract Bidding Example" ;

/* -- PROC DTREE statements                      -- */
proc dtree stagein=Stage3 probin=Prob3 payoffs=Payoff3
    graphics
    nowarning
    ;
evaluate;
treeplot / name="dt3" compress ybetween=1 cell
            hsymbol=6
            lstyleb=3 lwidth=1 lwidthb=1;
quit;

```

### Output 7.3.1 Decision Tree for the Contract Bidding Problem

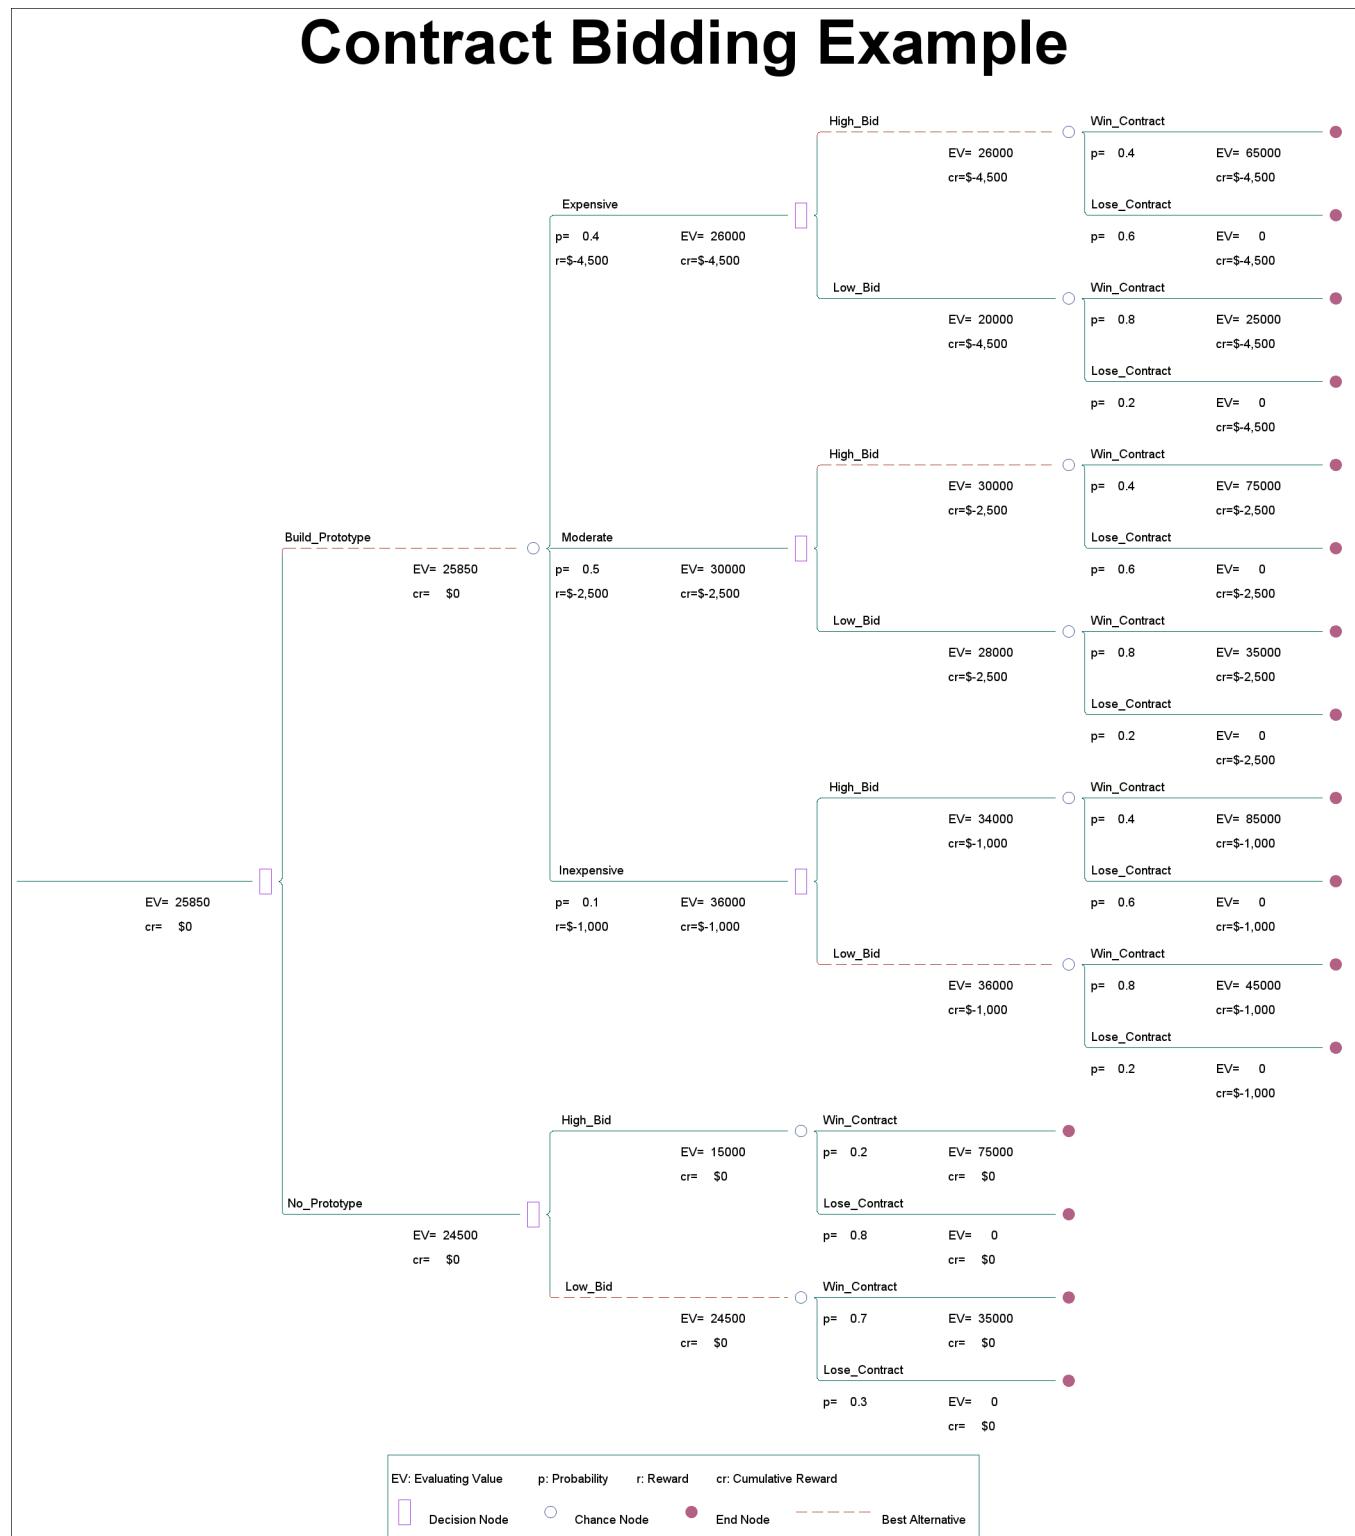

With the information on this decision tree, the production manager can select the optimal bidding strategy:

- He should build a prototype to accompany the bid and always bid high unless the cost for building the prototype is as low as \$1,000. This optimal strategy yields an expected return of \$25,850.
- If no prototype is built, the preferred decision is to make a low bid. In this case the expected return is \$24,500.

## Example 7.4: Research and Development Decision Problem

This example illustrates the use of the SYMBOL and GOPTIONS statements for controlling the appearance of the decision tree diagram. It also uses the ANNOTATE= option to add a customized legend to the diagram.

A typical problem encountered in a research and development setting involves two decisions: whether or not to conduct research, and whether or not to commercialize the results of that research. Suppose that research and development for a specific project will cost \$350,000, and there is a 0.4 probability that it will fail. Also suppose that the different levels of market success and their corresponding probabilities are:

**Table 7.23** Levels of Market Success and Their Probabilities

Market Success	Net Return	Probability
Great	\$1,000,000	0.25
Good	\$500,000	0.35
Fair	\$200,000	0.30
Poor	-\$250,000	0.10

The structure of the model is represented in the STAGEIN= data set Stage4.

```
/* -- create the STAGEIN= data set                                -- */
data Stage4;
input _STNAME_ $ 1-16 _STTYPE_ $ 17-20
      _OUTCOM_ $ 21-32 _REWARD_ dollar12.0
      _SUCC_ $ 45-60;
datalines;
R_and_D      D  Not_Conduct .
               .  Conduct    -$350,000  RD_Outcome
RD_Outcome   C  Success   .
               .  Failure   .
Production   D  Produce   .
               .  Abandon   .
Sales        C  Great    .
               .  Good     .
               .  Fair     .
               .  Poor     .
;
```

The probability distributions for the various outcomes of the chance stages are given in the PROBIN= data set named Prob4.

```
/* -- create the PROBIN= data set                                -- */
data Prob4;
input _EVENT1_ $ _PROB1_ _EVENT2_ $12. _PROB2_;
datalines;
Success      0.6      Failure    0.4
Great        0.25     Good       0.35
Fair         0.30     poor       0.1
;
```

The payoffs are given in the PAYOFFS= data set Payoff4.

```
/* -- create the PAYOFFS= data set                                -- */
data Payoff4;
input _STATE_ $12. _VALUE_ dollar12.0;
datalines;
Great      $1,000,000
Good       $500,000
Fair        $200,000
Poor      -$250,000
;
```

The following DATA step builds a data set that contains the Annotate description of a legend. Refer to the chapter on the annotate facility in *SAS/GRAF Software: Reference* for a description of the Annotate facility.

```
/* -- create the ANNOTATE= data set for legend      -- */
data Legend;
length FUNCTION $ 8;
length STYLE $ 16;
WHEN = 'B'; POSITION='0';
XSYS='4'; YSYS='4';
input FUNCTION $ X Y STYLE & 16. SIZE COLOR $ TEXT $ & 16.;
datalines;
move      8   2.1  .
draw      12  2.1  .
label     14   2   Cumberland AMT  0.6 black  BEST ACTION
symbol    9   3.5  marker      0.6 red    A
label     14   3.2  Cumberland AMT  0.6 black  END NODE
symbol    9   4.7  marker      0.6 blue   P
label     14   4.4  Cumberland AMT  0.6 black  CHANCE NODE
symbol    9   5.9  marker      0.6 green  U
label     14   5.6  Cumberland AMT  0.6 black  DECISION NODE
label     8   7.0  Cumberland AMT  0.6 black  LEGEND:
move      5   8.5  .
draw      35  8.5  .
draw      35   1   .
draw      5   1   .
draw      5   8.5  .
```

The following program invokes PROC DTREE, which evaluates the decision tree and plots it on a graphics device using the Annotate data set Legend to draw the legend.

```

/* define symbol characteristics for chance nodes and */
/* links except those that represent optimal decisions */
symbol1 f=marker h=1.8 v=P c=blue w=5 l=1;

/* define symbol characteristics for decision nodes      */
/* and links that represent optimal decisions           */
symbol2 f=marker h=1.8 v=U cv=green ci=red w=10 l=1;

/* define symbol characteristics for end nodes          */
symbol3 f=marker h=1.8 v=A cv=red;

/* define graphics options                             */
goptions htext=1.2;

/* -- define title -- */
title f='Cumberland AMT'
h=2.5 'Research and Development Decision';

/* -- PROC DTREE statements                         -- */
proc dtree
  stagein=Stage4 probin=Prob4 payoffs=Payoff4
  criterion=maxce rt=1800000
  graphics annotate=Legend nolg ;

evaluate;

treeplot / linka=1 linkb=2
          symbold=2 symbolc=1 symbole=3 compress name="dt4";

quit;


```

The SYMBOL1, SYMBOL2, and SYMBOL3 statements create three SYMBOL definitions that contain information for drawing nodes and links. The Legend data set and the ANNOTATE= option specified in the PROC DTREE statement cause the procedure to produce a customized legend for the decision tree diagram. The LINKA=, LINKB=, SYMBOLD=, SYMBOLC=, and SYMBOLE= specifications in the TREEPLOT statement tell PROC DTREE how to use SYMBOL definitions to draw the decision tree. Table 7.24 describes the options in SYMBOL definitions used to draw the decision tree diagram.

The decision tree diagram produced by the TREEPLOT statement is shown in Output 7.4.1. As illustrated on the decision tree, the program recommends that one should not conduct the research and development of the product if he or she is risk averse with a risk tolerance of \$1,800,000. However, if he or she decides to undertake the research and development and it is a success, then he or she should commercialize the product.

**Table 7.24** The Usage of SYMBOL Definitions

SYMBOL Definition	Specification	Description	Used to Draw
The First	<i>C=blue</i> <i>L=1</i> <i>W=3</i>	Color Line Type Thickness	All links except those that indicate optimal decisions
	<i>C=blue</i> <i>F=marker</i> <i>H=2</i> <i>V=P</i>	Color Font Height Symbol	Chance nodes
The Second	<i>CI=red</i> <i>L=1</i> <i>W=3</i>	Color Line Type Thickness	All links that indicate optimal decisions
	<i>CV=green</i> <i>F=marker</i> <i>H=2</i> <i>V=U</i>	Color Font Height Symbol	Decision nodes
The Third	<i>CV=red</i> <i>F=marker</i> <i>H=2</i> <i>V=A</i>	Color Font Height Symbol	End nodes

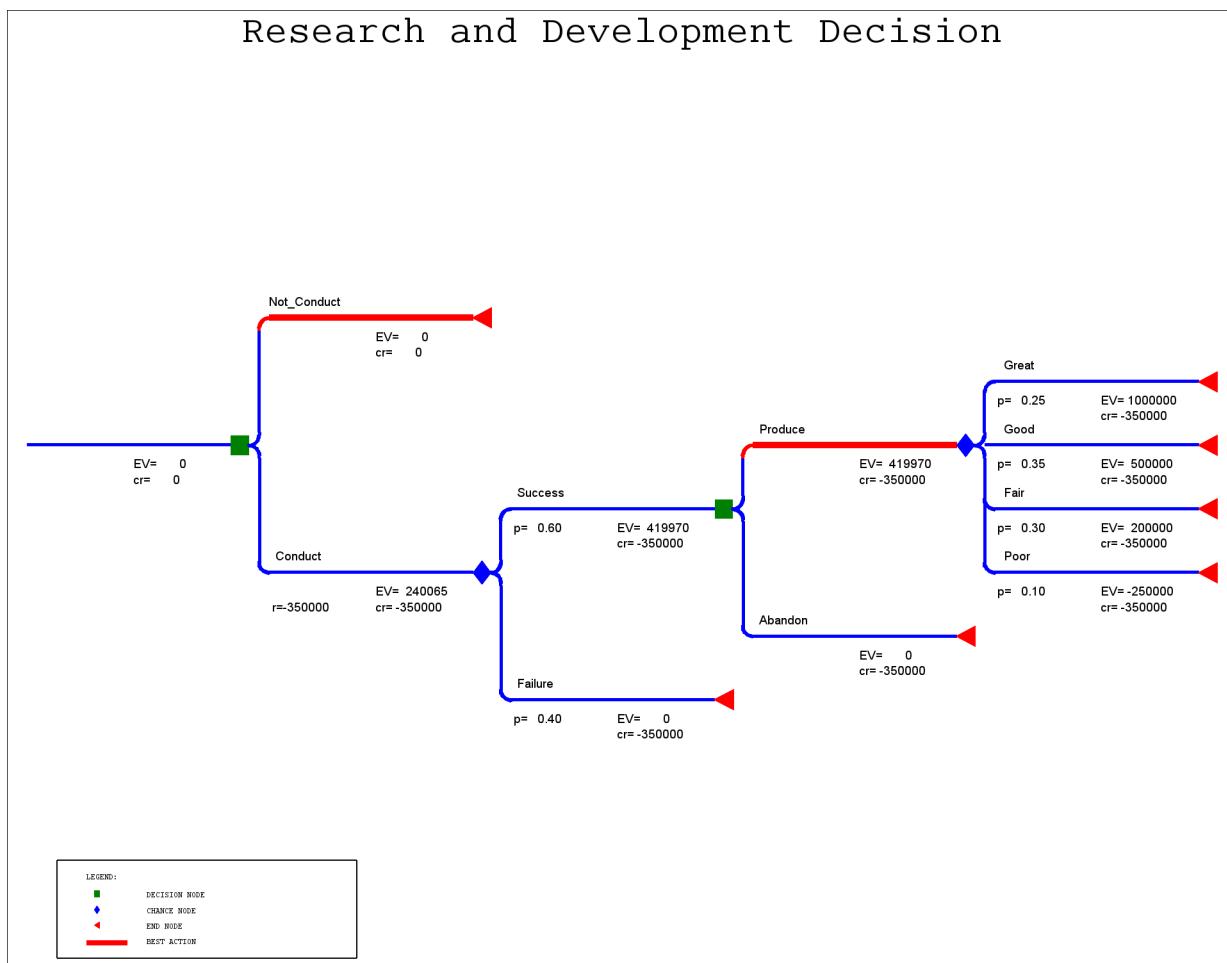**Output 7.4.1** Research and Development Decision Tree**Example 7.5: Loan Grant Decision Problem**

Many financial decisions are difficult to analyze because of the variety of available strategies and the continuous nature of the problem. However, if the alternatives and time frame can be restricted, then decision analysis can be a useful analysis tool.

For example, a loan officer is faced with the problem of deciding whether to *approve* or *deny* an application for a one-year \$30,000 loan at the current rate of 15% of interest. If the application is approved, the borrower will either *pay off* the loan in full after one year or *default*. Based on experience, the default rate is about 36 out of 700. If the loan is denied, the money is put in government bonds at the interest rate of 8%.

To obtain more information about the applicant, the loan officer engages a credit investigation unit at a cost of \$500 per person that will give either a *positive* recommendation for making a loan or a *negative* recommendation. Past experience with this investigator yields that of those who ultimately paid off their loans, 570 out of 664 were given a positive recommendation. On the other hand, 6 out of 26 that had defaulted had also been given a positive recommendation by the investigator.

The **STAGEIN=** data set, Stage6, gives the structure of the decision problem.

```

/* -- create the STAGEIN= data set                                -- */
data Stage6;
format _STNAME_ $14. _STTYPE_ $2. _OUTCOM_ $20. _SUCC_ $14. ;
input _STNAME_ $ _STTYPE_ $ _OUTCOM_ & _SUCC_ $ ;
datalines;
Application      D   Approve loan          Payment
.                .   Deny loan            .
Payment          C   Pay off             .
.                .   Default              .
Investigation    D   Order investigation  Recommendation
.                .   Do not order        Application
Recommendation   C   Positive           Application
.                .   Negative            Application
;

```

The PROBIN= data set Prob6 gives the probability distributions for the random events at the chance nodes.

```

/* -- create the PROBIN= data set                                -- */
data Prob6;
length _GIVEN_ _EVENT1_ _EVENT2_ $16;

_Event1_='Pay off';     _Event2_='Default';
_Prob1_=664/700;         _Prob2_=1.0-_Prob1_;
output;

_Given_='Pay off';
_Event1_='Positive';    _Event2_='Negative';
_Prob1_=570/664;         _Prob2_=1.0-_Prob1_;
output;

_Given_='Default';
_Event1_='Positive';    _Event2_='Negative';
_Prob1_=6/26;             _Prob2_=1.0-_Prob1_;
output;

run;

```

The PAYOFFS= data set Payoff6 gives the payoffs for the various scenarios. Notice that the first observation in this data set indicates that if the officer denies the loan application, then payoffs are the interest from the money invested in government bonds. The second and the third observations are redundant for the basic analysis but are needed to determine the value of information as shown later.

```

/* -- create the PAYOFFS= data set                                -- */
data Payoff6(drop=loan);
length _STATE_ _ACT_ $24;

loan=30000;

_ACT_='Deny loan';    _VALUE_=loan*0.08;   output;
_STATE_='Pay off';    _VALUE_=loan*0.08;   output;
_STATE_='Default';    _VALUE_=loan*0.08;   output;

_ACT_='Approve loan';

```

```

_STATE_='Pay off';    _VALUE_=loan*0.15;      output;
_STATE_='Default';   _VALUE_=-1.0*loan;      output;

run;

```

The following code invokes the DTREE procedure to solve this decision problem.

```

/* -- define title                                -- */
title 'Loan Grant Decision';

/* -- PROC DTREE statements                      -- */
proc dtree
  stagein=Stage6 probin=Prob6 payoffs=Payoff6
  summary target=investigation nowarning;

  modify 'Order investigation' reward -500;

  evaluate;

  OPTIONS LINESIZE=85;
  summary / target=Application;
  OPTIONS LINESIZE=80;

```

Note that the \$500 investigation fee is not included in the Stage6 data set. Since the outcome '**Order investigation**' is the only outcome that has a nonzero reward, it is easier to set the reward for this outcome using the **MODIFY** statement. The quotes that enclose the outcome name in the **MODIFY** statement are necessary because the outcome name contains a space.

The results in [Output 7.5.1](#) and [Output 7.5.2](#) indicate that it is optimal to do the following:

- The loan officer should order the credit investigation and approve the loan application if the investigator gives the applicant a positive recommendation. On the other hand, he should deny the application if a negative recommendation is given to the applicant.
- Furthermore, the loan officer should order a credit investigation if the cost for the investigation is less than  $\$3,725 - \$2,726 = \$999$ .

#### **Output 7.5.1** Summary of the Loan Grant Decision for Investigation

#### **Loan Grant Decision**

#### **The DTREE Procedure**

#### **Optimal Decision Summary**

<b>Order of Stages</b>	
<b>Stage</b>	<b>Type</b>
<b>Investigation</b>	Decision
<b>Recommendation</b>	Chance
<b>Application</b>	Decision
<b>Payment</b>	Chance
<b><u>ENDST_</u></b>	End

**Output 7.5.1** *continued*

Decision Parameters		
Decision Criterion: Maximize Expected Value (MAXEV)		
Optimal Decision Yields: 3225		
<b>Optimal Decision Policy</b>		
Up to Stage Investigation		
Alternatives or Outcomes	Cumulative Reward	Evaluating Value
Order investigation	-500	3725*
Do not order	0	2726

**Output 7.5.2** Summary of the Loan Grant Decision for Application**Loan Grant Decision****The DTREE Procedure****Optimal Decision Summary**

Order of Stages	
Stage	Type
Investigation	Decision
Recommendation	Chance
Application	Decision
Payment	Chance
<u>ENDST</u>	End

Decision Parameters		
Decision Criterion: Maximize Expected Value (MAXEV)		
Optimal Decision Yields: 3225		

**Optimal Decision Policy**

## Up to Stage Application

Alternatives or Outcomes	Positive	Approve loan	Cumulative Reward	Evaluating Value
Order investigation	Positive	Approve loan	-500	4004*
Order investigation	Positive	Deny loan	-500	2400
Order investigation	Negative	Approve loan	-500	-3351
Order investigation	Negative	Deny loan	-500	2400*
Do not order		Approve loan	0	2726*
Do not order		Deny loan	0	2400

Now, the loan officer learns of another credit investigation company that claims to have a more accurate credit checking system for predicting whether the applicants will default on their loans. However, he has not been able to find out what the company charges for their service or how accurate their credit checking system is. Perhaps the best thing he can do at this stage is to assume that the company can predict perfectly whether or not applicants will default on their loans and determine the maximum amount to pay for this perfect investigation. The answer to this question can be found with the **PROC DTREE** statements:

```

save;
move payment before investigation;
evaluate;
recall;

```

Notice that moving the stage '**Payment**' to the beginning of the tree means that the new decision tree contains two scenarios that are not in the original tree: the scenario '**Pay off**' and '**Deny loan**', and the scenario '**Default**' and '**Deny loan**'. The second and third observations in the Payoff6 data set supply values for these new scenarios. If these records are not included in the **PAYOFFS=** data set, then PROC DTREE assumes they are 0.

Also notice that the **SUMMARY** and **TARGET=** options are specified globally in the **PROC DTREE** statement and hence are not needed in the **EVALUATE** statement. The results from the DTREE procedure are displayed in [Output 7.5.3](#).

### **Output 7.5.3** Summary of the Loan Grant Decision with Perfect Information

#### **Loan Grant Decision**

#### **The DTREE Procedure**

#### **Optimal Decision Summary**

<b>Order of Stages</b>	
<b>Stage</b>	<b>Type</b>
<b>Payment</b>	Chance
<b>Investigation</b>	Decision
<b>Recommendation</b>	Chance
<b>Application</b>	Decision
<b><u>ENDST_</u></b>	End

---

#### **Decision Parameters**

**Decision Criterion:** Maximize Expected Value (MAXEV)  
**Optimal Decision Yields:** 4392

---



---

#### **Optimal Decision Policy**

#### **Up to Stage Investigation**

<b>Alternatives or Outcomes</b>		<b>Cumulative Reward</b>	<b>Evaluating Value</b>
<b>Pay off</b>	<b>Order investigation</b>	-500	4500
<b>Pay off</b>	<b>Do not order</b>	0	4500*
<b>Default</b>	<b>Order investigation</b>	-500	2400
<b>Default</b>	<b>Do not order</b>	0	2400*

The optimal decision summary in [Output 7.5.3](#) shows that the yields with perfect investigation is \$4,392. Recall that the yield of alternative '**Do not order**' the investigation, as shown in [Output 7.5.1](#), is \$2,726.

Therefore, the maximum amount he should pay for the perfect investigation can be determined easily as

$$\begin{aligned}\text{VPI} &= \text{Value with Perfect Investigation} - \text{Value without Investigation} \\ &= \$4,392 - \$2,726 \\ &= \$1,666\end{aligned}$$

Note that if you use the **VPI** statement to determine the value of a perfect investigation, the result is different from the value calculated previously.

```
vpi payment;
```

```
NOTE: The currently optimal decision yields 3225.4725275.
NOTE: The new optimal decision yields 4392.
NOTE: The value of perfect information of stage Payment
      yields 1166.5274725.
```

The reason for this difference is that the **VPI** statement causes PROC DTREE first to determine the value with perfect information, then to compare this value with the value with current information available (in this example, it is the recommendation from the original investigation unit). Therefore, the **VPI** statement returns a value that is calculated as

$$\begin{aligned}\text{VPI} &= \text{Value with Perfect Information} - \text{Value with Current Information} \\ &= \$4,392 - \$3,225 \\ &= \$1,167\end{aligned}$$

The loan officer considered another question regarding the maximum amount he should pay to a company to help collect the principal and the interest if an applicant defaults on the loan. This question is similar to the question concerning the improvement that can be expected if he can control whether or not an applicant will default on his loan (of course he will always want the applicant to pay off in full after one year). The answer to this question can be obtained with the following statements:

```
modify payment type;
evaluate;
```

**Output 7.5.4** Summary of the Loan Grant Decision with Perfect Control**Loan Grant Decision****The DTREE Procedure****Optimal Decision Summary**

Order of Stages	
Stage	Type
Investigation	Decision
Recommendation	Chance
Application	Decision
Payment	Decision
<u>ENDST_</u>	End

Decision Parameters	
Decision Criterion: Maximize Expected Value (MAXEV)	
Optimal Decision Yields: 4500	

Optimal Decision Policy		
Up to Stage Investigation		
Alternatives or Outcomes	Cumulative Reward	Evaluating Value
Order investigation	-500	4500
Do not order	0	4500*

The result is obvious and is shown in [Output 7.5.4](#). Using a calculation similar to the one used to calculate the value of a perfect investigation, the maximum amount one should pay for this kind of service is  $\$4,500 - \$2,726 = \$1,774$ . As previously described, this value is different from the value obtained by using the **VPC** statement. In fact, if you specify the statement

```
vpc payment;
```

you get the value of VPC, which is \$1,274.53, from the SAS log as

```
NOTE: The currently optimal decision yields 3225.4725275.
NOTE: The new optimal decision yields 4500.
NOTE: The value of perfect control of stage Payment yields
      1274.5274725.
```

Obviously, all of the values of investigation and other services depend on the value of the loan. Since each of the payoffs for the various scenarios given in the Payoff6 data set is proportional to the value of loan, you can safely assume that the value of the loan is 1 unit and determine the ratio of the value for a particular service to the value of the loan. To obtain these ratios, change the value of the variable LOAN to 1 in the Payoff6 data set and invoke PROC DTREE again as follows:

```

/* -- create the alternative PAYOFFS= data set -- */
data Payoff6a(drop=loan);
length _STATE_ _ACT_ $24;
loan=1;

_ACT_='Deny loan';   _VALUE_=loan*0.08;      output;
_STATE_='Pay off';   _VALUE_=loan*0.08;      output;
_STATE_='Default';   _VALUE_=loan*0.08;      output;

_ACT_='Approve loan';
_STATE_='Pay off';   _VALUE_=loan*0.15;      output;
_STATE_='Default';   _VALUE_=-1.0*loan;      output;
run;

/* -- PROC DTREE statements                                -- */
title 'Loan Grant Decision';

proc dtree
    stagein=Stage6 probin=Prob6 payoffs=Payoff6a
    nowarning;

evaluate / summary target=investigation;

save;
move payment before investigation;
evaluate;

recall;
modify payment type;
evaluate;

quit;

```

The optimal decision summary given in Output 7.5.5 shows that the ratio of the value of investigation that the loan officer currently engages in to the value of the loan is  $0.1242 - 0.0909 = 0.0333$  to 1.

#### Output 7.5.5 Summary of the Loan Grant Decision with 1 Unit Loan

##### Loan Grant Decision

##### The DTREE Procedure

##### Optimal Decision Summary

Order of Stages	
Stage	Type
Investigation	Decision
Recommendation	Chance
Application	Decision
Payment	Chance
_ENDST_	End

**Output 7.5.5** *continued*

Decision Parameters		
Decision Criterion: Maximize Expected Value (MAXEV)		
Optimal Decision Yields: 0.1242		
Optimal Decision Policy		
Up to Stage Investigation		
Alternatives or Outcomes	Cumulative Reward	Evaluating Value
Order investigation		0.1242*
Do not order		0.0909

The following messages are written to the SAS log:

**NOTE: Present order of stages:**

Investigation(D), Recommendation(C), Application(D),  
Payment(C), \_ENDST\_(E).

**NOTE: The current problem has been successfully saved.**

**NOTE: Present order of stages:**

Payment(C), Investigation(D), Recommendation(C),  
Application(D), \_ENDST\_(E).

**NOTE: The currently optimal decision yields 0.1464.**

**NOTE: The original problem has been successfully recalled.**

**NOTE: Present order of stages:**

Investigation(D), Recommendation(C), Application(D),  
Payment(C), \_ENDST\_(E).

**NOTE: The type of stage Payment has been changed.**

**NOTE: The currently optimal decision yields 0.15.**

The preceding messages show that the ratio of the value of perfect investigation to the value of a loan is  $0.1464 - 0.0909 = 0.0555$  to 1, and the ratio of the maximum amount the officer should pay for perfect control to the value of loan is  $0.15 - 0.0909 = 0.591$  to 1.

**Output 7.5.6**, produced by the following statements, shows a table of the values of the investigation currently engaged in, the values of perfect investigation, and the values of perfect control for loans ranging from \$10,000 to \$100,000.

```
/* create the data set for value of loan */
/* and corresponding values of services */
data Datav6(drop=k ratio1 ratio2 ratio3);
```

```

label loan="Value of Loan"
      vci="Value of Current Credit Investigation"
      vpi="Value of Perfect Credit Investigation"
      vpc="Value of Perfect Collecting Service";

      /* calculate ratios */
ratio1=0.1242-0.0909;
ratio2=0.1464-0.0909;
ratio3=0.15-0.0909;

Loan=0;
do k=1 to 10;

      /* set the value of loan */
loan=loan+10000;

      /* calculate the values of various services */
vci=loan*ratio1;
vpi=loan*ratio2;
vpc=loan*ratio3;

      /* output current observation */
output;
end;
run;

/* print the table of the value of loan */
/* and corresponding values of services */
title 'Value of Services by Value of Loan';

proc print label;
  format loan vci vpi vpc dollar12.0;
run;

```

#### Output 7.5.6 Values of Loan and Associated Values of Service

##### Value of Services by Value of Loan

Obs	Value of Loan	Value of Current Credit Investigation	Value of Perfect Credit Investigation	Value of Perfect Collecting Service
1	\$10,000	\$333	\$555	\$591
2	\$20,000	\$666	\$1,110	\$1,182
3	\$30,000	\$999	\$1,665	\$1,773
4	\$40,000	\$1,332	\$2,220	\$2,364
5	\$50,000	\$1,665	\$2,775	\$2,955
6	\$60,000	\$1,998	\$3,330	\$3,546
7	\$70,000	\$2,331	\$3,885	\$4,137
8	\$80,000	\$2,664	\$4,440	\$4,728
9	\$90,000	\$2,997	\$4,995	\$5,319
10	\$100,000	\$3,330	\$5,550	\$5,910

---

## Example 7.6: Petroleum Distributor's Decision Problem

The president of a petroleum distribution company currently faces a serious problem. His company supplies refined products to its customers under long-term contracts at guaranteed prices. Recently, the price for petroleum has risen substantially and his company will lose \$450,000 this year because of its long-term contract with a particular customer. After a great deal of discussion with his legal advisers and his marketing staff, the president learns that the contract contains a clause that may be beneficial to his company. The clause states that when circumstances are beyond its control, the company may ask its customers to pay the prevailing market prices for up to 10% of the promised amount.

Several scenarios are possible if the clause is invoked. If the customer accepts the invocation of the clause and agrees to pay the higher price for the 10%, the company would turn a loss of \$450,000 into a net profit of \$600,000. If the customer does not accept the invocation, the customer may sue for damages or accept a settlement of \$900,000 (resulting in a loss of \$400,000) or simply decline to press the issue. In any case, the distribution company could then sell the 10% on the open market for an expected value of \$500,000. However, the lawsuit would result in one of three possible outcomes: the company wins and pays no damages; the company loses and pays normal damages of \$1,500,000; the company loses and pays double damages of \$3,000,000. The lawyers also feel that this case might last three to five years if the customer decides to sue the company. The cost of the legal proceedings is estimated as \$30,000 for the initial fee and \$20,000 per year. The likelihood of the various outcomes are also assessed and reported as in [Table 7.25](#). Suppose that the company decides to use a discount rate of 10% to determine the present value of future funds.

**Table 7.25** Likelihood of the Outcomes in the Petroleum Distributor's Decision

Uncertainty	Outcome	Probability
Customer's Response	Accept the Invocation	0.1
	Reject the Invocation	0.9
Customer's Action if the Invocation is being Rejected	Press the Issue	0.1
	Settle the Case	0.45
	Sue for Damages	0.45
Case Last	3 Years	0.3
	4 Years	0.4
	5 Years	0.3
Lawsuit Result	Pay No Damages	0.15
	Pay Normal Damages	0.65
	Pay Double Damages	0.2

The structure for this decision problem is given in the **STAGEIN=** data set named Stage7.

```
/* -- create the STAGEIN= data set                                -- */
data Stage7;
  format _OUTCOM1 $14. _OUTCOM2 $14. ;
  input _STNAME_ $ _STTYPE_ $ _OUTCOM1 $ 
        _SUCC1 $ _OUTCOM2 $ _SUCC2 $ ;
  datalines;
Action   D   Invoking      Response  Not_Invoking    .
Response C   Accept       .          Refuse      Lawsuit
Lawsuit  C   Press_Issue  .          Settle     .

```

```

        .     Sue           Last
Last      C   3_Years       Result    4_Years       Result
        .   5_Years       Result
Result    C   No_Damages   .
        .   Double_Damages .
;

```

The **PROBIN=** data set Prob7 contains the probability distributions for the chance nodes.

```

/* -- create the PROBIN= data set                                -- */
data Prob7;
  format _EVENT1_ _EVENT2_ $14.;
  input _EVENT1_ $ _PROB1_ _EVENT2_ $ _PROB2_ ;
  datalines;
Accept      0.1     Refuse      0.9
Press_Issue 0.1     Settle      0.45
Sue         0.45    .
3_Years     0.3     4_Years     0.4
5_Years     0.3     .
No_Damages  0.15    Normal_Damages 0.65
Double_Damages 0.20 .
;

```

The **PAYOFFS=** data set Payoff7 defines the payoffs for the various scenarios.

```

/* -- create the PAYOFFS= data set                                -- */
data Payoff7(drop=i j k D PCOST);
  length _ACTION_ _STATE1-_STATE4 $16;

  /* possible outcomes for the case last                         */
  array YEARS{3}    $16. _TEMPORARY_ ('3_Years',
                                      '4_Years',
                                      '5_Years' );

  /* numerical values for the case last  */
  array Y{3}          _TEMPORARY_ (3, 4, 5);

  /* possible outcomes for the size of judgment */
  array DAMAGES{3} $16. _TEMPORARY_ ('No_Damages',
                                      'Normal_Damages',
                                      'Double_Damages' );

  /* numerical values for the size of judgment */
  array C{3}          _TEMPORARY_ (0, 1500, 3000);

D=0.1;                                     /* discount rate */

  /* payoff for the scenario which the                         */
  /* 10 percent clause is not invoked                         */
  _ACTION_='Not_Invoking'; _VALUE_=-450;   output;

  /* the clause is invoked */
  _ACTION_='Invoking';

```

```

/* payoffs for scenarios which the clause is */
/* invoked and the customer accepts the      */
/* invocation                                */
_STATE1='Accept';           _VALUE_=600;   output;

/* the customer refuses the invocation      */
_STATE1='Refuse';

/* payoffs for scenarios which the clause is */
/* invoked and the customer refuses the      */
/* invocation but decline to press the issue */
_STATE2='Press_Issue';       _VALUE_=500;   output;

/* payoffs for scenarios which the clause is */
/* invoked and the customer refuses the      */
/* invocation but willing to settle out of   */
/* court for 900K                            */
_STATE2='Settle';          _VALUE_=500-900; output;

/* the customer will sue for damages        */
_STATE2='Sue';
do i=1 to 3;
  _STATE3=YEARS{i};

/* determine the cost of proceedings         */
PCOST=30; /* initial cost of the proceedings */

/* additional cost for every years in      */
/* in present value                         */
do k=1 to Y{i};
  PCOST=PCOST+(20/((1+D)**k));
end;

/* loop for all poss. of the lawsuit result */
do j=1 to 3;
  _STATE4=DAMAGES{j}; /* the damage have to paid */

  /* compute the net return in present value */
  _VALUE_=500-PCOST-(C{j}/((1+D)**Y{i}));

  /* output an observation for the payoffs */
  /* of this scenario                      */
  output;
end;
end;

run;

/* -- print the payoff table                */
/* title "Petroleum Distributor's Decision"; */
/* title3 "Payoff Table";                  */
-- */

proc print;

```

```
run;
```

The payoff table of this problem is displayed in [Output 7.6.1](#).

### **Output 7.6.1 Payoffs for the Petroleum Distributor's Problem**

#### **Petroleum Distributor's Decision**

##### **Payoff Table**

<u>Obs</u>	<u>ACTION</u>	<u>STATE1</u>	<u>STATE2</u>	<u>STATE3</u>	<u>STATE4</u>	<u>VALUE_</u>
1	Not_Invoking					-450.00
2	Invoking	Accept				600.00
3	Invoking	Refuse	Press_Issue			500.00
4	Invoking	Refuse	Settle			-400.00
5	Invoking	Refuse	Sue	3_Years	No_Damages	420.26
6	Invoking	Refuse	Sue	3_Years	Normal_Damages	-706.71
7	Invoking	Refuse	Sue	3_Years	Double_Damages	-1833.68
8	Invoking	Refuse	Sue	4_Years	No_Damages	406.60
9	Invoking	Refuse	Sue	4_Years	Normal_Damages	-617.92
10	Invoking	Refuse	Sue	4_Years	Double_Damages	-1642.44
11	Invoking	Refuse	Sue	5_Years	No_Damages	394.18
12	Invoking	Refuse	Sue	5_Years	Normal_Damages	-537.20
13	Invoking	Refuse	Sue	5_Years	Double_Damages	-1468.58

Note that the payoffs of the various scenarios in [Output 7.6.1](#) are in thousands of dollars and are *net present values* (NPV) (Baird 1989). For example, the payoff for the following scenario “invoking the clause; the customer refuses to accept this and sues for damages; the case lasts four years and the petroleum distribution company loses and pays double damages” is calculated as

$$\begin{aligned} \text{Payoff} &= 500 - \text{NPV of proceedings cost} \\ &\quad - \text{NPV of damages of } 3,000,000 \\ &= -1642.44 \end{aligned}$$

where

$$\text{NPV of proceedings cost} = 30 + \sum_{k=1}^4 20/(1+0.1)^k$$

and

$$\text{NPV of damages of } 3,000,000 = 3000/(1+0.1)^4$$

This is because the company can sell the 10% for \$500,000 immediately and pay the \$3,000,000 damages four years from now. The net present value of the proceedings is determined by paying the \$30,000 initial fee now and a fee of \$20,000 after every year up to four years. The value of 0.1 is the discount rate used.

The following statements evaluate the problem and plot the optimal solution.

```

/* -- define graphics options                                -- */
goptions colors=(green red blue);
goptions hsize=8 in vsize=8.4 in;

/* -- define title                                         -- */
title h=2.5 "Petroleum Distributor's Decision";

/* -- PROC DTREE statements                                -- */
proc dtree stagein=Stage7 probin=Prob7 payoffs=Payoff7;
  evaluate / summary;
  treeplot / graphics compress nolg name="dt6p1" ftext='Cumberland AMT'
    ybetween=1 cell lwidth=2 lwidthb=3 hsymbol=3;
quit;

```

The optimal decision summary in [Output 7.6.2](#) suggests that the president should invoke the 10% clause because it would turn a loss of \$450,000 into an expected loss of \$329,000 in present value.

### **Output 7.6.2** Summary of the Petroleum Distributor's Decision

#### **Petroleum Distributor's Decision**

##### **The DTREE Procedure**

##### **Optimal Decision Summary**

<b>Order of Stages</b>	
<b>Stage</b>	<b>Type</b>
Action	Decision
Response	Chance
Lawsuit	Chance
Last	Chance
Result	Chance
<u>_ENDST_</u>	End

##### **Decision Parameters**

**Decision Criterion:** Maximize Expected Value (MAXEV)  
**Optimal Decision Yields:** -329

##### **Optimal Decision Policy**


##### **Up to Stage Action**

<b>Alternatives or Outcomes</b>	<b>Cumulative Reward</b>	<b>Evaluating Value</b>
Invoking		-329*
<u>Not_Invoking</u>		-450

The decision tree for this problem is shown in [Output 7.6.3](#). There you can find the expected value of each scenario.

Output 7.6.3 Decision Tree for the Petroleum Distributor's Decision

# Petroleum Distributor's Decision

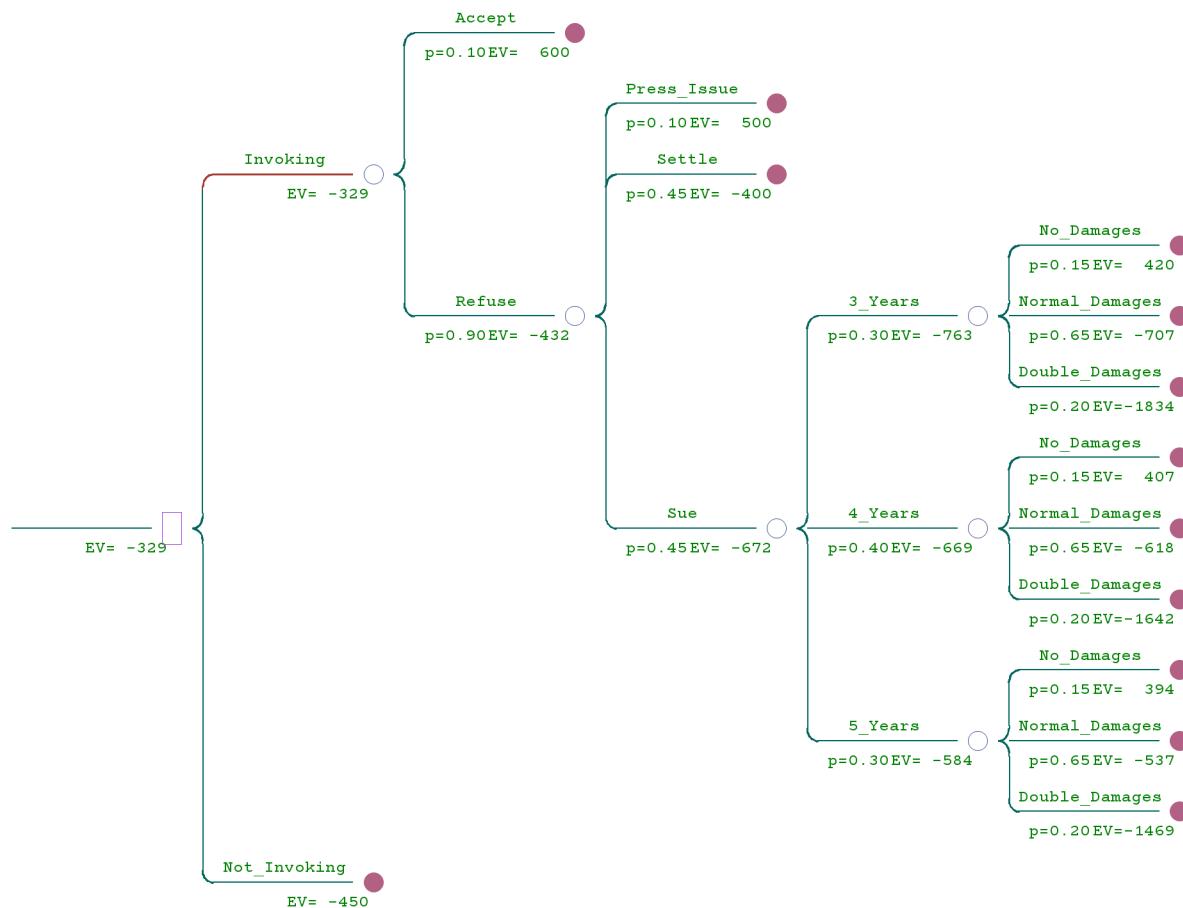

The president feels that the estimated likelihood of lawsuit outcomes is fairly reliable. However, the assessment of the likelihood of the customer's response and reaction is extremely difficult to estimate. Because of this, the president would like to keep the analysis as general as possible. His staff suggests using the symbols  $p$  and  $q$  to represent the probability that the customer will accept the invocation and the probability that the customer will decline to press the issue if he refuses the invocation, respectively. The probabilities of the other possible outcomes about the customer's response and reaction to the invocation of the 10% clause are listed in [Table 7.26](#).

**Table 7.26** Probabilities of the Petroleum Distributor's Decision

Uncertainty	Outcome	Probability
Customer's Response	Accept the Invocation	$p$
	Reject the Invocation	$1 - p$
Customer's Action if the Invocation is being Rejected	Press the Issue	$q$
	Settle the Case	$(1 - q)/2$
	Sue for Damages	$(1 - q)/2$

Now from the decision tree shown in [Output 7.6.3](#), the expected value of the outcome '**Refuse**' is

$$\begin{aligned} EV &= 500q - 400(1 - q)/2 - 672(1 - q)/2 \\ &= 500q - 200 + 200q - 336 + 336q \\ &= 1036q - 536 \end{aligned}$$

Hence, the expected payoff if the petroleum distribution company invokes the clause is

$$\begin{aligned} EV &= 600p + (1036q - 536)(1 - p) \\ &= 1136p + 1036q - 1036pq - 536 \\ &= 1136p + 1036(1 - p)q - 536 \end{aligned}$$

Therefore, the president should invoke the 10% clause if

$$1136p + 1036(1 - p)q - 536 > -450$$

or

$$q > \frac{86 - 1136p}{1036 - 1036p}$$

This result is depicted in [Output 7.6.4](#), which is produced by the following statements:

```

/* -- create data set for decision diagram      -- */
data Data7(drop=i);
P=0.0;                      /* initialize P */

/* loop for all possible values of P */
do i=1 to 21;

/* determine the corresponding Q */
Q=(86-(1136*P))/(1036*(1.0-P));
if Q < 0.0 then Q=0.0;

/* output this data point */
output;

/* set next possible value of P   */
P=P+0.005;
end;

run;

/* create the ANNOTATE= data set for labels of  */
/* decision diagram                         */
data label;
length FUNCTION STYLE COLOR $8;
length XSYS YSYS             $1;
length WHEN POSITION          $1;
length X Y                   8;
length SIZE ROTATE           8;

WHEN = 'A';
POSITION='0';
XSYS='2';
YSYS='2';
input FUNCTION $ X Y STYLE $ SIZE COLOR $
      ROTATE TEXT $ & 16.;
datalines;
label  0.01  0.04  centx  2      black  .    Do Not
label  0.01  0.03  centx  2      black  .    Invoke
label  0.01  0.02  centx  2      black  .    The Clause
label  0.06  0.06  centx  2      black  .    Invoke The
label  0.06  0.05  centx  2      black  .    Clause
;

/* -- define symbol characteristics for boundary -- */
symbol1 i=joint v=NONE l=1 ci=black;

/* -- define pattern for area fill               -- */
pattern1 value=msolid color=cyan;
pattern2 value=msolid color=green;

/* -- define axis characteristics              -- */
axis1 label=('Pr(Accept the Invocation)')

```


```

order=(0 to 0.1 by 0.01) minor=none;
axis2 label=(angle=90 'Pr(Press the Issue)')
order=(0 to 0.1 by 0.01) minor=none;

/* -- plot decision diagram                                */
title h=2.5 "Petroleum Distributor's Decision";
proc gplot data=Data7 ;
  plot Q*P=1 / haxis=axis1
    vaxis=axis2
    annotate=label
    name="dt6p2"
    frame
    areas=2;
run;
quit;

```

Output 7.6.4 Decision Diagram for the Petroleum Distributor's Problem

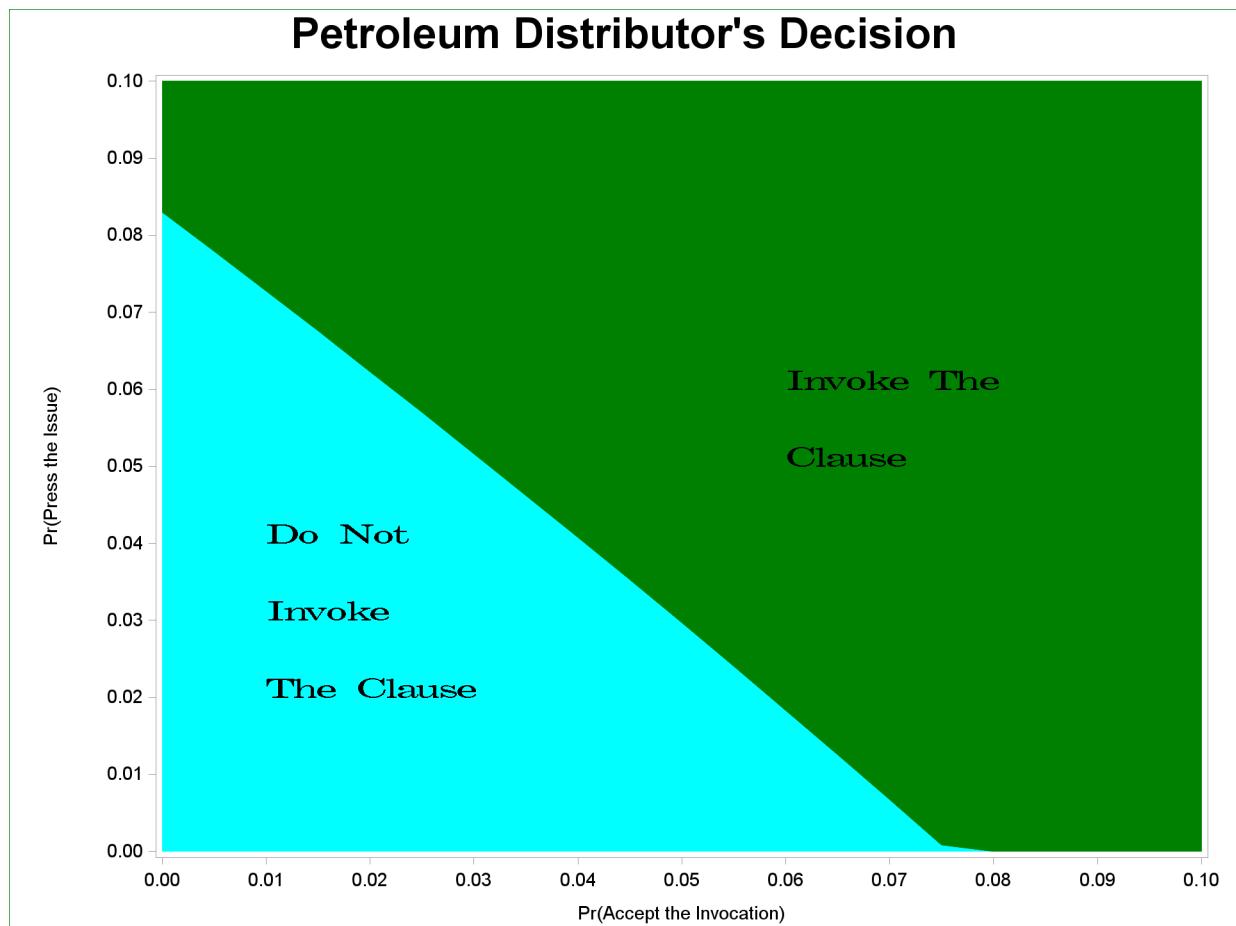

The decision diagram in [Output 7.6.4](#) is an analysis of the sensitivity of the solution to the probabilities that the customer will accept the invocation and that the customer will decline to press the issue. He should invoke the clause if he feels the customer's probabilities of outcomes '**Accept**' and '**Press\_Issue**',  $p$  and  $q$ , are located in the upper-right area marked as '**Invoke The Clause**' in [Output 7.6.4](#) and should not invoke the clause otherwise. Note that the values  $p = 0.1$  and  $q = 0.1$  used in this example are located on the upper right corner on the diagram.

## Statement and Option Cross-Reference Tables

The following tables reference the statements and options in the DTREE procedure (except the **PROC DTREE** statement and the **QUIT** statement) that are illustrated by the examples in this section.

**Table 7.27** Statements Specified in Examples

Statement	1	2	3	4	5	6
EVALUATE	X	X	X	X	X	X
MODIFY					X	
MOVE					X	
RECALL					X	
RESET	X					
SAVE					X	
SUMMARY	X	X			X	
TREEPLOT			X	X		
VARIABLES	X					X
VPC					X	
VPI					X	

**Table 7.28** Options Specified in Examples

Option	1	2	3	4	5	6
ANNOTATE=			X			
COMPRESS		X	X	X		X
CRITERION=	X	X		X		
EVENT=	X					
FTEXT=			X			X
GRAPHICS			X	X		X
HSYMBOL=			X			X
LINKA=				X		
LINKB=				X		
LINKC=						
LSTYLEB=			X			
LWIDTH=			X			X
LWIDTHB=			X			X
NAME=			X	X		X
NOLEGEND				X		X
NOWARNING	X	X	X		X	
OUTCOME=	X					
PAYOUTS=	X	X	X	X	X	X
PROB=	X					
PROBIN=	X	X	X	X	X	X
REWARD=	X					
RT=	X	X		X		
STAGE=	X					
STAGEIN=	X	X	X	X	X	X
STATE=	X					
SUCCESSOR=	X					
SUMMARY					X	X
SYMBOLC=				X		
SYMBOLD=				X		
SYMBOLE=				X		
TARGET=	X	X			X	
TYPE=	X					
VALUE=			X			
YBETWEEN=						X

## References

- Baird, B. F. (1989). *Managerial Decisions under Uncertainty: An Introduction to the Analysis of Decision Making*. New York: John Wiley & Sons.
- Howard, R. A. (1968). “The Foundations of Decision Analysis.” *IEEE Transactions on System Science and Cybernetics* SSC-4:211–219.
- Howard, R. A. (1988). “Decision Analysis: Practice and Promise.” *Management Science* 34:679–695.
- Kuhfeld, W. F. (2010). *Statistical Graphics in SAS: An Introduction to the Graph Template Language and the Statistical Graphics Procedures*. Cary, NC: SAS Institute Inc.
- Raiffa, H. (1970). *Decision Analysis Introductory Lectures on Choices under Uncertainty*. Reading, MA: Addison-Wesley.

# Chapter 8

## The GANTT Procedure

### Contents

---

Overview: GANTT Procedure . . . . .	484
Getting Started: GANTT Procedure . . . . .	487
Syntax: GANTT Procedure . . . . .	492
Functional Summary . . . . .	492
PROC GANTT Statement . . . . .	496
BY Statement . . . . .	499
CHART Statement . . . . .	499
ID Statement . . . . .	524
Details: GANTT Procedure . . . . .	525
Schedule Data Set . . . . .	525
Missing Values in Input Data Sets . . . . .	526
Specifying the PADDING= Option . . . . .	528
Page Format . . . . .	528
Multiple Calendars and Holidays . . . . .	530
Full-Screen Version . . . . .	531
Graphics Version . . . . .	535
Specifying the Logic Options . . . . .	545
Automatic Text Annotation . . . . .	552
Web-Enabled Gantt Charts . . . . .	556
Mode-Specific Differences . . . . .	557
Displayed Output . . . . .	558
Macro Variable _ORGANTT . . . . .	559
Computer Resource Requirements . . . . .	561
ODS Style Templates . . . . .	561
Examples: GANTT Procedure . . . . .	566
Line-Printer Examples . . . . .	566
Example 8.1: Printing a Gantt Chart . . . . .	566
Example 8.2: Customizing the Gantt Chart . . . . .	570
Graphics Examples . . . . .	575
Example 8.3: Marking Holidays . . . . .	576
Example 8.4: Marking Milestones and Special Dates . . . . .	582
Example 8.5: Using the COMPRESS Option . . . . .	585
Example 8.6: Using the MININTERVAL= and SCALE= Options . . . . .	586
Example 8.7: Using the MINDATE= and MAXDATE= Options . . . . .	590
Example 8.8: Variable-Length Holidays . . . . .	592
Example 8.9: Multiple Calendars . . . . .	595

Example 8.10: Plotting the Actual Schedule . . . . .	598
Example 8.11: Comparing Progress Against a Baseline Schedule . . . . .	600
Example 8.12: Using the COMBINE Option . . . . .	603
Example 8.13: Plotting the Resource-Constrained Schedule . . . . .	604
Example 8.14: Specifying the Schedule Data Directly . . . . .	606
Example 8.15: BY Processing . . . . .	610
Example 8.16: Gantt Charts by Persons . . . . .	613
Example 8.17: Using the HEIGHT= and HTOFF= Options . . . . .	617
Example 8.18: Drawing a Logic Gantt Chart Using AON Representation . . . . .	619
Example 8.19: Specifying the Logic Control Options . . . . .	621
Example 8.20: Nonstandard Precedence Relationships . . . . .	628
Example 8.21: Using the SAS/GRAFH ANNOTATE= Option . . . . .	631
Example 8.22: Using the Automatic Text Annotation Feature . . . . .	636
Example 8.23: Multiproject Gantt Charts . . . . .	638
Example 8.24: Multisegment Gantt Charts . . . . .	641
Example 8.25: Zoned Gantt Charts . . . . .	645
Example 8.26: Web-Enabled Gantt Charts . . . . .	646
Example 8.27: Using the CHARTWIDTH= Option . . . . .	651
Example 8.28: Using the TIMEAXISFORMAT= Option . . . . .	656
Statement and Option Cross-Reference Tables . . . . .	658
References . . . . .	660

---

## Overview: GANTT Procedure

The GANTT procedure produces a Gantt chart, which is a graphical scheduling tool for the planning and control of a project. In its most basic form, a Gantt chart is a bar chart that plots the tasks of a project versus time. PROC GANTT displays a Gantt chart that corresponds to a project schedule such as that produced by the CPM procedure or one that is input directly to the procedure. PROC GANTT offers several options and statements for tailoring the chart to your needs.

Using PROC GANTT, you can plot the predicted early and late schedules and identify critical, supercritical, and slack activities. In addition, you can visually monitor a project in progress with the actual schedule and compare the actual schedule against a target baseline schedule. You can also graphically view the effects of scheduling a project subject to resource limitations. Any combination of these schedules can be viewed simultaneously (provided the relevant data exist) together with any user-specified variables of interest, such as project deadlines and other important dates. PROC GANTT enables you to display the early, late, and actual schedules in a single bar to produce a more meaningful schedule for tracking an activity in progress.

PROC GANTT can display the **project logic** on the Gantt chart by exhibiting dependencies between tasks by using directed arcs to link the related activities. You can use either the activity-on-arc (**AOA**) or Activity-on-Node (**AON**) style of input for defining the project network. In addition, the GANTT procedure recognizes nonstandard precedence types. With PROC GANTT, you can display weekends, holidays, and multiple calendars, and you can depict milestones, reference lines, and a timenow line on the chart. PROC GANTT

enables you to annotate text and graphics on the Gantt chart and provides you with a wide variety of options to control and customize the graphical appearance of the chart.

The GANTT procedure also supports an automatic [text annotation](#) facility that is designed specifically for labeling Gantt charts independently of the SAS/GRAPH Annotate facility. It enables you to display label strings with a minimum of effort and data entry while providing the capability for more complex chart labeling situations. An important feature of this facility is the ability to link label coordinates and text strings to variables in the Schedule data set. This means that you can preserve the Label data set even though the schedule dates may change. Several options enable you to customize the annotation, such as the clipping of text strings that run off the page or the chart and the specification of a split character to split labels that are too long.

Using the GANTT procedure, you can produce a wide variety of Gantt charts. You can generate zoned Gantt charts with several options to control its appearance. You can display a zone variable column as well as draw a line demarcating the different zones. You can also control the bar height and bar offset of each type of schedule bar. This enables you to change the display order of the schedules as well as giving you the capability to produce a Gantt chart with embedded bars. You can override the default schedule bar pattern assignments at the activity level. In addition, you can restrict the schedule types to which the specified pattern is to be applied. You can also override the text color for selected columns of activity text at the activity level. These features facilitate the production of multiproject and multiprocess Gantt charts. Finally, you can also associate HTML pages with activity bars and create Web-enabled Gantt charts.

The GANTT procedure enables you to control the number of pages output by the procedure in both horizontal and vertical directions. In addition, you can control the number of jobs displayed per page as well as the number of tickmarks displayed per page. You can display ID variables on every page and even let the procedure display the maximum number of ID variables that can fit on one page. You can number the pages, justify the Gantt chart in the horizontal and vertical directions with respect to the page boundaries, and maintain the original aspect ratio of the Gantt chart on each page.

PROC GANTT gives you the option of displaying the Gantt chart in one of three modes: line-printer, full-screen, or graphics mode. The default mode is graphics mode, which enables you to produce charts of high resolution quality. Graphics mode requires SAS/GRAPH software. See the section “[Graphics Version](#)” on page 535 for more information on producing high-quality Gantt charts. You can also produce line-printer quality Gantt charts by specifying the LINEPRINTER option in the PROC GANTT statement. In addition to submitting the output to either a plotter or printer, you can view the Gantt chart at the terminal in full-screen mode by specifying the FULLSCREEN option in the PROC GANTT statement. See the section “[Full-Screen Version](#)” on page 531 for more information on viewing Gantt charts in full-screen mode. The GANTT procedure also produces a macro variable that indicates the status of the invocation and also contains other useful statistics about the Gantt charts generated by the invocation.

There are several distinctive features that characterize the appearance of the chart produced by the GANTT procedure:

- The horizontal axis represents time, and the vertical axis represents the sequence of observations in the data set.
- Both the time axis and the activity axis can be plotted across more than one page.
- The procedure automatically provides extensive labeling of the time axis, enabling you to determine easily the exact time of events plotted on the chart. The labels are determined on the basis of the formats of the times being plotted. You can also specify user-defined formats for the labeling.

- In graphics mode, the **COMPRESS** option in the **CHART** statement enables you to produce the entire Gantt chart on one page. The **PCOMPRESS** option enables you to produce the entire Gantt chart on one page while maintaining the original aspect ratio of the Gantt chart. Both these options work in conjunction with the **HPAGES=** and **VPAGES=** options, which specify the number of pages in the horizontal and vertical directions for the chart.

Project information is communicated into PROC GANTT using SAS data sets. The input data sets used by PROC GANTT are as follows:

- The **Schedule data set** contains the early, late, actual, resource-constrained, and baseline schedules and any other activity-related information. The activity-related information can include precedence information, calendar used by the activity, special dates, and any other information that you want to identify with each activity. This data set can be the same as the Schedule data set produced by **PROC CPM**, or it can be created separately by a DATA step. Each observation in the Schedule data set represents an activity and is plotted on a separate row of the chart unless activity splitting during resource-constrained scheduling has caused an activity to split into disjoint segments. For details regarding the output format in this case, see the section “**Displayed Output**” on page 558.
- The **Precedence (Logic) data set** contains the precedence information of the project in **AON** format in order to draw a Logic Gantt chart of the project. Specifying this data set is not necessary if the precedence information exists in the Schedule data set. If the data set is specified, however, the **ACTIVITY** variable must exist in both the Schedule and Precedence data sets.

Typically you would use this feature when scheduling in **PROC CPM** with nonstandard precedence constraints where the **LAG** variables are not transferred to the Schedule data set or with the **COLLAPSE** option. Setting the Precedence data set for PROC GANTT to be the Activity data set (used in **PROC CPM**) establishes the required precedence relationships. This is also a convenient feature when drawing several Gantt charts for the same project with different schedule information (such as when monitoring a project in progress). Specifying a Precedence data set avoids having to duplicate the precedence information in every Schedule data set.

- The **Label data set** contains the label information of the project that enables you to draw labeled Gantt charts independently of the SAS/GRAF Annotate facility. It requires a minimum of effort and provides you with a convenient mechanism to link label strings and their coordinates to variables in the Schedule data set. Another convenient feature is its ability to replicate labels across all activities. Both these features facilitate reuse of the Label data set.
- The **Workday and the Calendar data sets** together enable you to represent any type of work pattern, during a week and within each day of the week, on the Gantt chart. The same Workday and Calendar data sets used by **PROC CPM** can also be passed to PROC GANTT.
- The **Holiday data set** enables you to associate standard holidays and vacation periods with each calendar and represent them on the Gantt chart. Like the Workday and Calendar data sets, the same Holiday data set used by **PROC CPM** can also be used by PROC GANTT.
- The **Annotate data set** contains the graphics and text that are to be annotated on the Gantt chart. This data set is used by the GANTT procedure in conjunction with the Annotate facility in SAS/GRAF software.

The GANTT procedure produces one output data set.

- The **Imagemap data set** contains the outline coordinates for the schedule bars used in the Gantt chart that can be used to generate HTML MAP tags.

When displaying the precedence relationships between activities on the Gantt chart, bear in mind the following facts with regard to data sets used by PROC GANTT:

- The Schedule data set (and optionally the Precedence data set) contains the variables that define the precedence relationships between activities in the project.
- You can handle nonstandard precedence constraints in PROC GANTT when using **AON** format by identifying the **LAG** variables in the **CHART** statement.
- When you use **PROC CPM** to produce the schedule for a project with nonstandard precedence relationships, the **LAG** variables are not automatically included in the Schedule data set. Use an **ID** statement or the **XFERVARS** option in the **PROC CPM** statement to add them.
- When you generate the schedule using **PROC CPM** with the **COLLAPSE** option, it is recommended that you use the Activity data set to define the precedence relationships for the Gantt procedure by specifying the **PRECDATA=** option in the **PROC GANTT** statement. This ensures that all the relevant precedence information is extracted.

Each option and statement available in the GANTT procedure is explained in the section “[Syntax: GANTT Procedure](#)” on page 492. The section “[Examples: GANTT Procedure](#)” on page 566 illustrates most of these options and statements.

## Getting Started: GANTT Procedure

In order to draw a Gantt chart, at the very minimum you need a **Schedule** data set. This data set is expected to be *similar* to the **OUT=** Schedule data set produced by **PROC CPM**, with each observation representing an activity in the project. It is possible to obtain a detailed Gantt chart by specifying the following single statement:

```
PROC GANTT DATA= SAS-data-set ;
```

The data set specified is the Schedule data set produced by **PROC CPM**.

As an example of this, consider the software development project in the “Getting Started” section in Chapter 4, “[The CPM Procedure](#).“ The output schedule for this example is saved in a data set, INTRO1, which is displayed in Figure 8.1.

**Figure 8.1** Software Project Plan**Project Schedule**

Obs	activity	succesr1	succesr2	duration	descript
1	TESTING	RECODE		20	Initial Testing
2	PRELDOC	DOCEDREV QATEST		15	Prel. Documentation
3	MEETMKT	RECODE		1	Meet Marketing
4	RECODE	DOCEDREV QATEST		5	Recoding
5	QATEST	PROD		10	QA Test Approve
6	DOCEDREV	PROD		10	Doc. Edit and Revise
7	PROD			1	Production


  

Obs	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
1	01MAR04	20MAR04	01MAR04	20MAR04	0	0
2	01MAR04	15MAR04	11MAR04	25MAR04	10	10
3	01MAR04	01MAR04	20MAR04	20MAR04	19	19
4	21MAR04	25MAR04	21MAR04	25MAR04	0	0
5	26MAR04	04APR04	26MAR04	04APR04	0	0
6	26MAR04	04APR04	26MAR04	04APR04	0	0
7	05APR04	05APR04	05APR04	05APR04	0	0

The following code produces the Gantt chart shown in Figure 8.2.

```
title 'Line-Printer Gantt Chart';
proc gantt lineprinter data=intro1;
run;
```


The DATA= option could be omitted if the INTRO1 data set is the most recent data set created; by default, PROC GANTT uses the \_LAST\_ data set.

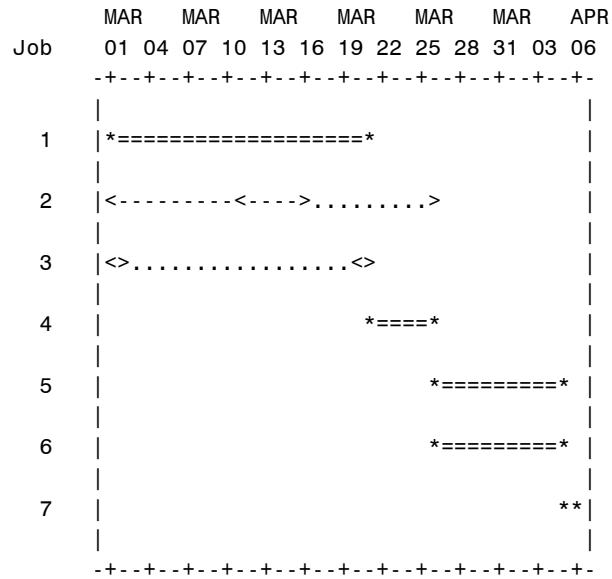**Figure 8.2** Line-Printer Gantt Chart**Line-Printer Gantt Chart****LEGEND**

Symbol	Explanation
<---->	Duration of a Normal Job
>....>	Slack Time for a Normal Job
*====*	Duration of a Critical Job


You can produce a high-resolution graphics quality Gantt chart by specifying the GRAPHICS option instead of the LINEPRINTER option in the PROC GANTT statement. Graphics mode is also the default display mode. The resulting Gantt chart is shown in Figure 8.3.

```
proc gantt graphics data=introl;
run;
```

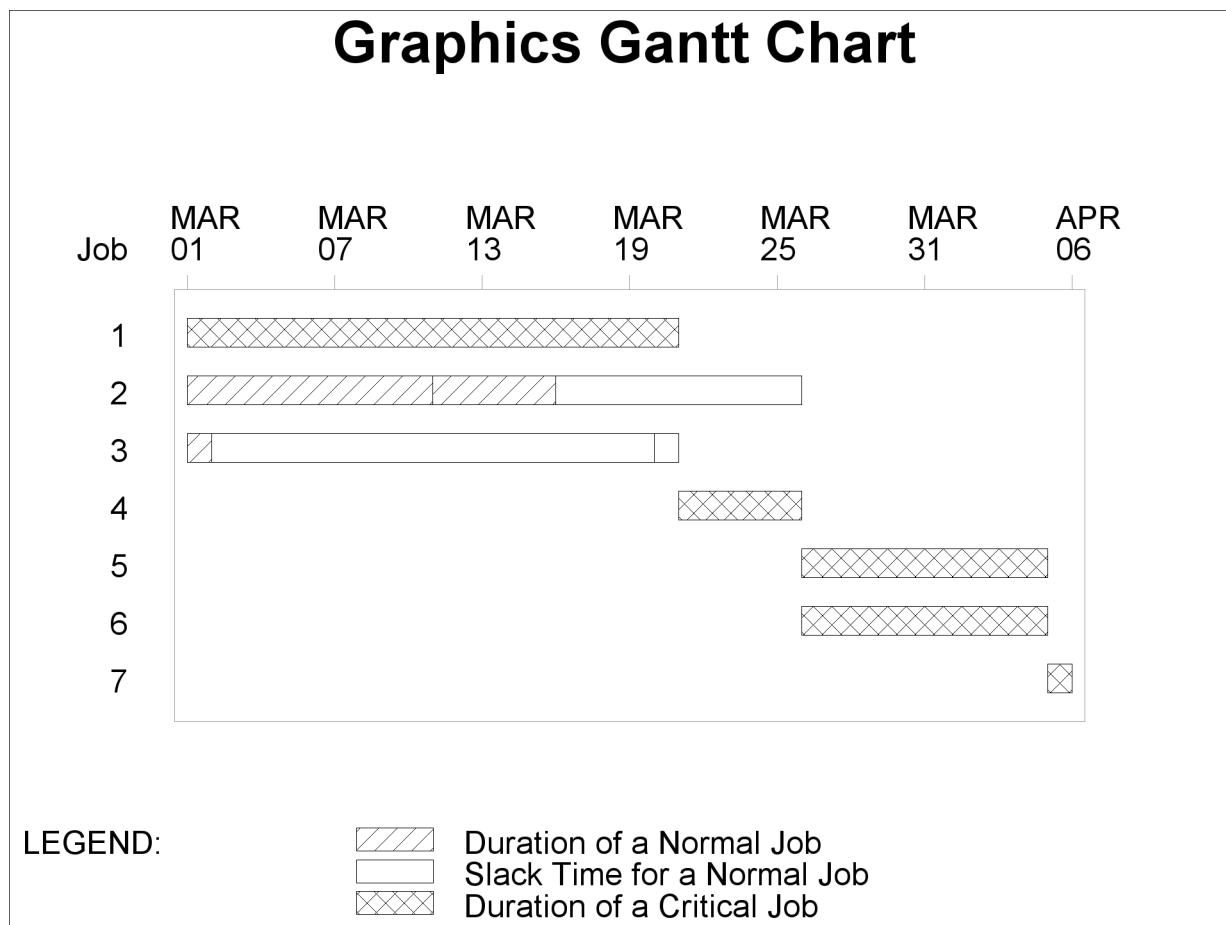**Figure 8.3** Graphics Gantt Chart

Finally, you can draw a Logic Gantt chart by defining the precedence information to PROC GANTT in AON format using the ACTIVITY= and SUCCESSOR= options in the CHART statement. The Logic Gantt chart is shown in Figure 8.4.

```
proc gantt data=introl;
  chart / activity=activity successor=(succesr1-succesr2);
run;
```

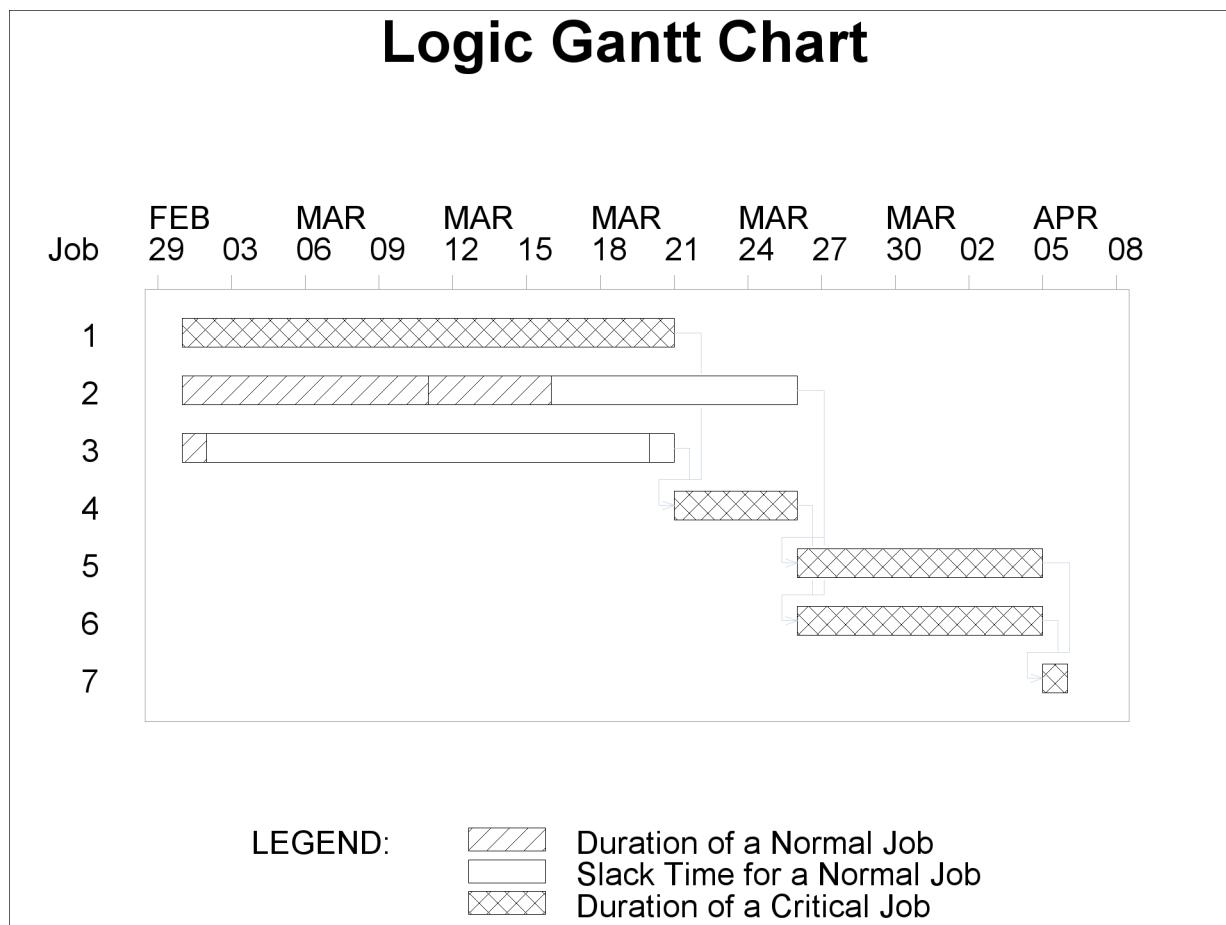**Figure 8.4** Logic Gantt Chart

For further examples illustrating typical invocations of the GANTT procedure when managing projects, see Chapter 3, “Introduction to Project Management.”

## Syntax: GANTT Procedure

The following statements are used in PROC GANTT:

```
PROC GANTT options ;
  BY variables ;
  CHART specifications / options ;
  ID variables ;
```

## Functional Summary

Table 8.1 outlines the options available for the GANTT procedure, classified by function.

**Table 8.1** Functional Summary

Description	Statement	Option
<b>Axis Formatting Options</b>		
Specifies the increment for labeling axis	CHART	INCREMENT=
Specifies the ending time for axis	CHART	MAXDATE=
Specifies the starting time for axis	CHART	MINDATE=
Specifies the smallest interval identified on chart	CHART	MININTERVAL=
Suppresses time portion of datetime tickmark	CHART	NOTMTIME
Specifies the number of columns per mininterval	CHART	SCALE=
Specifies the format of time axis labels	CHART	TIMEAXISFORMAT=
Uses first plot variable format for tickmarks	CHART	USEFORMAT
<b>Bar Enhancement Options</b>		
Specifies the actual bar height	CHART	ABARHT=
Specifies the actual bar offset	CHART	ABAROFF=
Specifies the default bar height	CHART	BARHT=
Specifies the default bar offset	CHART	BAROFF=
Specifies the baseline bar height	CHART	BBARHT=
Specifies the baseline bar offset	CHART	BBAROFF=
Specifies the color of connect line	CHART	CHCON=
Specifies the early/late bar height	CHART	EBARHT=
Specifies the early/late bar offset	CHART	EBAROFF=
Specifies the holiday bar height	CHART	HBARHT=
Specifies the holiday bar offset	CHART	HBAROFF=
Specifies the character for drawing connect line	CHART	HCONCHAR=
Draws a horizontal connect line	CHART	HCONNECT
Specifies the characters for drawing schedule	CHART	JOINCHAR=
Specifies the line style of connect line	CHART	LHCON=
Suppresses PATTERN variable for bar fills	CHART	NOPATBAR
Specifies the overprint character for schedule variables	CHART	OVERLAPCH=
Specifies the overprint character for CHART variables	CHART	OVPCHAR=
Specifies the schedule types that use the PATTERN variable	CHART	PATLEVEL=

**Table 8.1** *continued*

Description	Statement	Option
Specifies the PATTERN variable for bar fills and text color	CHART	PATTERN=
Specifies the resource bar height	CHART	RBARHT=
Specifies the resource bar offset	CHART	RBAROFF=
Specifies the characters for plotting times	CHART	SYMCHAR=
<b>Calendar Options</b>		
Specifies the calendar identifier	CHART	CALID=
Specifies the length of the workday	CHART	DAYLENGTH=
Specifies the beginning of the workday	CHART	DAYSTART=
Marks all breaks in a day	CHART	MARKBREAK
Marks all non-working days	CHART	MARKWKND
<b>Data Set Options</b>		
Specifies the Annotate data set	GANTT	ANNOTATE=
Specifies the Calendar data set	CHART	ANNOTATE=
Specifies the Schedule data set	GANTT	CALEDATA=
Specifies the Holiday data set	GANTT	DATA=
Specifies the Imagemap output data set	GANTT	IMAGEMAP=
Specifies the Label data set	GANTT	LABDATA=
Specifies the Precedence (Logic) data set	GANTT	PRECDATA=
Specifies the Work pattern data set	GANTT	WORKDATA=
<b>Graphics Catalog Options</b>		
Specifies the description of the catalog entry	CHART	DESCRIPTION=
Specifies the name of graphics catalog	GANTT	GOUT=
Specifies the name of catalog entry	CHART	NAME=
<b>Holiday Options</b>		
Specifies the character for plotting holidays	CHART	HOLICHAR=
Specifies the holiday start variable	CHART	HOLIDAY=
Specifies the holiday duration variable	CHART	HOLIDUR=
Specifies the holiday finish variable	CHART	HOLIFIN=
Specifies the holiday duration units	CHART	INTERVAL=
<b>ID Variable Options</b>		
Specifies the number of columns between ID variables	CHART	BETWEEN=
Marks critical activities	CHART	CRITFLAG
Specifies the activity text columns that use pattern color	CHART	CTEXTCOLS=
Allows duplicate ID values	CHART	DUPOK
Displays ID variables on every page	CHART	IDPAGES
Maximizes number of ID variables on page	CHART	MAXIDS
Suppresses job number	CHART	NOJOBNUM

**Table 8.1** *continued*

Description	Statement	Option
Specifies the split character for dividing ID labels	GANTT	SPLIT=
Strips leading blanks from character variables	GANTT	STRIPIDBLANKS
<b>Labeling Options</b>		
Specifies the label variable linking to Schedule data set	CHART	LABVAR=
Specifies the rules for label layout	CHART	LABRULE=
Specifies the split character for labels	CHART	LABSPLIT=
Specifies the maximum number of digits in integer label	GANTT	LABMAXINT=
<b>Logic Options</b>		
Specifies the activity variable for AON format	CHART	ACTIVITY=
Uses AOA precedence specifications	CHART	AOA
Specifies the color of precedence connections	CHART	CPREC=
Specifies the headnode variable for AOA format	CHART	HEAD=
Specifies the lag variable for AON format	CHART	LAG=
Specifies the schedule bar connected to precedence lines	CHART	LEVEL=
Specifies the line style of precedence connections	CHART	LPREC=
Specifies the maximum displacement of local vertical	CHART	MAXDISLV=
Specifies the minimum interdistance of global verticals	CHART	MININTGV=
Specifies the minimum offset of global vertical	CHART	MINOFFGV=
Specifies the minimum offset of local vertical	CHART	MINOFFLV=
Suppresses drawing arrow head	CHART	NOARROWHEAD
Suppresses automatic range extension	CHART	NOEXTRANGE
Terminates procedure if bad precedence data	CHART	SHOWPREC
Specifies the successor variable for AON format	CHART	SUCCESSOR=
Specifies the tailnode variable for AOA format	CHART	TAIL=
Specifies the width of precedence connections	CHART	WPREC=
<b>Milestone Options</b>		
Specifies the milestone color	CHART	CMILE=
Specifies the duration variable	CHART	DUR=
Specifies the font for the milestone symbol	CHART	FMILE=
Specifies the milestone height	CHART	HMILE=
Specifies the milestone character	CHART	MILECHAR=
Specifies the value for the milestone symbol	CHART	VMILE=
<b>Miscellaneous Options</b>		
Invokes full-screen version	GANTT	FS
Invokes graphics version	GANTT	GRAPHICS
Invokes line-printer version	GANTT	LP
Specifies the maximum number of decimals for a number	GANTT	MAXDEC=
Specifies the unit for padding finish times	CHART	PADDING=
Specifies the upper limit on number of pages	CHART	PAGES=
Displays summary of symbols and patterns	CHART	SUMMARY

**Table 8.1** *continued*

Description	Statement	Option
<b>Page Layout Options</b>		
Positions chart at bottom of page	CHART	BOTTOM
Specifies the axis color	CHART	CAXIS=
Specifies the frame fill color	CHART	CFRAME=
Specifies the width of the chart axis area	CHART	CHARTWIDTH=
Draws chart on one page in graphics mode	CHART	COMPRESS
Fills each page as much as possible	CHART	FILL
Specifies the characters for table outlines and dividers	CHART	FORMCHAR=
Specifies the number of pages spanning time axis	CHART	HPAGES=
Left justifies chart	CHART	LEFT
Specifies the line width	CHART	LWIDTH=
Specifies the number of activities on each page	CHART	NJOBS=
Suppresses frame	CHART	NOFRAME
Suppresses legend	CHART	NOLEGEND
Suppresses page number at upper right corner	CHART	NOPAGENUM
Specifies the number of tickmarks on each page	CHART	NTICKS=
Displays page number at upper right corner	CHART	PAGENUM
Draws chart proportionally on one page	CHART	PCOMPRESS
Right justifies chart	CHART	RIGHT
Specifies the number of rows between consecutive activities	CHART	SKIP=
Positions chart at top of page	CHART	TOP
Specifies the number of pages spanning activity axis	CHART	VPAGES=
<b>Reference Line Options</b>		
Specifies the reference line color	CHART	CREF=
Specifies the reference line style	CHART	LREF=
Specifies the placement of the reference lines	CHART	REF=
Specifies the reference line character	CHART	REFCHAR=
Specifies that reference lines should be labeled	CHART	REFLABEL
<b>Schedule Selection Options</b>		
Specifies the actual start variable	CHART	A_START=
Specifies the actual finish variable	CHART	A_FINISH=
Specifies the baseline start variable	CHART	B_START=
Specifies the baseline finish variable	CHART	B_FINISH=
Concatenates early/late and actual schedules	CHART	COMBINE
Specifies the early start variable	CHART	E_START=
Specifies the early finish variable	CHART	E_FINISH=
Specifies the late start variable	CHART	L_START=
Specifies the late finish variable	CHART	L_FINISH=
Specifies the resource-constrained start variable	CHART	S_START=
Specifies the resource-constrained finish variable	CHART	S_FINISH=

**Table 8.1** *continued*

Description	Statement	Option
<b>Timenow Line Options</b>		
Specifies the timenow line color	CHART	CTNOW=
Specifies the timenow line style	CHART	LTNOW=
Suppresses the timenow label	CHART	NOTNLABEL
Specifies the placement of the timenow line	CHART	TIMENOW=
Specifies the timenow line character	CHART	TNCHAR=
Specifies the timenow line width	CHART	WTNOW=
<b>Text Formatting Options</b>		
Specifies the text color	CHART	CTEXT=
Specifies the text font	CHART	FONT=
Specifies the text height multiplier	CHART	HEIGHT=
Specifies the vertical offset for the activity text	CHART	HTOFF=
<b>Web Options</b>		
Specifies the Imagemap output data set	GANTT	IMAGEMAP=
Specifies the HTML variable	CHART	WEB=
<b>Zone Options</b>		
Specifies the zone line color	CHART	CZONE=
Specifies the zone line style	CHART	LZONE=
Suppresses the zone column	CHART	NOZONECOL
Displays only new zone values	CHART	ONEZONEVAL
Specifies the zone line width	CHART	WZONE=
Specifies the zone variable	CHART	ZONE=
Specifies the zone line offset	CHART	ZONEOFF=
Specifies the zone line span	CHART	ZONESPAN=

---

## PROC GANTT Statement

**PROC GANTT** *options* ;

The following options can appear in the PROC GANTT statement.

**ANNOTATE=SAS-data-set**

**ANNO=SAS-data-set**

specifies the input data set that contains the appropriate Annotate variables for the purpose of adding text and graphics to the Gantt chart. The data set specified must be an Annotate-type data set. See the section “[Annotate Processing](#)” on page 537 for information specifically on annotate processing with the GANTT procedure.

The data set specified with the ANNOTATE= option in the PROC GANTT statement is a “global” ANNOTATE= data set, in the sense that the information in this data set is displayed on every Gantt

chart produced in the current invocation of PROC GANTT. This option is available only in graphics mode.

See [Example 8.21, “Using the SAS/GGRAPH ANNOTATE= Option,”](#) for further illustration of this option.

#### **CALEDATA=SAS-data-set**

#### **CALENDAR=SAS-data-set**

identifies a SAS data set that specifies the work pattern during a standard week for *each* of the calendars that is to be used in the project. Each observation of this data set (also referred to as the Calendar data set) contains the name or the number of the calendar being defined in that observation, the names of the shifts or work patterns used each day, and, optionally, a standard workday length in hours. For details on the structure of this data set, see the section [“Multiple Calendars and Holidays”](#) on page 530. The work shifts referred to in the CALEDATA data set are defined in the WORKDATA data set.

#### **DATA=SAS-data-set**

names the SAS data set that carries the schedule information to be used by PROC GANTT. If the DATA= option is omitted, the most recently created SAS data set is used. This data set, also known as the Schedule data set, contains all the time variables (early, late, actual, resource-constrained, and baseline start and finish times, and any other variables to be specified in a CHART statement) that are to be plotted on the chart. For projects that use [multiple calendars](#), this data set also identifies the calendar that is used by each activity. The Schedule data set also contains precedence information when drawing a Logic Gantt chart in graphics mode. See the section [“Schedule Data Set”](#) on page 525 for more details.

#### **FULLSCREEN**

#### **FS**

indicates that the Gantt chart be drawn in full-screen mode. This mode enables you to scroll horizontally and vertically through the output using commands, pull-down menus, or function keys. See the section [“Full-Screen Version”](#) on page 531 for more information.

#### **GOUT=graphics catalog**

specifies the name of the graphics catalog used to save the output produced by PROC GANTT for later replay. This option is available only in graphics mode.

#### **GRAPHICS**

indicates that the Gantt chart produced be of high-resolution quality. This is the default mode of display. If you invoke the GANTT procedure in Graphics mode, but you do not have SAS/GGRAPH software licensed at your site, the procedure stops and issues an error message. See the section [“Graphics Version”](#) on page 535 for more information.

#### **HOLIDATA=SAS-data-set**

names the SAS data set that specifies holidays. These holidays can be associated with specific calendars that are also identified in the HOLIDATA data set (also referred to as the Holiday data set). The HOLIDATA= option must be used with the HOLIDAY= option in the CHART statement, which specifies the variable in the SAS data set that contains the start time of holidays. Optionally, the data set can include a variable that specifies the length of each holiday or a variable that identifies the finish time of each holiday (if the holidays are longer than one unit of the INTERVAL= option). For projects involving [multiple calendars](#), this data set can also include the variable named by the CALID= option that identifies the calendar to be associated with each holiday.

**IMAGEMAP=SAS-data-set**

names the SAS data set that receives a description of the areas of a graph and a link for each area. This information is for the construction of HTML image maps. You use a SAS DATA step to process the output file and generate your own HTML files. The graph areas correspond to the link information that comes from the **WEB** variable in the schedule data set. This gives you complete control over the appearance and structure of your HTML pages.

**LABDATA=SAS-data-set****LABELDATA=SAS-data-set****LABEL=SAS-data-set**

specifies the input data set that contains the label specific information. This option is required to initiate the **automatic text annotation** of the Gantt chart. See the section “**Label Data Set**” on page 553 for information on the variables it can contain. This option is available only in graphics mode.

**LABMAXINT=n****LMI=n**

specifies the maximum number of digits in the integer part when displaying an unformatted numeric as a string. The default value is 16. The maximum number of decimal positions is specified using the **MAXDEC=** option in the **PROC GANTT** statement. This option is applicable only to labels defined with the Label data set.

**LINEPRINTER****LP**

indicates that the Gantt chart be drawn in line-printer mode.

**MAXDEC=n****M=n**

indicates the maximum number of decimal positions displayed for a number. A decimal specification in a format overrides a MAXDEC= specification. The default value of MAXDEC= is 2.

**PRECDATA=SAS-data-set**

names the SAS data set that contains the variables that define the precedence constraints in **AON** format. This data set is required if the **Schedule data set** does not contain the required precedence information as, for example, when the **COLLAPSE** option in **PROC CPM** causes some observations to be excluded from the Schedule data set. When this option is specified, it is mandatory that the **ACTIVITY** variable exist in both data sets and be identical in both type and length. This option is available only in graphics mode.

**SPLIT='character'****S='character'**

splits labels used as column headings where the split character appears. When you define the value of the split character, you must enclose it in single quotes. In PROC GANTT, column headings for **ID** variables consist of either variable labels (if they are present and space permits) or variable names. If the variable label is used as the column heading, then the split character determines where the column heading is to be split.

**WORKDATA=SAS-data-set**

**WORKDAY=SAS-data-set**

identifies a SAS data set that defines the work pattern during a standard working day. Each numeric variable in this data set (also referred to as the Workday data set) is assumed to denote a unique shift pattern during one working day. The variables must be formatted as SAS time values, and the observations are assumed to specify, alternately, the times when consecutive shifts start and end.

## BY Statement

**BY** *variables* ;

A BY statement can be used with PROC GANTT to obtain separate Gantt charts for observations in groups defined by the BY variables. When a BY statement appears, the procedure expects the schedule data to be sorted in order of the BY variables. If your Schedule data set is not sorted, use the SORT procedure with a similar BY statement to sort the data. The chart for each BY group is formatted separately based only on the observations within that group.

## CHART Statement

**CHART** *specifications / options* ;

The options that can appear in the CHART statement are listed below. The options are classified under appropriate headings: first, all options that are valid for all modes of the procedure are listed, followed by the options classified according to the mode (line-printer, full-screen, or graphics) of invocation of the procedure. Most of the options in line-printer and full-screen modes are also valid in graphics mode with similar interpretations. The differences and similarities in interpretation of the options are documented under the section “Mode-Specific Differences” on page 557.

### General Options

The CHART statement controls the format of the Gantt chart and specifies additional variables (other than early, late, actual, resource-constrained, and baseline start and finish times) to be plotted on the chart. For example, suppose a variable that you want to specify in the CHART statement is one that contains the target finish date for each activity in a project; that is, if FDATE is a variable in the Schedule data set containing the desired finish date for each activity, the CHART statement can be used to mark the value of FDATE on the chart for each activity. A CHART specification can be one of the following types:

*variable\_1 ... variable\_n*

*variable\_1='symbol\_1' ... variable\_n='symbol\_n'*

*(variables)=symbol\_1 ... (variables)=symbol\_n'*

*variable\_1 ... variable\_n*

indicates that each variable is to be plotted using the default symbol, the first character of the variable name. For example, the following statement

**CHART SDATE FDATE;**

causes the values of SDATE to be plotted with an ‘S’ and the values of FDATE with an ‘F’.

**variable\_1='symbol\_1' ... variable\_n='symbol\_n'**

indicates that each variable is to be plotted using the symbol specified. The symbol must be a single character enclosed in quotes.

**(variables)='symbol\_1' ... (variables)='symbol\_n'**

indicates that each variable within the parentheses is to be plotted using the symbol associated with that group. The symbol must be a single character enclosed in single quotes. For example, the following statement

```
CHART (ED SD)='*'  
(FD LD)='+';
```

plots the values of the variables in the first group using an asterisk (\*) and the values of the variables in the second group using a plus sign (+).

A single CHART statement can contain specifications in more than one of these forms. Also, each CHART statement produces a separate Gantt chart.

**NOTE:** It is not necessary to specify a CHART statement if default values are to be used to draw the Gantt chart.

The following options can appear in the CHART statement.

**A\_FINISH=variable**

**AF=variable**

specifies the variable that contains the actual finish time of each activity in the [Schedule data set](#). This option is not required if the default variable name A\_FINISH is used.

**A\_START=variable**

**AS=variable**

specifies the variable that contains the actual start time of each activity in the [Schedule data set](#). This option is not required if the default variable name A\_START is used.

**B\_FINISH=variable**

**BF=variable**

specifies the variable that contains the baseline finish time of each activity in the [Schedule data set](#). This option is not required if the default variable name B\_FINISH is used.

**B\_START=variable**

**BS=variable**

specifies the variable that contains the baseline start time of each activity in the [Schedule data set](#). This option is not required if the default variable name B\_START is used.

**BETWEEN=number**

specifies the number of columns between two consecutive [ID](#) variable columns. This option gives you greater flexibility in spacing the ID columns. The default value of the BETWEEN= option is 3.

**CALID=variable**

specifies the variable in the [Schedule](#), [Holiday](#), and [Calendar](#) data sets that is used to identify the name or number of the calendar to which each observation refers. This variable can be either numeric or character depending on whether the different calendars are identified by unique numbers or names, respectively. If this variable is not found in any of the three data sets, PROC GANTT looks for a default variable named \_CAL\_ in that data set (a warning message is issued to the log). For each activity in the [Schedule data set](#), this variable identifies the calendar that is used to mark the appropriate holidays and weekends for the activity. For further details, see the section “[Multiple Calendars and Holidays](#)” on page 530.

**COMBINE**

concatenates the early/late and actual schedule bars of an activity into a single bar and draws a timenow line on the Gantt chart. The COMBINE option does not affect the resource-constrained or baseline schedule bars. If the [TIMENOW=](#) option is not specified, it is implicitly assumed to exist and set to missing. The computation of TIMENOW is then carried out as described in the [TIMENOW=](#) option. Since the timenow line represents the instant at which a “snapshot” of the project is taken, values less than TIMENOW can be regarded as the “past” and values greater or equal to TIMENOW can be regarded as the “future.” The GANTT procedure uses this property of the timenow line to partition the chart into two regions; the region to the left of the timenow line reporting only the actual schedule (events that have already taken place), and the region to the right (including the timenow line) reporting only the predicted early/late schedule.

**CRITFLAG****FLAG**

indicates that critical jobs be flagged as being critical or super-critical. An activity is critical if its total float is zero. If the total float is negative, the activity is super-critical. Critical activities are marked ‘CR,’ and super-critical activities are marked ‘SC’ on the left side of the chart.

**DAYLENGTH=daylength**

specifies the length of the workday. Each workday is plotted starting at the beginning of the day as specified in the [DAYSTART=](#) option and ending *daylength* hours later. The value of *daylength* should be a SAS time value. If the [INTERVAL=](#) option is specified as DTSECOND, DTMINUTE, DTHOUR, or DTDAY, the default value of *daylength* is 24 hours. If the [INTERVAL=](#) option is specified as WORKDAY or DTWRKDAY, the default value of *daylength* is 8 hours. For other values of the [INTERVAL=](#) option, the DAYLENGTH= option is ignored.

**NOTE:** The DAYLENGTH= option is needed to mark the non-worked periods within a day correctly (if the [MARKBREAK](#) option is in effect). The DAYLENGTH= option is also used to determine the start and end of a weekend precisely (to the nearest second). This accuracy is needed if you want to depict on a Gantt chart the exact time (for example, to within the nearest hour) for the start and finish of holidays or weekends. This option is used only if the times being plotted are SAS datetime values.

**DAYSTART=daystart**

specifies the start of the workday. The end of the day, *dayend*, is computed as *daylength* seconds after *daystart*. The value of *daystart* should be a SAS time value. This option is to be specified only when the value of the [INTERVAL=](#) option is one of the following: WORKDAY, DTSECOND, DTMINUTE, DTHOUR, DT DAY, or DTWRKDAY. For purposes of denoting on the Gantt chart, the weekend is assumed to start at *dayend* on Friday and end at *daystart* on Monday morning. Of course, if the [SCALE=](#) and [MININTERVAL=](#) values are such that the resolution is not very high, you will be unable

to discern the start and end of holidays and weekends to the nearest hour. The default value of *daystart* is 9:00 a.m. if INTERVAL=WORKDAY or INTERVAL=DTWRKDAY, and midnight otherwise.

#### **DUPOK**

causes duplicate values of ID variables *not to be skipped*. As described later in the [ID Statement](#) section, if two or more consecutive observations have the same combination of values for all the ID variables, only the first of these observations is plotted. The DUPOK option overrides this behavior and causes *all* the observations to be plotted.

#### **DURATION=variable**

##### **DUR=variable**

identifies a variable in the [Schedule data set](#) that determines whether or not an activity is to be regarded as a milestone with respect to a specific schedule. This option is not required if the default variable name *\_DUR\_* is used. A value of 0 for this variable indicates that if the start and finish times of the activity with respect to a given schedule are identical (a schedule taken to mean early, late, actual, resource-constrained or baseline), then the activity is represented by a milestone with respect to the given schedule. A nonzero value treats identical start and finish times in the default manner by implicitly padding the finish times as specified by the [PADDING=](#) option. The milestone symbol is defined by the [MILECHAR=](#) option in line-printer and full-screen modes and by the [CMILE=](#), [FMILE=](#), [HMILE=](#), and [VMILE=](#) options in graphics mode; these four options represent the color, font, height, and value of the symbol, respectively. See the descriptions of these options for their default values. To illustrate, suppose that the observations for activities **A** and **B** from the Schedule data set are as follows:

ACTIVITY	E_START	E_FINISH	A_START	A_FINISH	_DUR_
<b>A</b>	27JUL04	27JUL04	31JUL04	31JUL04	1
<b>B</b>	31JUL04	31JUL04	01AUG04	02AUG04	0

In this example, the actual schedule for activity **A** begins on ‘31JUL04’ and finishes at the end of the day, as explained in the section “[Schedule Data Set](#)” on page 525. PROC GANTT uses the *\_DUR\_* variable to recognize that activity **A** has nonzero duration, pads the finish time by a PADDING= unit, and displays a bar representing one day. In contrast, the value of ‘0’ for *\_DUR\_* in activity **A** alerts PROC GANTT that padding be ignored for any schedule with identical start and finish times. Consequently, the early schedule for activity **B** is represented on the chart by the milestone symbol at ‘31JUL04.’ The actual schedule, however, not having identical start and finish times, is padded as usual and plotted as starting on ‘01AUG04’ and finishing at the end of ‘02AUG04.’

#### **E\_FINISH=variable**

##### **EF=variable**

specifies the variable that contains the early finish time of each activity in the [Schedule data set](#). This option is not required if the default variable name E\_FINISH is used.

#### **E\_START=variable**

##### **ES=variable**

specifies the variable that contains the early start time of each activity in the [Schedule data set](#). This option is not required if the default variable name E\_START is used.

**FILL**

causes each page of the Gantt chart to be filled as completely as possible before a new page is started (when the size of the project requires the Gantt chart to be split across several pages). If the FILL option is not specified, the pages are constrained to contain an approximately equal number of activities. The FILL option is not valid in full-screen mode because all of the activities are plotted on one logical page.

**HCONNECT**

causes a line to be drawn for each activity from the left boundary of the chart to the beginning of the bar for the activity. This feature is particularly useful when the Gantt chart is drawn on a large page. In this case, the schedule bars for some of the activities may not start close enough to the left boundary of the chart; the connecting lines help to identify the activity associated with each bar.

**HOLIDAY=(variable)****HOLIDAYS=(variable)**

specifies the date or datetime variable in the **Holiday** data set that identifies holidays to be marked on the schedule. If there is no end time nor duration specified for the holiday, it is assumed to start at the time specified by the HOLIDAY variable and last one unit of *interval*, where *interval* is the value of the **INTERVAL=** option.

**HOLIDUR=(variable)****HDURATION=(variable)**

specifies the variable in the **Holiday** data set that identifies the durations of the holidays that are to be marked on the schedule.

**HOLIFIN=(variable)****HOLIEND=(variable)**

specifies the date or datetime variable in the **Holiday** data set that identifies the finish times of the holidays that are to be marked on the schedule.

**IDPAGES**

displays ID variables on every page. By default, the ID variables are displayed only on the first page.

**INCREMENT=increment**

specifies the number of *minintervals* between time axis labels on the Gantt chart. If the INCREMENT= option is not specified, a value is chosen that provides the maximum possible labeling.

**INTERVAL=interval****HOLINTERVAL=interval**

specifies the units for the values of the HOLIDUR variables. Valid values for this option are DAY, WEEKDAY, WORKDAY, DTSECOND, DTMINUTE, DT HOUR, DTDAY, or DTWRKDAY. If the value for the INTERVAL= option has been specified as WEEKDAY, WORKDAY, or DTWRKDAY, weekends are also marked on the Gantt chart with the same symbol as holidays for line-printer quality charts. Graphics-quality Gantt charts use the same PATTERN statement as the one used for marking holidays. The default value of the INTERVAL= option is DAY if the times being plotted are SAS date values and is DTDAY if the times being plotted are SAS datetime values. See the section “[Specifying the INTERVAL= Option](#)” on page 531 for further information regarding this option.

**L\_FINISH=variable****LF=variable**

specifies the variable that contains the late finish time of each activity in the **Schedule** data set. This option is not required if the default variable name L\_FINISH is used.

**L\_START=variable****LS=variable**

specifies the variable that contains the late start time of each activity in the **Schedule** data set. This option is not required if the default variable name L\_START is used.

**MARKBREAK**

causes all breaks (non-worked periods) during a day to be marked on the Gantt chart. The symbol used for marking the breaks is the same as the **HOLICCHAR=** symbol. This option may not be of much use unless the chart has been plotted with a scale that enables you to discern the different hours within a day on the Gantt chart. For instance, if the chart is in terms of days, there is no point in trying to show the breaks within a day; on the other hand, if it is in terms of hours or seconds, you may want to see the start and end of the various shifts within a day. This option turns on the **MARKWKND** option.

**MARKWKND**

causes all weekends (or non-worked days during a week) to be marked on the Gantt chart. The symbol used for marking weekends is the same as the **HOLICCHAR=** symbol. Note that weekends are also marked on the chart if the value of the **INTERVAL=** option is WEEKDAY, WORKDAY, or DTWRKDAY.

**MAXDATE=maxdate**

specifies the end time for the time axis of the chart. The default value is the largest value of the times being plotted unless the logic options are invoked without the **NOEXTRANGE** option in the **CHART** statement. For a discussion of the default behavior in this instance, see the section “[Formatting the Axis](#)” on page 548.

**MAXIDS**

displays as many consecutive **ID** variables as possible in the presence of an **ID** statement. In the absence of this option, the default displays *all* of the variables or *none* if this is not possible.

**MINDATE=mindate**

specifies the starting time for the time axis of the chart. The default value is the smallest value of the times being plotted unless the logic options are invoked without the **NOEXTRANGE** option in the **CHART** statement. For a discussion of the default behavior in this instance, see the section “[Formatting the Axis](#)” on page 548.

**MININTERVAL=mininterval**

specifies the smallest interval to be identified on the chart. For example, if MININTERVAL=DAY, then one day is represented on the chart by *scale* (see the **SCALE=** option) number of columns. The default value of the **MININTERVAL=** option is chosen on the basis of the formats of the times being plotted, as explained in the section “[Specifying the MININTERVAL= Option](#)” on page 529. See also the section “[Page Format](#)” on page 528 for a further explanation of how to use the **MININTERVAL=** option in conjunction with the **SCALE=** option.

**NOJOBNUM**

suppresses displaying an identifying job number for each activity. By default, the job number is displayed to the left of the Gantt chart.

**NOLEGEND**

suppresses displaying the concise default legend at the bottom of each page of the Gantt chart. The NOLEGEND option is not effective in full-screen mode.

**NOTNLABEL**

suppresses displaying the timenow label. By default, the label is displayed on the bottom border of the chart.

**PADDING=padding****FINPAD=padding**

requests that finish times on the chart be increased by one *padding* unit. An exception to this is when a milestone is to be plotted. See the **DUR=** option for further information regarding this. The PADDING= option enables the procedure to mark the finish times as the end of the last time period instead of the beginning. Possible values for *padding* are NONE, SECOND, MINUTE, HOUR, DAY, WEEK, MONTH, QTR, YEAR, DTSECOND, DTMINUTE, DTHOUR, DTWEEK, DTMONTH, DTQTR, or DTYEAR. The default value is chosen on the basis of the format of the times being plotted. See the section “Specifying the PADDING= Option” on page 528 for further explanation of this option.

**PAGELIMIT=pages****PAGES=pages**

specifies an upper limit on the number of pages allowed for the Gantt chart. The default value of *pages* is 100. This option is useful for preventing a voluminous amount of output from being generated by a wrong specification of the **MININTERVAL=** or **SCALE=** option. This option is ignored in full-screen mode.

**REF=values**

indicates the position of one or more vertical reference lines on the Gantt chart. The values allowed are constant values. Only those reference lines that fall within the scope of the chart are displayed.

In line-printer and full-screen modes, the reference lines are displayed using the character specified in the **REFCHAR=** option. In graphics mode, use the **CREF=**, **LREF=**, and **LWIDTH=** options to specify the color, style, and width of the reference lines.

**REFLABEL**

specifies that the reference lines are to be labeled. The labels are formatted in the same way as the time axis labels and are placed along the bottom border of the Gantt chart at the appropriate points. If the reference lines are too numerous and the scale does not allow all the labels to be nonoverlapping, then some of the labels are dropped.

**S\_FINISH=variable****SF=variable**

specifies the variable that contains the resource-constrained finish time of each activity in the **Schedule** data set. This option is not required if the default variable name S\_FINISH is used.

**S\_START=variable****SS=variable**

specifies the variable that contains the resource-constrained start time of each activity in the [Schedule data set](#). This option is not required if the default variable name S\_START is used.

**SCALE=scale**

requests that *scale* number of columns on the chart represent one unit of *mininterval* where *mininterval* is the value of the [MININTERVAL=](#) option. In line-printer and graphics modes, the default value of the SCALE= option is 1 if the time axis of the chart is too wide to fit on one page. If the time axis fits on less than one page, then a default value is chosen that expands the time axis as much as possible but still fits the time axis on one page. In full-screen mode, the default value of the SCALE= option is always 1.

**SKIP=skip****S=skip**

requests that *skip* number of lines be skipped between the plots of the schedules of two activities. The SKIP= option can take integer values between 0 and 4, inclusive. In graphics mode, 0 is not a valid value. The default value of the SKIP= option is 1.

**STRIPIDBLANKS****STRIPID**

strips all leading blanks from character ID variables. The default behavior is to preserve any leading blanks.

**SUMMARY**

requests that a detailed description of all symbols and patterns that are used in the Gantt chart be displayed before the first page of the chart. In line-printer mode, this description includes examples of some strings that could occur in the body of the Gantt chart. The SUMMARY option is not supported in full-screen mode.

**TIMEAXISFORMAT=format|(format\_1 <..., format\_3>)****TAFORMAT=format|(format\_1 <..., format\_3>)**

specifies formats for up to three rows of time-axis labeling. One time-axis row is displayed for each format specified. The formats control the rows of the time-axis from top to bottom. Missing formats yield a blank row.

**TIMENOW=value**

specifies the position for the timenow line on the chart. If the value is invalid or set to missing, TIMENOW is set to be the time period that follows the maximum of all specified actual times. If there are no actual times, TIMENOW is set to be equal to the current date. The value of TIMENOW is written to the log.

The timenow line has precedence over all other variables and reference lines and is drawn only if it falls within the range of the chart axis. If TIMENOW is based on the maximum of the actual times, and the [MAXDATE=](#) option is not specified, then the range of the chart axis is increased, if necessary, to display the timenow line. The timenow line is labeled by default; the label is formatted in the same way as the time axis and is placed along the bottom border of the chart. The timenow line is displayed in line-printer and full-screen modes using the character specified by the [TNCHAR=](#) option (or **T**, if none is specified) in the [CHART](#) statement. In graphics mode, use the **CTNOW=**, **LTNOW=**, and

**WTNOW=** options in the CHART statement to specify the color, style, and width of the timenow line. In the presence of a timenow line, the actual schedule for an activity with an actual start less than TIMENOW and a missing actual finish time is represented on the Gantt chart by a bar that begins at the actual start and ends at TIMENOW to indicate that the activity is in progress at TIMENOW. This behavior is consistent with the convention used by PROC CPM. A warning is also issued to the log in this case.

#### USEFORMAT

specifies that the tickmark labels of the Gantt chart axis are to be displayed using the format associated with the first plot variable appearing in the order **E\_START=**, **E\_FINISH=**, **L\_START=**, **L\_FINISH=**, **A\_START=**, **A\_FINISH=**, **S\_START=**, **S\_FINISH=**, **B\_START=**, **B\_FINISH=**. This format is also used for labeling any reference lines and the timenow line.

**NOTE:** An INFORMAT statement might be necessary to identify user-defined formats. This enables the GANTT procedure to recognize the data type of the start and finish times specified in the input data set.

### Full-Screen and Line-Printer Options

The following options can appear in the CHART statement and are specifically for the purpose of producing Gantt charts in line-printer and full-screen modes.

#### FORMCHAR[ *index list* ]='string'

defines the characters to be used for constructing the chart outlines and dividers. The value is an 11-character string: the first character represents the vertical bar, the second character represents the horizontal bar, and the remaining characters represent the upper left, upper middle, upper right, middle left, middle middle (cross), middle right, lower left, lower middle, and lower right, respectively. The default value of the FORMCHAR= option is ' |----|+|---'. You can substitute any character or hexadecimal string to customize the chart appearance. Use an index list to specify which default form character each supplied character replaces, or replace the entire default string by specifying the full 11 character replacement string with no index list. For example, change the four corners to asterisks by using

```
formchar(3 5 9 11) = '****'
```

Specifying the following produces charts with no outlines or dividers.

```
formchar= '           ' (11 blanks)
```

If you route your output to an IBM 6670 printer that uses an extended font (typestyle 27 or 225) with input character set 216, it is recommended that you specify

```
formchar= 'FABFACCCBCEB8FECABCBBB'X
```

If you use a printer with a TN (text) print train, it is recommended that you specify the following:

```
formchar= '4FBFACBFBC4F8F4FABBFB'X
```

**HCONCHAR=**'character'

specifies the symbol to be used for drawing the connecting line described in the **HCONNECT** option. The default character is -. This is a line-printer option and is not valid in conjunction with the **GRAPHICS** option. For corresponding graphics options, see the **LHCON=** and **CHCON=** options described later in this section under “Graphics Options.”

**HOLICCHAR=**'character'

indicates the character to display for holidays. Note that PROC GANTT displays only those holidays that fall within the duration or the slack time of an activity. The default character used for representing holidays is !.

**JOINCHAR=**'string'

defines a string eight characters long that identifies nonblank characters to be used for drawing the schedule. The first two symbols are used to plot the schedule of an activity with positive total float. The first symbol denotes the duration of such an activity while the second symbol denotes the slack present in the activity’s schedule. The third symbol is used to plot the duration of a *critical* activity (with zero total float). The next two symbols are used to plot the schedule of a *supercritical* activity (one with negative float). Thus, the fourth symbol is used to plot the negative slack of such an activity starting from the late start time (to early start time), and the fifth symbol is used to plot the duration of the activity (from early start to early finish). The sixth symbol is used to plot the actual schedule of an activity if the **A\_START** and **A\_FINISH** variables are specified. The seventh symbol is used to plot the resource-constrained schedule of an activity if the **S\_START** and **S\_FINISH** variables are specified. The eighth symbol is used to plot the baseline schedule of an activity if the **B\_START** and **B\_FINISH** variables are specified. The default value of the **JOINCHAR=** option is '-.=--\*-\*-'.

**MILECHAR=**'character'

indicates the character to display for the milestone symbol. If this option is not used, the letter **M** is used. In the event that another milestone or a character representing a start or finish time is to be plotted in this column, the **OVERLAPCH=** character is used.

**OVERLAPCH=**'character'**OVLPCHAR=**'character'

indicates the overprint character to be displayed when more than one of the symbols in **SYM-CHAR=**'string' or **MILECHAR=**'character' are to be plotted in the same column. The default character is \*.

**OVPCHAR=**'character'

indicates the character to be displayed if one of the variables specified in the **CHART** statement is to be plotted in the same column as one of the start or finish times. If no **OVPCHAR=** option is given, the ‘at’ symbol (@) is used. Note that if one of the **E\_START**, **E\_FINISH**, **L\_START**, **L\_FINISH**, **A\_START**, **A\_FINISH**, **S\_START**, **S\_FINISH**, **B\_START**, or **B\_FINISH** times coincides with another, the overprint character to be displayed can be specified separately using the **OVERLAPCH=** option.

**REFCHAR=**'character'

indicates the character to display for reference lines. If no **REFCHAR=** option is given, the vertical bar (|) is used. If a time variable value is to be displayed in the column where a **REF=** value goes, the plotting symbol for the time variable is displayed instead of the **REFCHAR=** value. Similarly, the **HOLICCHAR=** symbol has precedence over the **REFCHAR=** value.

**SYMCHAR=**'string'

defines the symbols to be used for plotting the early start, late start, early finish, late finish, actual start and finish, resource-constrained start and finish, and baseline start and finish times, in that order. The default value is '<>>\*<>[]'. If any of the preceding symbols coincide with one another or with the milestone symbol, the symbol plotted is the one specified in the **OVERLAPCH=** option (or \*, if none is specified). If the actual, resource-constrained, and baseline schedules are not plotted on the chart, you can specify only the first four symbols. If fewer than the required number of symbols are specified, nonspecified symbols are obtained from the default string.

**TNCHAR=**'character'

indicates the character to display for the timenow line. If this option is not used, the letter **T** is used.

## Graphics Options

The following describes the interpretation of the CHART specification in graphics mode. Note that the GANTT procedure is not supported with the ActiveX or Java series of devices on the GOPTIONS statement.

As before, the CHART statement controls the format of the Gantt chart and specifies additional variables (other than the early, late, actual, resource-constrained, and baseline start and finish times) to be plotted on the chart. The same forms for the specification of CHART variables (as in the line-printer and full-screen version) are allowed, although the interpretation is somewhat different. Each form of specification is repeated here with a corresponding description of the interpretation. Note that the symbols for any activity are plotted on a line above the one corresponding to that activity. In addition to plotting the required symbol, PROC GANTT draws a vertical line below the symbol in the same color as the symbol. The length of the line is the same as the height of the bars (referred to as bar height) that represent the durations of the activities on the Gantt chart. This line helps identify the exact position of the plotted value. See also the section “[Special Fonts for Project Management and Decision Analysis](#)” on page 543 for information on a special set of symbols that are suitable for representing CHART variables on a Gantt chart.

*variable1 . . . variablen*

indicates that each variable is to be plotted using symbols specified in **SYMBOL** statements. The *i*th variable in the list is plotted using the plot symbol, color, and font specified in the *i*th **SYMBOL** statement. The height specified in the **SYMBOL** statement is multiplied by the bar height to obtain the height of the symbol that is plotted. Thus, if **H=0.5** in the first **SYMBOL** statement, and the bar height is 5% of the screen area, then the first symbol is plotted with a height of 2.5%. For example, suppose the following two **SYMBOL** statements are in effect:

```
SYMBOL1 V=STAR C=RED    H=1;
SYMBOL2 V=V      C=GREEN H=0.5 F=GREEK;
```

Then, the following statement

```
CHART SDATE FDATE;
```

causes values of SDATE to be plotted with a red star that is as high as each bar and the values of FDATE with an inverted green triangle that is half as high as the bar height. See the section “[Using SYMBOL Statements](#)” on page 541 for further information on using the **SYMBOL** statement.

**variable1='symbol1' ... variablen='symboln'**

indicates that each variable is to be plotted using the symbol specified. The symbol must be a single character enclosed in quotes. The font used for the symbol is the same as the font used for the text.

**(variables)='symbol1' ... (variables)='symboln'**

indicates that each variable in parentheses is to be plotted using the symbol associated with that group. The symbol must be a single character enclosed in single quotes. For example, the following statement

```
CHART (ED SD)='*'  
(FD LD)='+';
```

plots the values of variables in the first group using an asterisk (\*) and the values of variables in the second group using a plus sign (+).

A single **CHART** statement can contain requests in more than one of these forms.

**NOTE:** It is not necessary to specify a CHART statement if only default values are used to draw the Gantt chart.

The following options can appear in the CHART statement specifically for the production of high-resolution graphics quality Gantt charts.

#### **ABARHT=***h*

specifies that the height of the actual schedule bar be *h* cellheights. The value of *h* is restricted to be a positive real number. The default bar height is one cellheight. This specification will override a **BARHT=** specification. In the event that the actual schedule bar corresponds to the logic bar (using the **LEVEL=** option), the value is ignored and the default value is used instead. Any non-working days corresponding to this schedule bar are also drawn using the same height as the schedule bar unless the **HBARHT=** option is specified.

#### **ABAROFF=***d*

specifies that the actual schedule bar be offset *d* cellheights from its default position. A value of zero corresponds to the default position. The direction of increase is from top to bottom. This specification will override a **BAROFF=** specification. In the event that the actual schedule bar corresponds to the logic bar (specified using the **LEVEL=** option), the value is ignored and the default value is used instead. Any non-working days corresponding to this schedule bar are drawn using the offset of the schedule bar unless the **HBAROFF=** option is specified.

#### **ACTIVITY=***variable*

#### **ACT=***variable*

specifies the variable identifying the names of the nodes representing activities in the Schedule data set. This option is required when the precedence information is specified using the AON format. The variable can be either numeric or character in type. If the **PRECDATA=** option is specified, then this variable must also exist in the Precedence data set and have identical type and length.

#### **ANNOTATE=SAS-data-set**

#### **ANNO=SAS-data-set**

specifies the input data set that contains the appropriate Annotate variables for the purpose of adding text and graphics to the Gantt chart. The data set specified must be an Annotate-type data set. See also the section “[Annotate Processing](#)” on page 537 for information specifically on annotate processing with the GANTT procedure.

The ANNOTATE= data set specified in a **CHART** statement is used only for the Gantt chart created by that particular CHART statement. You can also specify an ANNOTATE= data set in the **PROC GANTT** statement, which provides “global” Annotate information to be used for all Gantt charts created by the procedure.

### **AOA**

causes PROC GANTT to use the specification for the AOA format for producing a Logic Gantt chart when the precedence information has been specified in both **AOA** format (**TAIL=** and **HEAD=** options) and **AON** format (**ACTIVITY=**, **SUCCESSOR=**, and, optionally, **LAG=** options). The default behavior is to use the AON format.

### **BARHT=*h***

specifies that the height of all the schedule bars be *h* cellheights. The value of *h* is restricted to be a positive real number. The default value is one cellheight. This specification can be overridden for each schedule type by specifying the bar height option appropriate for that schedule type. If a Logic Gantt chart is produced, the specified bar height is ignored for the logic bar (specified using the **LEVEL=** option) and the default bar height of one cellheight is used for it instead. All non-working days corresponding to a schedule bar are drawn using the height of the schedule bar unless the **HBARHT=** option is specified.

### **BAROFF=*d***

specifies that all the schedule bars be offset *d* cellheights from their default positions. A value of zero corresponds to the default positions. The direction of increase is from top to bottom. This specification can be overridden for each schedule type by specifying the bar offset option that is appropriate for that schedule type. If a Logic Gantt chart is produced, the specified bar offset is ignored for the logic bar (specified using the **LEVEL=** option) and the default bar offset of zero used instead.

### **BBARHT=*h***

specifies that the height of the baseline schedule bar be *h* cellheights. The value of *h* is restricted to be a positive real number. The default bar height is one cellheight. This specification overrides a **BARHT=** specification. In the event that the baseline schedule bar corresponds to the logic bar (using the **LEVEL=** option), the value is ignored and the default value is used instead. Any non-working days corresponding to this schedule bar are also drawn using the same height as the schedule bar unless the **HBARHT=** option is specified.

### **BBAROFF=*d***

specifies that the baseline schedule bar be offset *d* cellheights from its default position. A value of zero corresponds to the default position. The direction of increase is from top to bottom. This specification overrides a **BAROFF=** specification. In the event that the baseline schedule bar corresponds to the logic bar (specified using the **LEVEL=** option), the value is ignored and the default value is used instead. Any non-working days corresponding to this schedule bar are drawn using the offset of the schedule bar unless the **HBAROFF=** option is specified.

### **BOTTOM**

#### **BJUST**

positions the bottom of the Gantt chart at the bottom of the page, just above the footnotes. This option is ignored if you specify the **TOP** or **TJUST** option.

**CAXIS**=*color***CAXES**=*color***CA**=*color*

specifies the color to use for displaying axes for the Gantt chart. The default color depends on the GOPTIONS statement and the GSTYLE system option; see the section “[ODS Style Templates](#)” on page 561 for more information.

**CFRAME**=*color***CFR**=*color*

specifies the color to use for filling the axis area. If the CFRAME= option is not specified and the GSTYLE system option is not in effect, then the axis area is not filled. If the GSTYLE system option is in effect, then the default color depends on the current ODS style template; see the section “[ODS Style Templates](#)” on page 561 for more information. The CFRAME= option is ignored if the NOFRAME option is specified.

**CHARTWIDTH**=*p***CHARTPCT**=*p*

specifies the width of the axis area as a percentage of the total Gantt chart width in the chart that would be produced if you had a page large enough to contain the entire chart without compression. The Gantt procedure rescales the chart so the axis area with is *p*% of the virtual chart width and the text area width is (100-*p*)% of the virtual chart width.

This option gives you the capability to generate Gantt charts that are consistent in their appearance. In the event that the chart fits on a single page, it is possible to get a smaller chart than had the CHARTWIDTH= option not been specified. You can use the [FILL](#) option in this case if you wish to use the entire page.

**CHCON**=*color*

specifies the color to use for drawing the horizontal connecting lines. The default color depends on the GOPTIONS statement and the GSTYLE system option; see the section “[ODS Style Templates](#)” on page 561 for more information.

**CMILE**=*color*

specifies the color to use for drawing the milestone symbol on the chart. If the CMILE= option is not specified, the default color of the milestones follows the rules for coloring the bars of the relevant schedule. For example, the milestone depicting a critical activity is drawn with the color of the fill pattern used for critical activities. For an activity with slack, the early start and late start milestone are drawn with the color of the fill pattern used for the duration and the slack time of a noncritical activity, respectively. You can also control the color at the activity level by using a [PATTERN](#) variable.

## **COMPRESS**

specifies that the Gantt chart be drawn on the number of output pages determined by the [HPAGES](#)= and [VPAGES](#)= options. If the HPAGES= option is not specified, the procedure assumes a default of HPAGES=1. If the VPAGES= option is not specified, the procedure assumes a default of VPAGES=1. The COMPRESS option does not attempt to maintain the aspect ratio of the Gantt chart. To maintain the aspect ratio of the Gantt chart, use the [PCOMPRESS](#) option instead.

**CPREC=***color*

specifies the color to use for drawing the precedence connections. The default color depends on the GOPTIONS statement and the GSTYLE system option; see the section “[ODS Style Templates](#)” on page 561 for more information.

**CREF=***color*

specifies the color to use for drawing vertical reference lines on the chart. The default color depends on the GOPTIONS statement and the GSTYLE system option; see the section “[ODS Style Templates](#)” on page 561 for more information.

**CTEXT=***color***CT=***color*

specifies the color to use for displaying text that appears on the chart, including variable names or labels, tickmark values, values of ID variables, and so on. The default color depends on the GOPTIONS statement and the GSTYLE system option; see the section “[ODS Style Templates](#)” on page 561 for more information.

**CTEXTCOLS=***name***CTEXTCOLS=***(namelist)***CPATTEXT=***name***CPATTEXT=***(namelist)***CACTTEXT=***name***CACTTEXT=***(namelist)*

names the columns of activity text to be displayed using the color of the PATTERN variable when one exists or from the fill pattern from a particular schedule bar.

A missing value for a PATTERN variable results in the default text color being used. The default text color is the value of the CTEXT= option.

In the absence of a PATTERN variable, the activity text color is the color of the fill pattern indicating the duration of the schedule identified by the PATLEVEL= option. If PATLEVEL=EARLY or PATLEVEL=LATE, the color depends on the status of the activity. Colors for critical duration, supercritical duration, and normal duration are used depending on whether the activity is critical, supercritical, or noncritical, respectively. If more than one level is specified, the first in order of appearance on the Gantt chart is used, that is, in order EARLY, LATE, ACTUAL, RESOURCE, BASELINE.

Possible values for the CTEXTCOLS= option are shown in the following table.

Value	Interpretation
ZONE	ZONE variable column
JOBNUM	Job number column
ID	ID variable columns
FLAG	Status flag column
ALL	All of the above (default)

**CTNOW=***color*

specifies the color to use for drawing the timenow line on the chart. The default color depends on the GOPTIONS statement and the GSTYLE system option; see the section “[ODS Style Templates](#)” on page 561 for more information.

**CZONE=***color***CZLINE=***color*

specifies the color to use for drawing the horizontal zone lines that demarcate the different zones on the chart. The default color depends on the GOPTIONS statement and the GSTYLE system option; see the section “[ODS Style Templates](#)” on page 561 for more information.

**DESCRIPTION=***'string'***DES=***'string'*

specifies a descriptive string, up to 40 characters in length, that appears in the description field of the master menu of PROC GREPLAY. If the DESCRIPTION= option is omitted, the description field contains a description assigned by PROC GANTT.

**EBarHT=***h***LBarHT=***h*

specifies that the height of the early/late schedule bar be *h* cellheights. The value of *h* is restricted to be a positive real number. The default bar height is one cellheight. This specification overrides a **BARHT=** specification. In the event that the early/late schedule bar corresponds to the logic bar (using the **LEVEL=** option), the value is ignored and the default value is used instead. Any non-working days corresponding to this schedule bar are also drawn using the same height as the schedule bar unless the **HBarHT=** option is specified.

**EBarOff=***d***LBarOff=***d*

specifies that the early/late schedule bar be offset *d* cellheights from its default position. A value of zero corresponds to the default position. The direction of increase is from top to bottom. This specification overrides a **BAROFF=** specification. In the event that the early/late schedule bar corresponds to the logic bar (specified using the **LEVEL=** option), the value is ignored and the default value is used instead. Any non-working days corresponding to this schedule bar are drawn using the offset of the schedule bar unless the **HBarOff=** option is specified.

**FONT=***font*

specifies the font to use for displaying job numbers, ID variables, legend, labels on the time axis, and so forth. The default font depends on the GOPTIONS statement and the GSTYLE system option; see the section “[ODS Style Templates](#)” on page 561 for more information.

**FMILE=***font*

specifies the font to use for drawing the milestone symbol on the chart. To select a symbol from the special symbol table, set FMILE=NONE or leave it unspecified. If the FMILE= option is specified without a corresponding **VMILE=** option, the value of the FMILE= option is ignored, and the default milestone symbol, a filled diamond, is used instead. A warning is issued to the log in this instance.

See also the section “[Special Fonts for Project Management and Decision Analysis](#)” on page 543 for information on a special set of symbols that are suitable for representing milestones on a Gantt chart.

**HBARHT=***h*

specifies that all non-working days be displayed with a bar which is *h* cellheights high. The default behavior is to use the same height as that of the schedule bar.

**HBAROFF=***d*

specifies that the bars which represent non-working days be offset *d* cellheights from their default positions. The default behavior is to use the same offset as that of the schedule bar.

**HEAD=***variable***HEADNODE=***variable*

specifies the variable (either character or numeric) in the **Schedule** data set that contains the name of the node that represents the finish of the activity. This option is required when the precedence information is specified using the **AOA** format.

**HEIGHT=***h*

specifies that the height for all text in PROC GANTT, excluding TITLE and FOOTNOTE statements, be *h* times the value of HTEXT=, the default text height specified in the GOPTIONS statement of SAS/GGRAPH. The value of *h* is a positive real number; the default value is 1.0.

To illustrate, suppose you have the specification HEIGHT=0.6 in the **CHART** statement and the following GOPTIONS statement:

```
GOPTIONS htext = 2 in;
```

Then the height for all text in PROC GANTT is  $0.6 \times 2 \text{ in} = 1.2 \text{ in}$ .

If the value of HTEXT= is not specified in a GOPTIONS statement, then the text height is determined by the font size attribute of the GraphDataText element of the current ODS style template. See the section “**ODS Style Templates**” on page 561 for more information about ODS styles.

For each activity, all text corresponding to the JOB, FLAG, and ID variables is displayed at a depth of *d* cells from the top of the first bar corresponding to the activity, where *d* is the value of the **HTOFF=** option. The default value of *d* is 1.0. Furthermore, the text strings do not overwrite one another and *skip*, the value of the **SKIP=** option, is not increased to accommodate a large text height. Subject to the preceding restrictions, PROC GANTT calculates the maximum allowable value for text height as the height occupied by (*skip* + the number of different schedule bars drawn per activity) blank lines. Specifically, this is the height between like bars corresponding to consecutive activities. If the specified text height exceeds this value, the height is truncated to the maximum allowable value and a warning is issued to the log. This option enables you to enlarge the text to at least the height occupied by all of the schedule bars, making it easier to read. This is especially useful when the value of the **VPOS=** option is very large, and several schedule bars are plotted for each activity. It also provides easier identification of the activity corresponding to a given schedule bar.

**HMILE=***height*

specifies the height in cells of the milestone symbol. The height is a positive real number; the default value is 1.0.

**HPAGES=***h*

specifies that the Gantt chart is to be produced using *h* horizontal pages. This, however, may not be possible due to intrinsic constraints on the output. For example, the GANTT procedure requires that every horizontal page represent at least one activity. Thus, the number of horizontal pages can

never exceed the number of activities in the project. Subject to such inherent constraints, the GANTT procedure attempts to use the specified value for the HPAGES= option; if this fails, it uses  $h$  as an upper bound. The exact number of horizontal pages used by the Gantt chart is given in the \_ORGANTT macro variable. See the section “[Macro Variable \\_ORGANTT](#)” on page 559 for further details.

The appearance of the chart with respect to the HPAGES= option is also influenced by the presence of other related procedure options. The HPAGES= option performs the task of determining the number of vertical pages in the absence of the VPAGES= option. If the [COMPRESS](#) or [PCOMPRESS](#) option is specified in this scenario, the chart uses one vertical page; if neither option is specified, the number of vertical pages is computed to display as much of the chart as possible in a proportional manner.

#### **HTOFF=d**

specifies that the line upon which all activity text rests, also referred to as the *font baseline*, is positioned at a depth of  $d$  cells below the top of the first bar. The default value of  $d$  is 1.0. The value of the HTOFF= option can be any nonnegative real number less than the (*skip + the number of different schedule bars per activity - 1*). A value of 0 positions text on the line corresponding to the top of the first bar. Assigning the maximum value corresponds to positioning text directly above the bar reserved for CHART variables of the next activity on the page. If a value larger than the maximum is specified, PROC GANTT truncates this value to the maximum and issues a warning to the log. Furthermore, if the [HEIGHT=](#) and HTOFF= values cause activity text to overwrite the text headings, PROC GANTT reduces the HTOFF= value accordingly and issues a warning to the log.

#### **LABVAR=variable**

specifies the variable that links observations in the [Label](#) data set (label definitions) to observations in the [Schedule](#) data set (activities). This variable must exist in both the Schedule data set and the Label data set and be identical in type and length. The variable can be either numeric or character in type. The linking can be a 1-1, 1-many, many-1, or many-many relationship. The linking can be used to extract positional information as well as the text string information from the Schedule data set for an observation in the Label data set when such information cannot be retrieved from the relevant variables in the Label data set.

If the \_Y variable does not exist or its value is missing, the vertical coordinate for a label’s placement position is determined from the activities that are linked to it and their relative positions on the activity axis of the Gantt chart. A value of -1 for \_Y implies linking of the label to every activity (assuming data values are used). This is equivalent to specifying the LABVAR= option in the [CHART](#) statement and linking every activity to the label. Note that any Label data set observation with dual linkage definitions is ignored. That is, an observation with \_Y equal to -1 and with a nonmissing value for the LABVAR= variable is ignored.

The following rules apply to label definitions in the Label data set that are linked to activities in the Schedule data set:

- If the `_X` variable does not exist in the Label data set or its value is missing, the horizontal coordinate is extracted from the Schedule data set using the `_XVAR` variable.
- If the `_LABEL` variable does not exist in the Label data set or its value is missing, the text string is determined from the Schedule data set using the `_LVAR` variable.

**LABRULE=***rule*

**LABFMT=***rule*

specifies the rule to use for laying out labels that are defined in the Label data set. Valid values for *rule* are PAGECLIP and FRAMCLIP. PAGECLIP displays a label at the specified location and clips any part of the label that runs off the page. A value of FRAMCLIP differs from PAGECLIP in that it clips all labels with data value coordinates that run off the frame of the Gantt chart. The default value for *rule* is PAGECLIP.

**LABSPLIT='***character***'**

**LABELSPLIT='***character***'**

splits labels that are defined in the Label data set wherever the split character appears. By default, if there are embedded blanks, the GANTT procedure attempts to split strings at suitable blanks so that the resulting lines are equal in length. To suppress the default splitting when using strings embedded with blanks, specify a dummy character not used in the labeling.

**LAG=***variable*

**LAG=(***variables***)**

specifies the variables identifying the lag types of the precedence relationships between an activity and its successors. Each **SUCCESSOR** variable is matched with the corresponding LAG variable; that is, for a given observation, the *i*th LAG variable defines the relationship between the activities specified by the **ACTIVITY** variable and the *i*th SUCCESSOR variable. The LAG variables must be character type and their values are expected to be specified as one of FS, SS, SF, FF, which denote ‘Finish-to-Start’, ‘Start-to-Start’, ‘Start-to-Finish’, ‘Finish-to-Finish’, respectively. You can also use the *keyword\_duration\_calendar* specification used by **PROC CPM** although PROC GANTT uses only the *keyword* information and ignores the lag *duration* and the lag *calendar*. If no LAG variables exist or if an unrecognized value is specified for a LAG variable, PROC GANTT interprets the lag as a ‘Finish-to-Start’ type. If the **PRECDATA=** option is specified, the LAG variables are assumed to exist in the Precedence data set; otherwise, they are assumed to exist in the Schedule data set.

**LEFT****LJUST**

displays the Gantt chart left-justified with the left edge of the page. This option has priority over the **RIGHT** or **RJUST** option. Note that when displaying a Gantt chart in graphics mode, the chart is centered in both horizontal and vertical directions in the space available after accounting for titles, footnotes, and notes. The chart justification feature enables you to justify the chart in the horizontal and vertical directions with the page boundaries.

**LEVEL=***number*

specifies the schedule bar to use for drawing the precedence connections. The default value of **LEVEL**= 1, which corresponds to the topmost bar.

**LHCON=***linetype*

specifies the line style (1 – 46) to be used for drawing the horizontal connecting line produced by the **HCONNECT** option described earlier in this section. Possible values for *linetype* are

- 1 solid line (the default value when **LHCON**= is omitted)
- 2 – 46 various dashed lines. See [Figure 8.5](#).

For the corresponding line-printer option, see the **HCONCHAR**= option described earlier in this section.

**LPREC=***linetype*

specifies the line style (1 – 46) to use for drawing the precedence connections. The default line style is 1, a solid line. See [Figure 8.5](#) for examples of the various line styles available.

**LREF=***linetype*

specifies the line style (1 – 46) to use for drawing the reference lines. The default line style is 1, a solid line. See [Figure 8.5](#) for examples of the various line styles available. For the corresponding line-printer option, see the **REFCHAR**= option described earlier.

**LTNOW=***linetype*


specifies the line style (1 – 46) to use for drawing the timenow line. The default line style is 1, a solid line. See [Figure 8.5](#) for examples of the various line styles available.

**LWIDTH=***linewidth*

specifies the line width to be used for drawing lines, other than the timenow line and precedence connection lines, used in the Gantt chart. The default width is 1.

**LZONE=***linetype***LZLINE=***linetype*

specifies the line style (1 – 46) to use for drawing the horizontal zone lines which demarcate the different zones on the chart. The default line style is 1, a solid line.

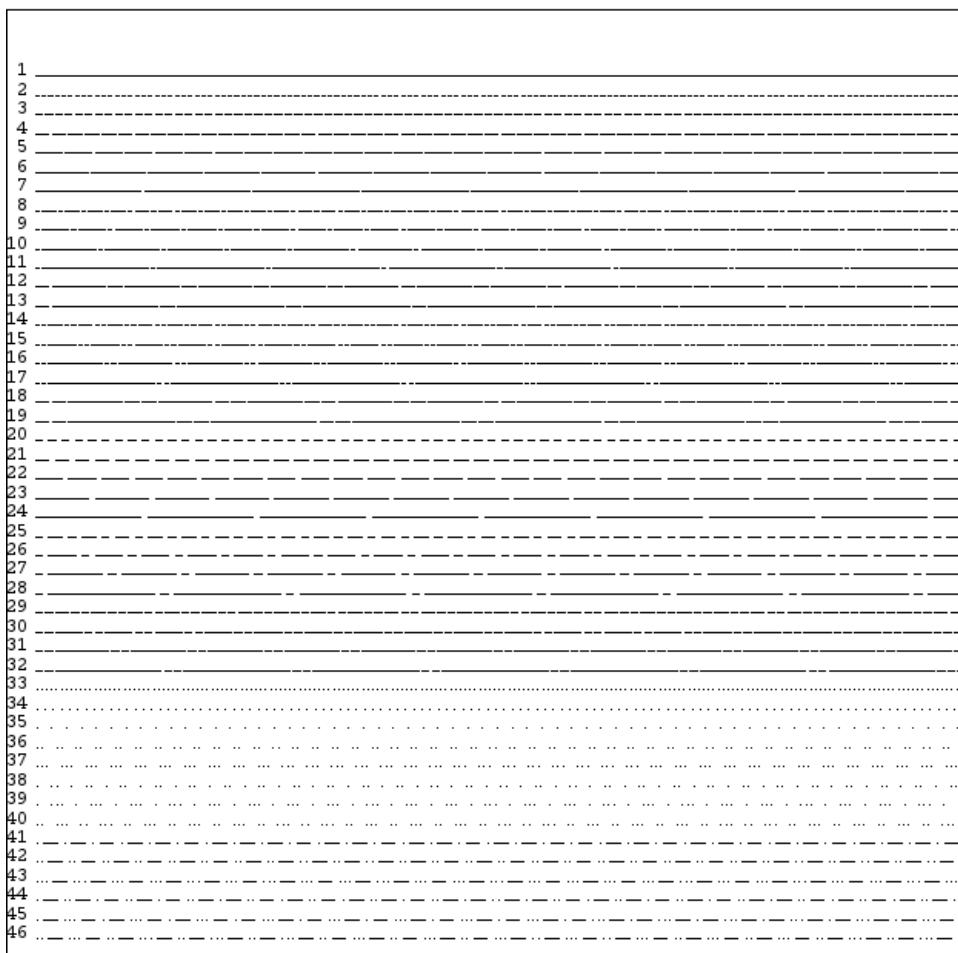**Figure 8.5** Valid Line Styles**MAXDISLV=***columns*

specifies the maximum allowable distance, in number of columns, that a local vertical can be positioned from its minimum offset to avoid overlap with a global vertical. The value of the MAXDISLV= option must be greater than or equal to 0.1; the default value is 1. For the definitions of global and local verticals, see the section “[Specifying the Logic Options](#)” on page 545.

**MININTGV=***columns*

specifies the minimum inter-distance, in number of columns, of any two global verticals to prevent overlap. The value of the MININTGV= option must be greater than or equal to 0.1; the default value is 0.75.

**MINOFFGV=***columns*

specifies the minimum offset, in number of columns, of a global vertical from the end of the bar with which it is associated. The value of the MINOFFGV= option must be greater than or equal to 0.1; the default value is 1.

**MINOFFLV=***columns*

specifies the minimum offset, in number of columns, of a local vertical from the end of the bar with which it is associated. The value of the MINOFFLV= option must be greater than or equal to 0.1; the default value is 1.

**NAME=**'*string*'

where '*string*' specifies a descriptive string, up to eight characters long, that appears in the name field of the master menu of the GREPLAY procedure. If you omit the NAME= option, the name field of the master menu contains the name of the procedure.

**NJOBS=***number***NACTS=***number*

specifies the number of jobs that should be displayed on a single page. This option overrides the **VPAGES=** option.

**NOARROWHEAD****NOARRHD**

suppresses the arrowhead when drawing the precedence connections.

**NOEXTRANGE****NOXTRNG**

suppresses the automatic extension of the chart axis range when drawing a Logic Gantt chart and neither the **MINDATE=** nor **MAXDATE=** option is specified.

**NOFRAME****NOFR**

suppresses drawing the vertical boundaries to the left and right of the Gantt chart; only the top axis and a parallel line at the bottom are drawn. If this option is not specified, the entire chart area is framed.

**NOPAGENUM**

suppresses numbering the pages of a multipage Gantt chart. This is the default behavior. To number the pages of a multipage Gantt chart on the upper right-hand corner of each page, use the **PAGENUM** option.

**NOPATBAR**

suppresses the use of the **PATTERN** variable for filling the schedule bars. The default fill patterns are used instead. Typically, this option is used when you want to color the activity text using the **CTEXTCOLS=** option but leave the bars unaffected by the **PATTERN** variable.

**NOTMTIME**

suppresses the display of the time portion of the axis tickmark label when the value of **MININTERVAL** is DTDAY. When **MININTERVAL=DTDAY**, the time axis tickmarks are labeled with three lines, the first indicating the month, the second indicating the day, and the third indicating the time. This option effectively lowers the first two lines by a line and drops the third line altogether.

**NOZONECOL**

suppresses displaying the **ZONE** variable column that is automatically done in the presence of a zone variable.

**NTICKS=***number***NINCRS=***number*

specifies the number of tickmarks that should be displayed on the first horizontal page of the Gantt chart. The number of tickmarks on the remaining horizontal pages is determined by the page width and the columns of text that are to be displayed (ZONE, IDs, flag, and so forth). The page width is determined to be the minimum width necessary to fit the first page. If the **IDPAGES** option is specified, the number of tickmarks is the same as that specified by the **NTICKS=** option. This option overrides the **HPAGES=** option.

**ONEZONEVAL**

displays the value of the **ZONE** variable in the ZONE variable column only for activities that begin a new zone. A blank string is displayed for all other activities.

**PAGENUM**

numbers the pages of the Gantt chart on the top right-hand corner of the page if the chart exceeds one page. The numbering scheme is from left to right, top to bottom.

**PATLEVEL=***name***PATLEVEL=**(*namelist*)

specifies the different schedule bar levels to fill using the **PATTERN** variable. By default, all of the schedule bar levels for an activity are filled using the pattern defined by the **PATTERN** variable. Note that holiday and non-working days are not filled with this pattern.

Possible values for the **PATLEVEL=** option and their actions are shown in the following table.

<b>Value</b>	<b>Interpretation</b>
EARLY	Early/Late schedule durations
LATE	Early/Late schedule durations
ACTUAL	Actual schedule durations
RESOURCE	Resource schedule duration
BASELINE	Baseline schedule duration
ALL	All of the above (default)

In the absence of a **PATTERN** variable, this option defines the schedule type that determines the color for the activity text columns (ZONE variable, ID variable, Job number, Critical Flag), which are identified with the **CTEXTCOLS=** option. In this case, only one schedule type is used, namely the first one appearing in the order EARLY, LATE, ACTUAL, RESOURCE, BASELINE.

**PATTERN=***variable***PATVAR=***variable*

specifies an integer variable in the Schedule data set that identifies the pattern for filling the schedule bars and coloring the milestones. The default **PATTERN** variable name is **\_PATTERN**. If the value of the **PATTERN** variable is missing for a particular activity, or if there is no **PATTERN** variable, the different schedule bars and milestones for the activity are drawn using the corresponding default patterns given in [Table 8.7](#). The procedure uses the defined or default pattern to fill all the schedule bars and color all the milestones associated with the activity, except for holidays and non-working days. Use the **PATLEVEL=** option to restrict the application of the defined pattern to selected schedule bar levels.

When plotting split activities, you have the additional capability of overriding the defined pattern at the segment level by specifying a value for the PATTERN variable for the schedule data set observation representing the segment. Setting it to missing results in inheriting the PATTERN variable value from the observation for the same activity with a missing SEGMT\_NO. For example, setting PATTERN=SEGMT\_NO in the CHART statement when using split activities results in each segment using a different pattern.

Note that, if the value of the PATTERN variable is  $n$  for a particular activity, the GANTT procedure uses the specifications in the  $n$ th generated PATTERN definition, not the specifications in the PATTERN  $n$  statement.

The chart legend and summary, when displayed, indicate the default patterns that identify the different schedule types represented on the Gantt chart as listed in Table 8.7. Since the PATTERN variable overrides these values at the activity level, you must be careful in interpreting the summary and legend when using a PATTERN variable, especially if any of the specified pattern definitions overlap with one of the default patterns.

#### **PCOMPRESS**

specifies that every output page of the Gantt chart is to be produced maintaining the original aspect ratio of the Gantt chart. The number of output pages is determined by the HPAGES= and VPAGES= options. In the absence of the HPAGES= and VPAGES= options, the PCOMPRESS option displays the Gantt chart on a single page.

#### **RBARHT= $h$**

#### **SBARHT= $h$**

specifies that the height of the resource-constrained schedule bar be  $h$  cellheights. The value of  $h$  is restricted to be a positive real number. The default bar height is one cellheight. This specification overrides a BARHT= specification. In the event that the resource-constrained schedule bar corresponds to the logic bar (using the LEVEL= option), the value is ignored and the default value is used instead. Any non-working days corresponding to this schedule bar are also drawn using the same height as the schedule bar unless the HBARHT= option is specified.

#### **RBAROFF= $d$**

#### **SBAROFF= $d$**

specifies that the resource-constrained schedule bar be offset  $d$  cellheights from its default position. A value of zero corresponds to the default position. The direction of increase is from top to bottom. This specification overrides a BAROFF= specification. In the event that the resource-constrained schedule bar corresponds to the logic bar (specified using the LEVEL= option), the value is ignored and the default value is used instead. Any non-working days corresponding to this schedule bar are drawn using the offset of the schedule bar unless the HBAROFF= option is specified.

#### **RIGHT**

#### **RJUST**

displays the Gantt chart right-justified with the right edge of the page. This option is ignored in the presence of the LEFT or LJUST option.

#### **SHOWPREC**

causes PROC GANTT to terminate in the event that a valid AOA or AON specification exists, and an error occurs either in the logic system (memory allocation, data structure creation, and so on) or simply due to bad data (missing values for the ACTIVITY, TAIL, HEAD variables, and so on). The default behavior is to attempt drawing the chart without the precedence connections.

**SUCCESSOR=variable****SUCC=variable****SUCCESSOR=(variables)****SUCC=(variables)**

specifies the variables identifying the names of the immediate successors of the node specified by the **ACTIVITY** variable. This option is required when the precedence information is specified in the **AON** format. These variables must have the same type as the **ACTIVITY** variable. If the **PRECDATA=** option has been specified, the **SUCCESSOR** variables are assumed to exist in the **Precedence** data set; otherwise, they are assumed to exist in the **Schedule** data set.

**TAIL=variable****TAILNODE=variable**

specifies the variable in the **Schedule** data set that contains the name of the node that represents the start of the activity. This option is required when the precedence information is specified using the **AOA** format. The variable can be either numeric or character in type.

**TOP****TJUST**

positions the top of the Gantt chart at the top of the page, just below the titles. This option has priority over the **BOTTOM** or **BJUST** option.

**VMILE=value**

specifies a plot symbol from the font specified in the **FMILE=** option to be used as the milestone symbol on the chart. If the **FMILE=** option is set to **NONE** or is not specified, then the milestone symbol is the symbol specified by the **VMILE=** option in the special symbol table shown in [Figure 8.7](#). The default milestone symbol is a filled diamond.

**VPAGES=v**

Specifies that the Gantt chart is to be produced using *v* vertical pages. This, however, may not be possible due to intrinsic constraints on the output. For example, the **GANTT** procedure requires that every vertical page represent at least one tickmark. Thus, the number of vertical pages can never exceed the number of tickmarks in the axis. Subject to such inherent constraints, the **GANTT** procedure attempts to use the specified value for the **VPAGES=** option; if this fails, it uses *v* as an upper bound. The exact number of vertical pages used by the Gantt chart is provided in the **\_ORGANTT** macro variable. See the section “[Macro Variable \\_ORGANTT](#)” on page 559 for further details.

The appearance of the chart with respect to the **VPAGES=** option is also influenced by the presence of other related procedure options. The **VPAGES=** option performs the task of determining the number of horizontal pages in the absence of the **HPAGES=** option. If the **COMPRESS** or **PCOMPRESS** option is specified in this scenario, the chart uses one horizontal page. If neither the **COMPRESS** nor **PCOMPRESS** option is specified, the number of horizontal pages is computed in order to display as much of the chart as possible in a proportional manner.

**WEB=variable****HTML=variable**

specifies the character variable in the schedule data set that identifies an HTML page for each activity. The procedure generates an HTML image map using this information for all the schedule bars, milestones, and ID variables corresponding to an activity.

**WPREC=***linewidth*

specifies the line width to use for drawing the precedence connections. The default width is 1.

**WTNOW=***linewidth*

specifies the line width to use for drawing the timenow line. The default width is 4.

**WZONE=***linewidth***WZLINE=***linewidth*

specifies the line width to use for drawing the horizontal zone lines which demarcate the different zones on the chart. The default linewidth is 1.

**ZONE=***variable***ZONEVAR=***variable*

names the variable in the Schedule data set that is used to separate the Gantt chart into zones. This option enables you to produce a zoned Gantt chart. The GANTT procedure does not sort the Schedule data set and processes the data in the order it appears in the Schedule data set. A change in the value of the zone variable establishes a new zone. By default, the GANTT procedure displays a ZONE variable column before the ID variable columns. You can suppress this column using the **NOZONECOL** option. The GANTT procedure also draws a horizontal line demarcating zones. By default, the line spans the entire chart in the horizontal direction, both inside and outside the axis area. You can control the span of this line using the **ZONESPAN=** option. You can also adjust the vertical offset of the line from its default position by using the **ZONEOFFSET=** option. In addition, you can also control the graphical attributes associated with this line such as color, style, and width using the **CZONE=**, **LZONE=**, and **WZONE=** options, respectively.

**ZONEOFF=d****ZONEOFFSET=d**

specifies the offset in cellheights of the zone line from its default position of 0.5 cell height above the top of the first schedule bar for the first activity in the zone. The default value of *d* is 0. The direction of increase is from top to bottom.

**ZONESPAN=name****ZONELINE=name**

specifies the span of the horizontal zone line that is drawn at the beginning of each new zone. Valid values for ‘name’ are LEFT, RIGHT, ALL, and NONE. The value of LEFT draws a line that spans the width of the columns of text that appear on the left hand side of the Gantt chart. The value of RIGHT draws a line that spans the width of the axis area which appears on the right-hand side of the chart. The value of ALL draws a line spanning both the preceding regions while the value of NONE suppresses the line altogether. The default value is ALL.

## ID Statement

**ID** *variables* ;

The ID statement specifies the variables to be displayed that further identify each activity. If two or more consecutive observations have the same combination of values for all the ID variables, only the first of these observations is plotted unless the **DUPOK** option is specified in the **CHART** statement.

By default, if the ID variables do not all fit on one page, they are all omitted and a message explaining the omission is printed to the log. You can override this behavior and display the maximum number of consecutive ID variables that can fit on a page by specifying the **MAXIDS** option in the CHART statement.

If the time axis of a Gantt chart spans more than one page, the ID variables are displayed only on the first page of each activity. You can display the ID variables on every page by specifying the **IDPAGES** option in the CHART statement.

## Details: GANTT Procedure

### Schedule Data Set

Often, the Schedule data set input to PROC GANTT is the output data set (the OUT= data set) produced by PROC CPM, sometimes with additional variables. Typically, this data set contains

- the start and finish times for the early and late schedules (E\_START, E\_FINISH, L\_START, and L\_FINISH variables)
- the actual start and finish times (A\_START and A\_FINISH variables) of activities that have been completed or are in progress for projects that are in progress or completed
- the resource-constrained start and finish times of the activities (S\_START and S\_FINISH variables) for projects that have been scheduled subject to resource constraints
- the baseline start and finish times (B\_START and B\_FINISH variables) of activities when monitoring and comparing the progress of a project against a target schedule

When such a data set is input as the Schedule data set to PROC GANTT, the procedure draws a Gantt chart showing five different schedules for each activity: the predicted early/late schedules using E\_START, E\_FINISH, L\_START, and L\_FINISH on the first line for the activity, the actual schedule using A\_START and A\_FINISH on the second line, the resource-constrained schedule using S\_START and S\_FINISH on the third line, and the baseline schedule using B\_START and B\_FINISH on the fourth line.

#### ***The SEGMT\_NO Variable***

Normally, each observation of the Schedule data set causes one set of bars to be plotted corresponding to the activity in that observation. If activity splitting has occurred during resource-constrained scheduling, the Schedule data set produced by PROC CPM contains more than one observation for each activity. It also contains a variable named SEGMT\_NO. For activities that are not split, this variable has a missing value. For split activities, the number of observations in the Schedule data set is equal to  $(1 + \text{the number of disjoint segments that the activity is split into})$ . The first observation corresponding to such an activity has SEGMT\_NO equal to missing, and the S\_START and S\_FINISH variables are equal to the start and finish times, respectively, of the entire activity. Following this observation, there are as many observations as the number of disjoint segments in the activity. All values for these segments are the same as the first observation for this activity except SEGMT\_NO, S\_START, S\_FINISH, and the duration. SEGMT\_NO is the index of the segment, S\_START and S\_FINISH are the resource-constrained start and finish times for this segment,

and duration is the duration of this segment. See the section “Displayed Output” on page 558 for details on how PROC GANTT treats the observations in this case.

**NOTE:** For a given observation in the Schedule data set, the finish times (E\_FINISH, L\_FINISH, A\_FINISH, S\_FINISH, and B\_FINISH) denote the last *day* of work when the variables are formatted as SAS *date* values; if they are formatted as SAS *time* or *datetime* values, they denote the last *second* of work. For instance, if an activity has E\_START=‘2JUN04’ and E\_FINISH=‘4JUN04’, then the earliest start time for the activity is the beginning of June 2, 2004, and the earliest finish time is the end of June 4, 2004. Thus, PROC GANTT assumes that the early, late, actual, resource-constrained, or baseline finish time of an activity is at the end of the time interval specified for the respective variable. The exceptions to this type of default behavior occur when either the DURATION= option or the PADDING= option is in effect. See the section “Specifying the PADDING= Option” on page 528 for further details.

All start and finish times, and additional variables specified in the CHART statement must be numeric and have the same formats. The ID and BY variables can be either numeric or character. Although the data set does not have to be sorted, the output may be more meaningful if the data are in order of increasing early start time. Further, if the data set contains segments of split activities, the data should also be sorted by SEGMENT\_NO for each activity.

A family of options, available only in graphics mode, enables you to display the precedence relationships between activities on the Gantt chart. The precedence relationships are established by specifying a set of variables in the CHART statement; this can be done in one of two ways. These variables must lie in the Schedule data set and, optionally, in the Precedence data set defined by the PRECDATA= option in the PROC GANTT statement. See the section “Specifying the Logic Options” on page 545 for more details on producing a Logic Gantt chart.

Also available in graphics mode is an automatic text annotation facility that enables you to annotate labels on the Gantt chart independently of the SAS/GRAF Annotate facility. A useful property of this facility is the ability to link label coordinates and text strings to variables in the Schedule data set. You can create links of two types. An implicit link automatically links an observation in the Label data set to every observation in the Schedule data set. An explicit link uses a variable that must exist on both data sets and be identical in type and length. For more information on the linking variable in the automatic text annotation facility, see the section “Automatic Text Annotation” on page 552.

## Missing Values in Input Data Sets

Table 8.2 summarizes the treatment of missing values for variables in the input data sets used by PROC GANTT.

**Table 8.2** Treatment of Missing Values in PROC GANTT

Data Set	Variable	Action
CALEDATA	CALID	Default calendar (0 or “DEFAULT”)
	_SUN_, . . . ,_SAT_	Corresponding shift for default calendar
	D_LENGTH	DAYLENGTH, if available; else, 8:00, if INTERVAL=WORKDAY or DTWRKDAY; 24:00, otherwise
DATA	A_FINISH	Value ignored
	A_START	Value ignored
	ACTIVITY	Input error: logic options are ignored

**Table 8.2** (continued)

Data Set	Variable	Action
	B_FINISH	Value ignored
	B_START	Value ignored
	CALID	Default calendar (0 or “DEFAULT”)
	CHART	Value ignored
	DUR	Nonzero
	E_FINISH	Value ignored
	E_START	Value ignored
	HEADNODE	Input error: logic options are ignored
	ID	Missing
	L_FINISH	Value ignored
	L_START	Value ignored
	LAG	FS
	S_FINISH	Value ignored
	S_START	Value ignored
	SEGMT_NO	See the section “ <a href="#">Displayed Output</a> ” on page 558
	SUCCESSOR	Value ignored
	TAILNODE	Input error: logic options are ignored
	ZONE	Zone value
HOLIDATA	CALID	Holiday applies to all calendars defined
HOLIDATA	HOLIDAY	Observation ignored
HOLIDATA	HOLIDUR	Ignored, if HOLIFIN is not missing; else, 1.0
HOLIDATA	HOLIFIN	Ignored, if HOLIDUR is not missing; else, HOLIDAY + (1 unit of INTERVAL)
LABDATA	_ALABEL	0
LABDATA	_CLABEL	CTEXT=
LABDATA	_FLABEL	FONT=
LABDATA	_HLABEL	1
LABDATA	_JLABEL	L
LABDATA	_LABEL	Use _LVAR
LABDATA	_LVAR	Value ignored
LABDATA	_PAGEBRK	0
LABDATA	_RLABEL	0
LABDATA	_X	Use _XVAR
LABDATA	_XOFFSET	0
LABDATA	_XVAR	Value ignored
LABDATA	_XSYS	DATA
LABDATA	_Y	Use LABVAR=
LABDATA	_YOFFSET	0
LABDATA	_YSYS	DATA
LABDATA	LABVAR	Value ignored
PRECDATA	ACTIVITY	Input error: logic options are ignored
PRECDATA	LAG	FS
PRECDATA	SUCCESSOR	value ignored
WORKDATA	any numeric variable	00:00, if first observation; 24:00, otherwise

---

## Specifying the PADDING= Option

As explained in the section “Schedule Data Set” on page 525, the finish times in the Schedule data set denote the final time unit of an activity’s duration; that is, the activity finishes at the end of the day/second specified as the finish time. A plot of the activity’s duration should continue through the end of the final time unit. Thus, if the value of the E\_FINISH variable is ‘4JUN04’, the early finish time for the activity is plotted at the end of June 4, 2004 (or the beginning of June 5, 2004).

In other words, the finish times are *padded* by a day (second) if the finish time variables are formatted as SAS date (SAS time or datetime) values. This treatment is consistent with the meaning of the variables as output by PROC CPM. Default values of PADDING corresponding to different format types are shown in Table 8.3.

The PADDING= option is provided to override the default padding explained above. Valid values of this option are NONE, SECOND, MINUTE, HOUR, DAY, WEEK, MONTH, QTR, YEAR, DTSECOND, DTMINUTE, DTHOUR, DTWEEK, DTMONTH, DTQTR, and DTYEAR. Use the value NONE if you do not want the finish times to be adjusted.

**Table 8.3** Default Values of the PADDING= Option Corresponding to Format Type

Format	PADDING
SAS time value	SECOND
SAS date value	DAY
SAS datetime value	DTSECOND
Other	NONE

It is recommended that when plotting zero duration activities, you include a variable in the Schedule data set that has value zero if and only if the activity has zero duration. Defining this variable to the GANTT procedure using the DURATION= (or DUR=) option in the CHART statement ensures that a zero duration activity is represented on the chart by a Milestone. If this is not done, an activity with zero duration is shown on the chart as having a positive duration since finish times are padded to show the end of the last time unit.

---

## Page Format

The GANTT procedure divides the observations (activities) into a number of subgroups of approximately equal numbers. The size of each group is determined by the PAGESIZE system option. Similarly, the time axis is divided into a number of approximately equal divisions depending on the LINESIZE system option.

If the FILL option is specified, however, each page is filled as completely as possible before plotting on a new page. If both axes are split, the pages are ordered with the chart for each group of activities being plotted completely (the time axis occupying several consecutive pages, if needed) before proceeding to the next group.

If a BY statement is used, each BY group is formatted separately.

Two options that control the format of the chart are the **MININTERVAL=** and **SCALE=** options. The value for the **MININTERVAL=** option, denoted by *mininterval*, is the smallest time interval unit to be identified on the chart. The value for the **SCALE=** option, denoted by *scale*, is the number of columns to be used to denote one unit of *mininterval*. For example, if **MININTERVAL=MONTH** and **SCALE=10**, the chart is formatted so that 10 columns denote the period of one month. The first of these 10 columns denotes the start of the month and the last denotes the end, with each column representing approximately three days. Further, the **INCREMENT=** option can be used to control the labeling. In this example, if **INCREMENT=2**, then the time axis would have labels for alternate months.

### Specifying the MININTERVAL= Option

The value specified for the **MININTERVAL=** option is the smallest time interval unit to be identified on the chart. If the time values being plotted are SAS *date* values, the valid values for *mininterval* are DAY, WEEK, MONTH, QTR, or YEAR. If the values are SAS *datetime* values, valid values for *mininterval* are DTSECOND, DTMINUTE, DTHOUR, DTDAY, DTWEEK, DTMONTH, DTQTR, or DTYEAR. If they are SAS *time* values, then valid values are SECOND, MINUTE, or HOUR.

**NOTE:** If the times being plotted are SAS *datetime* values and *mininterval* is either DTSECOND, DTMINUTE, or DTHOUR, the output generated could run into several thousands of pages. Therefore, be careful when choosing a value for *mininterval*.

Table 8.4 shows the default values of *mininterval* corresponding to different formats of the times being plotted on the chart.

**Table 8.4** Default Values of the MININTERVAL= Option

Format	MININTERVAL= Value
DATEw.	DAY
DATETIMEw.d	DTDAY
HHMMw.d	HOUR
MONYYw.	MONTH
TIMEw.d	HOUR
YYMMDDw.	MONTH
YYQw.	MONTH

### Labeling on the Time Axis

If the variables being plotted in the chart are unformatted numeric values, the time axis is labeled by the corresponding numbers in increments specified by the **INCREMENT=** option. However, if the variables have *date*, *datetime*, or *time* formats, then the time axis is labeled with two or three lines. Each line is determined by the value of *mininterval*, which in turn is determined by the format of the plotted times (see Table 8.4). Table 8.5 illustrates the format of the label corresponding to different values of *mininterval*.

**Table 8.5** Label Format Corresponding to MININTERVAL= Value

MININTERVAL= Value	First Line	Second Line	Third Line
DAY, WEEK, DTWEEK	Month	Day	
MONTH, QTR, YEAR,	Year	Month	
DTMONTH, DTQTR,			
DTYEAR			
DTSECOND, DTMINUTE,	Month	Day	Time
DTHOUR, DTDAY			
SECOND, MINUTE, HOUR	Time		

## Multiple Calendars and Holidays

Work pertaining to a given activity is assumed to be done according to a particular *calendar*. A calendar is defined in terms of a *work pattern* for each day and a *workweek structure* for each week. In addition, each calendar may include holidays during the year. See the “[Multiple Calendars](#)” section in the [PROC CPM](#) chapter for details on how calendars are defined and how all the options work together. In this chapter, a less detailed description is provided. [PROC GANTT](#) uses the same structure as PROC CPM for defining calendars, but the options for using them differ in minor ways. The following are the differences in syntax:

- The [CALID](#) variable is specified as an option in the [CHART](#) statement and is not a separate statement as in PROC CPM.
- The [HOLIDAY](#) variable is specified as an option in the [CHART](#) statement and is not a separate statement as in PROC CPM.
- The [HOLIDUR](#) and [HOLIFIN](#) variables are specified as options in the [CHART](#) statement and not in a separate [HOLIDAY](#) statement.
- The [INTERVAL=](#) option is specified in the [CHART](#) statement and not in the procedure statement as in PROC CPM.

The [WORKDATA](#) (or Workday) data set specifies distinct shift patterns during a day. The [CALEDATA](#) (or Calendar) data set specifies a typical workweek for all the calendars in the project; for each day of a typical week, it specifies the shift pattern that is followed. The [HOLIDATA](#) (or Holiday) data set specifies a list of holidays and the calendars that they refer to; holidays are defined either by specifying the start of the holiday and its duration in *interval* units, where the [INTERVAL=](#) option has been specified as *interval*, or by specifying the start and end of the holiday period. If both the [HOLIDUR](#) and the [HOLIFIN](#) variables have missing values in a given observation, the holiday is assumed to start at the date and time specified for the [HOLIDAY](#) variable and last one unit of *interval*. If a given observation has valid values for both the [HOLIDUR](#) and the [HOLIFIN](#) variables, only the [HOLIFIN](#) variable is used so that the holiday is assumed to start and end as specified by the [HOLIDAY](#) and [HOLIFIN](#) variables, respectively. The [Schedule](#) data set (the [DATA=](#) data set), specifies the calendar that is used by each activity in the project through the [CALID](#) variable (or a default variable [\\_CAL\\_](#)). Each of the three data sets used to define calendars is described in greater detail in the “[Multiple Calendars](#)” section in the [PROC CPM](#) chapter.

Each new value for the CALID variable in either the Calendar or the Holiday data set defines a new calendar. If a calendar value appears in the Calendar data set and not in the Holiday data set, it is assumed to have the same holidays as the default calendar (the default calendar is defined in the [PROC CPM](#) chapter). If a calendar value appears in the Holiday data set and not in the Calendar data set, it is assumed to have the same work pattern structures (for each week and within each day) as the default calendar. In the Schedule data set, valid values for the CALID variable are those that are defined in either the Calendar or the Holiday data set.

All the holiday, workday and workweek information is used by PROC GANTT for display only; in particular, the weekend and shift information is used only if the [MARKWKND](#) or [MARKBREAK](#) option is in effect. The value of the INTERVAL= option, which has a greater scope in PROC CPM, is used here only to determine the end of holiday periods appropriately. Further, the Workday, Calendar, and Holiday data sets and the processing of holidays and different calendars are supported only when *interval* is DAY, WEEKDAY, WORKDAY, DTSECOND, DTMINUTE, DTHOUR, DTDAY, or DTWKDAY.

### Specifying the INTERVAL= Option

The INTERVAL= option is needed only if you want holidays or breaks or both during a week or day to be indicated on the Gantt chart. The value of INTERVAL= is used to compute the start and end of holiday periods to be compatible with the way they were computed and used by [PROC CPM](#). Further, if the [MARKWKND](#) or [MARKBREAK](#) option is in effect, the INTERVAL= option, in conjunction with the [DAYSTART=](#) and [DAYLENGTH=](#) options and the [Workday](#), [Calendar](#), and [Holiday](#) data sets, helps identify the breaks during a standard week or day as well as the holidays that are to be marked on the chart. Valid values of *interval* are DAY, WEEKDAY, WORKDAY, DTSECOND, DTMINUTE, DTHOUR, DTDAY, and DTWKDAY. If *interval* is WEEKDAY, WORKDAY, or DTWKDAY, the MARKWKND option is in effect; otherwise, breaks during a week are indicated only if MARKWKND is specified and breaks within a day are marked only if MARKBREAK is specified.

## Full-Screen Version

You can invoke PROC GANTT in full-screen mode by specifying [FS](#) (or [FULLSCREEN](#)) in the [PROC GANTT statement](#). The full-screen mode offers you a convenient way to browse the Gantt chart for the project. For large projects, where the chart could span several pages, the full-screen mode is especially convenient because you can scroll around the output using commands on the command line, pull-down menus, or function keys. You can scroll vertically to a given job on the task axis by specifying a job number or scroll horizontally to a given point in time along the time axis by specifying a date. You can optionally display the title and the legend.

The specifications for the full-screen version of PROC GANTT and the output format are the same as those for the line-printer version. The following is a list of the few minor differences:

- The [FILL](#) option is not relevant in this case because all of the activities are plotted on one logical page.
- The [NOLEGEND](#) option is not effective. The screen always displays only the body of the chart along with the ID columns. To see what the symbols mean, you can use the [SHOW LEGEND](#) command, which causes the legend to be displayed at the bottom of the chart. To delete the legend, use the [DELETE LEGEND](#) command.
- The [SUMMARY](#) option is not supported in full-screen mode.

- The **SCALE=** option works the same way as in the line-printer version, except for its default behavior. The default value is always 1, unlike in the line-printer case where, if the time axis fits on less than one page, the default value is chosen so that the time axis fills as much of the page as possible.

## Output Format

The output format is similar to the line-printer version of PROC GANTT. When PROC GANTT is invoked with the **FS** option, the screen is filled with a display of the Gantt chart. The display consists of column headings at the top and ID values (if an **ID** statement is used to specify ID variables) at the left. The body of the chart occupies the bottom right portion of the display. The column headings can be scrolled left or right, the ID values can be scrolled up or down, and the body of the chart can scroll along both directions. The display does not include the **TITLES** or **LEGEND**.

In addition to using the symbols and join characters as described for the line-printer version of PROC GANTT, the full-screen version also uses different colors to distinguish the types of activities and their associated bars.

You can use the **FIND** command to locate a particular job (by job number) or a particular time along the time axis. The format of the FIND command is **FIND JOB *n*** or **FIND TIME *t***. All the commands that are specific to PROC GANTT are described as follows.

## Local Commands

Table 8.6 lists the commands that can be used in the full-screen version of PROC GANTT.

**Table 8.6** Full-Screen Commands and Their Purpose

Scrolling	Controlling Display	Exiting
BACKWARD	SHOW	END
FORWARD	DELETE	CANCEL
LEFT	FIND	
RIGHT		
TOP		
BOTTOM		
VSCROLL		
HSCROLL		

### BACKWARD

scrolls towards the top of the Gantt chart by the **VSCROLL** amount. A specification of BACKWARD MAX scrolls to the top of the chart. You can also specify the vertical scroll amount for the current command as BACKWARD PAGE | HALF | *n*. Note that during vertical scrolling, the column headings are not scrolled.

### BOTTOM

scrolls to the bottom of the Gantt chart.

**DELETE LEGEND | TITLE**

deletes the legend or the title from the screen. A specification of DELETE LEGEND deletes the legend from the current display; DELETE TITLE deletes the current title (titles) from the current display.

**END**

ends the current invocation of the procedure.

**FIND**

scrolls to the specified position on the chart. The format of the command is FIND JOB *n* or FIND TIME *t*.

A specification of FIND JOB *n* scrolls backward or forward, as necessary, in order to position the activity with job number *n* on the screen. The specified activity is positioned at the top of the screen, unless this would result in blank space at the bottom of the screen. In this instance, the chart is scrolled down to fit as many jobs as space permits.

A specification of FIND TIME *t* scrolls left or right, as necessary, in order to position the time *t* on the time axis to appear on the screen. The specified time is positioned at the left boundary of the displayed chart area unless this would result in blank space at the right of the screen. In this instance, the chart is scrolled to the right to fit as much of the time axis as space permits.

**FORWARD**

scrolls towards the bottom of the Gantt chart by the **VSCROLL** amount. A specification of FORWARD MAX scrolls to the bottom of the chart. You can also specify the vertical scroll amount for the current command as FORWARD PAGE | HALF | *n*. Note that during vertical scrolling, the column headings are not scrolled.

**HELP**

displays a HELP screen listing all the full-screen commands specific to PROC GANTT.

**HOME**

moves the cursor to the command line.

**HSCROLL**

sets the amount of information that scrolls horizontally when you execute the **LEFT** or **RIGHT** command. The format is HSCROLL PAGE | HALF | *n*. The specification is assumed to be in number of columns. A specification of HSCROLL PAGE sets the scroll amount to be the number of columns in the part of the screen displaying the plot of the schedules. A specification of HSCROLL HALF is half that amount; HSCROLL *n* sets the horizontal scroll amount to *n* columns. The default setting is PAGE.

**KEYS**

displays current function key settings.

**LEFT**

scrolls towards the left boundary of the Gantt chart by the **HSCROLL** amount. A specification of LEFT MAX scrolls to the left boundary. You can also specify the horizontal scroll amount for the current command as LEFT PAGE | HALF | *n*. Note that during horizontal scrolling, the ID columns are not scrolled.

**RIGHT**

scrolls towards the right boundary of the Gantt chart by the **HSCROLL** amount. A specification of **RIGHT MAX** scrolls to the right boundary. You can also specify the horizontal scroll amount for the current command as **RIGHT PAGE | HALF | *n***. Note that during horizontal scrolling, the ID columns are not scrolled.

**SHOW LEGEND | TITLE**

displays the legend or the title on the screen. A specification of **SHOW LEGEND** displays the legend in the bottom portion of the current display; **SHOW TITLE** displays the current title (titles) in the top portion of the current display.

**TOP**

scrolls to the top of the Gantt chart.

**VSCROLL**

sets the amount of information that scrolls vertically when you execute the **BACKWARD** or **FORWARD** command. The format is **VSCROLL PAGE | HALF | *n***. The specification is assumed to be in number of rows. A specification of **VSCROLL PAGE** sets the scroll amount to be the number of rows in the part of the screen displaying the plot of the schedules. A specification of **VSCROLL HALF** is half that amount; **VSCROLL *n*** sets the vertical scroll amount to *n* rows. The default setting is **PAGE**.

## Global Commands

Most of the global commands used in SAS/FSP software are also valid with PROC GANTT. Some of the commands used for printing screens are described below.

SAS/FSP software provides you with a set of printing commands that enable you to take pictures of windows and to route those pictures to a printer or a file. Whether you choose to route these items directly to a printer queue or to a print file, SAS/FSP software provides you with a means of specifying printing instructions. The following is an overview of these related commands and their functions:

**FREE**

releases all items in the print queue to the printer. This includes pictures taken with the **SPRINT** command as well as items sent to the print queue with the **SEND** command. All items in the print queue are also automatically sent to the printer when you exit the procedure, send an item that uses a different form, or send an item to a print file. Items are also sent automatically when internal buffers have been filled.

**Items sent to a file:** If you have routed pictures taken with the **SPRINT** command to a file rather than to a printer, the file is closed when you execute a **FREE** command. It is also closed when you send an item that uses a different form, send items to a different print file or to the print queue, or exit the procedure.

**NOTE:** Any items sent to the same print file after it has been closed will replace the current contents.

**PRTFILE** 'filename'**PRTFILE** fileref**PRTFILE CLEAR**

specifies a file to which the procedure sends pictures taken with the **SPRINT** command instead of sending them to the default printer. You can specify an actual filename or a previously assigned fileref.

**Using a filename:** To specify a file named *destination-file*, execute

```
prtfile 'destination-file'
```

where *destination-file* follows your system's conventions. Note that quotes are required when you specify a filename rather than a fileref.

**Using a fileref:** You can also specify a previously assigned fileref.

**Using the default:** Specify PRTFILE CLEAR to prompt the procedure to route information once again to the queue for the default printer.

**Identify the current print file:** Specify PRTFILE to prompt the procedure to identify the current print file.

**SPRINT [NOBORDER][NOCMD]**

takes a picture of the current window exactly as you see it, including window contents, border, and command line. By default, the picture is sent to the queue for the default printer.

**Border and command line:** By default, both the window border and command line are included in the picture you take with the SPRINT command. You can capture a picture of the window contents that excludes either the window border, the command line, or both. Specify the NOBORDER option to exclude the border and the NOCMD option to exclude the command line. Taking a picture of the window contents without the border and command line is a convenient way to print text for a report.

**Destination:** The destination of the picture captured with the SPRINT command is determined by the PRTFILE command. By default, the picture goes to the default printer. Use the PRTFILE command if you want it sent to a file instead. Each time you execute the SPRINT command, the picture you take is appended to the current print file; it does not write over the current file. See the **PRTFILE** command for further explanation.

## Graphics Version

### Formatting the Chart

If necessary, **PROC GANTT** divides the Gantt chart into several pages. You can force the Gantt chart to fit on one page by specifying the **COMPRESS** option in the **CHART** statement. You can achieve a similar result using the **PCOMPRESS** option, which also maintains the aspect ratio. In addition, you can fit the chart into a prescribed number of horizontal and vertical pages by using the **HPAGES=** and **VPAGES=** options in the **CHART** statement.

The amount of information contained on each page is determined by the values of the graphics options **HPOS=** and **VPOS=** specified in a **GOPTIONS** statement. If any compression of the Gantt chart is performed, the values of HPOS and VPOS are increased, as necessary, to the number of rows and columns respectively,

that the entire chart occupies in uncompressed mode. The default height of each row of the Gantt chart is computed as  $(100/v)\%$  of the screen height where  $VPOS=v$ . Thus, the larger the value of VPOS, the narrower the row. You can control the default bar height and default bar offset by using the **BARHT=** option and the **BAROFF=** option, respectively. You can further override these at the schedule level. For example, the **ABARHT=** option affects only the height of the actual schedule bars. The screen is assumed to be divided into  $h$  columns where  $HPOS=h$ ; thus, each column is assumed to be as wide as  $(100/h)\%$  of the screen width. Hence, the specifications **SCALE=10** and **MININTERVAL=WEEK** imply that a duration of one week is denoted by a bar of length  $(1000/h)\%$  of the screen width.

The height of the text characters is controlled by both the **HEIGHT=** option in the CHART statement and the **HTEXT=** option specified in a GOPTIONS statement. The text height is set equal to the product of the **HEIGHT=** and **HTEXT=** values. (If neither the **HEIGHT=** option nor the **HTEXT=** option has been specified, the text height is given by the font size attribute of the GraphDataText element of the current ODS style template. See the section “[ODS Style Templates](#)” on page 561 for more information about ODS styles.) The units in which the text height is measured are those of the **HTEXT=** option. By default, the value of **HEIGHT=** is 1, which sets the text height to be equal to the **HTEXT=** value. The default value of **HTEXT=** is 1 unit, where a unit is defined by the **GUNIT=** option in a GOPTIONS statement. Thus, in the absence of the **HEIGHT=**, **HTEXT=**, and **GUNIT=** options, and with no font size provided by the current ODS style template, the text height is the same as the bar height, namely one cell height. Increasing the value of **HEIGHT=** is useful when you use the **COMPRESS** option, particularly when you have a very large chart. Since the chart is scaled as appropriate to fit on one page, the text can be very hard to discern, or even illegible, and would benefit from enlargement. Relative positioning of the font baseline for activity text is controlled by the **HTOFF=** option in the CHART statement. By default, the font baseline for an activity is at the bottom of the first bar corresponding to the activity.

The color of the text characters is specified by using the **CTEXT=** option in the CHART statement. The default color depends on the GOPTIONS statement and the GSTYLE system option; see the section “[ODS Style Templates](#)” on page 561 for more information. You can override the text colors for selected columns of activity text at the activity level by using a **PATTERN** variable in the Schedule data set and specifying the **CTEXTCOLS=** option in the CHART statement.

The font used for the text characters is specified with the **FONT=** option in the CHART statement. The default font depends on the GOPTIONS statement and the GSTYLE system option; see the section “[ODS Style Templates](#)” on page 561 for more information.

Global **PATTERN statements** are used to specify the fill pattern for the different types of bars drawn on the Gantt chart. Each fill pattern can be associated with a color. Patterns can be used to reflect the status of an activity (normal, critical, supercritical) in the predicted early/late schedule, to indicate the different schedule types (actual, resource-constrained, baseline), and to represent weekends, holidays and breaks on the Gantt chart. See the section “[Using PATTERN Statements](#)” on page 537 for details. In addition, you can override these fill patterns for selected schedules at an activity level by using a **PATTERN** variable in the Schedule data set and specifying the **PATLEVEL=** option in the CHART statement.

You can use global **SYMBOL statements** to define the symbols that represent CHART variables in the Gantt chart. The **SYMBOL** statement enables you to select symbols from different fonts and modify their appearance to suit your requirements. You can specify a color and a height for the symbol in addition to a variety of other options. See the section “[Using SYMBOL Statements](#)” on page 541 for details.

## Annotate Processing

The Annotate facility enables you to enhance graphics output produced by PROC GANTT. However, if the only items being annotated are symbols and text strings, it is recommended that you use the [Automatic Text Annotation](#) facility that is built into the Gantt procedure instead. This facility was developed specifically for labeling Gantt charts; it has some very useful features and requires a minimum of effort.

To use the SAS/GGRAPH Annotate facility, you must create an Annotate data set that contains a set of graphics commands that can be superimposed on the Gantt chart. This data set has a specific format and must contain key variables. Each observation in the Annotate data set represents a command to draw a graphics element or perform an action. The values of the variables in the observation determine what is done and how it is done. The observations in an Annotate data set can be created by explicitly assigning values to the Annotate variables through a DATA step or SAS/FSP procedure or by implicitly assigning values with Annotate macros within a SAS DATA step. The process of creating Annotate observations is greatly simplified through the use of Annotate macros.

Coordinates specify where graphic elements are to be positioned. A coordinate system, in turn, determines how coordinates are interpreted. There are several different coordinate systems that are used by the Annotate facility. Typically, one of three major drawing areas can be associated with any coordinate system: data area, procedure output area, and graphics output area. This chapter explains the coordinate system that is based on the data area of PROC GANTT.

When annotating a graph produced by any of the graphics procedures, you may find it helpful to use data coordinates that refer to the data values corresponding to the graph that is being annotated. For example, if you want to label a particular activity of a Gantt chart with additional text, you can position the text accurately if you use data coordinates instead of screen coordinates. With respect to PROC GANTT, the Annotate facility uses the time axis and the activity axis of the Gantt chart as the basis for the data coordinate system. To use this feature, create a Annotate data set based on the Schedule data set that is input to the procedure, utilizing Annotate macros whenever possible to simplify the process.

**NOTE:** The data coordinate system enables you to annotate the graph even if it spans multiple pages. However, each annotation must be entirely contained within a given page. For example, you cannot annotate a line on the Gantt chart that runs from one page of the chart to another.

In addition to a coordinate system based on the data, you can select a coordinate system based on either the procedure output area or the Graphics output area. You would typically need to use one of these systems, for example, if you want to annotate text outside the chart area.

## Using PATTERN Statements

PROC GANTT uses those patterns that are available with the GCHART procedure. PROC GANTT uses a maximum of nine different patterns to denote various phases in an activity's duration and the various types of schedules that are plotted. Patterns are specified in PATTERN statements that can be used anywhere in your SAS program. [Table 8.7](#) lists the function of each of the first nine PATTERN statements that are used by PROC GANTT.

Any PATTERN statements that you specify are used. If more are needed, default PATTERN statements are used.

You can override any of these patterns at the activity level by using a PATTERN variable in the schedule data set. A PATTERN variable is identified by specifying the PATTERN= option in the CHART statement or by the presence of the default \_PATTERN variable.

**Table 8.7** PATTERN Statements used by PROC GANTT

PATTERN	Used to Denote
1	Duration of a noncritical activity
2	Slack time for a noncritical activity
3	Duration of a critical activity
4	Slack time for a supercritical activity
5	Duration of a supercritical activity
6	Actual duration of an activity
7	Break due to a holiday
8	Resource-constrained duration of an activity
9	Baseline duration of an activity

Refer to the SAS/GGRAPH documentation for a detailed description of PATTERN statements. Most of the relevant information is reproduced here for the sake of completeness.

### **PATTERN Statement Syntax**

The general form of a PATTERN statement is

**PATTERN***n options;*

where

- *n* is a number ranging from 1 to 255. If you do not specify a number after the keyword PATTERN, PATTERN1 is assumed.
- *options* enables you to specify the colors and patterns used to fill the bars in your output.

PATTERN statements are additive; if you specify a C= or V= option in a PATTERN statement and then omit that option in a later PATTERN statement ending in the same number, the option remains in effect. To turn off options specified in a previous PATTERN*n* statement, either specify all options in a new PATTERN*n* statement, or use the keyword PATTERN*n* followed by a semicolon. For example, the following statement turns off any C= or V= option specified in previous PATTERN3 statements:

```
pattern3;
```

You can reset options in PATTERN statements to their default values by specifying a null value. A comma can be used (but is not required) to separate a null parameter from the next option.

For example, both of the following statements cause the C= option to assume its default value (the value of the CPATTERN= option or the first color in the COLORS= list):

```
pattern c=, v=solid;
```

or

```
pattern c= v=solid;
```

In the following statement, both options are reset to their default values:

```
pattern2 c= v=;
```

You can also turn off options by specifying the RESET= option in a GOPTIONS statement.

### **General options**

You can specify the following options in a PATTERN statement.

**COLOR=** *color*

**C=** *color*

specifies the color to use for a bar or other area to be filled. If you do not specify the C= option in a PATTERN statement, the procedure uses the value you specified for the CPATTERN= option in a GOPTIONS statement. If you omitted the CPATTERN= option, the procedure uses the pattern specified by the V= option (see below) with each color in the COLORS= list before it uses the next PATTERN statement.

**REPEAT=** *n*

**R=** *n*

specifies the number of times the PATTERN statement is to be reused. For example, the following statement represents one pattern to be used by SAS/GRAFH software:

```
pattern1 v=x3 c=red;
```

You can use the REPEAT= option in the statement to repeat the pattern before going to the next pattern. For example, if you specify the following statements, PATTERN1 is repeated ten times before PATTERN2 is used:

```
pattern1 v=x3 c=red r=10;
pattern2 v=s c=blue r=10;
```

Remember that if you omit the COLOR= option in the PATTERN statement and you do not specify the CPATTERN= option, SAS/GRAFH software repeats the pattern for each color in the current COLORS= list. If you specify the R= option in a PATTERN statement from which the C= option is omitted, the statement cycles through the COLORS= list the number of times given by the value of the R= option.

For example, if the current device has seven colors, then the following statement results in 70 patterns because each group of seven patterns generated by cycling through the COLORS= list is repeated ten times:

```
pattern v=x3 r=10;
```

**VALUE=** *value***V=** *value*

specifies the pattern to use for a bar or other area to be filled. The valid values you can use depend on what procedure you are using and the type of graph you are producing. In PROC GANTT, which produces bars, you must use one of the pattern values shown in Figure 8.6.


In a PATTERN statement, if you specify a value for the V= option but not for the C= option, the procedure uses the value you specified for the CPATTERN= option in a GOPTIONS statement. If you omitted the CPATTERN= option, the procedure uses the pattern specified for the V= option with each color in the COLORS= list before it uses the next PATTERN statement. Thus, if you specify the following statements, the PATTERN1 statement is used for the first type of bar, namely, for the duration of a noncritical activity:

```
pattern1 c=red    v=x3;
pattern2          v=s;
pattern3 c=blue   v=13;
pattern4 c=green  v=r4;

proc gantt data=sched;
```

The PATTERN2 statement is used for the second type of bar, namely, for the slack time of a noncritical activity. Because a C= value is not specified in the PATTERN2 statement, SAS/GRAPH software uses the PATTERN2 statement and cycles through the colors in the COLORS= list for the device to obtain as many patterns as there are colors in the list. If needed, the PATTERN3 and PATTERN4 values are then used for any remaining types of bars.

**Figure 8.6** Pattern Selection Guide

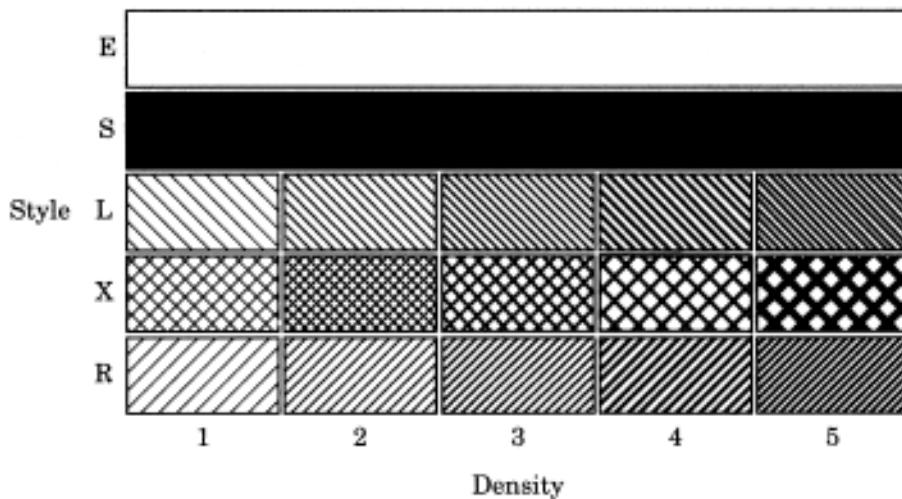

## Using SYMBOL Statements

You can specify a SYMBOL statement anywhere in your SAS program. SYMBOL statements give PROC GANTT information about the characters to be used for plotting the CHART variables.

See also the section “Special Fonts for Project Management and Decision Analysis” on page 543 for a description of some typically used Gantt chart symbols that can be specified using a SYMBOL statement.

Refer to the SAS/GGRAPH documentation for a detailed description of SYMBOL statements. Most of the relevant information is reproduced here for the sake of completeness.

### ***SYMBOL Statement Syntax***

The general form of a SYMBOL statement is

**SYMBOL***n options;*

where

- *n* is a number ranging from 1 to 255. Each SYMBOL statement remains in effect until you specify another SYMBOL statement ending in the same number. If you do not specify a number following the keyword SYMBOL, SYMBOL1 is assumed.
- *options* enables you to specify the plot characters and color.

SYMBOL statements are additive; that is, if you specify a given option in a SYMBOL statement and then omit that option in a later SYMBOL statement ending in the same number, the option remains in effect. To turn off all options specified in previous SYMBOL statements, you can specify all options in a new SYMBOL*n* statement, use the keyword SYMBOL*n* followed by a semicolon, or specify a null value. A comma can be used (but is not required) to separate a null parameter from the next option.

For example, both of the following statements cause the C= option to assume its default value (the value of the CSYMBOL= option or the first color in the COLORS= list):

```
symbol1 c=, v=plus;
```

and

```
symbol1 c= v=plus;
```

In the following statement, both options are reset to their default values:

```
symbol4 c= v=;
```

You can also turn off options by specifying the RESET= option in a GOPTIONS statement.

### **General options**

You can specify the following options in the SYMBOL statement.

#### **COLOR=***color*

##### **C=***color*

specifies the color to use for the corresponding plot specification. If you do not specify the C= option in a SYMBOL statement, the procedure uses the value you specified for the CSYMBOL= option in a GOPTIONS statement. If you omit the CSYMBOL= option, the procedure uses the value specified by the V= option with each color in the COLORS= list before it uses the next SYMBOL statement.

#### **FONT=***font*

##### **F=***font*

specifies the font from which the symbol corresponding to the value specified with the V= option is to be drawn. If you do not specify a font, the V= option specifies the symbol from the special symbol table shown in [Figure 8.7](#).

#### **H=***height*

specifies the height of the symbol that is to be drawn.

For example, this SYMBOL statement

```
symbol1 c=green v=K f=special h=2;
```

indicates that the symbol at each data point is the letter K from the SPECIAL font (a filled square), drawn in green, the height being twice the bar height.

#### **REPEAT=***n*

##### **R=***n*

specifies the number of times the SYMBOL statement is to be reused.

#### **V=***special-symbol*

#### **V=**'*string*'

identifies the symbols from the font specified by the FONT= option in the SYMBOL statement for the corresponding plot specifications. If the FONT= option is not specified, the plot symbol is the symbol corresponding to the value of V= in the special symbol table shown in [Figure 8.7](#). Also permitted without a FONT= specification are the letters A through W and the numbers 0 through 9. If the font is a symbol font, such as MARKER, the string specified with the V= option is the character code for the symbol. If the font is a text font, such as SWISS, the string specified with the V= option is displayed as the plot symbol. By default, the value of V= is PLUS, which produces the plus symbol (+) from the special symbol table.

Note that if you use the special symbol comma (,) with the V= option, you must enclose the comma in quotes as illustrated in the following statement:

```
symbol1 v=' , ';
```

**Figure 8.7** Special Symbol Table


VALUE=	Plot Symbol	VALUE=	Plot Symbol
PLUS	+	%	(percent)
X	×	&	(ampersand)
STAR	*	'	(single quote)
SQUARE	□	=	(equals)
DIAMOND	◇	-	(hyphen)
TRIANGLE	△	@	(at)
HASH	#	*	(asterisk)
Y	Y	+	(plus)
Z	Z	>	(greater than)
PAW	..	.	(period)
POINT	.	<	(less than)
DOT	●	,	(comma)
CIRCLE	○	/	(slash)
_ (underscore)	◻	?	(question mark)
" (double quote)	♠	(	(left parenthesis)
# (pound sign)	♥	)	(right parenthesis)
\$ (dollar sign)	◇	:	(colon)

Note: The words or special characters in the VALUE= column are entered exactly as shown.


## Special Fonts for Project Management and Decision Analysis

Two special marker fonts, ORFONT and ORFONTE, are available in versions 6.08 and later. These two fonts are meant to be used with SAS/OR software and provide a variety of symbols that are typically used in Project Management and Decision Analysis. The fonts ORFONT and ORFONTE are shown in [Figure 8.8](#) and [Figure 8.9](#), respectively. The fonts behave like any SAS/GPGRAPH font providing you with the capability to control attributes such as color and height.

**Figure 8.8** ORFONT - A Filled Font

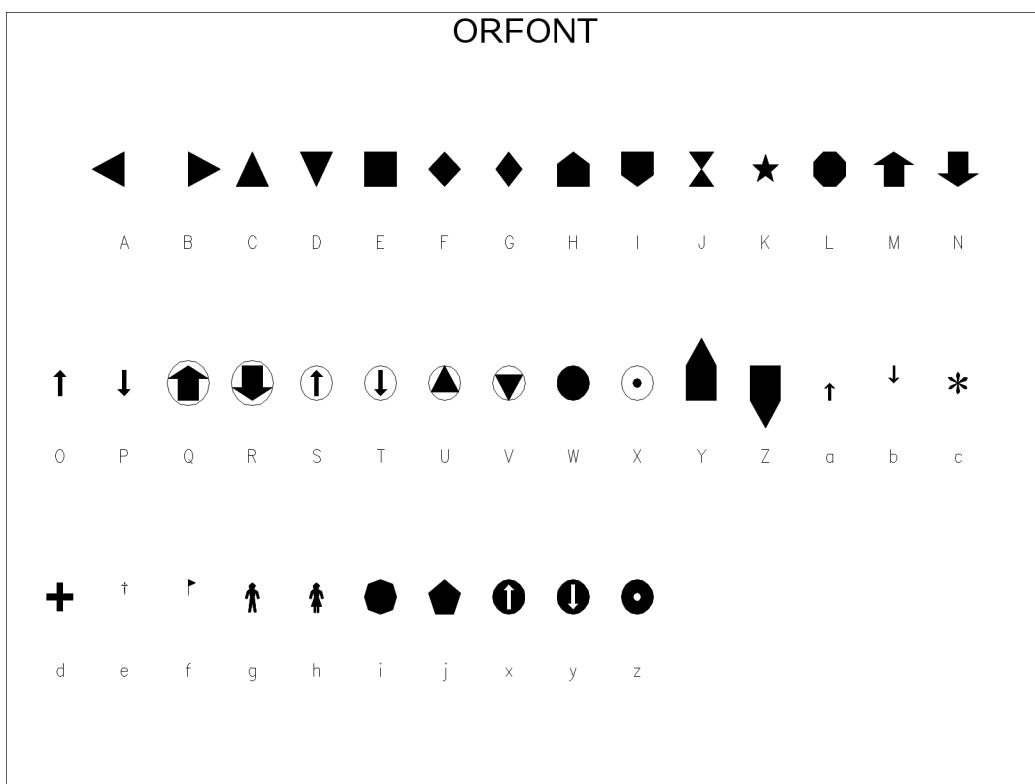

**Figure 8.9** ORFONTE - An Empty Font

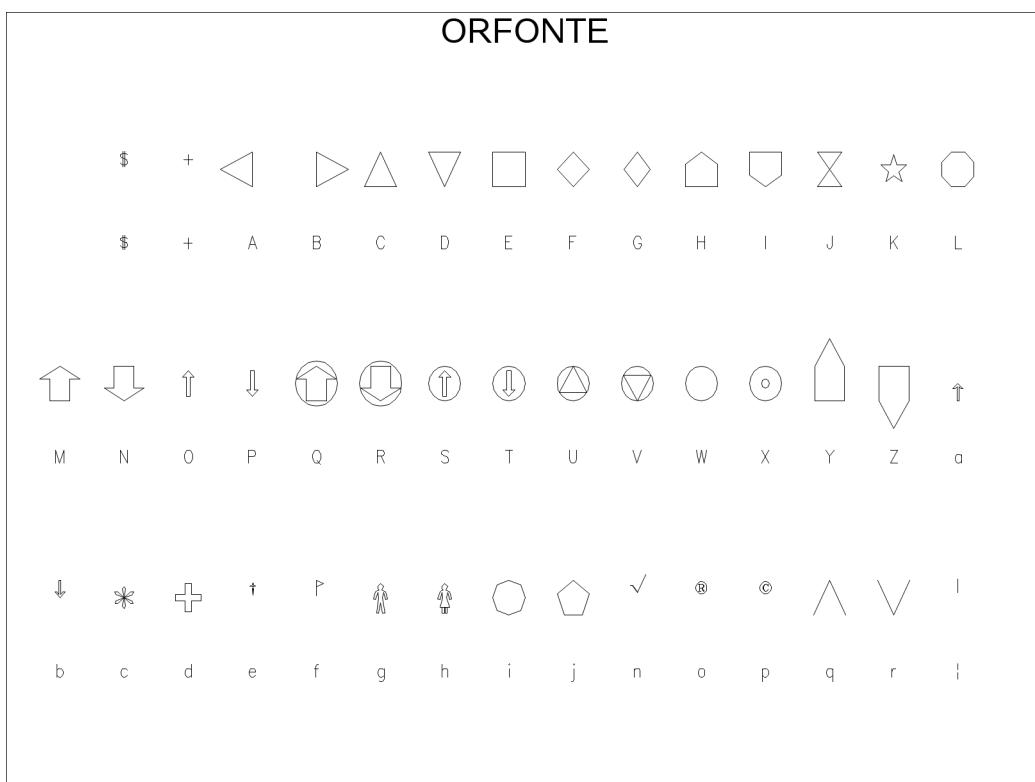

For example, to use a filled yellow “doghouse” symbol to represent milestones on the Gantt chart, specify the options

```
VMILE="H"  FMILE=ORFONT  CMILE=YELLOW
```

in the CHART statement.

If you wish to represent a CHART variable with an empty blue “circled arrow,” then specify the following options in the corresponding SYMBOL statement.

```
V="Q"  F=ORFONTE  C=BLUE;
```

## Specifying the Logic Options

The Logic options are a family of options used with the GANTT procedure that enable you to view the precedence relationships between activities on the Gantt chart. The Logic options constitute a high-resolution graphics feature and, as such, are only valid with specification of the GRAPHICS option in the PROC GANTT statement. The Logic options can accommodate nonstandard precedence relationships. The Logic options enable you to control the color, line style, and width of the connecting arcs as well as their layout and positioning on the Gantt chart. You can specify the precedence information required to draw the connections in one of two formats and store it in a data set different from the Schedule data set. You can also use the Schedule data set produced by [PROC CPM](#) to provide the precedence information. When using the Schedule data set from [PROC CPM](#), you can ensure that all the relevant precedence information exists in the data set by either specifying the [XFERVARS](#) option in the [PROC CPM](#) statement or by using an [ID](#) statement.

The Logic options are not valid with the specification of either a [BY](#) statement or the [COMBINE](#) option in the [CHART](#) statement.

In order to invoke the logic options, you need to, minimally, specify a set of variables that defines the precedence relationships between tasks. This can be done using one of two formats for defining project networks, the AOA specification or the AON specification.

### Activity-on-Arc (AOA) Specification

In the AOA specification, each activity of the project is represented by an arc. The node at the tail of the arc represents the start of the activity, and the node at the head of the arc represents the finish of the activity. The relationship between an activity and its successor is represented by setting the tail node of the successor arc to be the head node of the activity arc. One of the disadvantages of using the AOA method is that it cannot accommodate nonstandard lag types; all lag types are of the Finish-to-Start (FS) type.

The variables required by PROC GANTT to establish a valid AOA specification are defined using the [HEADNODE=](#) and [TAILNODE=](#) options in the [CHART](#) statement.

### Activity-on-Node (AON) Specification

In the AON specification, each activity is represented by a node. All arcs originating from an activity terminate at its successors. Consequently, all arcs terminating at an activity originate from its predecessors.

The variables required by PROC GANTT to establish a valid AON specification are defined by the **ACTIVITY=** and **SUCCESSOR=** options in the **CHART** statement.

Optionally, nonstandard precedence relationships can be specified using the **LAG=** option in the **CHART** statement to define a variable that defines the lag type of a relationship.

### Precedence Data Set

When using the **AON** specification, you can specify the precedence information using a data set different from the **Schedule** data set. This is particularly useful when producing several Gantt charts for the same project with different schedule information as would typically be the case when monitoring a project in progress. It eliminates the requirement that the precedence information exist in each Schedule data set and enables for more compact data. This separate data set is specified by the **PRECDATA=** option in the **PROC GANTT statement** statement and is referred to as the *Precedence data set*.

In order to graphically represent the precedence relationships derived from the Precedence data set on the Gantt chart, you must link the Precedence data set with the Schedule data set by means of a common variable. This common variable is selected as the **ACTIVITY** variable by virtue of the fact that it always exists in the Precedence data set. Thus, when using the Precedence data set, you need to ensure that the **ACTIVITY** variable exists in the Schedule data set, too.

In the event that both a valid **AOA** and a valid AON specification exist, PROC GANTT uses the AON specification by default. To override the default, use the **AOA** option in the **CHART** statement.

### Drawing the Precedence Connections

The relationship between an activity and its successor is represented on the Gantt chart by a series of horizontal and vertical line segments that connect their schedule bars corresponding to a specified type (early/late, actual, and so forth). For a given connection, the intersection of a horizontal segment with a vertical segment is called a *turning point* of the connection. The type of the schedule bar used for the connection, also called the *logic bar*, is determined by the **LEVEL=** option in the **CHART** statement.

Every connection is comprised of either three or five segments and is termed a 3-segment or a 5-segment connection, respectively. The segments are routed in the following sequence:

- a) a horizontal segment that originates from the appropriate end of the logic bar corresponding to the activity. The length of this segment is controlled by the **MINOFFGV=** and **MININTGV=** options in the **CHART** statement.
- b) a vertical segment traveling from activity to the successor
- c) a horizontal segment traveling towards the appropriate end of the successor's logic bar. The length of this segment is determined by the **MINOFFLV=** and **MAXDISLV=** options in the **CHART** statement.
- d) a vertical and horizontal segment into the logic bar of the successor

Every connection begins with a horizontal line segment originating from the activity's logic bar and ends with a horizontal line segment terminating at the successor's logic bar. If the lag type of the relationship is SS or SF, the initial horizontal segment originates from the left end of the activity's logic bar, otherwise it originates from the right end of the logic bar. If the lag type of the relationship is SS or FS, the final horizontal segment terminates at the left end of the successor's logic bar, otherwise it terminates at the right end of the logic bar.

**NOTE:** The ends of the bars must be consistent with the lag type of the connection if it is to be drawn; that is, the left end of the activity's logic bar must represent a start time if an SS or SF lag type connection is to be drawn, and the right end of the activity's logic bar must represent a finish time if an FS or FF lag type connection is to be drawn.


Violation of these conditions is unlikely when using the Schedule data set generated by PROC CPM. An example violating these conditions is a Schedule data set containing incorrect or invalid data. The following example illustrates two observations that are in violation of these conditions. The first observation is invalid data (E\_START greater than E\_FINISH) while the second observation is incomplete (missing E\_START and L\_FINISH times).

E_START	E_FINISH	L_START	L_FINISH
03MAR04	01MAR04	.	.
.	05MAR04	07MAR04	.

The following figure illustrates two typical precedence connections between an activity and its successor.

ACTIVITY	SUCCESSOR	LAG
A	C	FS
B	C	FS

**Figure 8.10** Typical Precedence Connections

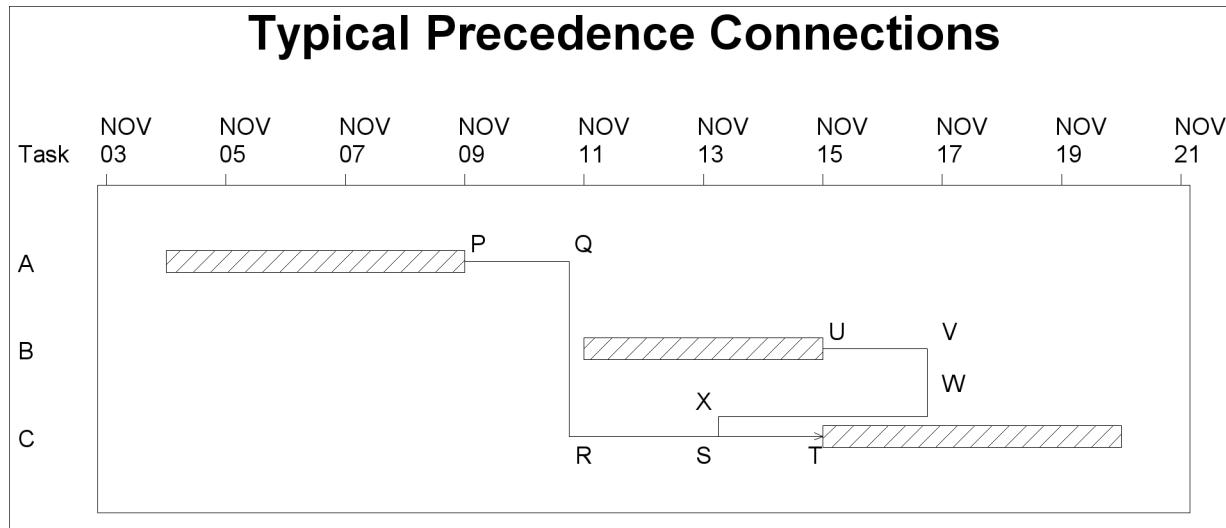

The connection from activity **A** to activity **C** is comprised of three segments PQ, QR, and RT whereas the connection from activity **B** to activity **C** is made up of five segments UV, VW, WX, XS, and ST; the two additional segments correspond to the optional segments mentioned in item **d**) above. Points Q, R, V, W, X, and S are turning points.

## Formatting the Axis

If neither **MINDATE=** nor **MAXDATE=** have been specified, the time axis of the Gantt chart is extended by a small amount in the appropriate direction or directions in an attempt to capture all of the relevant precedence connections on the chart. While this will succeed for the majority of Gantt charts, it is by no means guaranteed. If connection lines still tend to run off the chart, you can perform one or both of the following tasks.

- Use the **MINDATE=** or **MAXDATE=** options (or both) in the **CHART** statement to increase the chart range as necessary.
- Decrease the values of the **MINOFFGV=**, **MININTGV=**, **MAXDISLV=**, and **MINOFFLV=** options to reduce the horizontal range spanned by the vertical segments so that they will lie within the range of the time axis.

On the other hand, if the automatic extension supplied by **PROC GANTT** is excessive, you can suppress it by specifying the **NOEXTRANGE** option in the **CHART** statement.

The following section, “Controlling the Layout,” addresses the **CHART** statement options **MINOFFGV=**, **MININTGV=**, **MINOFFLV=**, and **MAXDISLV=** which control placement of the vertical segments that make up a connection. For most Gantt charts, default values of these options will suffice since their usage is typically reserved for “fine tuning” chart appearance. This section can be skipped unless you want to control the layout of the connection. The description of the layout methodology and concepts is also useful to help you understand the routing of the connections in a complex network with several connections of different types.

## Controlling the Layout

The concepts of global and local verticals are first introduced in order to describe the function of the segment placement controls.


### **Global Verticals**

In the interest of minimizing clutter on the chart, each activity is assigned a maximum of two vertical tracks for *placement* of the vertical segment described in item **b**) above. One vertical track is maintained for SS and SF lag type connections and is referred to as the *start global vertical* of the activity, while the other vertical track is maintained for FS and FF lag type connections and is referred to as the *finish global vertical* of the activity. The term *global vertical* refers to either start global vertical or finish global vertical.

**NOTE:** The use of the term “global” is attributed to the fact that in any connection from an activity to its successor, the global vertical of the activity corresponds to the *only segment* that travels from activity to successor.

Figure 8.11 illustrates the two global verticals of activity **A**.

**Figure 8.11** Global Verticals

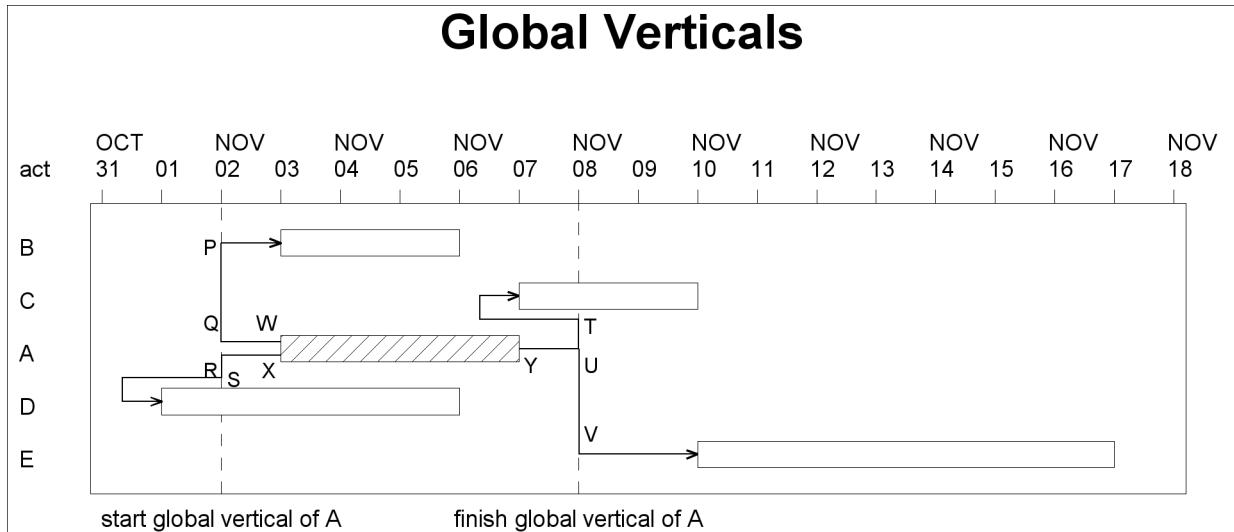

Activity **A** has four successors: activities **B**, **C**, **D**, and **E**. The lag type of the relationship between **A** and **B** is nonstandard, namely ‘Start-to-Start’, as is that between **A** and **D**. The other two lag types are standard. The start and finish global verticals of activity **A** are represented by the two dotted lines. The vertical segments of the SS lag type connections from **A** to **B** and from **A** to **D** that are placed along the start global vertical of **A** are labeled PQ and RS, respectively. The vertical segments of the FS lag type connections from **A** to **C** and from **A** to **E** that are placed along the finish global vertical of **A** are labeled TU and UV, respectively.

For a given connection from activity to successor, the vertical segment that is placed on the activity global vertical is connected to the appropriate end of the logic bar by the horizontal segment described in item **a**) above. The minimum length of this horizontal segment is specified with the **MINOFFGV=** option in the **CHART** statement. Further, the length of this segment is affected by the **MININTGV=** option in the **CHART** statement, which is the minimum interdistance of any two global verticals. In Figure 8.11, the horizontal segments QW and RX connect the vertical segments PQ and RS, respectively, to the logic bar and the horizontal segment YU connects both vertical segments TU and UV to the logic bar.

### **Local Verticals**

Each activity has seven horizontal tracks associated with it, strategically positioned on either end of the logic bar, above the first bar of the activity, and below the last bar of the activity. These tracks are used for the *placement* of the horizontal segments described in items **c**) and **d**), respectively.

Figure 8.12 illustrates the positions of the horizontal tracks for an activity in a Gantt chart with four schedule bars. Three of the horizontal tracks, namely **track 1**, **track 4**, and **track 7**, service the start of the logic bar and are connected to one another by a vertical track referred to as the *Start Local Vertical*. Similarly, the horizontal tracks **track 2**, **track 3**, **track 5**, and **track 6** service the finish of the bar and are interconnected by a vertical track referred to as the *Finish Local Vertical*. The local verticals are used for *placement* of the vertical segment described in item **d**) above.


**NOTE:** The use of the term “local” is attributed to the fact that the local vertical is used to connect horizontal tracks associated with the *same* activity.

Notice that **track 1** and **track 7** terminate upon their intersection with the start local vertical and that **track 2** and **track 6** terminate upon their intersection with the finish local vertical.

The minimum distance of a local vertical from its respective bar end is specified with the **MINOFFLV=** option in the CHART statement. The maximum displacement of the local vertical from this point is specified using the **MAXDISLV=** option in the CHART statement. The **MAXDISLV=** option is used to offset the local vertical in order to prevent overlap with any global verticals.

Arrowheads are drawn by default on the horizontal tracks corresponding to the logic bar, namely **track 3**, **track 4**, and **track 5**, upon entering the bar and on continuing pages. The **NOARROWHEAD** option is used to suppress the display of arrowheads.

**Figure 8.12** Local Verticals

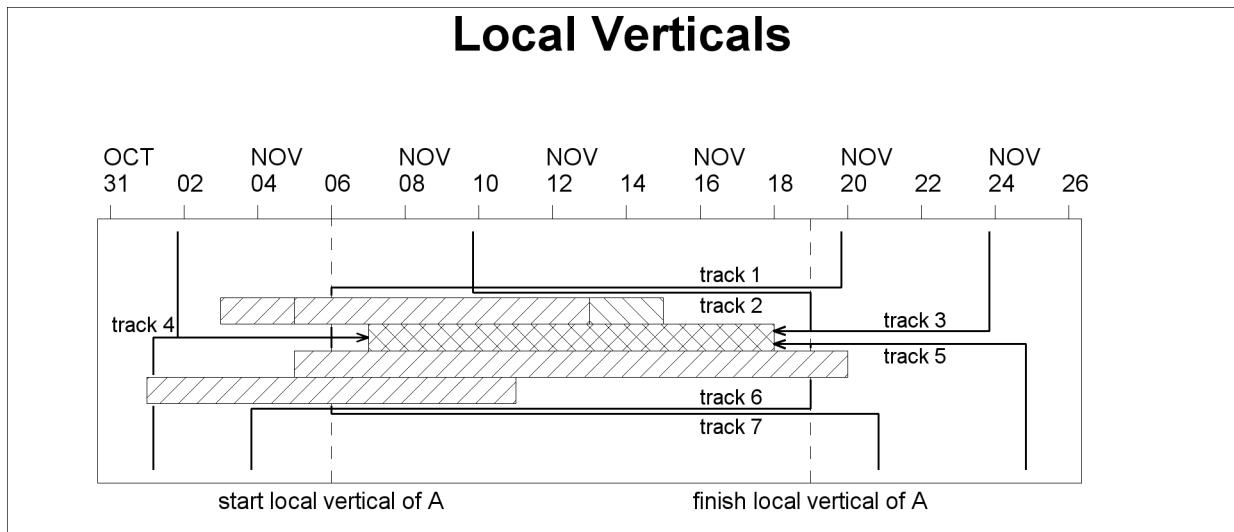

### **Routing the Connection**

The routing of the precedence connection from an activity to its successor is dependent on two factors, namely


- the horizontal displacement of the appropriate global vertical of the activity relative to the appropriate local vertical of the successor
- the vertical position on the task axis of the activity relative to the successor

The routing of a SS or FS type precedence connection from activity to successor is described below. A similar discussion holds for the routing of a SF or FF type precedence connection.

Suppose the activity lies above the successor. Let the start local vertical of the successor be denoted by  $s/lv$ , and let the appropriate global vertical of the activity be denoted by  $gv$ .

#### **Case 1:**


If  $gv$  lies to the left of  $s/lv$ , then the connection is routed vertically down along  $gv$  onto **track 4** of the successor, on which it is routed horizontally to enter the bar. The resulting 3-segment connection is shown in Figure 8.13.

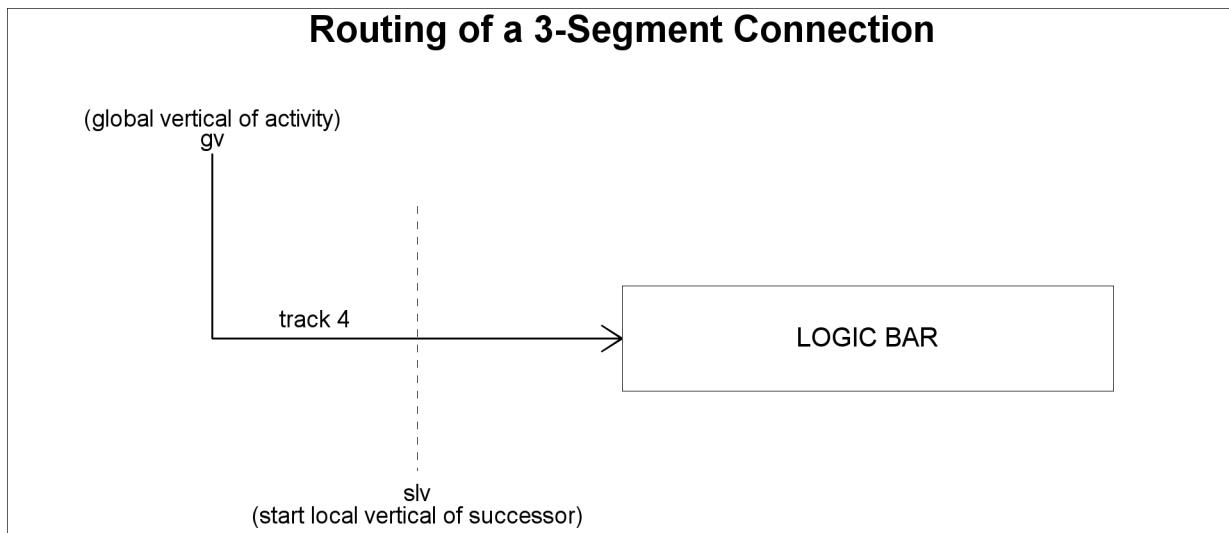**Figure 8.13** 3-Segment Connection

An example of this type of routing is illustrated by the connection between activities **A** and **C** in Figure 8.10.

#### Case 2:

If *gv* lies to the right of *slv*, then the connection is routed vertically down along *gv* onto **track 1** of the successor, horizontally to the left to meet *slv*, vertically down along *slv* onto **track 4** of the successor and horizontally to the right to enter the bar. The resulting 5-segment connection is shown in Figure 8.14.

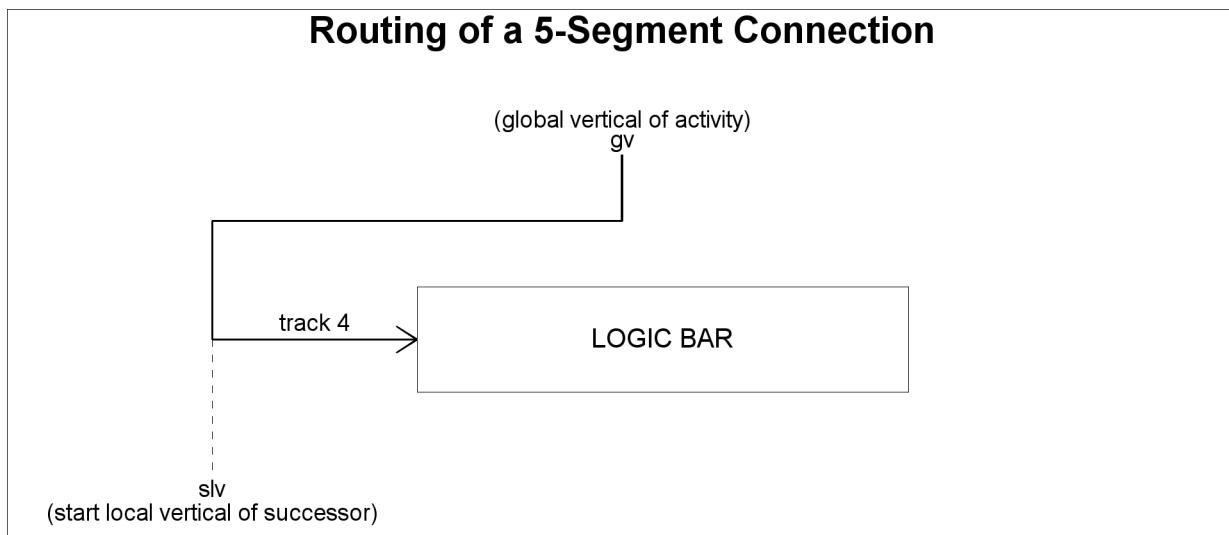**Figure 8.14** 5-Segment Connection

This type of routing is illustrated by the connection between activities **B** and **C** in Figure 8.10.

An identical description applies when the activity lies below the successor, with the only difference being that **track 7** is used in place of **track 1** (see Figure 8.12).

---

## Automatic Text Annotation

The automatic text annotation feature is designed specifically for labeling Gantt charts independently of the SAS/GRAPH Annotate facility. This facility enables you to display label strings with a minimum of effort and data entry while providing the capability for more complex chart labeling situations. Some of the properties that characterize this feature are

- the ability to tag labels. This enables you to define 1-1, 1-many, many-1, and many-many relationships.
- the ability to link label coordinates and label strings to variables in the Schedule data set. This enables the Label data set to remain unchanged even if the Schedule data set changes, such as when monitoring a project.
- the ability to automatically format or convert numeric variable values that have been specified for label text strings
- the ability to automatically split strings embedded with blanks to make the pieces as equal in length as possible, with the provision to override this behavior by specifying a split character
- the ability to mix data and percentage coordinates
- the ability to clip labels running off the frame of the Gantt chart

All relevant information is contained in a SAS data set specified using the **LABDATA=** data set option in the **PROC GANTT** statement. This data set is also referred to as the Label data set in the context of this documentation. The Label data set is required to contain certain variables in order to determine the label string and the positional information related to the string. At the very least, it requires three variables, one to determine the string to be displayed, one to determine the horizontal position, and one to determine the vertical position. The procedure terminates if it cannot find the required variables.

**Table 8.8** Special Symbol Table

Determining the ...	requires the following variables
Label text string	_LVAR and/or _LABEL
Horizontal placement position	_XVAR and/or _X
Vertical placement position	LABVAR= and/or _Y

The **LABVAR** variable refers to the variable specified with the **LABVAR=** option in the **CHART** statement. It is the LABVAR variable that links the **Schedule** and **Label** data sets together. As far as possible, the procedure attempts to use the **\_X**, **\_Y**, and **\_LABEL** variables in the Label data set. However, a link established using the LABVAR variable makes the Schedule data set a secondary source of information for determining positional and text string information for linked observations. The exact meaning of the preceding variables is explained later in this chapter.

Note that, other than the preceding requirements, there are no further restrictions on the Label data set. In fact, the Schedule data set can also be specified as the Label data set as long as the required variables are present.

There are several optional variables in the Label data set. These variables enable you to specify offsets in both horizontal and vertical directions from the given coordinate position; adjust graphical attributes such as baseline angles, character rotations, colors, fonts, and heights; control justification of strings; control placement behavior at pagebreaks; and specify coordinate reference systems for the horizontal and vertical values.

## **Label Data Set**

You specify the Label data set using the **LABDATA=** option in the **PROC GANTT** statement. This initiates the labeling of the Gantt chart. The Label data set contains the information that provides the means of determining the label strings and their placement positions. As far as possible, the procedure attempts to use the **\_X**, **\_Y**, and **\_LABEL** variables in the Label data set to extract the horizontal position, the vertical position, and the text string, respectively. The Schedule data set acts as a secondary source of information for all Label data set observations that are linked to it. The priority mechanism is described in the section “Determining the Vertical Position” on page 553.

## **Determining the Vertical Position**

You can specify the vertical position for a label string in one of two ways, either directly by using the **\_Y** variable in the Label data set or indirectly by associating the label with an activity or activities. In the latter case, the vertical position is determined by the relative position of the activity on the activity axis of the Gantt chart.

### ***Directly using \_Y***

The procedure determines the vertical position using the **\_Y** variable. You specify the coordinate system for the value of **\_Y** with the optional **\_YSYS** variable. A value of DATA or DATAVAL for the **\_YSYS** variable indicates that the unit of measurement is data values. This is also the default coordinate system for **\_Y**. A value of PCT or PCTVAL indicates that the unit of measurement is percentage of the procedure output area. When the coordinate system for **\_Y** is based on data values, the values that **\_Y** can take are restricted to positive real numbers with the exception of -1, which is a special value indicating that the label be displayed for every activity. In effect, this is a more concise way of linking a label to every activity.

### ***Indirectly using LABVAR=***

If the **\_Y** variable does not exist or its value is missing, the procedure uses the value of the **LABVAR** variable to determine the vertical position of the label. If the **LABVAR=** option is specified and the value of the **LABVAR** variable is nonmissing, the observation is displayed for every activity that provides a matching value for the **LABVAR** variable. It is quite possible that there are no activities that provide a match, in which case the Label data set observation is ignored. Likewise, the Label data set observation is ignored if the value of the **LABVAR** variable is missing,

When the vertical position is based on an integer value for **\_Y** or linkage using the **LABVAR** variable, the default position for the baseline of the string is the top of the first schedule bar corresponding to the activity (unless offsets **\_XOFFSET** or **\_YOFFSET** are used).

## **Determining the Horizontal Position**

The procedure attempts to determine the horizontal position using the **\_X** variable. You specify the coordinate system for the value of **\_X** with the optional **\_XSYS** variable. A value of DATA or DATAVAL for the **\_XSYS** variable indicates that the unit of measurement is data values. This is also the default coordinate system for

X. A value of PCT or PCTVAL indicates that the unit of measurement is percentage of the procedure output area.

If the X variable does not exist or its value is missing, the procedure ignores the Label data set observation if the observation is not linked to an activity in the Schedule data set. However, if the label is linked to an activity (either by the **LABVAR** variable or a value of -1 for Y, as described previously), the procedure extracts the horizontal position using the XVAR variable in the Label data set. The XVAR variable values are names of numeric variables in the Schedule data set. If the XVAR value is not missing, the horizontal position is the value of the specified variable in the Schedule data set corresponding to the activity. If no such variable exists in the Schedule data set or its value is missing, no label is displayed for this particular (activity, label) link. As with the X variable, the XSYS variable names the unit of measurement for the associated Schedule data set variable.

## Coordinate Systems

Coordinates can be specified in data values and percentages. It is important to note a significant difference between these two systems when using multiple pages. A data coordinate value is a point along either the time or activity axis, and it can be related to a page number and to a position on that page in the relevant direction. A percentage value, on the other hand, cannot be related to a particular page and, as such, is treated as applicable to every single page. It is possible to mix data and percentage coordinates. That is, the horizontal position can be in data values and the vertical position can be in percentage values, and vice versa. By mixing coordinate systems, you can get as flexible as you want in labeling Gantt charts.

- If both coordinates are in data values, the label is displayed at a specific coordinate on a specific page.
- If the horizontal coordinate is a percentage, the label is displayed at this horizontal position for every page that corresponds to the vertical position. Likewise, if the vertical position is a percentage, the label is displayed at this vertical position for every page that corresponds to the horizontal position. For example, you can display certain headings at the top of the Gantt chart or at the bottom of the Gantt chart by using a data value for the vertical position and a percentage value for the horizontal position.
- If the horizontal and vertical coordinates are both percentages, the label is displayed on every page at the specified coordinate. This feature can be used to display text that appears on every page, much like titles and footnotes, for example.

## Determining the Label String

The technique for determining the label string is similar to that of determining the horizontal position.

As far as possible, the procedure attempts to use the LABEL variable. If the LABEL variable does not exist or its value is missing, the procedure ignores the label data observation if the observation is not linked to an activity in the **Schedule** data set. However, if the label is linked to an activity (either by the **LABVAR** variable or a value of -1 for Y, as described previously), the procedure extracts the text string from the Schedule data set using the LVAR variable. The LVAR variable values are names of variables in the Schedule data set. If the LVAR value is not missing, the text string is the value of the specified variable in the Schedule data set corresponding to the activity. If no such variable exists in the Schedule data set or if the value is missing, no label is displayed for this particular (activity, label) link.

Note that the `_LABEL` variable and the Schedule data set variables named by `_LVAR` are not restricted to be of character type. These variables can be character or numeric, formatted or unformatted. The strings are displayed using the following rules:

- If the variable is of character type, the label is the character string corresponding to the given activity.
- If the variable is of numeric type and formatted, the label is the formatted string.
- If the variable is of numeric type and unformatted, the label is the number displayed as a string with an integer part of up to `LABMAXINT=` digits and a maximum of `MAXDEC=` decimal positions. The `LABMAXINT=` and `MAXDEC=` options are specified in the PROC GANTT statement and their default values are 16 and 2, respectively.

## Optional Information

In addition to specifying the horizontal and vertical coordinates as described previously, you can also specify a relative offset from these values using the `_XOFFSET` and `_YOFFSET` variables. These are optional variables and their default values are both 0. The unit of measurement for the `_XOFFSET` variable is in `MININTERVAL` units, and the direction of increase is from left to right. The unit of measurement for the `_YOFFSET` variable is in barheights, and the direction of increase is from top to bottom. When labels are split, the offset variables pertain only to the first piece of the label. The positions of the remaining split pieces are determined from the positioning of the first piece. The adjusted coordinate after taking the offsets into account is what is used for the placement of the string and is known as the referenced coordinate.

You can control the color and font of the label strings using the `_CLABEL` and `_FLABEL` variables, respectively. The values for the `_CLABEL` variable are any valid SAS/GRAFH color names. If the `_CLABEL` variable does not exist or its value is missing, the value of the `CTEXT=` option in the `CHART` statement is used. The values for the `_FLABEL` variable are any valid SAS/GRAFH font names. If the `_FLABEL` variable does not exist or its value is missing, the value of the `FONT=` option in the `CHART` statement is used.

You can control the height of the label strings with the `_HLABEL` variable. The units of measurement are in barheights. If the `_HLABEL` variable does not exist or its value is missing, the default value of 1 is used.

You can specify the angle of the character baseline with respect to the horizontal in degrees using the `_ALABEL` variable. If the `_ALABEL` variable does not exist or its value is missing, the default value of 0 is used. You can specify the rotation angle of each character in the string in degrees with the `_RLABEL` variable. If the `_RLABEL` variable does not exist or its value is missing, the default value of 0 is used.

You can control the alignment of the string with the `_JLABEL` variable. Strings can be displayed left-justified, right-justified, or centered at the specified coordinate. By default, all strings are displayed left-justified. The valid values are L or LEFT for left justification, R or RIGHT for right justification, and C or CENTER for centered justification.

The `_PAGEBRK` variable gives you displaying control when the referenced coordinate of a label coincides with a pagebreak tickmark and the horizontal coordinate is measured in data values. You can specify on which of the two pages you would like the label to be displayed. The default always displays the label on the first page associated with the common tickmark except when the tickmark is the very first tickmark on the Gantt chart. Valid values are 0 (default), 1 (use first page), or 2 (use second page).

## Variables in the LABELDATA= data set

The following table lists all the variables associated with the Label data set and their interpretations by the GANTT procedure. The table also lists for each variable its type, the possible values it can assume, and its default value.

**Table 8.9** Label Data Set Variables

Name	Type	Description	Allowed Values	Defaults
_Y	N	y position		
_X	N	x position		
_LABEL	C/N	Label string		
_XVAR	C	Name of numeric SAS var in DATA= ds for x position		
_LVAR	C	Name of SAS var in DATA= ds for label string		
_XSYS	C	Coordinate system for _X, _XVAR	DATA, DATAVAL, PCT, PCTVAL	DATA
_YSYS	C	Coordinate system for _Y	DATA, DATAVAL, PCT, PCTVAL	DATA
_PAGEBRK	N	Resolve pagebreak referenced display	0, 1, 2	0
_XOFFSET	N	Horizontal offset in minintervals		0
_YOFFSET	N	Vertical offset in bar heights		0
_ALABEL	N	Baseline angle in degrees		0
_CLABEL	C	SAS/GRAFH color name		CTEXT=
_FLABEL	C	SAS/GRAFH font name		FONT=
_HLABEL	N	Height in barheights		1
_JLABEL	C	Justify text	L, LEFT, R, RIGHT, C, CENTER	L
_RLABEL	N	Character rotation in degrees		0
LABVAR=	C/N	Variable linking activities to labels		

---

## Web-Enabled Gantt Charts

The **WEB** variable enables you to define an HTML reference for each activity. This HTML reference is currently associated with all the schedule bars, milestones, and ID variables that correspond to the activity. The WEB variable is a character variable, and the values need to be of the form “HREF=htmlpage.”

In addition, you can also store the coordinate and link information defined by the WEB= option in a SAS data set by specifying the **IMAGEMAP=** option in the **PROC GANTT** statement. By processing this SAS data set using a DATA step, you can generate customized HTML pages for your Gantt chart.

---

## Mode-Specific Differences

All the options that are valid for line-printer, full-screen, and graphics mode Gantt charts are explained in detail in the section “[Syntax: GANTT Procedure](#)” on page 492. With few exceptions, the options listed in the section “[General Options](#)” on page 499 have the same interpretation in all three modes.

[Table 8.10](#) lists those line-printer options that have a different interpretation for the graphics version of PROC GANTT. [Table 8.11](#) lists options specific for graphics charts and the equivalent line-printer/full-screen option. [Table 8.12](#) lists options specific for line-printer and full-screen charts and the equivalent graphics option.

**Table 8.10** Line-Printer Options and Corresponding Graphics Interpretation

Line-Printer Option	Graphics Mode Interpretation
SCALE=scale	One column is denoted by $(1/h)\%$ of the screen width, where HPOS=h.
SKIP=skip	skip number of bar heights are skipped between the bars for two consecutive activities. The value 0 is not valid in the graphics case.

**Table 8.11** Graphics Mode Options and Line-Printer/Full-Screen Equivalent

Graphics Option/Statement	Line-Printer/Full-Screen Equivalent
LHCON= <i>linetype</i>	HCONCHAR='character'
LREF= <i>linetype</i>	REFCHAR='character'
LTNOW= <i>linetype</i>	TNCHAR='character'
NOFRAME	FORMCHAR='string'
PATTERN statement	JOINCHAR='string' and SYMCHAR='string'
SYMBOL statement	First character of variable name is plotted (See <a href="#">CHART specifications</a> )
VMILE= <i>value</i>	MILECHAR='character'
WTNOW= <i>width</i>	TNCHAR='character'

**Table 8.12** Line-Printer/Full-Screen Mode Specific Options

Line-Printer/Full-Screen Option	Graphics Equivalent
FORMCHAR='string'	NOFRAME
HCONCHAR='character'	LHCON= <i>linetype</i> , CHCON= <i>color</i>
HOLICHR='character'	PATTERN statement 7
JOINCHAR='string'	PATTERN statements 1-6, 8, and 9
MILECHAR='character'	VMILE= <i>value</i> , FMILE= <i>font</i> , HMILE= <i>height</i> , CMILE= <i>color</i>
REFCHAR='character'	LREF= <i>linetype</i> , CREF= <i>color</i>
SYMCHAR='string'	PATTERN statements 1-6, 8, and 9
TNCHAR='character'	LTNOW= <i>linetype</i> , WTNOW= <i>width</i> , CTNOW= <i>color</i>

---

## Displayed Output

The GANTT procedure produces one or more pages of displayed values and a plot of the schedule. If the **SUMMARY** option is specified, the chart is preceded by a detailed description of the symbols used. A legend is displayed at the foot of the chart on each page unless suppressed by the **NOLEGEND** option. The main body of the output consists of columns of the **ID** values and the Gantt chart of the schedule.

For each activity in the project, PROC GANTT displays the values of the ID variables in the ID columns and plots any combination of the following schedules: the predicted schedule as specified by the early and late start and finish times, the actual schedule as specified by the actual start and finish times, the resource-constrained schedule as specified by the resource-constrained start and finish times, and the baseline schedule as specified by the baseline start and finish times. The procedure looks for default variable names for each of these times (E\_START for early start, E\_FINISH for early finish, S\_START for resource-constrained start times, and so on), or you can explicitly specify the names of the appropriate variables using the **ES=**, **EF=**, **LS=**, ... options.

By specifying the **COMBINE** option in the **CHART** statement, you can request PROC GANTT to represent early, late, and actual schedule information on a single bar rather than use two separate bars (one for the early and late schedules and the other for the actual schedule.) PROC GANTT automatically draws a timenow line when the **COMBINE** option is specified with the property that all times to the left of the line represent the actual schedule times (that is, times that have already taken place) and all times to the right of the line represent the predicted early/late schedule times (times that have not yet taken place.)

Normally, each observation in the **Schedule** data set is assumed to denote a new activity, and a new set of ID values are displayed and the schedules corresponding to this activity are plotted on the chart. There are two exceptions to this rule:

- If the ID values for two or more consecutive observations are identical, only the first such observation is used.
- If there is a variable named **SEGMT\_NO** in the **Schedule** data set, PROC GANTT assumes that the data set contains observations for segments of activities that were split during resource-constrained scheduling. In accordance with the conventions used by **PROC CPM**, only observations with a missing value for **SEGMT\_NO** are assumed to denote a new activity. Further, the data are assumed to be sorted by **SEGMT\_NO** for each activity. For each activity, PROC GANTT plots the schedules corresponding to the **ES**, **EF**, **LS**, **LF**, **AS**, and **AF** variables on the basis of the first observation for this activity, namely the observation with a missing value for the **SEGMT\_NO** variable. This observation is also the one used for displaying values for the **ID** variables for this activity. If the activity is not split, this same observation is also the one used to plot the resource-constrained schedule as well as the baseline schedule. However, if the activity is split, then all the observations for this activity with integer values for the variable **SEGMT\_NO** are used to plot the resource-constrained schedule as disjoint segments on the line used for plotting the **S\_START** and **S\_FINISH** times. Furthermore, PROC GANTT plots the baseline schedule corresponding to the **BS** and **BF** variables based on the last such observation, namely the observation with the largest value for the **SEGMT\_NO** variable.

In addition to the schedules that are plotted, the Gantt chart also displays any variables specified in the **CHART** statement. Holidays, weekends, and breaks within a day are marked as appropriate. For details on how to specify holidays, weekends, and breaks within a day, see the section “[Multiple Calendars and](#)

*Holidays*" on page 530. You can also represent zero duration activities with **milestone symbols**, draw a **timenow line** to reflect the current time of the project, draw horizontal **connect** lines, draw vertical **reference lines**, and group the activities by **zones** on the Gantt chart. It is important to note that all times are plotted at the start of the appropriate time period. Thus, if the chart starts on June 1, 2004, in column 15 of the page and the value of **E\_START** is '2JUN04,' **MININTERVAL=DAY**, and **SCALE=5**, then the early start time is plotted in column 20.

Each activity is identified by a job number (unless the **NOJOBNUM** option is used), which appears as the first column of activity text. The next column of activity text identifies the values of the **ZONE=** variable, if specified. This column can be suppressed by specifying the **NOZONECOL** option in the CHART statement. Next to appear are the ID variables in the order in which they are specified in the CHART statement. If the time axis of the chart is very wide, causing it to be divided across more than one page, the ID variables, by default, do not appear on continuation pages. You need to specify the **IDPAGES** option to produce the ID variable columns on every page. By default, if the ID variables occupy too much space, leaving no room for the chart to be started on the first page, they are omitted and a warning message is printed to the log. You can override this behavior by using the **MAXIDS** option. Column headings for the ZONE and ID variables consist of either variable labels (if they are present and if space permits) or variable names. To suppress variable labels in column headings, use the **NOLABEL** system option. If a ZONE or ID variable is formatted, the value is displayed using that format. If the **CRITFLAG** option is specified, a flag is displayed to the right of the ID values that indicates how critical the activity is. This flag is also repeated on continuation pages if the time axis occupies more than one page. The body of the chart starts to the right of this flag.

By default, the GANTT procedure is invoked in graphics mode. In graphics mode, you can fit the Gantt chart entirely on one page by specifying the **COMPRESS** option in the CHART statement. The **HPAGES=** and **VPAGES=** options take this one step further by enabling you to control the number of pages that you want the Gantt chart to be compressed into. The **PCOMPRESS** option behaves much like the **COMPRESS** option except that all compression is performed in a proportional manner, that is, by maintaining the aspect ratio of the Gantt chart.

PROC GANTT can display the precedence relationships (including nonstandard types) between activities on the Gantt chart by means of directed links between activities. Each link is drawn so as to convey the type of precedence relationship it represents. See the section "[Specifying the Logic Options](#)" on page 545 for a detailed description on how this can be done.

In addition, graphics mode provides you with the easy-to-use **automatic text annotation facility** to generate labels on the Gantt chart. You can link labels and their coordinates to variables in the schedule data set and also have complete control over all attributes such as font, color, angle, rotation, and so forth. You also have the additional capability of annotating text and graphics independently on the Gantt chart by using the SAS/GRAF Annotate facility.

The GANTT procedure offers you a wide variety of options in addition to text, bar, symbol, and line formatting controls to customize your Gantt chart. These features enable you to create a wide variety of charts such as Logic Gantt charts, zoned Gantt charts, multiproject Gantt charts, **Web-enabled Gantt charts**, and multiprocess Gantt charts, to name but a few.

## Macro Variable \_ORGANTT

The GANTT procedure defines a macro variable named **\_ORGANTT**, which is set at procedure termination. This variable contains a character string that indicates the status of the procedure and also provides chart

specific information with respect to each Gantt chart produced by invocation of the GANTT procedure. This includes charts resulting from multiple **CHART** statements and **BY** groups.

The format of the \_ORGANTT string for a GANTT procedure invocation with  $n$  CHART statements is as follows:

```
STATUS= REASON= CHART1 chart1info # ... CHARTn chartninfo #
```

where the value of STATUS= is either SUCCESSFUL or ERROR\_EXIT, and the value of REASON= is one of the following:

- BADDATA\_ERROR
- MEMORY\_ERROR
- IO\_ERROR
- SEMANTIC\_ERROR
- SYNTAX\_ERROR
- GANTT\_BUG
- UNKNOWN\_ERROR

The notation chart $i$ info is a string of the form

```
SCALE= INCREMENT= SKIP= HPAGES= VPAGES= SEGNAME=
```

if there are no BY groups, and it is a string of the form

BY1 by1info: ... BY $m$  by $m$ info:

where by $j$ info is a string of the form

```
SCALE= INCREMENT= SKIP= HPAGES= VPAGES= SEGNAME=
```

if there are  $m$  BY groups. In other words, the macro contains an informational substring for every chart produced, using the symbol “#” as a CHART statement delimiter and the symbol “:” as a BY statement delimiter within CHART statements.

The chart specific information given in \_ORGANTT is described below along with the identifying keyword preceding it. It should be noted that these values refer to those actually used in producing the chart and are not necessarily the same as those specified in the invocation of the procedure.

- SCALE= The value of scale
- INCREMENT= The value of increment
- SKIP= The value of skip
- HPAGES= The number of horizontal pages
- VPAGES= The number of vertical pages
- SEGNAME= The name of the first chart segment in graphics mode

**NOTE:** Some of the information might be redundant or predictable in certain display modes. For example, the value of SEGNAME= is empty in line-printer and full-screen modes. The values of HPAGES= and VPAGES= are equal to 1 in full-screen mode.

This information can be used when PROC GANTT is one step in a larger program that needs to determine whether the procedure terminated successfully or not. Because \_ORGANTT is a standard SAS macro variable, it can be used in the ways that all macro variables can be used.

---

## Computer Resource Requirements

There is no inherent limit on the size of the project that the GANTT procedure can accommodate. The number of activities in the Gantt chart is restricted only by the amount of memory available. Other memory-dependent factors are the type of Gantt chart required and the desired display mode.

Naturally, there needs to be a sufficient amount of core memory available in order to invoke and initialize the SAS System as well as to meet the memory requirements of the specific mode in which you invoke the procedure. For example, more memory is required when you use high-resolution graphics than when you use line-printer mode because the graphics sublibrary has to be loaded. The procedure attempts to store all the data in core memory. However, if there is insufficient core memory available for the entire project, the GANTT procedure resorts to using utility data sets and swaps between core memory and utility data sets as necessary.

The data storage requirement for the GANTT procedure is proportional to the number of activities in the project, and it depends on the number of schedule variables, the number of ID variables, and whether the Logic and Labeling options have been specified or not.

---

## ODS Style Templates

ODS style templates, or *styles*, control the overall look of your output. An ODS style template consists of a set of *style elements*. A style element is a collection of *style attributes* that apply to a particular feature or aspect of the output. You can specify a value for each attribute in a style. See Chapter 21, “Statistical Graphics Using ODS” (*SAS/STAT User’s Guide*), for a thorough discussion of ODS Graphics.

To create your own style or to modify a style for use with ODS Graphics, you need to understand the relationships between style elements and graph features. This information is provided in the ODS Graphics documentation at <http://support.sas.com/documentation/onlinedoc/base/>. You can create and modify style templates with the TEMPLATE procedure. For more information, see the section “TEMPLATE Procedure: Creating a Style Template” in the *SAS Output Delivery System: User’s Guide*. Kuhfeld (2010) also offers detailed information and examples.

## PROC GANTT Style Template

A predefined ODS style template named GANTT is available for the GANTT procedure. You can use the template to maintain a consistent appearance in all graphical output produced by the procedure.

To change the current style, specify the `STYLE=` option in an ODS destination statement. The specified style is applied to all output for that destination until you change or close the destination or start a new SAS session. For example, the following statement specifies that ODS should apply the GANTT style template to all HTML output:

```
ods html style=gantt;
```

To disable the use of graphical styles, specify the SAS system option NOGSTYLE.

The parent style template for the GANTT style is the DEFAULT style. Table 8.13 lists the style elements (in bold) and corresponding attributes specified in the GANTT style. The table also indicates which (if any) PROC GANTT options or graphics options (in a GOPTIONS statement) can be used to override the value of a style attribute.

**Table 8.13** Style Elements and Attributes in the GANTT Style


Element/Attributes	Description	GANTT Option	GOPTION
<b>GraphColors</b>	Colors of various graph features	PATTERN=	CPATTERN=, COLORS=
gdata1	Duration of a noncritical activity	PATTERN=	CPATTERN=, COLORS=
gdata2	Slack time for a noncritical activity	PATTERN=	CPATTERN=, COLORS=
gdata3	Duration of a critical activity	PATTERN=	CPATTERN=, COLORS=
gdata4	Slack time for a supercritical activity	PATTERN=	CPATTERN=, COLORS=
gdata5	Duration of a supercritical activity	PATTERN=	CPATTERN=, COLORS=
gdata6	Actual duration of an activity	PATTERN=	CPATTERN=, COLORS=
gdata7	Break due to a holiday	PATTERN=	CPATTERN=, COLORS=
gdata8	Resource-constrained duration of an activity	PATTERN=	CPATTERN=, COLORS=
gdata9	Baseline duration of an activity	PATTERN=	CPATTERN=, COLORS=
gaxis	Axis	CAXIS=	COLORS=
ggrid	Horizontal connecting lines, zone lines	CHCON=, CZONE=	COLORS=
gdata	Default		COLORS=
gcdata	Precedence connections	CPREC=	COLORS=
referencelines	Reference and timenow lines	CREF=, CTNOW=	COLORS=
gtextt	Title text		CTITLE=
gtext	Text		CTEXT=
glabel	Labels		COLORS=

**Table 8.13** (continued)

<b>Element/Attributes</b>	<b>Description</b>	<b>GANTT Option</b>	<b>OPTION</b>
<b>GraphFonts</b>	Fonts for various graph features		
GraphDataFont	Default		FONT=
GraphLabelFont	Labels		FONT=
GraphTitleFont	Title text		FTITLE=
<b>GraphAxisLines</b>	Attributes related to graph axes		
Color	GraphColors('gaxis')	CAXIS=	COLORS=
<b>GraphGridLines</b>	Attributes related to horizontal connecting lines and zone lines		
Color	GraphColors('ggrid')	CHCON=, CZONE=	COLORS=
<b>GraphConnectLine</b>	Attributes related to precedence connections		
Color	GraphColors('gadata')	CPREC=	COLORS=
<b>GraphReference</b>	Attributes related to reference and timenow lines		
Color	GraphColors('greferencelines')	CREF=, CTNOW=	COLORS=
<b>GraphLabelText</b>	Attributes related to general text		
Color	GraphColors('gtext')	CTEXT=	COLORS=
Font	GraphFonts('GraphDataFont')	FONT=	FONT=
<b>GraphTitleText</b>	Attributes related to title text		
Color	GraphColors('gtextt')		CTITLE=
Font	GraphFonts('GraphTitleFont')		FTITLE=
<b>GraphTitle1Text</b>	Attributes related to the first title text		
Color	GraphColors('gtextt')		CTITLE=
Font	GraphFonts('GraphTitleFont')		FTITLE=
<b>GraphLabelText</b>	Attributes related to label text		
Color	GraphColors('glabel')	_CLABEL variable in the LABDATA= data set	COLORS=
Font	GraphFonts('GraphLabelFont')	_FLABEL variable in the LABDATA= data set	FONT=
<b>GraphDataDefault</b>	Default values for the attributes specified in <a href="#">Table 8.14</a>		
Color	GraphColors('gdata')		COLORS=

Attributes that you do not override retain the values specified in the style template.

[Figure 8.15](#) demonstrates features of the GANTT graphical style. The GANTT chart in the figure is the first output from [Example 8.11](#).

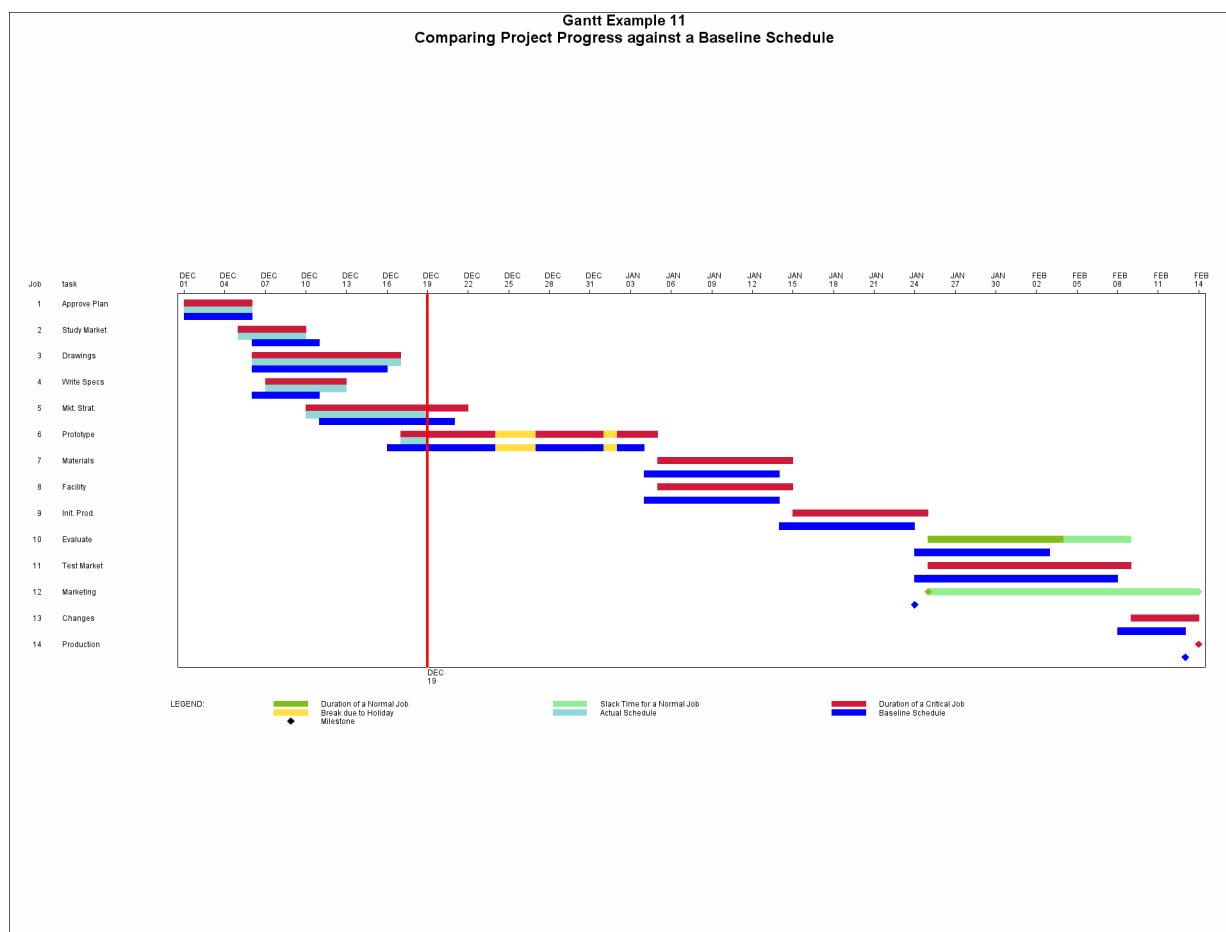**Figure 8.15** GANTT Style Template: Example

## Default Values

If the SAS system option GSTYLE is in effect (this is the default), then the default values of certain PROC GANTT options can depend on the current ODS style template. Table 8.14 lists these PROC GANTT options and lists the order in which PROC GANTT searches for each option's default value. The order assumes that the GSTYLE system option is in effect; if that is not the case, then the steps that refer to ODS style templates are ignored. Names with arguments indicate style elements and attributes of the current ODS style template. For example, “GraphAxisLines(‘Color’)” refers to the Color attribute of the GraphAxisLines element.

**Table 8.14** PROC GANTT Options: Search Orders for Default Values

Option	Search Order for Default Color
CAXIS=	<ol style="list-style-type: none"> <li>1. The Color attribute of the GraphAxisLines element of the current ODS style template</li> <li>2. The Color attribute of the GraphDataDefault element of the current ODS style template</li> <li>3. The first color in the COLORS= list in the GOPTIONS statement</li> </ol>
CFRAME=	<ol style="list-style-type: none"> <li>1. No color filling the axis area (if the GSTYLE system option is not in effect)</li> </ol>

**Table 8.14** (continued)

<b>Option</b>	<b>Search Order for Default Color</b>
	<ol style="list-style-type: none"> <li>2. The Color attribute of the GraphWalls element of the current ODS style template</li> <li>3. No color filling the axis area</li> </ol>
<b>CHCON=</b>	<ol style="list-style-type: none"> <li>1. The Color attribute of the GraphGridLines element of the current ODS style template</li> <li>2. The Color attribute of the GraphDataDefault element of the current ODS style template</li> <li>3. The first color in the COLORS= list in the GOPTIONS statement</li> </ol>
<b>CPREC=</b>	<ol style="list-style-type: none"> <li>1. The Color attribute of the GraphConnectLine element of the current ODS style template</li> <li>2. The Color attribute of the GraphDataDefault element of the current ODS style template</li> <li>3. The first color in the COLORS= list in the GOPTIONS statement</li> </ol>
<b>CREF=</b>	<ol style="list-style-type: none"> <li>1. The Color attribute of the GraphReference element of the current ODS style template</li> <li>2. The Color attribute of the GraphDataDefault element of the current ODS style template</li> <li>3. The first color in the COLORS= list in the GOPTIONS statement</li> </ol>
<b>CTEXT=</b>	<ol style="list-style-type: none"> <li>1. The value specified for the CTEXT= option in the GOPTIONS statement</li> <li>2. The Color attribute of the GraphDataText element of the current ODS style template</li> <li>3. The Color attribute of the GraphDataDefault element of the current ODS style template</li> <li>4. The first color in the COLORS= list in the GOPTIONS statement</li> </ol>
<b>CTNOW=</b>	<ol style="list-style-type: none"> <li>1. The Color attribute of the GraphReference element of the current ODS style template</li> <li>2. The Color attribute of the GraphDataDefault element of the current ODS style template</li> <li>3. The first color in the COLORS= list in the GOPTIONS statement</li> </ol>
<b>CZONE=</b>	<ol style="list-style-type: none"> <li>1. The Color attribute of the GraphGridLines element of the current ODS style template</li> <li>2. The Color attribute of the GraphDataDefault element of the current ODS style template</li> <li>3. The first color in the COLORS= list in the GOPTIONS statement</li> </ol>
<b>FONT=</b>	<ol style="list-style-type: none"> <li>1. The value specified for the FTEXT= option in the GOPTIONS statement</li> <li>2. The Font attribute of the GraphDataText element of the current ODS style template</li> <li>3. The default hardware font for the graphics output device</li> </ol>

---

## Examples: GANTT Procedure

This section contains examples that illustrate several of the options and statements available with PROC GANTT in the different display modes. [Example 8.1](#) and [Example 8.2](#) illustrate the GANTT procedure in line-printer mode, and [Example 8.3](#) through [Example 8.27](#) illustrate the GANTT procedure in graphics mode.

---

### Line-Printer Examples

[Example 8.1](#) shows how to obtain a basic line-printer Gantt chart using the default options. [Example 8.2](#) demonstrates how to use various options to customize the Gantt chart for the same project.

---

#### Example 8.1: Printing a Gantt Chart

This example shows how to use the GANTT procedure to obtain a basic line-printer Gantt chart using the default options. The following data describe the precedence relationships among the tasks involved in the construction of a typical floor in a multistory building. The first step saves the precedence relationships in a SAS data set. The variable ACTIVITY names each task, the variable DUR specifies the time it takes to complete the task in days, and the variables SUCCESS1 to SUCCESS4 specify tasks that are immediate successors to the task identified by the ACTIVITY variable.

PROC CPM determines the shortest schedule for the project that finishes before September 1, 2004. The solution schedule, saved in a SAS data set, is next sorted by the early start time before invoking the GANTT procedure to plot the schedule. Since the DATA= option is not specified, PROC GANTT uses the sorted data set to produce the schedule since it is the most recently created data set. The Gantt chart in [Output 8.1.1](#) is plotted on two pages because there are too many observations (29) to fit on one page. Note that the observations are split into two groups containing 15 and 14 observations, respectively, so that the chart size on each page is approximately equal. The time axis is labeled from June 21, 2004, to September 1, 2004, since these are the minimum and maximum dates in the Schedule data set. A legend is displayed at the bottom of the chart on each page.

```

title 'Gantt Example 1';
title2 'Printing a Gantt Chart';

data;
  format activity $20. success1 $20. success2 $20. success3 $20.
        success4 $20.;
  input activity dur success1-success4;
  datalines;
form          4 pour . . .
pour          2 core . . .
core          14 strip spray_fireproof insulate_walls .
strip         2 plumbing curtain_wall risers doors
strip         2 electrical_walls balance_elevator . .
curtain_wall 5 glaze_sash . .
glaze_sash    5 spray_fireproof insulate_walls . .
spray_fireproof 5 ceil_fixtures . .

```

```

ceil_ducts_fixture 5 test . . .
plumbing          10 test . . .
test              3 insulate_mechanical . . .
insulate_mechanical 3 lath . . .
insulate_walls    5 lath . . .
risers            10 ceil_ducts_fixture . . .
doors             1 port_masonry . . .
port_masonry      2 lath finish_masonry . .
electrical_walls 16 lath . . .
balance_elevator  3 finish_masonry . . .
finish_masonry    3 plaster marble_work . .
lath              3 plaster marble_work . .
plaster           5 floor_finish tiling acoustic_tiles .
marble_work       3 acoustic_tiles . .
acoustic_tiles    5 paint finish_mechanical . .
tiling            3 paint finish_mechanical . .
floor_finish      5 paint finish_mechanical . .
paint              5 finish_paint . . .
finish_mechanical 5 finish_paint . . .
finish_paint      2 caulking_cleanup . . .
caulking_cleanup   4 finished . . .
;

* invoke cpm to find the optimal schedule;

proc cpm finishbefore date='1sep04'd;
  activity activity;
  duration dur;
  successors success1-success4;
run;


* sort the schedule by the early start date;

proc sort;
  by e_start;
run;


* invoke proc gantt to print the schedule;

proc gantt lineprinter;
run;

```

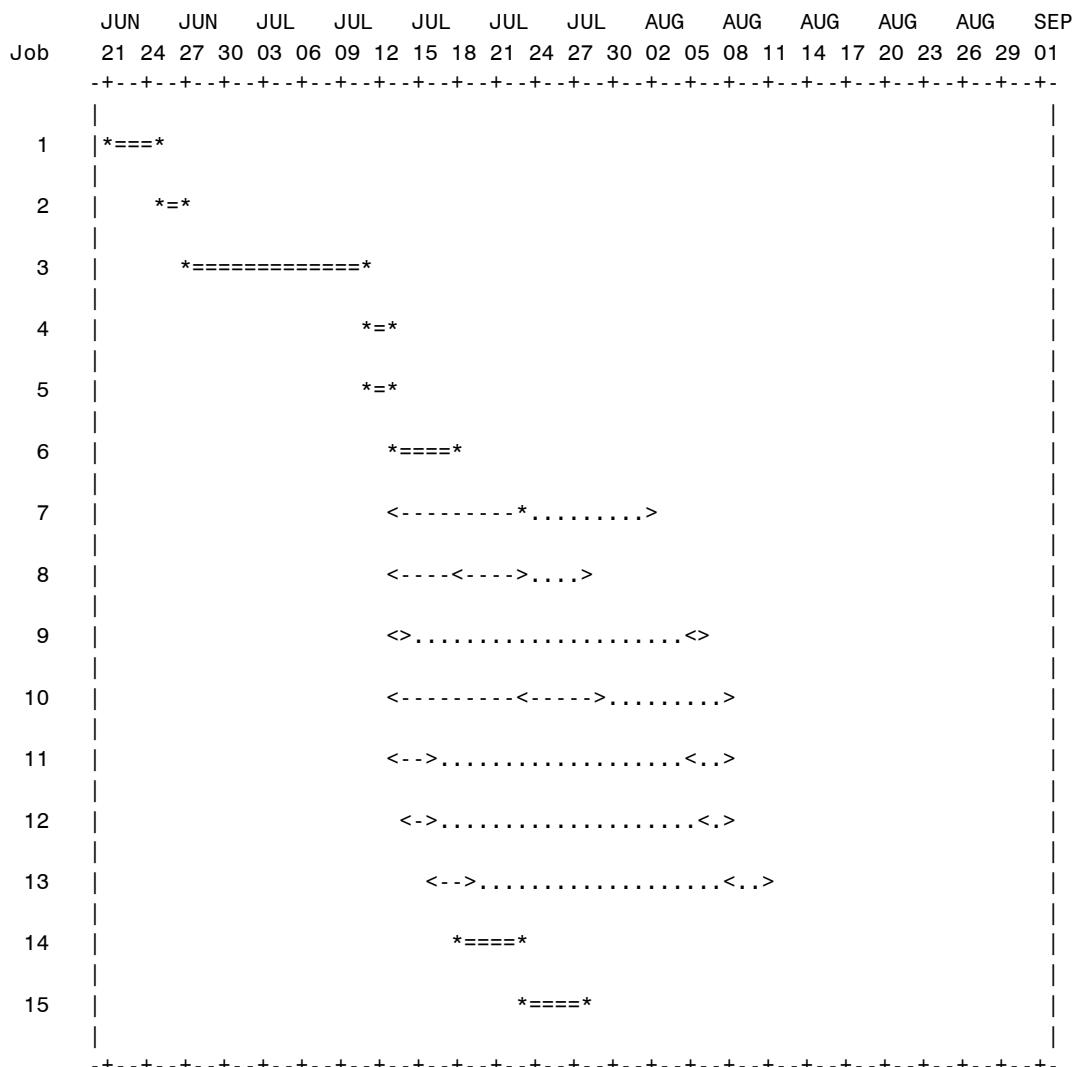**Output 8.1.1** Printing a Gantt Chart**Gantt Example 1**  
**Printing a Gantt Chart****LEGEND**

Symbol	Explanation
<---->	Duration of a Normal Job
>....>	Slack Time for a Normal Job
*====*	Duration of a Critical Job

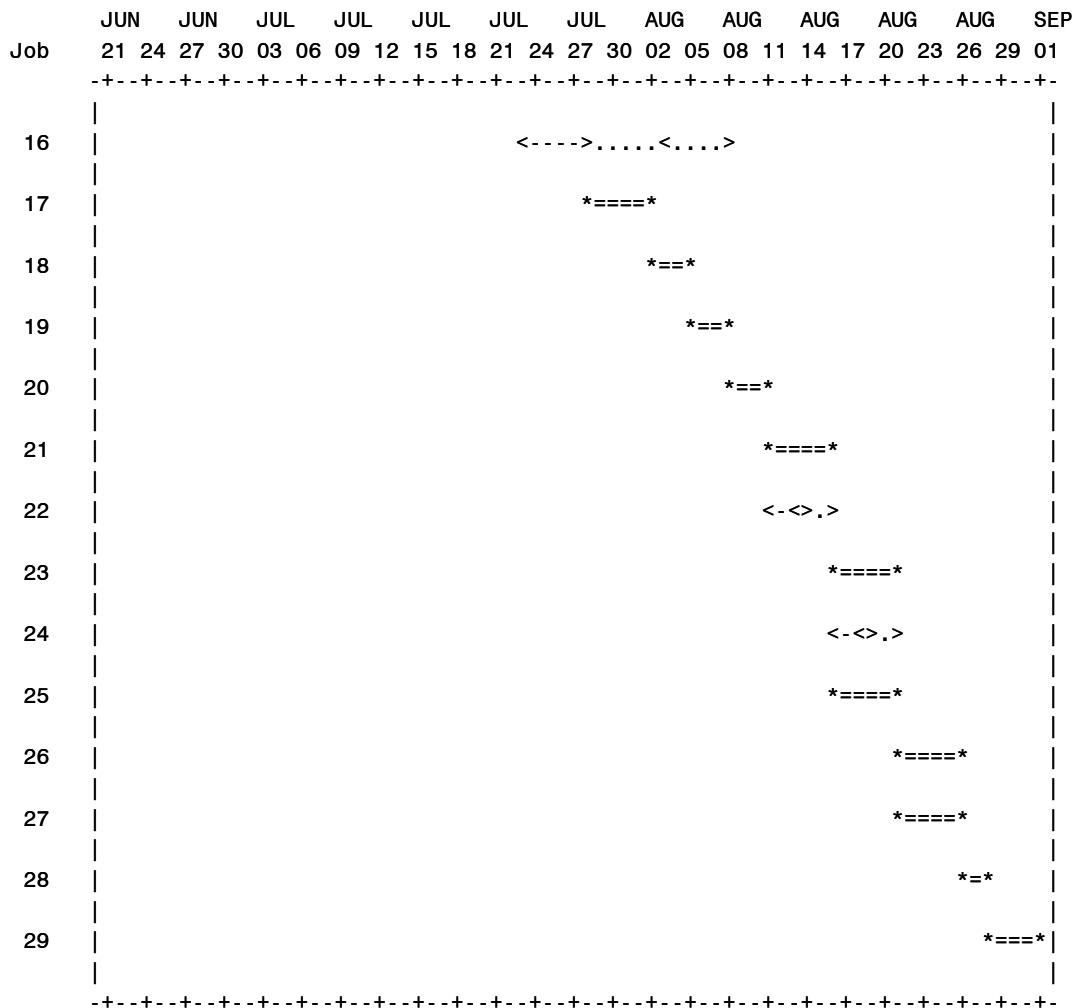**Output 8.1.1** *continued***Gantt Example 1**  
**Printing a Gantt Chart****LEGEND**

Symbol	Explanation
<---->	Duration of a Normal Job
>....>	Slack Time for a Normal Job
*=====*	Duration of a Critical Job

---

## Example 8.2: Customizing the Gantt Chart

This example shows how to control the format of the Gantt chart using CHART statement options. The Schedule data set used by PROC GANTT is the same as that used in [Example 8.1](#). Output 8.2.1 is on three pages; the first page contains a detailed description of the various symbols used by the procedure to plot the schedule. This description is produced by using the SUMMARY option. The next two pages contain the Gantt chart. The LINEPRINTER option invokes the procedure in line-printer mode. The FILL option causes the first page to be filled as completely as possible before the second page is started. Thus, the first page of the chart contains 20 activities while the second page contains only 8 activities.

The MININTERVAL=WEEK specification defines the units of time for axis labeling. The SCALE=5 specification causes five columns of the chart to be used to display one week. The SKIP=2 specification causes two lines to be skipped between observations. The NOLEGEND option suppresses displaying of the legend, while the NOJOBNUM option causes job numbers to be omitted. The CRITFLAG option is used to produce the flag to the left of the main chart indicating if an activity is critical. Specifying BETWEEN=2 sets the number of columns between consecutive ID columns equal to 2. The REF= option produces the reference lines shown on the chart on the specified dates. The ID statement is used to display the activity names to the left of the chart. The ID statement also causes the activity ‘strip’ to appear only once in the chart. Thus, there are only 28 activities in this chart instead of 29, as in [Example 8.1](#).

```
title 'Gantt Example 2';
title2 'Customizing the Gantt Chart';

proc gantt lineprinter;
  chart / summary
    fill
    mininterval=week scale=5
    skip=2
    nolegend
    nojobnum critflag between=2
    ref='10jun04'd to '30aug04'd by 15;
  id activity;
run;
```

**Output 8.2.1** Customizing the Gantt Chart**Gantt Example 2  
Customizing the Gantt Chart**

## Summary

Symbols used for different times on the schedule

Variable	Symbol	Variable	Symbol
----------	--------	----------	--------

E_START	<	L_START	<
E_FINISH	>	L_FINISH	>

## Miscellaneous Symbols

Symbol	Explanation
--------	-------------

	Reference Line
*	Overprint character when start or finish times coincide

Symbols used for joining start and/or finish times

Symbol	Explanation
--------	-------------

-	Duration of non-critical job
.	Slack time for non-critical job
=	Duration of critical job
-	Slack time(neg.) for supercritical job
*	Duration of supercritical job

**Output 8.2.1** *continued***Gantt Example 2**  
**Customizing the Gantt Chart****Summary (Contd.)**

Some examples of typical strings

String	Description
<--->...<...>	Duration followed by slack time: early finish before late start
<---<--->...>	Duration followed by slack time: early finish after late start
<---*...>	Duration followed by slack time: early finish equals late start
*====*	Duration of job on critical path
<--->---<***>	Duration preceded by negative slack time for a supercritical job: late finish before early start
<---<***>***>	Duration preceded by negative slack time for a supercritical job: late finish after early start
<---****>	Duration preceded by negative slack time for a supercritical job: late finish equals early start

**Output 8.2.1** *continued***Gantt Example 2**  
**Customizing the Gantt Chart**

activity	Flag	JUN 21	JUN 28	JUL 05	JUL 12	JUL 19	JUL 26	AUG 02	AUG 09	AUG 16	AUG 23	AUG 30	SEP 06
		-+-----+	-+-----+	-+-----+	-+-----+	-+-----+	-+-----+	-+-----+	-+-----+	-+-----+	-+-----+	-+-----+	-+-----+
form	CR	*==*											
pour	CR		**										
core	CR			*=====*									
strip	CR					**							
curtain_wall	CR						*==*						
plumbing							<-----*	.....>					
risers							<--<--->	.>					
doors							* .....	.....<>					
electrical_walls							<-----<	-->.....>					
balance_elevator							<->.....	.....<. >					
port_masonry							<->.....	.....<>					
finish_masonry							<->.....	.....< >					
glaze_sash	CR						*==*						
spray_fireproof	CR							*  =*					
insulate_walls								< ->.....<..>					

## **Output 8.2.1** *continued*

## Gantt Example 2 Customizing the Gantt Chart

---

## Graphics Examples

The following examples illustrate the use of graphics options and the use of PATTERN and SYMBOL statements to produce high resolution graphics quality Gantt charts. In [Example 8.3](#), an extra input data set containing the holiday information is used to mark the holidays used in computing the schedule by PROC CPM. [Example 8.4](#) illustrates the use of the CHART statement to specify milestones and additional variables to be plotted on the chart. [Example 8.5](#) illustrates the use of the COMPRESS option to fit an entire Gantt chart on one page. [Example 8.6](#) illustrates the use of the MININTERVAL= and SCALE= options to control the width of the chart; this example also shows how the chart is divided and continued on the succeeding page when the time axis extends beyond one page. In [Example 8.7](#), the MINDATE= and MAXDATE= options are used to permit viewing of only a portion of the schedule in greater detail. [Example 8.8](#) uses the HOLIDUR= option in conjunction with the INTERVAL= option to mark holidays of varying lengths on the Gantt chart. [Example 8.9](#) illustrates the use of the CALENDAR and WORKDAY data sets to mark holiday information from different calendars on the chart.

In [Example 8.10](#), the actual schedule for each activity is plotted on a separate line in addition to the early and late schedules. [Example 8.11](#) illustrates tracking a project and comparing its progress against a baseline schedule. In [Example 8.12](#), the COMBINE option is used to concatenate the early, late, and actual schedules of a project in progress to produce a single concise schedule that retains all of the vital information of the former schedules. [Example 8.13](#) shows the resource-constrained schedule containing split segments of activities. The ability to bypass the project scheduler, PROC CPM, and directly specify the schedule information to PROC GANTT is demonstrated in [Example 8.14](#). [Example 8.15](#) illustrates the use of the BY statement to obtain Gantt charts for different projects in a multiproject environment. In [Example 8.16](#), the GANTT procedure is used after some data manipulation steps to produce Gantt charts for individuals, each working on different subsets of activities in the project.

In [Example 8.17](#), the HEIGHT= and HTOFF= options are used to modify the text height in relation to the height of the activity bars. The next three examples show you how to invoke the different logic options in order to draw a Logic Gantt chart that displays the precedence relationships between activities. [Example 8.18](#) illustrates use of the ACTIVITY= and SUCCESSOR= options to specify the precedence information in AON format and the LEVEL= option to specify the bar type for the connections. In [Example 8.19](#), the routing control options MAXDISLV=, MAXOFFGV=, MAXOFFLV=, and MININTGV= are used in connection with a project that is specified in AOA format using the TAIL= and HEAD= options in the CHART statement. [Example 8.20](#) demonstrates the specification of nonstandard lag types using the LAG= option in the CHART statement. This example also illustrates use of the PRECDATA= option in the PROC GANTT statement. In [Example 8.21](#), the ANNOTATE= option is used to add graphics and text on a Gantt chart. [Example 8.22](#) illustrates the Automatic Text Annotation facility to label the Gantt chart independently of the SAS/GRAF Annotate facility. In [Example 8.23](#) a PATTERN variable and a Label data set are used to generate Gantt charts for multiprojects. A very useful chart in project management and multiprocess environments is the multisegment Gantt chart. [Example 8.24](#) illustrates the use of the SEGMT\_NO variable and the PATTERN variable to produce a versatile multisegment Gantt chart. In [Example 8.25](#) the ZONE= option is used to produce a zoned Gantt chart. [Example 8.26](#) shows you how to produce a “Web-enabled” Gantt chart that you can use to drill-down your project. Finally, [Example 8.27](#) uses the CHARTWIDTH= option to produce Gantt charts that are consistent in appearance.

In all the examples presented, the early and late schedules are specified in the data set by means of the variables E\_START, E\_FINISH, L\_START, and L\_FINISH; hence, the ES=, EF=, LS=, and LF= options are not needed in the CHART statement. Unless otherwise specified, the pattern statements used in the examples are as follows:

```
pattern1 c=green v=s;      /* duration of a non-critical activity */
pattern2 c=green v=e;      /* slack time for a noncrit. activity */
pattern3 c=red v=s;        /* duration of a critical activity */
pattern4 c=magenta v=e;   /* slack time for a supercrit. activity */
pattern5 c=magenta v=s;   /* duration of a supercrit. activity */
pattern6 c=cyan v=s;       /* actual duration of an activity */
pattern7 c=black v=e;      /* break due to a holiday */
pattern8 c=blue v=s;       /* resource schedule of activity */
pattern9 c=brown v=s;     /* baseline schedule of activity */
```

### Example 8.3: Marking Holidays

This example uses the widget manufacturing project introduced in Chapter 4, “[The CPM Procedure](#).“ The data sets used in this example are the same as those used in [Example 4.8](#) to illustrate holiday processing in PROC CPM. The WIDGET data set describes the project in AON format. The variable TASK identifies the activity and the variables SUCC1, SUCC2, and SUCC3 identify the successors to TASK. The variable DAYS defines the duration of an activity. Another data set, HOLIDAYS, defines the holidays that need to be taken into account when scheduling the project. Although the HOLIDAYS data set contains three variables HOLIDAY, HOLIFIN, and HOLIDUR, the HOLIDUR variable is not used in this example. Thus, the Christmas holiday starts on December 24, 2003, and finishes on December 26, 2003. PROC CPM schedules the project to start on December 1, 2003, and saves the schedule in a data set named SAVEH. This data set is shown in [Output 8.3.1](#).

Next, the GANTT procedure is invoked with the specification of HOLIDATA= HOLIDAYS in the PROC GANTT statement and the HOLIDAY= and HOLIEND= options in the CHART statement, causing the Christmas and New Year holidays to be marked on the chart. The resulting Gantt chart is shown in [Output 8.3.2](#). Note that the procedure marks the duration of the holiday with the pattern corresponding to the seventh PATTERN statement. (See the section “[Graphics Examples](#)” on page 575 for a list of the pattern statements used in the examples.)

```

options ps=60 ls=80;

title h=2 'Gantt Example 3';
title2 'Marking Holidays';

/* Activity-on-Node representation of the project */
data widget;
  format task $12. succ1-succ3 $12. ;
  input task & days succ1 & succ2 & succ3 & ;
  datalines;
Approve Plan    5 Drawings      Study Market   Write Specs
Drawings        10 Prototype    .             .
Study Market    5 Mkt. Strat.  .             .
Write Specs     5 Prototype    .             .
Prototype       15 Materials   Facility      .
Mkt. Strat.    10 Test Market Marketing   .
Materials       10 Init. Prod.  .             .
Facility        10 Init. Prod.  .             .
Init. Prod.    10 Test Market Marketing   Evaluate
Evaluate        10 Changes     .             .
Test Market     15 Changes     .             .
Changes         5 Production  .             .
Production      0 .           .             .
Marketing       0 .           .             .
;

data holidays;
  format holiday holifin date7.;
  input holiday & date7. holifin & date7. holidur;
  datalines;
24dec03 26dec03 4
01jan04 .
;
;

* schedule the project subject to holidays;
proc cpm data=widget holidata=holidays
  out=saveh date='1dec03'd ;
  activity task;
  succ    succ1 succ2 succ3;
  duration days;
  holiday holiday / holifin=(holifin);
  run;

* sort the schedule by the early start date ;
proc sort;
  by e_start;
  run;

* print the schedule;
proc print data=saveh;
  var task days e_start e_finish l_start l_finish
    t_float f_float;
  run;

```

**Output 8.3.1** Schedule Data Set SAVEH**Gantt Example 3  
Marking Holidays**


Obs	task	days	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
1	Approve Plan	5	01DEC03	05DEC03	01DEC03	05DEC03	0	0
2	Drawings	10	06DEC03	15DEC03	06DEC03	15DEC03	0	0
3	Study Market	5	06DEC03	10DEC03	09JAN04	13JAN04	30	0
4	Write Specs	5	06DEC03	10DEC03	11DEC03	15DEC03	5	5
5	Mkt. Strat.	10	11DEC03	20DEC03	14JAN04	23JAN04	30	30
6	Prototype	15	16DEC03	03JAN04	16DEC03	03JAN04	0	0
7	Materials	10	04JAN04	13JAN04	04JAN04	13JAN04	0	0
8	Facility	10	04JAN04	13JAN04	04JAN04	13JAN04	0	0
9	Init. Prod.	10	14JAN04	23JAN04	14JAN04	23JAN04	0	0
10	Evaluate	10	24JAN04	02FEB04	29JAN04	07FEB04	5	5
11	Test Market	15	24JAN04	07FEB04	24JAN04	07FEB04	0	0
12	Marketing	0	24JAN04	24JAN04	13FEB04	13FEB04	20	20
13	Changes	5	08FEB04	12FEB04	08FEB04	12FEB04	0	0
14	Production	0	13FEB04	13FEB04	13FEB04	13FEB04	0	0

```
* plot the schedule;
proc gantt holidata=holidays data=saveh;
  chart / holiday=(holiday) holiend=(holifin);
  id task;
run;
```


### **Output 8.3.2** Marking Holidays on the Gantt Chart

## Gantt Example 3

## Marking Holidays

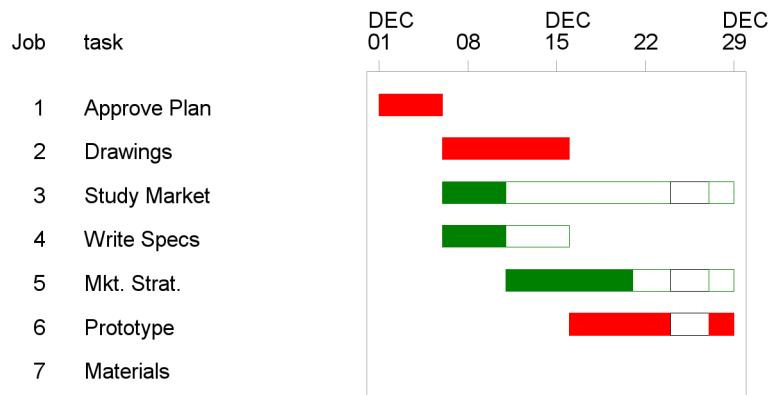


## LEGEND:



**Output 8.3.2** *continued*

## Gantt Example 3

Marking Holidays

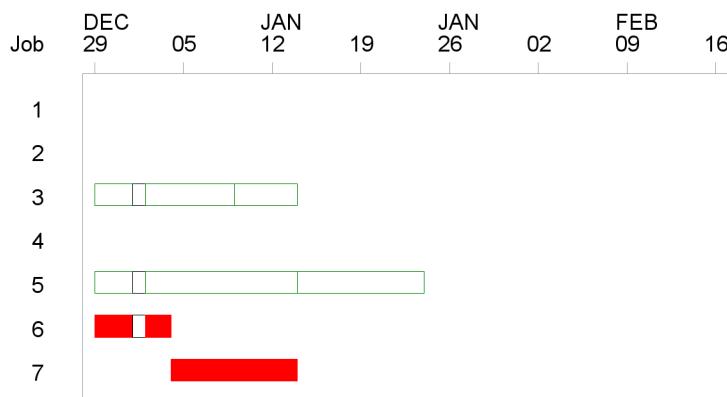


LEGEND:


	Duration of a Normal Job
	Slack Time for a Normal Job
	Duration of a Critical Job
	Break due to Holiday

**Output 8.3.2** *continued*

## Gantt Example 3

Marking Holidays

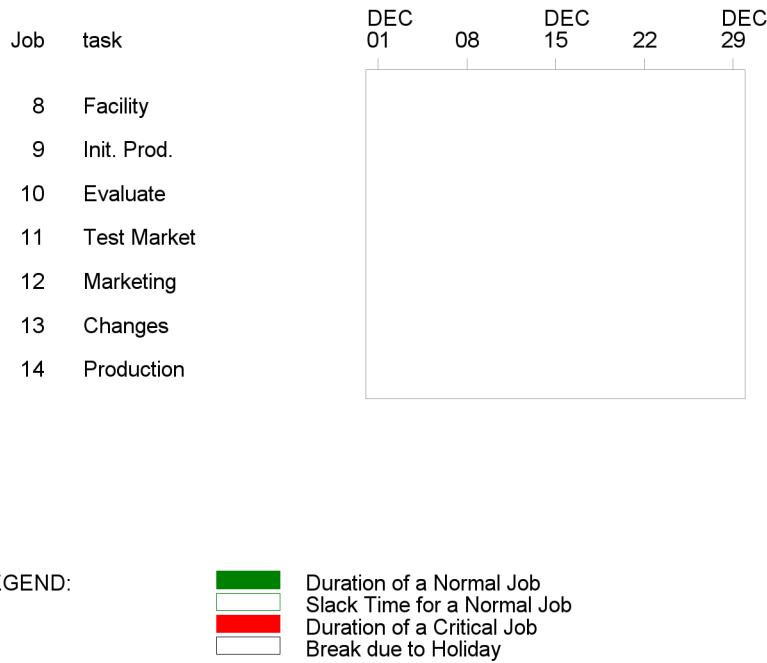

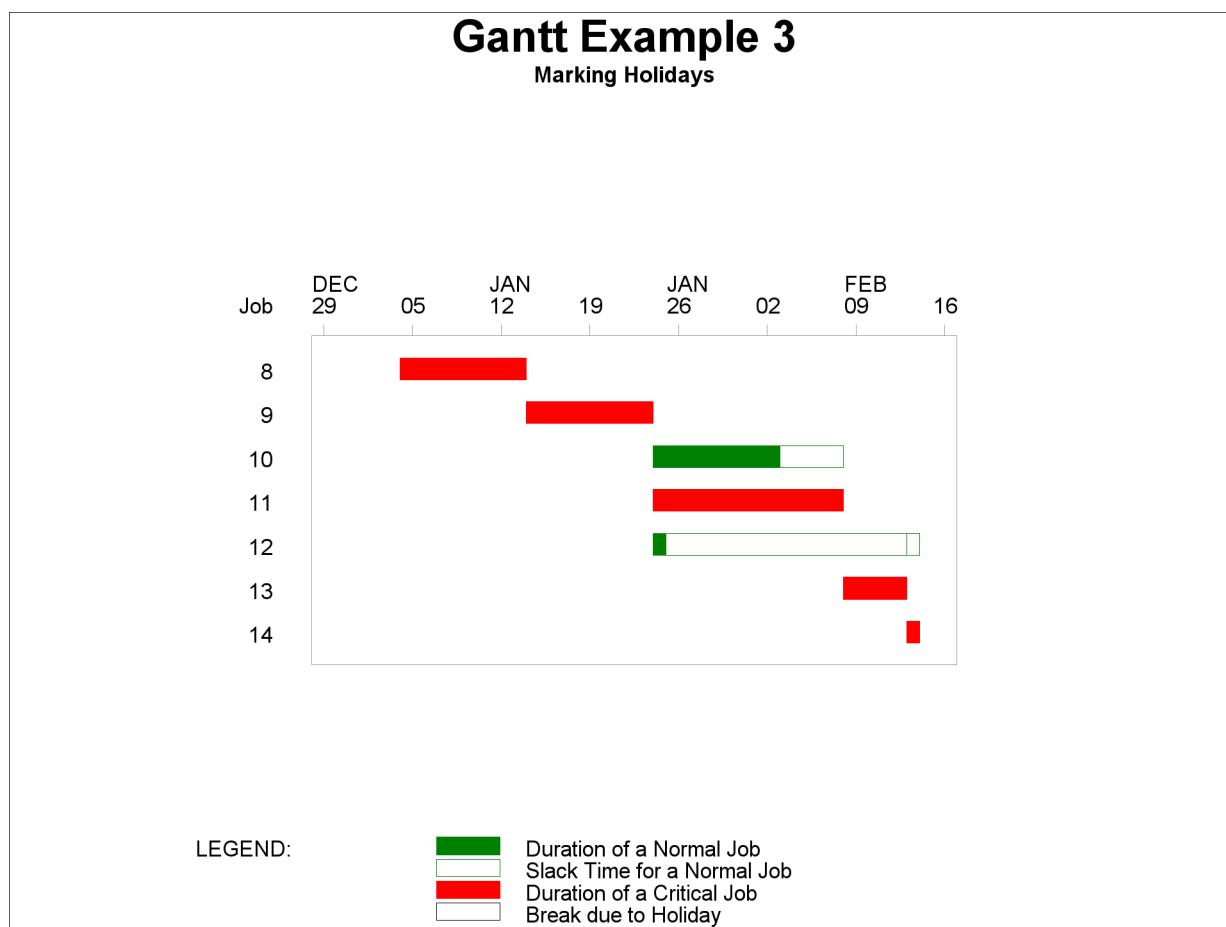Output 8.3.2 *continued***Example 8.4: Marking Milestones and Special Dates**

The widget manufacturing project described in Example 8.3 has two activities with zero duration, namely ‘Production’ and ‘Marketing.’ By default, PROC GANTT pads finish times by a padding unit, thus these two activities are represented on the Gantt chart as having a duration equal to one day (see the section “[Specifying the PADDING= Option](#)” on page 528 for further information on padding). In other words, based on start and finish times alone, PROC GANTT cannot distinguish between activities that are one day or zero days long; it needs knowledge of the activity duration variable, which is specified using the DUR= option in the CHART statement, in order to represent zero duration activities by a milestone symbol.

Now, suppose that the Engineering department would like to finish writing up the specifications before Christmas and have the prototype ready by mid-January. In addition, the Marketing department would like to develop a marketing concept by the year’s end. The data set, TARGET, contains the target dates for these activities. This data set is merged with the WIDGET data set to produce the WIDGETT data set. The WIDGETT data set is then input to the CPM procedure, which is invoked with an ID statement to ensure that the variable TARGET is passed to the Schedule data set. After sorting the Schedule data set by the early start time, PROC GANTT is used to produce a Gantt chart of the resulting schedule. The Gantt chart is shown in Output 8.4.1.

Before invoking PROC GANTT, you specify the required symbol using a SYMBOL statement. Specifying the variable TARGET in the CHART statement causes target dates to be marked on the chart with the symbol specified in the SYMBOL statement, a PLUS symbol in black. Specifying the DUR= option in the CHART statement causes zero duration schedules to be represented on the chart by the default milestone symbol, a filled diamond. To use a different milestone symbol, use the FMILE= and VMILE= options in the CHART statement. The duration and slack time of the activities are indicated by the use of the appropriate fill patterns as explained in the legend.

Colors for the milestone, axis, and text are specified using the options CMILE=, CAXIS=, and CTEXT=, respectively.

```

options ps=60 ls=100;

title h=2.5 'Gantt Example 4';
title2 h=1.5 'Marking Milestones and Special Dates';

proc cpm data=widgett date='1dec03'd;
  activity task;
  successor succ1-succ3;
  duration days;
  id target;
  run;


* sort the schedule by the early start date ;
proc sort;
  by e_start;
  run;


goptions htext=1.1 hpos=110 vpos=40;

* set up required pattern and symbol statements;
pattern1 c=green v=s;
pattern2 c=green v=e;
pattern3 c=red   v=s;
symbol   c=black v=plus;

* plot the schedule;
proc gantt;
  chart target / dur=days cmile=cyan
                ctext=blue caxis=cyan;
  id task;
  run;

```

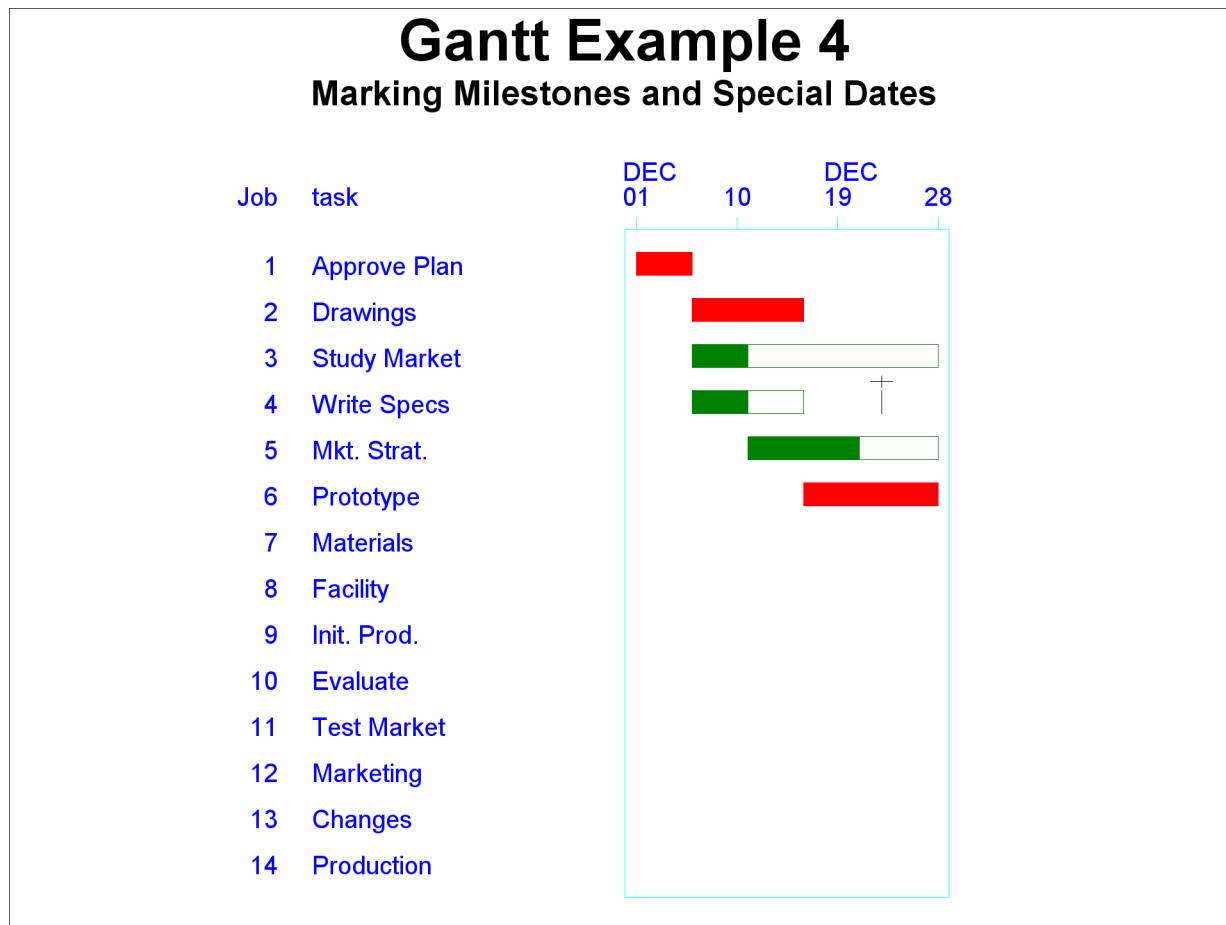**Output 8.4.1** Marking Milestones and Special Dates in Graphics Mode

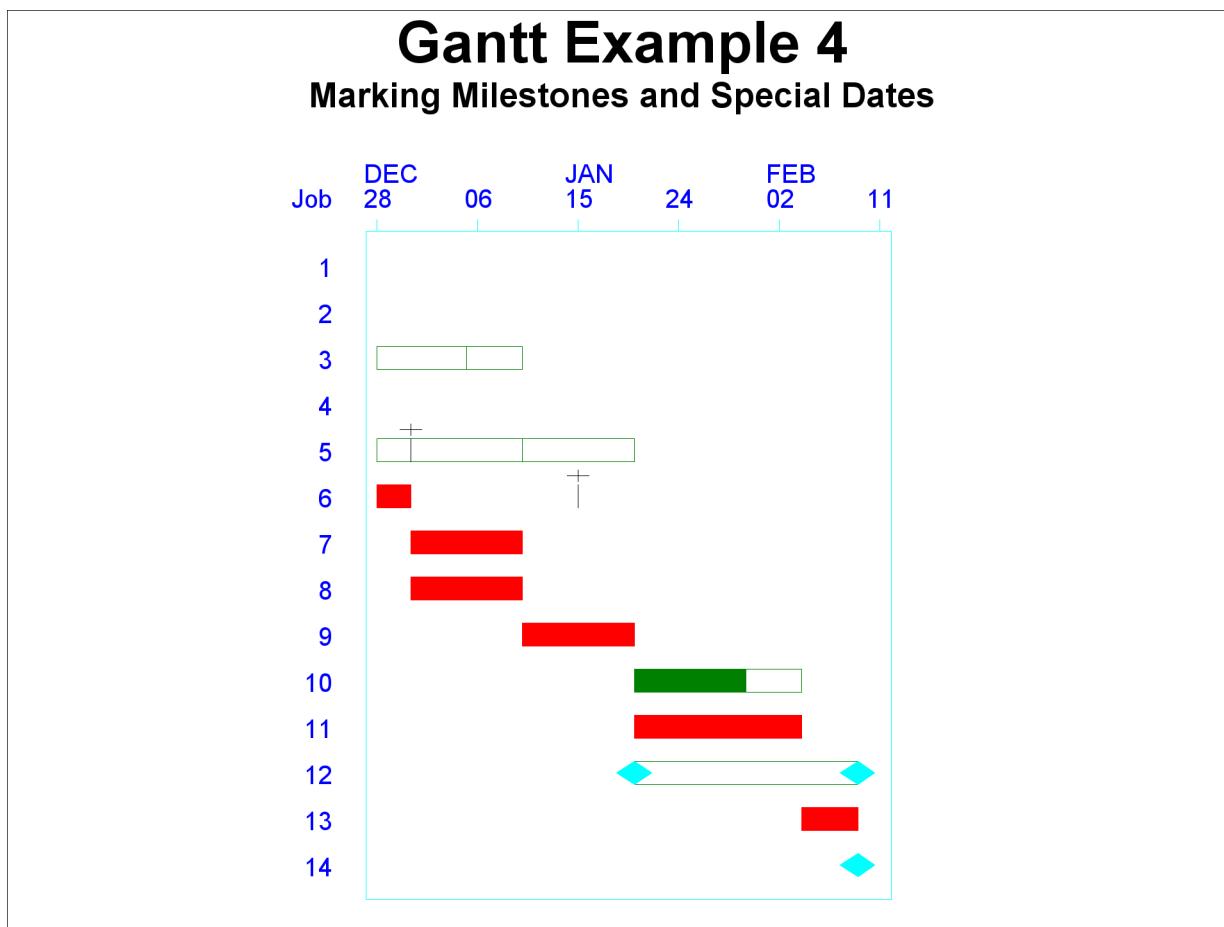Output 8.4.1 *continued***Example 8.5: Using the COMPRESS Option**


In the previous example, PROC GANTT produced two pages of output since the chart would not fit on a single page. One way to ensure that the entire chart fits on a single page in graphics mode is to adjust the values of HPOS and VPOS accordingly. An easier way that is independent of the values of HPOS and VPOS is to specify the COMPRESS option in the CHART statement. Output 8.5.1 shows the result of adding the COMPRESS option to the CHART statement in Example 8.4. The PCOMPRESS option would have a similar effect but would also maintain the aspect ratio. Some other options that can be used to control the number of pages generated are the HPAGES= and VPAGES= options.

```

title h=2 'Gantt Example 5';
title2 h=1.5 'Using the COMPRESS Option';

* plot the schedule on one page;
proc gantt;
  chart target / dur=days cmile=cyan
                ctext=blue caxis=cyan
                compress;
  id task;
run;

```

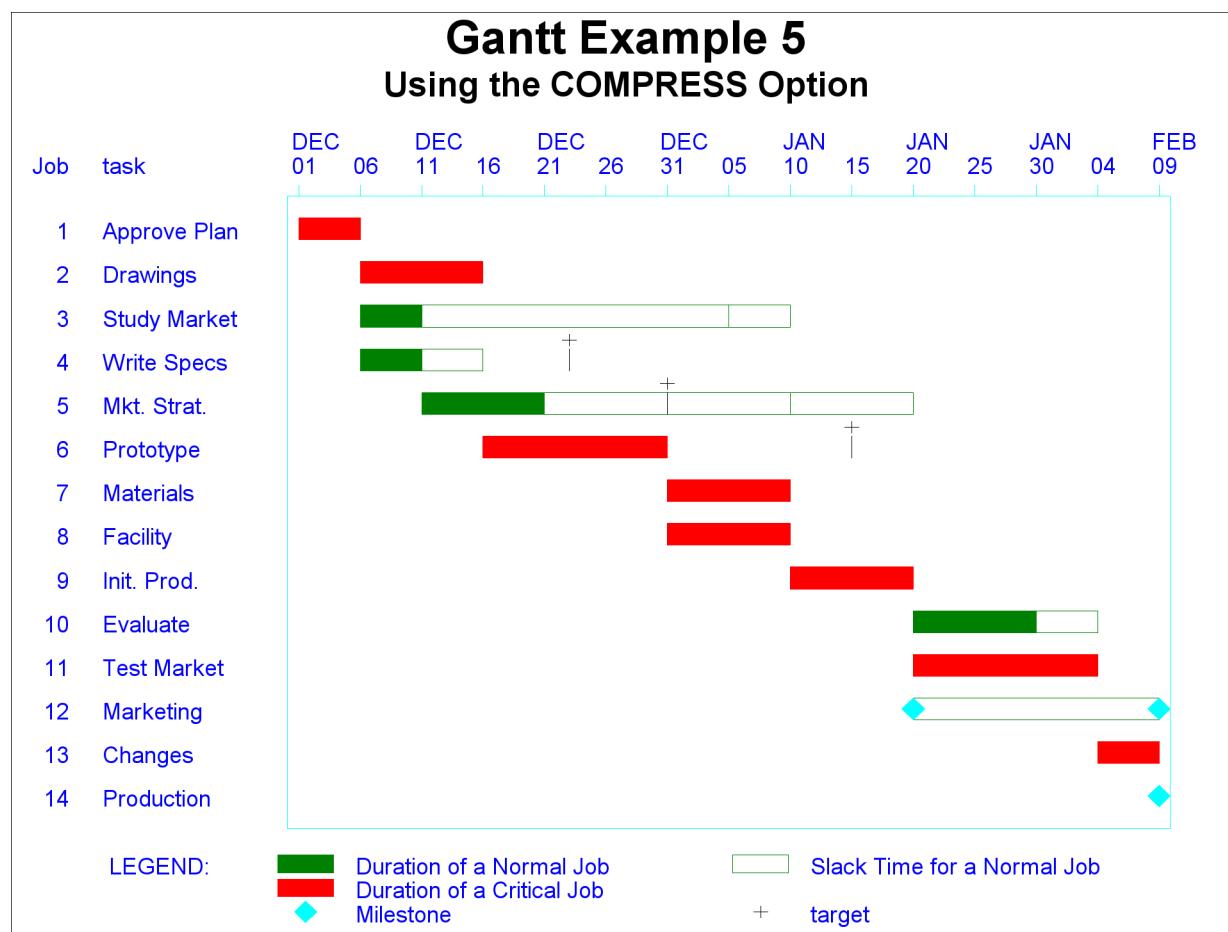**Output 8.5.1** Using the COMPRESS Option**Example 8.6: Using the MININTERVAL= and SCALE= Options**

The data sets used for this example are the same as those used to illustrate PROC CPM in Example 4.2. The data set WIDGAOA defines the project using the AOA specification. The data set DETAILS specifies the abbreviated and detailed names for each of the activities in addition to the name of the department that is responsible for that activity. Notice that a dummy activity has been added to the project in order to maintain the precedence relationships established by the WIDGET data set of the previous two examples that define the same project in AON format. The two data sets WIDGAOA and DETAILS are merged to form the WIDGETA data set that is input as the Activity data set to PROC CPM. The data set SAVE produced by PROC CPM and sorted by E\_START is shown in Output 8.6.1.

Because MININTERVAL=WEEK and SCALE=10, PROC GANTT uses  $(1000/h)\%$  of the screen width to denote one week, where  $h$  is the value of HPOS. Note that this choice also causes the chart to become too wide to fit on one page. Thus, PROC GANTT splits the chart into two pages. The first page contains the ID variable as well as the job number while the second page contains only the job number. The chart is split so that the displayed area on each page is approximately equal.

The milestone color is changed to green using the CMILE= option. The resulting Gantt chart is shown in Output 8.6.2.

```

options ps=60 ls=80;

title h=2 'Gantt Example 6';
title2 h=1.5 'Using the MININTERVAL= and SCALE= Options';

data widgaoa;
  format task $12.;
  input task & days tail head;
  datalines;
Approve Plan    5   1   2
Drawings       10  2   3
Study Market   5   2   4
Write Specs    5   2   3
Prototype      15  3   5
Mkt. Strat.    10  4   6
Materials      10  5   7
Facility        10  5   7
Init. Prod.    10  7   8
Evaluate       10  8   9
Test Market    15  6   9
Changes         5   9  10
Production     0   10  11
Marketing      0   6   12
Dummy          0   8   6
;

data details;
  format task $12. dept $13. descrpt $30.;
  input task & dept & descrpt & ;
  label dept = "Department"
        descrpt = "Activity Description";
  datalines;
Approve Plan  Planning      Finalize and Approve Plan
Drawings       Engineering   Prepare Drawings
Study Market   Marketing    Analyze Potential Markets
Write Specs    Engineering   Write Specifications
Prototype      Engineering   Build Prototype
Mkt. Strat.    Marketing    Develop Marketing Concept
Materials      Manufacturing Procure Raw Materials
Facility        Manufacturing Prepare Manufacturing Facility
Init. Prod.    Manufacturing Initial Production Run
Evaluate       Testing       Evaluate Product In-House
Test Market    Testing      Mail Product to Sample Market
Changes         Engineering  Engineering Changes
Production     Manufacturing Begin Full Scale Production
Marketing      Marketing    Begin Full Scale Marketing
Dummy          .           Production Milestone
;

data widgeta;
  merge widgaoa details;
run;

```

```

* schedule the project;
proc cpm data=widgeta date='1dec03'd out=save;
  tailnode tail;
  headnode head;
  duration days;
  id task dept descrpt;
  run;

* sort the schedule by the early start date ;
proc sort;
  by e_start;
  run;

goptions vpos=43 hpos=80;


* plot the schedule;
proc gantt graphics;
  chart / mininterval=week scale=10 dur=days
    cmile=green nolegend caxis=black
    ref='1dec03'd to '1feb04'd by month;
  id descrpt;
  run;

```

### Output 8.6.1 Schedule Data Set SAVE

#### Gantt Example 6 Using the MININTERVAL= and SCALE= Options


descrpt	dept	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT
Finalize and Approve Plan	Planning	01DEC03	05DEC03	01DEC03	05DEC03	0	0
Prepare Drawings	Engineering	06DEC03	15DEC03	06DEC03	15DEC03	0	0
Analyze Potential Markets	Marketing	06DEC03	10DEC03	05JAN04	09JAN04	30	0
Write Specifications	Engineering	06DEC03	10DEC03	11DEC03	15DEC03	5	5
Develop Marketing Concept	Marketing	11DEC03	20DEC03	10JAN04	19JAN04	30	30
Build Prototype	Engineering	16DEC03	30DEC03	16DEC03	30DEC03	0	0
Procure Raw Materials	Manufacturing	31DEC03	09JAN04	31DEC03	09JAN04	0	0
Prepare Manufacturing Facility	Manufacturing	31DEC03	09JAN04	31DEC03	09JAN04	0	0
Initial Production Run	Manufacturing	10JAN04	19JAN04	10JAN04	19JAN04	0	0
Evaluate Product In-House	Testing	20JAN04	29JAN04	25JAN04	03FEB04	5	5
Mail Product to Sample Market	Testing	20JAN04	03FEB04	20JAN04	03FEB04	0	0
Begin Full Scale Marketing	Marketing	20JAN04	20JAN04	09FEB04	09FEB04	20	20
Production Milestone		20JAN04	20JAN04	20JAN04	20JAN04	0	0
Engineering Changes	Engineering	04FEB04	08FEB04	04FEB04	08FEB04	0	0
Begin Full Scale Production	Manufacturing	09FEB04	09FEB04	09FEB04	09FEB04	0	0

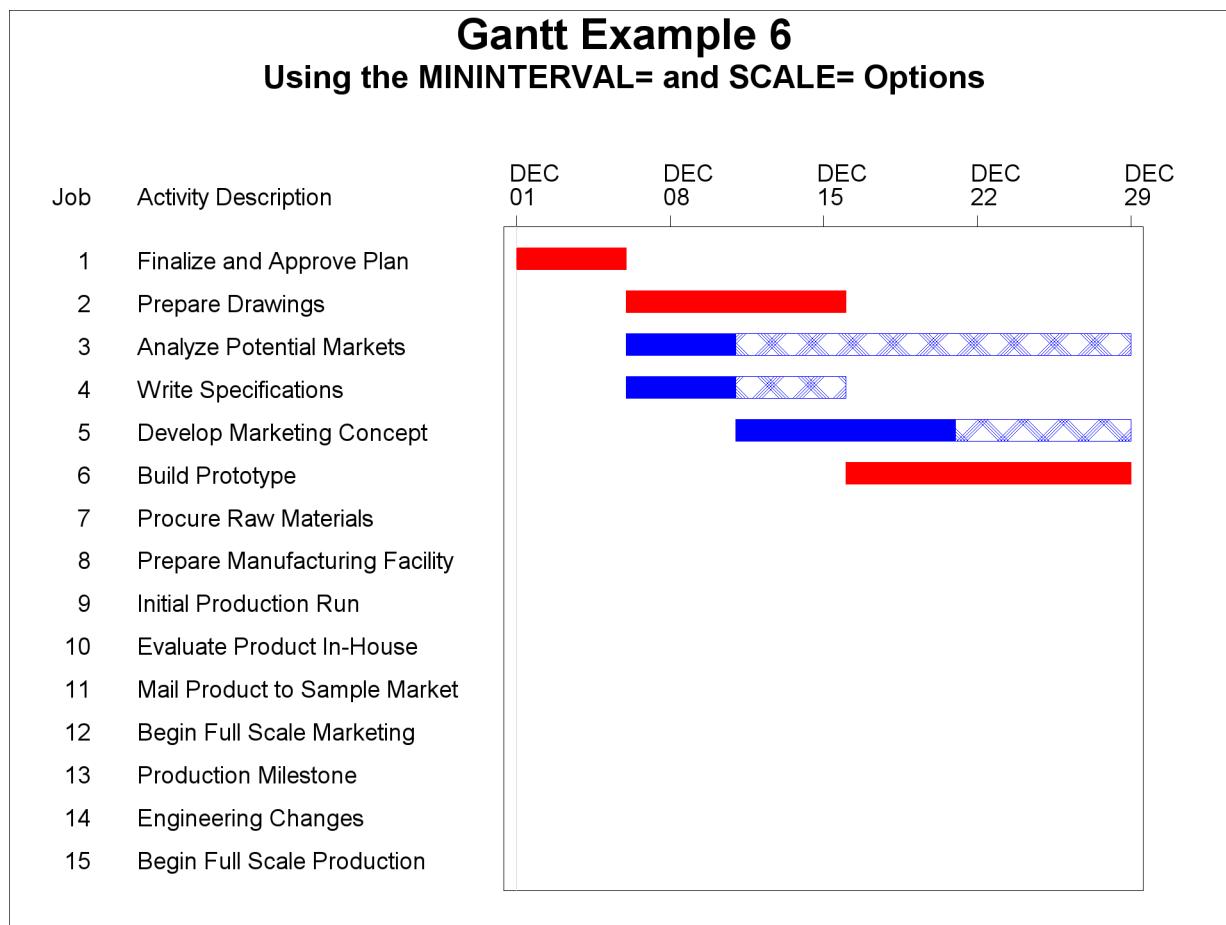**Output 8.6.2** Using the MININTERVAL= and SCALE= Options in Graphics Mode

## **Output 8.6.2** *continued*

## Gantt Example 6

### Using the MININTERVAL= and SCALE= Options

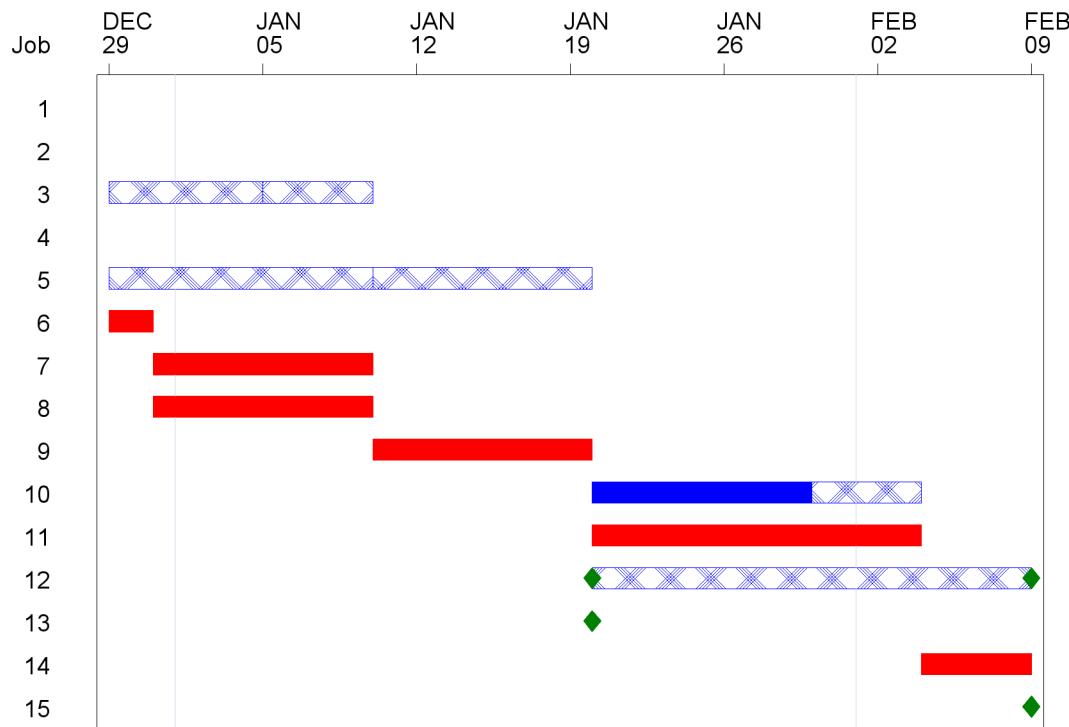

### Example 8.7: Using the MINDATE= and MAXDATE= Options

In this example, the SAVE data set from [Example 8.6](#) is used to display the schedule of the project over a limited time period. The start date and end date are specified by the MINDATE= and MAXDATE= options, respectively, in the CHART statement. As in [Example 8.5](#), the COMPRESS option is used to ensure that the region of the Gantt chart lying between January 1, 2004, and February 2, 2004, fits on a single page. The specification REF='5JAN04'D TO '2FEB04'D BY WEEK causes PROC GANTT to draw reference lines at the start of every week. Further, the reference lines are labeled using the REFLABEL option. The CREF= and LREF= options are specified in the CHART statement to indicate the color and line style, respectively, of the reference lines. The resulting Gantt chart is shown in [Output 8.7.1](#).

```


title h=2 'Gantt Example 7';
title2 h=1.5 'Using the MINDATE= and MAXDATE= Options';

goptions vpos=40 hpos=100;

* plot the schedule;
proc gantt graphics data=save;
  chart / mindate='1jan04'd maxdate='2feb04'd
    ref='5jan04'd to '2feb04'd by week
    reflabel cref=black lref=2 caxis=black
    compress dur=days nojobnum;
  id task;
run;

```

**Output 8.7.1** Using the MINDATE= and MAXDATE= Options in Graphics Mode

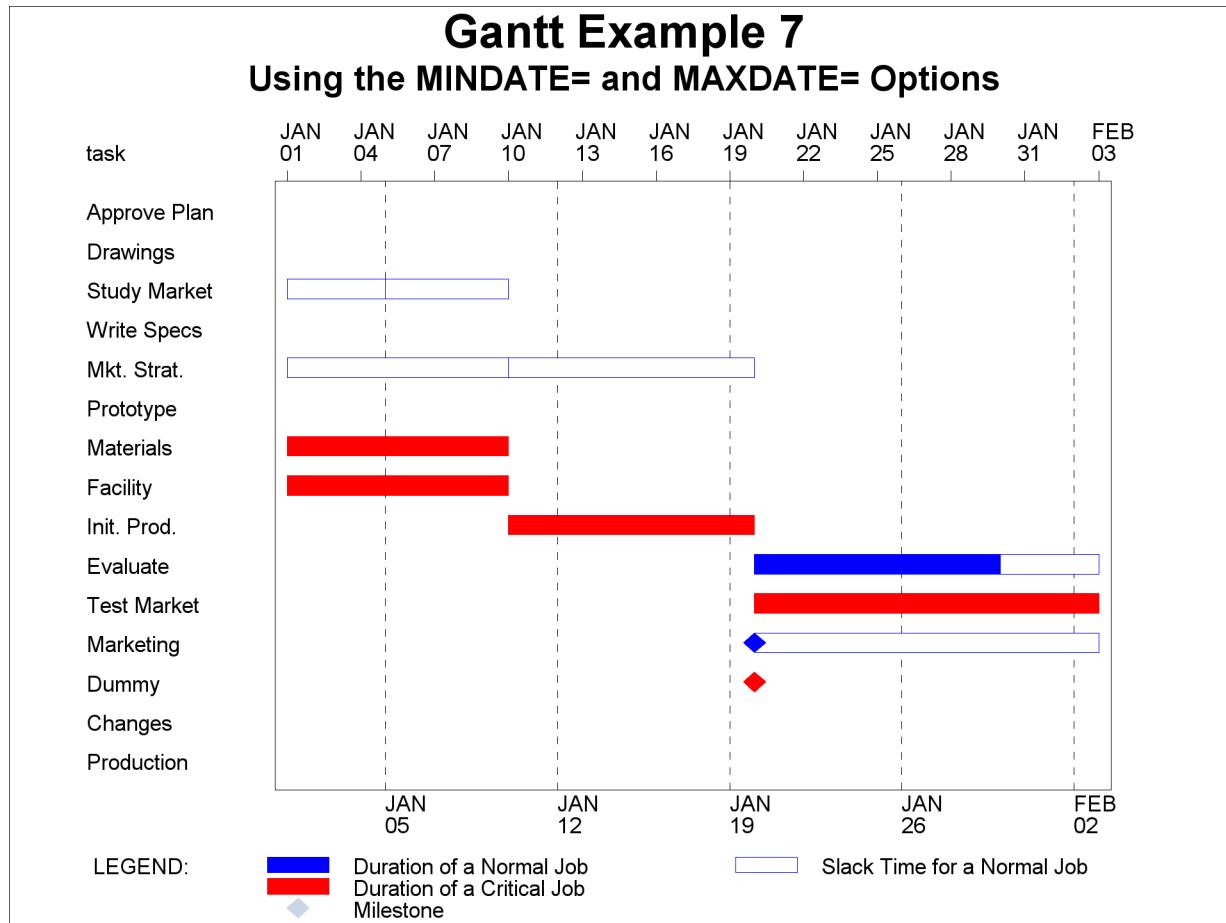

---

## Example 8.8: Variable-Length Holidays

This example shows how you can mark vacation periods that last longer than one day on the Gantt chart. This can be done by using the HOLIDUR= option in the CHART statement. Recall that holiday duration is assumed to be in *interval* units where *interval* is the value specified for the INTERVAL= option. The project data for this example are the same as the data used in the previous example. Suppose that in your scheduling plans you want to assign work on all days of the week, allowing for a Christmas vacation of four days starting from December 24, 2003, and a day off on January 1, 2004 for the New Year. The data set HOLIDAYS contains the holiday information for the project. First, the project is scheduled with INTERVAL=DAY so that the holidays are on December 24, 25, 26, and 27, 2003, and on January 1, 2004. PROC GANTT is invoked with INTERVAL=DAY to correspond to the invocation of PROC CPM. The desired font is specified by using the FONT= option in the CHART statement and the F= option in the TITLE statement. As an alternative, the desired font can be specified globally by using the FTEXT= option in a GOPTIONS statement. The resulting Gantt chart is shown in Output 8.8.1.

```


data holidays;
  format holiday holifin date7.;
  input holiday & date7. holifin & date7. holidur;
  datalines;
24dec03 27dec03 4
01jan04 .
;

* schedule the project subject to holidays;
proc cpm data=widgeta holidata=holidays out=sched1
  date='1dec03'd interval=day;
  tailnode tail;
  headnode head;
  duration days;
  id task dept descrpt;
  holiday holiday / holidur=(holidur);
  run;

* sort the schedule by the early start date ;
proc sort;
  by e_start;
  run;

* plot the schedule;
title h=2 f='Thorndale AMT' 'Gantt Example 8';
title2 h=1.5 f='Thorndale AMT' 'Variable Length Holidays: INTERVAL = DAY';
proc gantt holidata=holidays data=sched1 ;
  chart / holiday=(holiday) holidur=(holidur) font='Thorndale AMT'
    dur=days interval=day pcompress;
  id task;
  run;

```

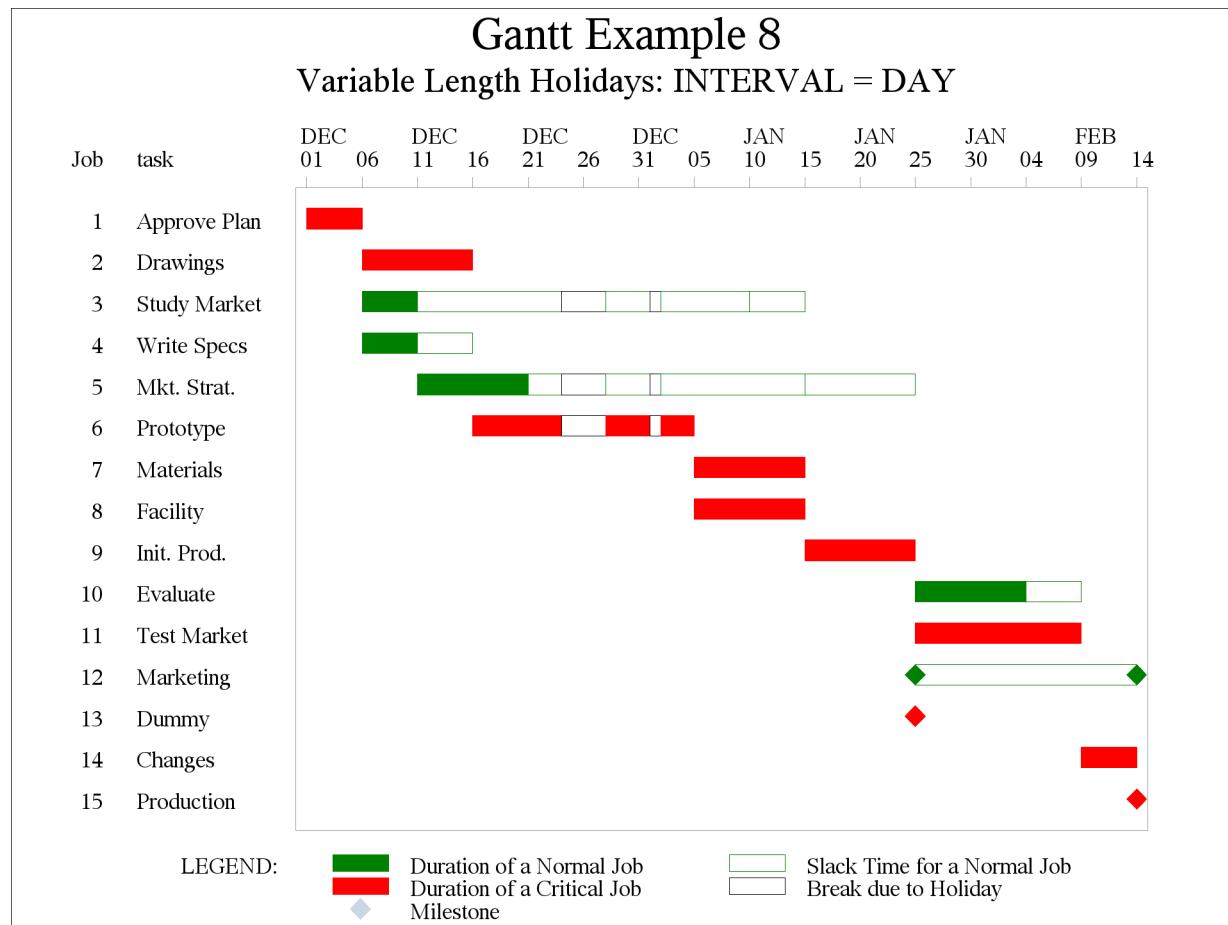**Output 8.8.1** Variable Length Holidays: INTERVAL=DAY


Next, consider the same project and Holiday data set, but invoke PROC CPM with INTERVAL=WEEKDAY. Then, the value '4' specified for the variable HOLIDUR is interpreted as 4 weekdays. The holidays are on December 24, 25, 26, and 29, 2003, and on January 1, 2004, because December 27 and 28 (Saturday and Sunday) are non-working days. The same steps are used as previously, except that INTERVAL is set to WEEKDAY instead of DAY in both PROC CPM and PROC GANTT. Suppose that the resulting data set is saved as SCHED2. The following invocation of PROC GANTT produces Output 8.8.2. Note that the use of INTERVAL=WEEKDAY causes weekends to be also marked on the chart.

```

title2 h=1.5 f='Thorndale AMT' 'Variable Length Holidays: INTERVAL=WEEKDAY';

proc gantt holidata=holidays data=sched2;
  chart / holiday=(holiday) holidur=(holidur)
    font='Thorndale AMT'
    height=1.4
    interval=weekday
    dur=days
    pcompress;
  id task;
run;

```

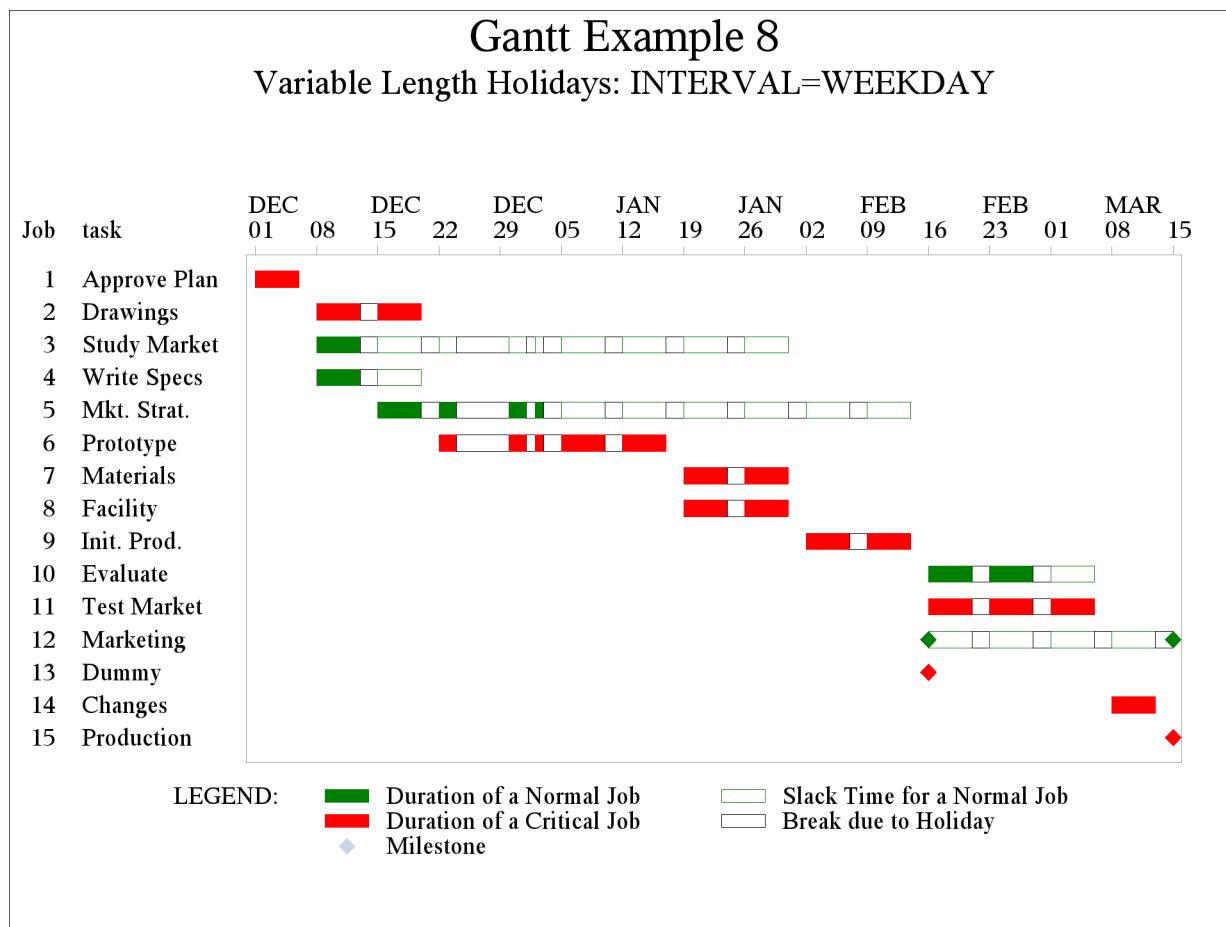**Output 8.8.2** Variable Length Holidays: INTERVAL=WEEKDAY


Finally, when the INTERVAL= option is specified as WORKDAY, the workday is assumed to be from 9:00 a.m. to 5:00 p.m., and the Christmas holiday period begins at 5:00 p.m. on December 23, 2003, and ends at 9:00 a.m. on December 30, 2004. PROC GANTT is invoked with the MARKBREAK option and MININTERVAL=DTHOUR so that all breaks during a day can be seen. Because the SCALE= option is not specified, each column denotes one hour of the schedule. Since the project duration is several days long, the entire Gantt chart would be spread across many pages. Simply specifying the COMPRESS or PCOMPRESS option will not be of much help since the text would be barely legible owing to the extent of the scaling. Hence, only a portion of the Gantt chart is shown in [Output 8.8.3](#) using the MINDATE= and MAXDATE= options. Note that the Gantt chart is labeled with the date as well as the time values on the time axis.

```

title2 h=1.5 f='Thorndale AMT' 'Variable Length Holidays: INTERVAL = WORKDAY';

proc gantt holidata=holidays data=sched3;
  chart / holiday=(holiday) holidur=(holidur)
    dur=days interval=workday
    font='Thorndale AMT'
    mininterval=dthour markbreak
    mindate='29dec03:09:00:00'dt
    maxdate='03jan04:00:00:00'dt
    pcompress height=1.5;
  id task;
  run;

```

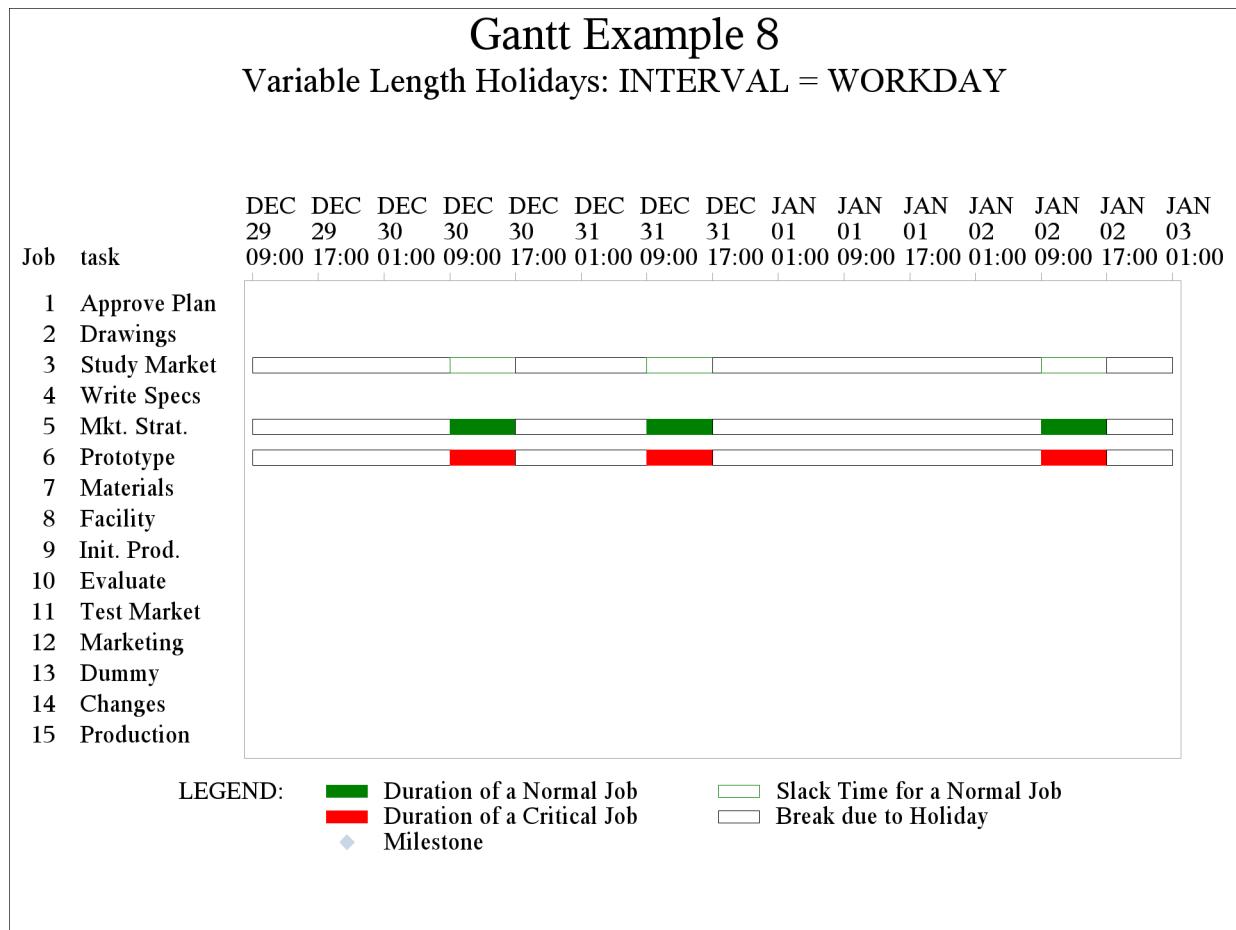**Output 8.8.3** Variable Length Holidays: INTERVAL=WORKDAY

## Example 8.9: Multiple Calendars

This example illustrates the use of multiple calendars within a project. The data for this example are the same as the data used in [Example 4.10](#) to illustrate the CPM Procedure. The input data sets to PROC CPM are displayed in [Output 8.9.1](#). The WORKDATA data set defines several shift patterns, which in turn are identified with four different calendars in the CALENDAR data set:

- The ‘DEFAULT’ calendar has five 8-hour workdays (8 a.m. - 4 p.m.) on Monday through Friday and holidays on Saturday and Sunday.
- The ‘OVT\_CAL’ calendar defines the “overtime” calendar that is followed by the Engineering department to build the prototype. The ‘OVT\_CAL’ calendar has five 10-hour workdays (8 a.m. - 6 p.m.) on Monday through Friday, a 4-hour halfday (8 a.m. - 12 noon) on Saturday and a holiday on Sunday.
- The ‘PROD\_CAL’ calendar defines the “production” calendar that is used for full-scale production of the widget. The ‘PROD\_CAL’ calendar consists of continuous work from Monday 8 a.m. through Saturday 6 p.m. except for two 2-hour breaks per day from 6 a.m. to 8 a.m. and from 6 p.m. to 8 p.m. Thus, ‘PROD\_CAL’ is made up of eleven 8-hour shifts per week; six day shifts and five night shifts.
- The ‘Eng\_cal’ calendar defines the calendar followed by the Engineering department for writing the specifications for the prototype. The ‘Eng\_cal’ calendar has the same work pattern as the default calendar with an extra holiday period of seven days starting on December 8, 2003.

The HOLIDATA data set defines the appropriate holidays for the different calendars. The project data set WIDGVAC includes a variable named CAL to identify the appropriate calendar for each activity.

#### **Output 8.9.1 Multiple Calendars: Data Sets**

##### **Multiple Calendars**

##### **Workdays Data Set**

Obs	fulday	halfday	ovtday	s1	s2	s3
1	8:00	8:00	8:00	.	8:00	.
2	16:00	12:00	18:00	6:00	18:00	6:00
3	.	.	.	8:00	20:00	8:00
4	.	.	.	18:00	.	18:00
5	.	.	.	20:00	.	.
6	.	.	.	.	.	.

##### **Calendar Data Set**

Obs	cal	_sun_	_mon_	_tue_	_wed_	_thu_	_fri_	_sat_
1	DEFAULT	holiday	fulday	fulday	fulday	fulday	holiday	
2	OVT_CAL	holiday	ovtday	ovtday	ovtday	ovtday	ovtday	halfday
3	PROD_CAL	holiday	s2	s1	s1	s1	s1	s3
4	Eng_cal							

##### **Holidays Data Set**

Obs	holiday	holifin	holidur	cal
1	08DEC03	.	.	7 Eng_cal
2	24DEC03	26DEC03	.	.
3	01JAN04	01JAN04	.	.

**Output 8.9.1** *continued***Project Data Set**

Obs	task	succ1	succ2	succ3	days	cal
1	Approve Plan Drawings		Study Market	Write Specs	5.5	DEFAULT
2	Drawings	Prototype			10.0	DEFAULT
3	Study Market	Mkt. Strat.			5.0	DEFAULT
4	Write Specs	Prototype			4.5	Eng_cal
5	Prototype	Materials	Facility		15.0	OVT_CAL
6	Mkt. Strat.	Test Market	Marketing		10.0	DEFAULT
7	Materials	Init. Prod.			10.0	DEFAULT
8	Facility	Init. Prod.			10.0	DEFAULT
9	Init. Prod.	Test Market	Marketing	Evaluate	10.0	DEFAULT
10	Evaluate	Changes			10.0	DEFAULT
11	Test Market	Changes			15.0	DEFAULT
12	Changes	Production			5.0	DEFAULT
13	Production				0.0	PROD_CAL
14	Marketing				0.0	DEFAULT

The program used to invoke PROC CPM and PROC GANTT follows. The CALENDAR= and WORKDAY= options are specified in the PROC GANTT statement to identify the CALEDATA and WORKDATA data sets, respectively. The CALID= option in the CHART statement names the variable identifying the calendar that each observation refers to in the WIDGVAC and CALEDATA data sets. Since the value of MININTERVAL= is DT DAY, setting the SCALE= value to 12 ensures that a single column on the Gantt chart represents two hours. This is done in order to be able to detect a two hour difference between schedules. Consequently, the MINDATE= and MAXDATE= options are used to control the output produced by PROC GANTT. The resulting Gantt chart is shown in Output 8.9.2. Notice the 5 column duration for ‘Prototype’ on December 29, 2003 representing a 10-hour day versus the 4 column duration for ‘Mkt. Strat.’ for the same day representing 8 hours of work. Although MAXDATE= is set to 8 a.m. on January 2, 2004, the last tick mark is the beginning of January 3, 2004. This is because the specified value of the MAXDATE= option does not correspond to a tick mark (based on the SCALE= and MININTERVAL= options); the value used is the first tick mark appearing after the value of the MAXDATE= option.

```

proc cpm date='01dec03'd interval=workday data=widgvac
      out=schedvac holidata=holidata
      workday=workdata calendar=caledata;
      holiday holiday / holifin=holifin holidur=holidur;
      activity task;
      duration days;
      successor succ1 succ2 succ3;
      calid cal;
      run;

title h=2 'Gantt Example 9';
title2 h=1.5 'Multiple Calendars';

proc gantt data=schedvac holidata=holidata
      workday=workdata calendar=caledata ;
      chart / holiday=(holiday) holiend=(holifin)
      calid=cal


```

```

markbreak scale=12
mindate='27dec03:00:00'dt
maxdate='02jan04:08:00'dt
pcompress;
id task;
run;

```

### Output 8.9.2 Multiple Calendars

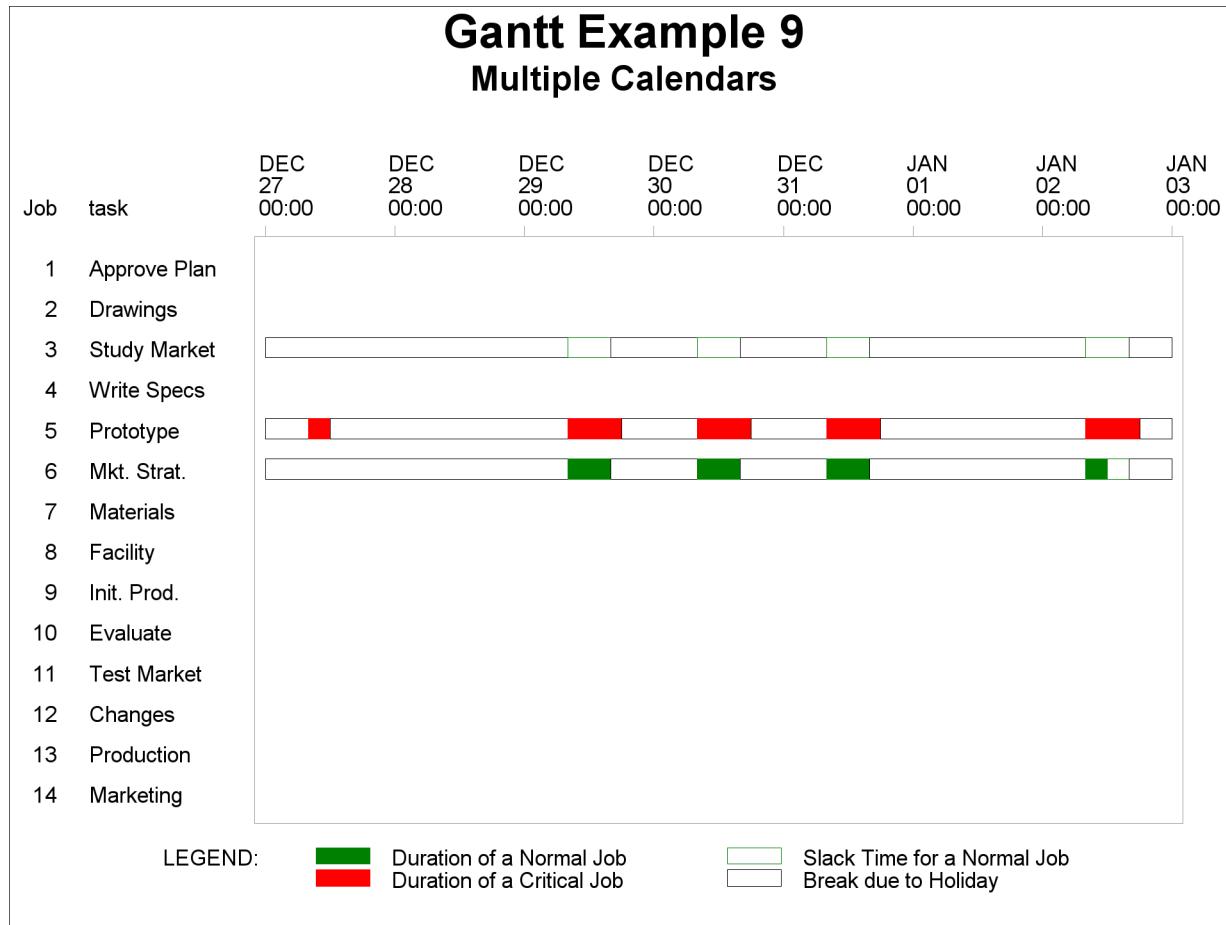


---

### Example 8.10: Plotting the Actual Schedule

Suppose that the project is complete and you want to compare the actual progress of the activities with the predicted schedule computed by PROC CPM. The following DATA step stores the actual start and finish times of each activity in a data set named COMPLETE. A data set named WIDGELA is then created that contains both the schedule obtained from PROC CPM (the data set SAVEH from [Example 8.3](#) is used because it does not contain the dummy activity) and the actual schedule. The resulting data set is sorted by early start time.

Fill patterns are specified using PATTERN statements, and the COMPRESS option is employed in order to draw the entire Gantt chart on one page. Predicted schedules as well as actual schedules are plotted on separate bars for each activity. The A\_START= and A\_FINISH= options in the CHART statement are used to specify the variables containing the actual start and finish times for each activity. The actual schedule

is plotted with the fill pattern specified in the sixth PATTERN statement. This example also illustrates the drawing of holidays in graphics mode. PROC GANTT uses the fill pattern specified in the seventh PATTERN statement to represent the holidays defined by the HOLIDATA= data set. The holidays are identified to PROC GANTT by specifying the HOLIDAY= and HOLIFIN= options in the CHART statement.

The HCONNECT option causes a connecting line to be drawn from the left boundary of the chart to the early start time for each activity. The CHCON= option specifies the color for drawing the connect lines. You can use the LHCN= option in the CHART statement to specify a line style other than the default style for the connect lines. The Gantt chart is shown in [Output 8.10.1](#).

```

data complete;
  format activity $12. sdate date7. fdate date7. ;
  input activity & sdate & date7. fdate & date7. ;
  datalines;
Approve Plan    01dec03  05dec03
Drawings        06dec03  16dec03
Study Market   05dec03  09dec03
Write Specs    07dec03  12dec03
Prototype       17dec03  03jan04
Mkt. Strat.    10dec03  19dec03
Materials       02jan04  11jan04
Facility        01jan04  13jan04
Init. Prod.    13jan04  21jan04
Evaluate        22jan04  01feb04
Test Market    23jan04  08feb04
Changes         05feb04  11feb04
Production      12feb04  12feb04
Marketing       26jan04  26jan04
;

* merge the computed schedule with the actual schedule;
data widgela;
  merge saveh complete;


* sort the data;
proc sort;
  by e_start;
  run;

* set vpos to 40 and hpos to 100;
goptions vpos=40 hpos=100;

title h=1.75 f='Albany AMT' 'Gantt Example 10';
title2 h=1.25
      f='Albany AMT' 'Plotting Actual Start and Finish Times on the Chart';

* plot the computed and actual schedules using proc gantt;
proc gantt graphics data=widgela holidata=holidays;
  chart / holiday=(holiday) holifin=(holifin)
        a_start=sdate a_finish=fdate
        dur=days font='Albany AMT' chcon=black
        hconnect compress ctext=blue height=1.5
        caxis=black cmile=blue;
  id task;
  run;

```

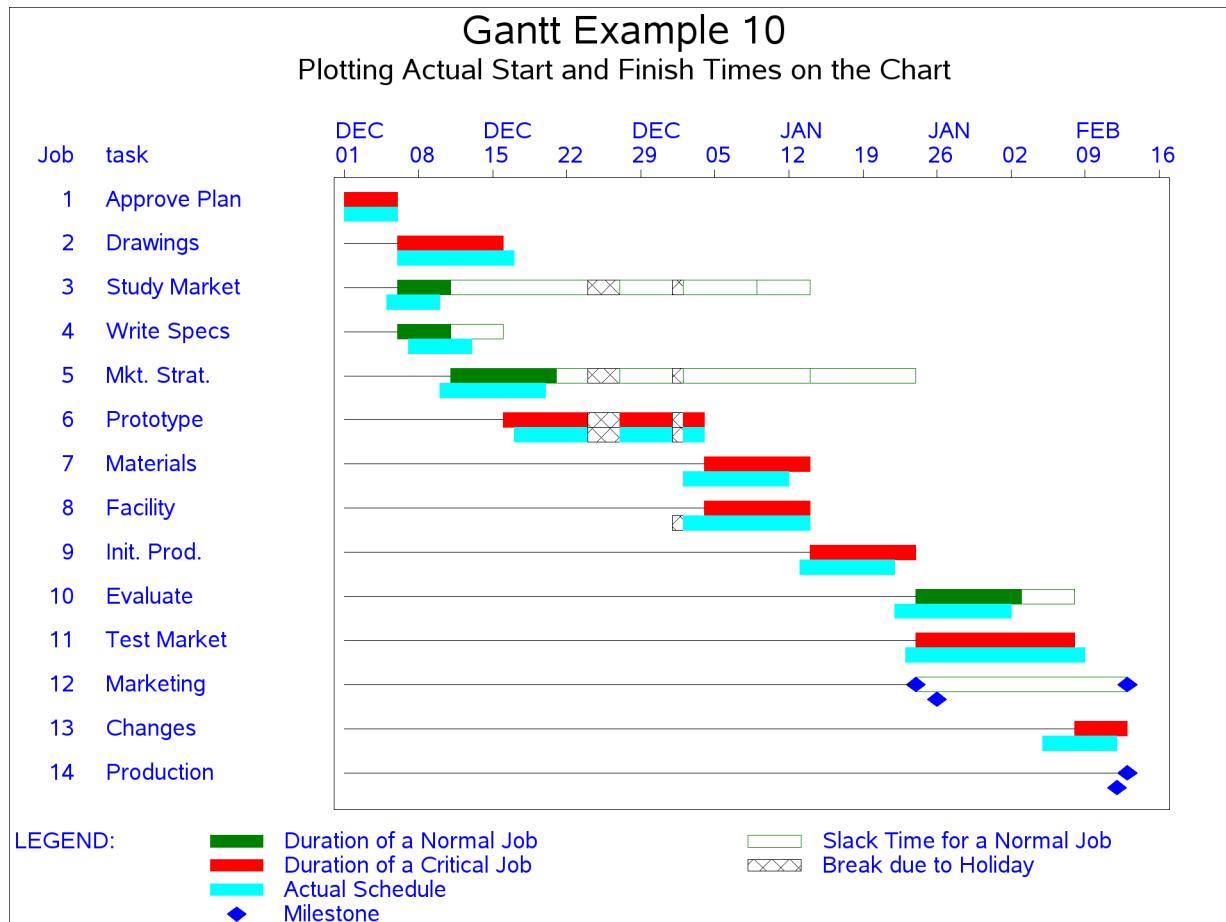**Output 8.10.1** Plotting the Actual Schedule on the Gantt Chart**Example 8.11: Comparing Progress Against a Baseline Schedule**

Suppose that the widget manufacturing project is currently in progress and you want to measure its performance by comparing it with a baseline schedule. For example, the baseline schedule may be the originally planned schedule, a target schedule that you would like to achieve, or an existing schedule that you intend to improve on. The data for this example come from [Example 4.13](#), which was used to illustrate the options available in PROC CPM. Prior to the beginning of the project, the predicted early schedule is saved by PROC CPM as the baseline schedule. Progress information for the project as of December 19, 2003, is saved in the ACTUAL data set. The variables SDATE and FDATE represent the actual start and actual finish times, respectively. The variables PCTC and RDUR represent the percent of work completed and the remaining days of work for each activity, respectively. PROC CPM is then invoked using the baseline and project progress information with TIMENOW set to December 19, 2003. The scheduling is carried out with the AUTOPUPDT option in order to automatically update progress information. The Schedule data set WIDGUPDT produced by PROC CPM is shown in [Output 8.11.1](#). Notice that the development of a marketing strategy (activity 5: ‘Mkt. Strategy’) and the building of the prototype (activity 6: ‘Prototype’) have a specified value for A\_START and a missing value for A\_FINISH, indicating that they are currently in progress at TIMENOW.

PROC GANTT is next invoked with the data set WIDGUPDT. This data set contains the actual schedule variables A\_START and A\_FINISH and the baseline schedule variables B\_START and B\_FINISH. The Gantt chart is drawn with three schedule bars per activity. The first bar represents the predicted early/late schedule based on the actual data specified, the second bar represents the actual schedule, and the third bar represents the baseline schedule. The TIMENOW= option is specified in the CHART statement to draw a timenow line on December 19, 2003. Actual schedule bars for ‘Mkt. Strategy’ and ‘Prototype’ are drawn up to TIMENOW to indicate that they are currently in progress. You can use the CTNOW=, LTNOW=, and WTNOW= options to change the color, style, and width of the timenow line, respectively. To suppress the timenow label displayed at the bottom of the axis, specify the NOTNLABEL in the CHART statement.

```

title h=1.2 'Gantt Example 11';

* estimate schedule based on actual data;
proc cpm data=widgact holidata=holidays
    out=widgupdt date='1dec03'd;
activity task;
succ    succ1 succ2 succ3;
duration days;
holiday holiday / holifin=(holifin);
baseline / compare=early;
actual / as=sdate af=fdate timenow='19dec03'd
        remdur=rdur pctcomp=pctc
        autoupd;
run;

* sort the data;
proc sort;
by e_start;
run;

* print the data;
title2 'Progress Data';

proc print;
var task e_: l_: a_start a_finish b_: ;
run;


title2 'Comparing Project Progress against a Baseline Schedule';

* plot the actual and baseline schedules using proc gantt;
proc gantt data=widgupdt holidata=holidays;
chart / holiday=(holiday) holifin=(holifin)
      timenow='19dec03'd dur=days
      scale=2 height=1.6
      pcompress;
id task;
run;

```

**Output 8.11.1** Schedule Data Set WIDGUPDT**Gantt Example 11  
Progress Data**

Obs task	E_START	E_FINISH	L_START	L_FINISH	A_START	A_FINISH	B_START	B_FINISH
1 Approve Plan	01DEC03	05DEC03	01DEC03	05DEC03	01DEC03	05DEC03	01DEC03	05DEC03
2 Study Market	05DEC03	09DEC03	05DEC03	09DEC03	05DEC03	09DEC03	06DEC03	10DEC03
3 Drawings	06DEC03	16DEC03	06DEC03	16DEC03	06DEC03	16DEC03	06DEC03	15DEC03
4 Write Specs	07DEC03	12DEC03	07DEC03	12DEC03	07DEC03	12DEC03	06DEC03	10DEC03
5 Mkt. Strat.	10DEC03	21DEC03	10DEC03	21DEC03	10DEC03	.	11DEC03	20DEC03
6 Prototype	17DEC03	04JAN04	17DEC03	04JAN04	17DEC03	.	16DEC03	03JAN04
7 Materials	05JAN04	14JAN04	05JAN04	14JAN04	.	.	04JAN04	13JAN04
8 Facility	05JAN04	14JAN04	05JAN04	14JAN04	.	.	04JAN04	13JAN04
9 Init. Prod.	15JAN04	24JAN04	15JAN04	24JAN04	.	.	14JAN04	23JAN04
10 Evaluate	25JAN04	03FEB04	30JAN04	08FEB04	.	.	24JAN04	02FEB04
11 Test Market	25JAN04	08FEB04	25JAN04	08FEB04	.	.	24JAN04	07FEB04
12 Marketing	25JAN04	25JAN04	14FEB04	14FEB04	.	.	24JAN04	24JAN04
13 Changes	09FEB04	13FEB04	09FEB04	13FEB04	.	.	08FEB04	12FEB04
14 Production	14FEB04	14FEB04	14FEB04	14FEB04	.	.	13FEB04	13FEB04

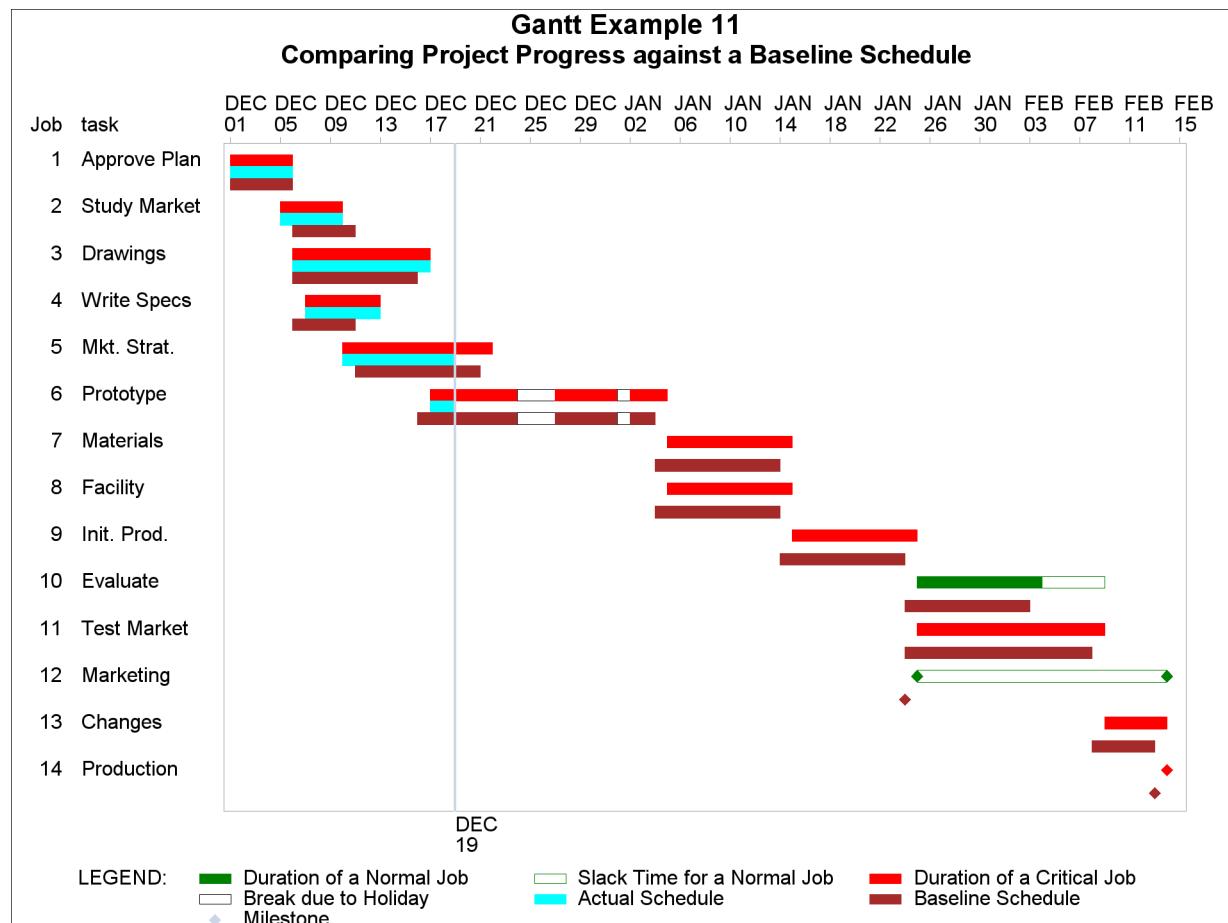**Output 8.11.2** Comparing Project Progress Against a Baseline Schedule

---

## Example 8.12: Using the COMBINE Option

When you monitor a project in progress, as in the previous example, it is evident that there are no actual dates beyond TIMENOW and that PROC CPM sets the early times to the corresponding actual times for activities that are completed or in progress (see [Output 8.11.1](#)). For example, activities 1 through 4 have their early schedule equal to the actual schedule. Activities 5 and 6 have their early start equal to the actual start; however the actual finish for these two activities is missing since they are in progress at TIMENOW. Finally, activities 7 through 14 have no actual information.

The COMBINE option in PROC GANTT exploits the fact that the early times are made consistent with the actual times to strip away a lot of the redundancy and produce a more compact Gantt chart while retaining all of the essential schedule information. Specifying the COMBINE option in the CHART statement of the previous example produces the Gantt chart in [Output 8.12.1](#). Instead of using two separate bars to draw the early/late schedule and the actual schedule, the COMBINE option causes PROC GANTT to use one bar to represent all three schedules and draws a timenow line. The actual schedule is shown to the left of TIMENOW and the early/late schedule is shown to the right of TIMENOW. Thus, for activities 1 through 4, the actual schedule is drawn on the first bar to the left of the timenow line. Activities 5 and 6 are in progress at TIMENOW, which is indicated by the actual start positioned to the left of TIMENOW and the predicted early/late schedule, based on the progress made up to TIMENOW, drawn to the right of TIMENOW. Activities 7 through 14 have not yet started, and this is reflected in their predicted early/late schedules drawn to the right of TIMENOW.

The COMBINE option draws a timenow line by default, and if the TIMENOW= option is not specified, the procedure computes the value of TIMENOW based on the schedule data as explained in the “Syntax” section. In this example, specifying the COMBINE option without the TIMENOW= option causes a timenow line to be drawn on December 18, 2003, since this is the first day following the largest actual value. The CTNOW= option is used to specify the color of the timenow line. You can change the line style and line width of the timenow line by specifying the LTNOW= and WTNOW= options, respectively, in the CHART statement.


```

title h=1.6 'Gantt Example 12';
title2 'Using the COMBINE Option';

* set vpos to 50 and hpos to 100;
goptions vpos=50 hpos=100;

* plot the combined and baseline schedules using proc gantt;
proc gantt graphics data=widgupdt holidata=holidays;
  chart / holiday=(holiday) holifin=(holifin)
        compress ctnow=red caxis=black
        height=1.5
        timenow='19dec03'd
        dur=days
        combine;
  id task;
  run;

```

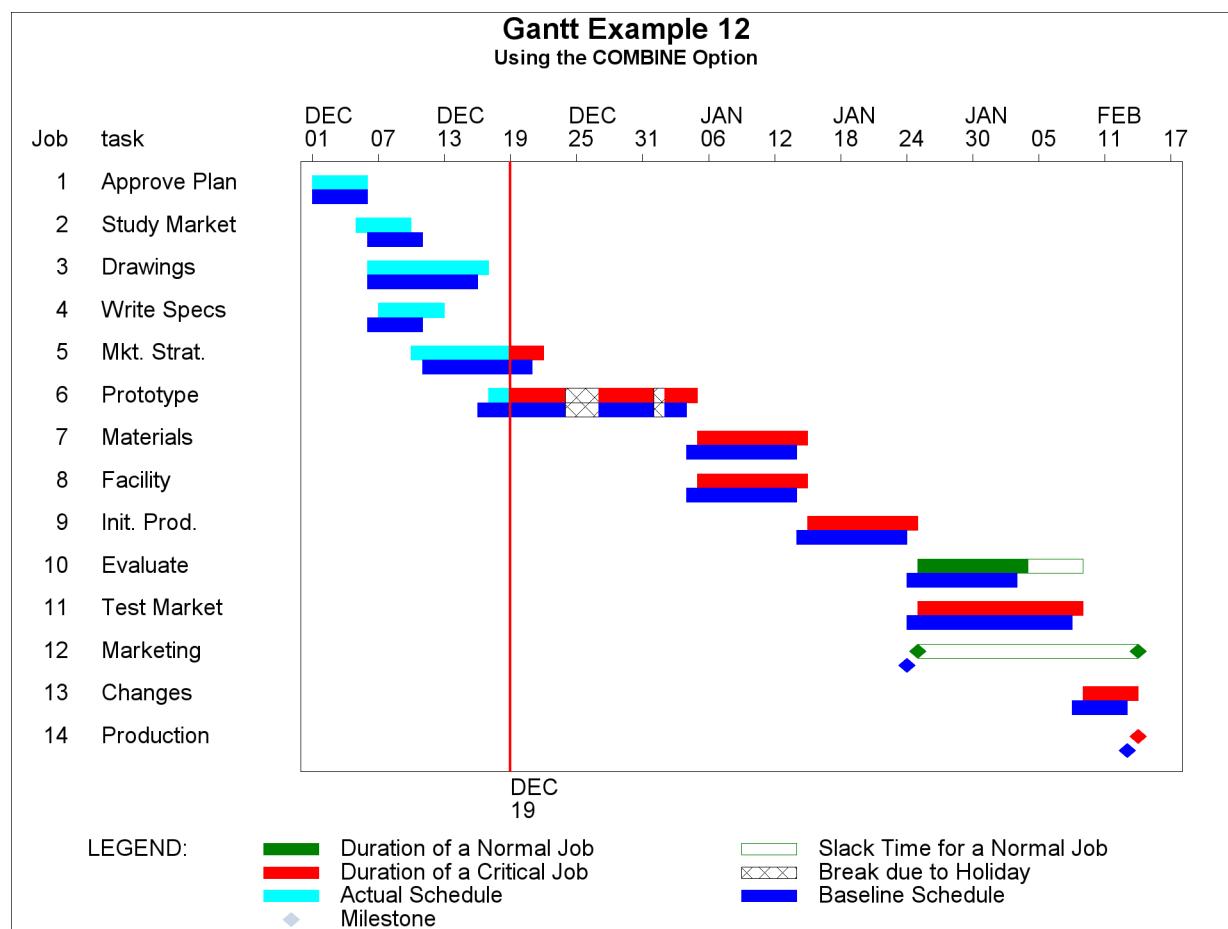**Output 8.12.1** Using the COMBINE Option in Graphics Mode**Example 8.13: Plotting the Resource-Constrained Schedule**

This example illustrates plotting the resource-constrained schedules on a Gantt chart. The schedule used is the one produced in [Example 4.19](#) using the CPM procedure. The output data set from PROC CPM is displayed in [Output 8.13.2](#). Notice that the activities ‘Drawings’ and ‘Mkt. Strat.’ have been split to produce a shorter project duration than if they had not been split.

PROC GANTT is invoked with all default options and an ID statement. The early/late schedule is drawn on the first bar, and the resource-constrained schedule is drawn on the second bar of each activity. The observations corresponding to the split segments of each activity have been combined to produce the plot of the resource-constrained schedule for that activity. Thus, even though the Schedule data set input to PROC GANTT contains 18 observations, the Gantt chart shows each of the 14 activities only once.

```

title h=1.75 'Gantt Example 13';
title2 h=1.25 'Resource Constrained Schedule';

* set vpos to 50 and hpos to 100;
goptions vpos=50 hpos=100;

```


```
* plot the resource-constrained schedule using proc gantt;
proc gantt data=spltschd holidata=holdata;
  chart / holiday=(hol) dur=days
        height=1.6 pcompress;
  id task;
run;
```

**Output 8.13.1** Schedule Data Set SPLTSCHD

**Gantt Example 13**  
**Project Schedule: Splitting Allowed**

Obs	Task	succ	SEGMT_NO	days	prodman	hrdware
1	Approve Plan	Drawings	.	5	1	.
2	Drawings	Prototype	.	10	.	1
3	Drawings	Prototype	1	2	.	1
4	Drawings	Prototype	2	8	.	1
5	Study Market	Mkt. Strat.	.	5	.	.
6	Write Specs	Prototype	.	5	.	.
7	Prototype	Materials	.	15	1	.
8	Mkt. Strat.	Test Market	.	10	1	.
9	Mkt. Strat.	Test Market	1	7	1	.
10	Mkt. Strat.	Test Market	2	3	1	.
11	Materials	Init. Prod.	.	10	.	.
12	Facility	Init. Prod.	.	10	.	.
13	Init. Prod.	Test Market	.	10	1	.
14	Evaluate	Changes	.	10	1	.
15	Test Market	Changes	.	15	.	.
16	Changes	Production	.	5	.	.
17	Production		.	0	1	.
18	Marketing		.	0	.	.

Obs	S_START	S_FINISH	E_START	E_FINISH	L_START	L_FINISH
1	01DEC03	05DEC03	01DEC03	05DEC03	01DEC03	05DEC03
2	08DEC03	23DEC03	08DEC03	19DEC03	08DEC03	19DEC03
3	08DEC03	09DEC03	08DEC03	19DEC03	08DEC03	19DEC03
4	12DEC03	23DEC03	08DEC03	19DEC03	08DEC03	19DEC03
5	08DEC03	12DEC03	08DEC03	12DEC03	21JAN04	27JAN04
6	08DEC03	12DEC03	08DEC03	12DEC03	15DEC03	19DEC03
7	24DEC03	15JAN04	22DEC03	13JAN04	22DEC03	13JAN04
8	15DEC03	20JAN04	15DEC03	29DEC03	28JAN04	10FEB04
9	15DEC03	23DEC03	15DEC03	29DEC03	28JAN04	10FEB04
10	16JAN04	20JAN04	15DEC03	29DEC03	28JAN04	10FEB04
11	16JAN04	29JAN04	14JAN04	27JAN04	14JAN04	27JAN04
12	16JAN04	29JAN04	14JAN04	27JAN04	14JAN04	27JAN04
13	30JAN04	12FEB04	28JAN04	10FEB04	28JAN04	10FEB04
14	13FEB04	26FEB04	11FEB04	24FEB04	18FEB04	02MAR04
15	13FEB04	04MAR04	11FEB04	02MAR04	11FEB04	02MAR04
16	05MAR04	11MAR04	03MAR04	09MAR04	03MAR04	09MAR04
17	12MAR04	12MAR04	10MAR04	10MAR04	10MAR04	10MAR04
18	13FEB04	13FEB04	11FEB04	11FEB04	10MAR04	10MAR04

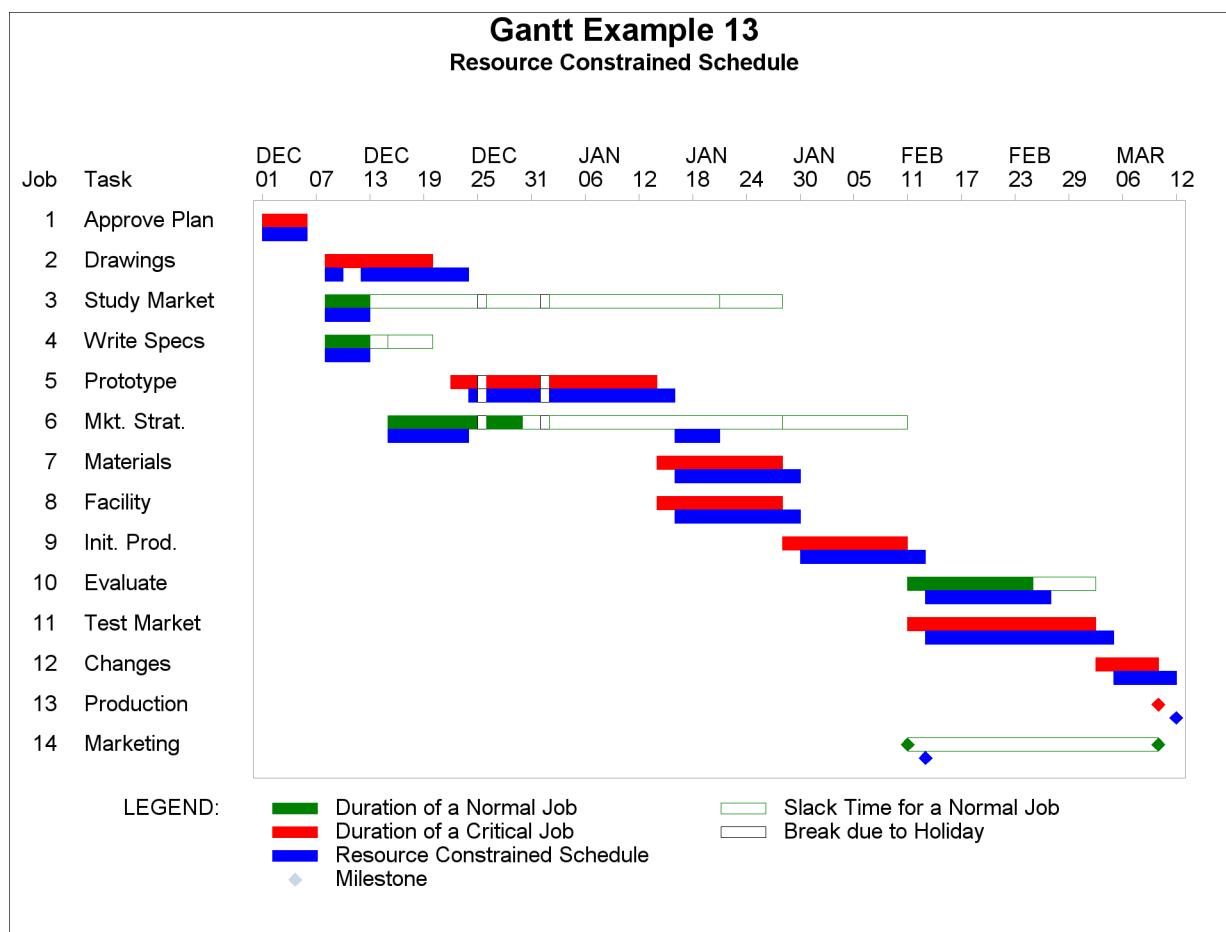**Output 8.13.2** Plotting the Resource-Constrained Schedule**Example 8.14: Specifying the Schedule Data Directly**

Although each of the examples shown so far uses PROC CPM to produce the Schedule data set for PROC GANTT, this is by no means a requirement of the GANTT procedure. While the CPM procedure is a convenient means for producing different types of schedules, you can create your own schedule and draw a Gantt chart of the schedule without any intervention from PROC CPM. This is done by storing the schedule information in a SAS data set and specifying the data set name using the DATA= option in the PROC GANTT statement. It is also not necessary for the variables in the data set to have specific names, although giving the variables certain names can eliminate the need to explicitly identify them in the CHART statement.

An example of the direct type of input can be seen in [Example 8.10](#) which illustrates plotting of the actual schedule. In [Example 8.10](#), PROC CPM was used to compute the predicted early/late schedule, which was then stored in the SAVEH data set. However, information about the actual schedule, which was provided in the COMPLETE data set, was not used by PROC CPM. Instead, this information was merged with the SAVEH data set to form WIDGELA, the Schedule data set for PROC GANTT. The variables representing the actual start and finish were identified to PROC GANTT using the A\_START= and A\_FINISH= options, respectively, in the CHART statement. The identification of the variables would not have been necessary if the start and finish variable names were A\_START and A\_FINISH, respectively.

The following example draws a Gantt chart of the early, late, and resource-constrained schedules for the widget manufacturing project. The schedule information is held in the WIDGDIR data set. The WIDGDIR data set contains the variables TASK, SEGMENT\_NO, DUR, RS, RF, E\_START, E\_FINISH, SDATE, and FDATE. The variable TASK identifies the activity. E\_START and E\_FINISH are recognized as the default names of the early start and early finish variables, respectively. The variables SDATE and FDATE define the late start and late finish times, respectively. Since these are not the default names for the late schedule variables, they need to be identified as such by specifying the LS= and LF= options (or the L\_START= and L\_FINISH= options) in the CHART statement. The variables RS and RF represent the resource-constrained start and finish times, respectively. As with the late schedule, these variables need to be identified to PROC GANTT by specifying the SS= and SF= options (or the S\_START= and S\_FINISH= options) in the CHART statement. Further, the SEGMENT\_NO variable identifies the segment number of the resource constrained schedule that an observation corresponds to since these are activities that start and stop multiple times before completion. The ZDUR variable is identified as a zero duration indicator by specifying the DUR= option in the CHART statement. Since ZDUR is zero for ‘Production’ and ‘Marketing,’ these activities are represented by milestones on the chart. Notice that although all the other activities have a value of ‘1’ for the ZDUR variable, any nonzero value will produce the same result. This is due to the fact that PROC GANTT only uses this variable as an *indicator* of whether the activity has zero duration or not, in contrast to the interpretation of the DURATION variable in PROC CPM.

```

options ps=60 ls=100;

title h=1.75 'Gantt Example 14';

/* Activity-on-Node representation of the project */
data widgdir;
  format task $12. rs rf e_start e_finish sdate fdate date7. ;
  input task & segmt_no zdur rs & date7. rf & date7.
    e_start & date7. e_finish & date7.
    sdate & date7. fdate & date7. ;
  datalines;
Approve Plan . 1 01DEC03 05DEC03 01DEC03 05DEC03 01DEC03 05DEC03
Drawings . 1 08DEC03 23DEC03 08DEC03 19DEC03 08DEC03 19DEC03
Drawings 1 1 08DEC03 09DEC03 08DEC03 19DEC03 08DEC03 19DEC03
Drawings 2 1 12DEC03 23DEC03 08DEC03 19DEC03 08DEC03 19DEC03
Study Market . 1 08DEC03 12DEC03 08DEC03 12DEC03 21JAN04 27JAN04
Write Specs . 1 08DEC03 12DEC03 08DEC03 12DEC03 15DEC03 19DEC03
Prototype . 1 24DEC03 15JAN04 22DEC03 13JAN04 22DEC03 13JAN04
Mkt. Strat. . 1 15DEC03 20JAN04 15DEC03 29DEC03 28JAN04 10FEB04
Mkt. Strat. 1 1 15DEC03 23DEC03 15DEC03 29DEC03 28JAN04 10FEB04
Mkt. Strat. 2 1 16JAN04 20JAN04 15DEC03 29DEC03 28JAN04 10FEB04
Materials . 1 16JAN04 29JAN04 14JAN04 27JAN04 14JAN04 27JAN04
Facility . 1 16JAN04 29JAN04 14JAN04 27JAN04 14JAN04 27JAN04
Init. Prod. . 1 30JAN04 12FEB04 28JAN04 10FEB04 28JAN04 10FEB04
Evaluate . 1 13FEB04 26FEB04 11FEB04 24FEB04 18FEB04 02MAR04
Test Market . 1 13FEB04 04MAR04 11FEB04 02MAR04 11FEB04 02MAR04
Changes . 1 05MAR04 11MAR04 03MAR04 09MAR04 03MAR04 09MAR04
Production . 0 12MAR04 12MAR04 10MAR04 10MAR04 10MAR04 10MAR04
Marketing . 0 13FEB04 13FEB04 11FEB04 11FEB04 10MAR04 10MAR04
;

```

```


data holdata;
  format hol date7.;
  input hol & date7. ;
  datalines;
25dec03
01jan04
;

/* set up required pattern statements */
pattern1 c=green v=s;      /* duration of a non-critical activity */
pattern2 c=green v=e;      /* slack time for a noncrit. activity */
pattern3 c=red v=s;        /* duration of a critical activity */
pattern4 c=magenta v=e;   /* slack time for a supercrit. activity */
pattern5 c=magenta v=s;   /* duration of a supercrit. activity */
pattern6 c=cyan v=s;       /* actual duration of an activity */
pattern7 c=black v=e;      /* break due to a holiday */
pattern8 c=blue v=s;       /* resource schedule of activity */
pattern9 c=brown v=s;     /* baseline schedule of activity */

title2 h=1.25 'Specifying the Schedule Data Directly';

proc gantt data=widgdir holdata=holdata;
  chart / holiday=(hol) dur=zdur
        ss=rs sf=rf ls=sdate lf=fdate
        height=1.5 pcompress;
  id task;
run;

```

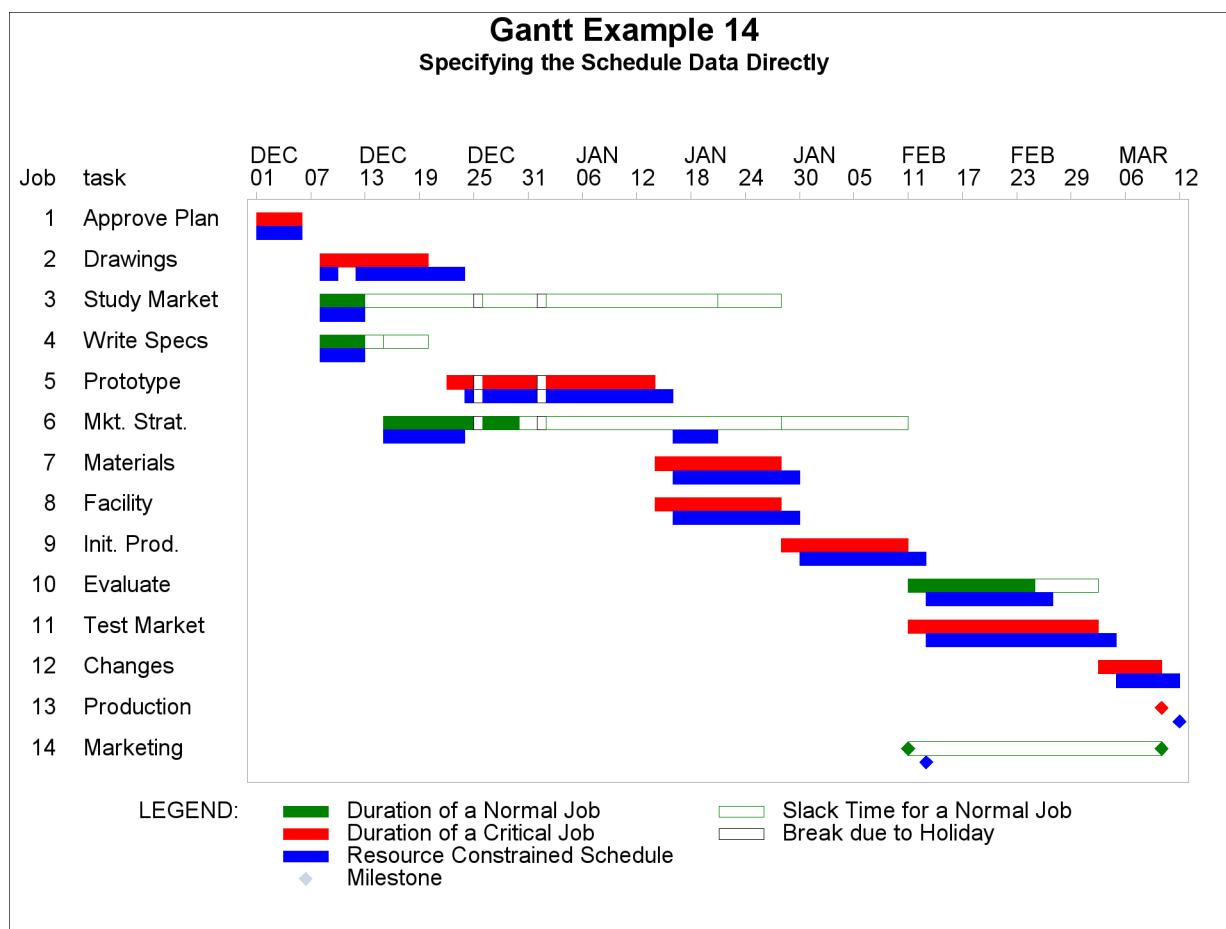**Output 8.14.1** Specifying the Schedule Data Directly

---

## Example 8.15: BY Processing

Every activity in the widget manufacturing project is carried out by one of five departments: Planning, Engineering, Marketing, Manufacturing, and Testing. The DETAILS data set in [Example 8.6](#) identifies the department responsible for each activity. Thus, the project can be thought of as made up of five smaller subprojects, a subproject being the work carried out by a department. A foreseeable need of the project manager and every department is a separate Gantt chart for each subproject. This example uses the WIDGETN data set from [Example 4.1](#), which is formed by merging the WIDGET data set with the DETAILS data set. After scheduling the master project using PROC CPM with DEPT as an ID variable, the Schedule data set is sorted by department name and early start time. The GANTT procedure is then invoked with the variable DEPT specified in the BY statement to obtain individual Gantt charts for each subproject. The Gantt charts for the five different subprojects are shown in [Output 8.15.1](#). The MINDATE= and MAXDATE= options have been specified to ensure a consistent date range across projects. Notice that the TITLE2 statement uses the text substitution option #BYVARn, which substitutes the name of the nth BY variable. The BY-LINE that appears below the titles identifies the current values of the BY variables. You can suppress this using the NOBYLINE option in an OPTION statement or the HBY option in a GOPTIONS statement. The SPLIT= option is specified to prevent the TASK variable label from being split on the embedded blank.

```



data widgetn;
  label task = "Activity Name";
  merge widget details;
  run;



proc cpm date='01dec03'd data=widgetn;
  activity task;
  duration days;
  successor succ1 succ2 succ3;
  id dept;
  run;


proc sort;
  by dept e_start;
  run;

proc gantt split('/');
  chart / pcompress scale=1 dur=days height=1.2
        mindate='01dec03'd maxdate='11feb04'd;
  by dept;
  id task;
  run;

```

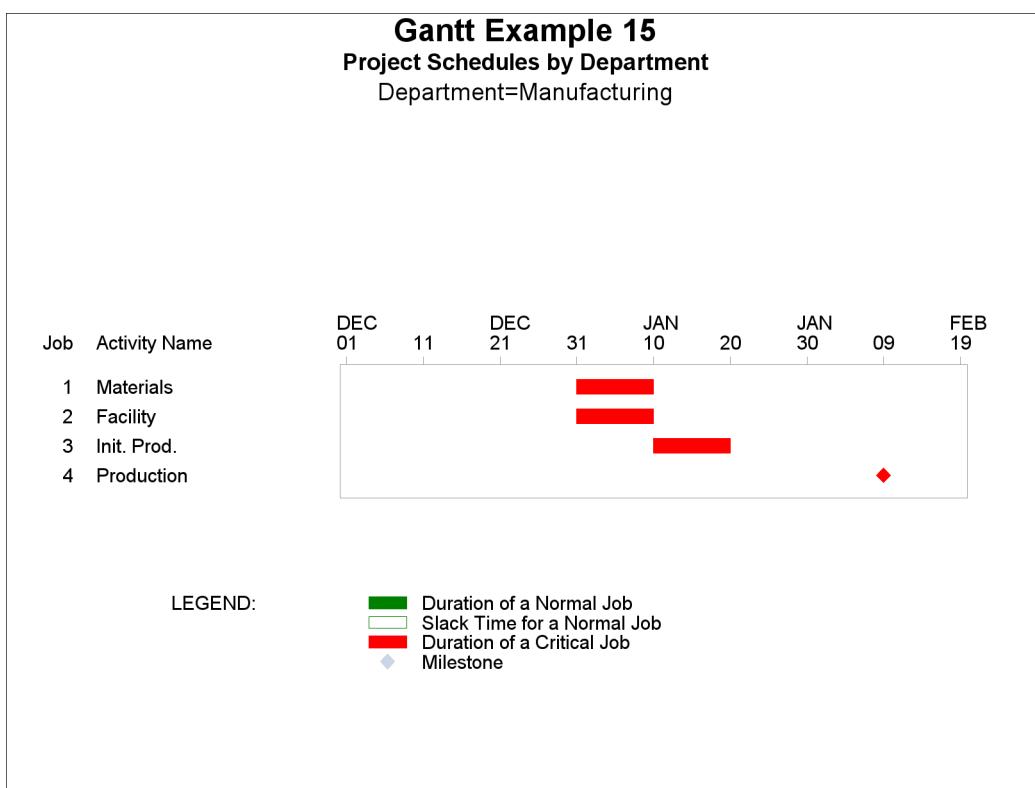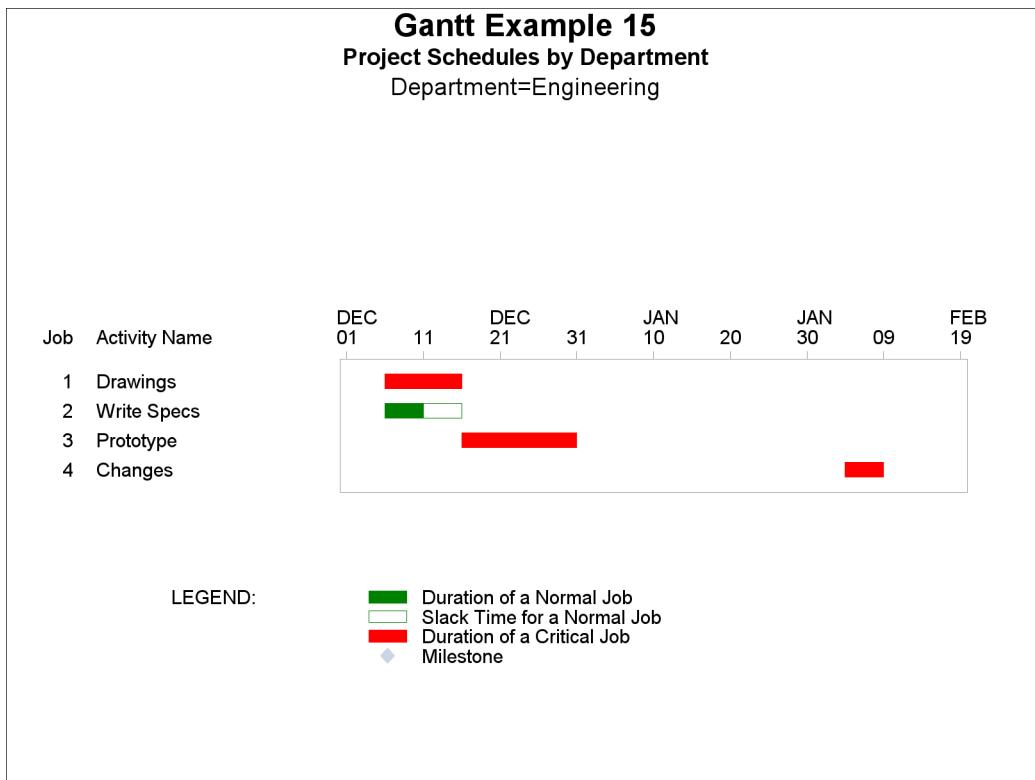**Output 8.15.1** Using BY Processing for Separate Gantt Charts

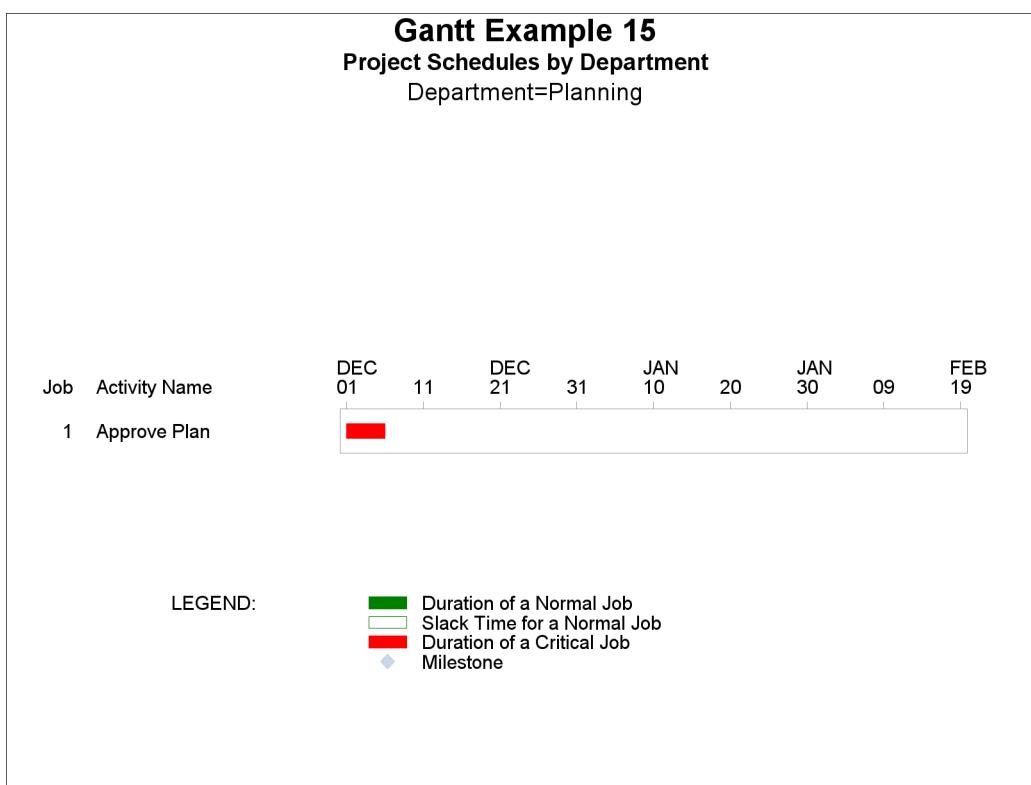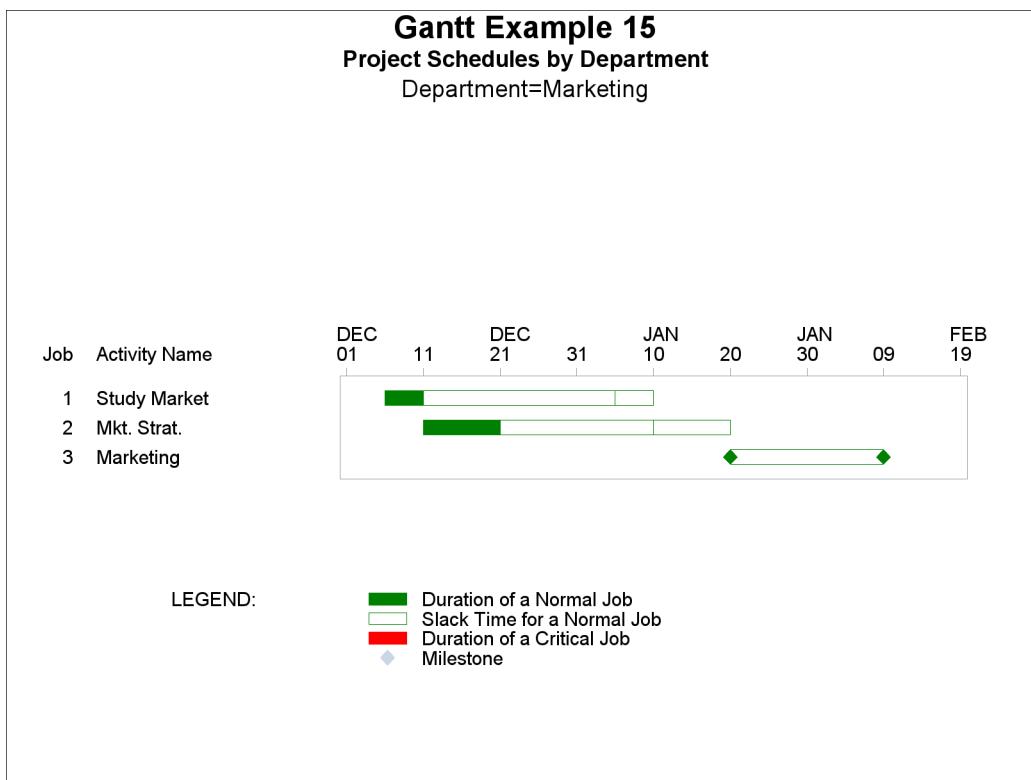**Output 8.15.1** *continued*

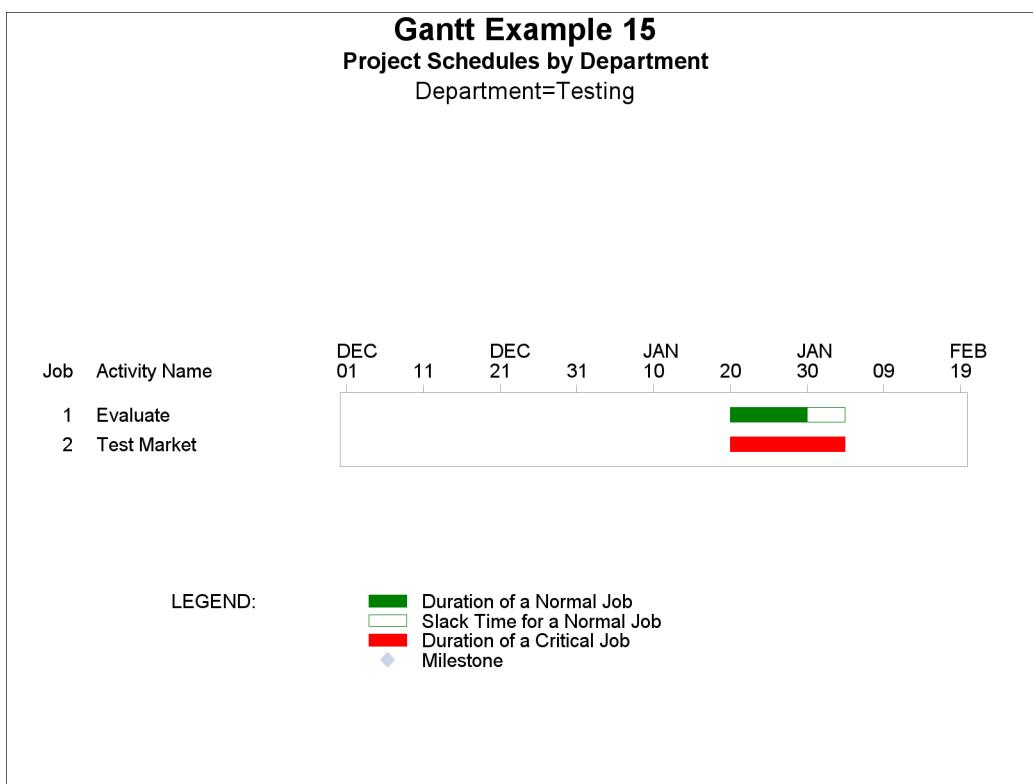**Output 8.15.1** *continued***Example 8.16: Gantt Charts by Persons**

Now suppose that you want to obtain individual Gantt charts for two people (Thomas and William) working on the widget manufacturing project. The data set WIDGBYGP, displayed in [Output 8.16.1](#), contains two new variables, THOMAS and WILLIAM. Each variable has a value ‘1’ for activities in which the person is involved and a missing value otherwise. Thus, a value of ‘1’ for the variable THOMAS in observation number 2 indicates that Thomas is working on the activity ‘Drawings.’

PROC CPM is used to schedule the project to start on December 1, 2003. A data set named PERSONS is created containing one observation per activity per person working on that activity and a new variable named PERSON containing the name of the person to which the observation pertains. For example, this new data set contains two observations for the activity ‘Write Specs,’ one with PERSON=‘Thomas’ and the other with PERSON=‘William,’ and no observation for the activity ‘Approve Plan.’ This data set is sorted by PERSON and E\_START, and displayed in [Output 8.16.2](#). PROC GANTT is next invoked with a BY statement to obtain individual charts for each person. The resulting Gantt charts are shown in [Output 8.16.3](#). The BY-LINE is suppressed by specifying the NOBYLINE option in an OPTIONS statement and the name of the person corresponding to the chart is displayed in the subtitle by using the #BYVAL substitution in the TITLE2 statement.

**Output 8.16.1 Data Set WIDGBYGP**  
**Data widgbyp**

Obs	task	days	tail	head	thomas	william
1	Approve Plan	5	1	2	.	.
2	Drawings	10	2	3	1	.
3	Study Market	5	2	4	.	.
4	Write Specs	5	2	3	1	1
5	Prototype	15	3	5	1	1
6	Mkt. Strat.	10	4	6	.	.
7	Materials	10	5	7	.	1
8	Facility	10	5	7	.	1
9	Init. Prod.	10	7	8	1	.
10	Evaluate	10	8	9	1	1
11	Test Market	15	6	9	.	.
12	Changes	5	9	10	1	.
13	Production	0	10	11	.	1
14	Marketing	0	6	12	.	.
15	Dummy	0	8	6	.	.

```

title h=1.75 'Gantt Example 16';

proc cpm data=widgbyp date='1dec03'd;
  tailnode tail;
  duration days;
  headnode head;
  id task thomas william;
run;

data persons;
  set _last_;
  if william^=. then do;
    person='William';
    output;
    end;
  if thomas^=. then do;
    person='Thomas';
    output;
    end;
  drop thomas william;
run;

proc sort data=persons;
  by person e_start;
run;

title2 'Data PERSONS';
proc print data=persons;
run;

```

```

/* suppress byline */
options nobyline;

options hpos=120 vpos=40 htext=1.1;



title2 h=1.25 'Personalized Gantt Chart for #BYVAL(person) ';
proc gantt data=persons;
chart / pcompress;
by person;
id task;
run;

```

### Output 8.16.2 Data Set PERSONS

**Gantt Example 16**  
**Data PERSONS**

Obs	tail	head	days	task	E_START	E_FINISH	L_START	L_FINISH	T_FLOAT	F_FLOAT	person
1	2	3	10	Drawings	06DEC03	15DEC03	06DEC03	15DEC03	0	0	Thomas
2	2	3	5	Write Specs	06DEC03	10DEC03	11DEC03	15DEC03	5	5	Thomas
3	3	5	15	Prototype	16DEC03	30DEC03	16DEC03	30DEC03	0	0	Thomas
4	7	8	10	Init. Prod.	10JAN04	19JAN04	10JAN04	19JAN04	0	0	Thomas
5	8	9	10	Evaluate	20JAN04	29JAN04	25JAN04	03FEB04	5	5	Thomas
6	9	10	5	Changes	04FEB04	08FEB04	04FEB04	08FEB04	0	0	Thomas
7	2	3	5	Write Specs	06DEC03	10DEC03	11DEC03	15DEC03	5	5	William
8	3	5	15	Prototype	16DEC03	30DEC03	16DEC03	30DEC03	0	0	William
9	5	7	10	Materials	31DEC03	09JAN04	31DEC03	09JAN04	0	0	William
10	5	7	10	Facility	31DEC03	09JAN04	31DEC03	09JAN04	0	0	William
11	8	9	10	Evaluate	20JAN04	29JAN04	25JAN04	03FEB04	5	5	William
12	10	11	0	Production	09FEB04	09FEB04	09FEB04	09FEB04	0	0	William

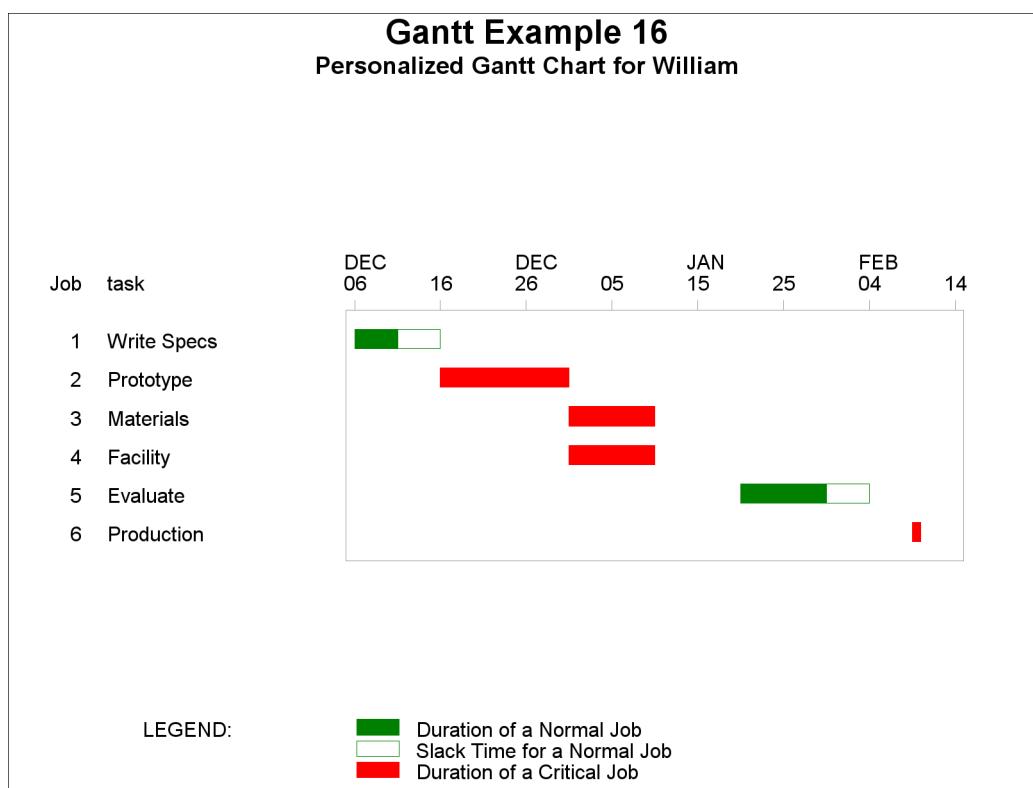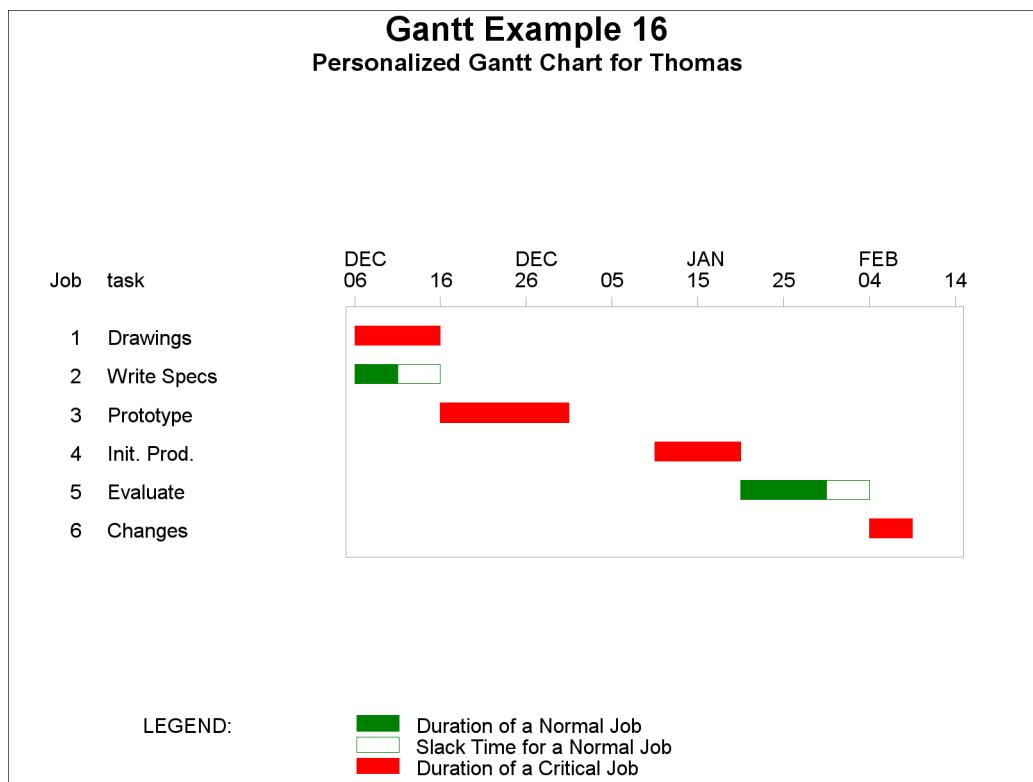**Output 8.16.3** Gantt Charts by Person

---

## Example 8.17: Using the HEIGHT= and HTOFF= Options

The following example illustrates two options that control the height and positioning of all text produced by PROC GANTT. The data used for this example come from [Example 8.13](#), which illustrates plotting of the resource-constrained schedule. PATTERN statements are specified in order to identify the fill patterns for the different schedule types and holidays. The resource-constrained schedule is drawn using the fill pattern from the eighth PATTERN statement. The HEIGHT= option is set to 2, indicating that the height of all text produced by PROC GANTT be equal to the height of two activity bars. This text includes activity text, legend text, and axis labeling text. The HTOFF= option is also set to 2, which drops the font baseline of the activity text by the height of one schedule bar causing the font baseline to be positioned at the bottom of the resource-constrained schedule bar. The resulting Gantt chart is displayed in [Output 8.17.1](#).

```

title 'Gantt Example 17';

* set up required pattern statements;


pattern1 c=blue v=s;      /* duration of a non-critical activity */
pattern2 c=blue v=e;      /* slack time for a noncrit. activity */
pattern3 c=red v=s;       /* duration of a critical activity */
pattern4 c=red v=e;       /* slack time for a supercrit. activity */
pattern5 c=red v=r2;      /* duration of a supercrit. activity */
pattern6 c=cyan v=s;      /* actual duration of an activity */
pattern7 c=blue v=r1;     /* break due to a holiday */
pattern8 c=red v=x1;      /* resource schedule of activity */
pattern9 c=blue v=s;      /* baseline schedule of activity */

* set vpos to 50 and hpos to 100;
goptions vpos=50 hpos=100;

title2 'Using the HEIGHT= and HTOFF= options';

* draw Gantt chart using height and htoff equal to 2;
proc gantt graphics data=spltschd holdata=holdata;
    chart / holiday=(hol) dur=days compress cmile=green caxis=black
          height=2 htoff=2;
    id task;
    run;

```

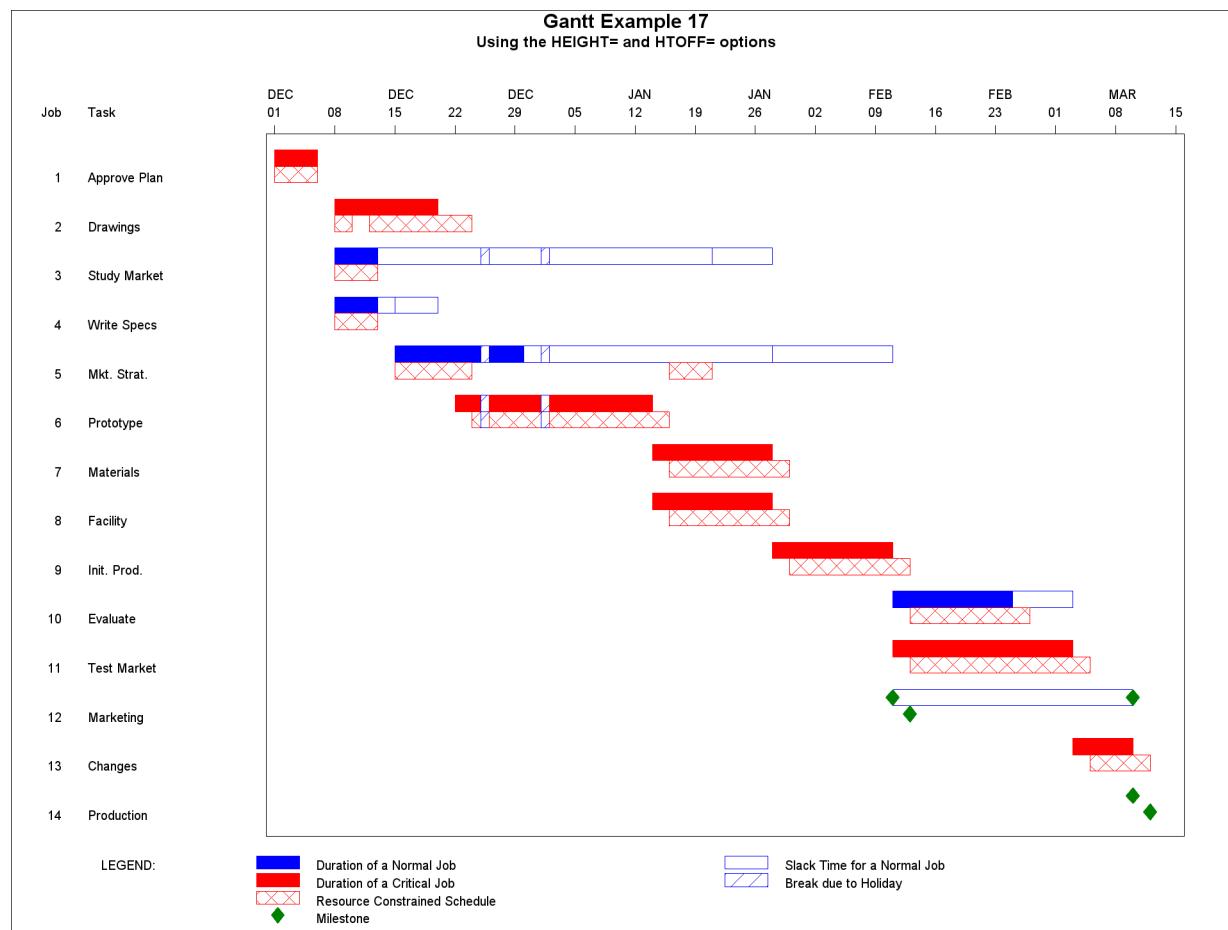**Output 8.17.1** Using the HEIGHT= and HTOFF= options

---

## Example 8.18: Drawing a Logic Gantt Chart Using AON Representation

This example uses the data of Example 8.10, which illustrates the drawing of the actual schedule. The ACTIVITY= and SUCCESSOR= options are specified in the CHART statement to define the precedence relationships using the AON format to PROC GANTT. Since no LAG= option is specified, the lag type of each connection is assumed to be Finish-to-Start (FS). In this case, the precedence defining variables exist in the WIDGELA data set; however, this is not a requirement. The precedence defining variables can belong to a different data set as long as the ACTIVITY variable is common to both data sets and the PRECDATA= option, identifying the Precedence data set, is specified in the PROC GANTT statement. Setting the LEVEL= option to 2 causes the actual schedule bar to be used as the logic bar; that is, PROC GANTT draws the precedence connections with respect to the actual schedule. By default, the precedence connections are drawn with respect to the first bar. The color of the precedence connections is specified with the CPREC= option in the CHART statement. You can change the line style and line width of the precedence connections by specifying the LPREC= and WPREC= options in the CHART statement. The resulting Gantt chart is shown in [Output 8.18.1](#).

```

title h=1.75 'Gantt Example 18';


title2 h=1.25 'Logic Gantt Chart: AON Representation and LEVEL= Option';

* sort the data;
proc sort;
  by e_start;
  run;

* set graphics options;
goptions vpos=50 hpos=100 htext=1.2;

* draw the logic Gantt chart;
proc gantt graphics data=widgela holidata=holidays;
  chart / holiday=(holiday) holifin=(holifin)
        a_start=sdate a_finish=fdate dur=days
        compress
        cmile=black
        activity=task successor=(succ1-succ3)
        caxis=black
        level=2
        cprec=blue;
  id task;
  run;

```

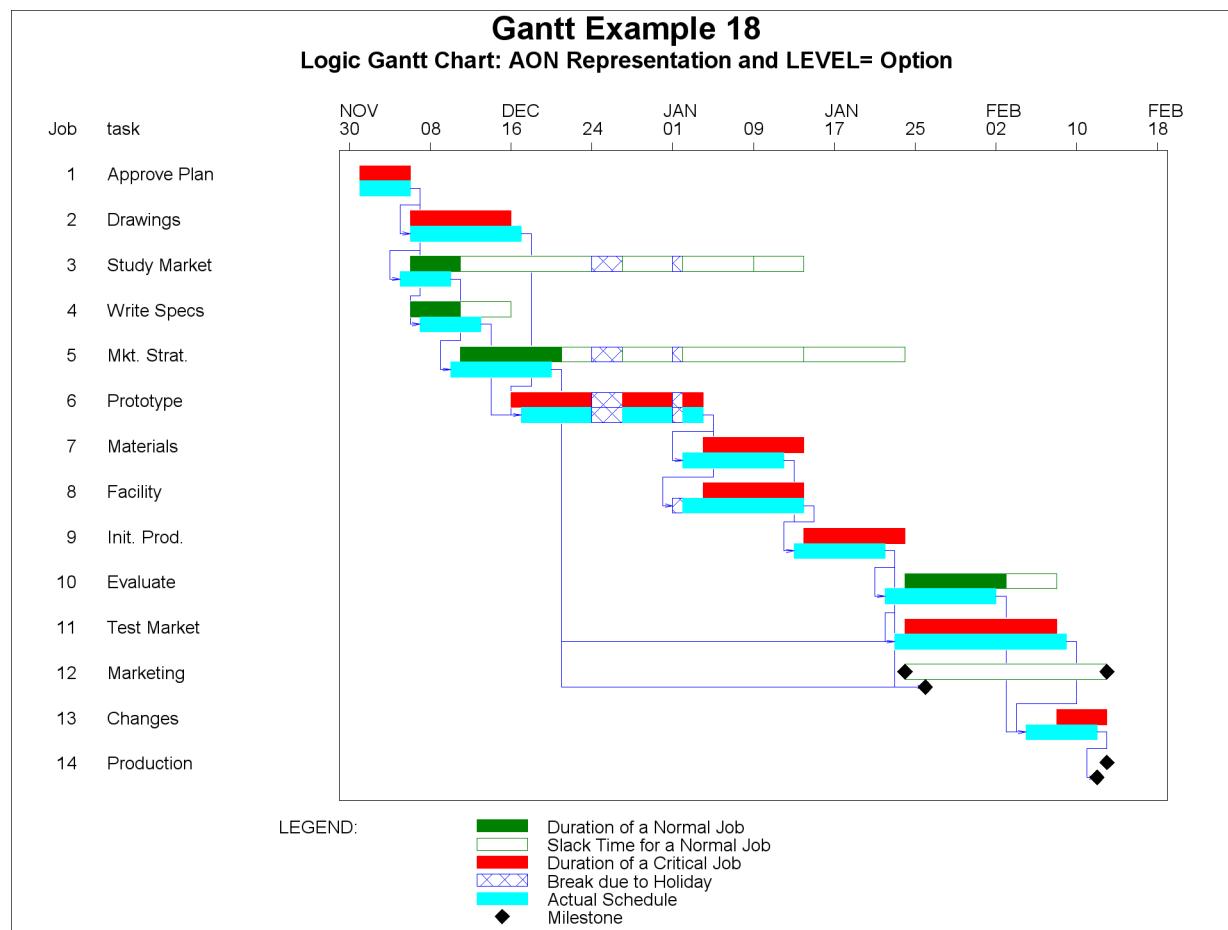**Output 8.18.1** Drawing a Logic Gantt Chart Using AON Representation

---

## Example 8.19: Specifying the Logic Control Options

This example illustrates four options that control the routing of a precedence connection from an activity to its successor on the logic Gantt chart. The example also illustrates the drawing of a Logic Gantt chart using the Activity-on-Arc format.

The Activity data set for PROC CPM is the WIDGETA data set from [Example 4.2](#), which defines the widget manufacturing project in AOA format. The project is scheduled subject to weekends, and the holidays are defined in the HOLDATA data set. The resulting schedule is stored in the output data set SAVEHP. The GANTT procedure is next invoked to produce a Logic Gantt chart by specifying the HEAD= and TAIL= options in the CHART statement. The resulting Logic Gantt chart is shown in [Output 8.19.1](#).

```

title h=1.75 'Gantt Example 19';

data holdata;
  format hol date7.;
  input hol & date7. ;
  datalines;
25dec03
01jan04
;

/* schedule the project subject to holidays and weekends;
proc cpm data=widgeta holdata=holdata out=savehp
      date='1dec03'd interval=weekday;
  tailnode tail;
  headnode head;
  duration days;
  holiday hol;
  id task dept descrpt;
run;

/* sort the schedule by the early start date;
proc sort;
  by e_start;
run;


/* set background to white and text to black;
goptions cback=white ctext=black;

/* set additional graphics options;
goptions vpos=50 hpos=100 htext=1.1;

/* plot the logic Gantt chart using AOA representation;
title2 h=1.25 'Logic Gantt Chart: AOA Representation';

proc gantt graphics data=savehp holdata=holdata;
  chart / compress cprec=blue caxis=black cmile=cyan
        increment=7 height=1.5
        dur=days holiday=(hol)
        head=head tail=tail;
  id task;
run;

```

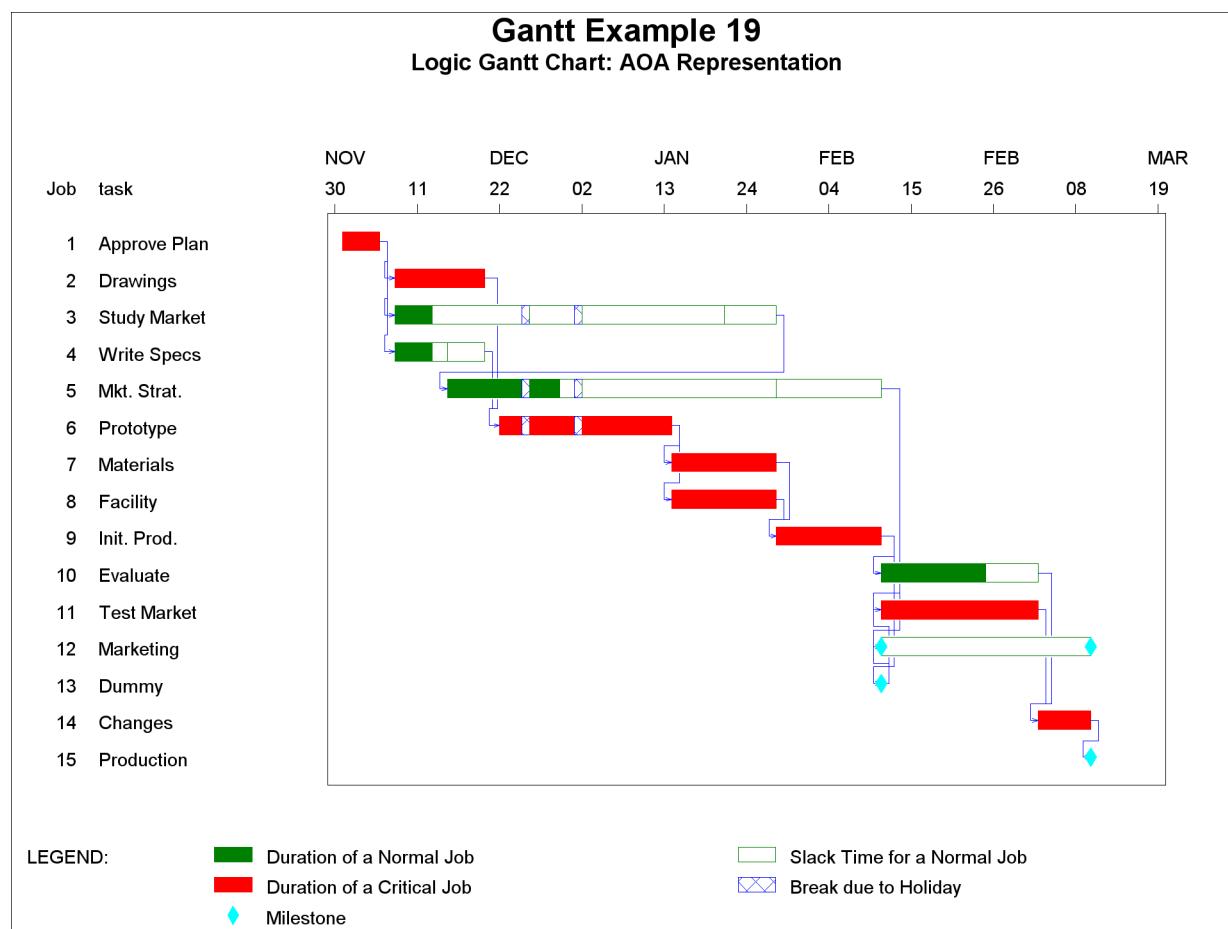**Output 8.19.1** Logic Gantt Chart: AOA Representation

The next invocation of PROC GANTT illustrates the effect of the MININTGV= and MINOFFGV= options, which control placement of the global verticals. The concept of global verticals is explained in the section “[Specifying the Logic Options](#)” on page 545. The data sets from the previous invocation of the GANTT procedure remain unchanged. The minimum distance of a global vertical from the end of the bar it is associated with is increased from its default of 1 cell to 2.5 cells by specifying MINOFFGV=2.5. Likewise, the minimum distance between any two global verticals is increased from its default of .75 cells to 2 cells by specifying MININTGV=2.0. The effects of these changes are visible in the resulting Logic Gantt chart shown in [Output 8.19.2](#).

```

goptions htext=1.4;


* illustrate the minintgv and minoffgv options;
title2 h=1.25
  'Logic Gantt Chart: AOA Representation, MININTGV=2 and MINOFFGV=2.5';

proc gantt graphics data=savehp holdata=holdata;
  chart / dur=days holiday=(hol) compress increment=7
    cprec=blue caxis=black cmile=cyan
    head=head tail=tail
    minintgv=2.0 minoffgv=2.5;
  id task;
  run;

```

Notice that now there is greater distance between vertical segments (corresponding to global verticals), and the horizontal segments leaving bars are longer.

#### Output 8.19.2 Specifying the MININTGV= and MINOFFGV= Options

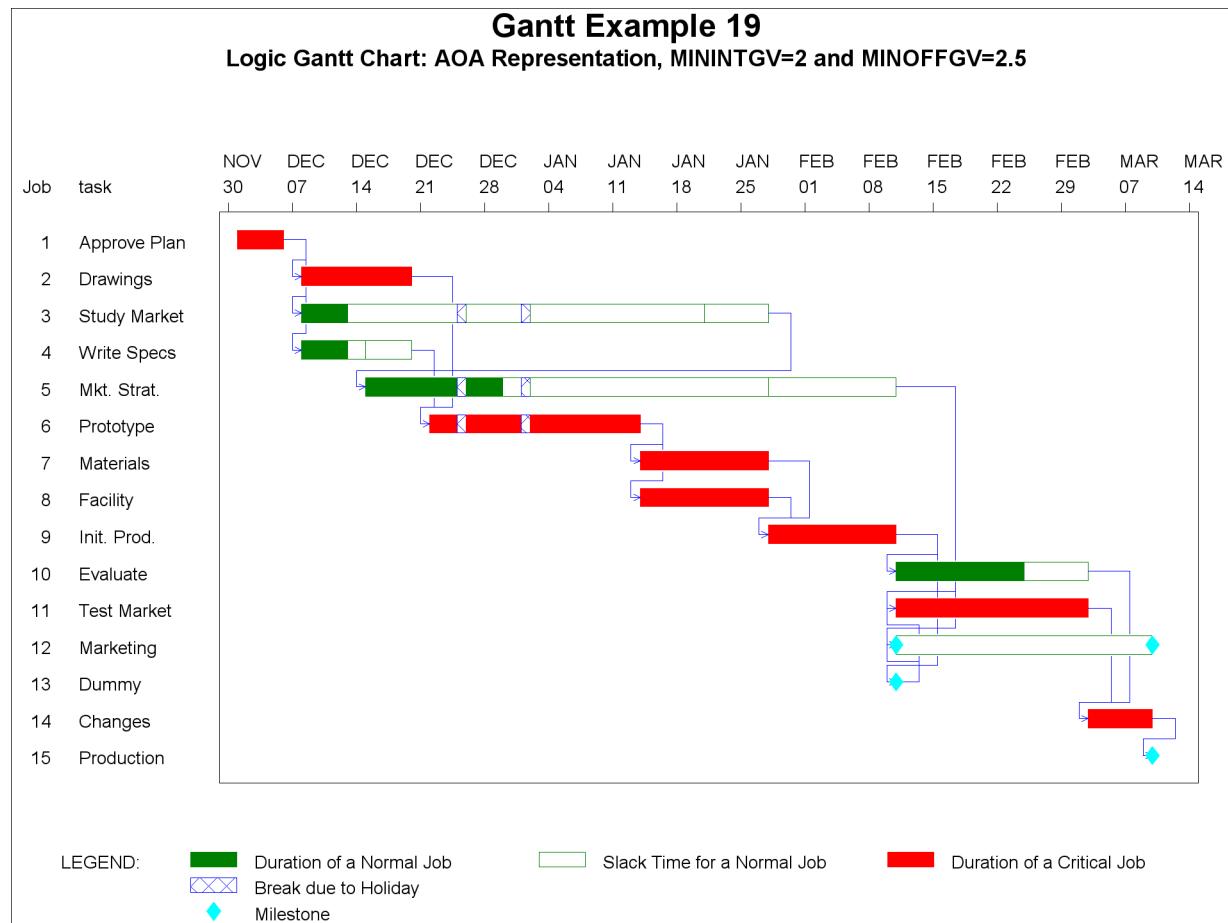


The MAXDATE= option is specified in the remaining Gantt calls in this example in order to focus on the schedule bars of the first few activities in the chart. The next two outputs illustrate the use of the MAXDISLV= option in the CHART statement. The MAXDISLV= option is used as a safeguard to limit the feasible region made available to PROC GANTT for placement of local verticals. The value specified dictates the maximum allowable displacement of the local vertical from its ideal position, that is, at a distance of MINOFFLV= from the end of the bar with which it is associated. However, this ideal position may tend to be positioned too close to a global vertical or even coincide with one. Depending on the cell width, this can result in visual misinterpretation of the Logic Gantt chart. In order to avoid this scenario, you should specify a reasonable value for the MAXDISLV= option to permit a certain amount of freedom for local vertical placement so as to distinguish between local and global verticals. Typically, use of this option is desirable when the value of the MININTGV= option, the minimum distance between global verticals, is relatively much greater than the value of the MAXDISLV= option.

To illustrate, consider the following Gantt call with a large MININTGV= value (10) and a relatively smaller MAXDISLV= value (0.3). Thus, for every local vertical, PROC GANTT has a very small interval that is less than a third of a cell wide in which to place that local vertical regardless of whether a global vertical runs through that interval or not. The result of this constraint is illustrated in the chart shown in Output 8.19.3. The local vertical for ‘Drawings’ is positioned as far as possible from the global vertical of ‘Approve Plan,’ but the value of the MAXDISLV= option restricts it from being positioned any further. Visually it is not pleasing, and it is difficult to distinguish the local and global verticals. A similar situation is evident with the local vertical of ‘Prototype’ and the global vertical of ‘Write Specs.’

```
goptions htext=1.2;

* illustrate the maxdislv option;
title2 h=1.25 'Logic Gantt Chart: AOA Representation and MAXDISLV=.3';

proc gantt graphics data=savehp holdata=holdata;
  chart / compress cprec=blue caxis=black cmile=cyan
    dur=days holiday=(hol)
    head=head tail=tail
    maxdislv=.3 minintgv=10
    maxdate='01feb04'd;
  id task;
  run;
```

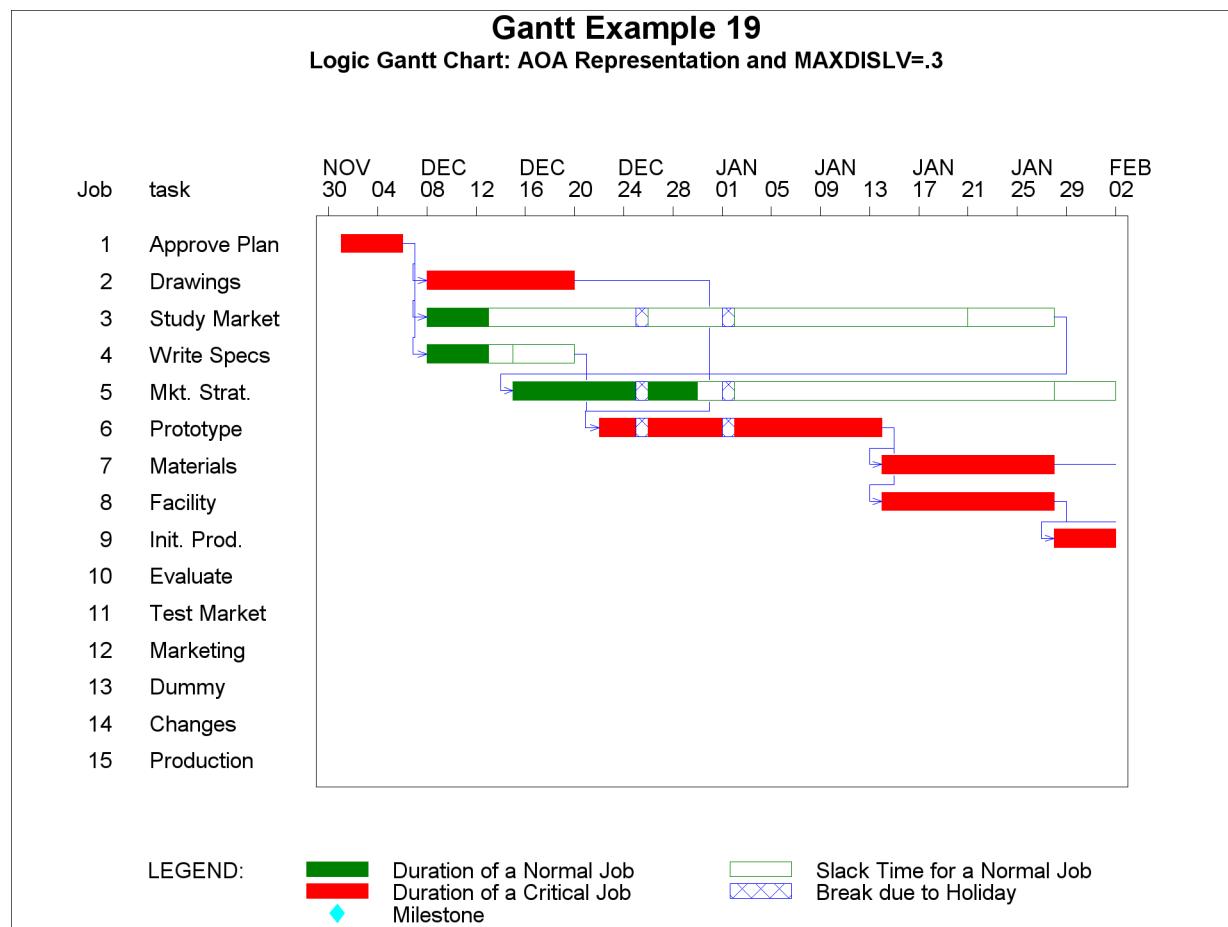**Output 8.19.3** Specifying the MAXDISLV= Option (I)

By reducing the value of MAXDISLV= even further, you can produce a chart that gives the appearance of a local vertical overlapping with a global vertical owing to resolution limitations of the display device. Theoretically, by design, this will never be the case. Recall that the value of the MAXDISLV= option is strictly positive and is at least one-tenth of a cell width.


The solution to this problem is to increase the value of the MAXDISLV= option so that the local vertical can be displaced further away from any adjacent global verticals. In the next invocation of PROC GANTT, the value of the MAXDISLV= option is increased to 2, resulting in a Logic Gantt chart in which the local verticals are staggered further away from nearby global verticals. This Gantt chart is displayed in [Output 8.19.4](#).

```

title2 h=1.25 'Logic Gantt Chart: AOA Representation and MAXDISLV=2';

proc gantt graphics data=savehp holidata=holodata;
  chart / compress cprec=blue caxis=black cmile=cyan
    dur=days holiday=(hol)
    head=head tail=tail
    maxdislv=2 minintgv=10
    maxdate='01feb04'd;
  id task;
run;

```

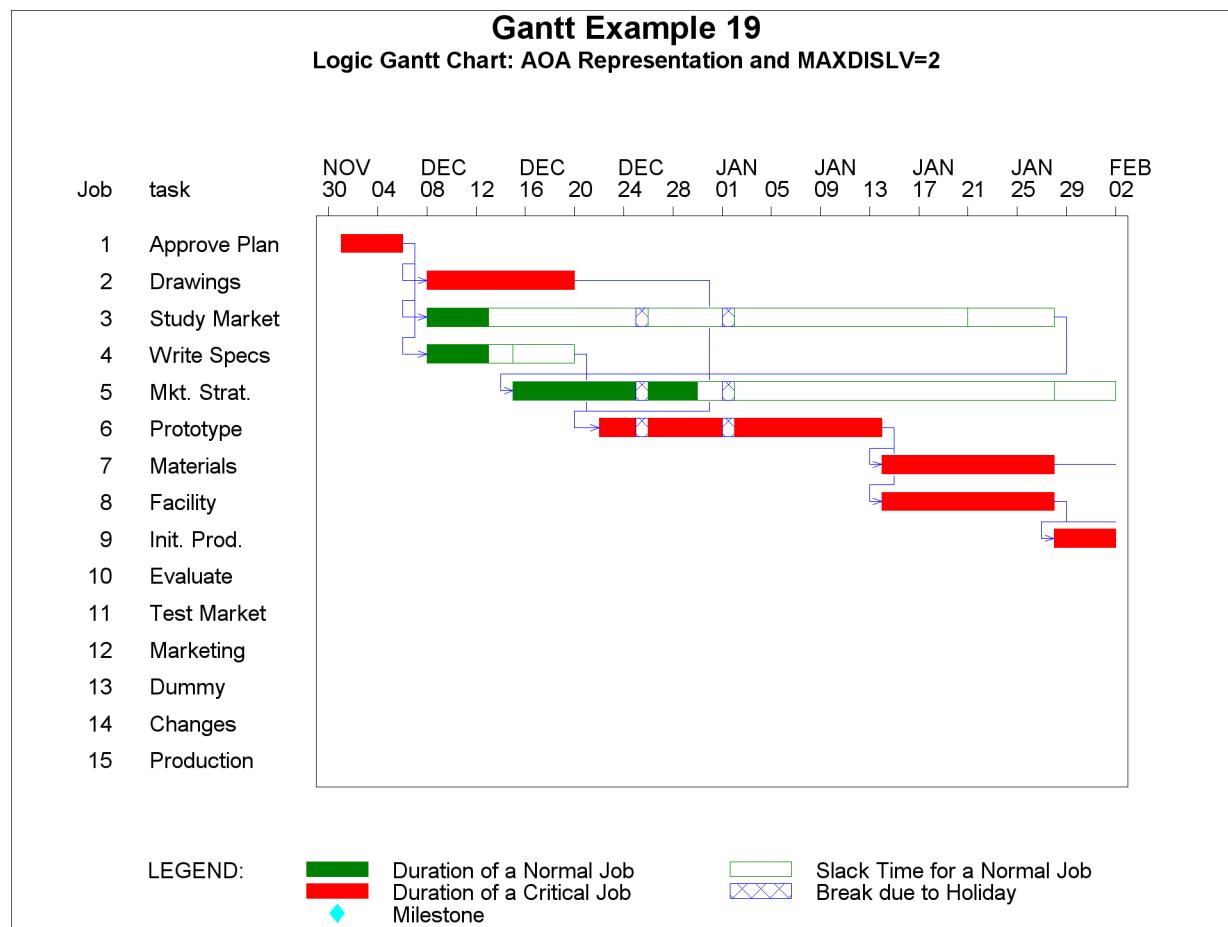**Output 8.19.4 Specifying the MAXDISLV= Option (II)**

The final Gantt chart in this example illustrates the use of the MINOFFLV= option in the CHART statement. This option specifies the minimum distance of a local vertical from the end of the bar with which it is associated. Although the position corresponding to the MINOFFLV= option is the position of choice for placement of the local vertical, the actual placement can differ from this position owing to the presence of nearby global verticals, as illustrated by Output 8.19.3 and Output 8.19.4. The maximum amount of displacement is determined by the value of the MAXDISLV= option.

In all of the preceding charts in this example, the connection from the activity, ‘Approve Plan,’ to each of its three successors, ‘Drawings’, ‘Study Market’, and ‘Write Specs’, is a 5-segment connection similar to the type illustrated in Figure 8.14. This is caused by backtracking of the activity’s global vertical to the successor’s local vertical as described in the section “Controlling the Layout” on page 548. To transform this connection into a 3-segment connection as shown in Figure 8.13, you need to position the local vertical to the right of the global vertical. The following invocation of PROC GANTT achieves this by specifying MINOFFLV=0.5, and the resulting Gantt chart is shown in Output 8.19.5. Notice that this option affects the positioning of *all* local verticals on the chart in contrast to the MAXDISLV= option, which affects only those local verticals that are close to global verticals.

```
* illustrate the minofflv option;
title2 h=1.25
'Logic Gantt Chart: AOA Representation and MINOFFLV=.5';


proc gantt graphics data=savehp holidata=holdata;
```

```

chart / compress cprec=blue caxis=black cmile=cyan
      dur=days holiday=(hol)
      head=head tail=tail
      minofflv=.5
      maxdate='01feb04'd;
id task;
run;

```

### Output 8.19.5 Specifying the MINOFFLV= Option

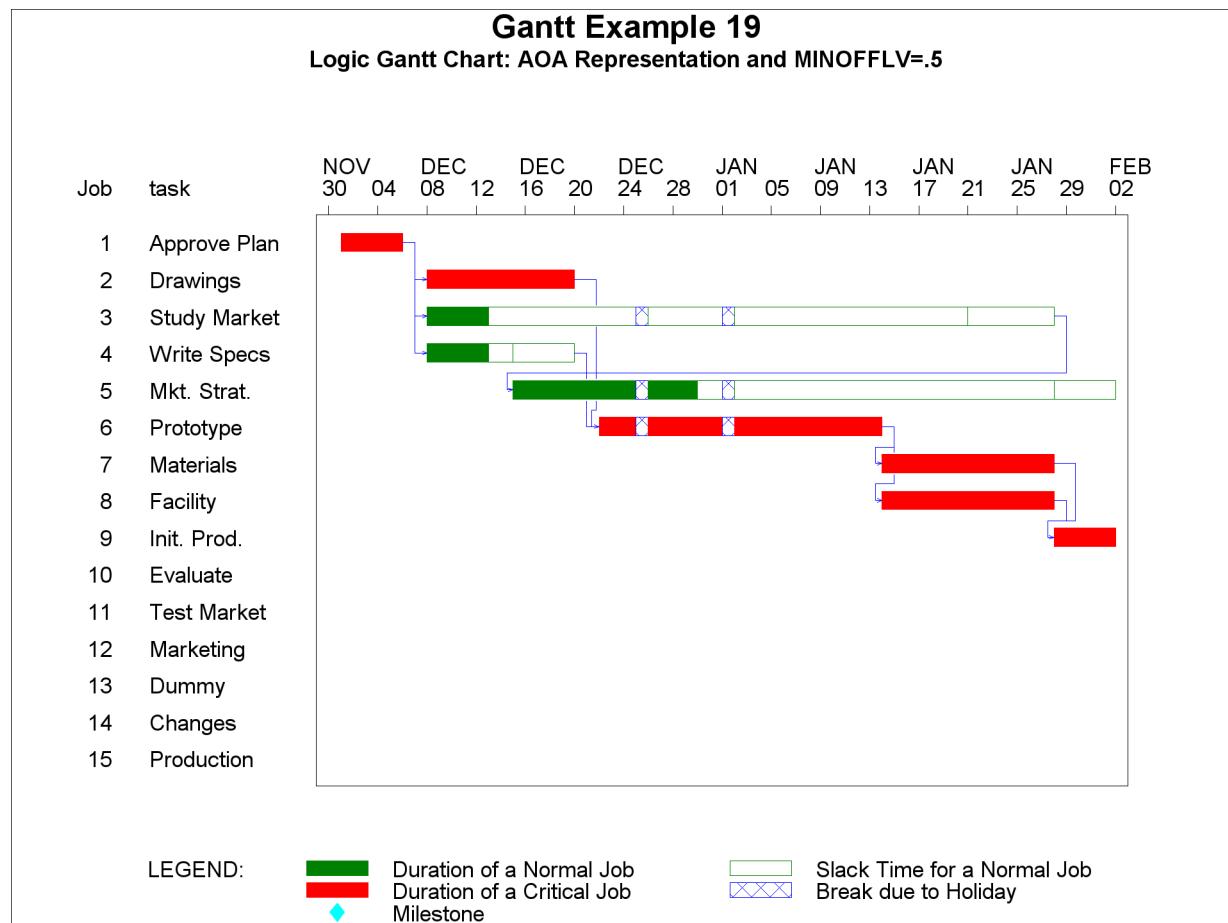

---

## Example 8.20: Nonstandard Precedence Relationships

This example demonstrates the use of nonstandard precedence relationships and specification of the PRECDATA= option in the PROC GANTT statement.

The project and nonstandard precedence relationships are defined by the WIDGLAG2 data set, which is a modification of the WIDGLAG data set that was used in [Example 4.11](#) to illustrate the CPM procedure. The activity and successor variables are represented by the TASK and SUCC variables, respectively, and the lag type of the relationship is defined by the LAGDUR variable. The LAGDUR variable defines the lag type in *keyword\_duration\_calendar* format for the purpose of passing the information to PROC CPM. Although PROC GANTT accepts this format for a lag variable, it does not use the *duration* and *calendar* values when drawing the connection since the schedule is already computed at this time (presumably by PROC CPM).

As in the WIDGLAG data set, the WIDGLAG2 data set specifies a Start-to-Start lag of nine days between the activity ‘Prototype’ and its successors, ‘Materials’ and ‘Facility,’ and a Finish-to-Start lag of two days between ‘Facility’ and ‘Init. Prod.’. In addition, changes to the widget design are permitted to be made no earlier than six days after in-house evaluation of the product has begun. Furthermore, the Engineering department has to ensure that there will be at least three days available for any changes that need to be carried out after the test market results have come in. These constraints are incorporated in the WIDGLAG data set by setting the value of the LAGDUR variable equal to ‘ss\_6’ for the relationship between ‘Evaluate’ and ‘Changes’ and equal to ‘ff\_3’ for the relationship between ‘Test Market’ and ‘Changes.’

The project is scheduled using PROC CPM subject to weekends and the holidays defined in the HOLIDAYS data set. Specifying the COLLAPSE option in the PROC CPM statement ensures that there is one observation per activity. The WIDGLAGH data set is created by deleting the successor variable from the Schedule data set produced by PROC CPM.

Since there is no precedence information contained in the WIDGLAGH data set, specifying DATA=WIDGLAGH in the PROC GANTT statement without the PRECDATA= option produces a nonprecedence Gantt chart. You can produce a Logic Gantt chart by specifying the precedence information using the PRECDATA= option in the PROC GANTT statement as long as the activity variable is common to both the schedule and Precedence data sets.

The Gantt chart shown in [Output 8.20.1](#) is produced by specifying PRECDATA= WIDGLAG2. The lag type of the precedence connections is indicated to PROC GANTT using the LAG= option in the CHART statement. The width of the precedence connections is set to 2 with the WPREC= option, and the color of the connections is set to blue using the CPREC= option. The MININTGV= and MINOFFLV= options are specified in the CHART statement in an attempt to minimize the number of 5-segment connections. A reference line with a line style of 2 is drawn at the beginning of every month by using the REF= and LREF= options in the CHART statement.

```
options ps=60 ls=100;

title h=2 'Gantt Example 20';

/* Activity-on-Node representation of the project with lags */
data widglag2;
  format task $12. succ $12. lagdur $4. ;
  input task & days succ & lagdur $ ;
  datalines;
  Approve Plan    5  Drawings
.
```

```

Approve Plan      5 Study Market   .
Approve Plan      5 Write Specs   .
Drawings          10 Prototype    .
Study Market      5 Mkt. Strat.   .
Write Specs        5 Prototype    .
Prototype          15 Materials    ss_9
Prototype          15 Facility     ss_9
Mkt. Strat.       10 Test Market  .
Mkt. Strat.       10 Marketing   .
Materials          10 Init. Prod.  .
Facility           10 Init. Prod.  fs_2
Init. Prod.        10 Test Market .
Init. Prod.        10 Marketing   .
Init. Prod.        10 Evaluate    .
Evaluate           10 Changes     ss_6
Test Market        15 Changes     ff_3
Changes            5 Production  .
Production         0 .           .
Marketing          0 .           .
;

data holidays;
  format holiday holifin date7.;
  input holiday & date7. holifin & date7. holidur;
  datalines;
24dec03 26dec03 4
01jan04 .
;

proc cpm data=widglag2 holidata=holidays date='1dec03'd
  interval=weekday collapse;
  activity task;
  succ      succ / lag = (lagdur);
  duration days;
  holiday  holiday / holifin=(holifin);
run;

data widglagh;
  set _last_;
  drop succ;
  run;

* set up required pattern statements;
pattern1 c=blue v=s; /* duration of a noncrit. activity */
pattern2 c=blue v=e; /* slack time for a noncrit. act. */
pattern3 c=red v=s; /* duration of a critical activity */
pattern4 c=red v=e; /* slack time for a supercrit. act. */
pattern5 c=red v=r2; /* duration of a supercrit. act. */
pattern6 c=cyan v=s; /* actual duration of an activity */
pattern7 c=black v=x1; /* break due to a holiday */

* set graphics options;
goptions vpos=50 hpos=100 htext=1.025;

```


```

title2 c=black h=1.5
'Nonstandard Precedence Relationships and the PRECDATA= Option';

proc gantt graphics data=widglagh preCDATA=widglag2
    holidata=holidays;
chart / compress dur=days height=1.5
    holiday=(holiday) holifin=(holifin)
    cmile=blue cprec=blue wprec=2
    ref='01dec03'd to '01mar04'd by month
    cref=black lref=2 reflabel caxis=black
    act=task succ=(succ) lag=(lagdur)
    minintgv=2 minofflv=.5;
id task;
run;

```

### Output 8.20.1 Nonstandard Precedence Relationships

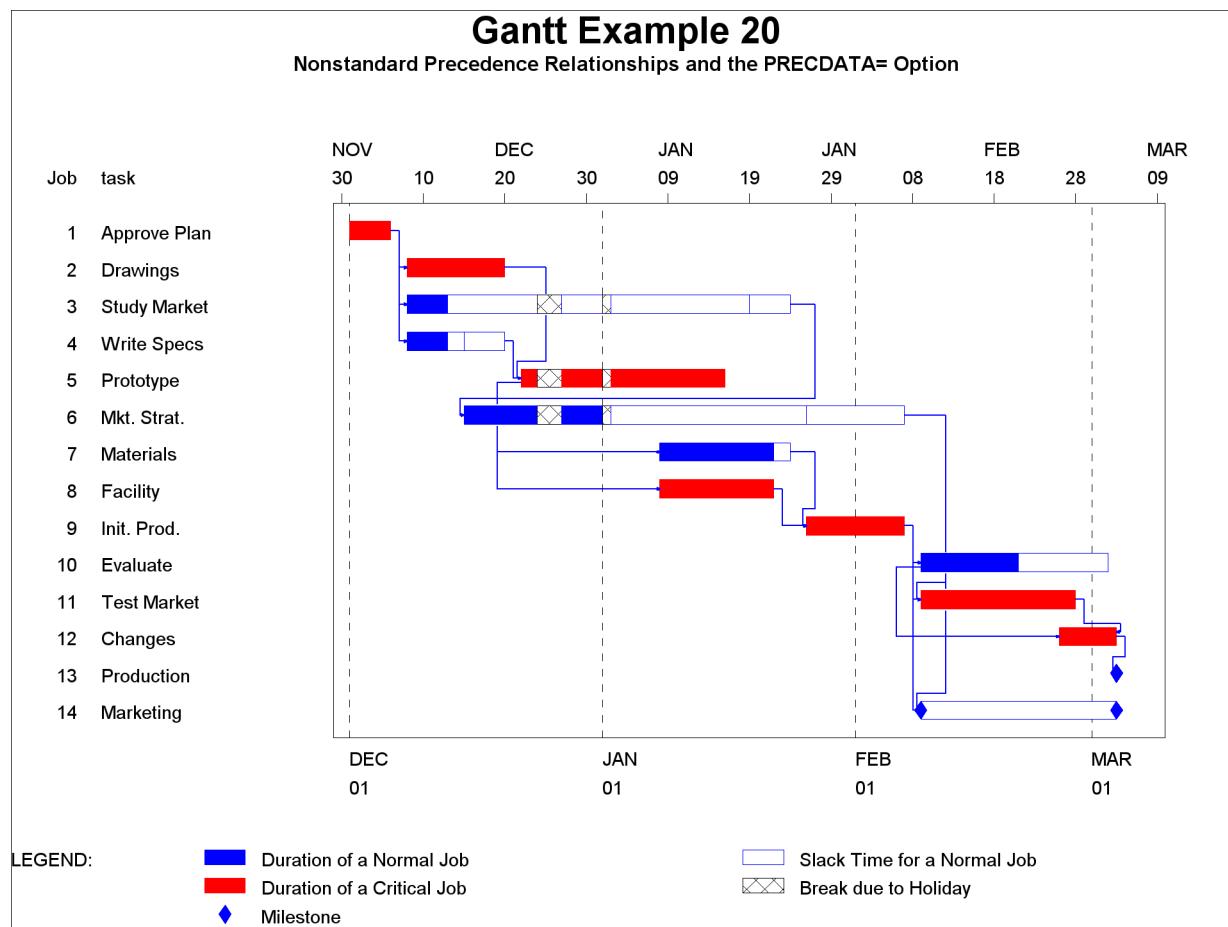

---

## Example 8.21: Using the SAS/GGRAPH ANNOTATE= Option

This example illustrates the use of the ANNOTATE= option to add graphics and text to the body of the Gantt chart. The intent of the first invocation of PROC GANTT is to display the resource requirements of each activity on the Gantt chart, while that of the second invocation is to plot the resource usage bar chart for the replenishable resource engineers and the resource availability curve for the consumable resource cost.

The data for this example come from [Example 4.15](#), in which the widget manufacturing project is scheduled using PROC CPM subject to resource constraints. The project network is defined in the WIDGRES data set using AOA format. The number of engineers needed per day per activity is a replenishable resource and is identified by the ENGINEER variable in the WIDGRES data set. The cost incurred per day per activity is a consumable resource and is identified by the ENGCOST variable in the WIDGRES data set. The WIDGRIN data set specifies the resource availabilities for the project. The schedule produced by PROC CPM using the default choice of LST as a heuristic is shown in [Output 8.21.1](#). The following programs assume that the schedule is stored in the WIDGSCH2 data set and that the resource usage is stored in the WIDGROU2 data set.

The Annotate macros are used in this example to simplify the process of creating Annotate observations. The ANNOMAC macro is first used to compile the Annotate macros and make them available for use. The Annotate data set ANNO1 is then created using the Annotate macros. The DCLANNO macro declares all Annotate variables except the TEXT variable, and the SYSTEM macro defines the Annotate reference system. The coordinate system defined here uses *date* for the horizontal scale and *job number* for the vertical scale. The text to be displayed contains the number of engineers required per day and the total cost over the duration of the activity. The LABEL macro is used to annotate the necessary text on the Gantt chart using the BRUSH font.

The GANTT procedure is invoked with the ANNOTATE=ANNO1 specification in the PROC GANTT statement. The resulting Gantt chart is shown in [Output 8.21.2](#). It is important to note that the job number will be used for the vertical scale even if NOJOBNUM is specified in the CHART statement.

**Output 8.21.1** Resource Constrained Schedule: Rule = LST**Resource Constrained Schedule: Rule = LST**

Obs	tail	head	days	task	engineer	engcost	S_START	S_FINISH	E_START	E_FINISH
1	1	2	5	Approve Plan	2	400	01DEC03	05DEC03	01DEC03	05DEC03
2	2	3	10	Drawings	1	200	08DEC03	19DEC03	08DEC03	19DEC03
3	2	4	5	Study Market	1	200	15DEC03	19DEC03	08DEC03	12DEC03
4	2	3	5	Write Specs	2	400	08DEC03	12DEC03	08DEC03	12DEC03
5	3	5	15	Prototype	4	800	26DEC03	16JAN04	22DEC03	13JAN04
6	4	6	10	Mkt. Strat.	.	.	22DEC03	06JAN04	15DEC03	29DEC03
7	5	7	10	Materials	.	.	19JAN04	30JAN04	14JAN04	27JAN04
8	5	7	10	Facility	2	400	19JAN04	30JAN04	14JAN04	27JAN04
9	7	8	10	Init. Prod.	4	800	02FEB04	13FEB04	28JAN04	10FEB04
10	8	9	10	Evaluate	1	200	16FEB04	27FEB04	11FEB04	24FEB04
11	6	9	15	Test Market	.	.	16FEB04	05MAR04	11FEB04	02MAR04
12	9	10	5	Changes	2	400	08MAR04	12MAR04	03MAR04	09MAR04
13	10	11	0	Production	4	800	15MAR04	15MAR04	10MAR04	10MAR04
14	6	12	0	Marketing	.	.	16FEB04	16FEB04	11FEB04	11FEB04
15	8	6	0	Dummy	.	.	16FEB04	16FEB04	11FEB04	11FEB04

Obs	L_START	L_FINISH	R_DELAY	DELAY_R	SUPPL_R
1	01DEC03	05DEC03	0		
2	08DEC03	19DEC03	0		
3	21JAN04	27JAN04	5	engineer	
4	15DEC03	19DEC03	0		
5	22DEC03	13JAN04	3	engineer	
6	28JAN04	10FEB04	0		
7	14JAN04	27JAN04	0		
8	14JAN04	27JAN04	0		
9	28JAN04	10FEB04	0		
10	18FEB04	02MAR04	0		
11	11FEB04	02MAR04	0		
12	03MAR04	09MAR04	0		
13	10MAR04	10MAR04	0		
14	10MAR04	10MAR04	0		
15	11FEB04	11FEB04	0		

```

title c=black h=1.75 'Gantt Example 21';
title2 c=black h=1.25 'Displaying Resource Requirements';

* set background to white and text to black;
goptions ctext=black cback=white;

* set graphics options;
goptions vpos=50 hpos=100 htext=1.01;

* begin annotate process;

* compile annotate macros;
%annomac;

```

```

* create annotate data set for first chart;
data ann01;
  %dclanno;      /* set length and type for annotate variables */
  %system(2,2,4); /* define annotate reference system           */
  set widgsch2;
  length lab $20;
  length TEXT $ 37;
  Y1 = _n_;
  lab='      ';


  if _n_=1 then do;
    %label('01dec03'd,13,
          'Format: Engineers per day, Total cost',*,0,0,1.2,brush,6);
    end;

  if engineer ^= . then do;
    /* create a text label */
    lab = put(engineer, 1.) || " Engineer";
    if engineer > 1 then lab = trim(lab) || "s";
    if days > 0 then lab = trim(lab) || ", " ||
                                put(engcost*days, dollar7.);
    /* position the text label */
    if y1 < 10 then do;
      x1 = max(l_finish, s_finish) + 2;
      %label(x1,y1,lab,black,0,0,1.0,brush, 6);
      end;
    else do;
      x1 = e_start - 2;
      %label(x1,y1,lab,black,0,0,1.0,brush, 4);
      end;
    end;
  run;

  * annotate the Gantt chart;
  proc gantt graphics data=widgsch2 holidata=holdata annotate=ann01;
  chart / pcompress holiday=(hol) interval=weekday increment=7
        ref='1dec03'd to '21mar04'd by week
        cref=blue lref=2
        dur=days cmile=black caxis=black;
  id task;
  run;

```

### Output 8.21.2 Using the ANNOTATE= Option

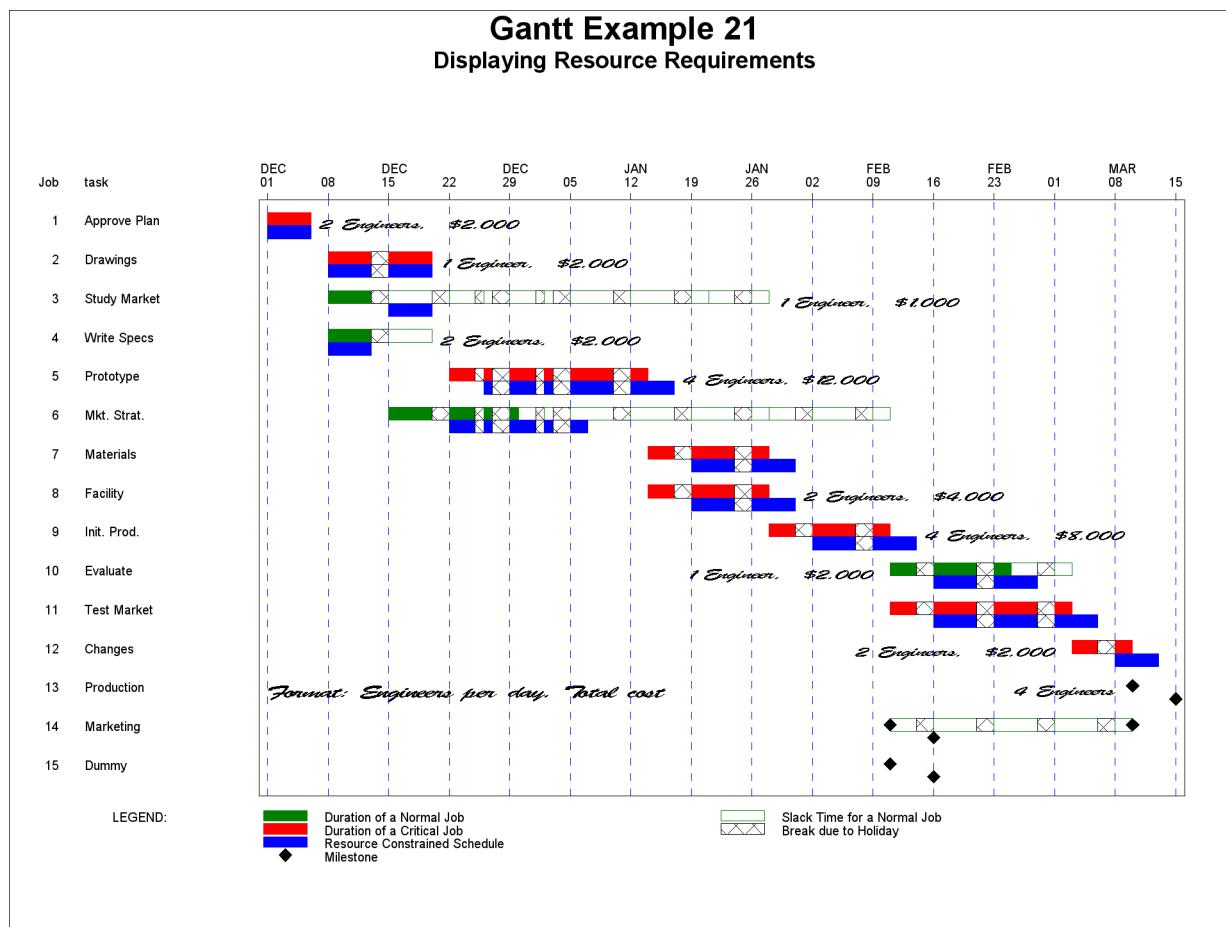

The next illustration of the ANNOTATE= option is to plot the resource usage bar chart for the replenishable resource engineers and the resource availability curve for the consumable resource cost. A DATA step determines the largest value of the cost availability throughout the life of the project in order to scale the costs accordingly. The CSCALE macro variable is required to represent cost availabilities on the Gantt chart. Since there are no further cash inflows after December 1, 2003, and there are 15 jobs represented on the chart, the value of the macro variable CSCALE is  $(15 - 1)/40000$ .

An Annotate data set, ANNO2, is created in much the same fashion as ANNO1, but it employs some additional macros. The BAR macro is used to draw the resource usage bar chart, and the DRAW and MOVE macros are used to draw the resource availability curve. The PUSH and POP macros are used as necessary to store and retrieve the last used coordinates from the stack, respectively. The resulting Gantt chart is displayed in Output 8.21.3.

```
* calculate scaling factor for cost curve;
data _null_;
  set widgrou2 end=final;
  retain maxcost;
  if aengcost > maxcost then maxcost=aengcost;
  if final then call symput('cscale',14/maxcost);
run;
```

```

* create annotate data set for second chart;
data anno2;
  %dclanno;      /* set length and type for annotate variables */
  %system(2,2,4); /* define annotate reference system           */
  set widgrou2;
  length lab $16;
  length TEXT $27;
  x1=_time_;
  y1=15-aengcost*symget('cscale');
  y2=reengineer;
  lab='      ';

  if _n_=1 then do;
    /* print labels */
    do i = 1 to 14 by 1;
      lab=put( (15-i) / symget('cscale'), dollar7.);
      %label('21mar04'd,i,lab,black,0,0,1.0,,4);
    end;
    do i = 0 to 4 by 1;
      lab=put(i,1. );
      %label('01dec03'd,15-i,lab,black,0,0,1.0,,6);
    end;
    %label('01dec03'd,10,
          'Resource Usage: Engineers',*,0,0,1.2,,6);
    %label('02jan04'd,4,
          'Resource Availability: Cost',*,0,0,1.2,,6);
    %move(x1,y1);
    %push;
  end;
  else do;
    /* draw cost availability curve */
    %pop;
    when='a';
    %draw(x1,y1,black,1,2);
    %push;
    /* draw engineer usage barchart */
    when='b';
    if y2 <= 14 then do;
      %bar(x1,15,x1+1,y2,blue,0,11);
    end;
  end;
run;


title c=black h=1.75 'Gantt Example 21';
title2 c=black h=1.25
      'Plotting Resource Usage and Resource Availability';

* annotate the Gantt chart;
proc gantt graphics data=widgsch2 holdidata=holdata annotate=anno2;
chart / pcompress holiday=(hol) interval=weekday increment=7
      mindate='1dec03'd maxdate='21mar04'd
      ref='1dec03'd to '21mar04'd by week
      cref=blue lref=2
      dur=days cmile=black caxis=black;

```

```
id task;
run;
```

### Output 8.21.3 Using the ANNOTATE= Option

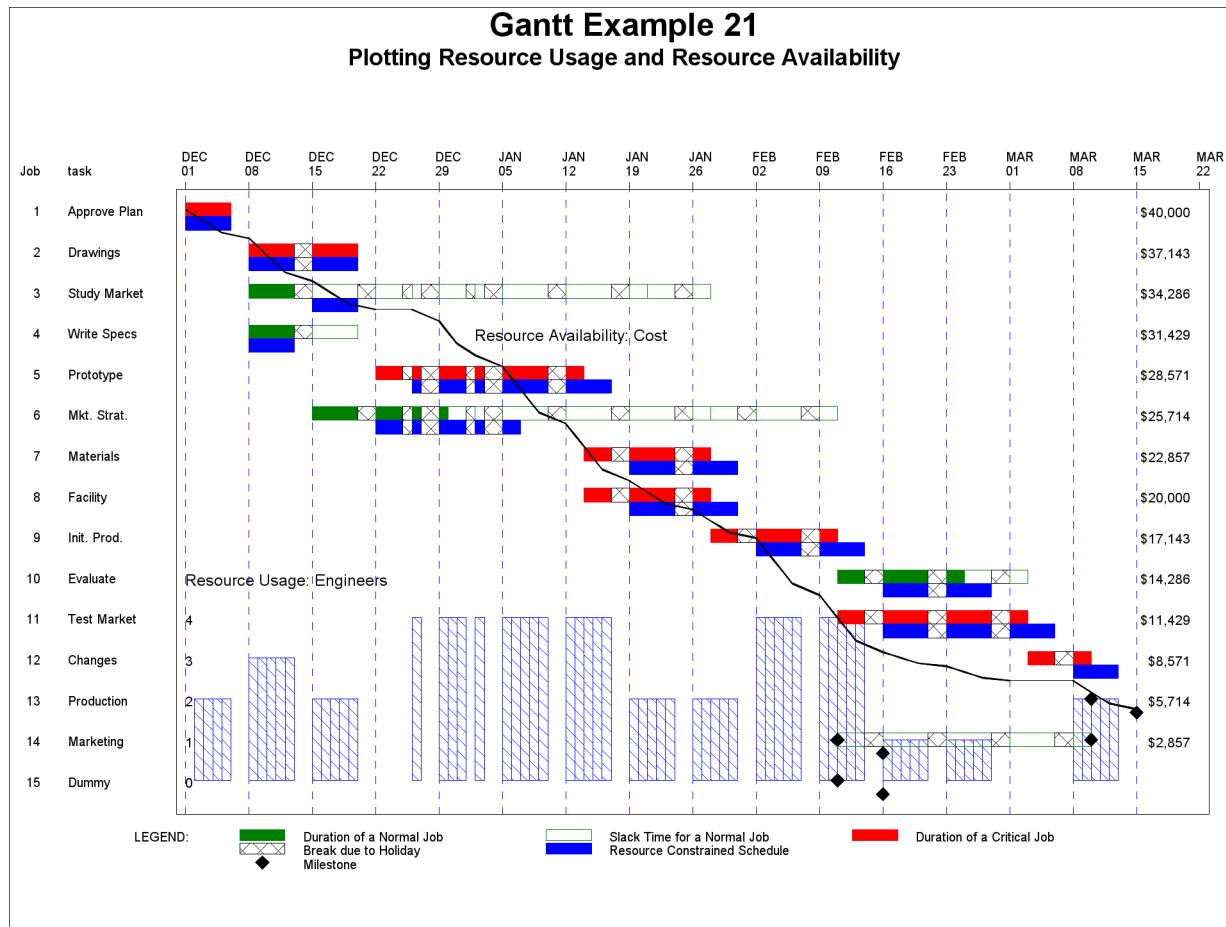

### Example 8.22: Using the Automatic Text Annotation Feature

The following example is a subplot of a larger project involving the maintenance of a pipeline and steam calender (Moder, Phillips, and Davis 1983), and it illustrates the automatic text annotation feature of the GANTT procedure. The SHUTDOWN data set is input as the activity data set to PROC CPM, and the project is scheduled to begin on June 1, 2004. PROC GANTT is used to produce a Gantt chart of the resulting schedule with the data set LABELS specified as a Label data set; the output is shown in Output 8.22.1. The LABVAR= option in the CHART statement specifies the ACT variable as the common linking variable. The LABSPLIT= option is specified in order to prevent the labels from splitting on embedded blanks.

The first observation in the LABELS data set causes the value of the ACT variable to be displayed at the E\_START time for every activity in the project. The value of \_YOFFSET='-.2' positions the baseline of the displayed text at 0.2 barheights above the top of the first bar for the activity. Similarly the second observation displays the ID variable at the E\_START time for each activity with the baseline positioned at 0.8 barheights below the bottom of the first bar for the activity. The heights for both these strings is 1 barheight. The next two observations in the LABELS data set display the symbols corresponding to the values 'N' and 'M' in the ORFONT font, rotated at an angle of 90 degrees, beside the milestones corresponding to the deactivation and

activation of the calender, respectively. Observations 5 and 6 indicate the start and finish of the “Maintenance Period” by displaying the indicated strings rotated 90 degrees at the start and finish times of the activity ‘Repair Calender.’ Finally, the last three observations provide headings for each of the three distinct regions on the chart. The \_JLABEL variable is used along with the \_XVAR variable to place the strings in the regions defined by the start and finish times of the ‘Repair Calender’ activity.

It should be noted that since the plot times are linked to variables rather than absolute values, the Label data set need not be changed even if the project is rescheduled. This is a convenient feature when monitoring a project in progress, since the annotation automatically places the labels at the appropriate times.

```

title c=black 'Gantt Example 22';

data shutdown;
  input act succ id & $20. dur;
  datalines;
1100 1110 Start Project      0
1110 1120 Procure Pipe      10
1120 1130 Prefab Pipe Sections 5
1130 1140 Deactivate Calender 0
1140 1150 Position New Pipe  1
1150 1160 Start Disassembly  0
1160 1170 Disassemble Calender 2
1170 1200 Finish Disassembly 0
1200 1300 Repair Calender   10
1300 1310 Start Assembly    0
1310 1320 Reassemble Calender 3
1320 1330 Finish Assembly   0
1330 1340 Connect Pipes     2
1340 1350 Adjust and Balance 1
1350 1360 Activate Calender  0
1360 1370 System Testing     1
1370 .   Finish Project      0
;

proc cpm data=shutdown date='01jun04'd interval=day
  out=sched;
  act act;
  succ succ;
  dur dur;
  id id;
run;

data labels;
  input act _y _xvar $ _lvar $ _yoffset _xoffset _label & $25.
    _alabel _hlabel _jlabel $ _flabel $ _clabel $;
  datalines;
. -1 e_start act -.3 0 .          0 1.5 . . .
. -1 e_start id 2.3 0 .          0 1.5 . . .
1130 . e_start . 1.5 -1 N        90 2 L orfont .
1350 . e_finish . 1.5 5 M        90 2 L orfont .
1200 17 e_start . 2.5 1 Start Maintenance Period 90 2 . .
1200 17 e_finish . 2.5 .5 Finish Maintenance Period 90 2 . .
1200 1 e_start . . -6 Shutdown   0 3 R . .
1200 1 e_start . . 2 Maintenance  0 3 L . .

```

```


1200 1 e_finish . . . 6 Start-Up 0 3 L . .
;

title2 'Automatic Text Annotation Example';

proc gantt data=sched labdata=labels graphics maxdec=0;
  chart / pcompress nolegend nojobnum dur=dur
    mininterval=day scale=5 skip=3 maxdate='14jul04'd
    labvar=act labsplit='/' ref='19jun04'd '29jun04'd
    height=1.5 lref=20;
run;

```

### Output 8.22.1 Using the LABDATA= Option

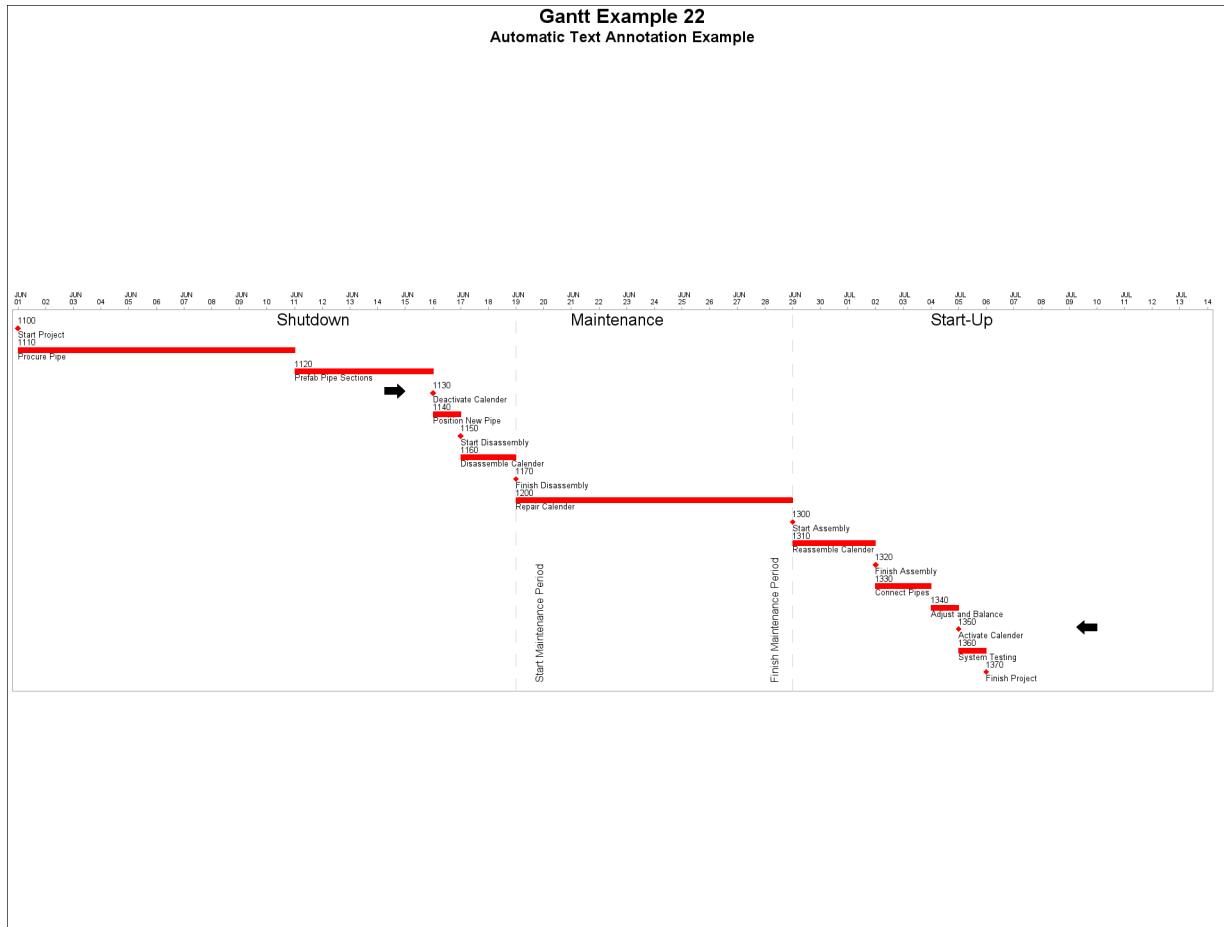


---

### Example 8.23: Multiproject Gantt Charts

The following example illustrates an application of the PATTERN variable to display summary bars for subprojects. The LAN Selection Project (Bostwick 1986) consists of eight subprojects, two of which represent the beginning and ending of the master project. The data set LANACT defines the structure of the project. The ACT and SUCC variables define the precedence relationships, the PARENT variable defines the parent task, and the DAYS variable contains the duration of the activity.

The project is scheduled using the CPM procedure with a PARENT statement to identify the parent. The schedule data set, SCHED, is created by appending a \_PATTERN variable to the output data set generated by CPM. The value of this variable is set to '4,' corresponding to subprojects, and set to missing otherwise. This results in the subproject bars being filled using PATTERN4, namely a solid black pattern. The ACTID variable is indented within the DATA step to reflect the level of each activity in the project hierarchy when used as the ID variable.

A Label data set, LABELS, is created in order to add markers to both ends of the schedule bars that correspond to subprojects. The two observations in the LABELS data set are linked to the SCHED data set with the \_PATTERN variable.

The GANTT procedure is next invoked to produce the Gantt chart in Output 8.23.1. The LAB-VAR=\_PATTERN specification establishes the link between the Schedule and Label data sets. The ACT= and SUCC= options are used to display the precedence relationships between activities.

```

pattern1 c=blue   v=r5;          /* Non-critical duration */
pattern2 c=blue   v=e;           /* Slack duration */
pattern3 c=red    v=x5;          /* Critical duration */
pattern4 c=black  v=s;           /* Project duration */

data lanact;
  format act $30. succ $30. parent $20.;
  input act & succ & parent & days;
  datalines;

Measure Current Volume      Forecast Future Volume      NEEDS ASSESSMENT 2
Literature Survey            Manufacturer Demos        MARKET SURVEY   5
Determine Current Users     Forecast Future Needs    NEEDS ASSESSMENT 2
Forecast Future Volume       Prepare Network Spec   NEEDS ASSESSMENT 2
Manufacturer Demos          Identify Vendors        MARKET SURVEY   5
Forecast Future Needs       Prepare Network Spec   NEEDS ASSESSMENT 2
Identify Vendors             .                           MARKET SURVEY   2
Prepare Network Spec        .                           NEEDS ASSESSMENT 2
Prepare RFQ                 Evaluate Vendor Responses VENDOR SELECTION 4
Prepare Cable Plan          Procure Cable           SITE PREPARATION 4
Evaluate Vendor Responses   Notify Final Candidate VENDOR SELECTION 15
Procure Cable               Install Cable            SITE PREPARATION 22
Notify Final Candidate     Negotiate Price/Config VENDOR SELECTION 1
Install Cable                .                           SITE PREPARATION 10
Negotiate Price/Config      Prepare Purchase Order VENDOR SELECTION 3
Prepare Purchase Order      .                           VENDOR SELECTION 1
Server Functional Spec     Server Detail Design   SPECIAL HARDWARE 5
Procure LAN Hardware        Receive Network Hardware NETWORK INSTALLATION 25
Server Detail Design       Server Coding           SPECIAL HARDWARE 10
Receive Network Hardware   Install LAN Hardware   NETWORK INSTALLATION 4
Server Coding               Test Server Code        SPECIAL HARDWARE 10
Install LAN Hardware        Test Network           NETWORK INSTALLATION 7
Test Server Code            Install/Integrate Server SPECIAL HARDWARE 5
Test Network                .                           NETWORK INSTALLATION 5
Install/Integrate Server   .                           SPECIAL HARDWARE 2
BEGIN PROCUREMENT           NEEDS ASSESSMENT      .
BEGIN PROCUREMENT           MARKET SURVEY         .
NEEDS ASSESSMENT            VENDOR SELECTION      .
NEEDS ASSESSMENT            SITE PREPARATION      .
MARKET SURVEY               Prepare Network Spec   .

```

```

VENDOR SELECTION           NETWORK INSTALLATION
VENDOR SELECTION           SPECIAL HARDWARE      .
SITE PREPARATION          Install LAN Hardware   .
NETWORK INSTALLATION      NETWORK AVAILABLE    .
SPECIAL HARDWARE          NETWORK AVAILABLE    .
;

proc sort data=lanact;
  by act;
  run;

proc cpm data=lanact out=lanout
  expand interval=workday date='03nov03'd;
  parent parent / wbs eso;
  activity act;
  duration days;
  successor succ;
  run;

/* create the schedule data set with a pattern variable */
data sched;
  label wbs_code='WBS';
  label actid='Project/Activity';
  set lanout;
  if proj_lev > 0 then do;
    if parent='' then _pattern=4;
    actid=act;
    do i=1 to proj_lev-1;
      actid = " " || actid;
    end;
    output;
  end;
  end;
;

proc sort data=sched;
  by es_asc wbs_code;
  run;

/* create the label data set */
data labels;
  _pattern=4;
  _flabel='orfont';
  _jlabel='c';
  _yoffset=0.925;
  _label='Z';
  _xvar='e_start ';
  output;
  _xvar='l_finish';
  output;
;
;

title1 f='Cumberland AMT' h=1.75 'Gantt Example 23';
title2 f='Cumberland AMT' h=1.25 'Displaying Summary Bars For Each Subproject';


```

```

proc gantt graphics data=sched labdata=labels;
  id actid wbs_code;
  chart / pcompress nojobnum ctext=black caxis=black
    mindate='01nov03'd maxdate='29feb04'd increment=7
    labvar=_pattern font='Cumberland AMT' height=1.5
    minoffgv=1.5 minofflv=1.5 cprec=black wprec=1
    scale=1.5 act=act succ=succ;
run;

```

#### Output 8.23.1 Using the PATTERN Variable and Labels

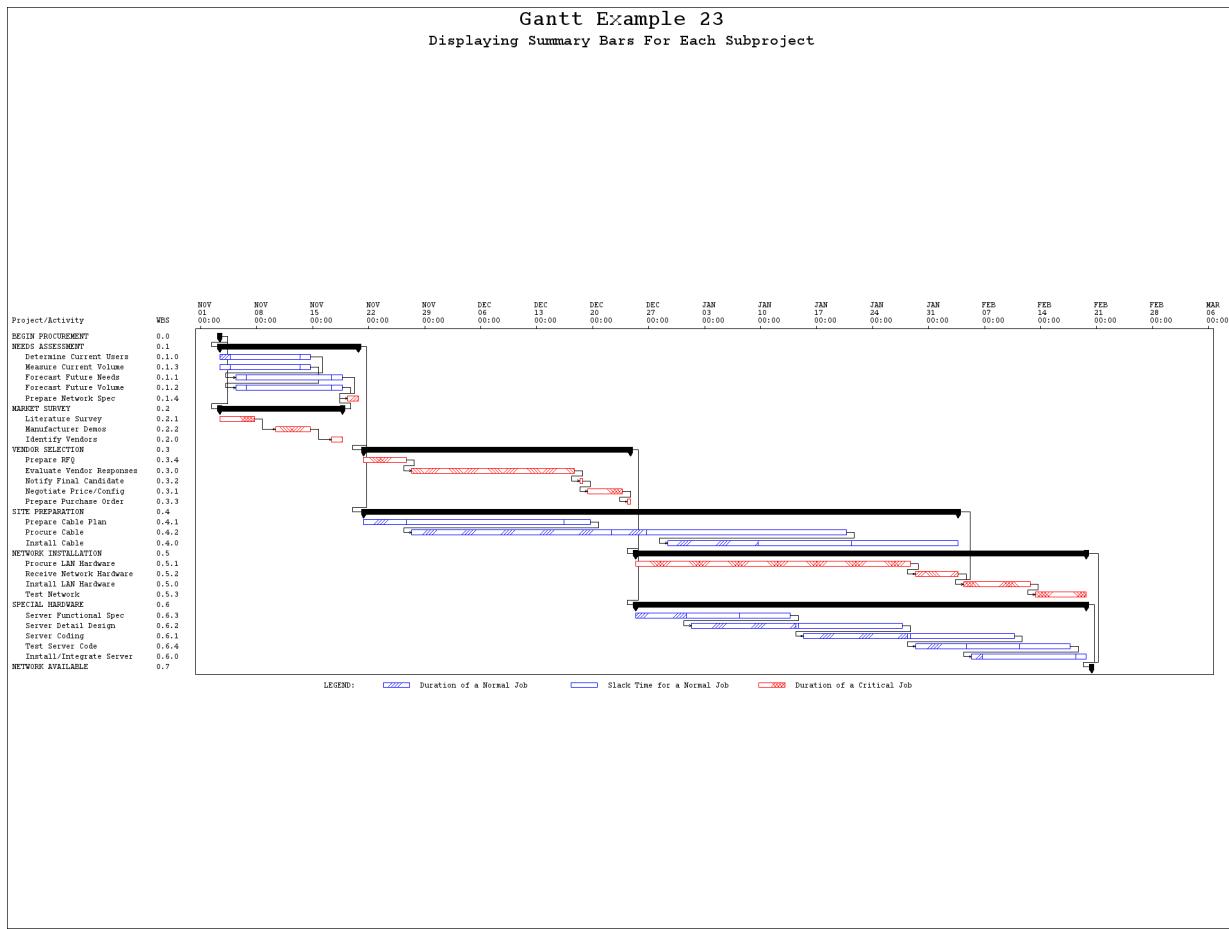

## Example 8.24: Multisegment Gantt Charts

The following is a simple example that illustrates the generation of multisegmented Gantt charts. The SCHED data set identifies the city, the arrival time, and the departure time for each of four traveling salespeople. In addition, a \_PATTERN variable is used to identify the pattern to be used for drawing the bar. The objective is to display the complete schedule for each sales person on a single row. This would require displaying several bars on a single row, each bar corresponding to the time spent in a city. In order to do this, you need first to sort the SCHED data set by Salesperson and Arrival Time and then to add a SEGMT\_NO variable that identifies the number of the segment that, in this case, is the order in which the salesperson visits the city. The resulting data set, NEWSCHED, is shown in Output 8.24.1. You next create the LABELS data set in order to identify the names of the cities above the bars; the resulting Gantt chart is shown in Output 8.24.2.

Notice that each bar is drawn using the pattern identified by the \_PATTERN variable in the SCHED data set. In the absence of the \_PATTERN variable, the pattern associated with the resource-constrained schedule would have been used for all the bars. This is the same mechanism that produced the split segments in Example 8.13 although the SEGMT\_NO variable in this case was automatically created by the CPM procedure.

```

data sched;
  format city $12. from to date7. ;
  input person $ city & from & date7. to & date7. _pattern;
  datalines;
Clark  New York      01May04  03May04  10
Clark  Boston        06May04  09May04  11
Clark  Wisconsin     12May04  15May04  12
Clark  Chicago       18May04  24May04  13
Clark  New York      28May04  02Jun04  10
Stevens Charlotte   02May04  04May04  14
Stevens Atlanta     08May04  10May04  15
Stevens Dallas      12May04  15May04  16
Stevens Denver       17May04  20May04  17
Stevens Nashville    27May04  02Jun04  18
Stevens Charlotte   04Jun04  06Jun04  14
Jackson Los Angeles  01May04  08May04  19
Jackson Las Vegas   11May04  18May04  20
Jackson Portland     21May04  23May04  21
Jackson Seattle      25May04  29May04  22
Rogers Miami         02May04  07May04  23
Rogers Tampa          11May04  15May04  24
Rogers New Orleans   18May04  24May04  25
Rogers Houston        28May04  01Jun04  26
;

/* Sort data by person, from */
proc sort data=sched;
  by person from;
  run;

/* Add Segmt_no variable */
data newsched;
  set sched;
  retain segmt_no;
  if person ne lag(person) then segmt_no=1;
  else segmt_no = segmt_no + 1;
  output;
  run;

proc print data=newsched;
  title2 'Data NEWSCHED';
  run;

data labels;
  _y=-1;
  _lvar="city";
  _xvar="from";
  _flabel="";
  _hlabel=0.75;

```

```

_yoffset = -.2;
run;

* set up required pattern statements;
pattern1 v=s r=25;


* set graphics options;
proc gantt graphics data=newsched labdata=labels;
id person;
chart / ss=from sf=to compress labsplit='.' scale=2
      nolegend nojobnum skip=3
      ref='01may04'd to '30jun04'd by week;
run;

```

### Output 8.24.1 NEWSCHED Data Set

#### Data NEWSCHED

Obs	city	from	to	person	_pattern	segmt_no
1	New York	01MAY04	03MAY04	Clark	10	1
2	Boston	06MAY04	09MAY04	Clark	11	2
3	Wisconsin	12MAY04	15MAY04	Clark	12	3
4	Chicago	18MAY04	24MAY04	Clark	13	4
5	New York	28MAY04	02JUN04	Clark	10	5
6	Los Angeles	01MAY04	08MAY04	Jackson	19	1
7	Las Vegas	11MAY04	18MAY04	Jackson	20	2
8	Portland	21MAY04	23MAY04	Jackson	21	3
9	Seattle	25MAY04	29MAY04	Jackson	22	4
10	Miami	02MAY04	07MAY04	Rogers	23	1
11	Tampa	11MAY04	15MAY04	Rogers	24	2
12	New Orleans	18MAY04	24MAY04	Rogers	25	3
13	Houston	28MAY04	01JUN04	Rogers	26	4
14	Charlotte	02MAY04	04MAY04	Stevens	14	1
15	Atlanta	08MAY04	10MAY04	Stevens	15	2
16	Dallas	12MAY04	15MAY04	Stevens	16	3
17	Denver	17MAY04	20MAY04	Stevens	17	4
18	Nashville	27MAY04	02JUN04	Stevens	18	5
19	Charlotte	04JUN04	06JUN04	Stevens	14	6

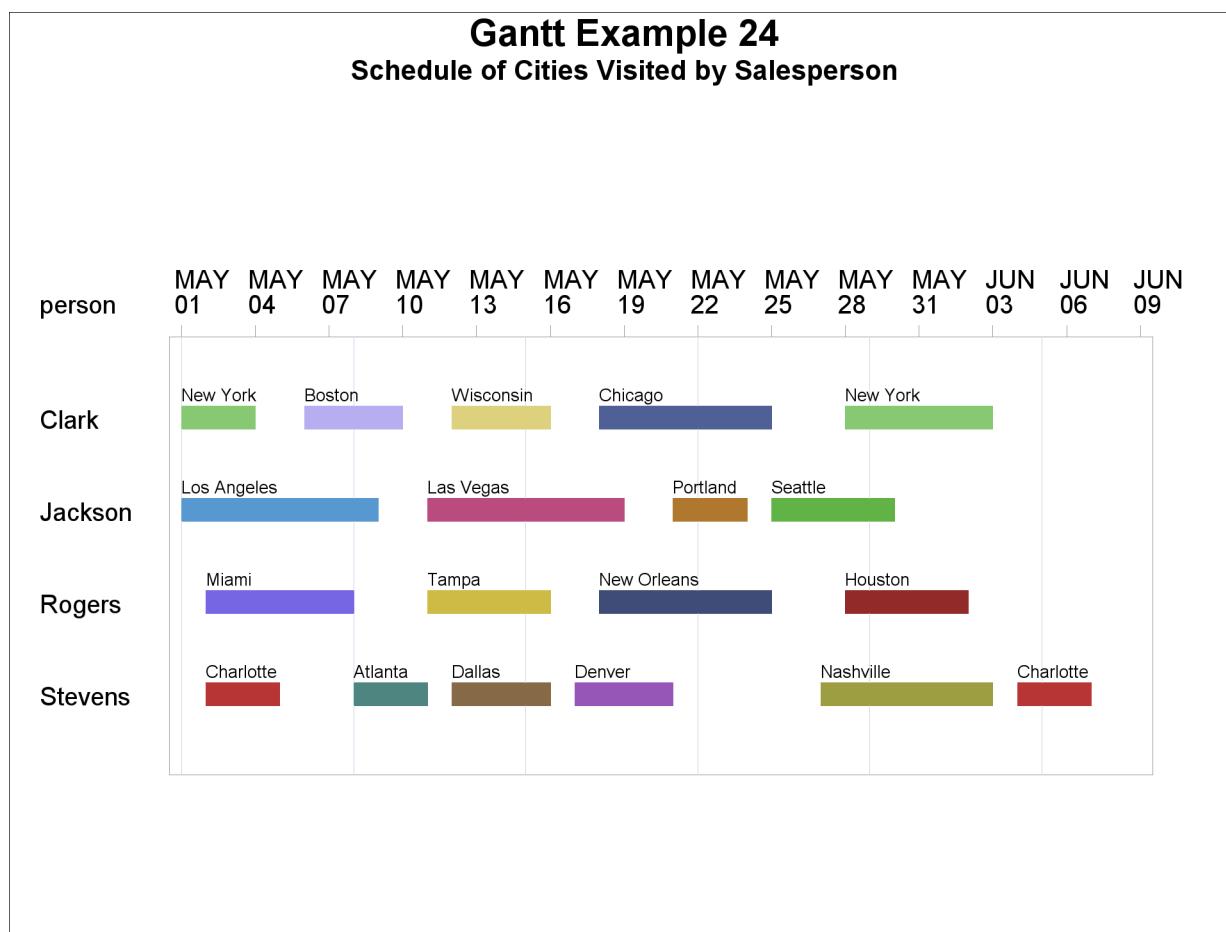**Output 8.24.2** Multisegment Gantt Chart

---

## Example 8.25: Zoned Gantt Charts

Example 8.15 illustrated the use of BY processing with the GANTT procedure to present separate Gantt charts for each department. Alternatively, you can use a zoned Gantt chart to display each of the departmental schedules on the same chart with the different department schedules separated by horizontal zone lines running across the chart. The ZONE variable divides the Activity axis into distinct zones. Activities with the same value of the ZONE variable belong to the same zone. This example produces a zoned Gantt chart using the schedule data from [Example 8.15](#). The ZONE=DEPT specification in the CHART statement identifies the DEPT variable as the ZONE variable. The ONEZONEVAL option specifies that the value of the ZONE variable be displayed only when beginning new zones. The resulting Gantt chart is shown in [Output 8.25.1](#). You can customize the color, style and width of the zone line by using the CZONE=, LZONE=, and WZONE= options, respectively. You can also control the span and offset of the zone line by specifying the ZONESPAN= and ZONEOFF= options, respectively, in the CHART statement.


```

proc cpm date='01dec03'd data=widgetn;
  activity task;
  duration days;
  successor succ1 succ2 succ3;
  id dept;
  run;

proc sort;
  by dept e_start;
  run;

proc gantt split('/');
  chart / pcompress scale=1 dur=days
    mindate='01dec03'd maxdate='11feb04'd
    zone=dept onezoneval czone=gray;
  id task;
  run;

```

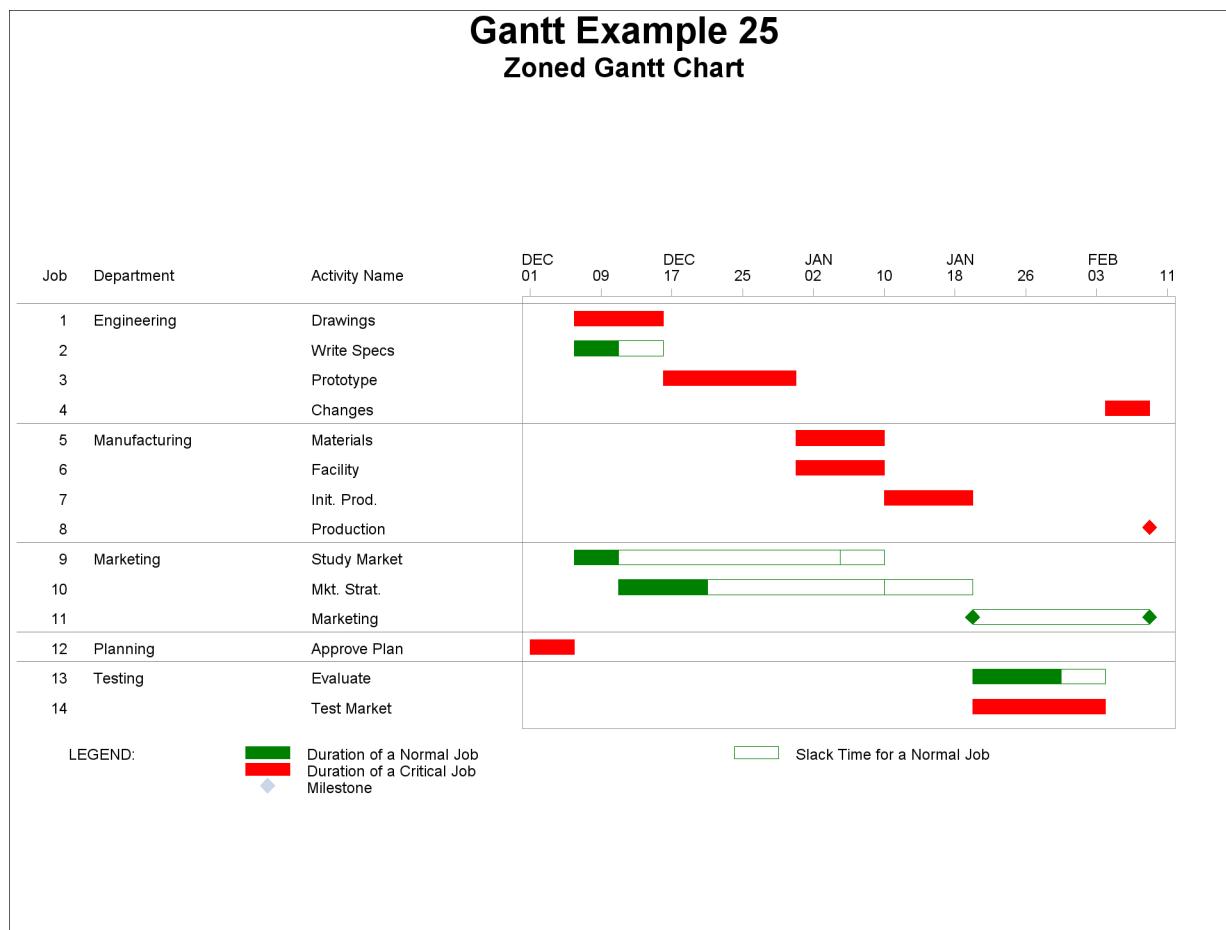**Output 8.25.1** Gantt Charts Zoned by Department**Example 8.26: Web-Enabled Gantt Charts**

This example illustrates the process of “Web-enabling” your Gantt charts. This feature enables you to associate a URL with each activity on a Gantt chart. By using this feature together with SAS/IntrNet software, you can develop some very powerful Project Management applications. SAS/IntrNet software provides you with the capability to perform data set queries and execute SAS applications in real time and view the results in HTML format using a Web browser.

This example takes advantage of the Output Delivery System (ODS) HTML statement to create a very simple “drill-down” Gantt application beginning from a summary Gantt chart of the “top level” projects in [Example 8.23](#). The objective is to display a detailed Gantt chart of the activities in a subproject when you click on the subproject bar.

In order to be able to click on an activity and invoke an action, you need to add variables to the schedule data set that associate a URL with each of the activities that you want linked. The following code adds the WEBVAR and WEBVAR2 variables to the LANOUT data set in [Example 8.23](#) to create the LANWEB data set. The WEBVAR variable uses the ALT= portion to identify information about an activity’s schedule that is to be displayed when the mouse hovers over the schedule bar. In addition, it uses the HREF= portion to associate the URL with the linked activity. The WEBVAR2 variable uses only the ALT= portion, so information in the detailed Gantt chart can still be displayed by hovering over the schedule bars.

The LANWEB data set is then sorted by the WBS\_CODE variable.

```

data lanweb;
  set lanout;
  length webvar $500;
  length webvar2 $500;

  /* WEBVAR is for the top-level summary chart */
  webvar='alt='|| quote(
    'Activity: '||trim(left(act))||'0D'x||
    '-----'||'0D'x||
    'Early Start: '||put(e_start, datetime.)||'0D'x||
    'Early Finish:'||put(e_finish, datetime.)||'0D'x||
    'Late Start:  '||put(l_start, datetime.)||'0D'x||
    'Late Finish: '||put(l_finish, datetime.) )||
    ' HREF=#'||trim(wbs_code) /* link to the anchors */
  ;
  
  /* WEBVAR2 is for the detailed charts */
  webvar2='alt='|| quote(
    'Activity: '||trim(left(act))||'0D'x||
    '-----'||'0D'x||
    'Early Start: '||put(e_start, datetime.)||'0D'x||
    'Early Finish:'||put(e_finish, datetime.)||'0D'x||
    'Late Start:  '||put(l_start, datetime.)||'0D'x||
    'Late Finish: '||put(l_finish, datetime.) )
  ;
run;

proc sort data=lanweb;
  by wbs_code;
run;

```

Before creating the charts, you need to specify that the GIF driver be used to create graphics output. ODS HTML output always creates a “body” file, which is a single HTML document containing the output from one or more procedures and is specified using the FILE= option in the ODS HTML statement.

```

goptions reset=all device=gif;

ods html file="Gantt_Sum.html";

```

For example, when you click on any of the schedule bars for an activity with WBS\_CODE='0.2', you link to an anchor labeled '0.2' in the body file Gantt\_Sum.html.

You are now ready to create the summary Gantt chart. You identify the WEBVAR variable to the GANTT procedure using the HTML= option in the CHART statement and invoke the procedure using a WHERE clause to produce a Gantt chart of the top-level activities.

```

/* Create the Summary Gantt Chart with Drill Down Action */
pattern1 c=green v=s;          /* Non-critical duration */
pattern2 c=green v=e;          /* Slack duration */
pattern3 c=red   v=s;          /* Critical duration */
goptions cback=white htext=1.1;

title1 h=2 'Gantt Example 26';

```

```

title2 h=1.5 'Project Summary Gantt Chart';

proc gantt data=lanweb;
  id act wbs_code;
  where proj_lev=1;
  label act='SUBPROJECT' wbs_code='WBS CODE';
  chart / pcompress nojobnum
    duration=days
    mininterval=week scale=2.5
    mindate='30oct03'd maxdate='29feb04'd
    ref='30oct03:00:00'dt to '01mar04:00:00'dt by dtmonth
    reflabel
    html=webvar
    act=act succ=succ cprec=black;
run;

```

The graph that is displayed when you click on one of the subprojects is determined by the name of the anchor that has been defined for the subproject. Before creating these graphs, you need to define the anchor name in an ODS HTML statement using the ANCHOR= option to add the anchor to the HTML body file. Since you have to create a chart for each subproject, you can automate this process by using a SAS macro.

```

/* Define the macro to generate the detail charts */
%macro gandet(wbs);

goptions device=gif;
ods html anchor=&wbs;

title1 h=2 'Gantt Example 26';
title2 h=1.5 "Detail Gantt Chart for WBS=&wbs;

proc gantt data=lanweb;
  id act wbs_code;
  where index(wbs_code,&wbs)=1;
  label act='SUBPROJECT' wbs_code='WBS CODE';
  chart / pcompress nojobnum
    duration=days
    mininterval=week scale=2.5
    mindate='30oct03'd maxdate='29feb04'd
    ref='30oct03:00:00'dt to '01mar04:00:00'dt by dtmonth
    reflabel html=webvar2
    act=act succ=succ cprec=black;
run;
%mend;

/* Generate each of the detail Gantt Charts */
%gandet('0.1');
%gandet('0.2');
%gandet('0.3');
%gandet('0.4');
%gandet('0.5');
%gandet('0.6');


```

Finally, use the ODS HTML CLOSE statement to close the body file and stop generating HTML output.


```
ods html close;
```

After you have closed the body file, you can display it in a browser window, as shown in Output 8.26.1, to view the output generated by this example.

### Output 8.26.1 Summary Gantt Chart

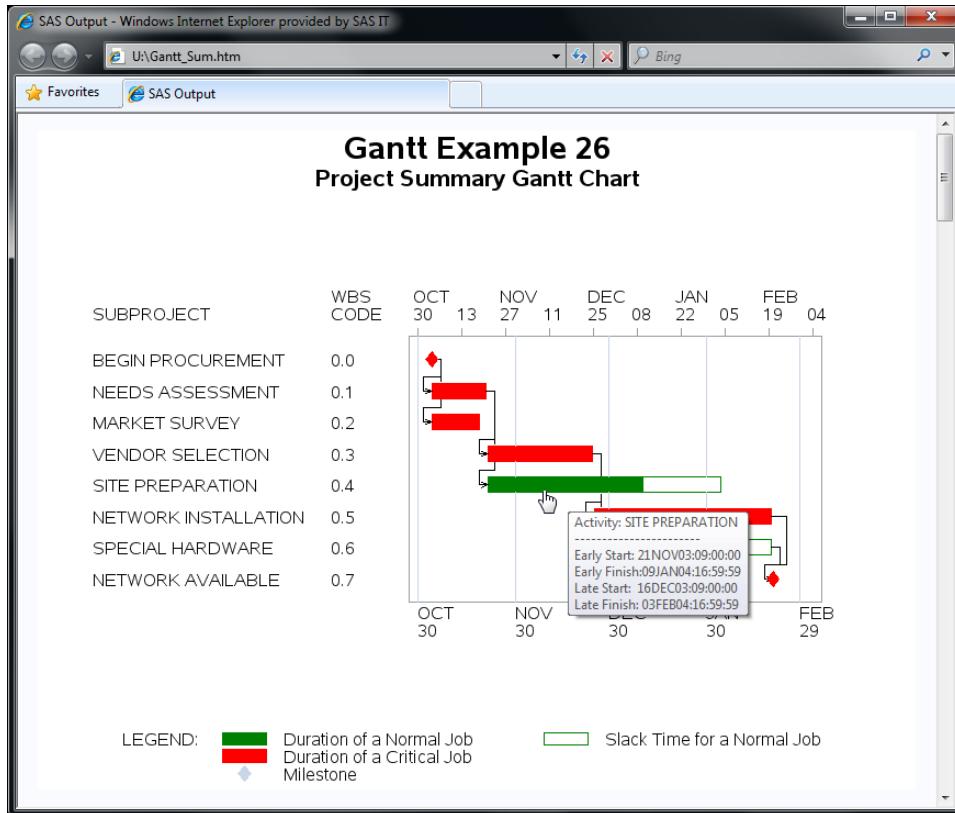


Notice the hand-shaped cursor on the SITE PREPARATION bar, which indicates that this bar is a “hot” link. The alternate text box displays the early and late schedules of the SITE PREPARATION activity. The status bar of the browser also shows that clicking the SITE PREPARATION bar will take you to the location identified by “Gantt\_Sum.html#W0.4,” which is shown in Output 8.26.2.

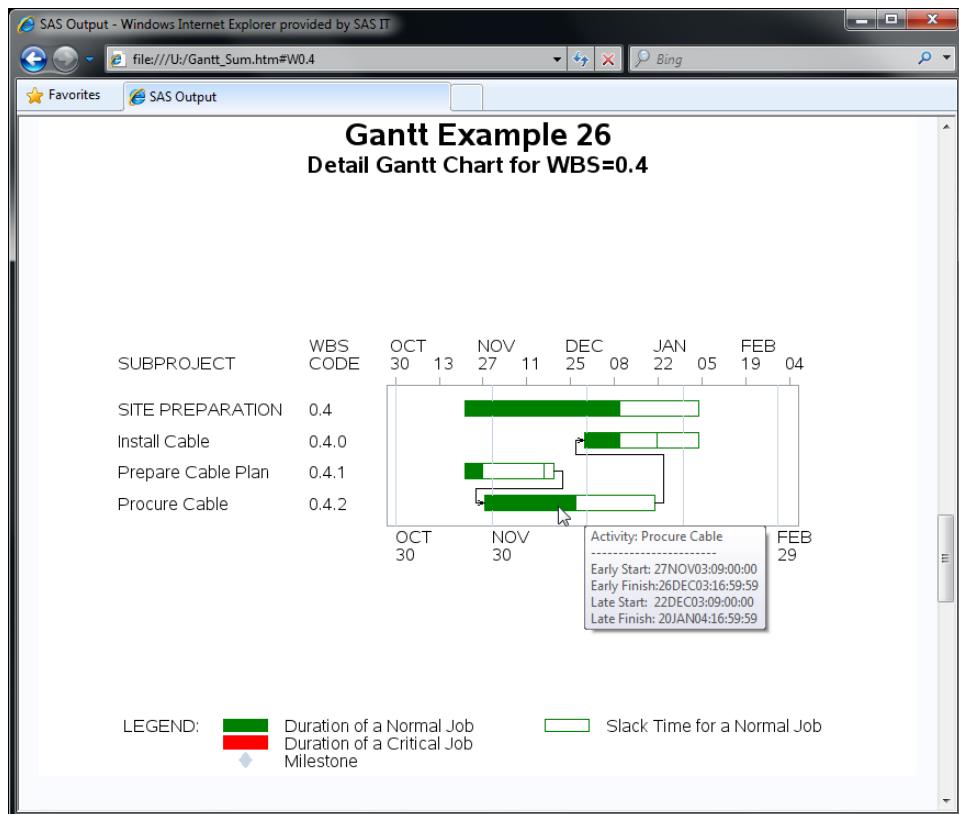**Output 8.26.2** Detail Gantt Chart for SITE PREPARATION

Similarly, the detail Gantt chart that is displayed when you click on the SPECIAL HARDWARE summary bar is shown in Output 8.26.3.

#### Output 8.26.3 Detail Gantt Chart for SPECIAL HARDWARE

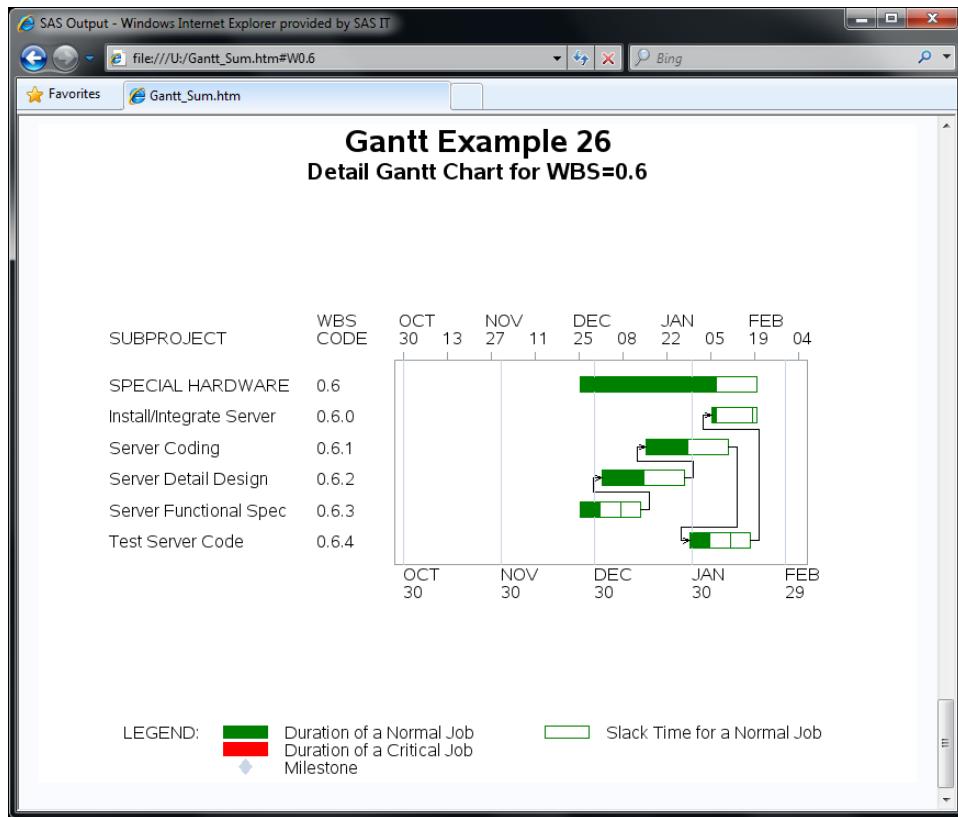


---

#### Example 8.27: Using the CHARTWIDTH= Option

This example illustrates the use of the CHARTWIDTH= option to create Gantt charts that are consistent in appearance. The data set used in this example is the SAVE data set created in Example 8.6.


Gantt charts are first produced using different values of the MINDATE= option, and without specifying the CHARTWIDTH= option. Output 8.27.1 shows a Gantt chart using MINDATE='1jan04', and Output 8.27.2 shows a Gantt chart using MINDATE='15aug03'. Notice that the chart in Output 8.27.2 has a much larger chart area than the chart in Output 8.27.1, and the 'Activity Description' column is compressed and rather difficult to read.


```
proc gantt data=save;
  chart / mindate='1jan04'd maxdate='1feb04'd
        dur=days nojobnum compress height=2.0
        ref='2jan04'd to '2feb04'd by week
        reflabel;
  id descript;
run;
```

```

proc gantt data=save;
  chart / mindate='15aug03'd maxdate='1feb04'd
        dur=days nojobnum compress height=2.0
        ref='16aug03'd to '2feb04'd by week
        reflabel;
  id descript;
run;

```

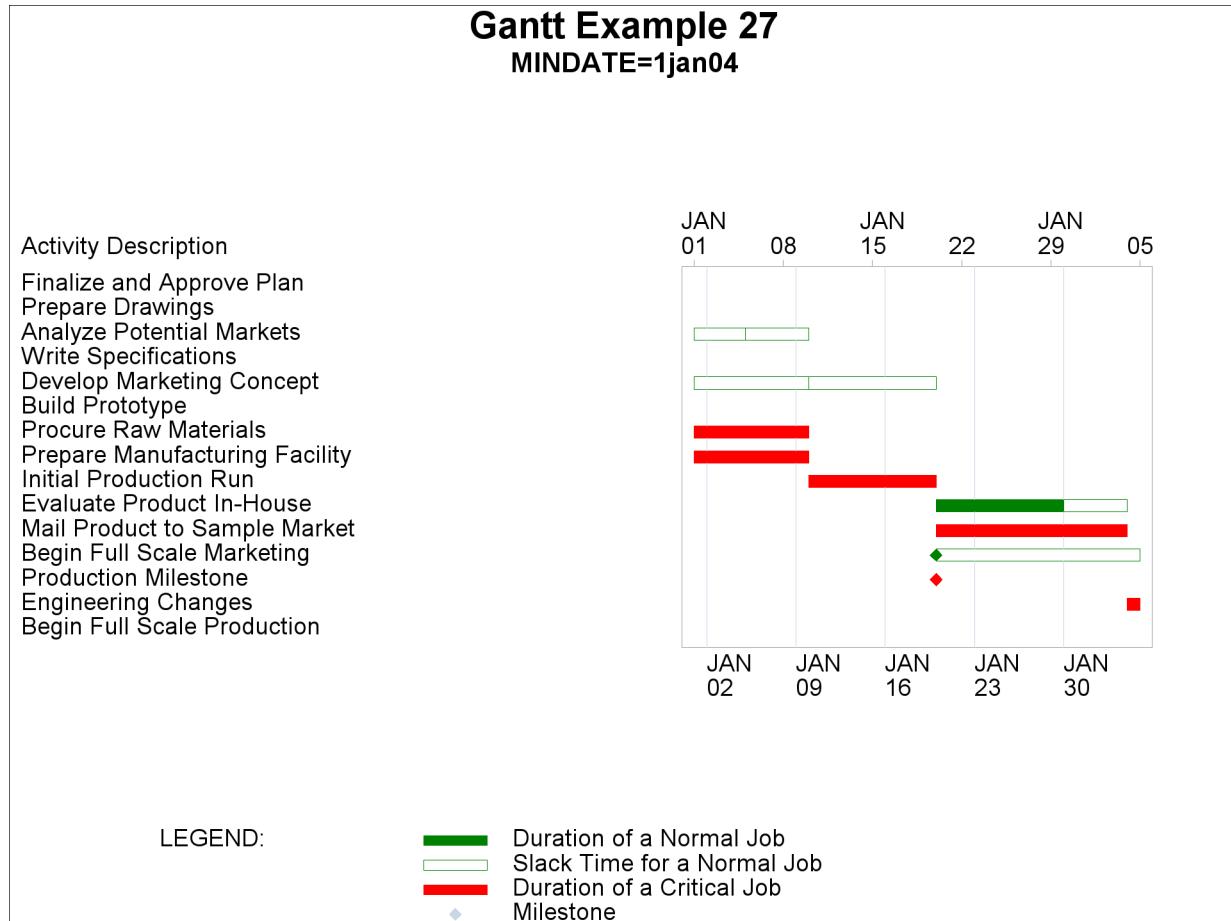**Output 8.27.1** Without the CHARTWIDTH= Option (MINDATE=1Jan04)

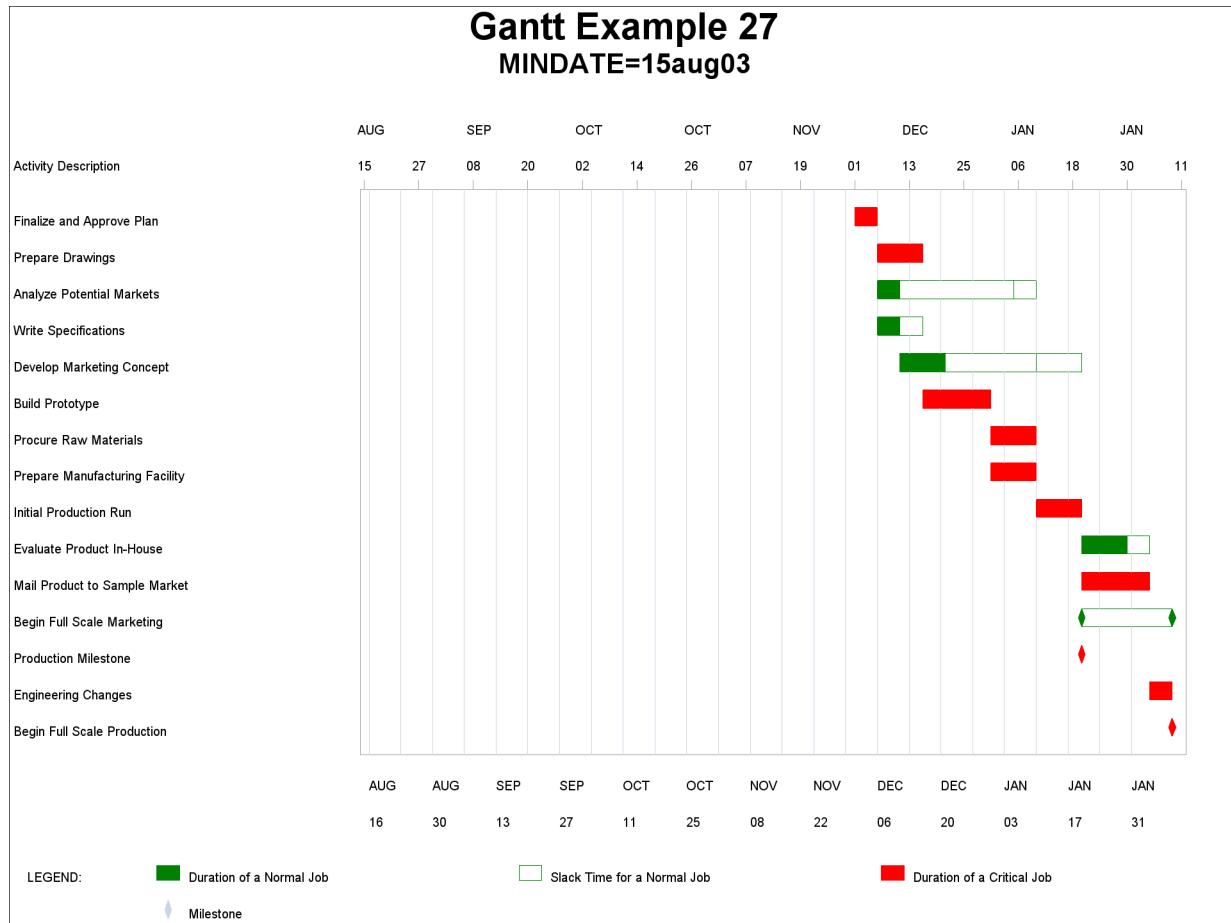**Output 8.27.2** Without the CHARTWIDTH= Option (MINDATE=15Aug03)


The same charts are now plotted with the CHARTWIDTH= option. The specification CHARTWIDTH=75 indicates that the chart is rescaled so the axis area is 75% of the chart width and the text area is 25% of the chart width. Therefore, specifying CHARTWIDTH=75 for both charts gives the two charts a consistent appearance. The output is shown in [Output 8.27.3](#) and [Output 8.27.4](#).


```

proc gantt data=save;
  chart / mindate='1jan04'd maxdate='1feb04'd
        dur=days nojobnum compress height=2.0
        ref='2jan04'd to '2feb04'd by week
        reflabel chartwidth=75;
  id descript;
  run;

proc gantt data=save;
  chart / mindate='15aug03'd maxdate='1feb04'd
        dur=days nojobnum compress height=2.0
        ref='16aug03'd to '2feb04'd by week
        reflabel chartwidth=75;
  id descript;
  run;

```

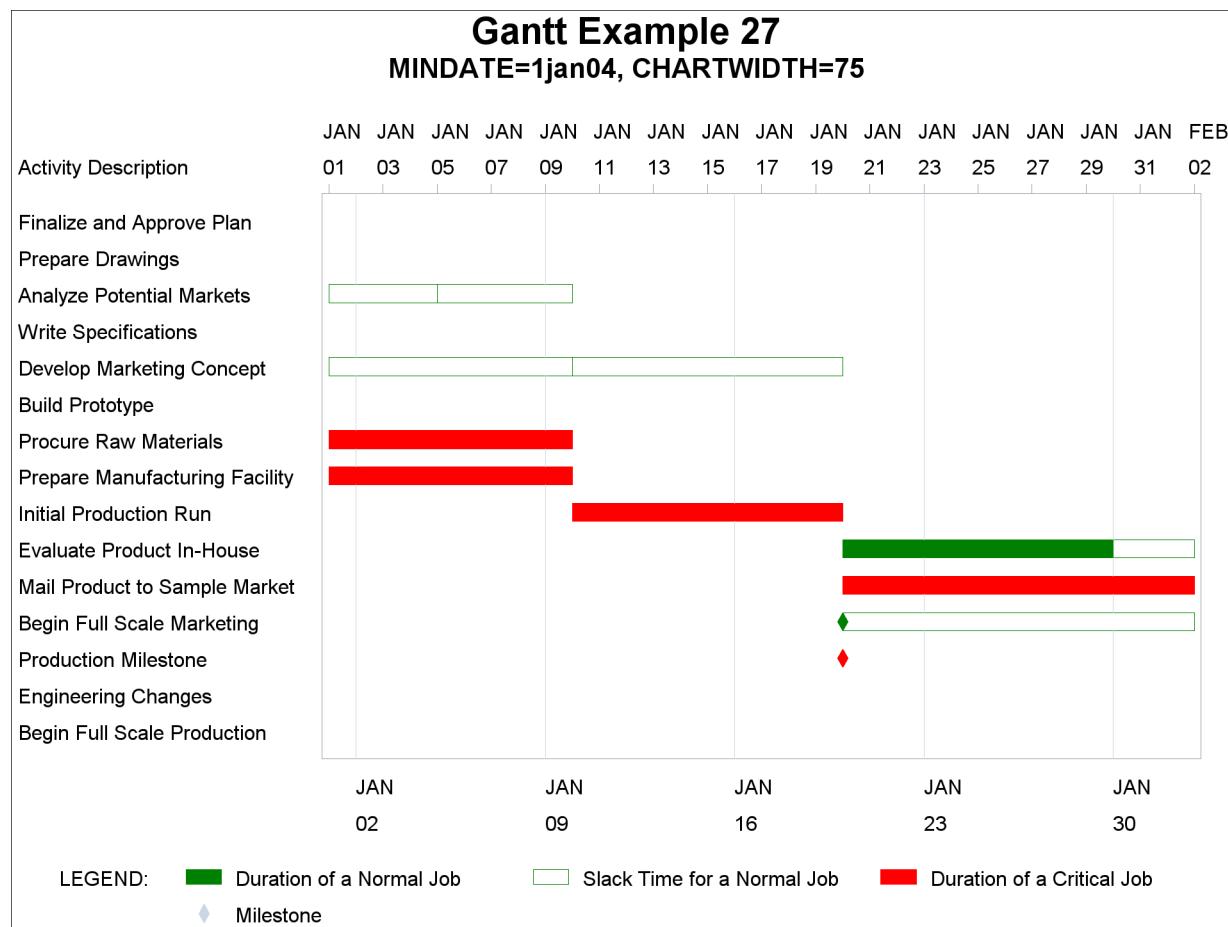**Output 8.27.3** Using the CHARTWIDTH= Option (MINDATE=1Jan04)

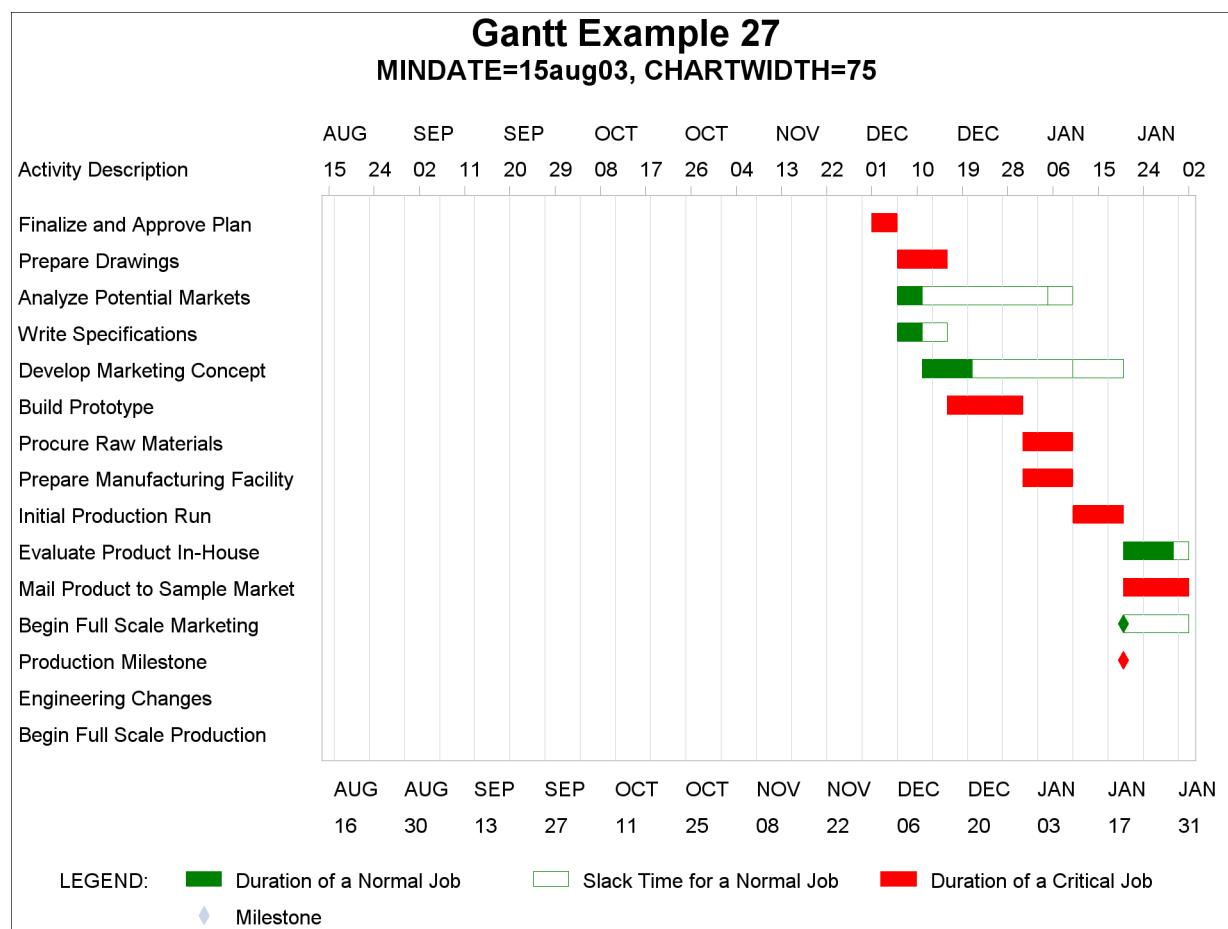**Output 8.27.4** Using the CHARTWIDTH= Option (MINDATE=15Aug03)

---

## Example 8.28: Using the TIMEAXISFORMAT= Option

The following statements illustrate the use of the TIMEAXISFORMAT= option to specify formats for up to three rows of time-axis labels. The Activity data set for PROC CPM is the WIDGETA data set from Example 4.2, which defines the widget manufacturing project in AOA format.

```
* schedule the project subject to holidays and weekends;
proc cpm data=widgeta out=savehp
    date='11mar09'd;
    successor tail;
    activity head;
    duration days;
    id task dept descrpt;
run;

* sort the schedule by the early start date ;
proc sort;
    by e_start;
run;

* define a date format that includes the day of the week;
proc format;
    picture dowdate (default=16) low-high = '%a, %d %b %Y'
        (datatype=date fill='0');
run;


* set up pattern statements;
pattern1 c=green v=s;      /* duration of a non-critical activity */
pattern2 c=green v=e;      /* slack time for a noncrit. activity */
pattern3 c=red v=s;       /* duration of a critical activity */
pattern4 c=magenta v=e;   /* slack time for a supercrit. activity */
pattern5 c=magenta v=s;   /* duration of a supercrit. activity */
pattern6 c=cyan v=s;      /* actual duration of an activity */
pattern7 c=black v=e;     /* break due to a holiday */
pattern8 c=blue v=s;      /* resource schedule of activity */
pattern9 c=brown v=s;     /* baseline schedule of activity */

* set graphics options;

* plot the logic Gantt chart using AOA representation;
proc gantt data=savehp (obs=6);
    chart / compress
        activity=head
        successor=tail
        mininterval=day
        increment=1
        dur=days
        maxdate='24MAR09'd
        taformat=(date7., dowdate., downame2.)
        cprec=black
        ;
    id task;
run;
```

The resulting Gantt chart, displayed in Output 8.28.1, contains one time-axis row for each format specified.

#### Output 8.28.1 Using the TIMEAXISFORMAT= Option

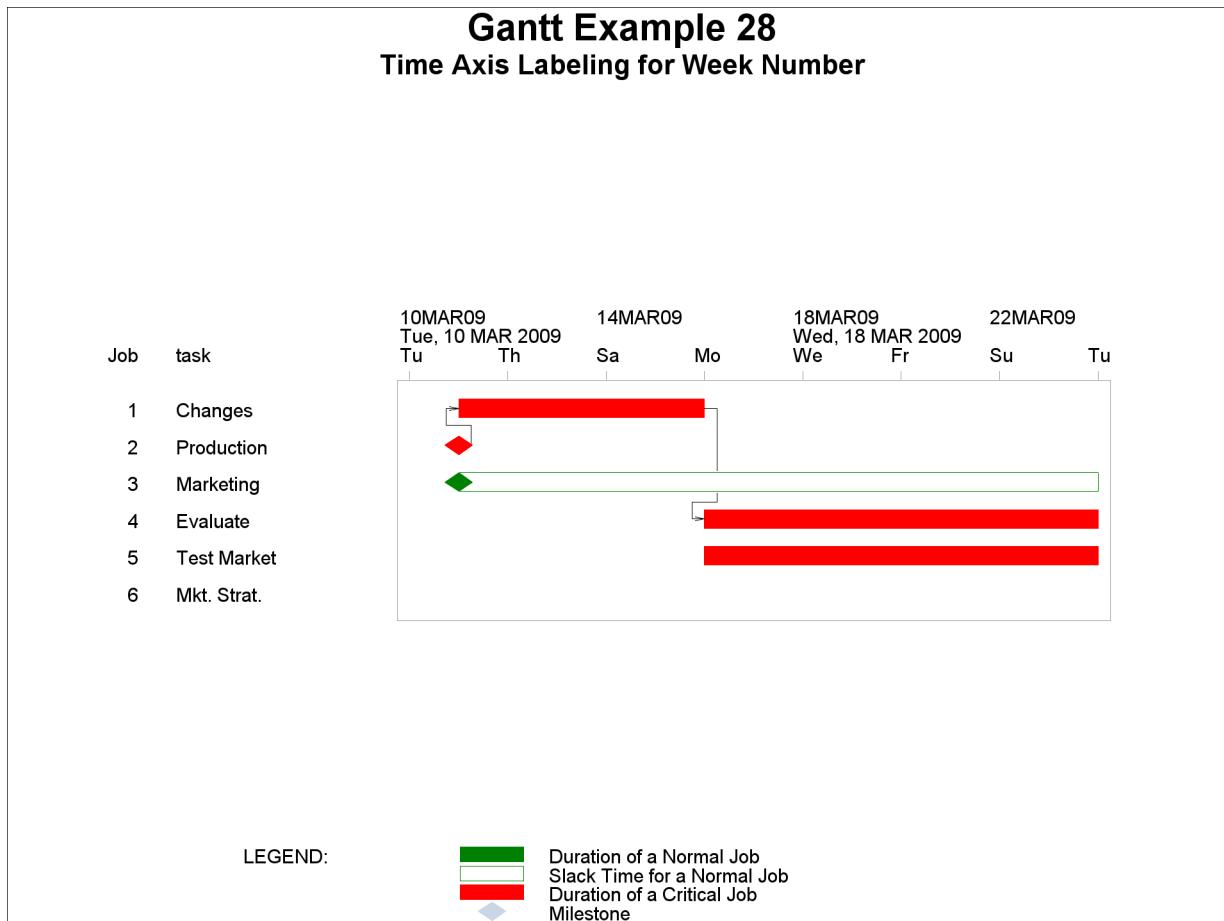

## Statement and Option Cross-Reference Tables

The next two tables show which examples in this section use each of the statements and options in the GANTT procedure.

**Table 8.15** Options Specified in Examples 4.1–4.14

Option	1	2	3	4	5	6	7	8	9	10	11	12	13	14
A_FINISH=									X					
A_START=									X					
BETWEEN=		X												
CALID=														
CALENDAR=									X					
CAXIS=				X	X	X	X			X				
CHART var			X	X										
CHCON=										X				
CMILE=			X	X	X					X				
COMBINE												X		
COMPRESS				X			X			X		X		
CREF=														
CRITFLAG	X			X	X					X				
CTEXT=										X				
CTNOW=											X			
DATA=		X				X	X	X	X	X	X	X	X	X
DUR=			X	X	X	X	X	X	X	X	X	X	X	X
FILL	X													
FONT=								X		X				
HCONNECT										X				
HEIGHT=									X	X	X	X	X	X
HOLIDATA=		X							X	X	X	X	X	X
HOLIDAY=		X							X	X	X	X	X	X
HOLIDUR=									X					
HOLIFIN=			X	X	X	X	X	X	X	X	X	X	X	X
ID	X	X							X	X	X	X	X	X
INTERVAL=									X					
LINEPRINTER	X	X												
L_FINISH=													X	
LREF=							X							
L_START=													X	
MARKBREAK								X	X	X				
MAXDATE=								X	X	X				
MINDATE=								X	X	X				
MININTERVAL=	X							X	X					
NOJOBNUM	X							X						
NOLEGEND	X													
PCOMPRESS								X	X					
REF=	X							X	X			X	X	

**Table 8.15** (continued)

**Table 8.16** Options Specified in Examples 4.15–4.28

Option	15	16	17	18	19	20	21	22	23	24	25	26	27	28
A_FINISH=				X										
A_START=				X										
ACTIVITY=					X				X			X		
ANNOTATE=						X								
BY	X	X												X
CAXIS=			X	X	X	X	X		X				X	
CHARTWIDTH=				X	X	X	X	X		X				X
CMILE=				X	X	X	X	X						X
COMPRESS				X	X	X	X			X			X	X
CPREC=					X	X	X					X		X
CREF=						X	X							
CTEXT=									X					
CZONE=										X				
DATA=		X	X	X	X	X	X	X	X	X		X	X	X
DUR=	X	X	X	X	X	X	X	X	X	X	X	X	X	X
FONT=						X				X				
HEAD=							X							
HEIGHT=	X		X		X	X		X	X					X
HOLIDATA=			X	X	X	X								
HOLIDAY=			X	X	X	X	X							
HOLIFIN=				X			X							
HTML=													X	
HTOFF=			X											
ID	X	X	X	X	X	X	X			X	X	X	X	X
INCREMENT=					X	X				X	X			X
INTERVAL=							X							
LABDATA=								X		X				
LABSPLIT=									X	X				
LABVAR=									X	X				
LAG=						X								
LEVEL=				X				X						
LREF=								X						

**Table 8.16** (continued)

<b>Option</b>	<b>15</b>	<b>16</b>	<b>17</b>	<b>18</b>	<b>19</b>	<b>20</b>	<b>21</b>	<b>22</b>	<b>23</b>	<b>24</b>	<b>25</b>	<b>26</b>	<b>27</b>	<b>28</b>
MAXDATE=	X				X		X	X	X		X	X	X	X
MAXDEC=								X						
MAXDISLV=					X									
MINDATE=	X					X		X			X	X	X	
MININTERVAL=							X	X						X
MININTGV=					X	X								
MINOFFGV=					X	X			X	X				
MINOFFLV=					X	X			X	X				
NOJOBNUM							X	X	X	X		X	X	
NOLEGEND							X	X	X	X				
ONEZONEVAL											X			
PCOMPRESS	X	X					X	X	X		X	X	X	
PRECDATA=						X								
REF=					X	X	X			X		X	X	X
REFLABEL					X	X								
SCALE=	X						X	X	X	X	X	X	X	
S_FINISH=								X	X	X				
SKIP=		X						X	X	X				
SPLIT=										X				
S_START=				X		X			X	X		X		X
SUCCESSOR=									X					
TAIL=					X									
TAFORMAT=						X								
WPREC=										X				
ZONE=											X			

## References

- Bostwick, S. (1986). "Software Helps Solve LAN Selection Puzzle." *Mini-Micro Systems* (February 14): 20–22.
- Kuhfeld, W. F. (2010). *Statistical Graphics in SAS: An Introduction to the Graph Template Language and the Statistical Graphics Procedures*. Cary, NC: SAS Institute Inc.
- Moder, J. J., Phillips, C. R., and Davis, E. W. (1983). *Project Management with CPM, PERT, and Precedence Diagramming*. New York: Van Nostrand Reinhold.

# Chapter 9

## The NETDRAW Procedure

### Contents

---

Overview: NETDRAW Procedure . . . . .	662
Getting Started: NETDRAW Procedure . . . . .	664
Syntax: NETDRAW Procedure . . . . .	668
Functional Summary . . . . .	668
PROC NETDRAW Statement . . . . .	672
ACTNET Statement . . . . .	673
Details: NETDRAW Procedure . . . . .	685
Network Input Data Set . . . . .	685
Variables in the Network Data Set . . . . .	687
Missing Values . . . . .	688
Layout of the Network . . . . .	688
Format of the Display . . . . .	690
Page Format . . . . .	691
Layout Data Set . . . . .	692
Controlling the Layout . . . . .	693
Time-Scaled Network Diagrams . . . . .	694
Zoned Network Diagrams . . . . .	696
Organizational Charts or Tree Diagrams . . . . .	696
Full-Screen Version . . . . .	697
Graphics Version . . . . .	700
Using the Annotate Facility . . . . .	701
Web-Enabled Network Diagrams . . . . .	702
Macro Variable _ORNETDR . . . . .	702
Computer Resource Requirements . . . . .	703
ODS Style Templates . . . . .	703
Examples: NETDRAW Procedure . . . . .	708
Example 9.1: Line-Printer Network Diagram . . . . .	708
Example 9.2: Graphics Version of PROC NETDRAW . . . . .	713
Example 9.3: Spanning Multiple Pages . . . . .	714
Example 9.4: The COMPRESS and PCOMPRESS Options . . . . .	718
Example 9.5: Controlling the Display Format . . . . .	721
Example 9.6: Nonstandard Precedence Relationships . . . . .	726
Example 9.7: Controlling the Arc-Routing Algorithm . . . . .	728
Example 9.8: PATTERN and SHOWSTATUS Options . . . . .	731
Example 9.9: Time-Scaled Network Diagram . . . . .	734
Example 9.10: Further Time-Scale Options . . . . .	738

Example 9.11: Zoned Network Diagram . . . . .	741
Example 9.12: Schematic Diagrams . . . . .	742
Example 9.13: Modifying Network Layout . . . . .	748
Example 9.14: Specifying Node Positions . . . . .	753
Example 9.15: Organizational Charts with PROC NETDRAW . . . . .	755
Example 9.16: Annotate Facility with PROC NETDRAW . . . . .	758
Example 9.17: AOA Network Using the Annotate Facility . . . . .	761
Example 9.18: Branch and Bound Trees . . . . .	765
Statement and Option Cross-Reference Tables . . . . .	770
<b>References . . . . .</b>	<b>772</b>

---

## Overview: NETDRAW Procedure

The NETDRAW procedure draws a network diagram of the activities in a project. Boxes (or nodes) are used to represent the activities, and lines (or arcs) are used to show the precedence relationships among the activities. Though the description of the procedure is written using project management terminology, PROC NETDRAW can be used to draw any network such as an organizational chart or a software flow diagram. The only information required by the procedure for drawing such a diagram is the name of each activity in the project (or node in the network) and a list of all its immediate successor activities (or nodes connected to it by arcs). Note that project networks are acyclic. However, the procedure can also be used to draw cyclic networks by specifying explicitly the coordinates for the nodes or by requesting the procedure to break the cycles in an arbitrary fashion.

The **ACTNET** statement in the NETDRAW procedure is designed to draw activity networks that represent a project in Activity-On-Node (AON) format. All network information is contained in SAS data sets. The input data sets used by PROC NETDRAW and the output data set produced by the procedure are as follows:

- The **Network** input data set contains the precedence information, namely, the activity-successor information for all the nodes in the network. This data set can be an **Activity** data set that is used as input to the CPM procedure or a **Schedule** data set that is produced by the CPM procedure, or it can even be a **Layout** data set produced by the NETDRAW procedure. The minimum amount of information that is required by PROC NETDRAW is the activity-successor information that can be obtained from any one of the preceding three possible types of data sets. The additional information in the input data set can be used by the procedure to add detail to the nodes in the diagram, and, in the case of the Layout data set, the procedure can use the **\_X\_** and **\_Y\_** variables to lay out the nodes and arcs of the diagram.
- The **Annotate** input data set contains the graphics and text that are to be annotated on the network diagram. This data set is used by the procedure through the Annotate facility in SAS/GRAF software.
- The **Layout** output data set produced by PROC NETDRAW contains all the information about the layout of the network. For each node in the network, the procedure saves the  $(x, y)$  coordinates; for each arc between each pair of nodes, the procedure saves the  $(x, y)$  coordinates of each turning point of the arc in a separate observation. Using these values, the procedure can draw the network diagram without recomputing node placement and arc routing.

Two issues arise in drawing and displaying a network diagram: the layout of the diagram and the format of the display. The layout of the diagram consists of placing the nodes of the network and routing the arcs of the network in an appropriate manner. The format of the display includes the size of the nodes, the distance between nodes, the color of the nodes and arcs, and the information that is placed within each node. Several options available in the ACTNET statement enable you to control the format of the display and the layout of the diagram; these options and their uses are explained in detail later in this chapter.

Following is a list of some of the key aspects of the procedure:

- The Network input data set specifies the activities (or nodes) in the network and their immediate successors. The amount of information displayed within each node can be controlled by the ID= option and by the use of default variables in the data set.
- The procedure uses the node-successor information to determine the placement of the nodes and the layout of the arcs connecting the nodes.
- By default, PROC NETDRAW uses the topological ordering of the activity network to determine the *x* coordinates of the nodes. In a time-based network diagram, the nodes can be ordered according to any numeric, SAS date, time, or datetime variable (the **ALIGN=** variable) in the input data set.
- The network does not have to represent a project. You can use PROC NETDRAW to draw any network. If the network has no cycles, then the procedure bases the node placement and arc routing on the precedence relationships. Alternately, you can specify explicitly the node positions or use the **ALIGN=** variable, and let the procedure determine the arc routing.
- To draw networks with cycles, use the **BREAKCYCLE** option. Alternately, you can use the **ALIGN=** option or specify the node positions so that the procedure needs only to determine the arc routing. See [Example 9.12](#) for an illustration of a cyclic network.
- The **ZONE=** option enables you to divide the network into horizontal bands or zones. This is useful in grouping the activities of the project according to some appropriate classification.
- The **TREE** option instructs PROC NETDRAW to check if the network is indeed a tree, and, if so, to exploit the tree structure in the node layout. This feature is useful for drawing organizational charts, hierarchical charts, and work break-down structures.
- PROC NETDRAW gives you the option of displaying the network diagram in one of three modes: graphics, line-printer, or full-screen. The default mode is graphics mode, which enables you to produce charts of high resolution quality. Graphics mode requires SAS/GRAF software. See the section “[Graphics Options](#)” on page 679 for more information about producing high-resolution quality network diagrams. You can also produce line-printer quality network diagrams by specifying the **LINEPRINTER (LP)** option in the PROC NETDRAW statement. In addition to sending the output to either a plotter or printer, you can view the network diagram at the terminal in full-screen mode by specifying the **FULLSCREEN (FS)** option in the PROC NETDRAW statement. See the section “[Full-Screen Options](#)” on page 678 for more information about viewing network diagrams in full-screen mode.
- The full-screen version of the procedure enables you to move the nodes around on the screen (subject to maintaining the precedence order of the activities) and thus change the layout of the network diagram.
- The graphics version of the procedure enables you to annotate the network diagram using the **Annotate** facility in SAS/GRAF software.

- The positions of the nodes and arcs of the layout determined by PROC NETDRAW are saved in an output data set called the [Layout](#) data set. This data set can be used again as input to PROC NETDRAW; using such a data set saves some processing time because the procedure does not need to determine the node and arc placement.
- If necessary, the procedure draws the network across page boundaries. The number of pages that are used depends on the number of print positions that are available in the horizontal and vertical directions.
- In graphics mode, the [COMPRESS](#) and [PCOMPRESS](#) options enable you to produce the network on one page. You can also control the number of pages used to create the network diagram with the [HPAGES=](#) and [VPAGES=](#) options.
- In graphics mode, the [ROTATE](#) and [ROTATETEXT](#) options enable you to produce a top-down tree diagram.

## Getting Started: NETDRAW Procedure

The first step in defining a project is to make a list of the activities in the project and determine the precedence constraints that need to be satisfied by these activities. It is useful at this stage to view a graphical representation of the project network. In order to draw the network, you specify the nodes of the network and the precedence relationships among them. Consider the software development project that is described in the “Getting Started” section of Chapter 4, “[The CPM Procedure](#).“ The network data are in the SAS data set SOFTWARE, displayed in [Figure 9.1](#).

**Figure 9.1** Software Project

**Software Project  
Data Set SOFTWARE**

Obs	descript	duration	activity	succesr1	succesr2
1	Initial Testing	20	TESTING	RECODE	
2	Prel. Documentation	15	PRELDOC	DOCEDREV QATEST	
3	Meet Marketing	1	MEETMKT	RECODE	
4	Recoding	5	RECODE	DOCEDREV QATEST	
5	QA Test Approve	10	QATEST	PROD	
6	Doc. Edit and Revise	10	DOCEDREV	PROD	
7	Production	1	PROD		

The following code produces the network diagram shown in Figure 9.2:


```

pattern1 v=e c=green;
pattern2 v=e c=red;

title h=3 'Software Project';
proc netdraw graphics data=software;
  actnet / act=activity htext=2
    succ=(succesr1 succesr2)
    pcompress separatearcs;
run;

```

**Figure 9.2 Software Project**

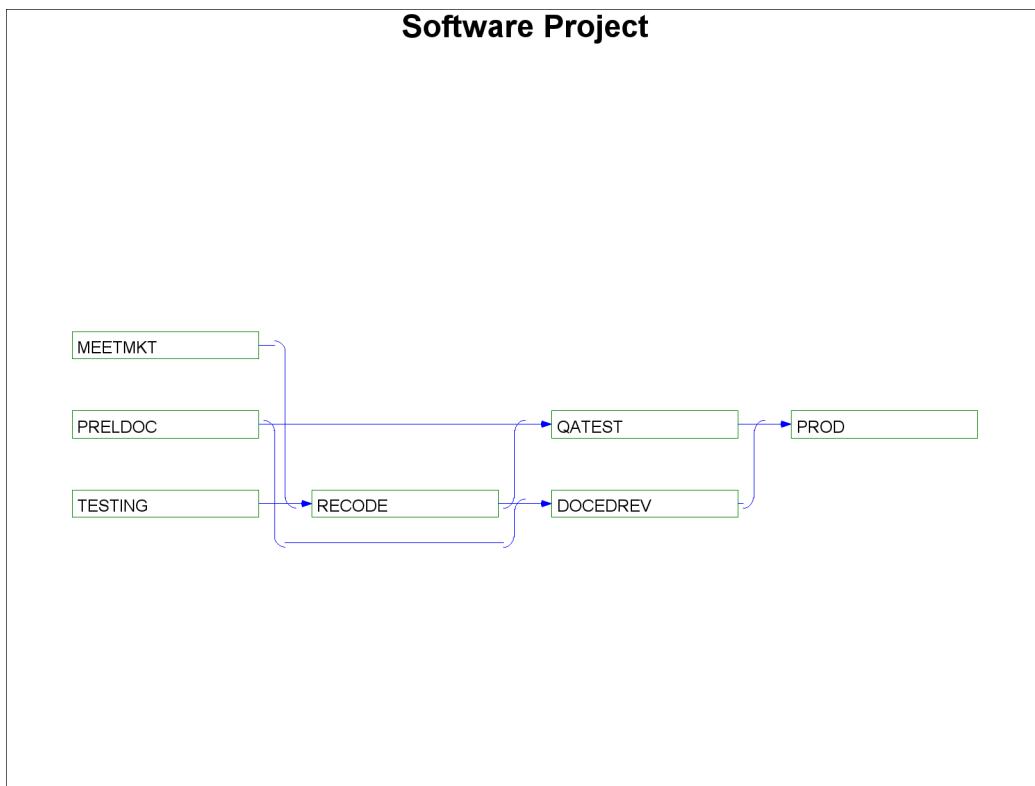

The procedure determines the placement of the nodes and the routing of the arcs on the basis of the topological ordering of the nodes and attempts to produce a compact diagram. You can control the placement of the nodes by specifying explicitly the node positions. The data set SOFTNET, shown in Figure 9.3, includes the variables `_X_` and `_Y_`, which specify the desired node coordinates. Note that the precedence information is conveyed using a single `SUCCESSOR` variable unlike the data set SOFTWARE, which contains two `SUCCESSOR` variables.


**Figure 9.3** Software Project: Specify Node Positions

**Software Project  
Data Set SOFTNET**

<b>Obs</b>	<b>descript</b>	<b>duration</b>	<b>activity</b>	<b>succesor</b>	<b>_x_</b>	<b>_y_</b>
1	Initial Testing	20	TESTING	RECODE	1	1
2	Meet Marketing	1	MEETMKT	RECODE	1	2
3	Prel. Documentation	15	PRELDOC	DOCEDREV	1	3
4	Prel. Documentation	15	PRELDOC	QATEST	1	3
5	Recoding	5	RECODE	DOCEDREV	2	2
6	Recoding	5	RECODE	QATEST	2	2
7	QA Test Approve	10	QATEST	PROD	3	3
8	Doc. Edit and Revise	10	DOCEDREV	PROD	3	1
9	Production	1	PROD		4	2

The following code produces a network diagram (shown in [Figure 9.4](#)) with the new node placement:

```
title h=3 'Software Project';
title2 h=2 'Controlled Layout';
proc netdraw graphics data=softnet;
  actnet / act=activity htext=1.25
    succ=(succesor)
    pcompress;
run;
```

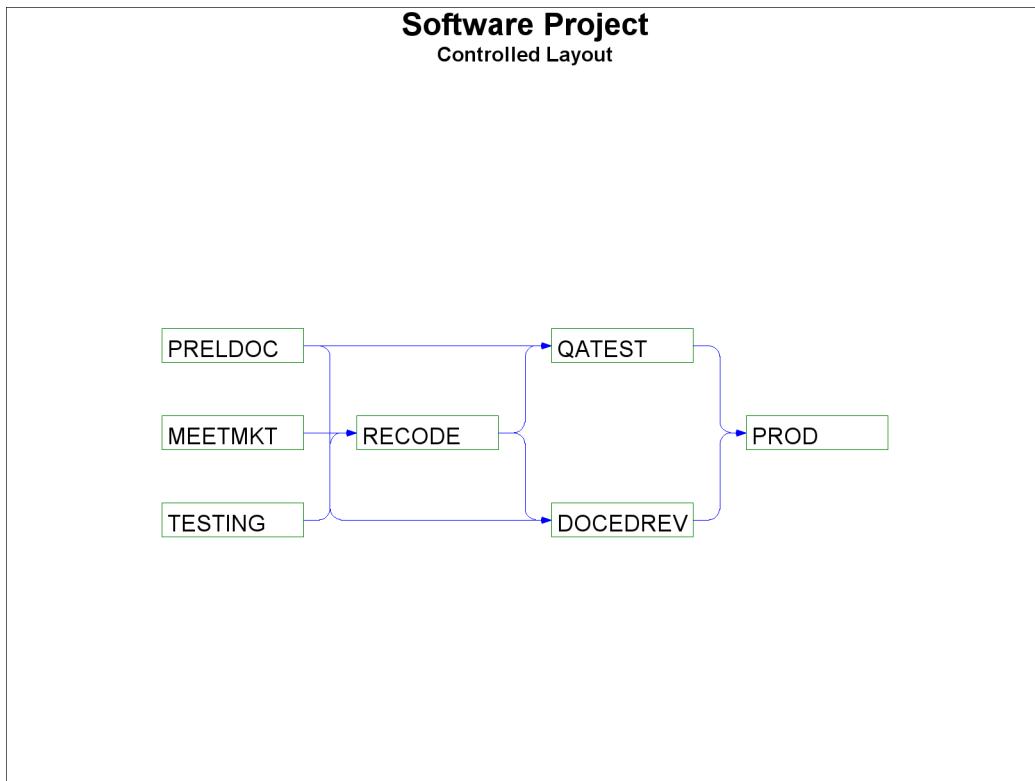**Figure 9.4** Software Project: Controlled Layout

**Figure 9.5** Software Project Schedule

<b>Software Project Project Schedule</b>					
<b>descrip</b>	<b>activity</b>	<b>succesr1</b>	<b>succesr2</b>	<b>duration</b>	<b>E_START</b>
<b>Initial Testing</b>	TESTING	RECODE		20	01MAR04
<b>Prel. Documentation</b>	PRELDOC	DOCEDREV QATEST		15	01MAR04
<b>Meet Marketing</b>	MEETMKT	RECODE		1	01MAR04
<b>Recoding</b>	RECODE	DOCEDREV QATEST		5	21MAR04
<b>QA Test Approve</b>	QATEST	PROD		10	26MAR04
<b>Doc. Edit and Revise</b>	DOCEDREV	PROD		10	26MAR04
<b>Production</b>	PROD			1	05APR04

<b>descrip</b>	<b>E_FINISH</b>	<b>L_START</b>	<b>L_FINISH</b>	<b>T_FLOAT</b>	<b>F_FLOAT</b>
<b>Initial Testing</b>	20MAR04	01MAR04	20MAR04	0	0
<b>Prel. Documentation</b>	15MAR04	11MAR04	25MAR04	10	10
<b>Meet Marketing</b>	01MAR04	20MAR04	20MAR04	19	19
<b>Recoding</b>	25MAR04	21MAR04	25MAR04	0	0
<b>QA Test Approve</b>	04APR04	26MAR04	04APR04	0	0
<b>Doc. Edit and Revise</b>	04APR04	26MAR04	04APR04	0	0
<b>Production</b>	05APR04	05APR04	05APR04	0	0


While the project is in progress, you may want to use the network diagram to show the current status of each activity as well as any other relevant information about each activity. PROC NETDRAW can also be used to produce a time-scaled network diagram using the schedule produced by PROC CPM. The schedule data for the software project described earlier are saved in a data set, INTRO1, which is shown in [Figure 9.5](#).

To produce a time-scaled network diagram, use the TIMESCALE option in the ACTNET statement, as shown in the following program. The MININTERVAL= and the LINEAR options are used to control the time axis on the diagram. The ID=, NOLABEL, and NODEFID options control the amount of information displayed within each node. The resulting diagram is shown in [Figure 9.6](#).

```

title h=3 'Software Project';
title2 h=2 'Time-Scaled Diagram';
proc netdraw graphics data=intro1;
  actnet / act=activity succ=(succ:)
    separatearcs pcompress htext=2
    timescale linear frame mininterval=week
    id=(activity duration) nolabel nodefid;
run;

```

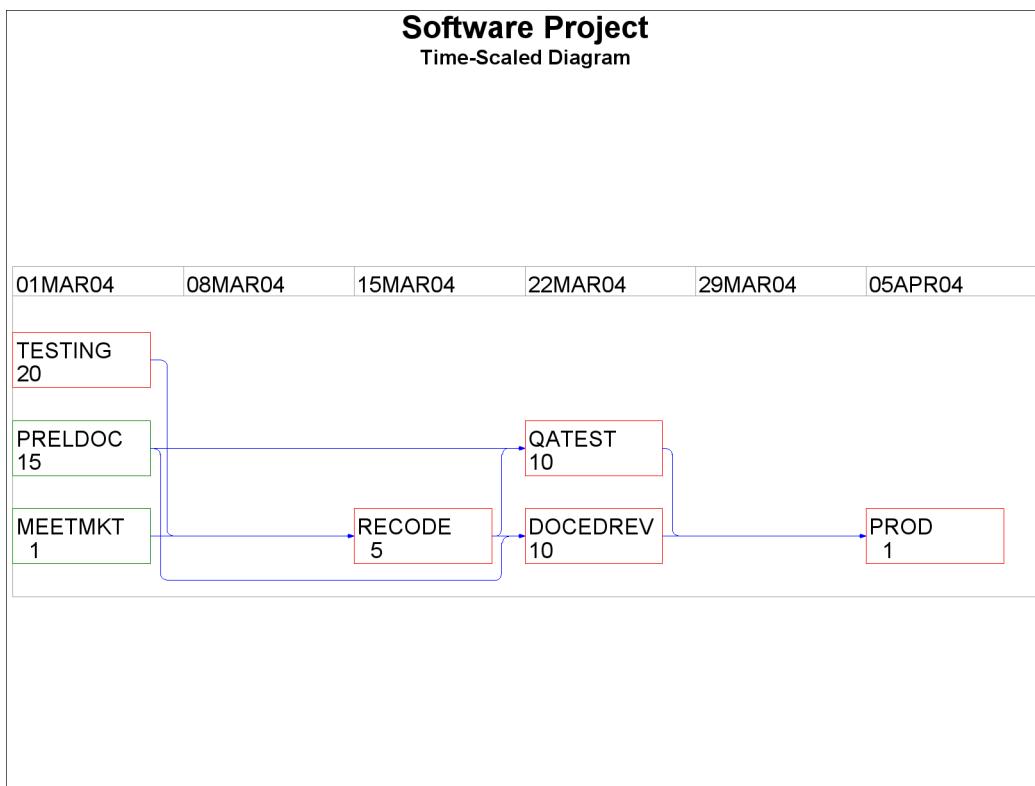**Figure 9.6** Software Project: Time-Scaled Network Diagram

Several other options are available to control the layout of the nodes, the appearance of the network, and the format of the time axis. For projects that have natural divisions, you can use the ZONE= option to divide the network into horizontal zones or bands. For networks that have an embedded tree structure, you can use the TREE option to draw the network like a tree laid out from left to right, with the root at the left edge of the diagram; in graphics mode, you can obtain a top-down tree with the root at the top of the diagram. For cyclic networks you can use the BREAKCYCLE option to enable the procedure to break cycles. All of these options are discussed in detail in the following sections.

## Syntax: NETDRAW Procedure

The following statements are used in PROC NETDRAW:

```
PROC NETDRAW options ;
  ACTNET / options ;
```

## Functional Summary

Table 9.1 outlines the options available for the NETDRAW procedure classified by function.

**Table 9.1** Functional Summary

Description	Statement	Option
<b>Color Options</b>		
Specifies the color of arcs	ACTNET	CARCS=
Specifies the color of time axis	ACTNET	CAXIS=
Specifies the fill color for critical nodes	ACTNET	CCNODEFILL=
Specifies the color of critical arcs	ACTNET	CCRITARCS=
Specifies the outline color of critical nodes	ACTNET	CCRITOUT=
Specifies the fill color for nodes	ACTNET	CNODEFILL=
Specifies the outline color of nodes	ACTNET	COUTLINE=
Specifies the color of reference lines	ACTNET	CREF=
Specifies the color of reference break lines	ACTNET	CREFBRK=
Specifies the text color	ACTNET	CTEXT=
<b>Data Set Specifications</b>		
Specifies the Annotate data set	ACTNET	ANNOTATE=
Specifies the Annotate data set	NETDRAW	ANNOTATE=
Specifies the Activity data set	NETDRAW	DATA=
Specifies the Network output data set	NETDRAW	OUT=
<b>Format Control Options</b>		
Specifies the height of node in character cells	ACTNET	BOXHT=
Specifies the width of node in character cells	ACTNET	BOXWIDTH=
Specifies the DURATION variable	ACTNET	DURATION=
Specifies the ID variables	ACTNET	ID=
Suppresses default ID variables	ACTNET	NODEFID
Suppresses ID variable labels	ACTNET	NOLABEL
Specifies the upper limit on number of pages	ACTNET	PAGES=
Indicates completed or in-progress activities	ACTNET	SHOWSTATUS
Specifies the horizontal distance between nodes	ACTNET	XBETWEEN=
Specifies the vertical distance between nodes	ACTNET	YBETWEEN=
<b>Full-Screen Options</b>		
Specifies the reference break line character	ACTNET	BRKCHAR=
Specifies the characters for node outlines and connections	ACTNET	FORMCHAR=
Specifies the reference character	ACTNET	REFCHAR=
<b>Graphics Catalog Options</b>		
Specifies the description for the catalog entry	ACTNET	DESCRIPTION=
Specifies the name for the catalog entry	ACTNET	NAME=
Specifies the name of the graphics catalog	NETDRAW	GOUT=
<b>Graphics Display Options</b>		
Specifies the length of arrowhead in character cells	ACTNET	ARROWHEAD=
Centers each ID variable within node	ACTNET	CENTERID
Compresses the diagram to a single page	ACTNET	COMPRESS

**Table 9.1** *continued*

Description	Statement	Option
Specifies the text font	ACTNET	FONT=
Specifies the text height	ACTNET	HEIGHT=
Specifies the horizontal margin in character cells	ACTNET	HMARGIN=
Specifies the number of horizontal pages	ACTNET	HPAGES=
Specifies the reference line style	ACTNET	LREF=
Specifies the reference break line style	ACTNET	LREFBRK=
Specifies the width of lines used for critical arcs	ACTNET	LWCRT=
Specifies the width of lines	ACTNET	LWIDTH=
Specifies the width of outline for nodes	ACTNET	LWOUTLINE=
Suppresses filling of arrowheads	ACTNET	NOARROWFILL
Suppresses page number	ACTNET	NOPAGENUMBER
Suppresses vertical centering	ACTNET	NOVCENTER
Specifies the number of nodes in horizontal direction	ACTNET	NXNODES=
Specifies the number of nodes in vertical direction	ACTNET	NYNODES=
Displays page number at upper right corner	ACTNET	PAGENUMBER
Specifies the PATTERN variable	ACTNET	PATTERN=
Proportionally compresses the diagram	ACTNET	PCOMPRESS
Draws arcs with rectangular corners	ACTNET	RECTILINEAR
Reverses the order of the y pages	ACTNET	REVERSEY
Rotates the network diagram	ACTNET	ROTATE
Rotates text within node by 90 degrees	ACTNET	ROTATETEXT
Draws arcs along distinct tracks	ACTNET	SEPARATEARCS
Specifies the vertical margin in character cells	ACTNET	VMARGIN=
Specifies the number of vertical pages	ACTNET	VPAGES=
<b>Layout Options</b>		
Breaks cycles in cyclic networks	ACTNET	BREAKCYCLE
Uses dynamic programming algorithm to route arcs	ACTNET	DP
Specifies the number of horizontal tracks between nodes	ACTNET	HTRACKS=
Routes arcs along potential node positions	ACTNET	NODETRACK
Disables use of dynamic programming to route arcs	ACTNET	NONDP
Blocks track along potential node positions	ACTNET	NONODETRACK
Restricts scope of arc layout algorithm	ACTNET	RESTRICTSEARCH
Uses spanning tree layout	ACTNET	SPANNINGTREE
Draws network as a tree, if possible	ACTNET	TREE
Specifies the number of vertical tracks between nodes	ACTNET	VTRACKS=
<b>Line-Printer Options</b>		
Specifies the reference break line character	ACTNET	BRKCHAR=
Specifies the characters for node outlines and connections	ACTNET	FORMCHAR=
Specifies the reference character	ACTNET	REFCHAR=
<b>Mode Options</b>		
Invokes full-screen version	NETDRAW	FULLSCREEN

**Table 9.1** *continued*

Description	Statement	Option
Invokes graphics version	NETDRAW	GRAPHICS
Invokes line-printer version	NETDRAW	LINEPRINTER
Suppresses display of diagram	NETDRAW	NODISPLAY
<b>Network Specifications</b>		
Specifies the ACTIVITY variable	ACTNET	ACTIVITY=
Specifies the LAG variables	ACTNET	LAG=
Specifies the SUCCESSOR variables	ACTNET	SUCCESSOR=
<b>Time-Scale Options</b>		
Specifies the ALIGN variable	ACTNET	ALIGN=
Draws reference lines at every level	ACTNET	AUTOREF
Draws a border around the network diagram and axes	ACTNET	FRAME
Draws all vertical levels	ACTNET	LINEAR
Specifies the maximum number of empty columns between tick marks	ACTNET	MAXNULLCOLUMN=
Specifies the smallest interval per level	ACTNET	MININTERVAL=
Specifies the number of levels per tick mark	ACTNET	NLEVELSPERCOLUMN=
Suppresses time axis on continuation pages	ACTNET	NOREPEATAXIS
Omits the time axis	ACTNET	NOTIMEAXIS
Stops procedure if align value is missing	ACTNET	QUITMISSINGALIGN
Draws zigzag reference line at breaks	ACTNET	REFBREAK
Shows all breaks in time axis	ACTNET	SHOWBREAK
Draws time-scaled diagram	ACTNET	TIMESCALE
Uses format of variable and not default	ACTNET	USEFORMAT
<b>Tree Options</b>		
Centers each node with respect to subtree	ACTNET	CENTERSUBTREE
Specifies the order of the children of each node	ACTNET	CHILDORDER=
Separates the sons of a node for symmetry	ACTNET	SEPARATESONS
Uses spanning tree layout	ACTNET	SPANNINGTREE
Draws network as a tree, if possible	ACTNET	TREE
<b>Web Options</b>		
Specifies the Image map output data set	NETDRAW	IMAGEMAP=
Specifies the HTML variable	ACTNET	WEB=
<b>Zone Options</b>		
Divides network into connected components	ACTNET	AUTOZONE
Suppresses zone labels	ACTNET	NOZONELABEL
Specifies the ZONE variable	ACTNET	ZONE=
Labels zones	ACTNET	ZONELABEL
Sets missing pattern values using zone	ACTNET	ZONEPAT
Leaves extra space between zones	ACTNET	ZONESPACE

---

## PROC NETDRAW Statement

**PROC NETDRAW** *options* ;

The following options can appear in the PROC NETDRAW statement.

**ANNOTATE=SAS-data-set**

specifies the input data set that contains the appropriate annotate variables for the purpose of adding text and graphics to the network diagram. The data set specified must be an Annotate data set. See the section “[Using the Annotate Facility](#)” on page 701 for further details about this option.

**DATA=SAS-data-set**

names the SAS data set to be used by PROC NETDRAW for producing a network diagram. If DATA= is omitted, the most recently created SAS data set is used. This data set, also referred to as the Network data set, contains the network information (ACTIVITY and SUCCESSOR variables) and any ID variables that are to be displayed within the nodes. For details about this data set, see the section “[Network Input Data Set](#)” on page 685.

**FULLSCREEN**

**FS**

indicates that the network be drawn in full-screen mode. This enables you to view the network diagram produced by NETDRAW in different scales; you can also move nodes around the diagram to modify the layout.

**GOUT=graphics-catalog**

specifies the name of the graphics catalog used to save the output produced by PROC NETDRAW for later replay. This option is valid only if the **GRAPHICS** option is specified.

**GRAPHICS**

indicates that the network diagram produced be of high-resolution quality. If you specify the GRAPHICS option, but you do not have SAS/GRAFH software licensed at your site, the procedure stops and issues an error message. GRAPHICS is the default mode.

**IMAGEMAP=SAS-data-set**

names the SAS data set that receives a description of the areas of a graph and a link for each area. This information is for the construction of HTML image maps. You use a SAS DATA step to process the output file and generate your own HTML files. The graph areas correspond to the link information that comes from the WEB variable in the Network data set. This gives you complete control over the appearance and structure of your HTML pages.

**LINEPRINTER**

**LP**

produces a network diagram of line-printer quality.

**NODISPLAY**

requests the procedure not to display any output. The procedure still produces the Layout data set containing the details about the network layout. This option is useful to determine node placement and arc routing for a network that can be used at a later time to display the diagram.

**OUT=SAS-data-set**

specifies a name for the output data set produced by PROC NETDRAW. This data set, also referred to as the [Layout](#) data set, contains the node and arc placement information determined by PROC NETDRAW to draw the network. This data set contains all the information that was specified in the [Network](#) data set to define the project; in addition, it contains variables that specify the coordinates for the nodes and arcs of the network diagram. For details about the Layout data set, see the section “[Layout Data Set](#)” on page 692.

If the OUT= option is omitted, the procedure creates a data set and names it according to the DATA*n* convention.

## ACTNET Statement

**ACTNET** / *options* ;

The ACTNET statement draws the network diagram. You can specify several options in this statement to control the appearance of the network. All these options are described in the current section under appropriate headings: first, all options that are valid for all modes of the procedure are listed, followed by the options classified according to the mode (full-screen, graphics, or line-printer) of invocation of the procedure.

### General Options

#### **ACTIVITY=***variable*

specifies the variable in the [Network](#) data set that names the nodes in the network. If the data set contains a variable called \_FROM\_, this specification is ignored; otherwise, this option is required.

#### **ALIGN=***variable*

specifies the variable in the [Network](#) data set containing the time values to be used for positioning each activity. This option triggers the [TIMESCALE](#) option that adds a time axis at the top of the network and aligns the nodes of the network according to the values of the ALIGN= variable. The minimum and maximum values of this variable are used to determine the time axis. The format of this variable is used to determine the default value of the [MININTERVAL=](#) option, which, in turn, determines the format of the time axis.

#### **AUTOREF**

draws reference lines at every tick mark. This option is valid only for time-scaled network diagrams.

#### **AUTOZONE**

enables automatic zoning (or dividing) of the network into connected components. This option is equivalent to defining an automatic zone variable that associates a tree number for each node. The tree number refers to a number assigned (by the procedure) to each distinct tree of a spanning tree of the network.

#### **BREAKCYCLE**

breaks cycles by reversing the back arcs of the network. The back arcs are determined by constructing an underlying spanning tree of the network. Once cycles are broken, the nodes of the network are laid out using a topological ordering of the new network formed from the original network by ignoring the back arcs. The back arcs are drawn after determining the network layout. Note that only the back arcs go from right to left.

**BOXHT=***boxht*

specifies the height of the box (in character cell positions) used for denoting a node. If this option is not specified, the height of the box equals the number of lines required for displaying all of the ID variable values for any of the nodes. See the ROTATETEXT option (under “Graphics Options”) for an exception.

**BOXWIDTH=***boxwdth*

specifies the width of the box (in character cell positions) used for denoting a node. If this option is not specified, the width of the box equals the maximum number of columns required for displaying all of the ID variable values for any of the nodes. See the ROTATETEXT option (under “Graphics Options”) for an exception.

**CENTERSUBTREE**

positions each node at the center of the subtree that originates from that node instead of placing it at the midpoint of its children (which is the default behavior). Note that the nodes are placed at integral positions along an imaginary grid, so the positioning may not be exactly at the center. This option is valid only in conjunction with the **TREE** option.

**CHILDORDER=***order*

orders the children of each node when the network is laid out using either the **TREE** or the **SPANNINGTREE** option. The valid values for this option are TOPDOWN and BOTTOMUP for default orientation, and LEFTRGHT and RGHTLEFT for rotated networks (drawn with the **ROTATETEXT** option). The default is TOPDOWN.

**DP**

causes PROC NETDRAW to use a dynamic programming (DP) algorithm to route the arcs. This DP algorithm is memory and CPU-intensive and is not necessary for most applications.

**DURATION=***variable*

specifies a variable that contains the duration of each activity in the network. This value is used only for displaying the durations of each activity within the node.

**FRAME**

encloses the drawing area with a border. This option is valid only for time-scaled or zoned network diagrams.

**HTRACKS=***integer*

controls the number of arcs that are drawn horizontally through the space between two adjacent nodes. This option enables you to control the arc-routing algorithm. The default value is based on the maximum number of successors of any node.

**ID=(***variables***)**

specifies the variables in the **Network** data set that are displayed within each node. In addition to the ID variables, the procedure displays the **ACTIVITY** variable, the **DURATION** variable (if the **DURATION=** option was specified), and any of the following variables in the **Network** data set: E\_START, E\_FINISH, L\_START, L\_FINISH, S\_START, S\_FINISH, A\_START, A\_FINISH, T\_FLOAT, and F\_FLOAT. See Chapter 4, “The CPM Procedure,” for a description of these variables. If you specify the **NODEFID** option, only the variables listed in the **ID=** option are displayed.

**LAG=variable****LAG=(variables)**

specifies the variables in the **Network** data set that identify the lag types of the precedence relationships between an activity and its successors. Each **SUCCESSOR** variable is matched with the corresponding LAG variable; that is, for a given observation, the *i*th LAG variable defines the relationship between the activities specified by the ACTIVITY variable and the *i*th SUCCESSOR variable. The LAG variables must be character type, and their values are expected to be specified as one of FS, SS, SF, or FF, which denote ‘Finish-to-Start’, ‘Start-to-Start’, ‘Start-to-Finish’, and ‘Finish-to-Finish’, respectively. You can also use the *keyword\_duration\_calendar* specification used by the CPM procedure, although PROC NETDRAW uses only the *keyword* information and ignores the lag *duration* and the lag *calendar*. If no LAG variables exist or if an unrecognized value is specified for a LAG variable, PROC NETDRAW interprets the lag as a ‘Finish-to-Start’ type.

This option enables the procedure to identify the different types of nonstandard precedence constraints (Start-to-Start, Start-to-Finish, and Finish-to-Finish) on graphics quality network diagrams by drawing the arcs from and to the appropriate edges of the nodes.

**LINEAR**

plots one column for every *mininterval* between the minimum and maximum values of the **ALIGN**= variable. By default, only those columns that contain at least one activity are displayed. This option is valid only for time-scaled network diagrams.

**MAXNULLCOLUMN=maxncol****MAXEMPTY=maxncol****MAXZCOL=maxncol****MAXNCOL=maxncol**

specifies the maximum number of empty columns between two consecutive nonempty columns. The default value for this option is 0. Note that specifying the **LINEAR** option is equivalent to specifying the **MAXNULLCOLUMN**= option to be infinity. This option is valid only for time-scaled network diagrams.

**MININTERVAL=mininterval**

specifies the smallest interval to be used per column of the network diagram. Thus, if **MININTERVAL**=DAY, each column is used to represent a day, and all activities that start on the same day are placed in the same column. The valid values for *mininterval* are SECOND, MINUTE, HOUR, DAY, WEEK, MONTH, QTR, and YEAR. The default value of *mininterval* is determined by the format of the **ALIGN**= variable. The tick labels are formatted on the basis of *mininterval*; for example, if *mininterval* is DAY, the dates are marked using the DATE7. format, and if *mininterval* is HOUR, the labels are formatted as TIME5. and so on. This option is valid only for time-scaled network diagrams.

**NLEVELSPERCOLUMN=npercol****NPERCOL=npercol**

contracts the time axis by specifying that activities that differ in **ALIGN**= value by less than *npercol* units of **MININTERVAL** can be plotted in the same column. The default value of *npercol* is 1. This option is valid only for time-scaled network diagrams.

**NODEFID**

indicates that the procedure need not check for any of the default ID variables in the Network data set; if this option is in effect, only the variables specified in the **ID=** option are displayed within each node.

**NODETRACK**

specifies that the arcs can be routed along potential node positions if there is a clear horizontal track to the left of the successor (or **\_TO\_**) node. This is the default option. To prevent the use of potential node positions, use the **NONODETRACK** option.

**NOLABEL**

suppresses the labels. By default, the procedure uses the first three letters of the variable name to label all the variables that are displayed within each node of the network. The only exception is the variable that is identified by the **ACTIVITY=** option.

**NONDP**

uses a simple heuristic to connect the nodes. The default mode of routing is NONDP, unless the **HTRACKS=** or **VTRACKS=** option (or both) are specified and set to a number that is less than the maximum number of successors. The NONDP option is faster than the **DP** option.

**NONODETRACK**

blocks the horizontal track along potential node positions. This option may lead to more turns in some of the arcs. The default is NODETRACK.

**NOREPEATAxis**

displays the time axis only on the top of the chart and not on every page. This option is useful if the different pages are to be glued together to form a complete diagram. This option is valid only for time-scaled network diagrams.

**NOTIMEAXIS**

suppresses the display of the time axis and its labels. Note that the nodes are still placed according to the time scale, but no axis is drawn. This option is valid only for time-scaled network diagrams.

**NOZONELABEL****NOZONEDESCR**

omits the zone labeling and the dividing lines. The network is still divided into zones based on the **ZONE** variable, but there is no demarcation or labeling corresponding to the zones.

**PAGES=npages**

specifies the maximum number of pages to be used for the network diagram in graphics and line-printer modes. The default value is 100.

**QUITMISSINGALIGN**

stops processing if the **ALIGN=** variable has any missing values. By default, the procedure tries to fill in missing values using the topological order of the network. This option is valid only for time-scaled network diagrams.

**REFBREAK**

shows breaks in the time axis by drawing a zigzag line down the diagram just before the tick mark at the break. This option is valid only for time-scaled network diagrams.

**RESTRICTSEARCH****RSEARCH**

restricts the scope of the arc layout algorithm by restricting the area of search for the arc layout when the DP option is in effect; this is useful in reducing the computational complexity of the dynamic programming algorithm. By default, using the DP algorithm to route the arcs, the y coordinates of the arcs can range through the entire height of the network. The RESTRICTSEARCH option limits the y coordinates to the minimum and the maximum of the y coordinates of the node and its immediate successors.

**SEPARATESONS**

separates the children (immediate successors) of a given node by adding an extra space in the center whenever it is needed to enable the node to be positioned at integral (x, y) coordinates. For example, if a node has two children, placing the parent node at the midpoint between the two children requires the y coordinate to be noninteger, which is not allowed in the Layout data set. By default, the procedure positions the node at the same y level as one of its children. The SEPARATESONS option separates the two children by adding a dummy child in between, thus enabling the parent node to be centered with respect to its children. This option is valid only in conjunction with the TREE option.

**SHOWBREAK**

shows breaks in the time axis by drawing a jagged break in the time axis line just before the tick mark corresponding to the break. This option is valid only for time-scaled network diagrams.

**SHOWSTATUS**

uses the variable STATUS (if it exists) in the Network data set to determine if an activity is in-progress or completed. Note that the STATUS variable exists in the Schedule data set produced by PROC CPM when used with an ACTUAL statement. If there is no STATUS variable or if the value is missing, the procedure uses the A\_FINISH and A\_START values to determine the status of the activity. If the network is drawn in line-printer or full-screen mode, activities in progress are outlined with the letter P and completed activities are outlined with the letter F; in high-resolution graphics mode, in-progress activities are marked with a diagonal line across the node from the bottom left to the top right corner, while completed activities are marked with two diagonal lines.

**SPANNINGTREE**

uses a spanning tree to place the nodes in the network. This method typically results in a wider layout than the default. However, for networks that have totally disjoint pieces, this option separates the network into connected components (or disjoint trees). This option is not valid for time-scaled or zoned network diagrams, because the node placement dictated by the spanning tree may not be consistent with the zone or the tickmark corresponding to the node.

**SUCCESSOR=(variables)**

specifies the variables in the Network data set that name all the immediate successors of the node specified by the ACTIVITY variable. This specification is ignored if the data set contains a variable named \_TO\_. At least one SUCCESSOR variable must be specified if the data set does not contain a variable called \_TO\_.

**TIMESCALE**

indicates that the network is to be drawn using a time axis for placing the nodes. This option can be used to align the network according to default variables. If the TIMESCALE option is specified without the ALIGN= option, the procedure looks for default variables in the following order: E\_START,

**L\_START**, **S\_START**, and **A\_START**. The first of these variables that is found is used as the **ALIGN=** variable.

### TREE

#### TREELAYOUT

requests the procedure to draw the network as a tree if the network is indeed a tree (that is, all the nodes have at most one immediate predecessor). The option is ignored if the network does not have a tree structure.

#### USEFORMAT

indicates that the explicit format of the **ALIGN=** variable is to be used instead of the default format based on the **MININTERVAL=** option. Thus, for example, if the **ALIGN** variable contains SAS date values, by default, the procedure uses the **DATE7.** format for the time axis labels irrespective of the format of the **ALIGN=** variable. The **USEFORMAT** option specifies that the variable's format should be used for the labels instead of the default format. This option is valid only for time-scaled network diagrams.

#### VTRACKS=integer

controls the number of arcs that are drawn vertically through the space between two adjacent nodes. A default value is based on the maximum number of successors of any node.

#### XBETWEEN=integer

#### HBETWEEN=integer

specifies the horizontal distance (in character cell positions) between two adjacent nodes. The value for this option must be at least 3; the default value is 5.

#### YBETWEEN=integer

#### VBETWEEN=integer

specifies the vertical distance (in character cell positions) between two adjacent nodes. The value for this option must be at least 3; the default value is 5.

#### ZONE=variable

names the variable in the **Network** data set used to separate the network diagram into zones.

#### ZONELABEL

#### ZONEDESCR

labels the different zones and draws dividing lines between two consecutive zones. This is the default behavior; to omit the labels and the dividing lines, use the **NOZONELABEL** option.

#### ZONESPACE

#### ZONELEVADD

draws the network with an extra row between two consecutive zones.

## Full-Screen Options

#### BRKCHAR=brkchar

specifies the character used for drawing the zigzag break lines down the chart at break points of the time axis. The default value is **>**. This option is valid only for time-scaled network diagrams.

**CARCS=***color*

specifies the color of the connecting lines (or arcs) between the nodes. The default value of this option is CYAN.

**CAXIS=***color*

specifies the color of the time axis. The default value is WHITE. This option is valid only for time-scaled network diagrams.

**CCRITARCS=***color*

specifies the color of arcs connecting critical activities. The procedure uses the values of the E\_FINISH and L\_FINISH variables (if they are present) in the *Network* data set to determine the critical activities. The default value is the value of the **CARCS=** option.

**CREF=***color*

specifies the color of the reference lines. The default value is WHITE. This option is valid only for time-scaled network diagrams.

**CREFBRK=***color*

specifies the color of the lines drawn to denote breaks in the time axis. The default value is WHITE. This option is valid only for time-scaled network diagrams.

**FORMCHAR** [*index list*]='*string*'

specifies the characters used for node outlines and arcs. See the section “Line-Printer Options” on page 685 for a description of this option.

**PATTERN=***variable*

specifies an integer-valued variable in the *Network* data set that identifies the color number for each node of the network. If the data set contains a variable called \_PATTERN, this specification is ignored. All the colors available for the full-screen device are used in order corresponding to the number specified in the PATTERN variable; if the value of the PATTERN variable is more than the number of colors available for the device, the colors are repeated starting once again with the first color. If a PATTERN variable is not specified, the procedure uses the first color for noncritical activities, the second color for critical activities, and the third color for supercritical activities.

**REFCHAR=***refchar*

specifies the reference character used for drawing reference lines. The default value is “l”. This option is valid only for time-scaled network diagrams.

**ZONEPAT**

indicates that if a **PATTERN** variable is not specified or is missing and if a **ZONE=** variable is present, then the node colors are based on the value of the **ZONE=** variable.

## Graphics Options

**ANNOTATE=SAS-data-set**

specifies the input data set that contains the appropriate annotate variables for the purpose of adding text and graphics to the network diagram. The data set specified must be an Annotate data set. See the section “Using the Annotate Facility” on page 701 for further details about this option.

**ARROWHEAD=***integer*

specifies the length of the arrowhead in character cell positions. You can specify ARROWHEAD = 0 to suppress arrowheads altogether. The default value is 1.

**CARCS=***color*

specifies the color to use for drawing the connecting lines between the nodes. The default color depends on the GOPTIONS statement and the GSTYLE system option; see the section “[ODS Style Templates](#)” on page 703 for more information.

**CAXIS=***color*

specifies the color of the time axis. This option is valid only for time-scaled network diagrams. The default color depends on the GSTYLE system option and the value of the **CTEXT=** option; see the section “[ODS Style Templates](#)” on page 703 for more information.

**CCNODEFILL=***color*

specifies the fill color for all critical nodes of the network diagram. If you specify this option, the procedure uses a solid fill pattern (with the color specified in this option) for all critical nodes, ignoring any fill pattern specified in the PATTERN statements; the PATTERN statements are used only to obtain the color of the outline for these nodes unless you specify the **CCRITOUT=** option. The default value for this option is the value of the **CNODEFILL=** option, if it is specified; otherwise, the procedure uses the PATTERN statements to determine the fill pattern and color.

**CCRITARCS=***color*

specifies the color of arcs connecting critical activities. The procedure uses the values of the E\_FINISH and L\_FINISH variables (if they are present) in the [Network](#) data set to determine the critical activities. The default value of this option is the value of the **CARCS=** option.

**CCRITOUT=***color*

specifies the outline color for critical nodes. The default value for this option is the value of the **COUTLINE=** option, if it is specified; otherwise, it is the same as the pattern color for the node.

**CENTERID**

centers the ID values placed within each node. By default, character valued **ID** variables are left justified and numeric ID variables are right justified within each node. This option centers the ID values within each node.

**CNODEFILL=***color*

specifies the fill color for all nodes of the network diagram. If you specify this option, the procedure uses a solid fill pattern with the specified color, ignoring any fill pattern specified in the PATTERN statements; the PATTERN statements are used only to obtain the color of the outline for the nodes, unless you specify the **COUTLINE=** option.

**COMPRESS**

draws the network on one physical page. By default, the procedure draws the network across multiple pages if necessary, using a default scale that allots one character cell position for each letter within the nodes. Sometimes, to get a broad picture of the network and all its connections, you may want to view the entire network on one screen. If the COMPRESS option is specified, PROC NETDRAW determines the horizontal and vertical transformations needed so that the network is compressed to fit on one screen.

**COUTLINE**=*color*

specifies an outline color for all nodes. By default, the procedure sets the outline color for each node to be the same as the fill pattern for the node. This option is useful when used in conjunction with a solid fill using a light color. Note that if an empty fill pattern is specified, then the COUTLINE= option will cause all nodes to appear the same.

**CREF**=*color*

specifies the color of the reference lines. This option is valid only for time-scaled network diagrams. The default color depends on the GSTYLE system option and the value of the **CTEXT**= option; see the section “[ODS Style Templates](#)” on page 703 for more information.

**CREFBRK**=*color*

specifies the color of the zigzag break lines. This option is valid only for time-scaled network diagrams. The default color depends on the GSTYLE system option and the value of the **CTEXT**= option; see the section “[ODS Style Templates](#)” on page 703 for more information.

**CTEXT**=*color***CT**=*color*

specifies the color of all text on the network diagram including variable names or labels, values of ID variables, and so on. The default color depends on the GOPTIONS statement and the GSTYLE system option; see the section “[ODS Style Templates](#)” on page 703 for more information.

**DESCRIPTION**=‘*string*’**DES**=‘*string*’

specifies a descriptive string, up to 40 characters in length, that appears in the description field of the master menu in PROC GREPLAY. If the DESCRIPTION= option is omitted, the description field contains a description assigned by PROC NETDRAW.

**FILLPAGE**

causes the diagram on each page to be magnified (if necessary) to fill up the page.

**FONT**=*font*

specifies the font of the text. The default font depends on the GOPTIONS statement and the GSTYLE system option; see the section “[ODS Style Templates](#)” on page 703 for more information.

**HEIGHT**=*h***HTEXT**=*h*

specifies that the height for all text in PROC NETDRAW (excluding the titles and footnotes) be *h* times the value of the global HTEXT= option, which is the default text height specified in the GOPTIONS statement of SAS/GPGRAPH. The value of *h* must be a positive real number; the default value is 1.0.

**HMARGIN**=*integer*

specifies the width of a horizontal margin (in number of character cell positions) for the network in graphics mode. The default width is 1.

**HPAGES**=*h***NXPAGES**=*h*

specifies that the network diagram is to be produced using *h* horizontal pages. However, it may not be possible to use *h* horizontal pages due to intrinsic constraints on the output.

For example, PROC NETDRAW requires that every horizontal page should contain at least one *x* level. Thus, the number of horizontal pages can never exceed the number of vertical levels in the network. The exact number of horizontal pages used by the network diagram is given in the \_ORNETDR macro variable. See the section “[Macro Variable \\_ORNETDR](#)” on page 702 for further details.

The appearance of the diagram with respect to the HPAGES= option is also influenced by the presence of other related procedure options. The HPAGES= option performs the task of determining the number of vertical pages in the absence of the VPAGES= option. If the COMPRESS or PCOMPRESS option is specified in this scenario, the chart uses one vertical page (unless the HPAGES= and VPAGES= options are specified). If neither the COMPRESS nor PCOMPRESS option is specified, the number of vertical pages is computed in order to display as much of the chart as possible in a proportional manner.

**LREF=***linestyle*

specifies the linestyle (1-46) of the reference lines. The default linestyle is 1, a solid line. See [Figure 8.5](#) in Chapter 8, “[The GANTT Procedure](#),” for examples of the various line styles available. This option is valid only for time-scaled network diagrams.

**LREFBRK=***linestyle*

specifies the linestyle (1-46) of the zigzag break lines. The default linestyle is 1, a solid line. See [Figure 8.5](#) in Chapter 8, “[The GANTT Procedure](#),” for examples of the various line styles available. This option is valid only for time-scaled network diagrams.

**LWCRIT=***integer*

specifies the line width for critical arcs and the node outlines for critical activities. If the LWCRIT= option is not specified, the procedure uses the value specified for the **LWIDTH=** option.

**LWIDTH=***integer*

specifies the line width of the arcs and node outlines. The default line width is 1.

**LWOUTLINE=***integer*

specifies the line width of the node outlines. The default line width for the node outline is equal to **LWIDTH** for noncritical nodes and **LWCRIT** for critical nodes.

**NAME=***'string'*

specifies a string of up to eight characters that appears in the name field of the catalog entry for the graph. The default name is NETDRAW. If either the name specified or the default name duplicates an existing name in the catalog, then the procedure adds a number to the duplicate name to create a unique name, for example, NETDRAW2.

**NOARROWFILL**

draws arrowheads that are not filled. By default, the procedure uses filled arrowheads.

**NOPAGENUMBER**

**NONUMBER**

suppresses the page numbers that are displayed in the top right corner of each page of a multipage network diagram. Note that the pages are ordered from left to right, bottom to top (unless the **REVERSEY** option is specified).

**NOVCENTER**

draws the network diagram just below the titles without centering in the vertical direction.

**NXNODES=*nx***

specifies the number of nodes that should be displayed horizontally across each page of the network diagram. This option determines the value of the **HPAGES=** option; this computed value of HPAGES overrides the specified value for the HPAGES= options.

**NYNODES=*ny***

specifies the number of nodes that should be displayed vertically across each page of the network diagram. This option determines the value of the **VPAGES=** option; this computed value of VPAGES overrides the specified value for the VPAGES= options.

**PAGENUMBER****PAGENUM**

numbers the pages of the network diagram on the top right-hand corner of the page if the diagram exceeds one page. The numbering scheme is from left to right, bottom to top (unless the **REVERSEY** option is specified).

**PATTERN=*variable***

specifies an integer-valued variable in the **Network** data set that identifies the pattern for filling each node of the network. If the data set contains a variable called **\_PATTERN**, this specification is ignored. The patterns are assumed to have been specified using PATTERN statements. If a PATTERN variable is not specified, the procedure uses the first PATTERN statement for noncritical activities, the second PATTERN statement for critical activities, and the third PATTERN statement for supercritical activities.

**PCOMPRESS**

draws the network diagram on one physical page. As with the COMPRESS option, the procedure determines the horizontal and vertical transformation needed so that the network is compressed to fit on one screen. However, in this case, the transformations are such that the network diagram is proportionally compressed. See [Example 9.4](#) for an illustration of this option.

If the HPAGES= and VPAGES= options are used to control the number of pages, each page of the network diagram is drawn while maintaining the original aspect ratio.

**RECTILINEAR**

draws arcs with rectangular corners. By default, the procedure uses rounded turning points and rounded arc merges in graphics mode.

**REVERSEY**

reverses the order in which the *y* pages are drawn. By default, the pages are ordered from bottom to top in the graphics mode. This option orders them from top to bottom.

**ROTATE**

rotates the network diagram to change the orientation of the network to be from top to bottom instead of from left to right. For example, you can use this option to draw a Bill of Materials diagram that is traditionally drawn from top to bottom with the Final Product drawn at the top of the tree. In addition to rotating the orientation of the network, use the **ROTATETEXT** option to rotate the text within each node. See [Example 9.18](#) for an illustration of this option.

This option is similar to the global graphics option, ROTATE (GOPTIONS ROTATE). Note that if the global graphics option is used, titles and footnotes also need to be drawn with an angle specification:

**A=90.** However, some device drivers ignore the global graphics option, ROTATE (for example, the SASGDDMX driver). Use the ROTATE option on the ACTNET statement for such device drivers.

#### **ROTATETEXT**

##### **RTEXT**

rotates the text within the nodes by 90 degrees. This option is useful when used in conjunction with the **ROTATE** option in the ACTNET statement (or the global graphics option ROTATE) to change the orientation of the network to be from top to bottom instead of from left to right. For example, you can use this option to draw an organizational chart that is traditionally drawn from top to bottom with the head of the organization at the top of the chart. If the ROTATETEXT option is specified, then the definitions of the **BOXHT=** and **BOXWIDTH=** options are reversed. See [Example 9.18](#) for an illustration of this option.

#### **SEPARATEARCS**

separates the arcs to follow distinct tracks. By default, the procedure draws all segments of the arcs along a central track between the nodes, which may cause several arcs to be drawn on top of one another. If the SEPARATEARCS option is specified, the procedure may increase the values of the **XBETWEEN=** and **YBETWEEN=** options to accommodate the required number of lines between the nodes.

#### **VMARGIN=integer**

specifies the width of a vertical margin (in number of character cell positions) for the network. The default width is 1.

#### **VPAGES=v**

#### **NYPAGES=v**

specifies that the network diagram is to be produced using *v* vertical pages. This, however, may not be possible due to intrinsic constraints on the output. For example, PROC NETDRAW requires that every vertical page should contain at least one y level. Thus, the number of vertical pages can never exceed the number of horizontal levels in the network. The exact number of vertical pages used by the procedure is provided in the **\_ORNETDR** macro variable. See the section “[Macro Variable \\_ORNETDR](#)” on page 702 for further details.

The appearance of the diagram with respect to the VPAGES= option is also influenced by the presence of other related procedure options. The VPAGES= option performs the task of determining the number of horizontal pages in the absence of the HPAGES= option (or the NXNODES= option). If the COMPRESS or PCOMPRESS option is specified (without the HPAGES= or NXNODES= options), the chart uses one horizontal page. If neither the COMPRESS nor PCOMPRESS option is specified, the number of horizontal pages is computed in order to display as much of the chart as possible in a proportional manner.

#### **WEB=variable**

#### **HTML=variable**

specifies the character variable in the Network data set that identifies an HTML page for each activity. The procedure generates an HTML image map using this information for each node in the network diagram.

**ZONEPAT**

indicates that if a PATTERN= variable is not specified or is missing and if a ZONE= variable is present, then the node patterns are based on the value of the ZONE= variable.

**Line-Printer Options****BRKCHAR=brkchar**

specifies the character used for drawing the zigzag break lines down the chart at break points of the time axis. The default value is >. This option is valid only for time-scaled network diagrams.

**FORMCHAR [index list]=‘string’**

specifies the characters used for node outlines and arcs. The value is a string 20 characters long. The first 11 characters define the 2 bar characters, vertical and horizontal, and the 9 corner characters: upper-left, upper-middle, upper-right, middle-left, middle-middle (cross), middle-right, lower-left, lower-middle, and lower-right. These characters are used to outline each node and connect the arcs. The nineteenth character denotes a right arrow. The default value of the FORMCHAR= option is |----|+|---+=|-/\<>\*. Any character or hexadecimal string can be substituted to customize the appearance of the diagram. Use an index list to specify which default form character each supplied character replaces, or replace the entire default string by specifying the full character replacement string without an index list. For example, change the four corners of each node and all turning points of the arcs to asterisks by specifying

```
FORMCHAR (3 5 7 9 11) = '*****'
```

Specifying

```
formchar= ' (11 blanks)
```

produces a network diagram with no outlines for the nodes (as well as no arcs). For further details about the FORMCHAR= option see Chapter 7, “[The DTREE Procedure](#),” and Chapter 8, “[The GANTT Procedure](#).”

**REFCHAR=refchar**

specifies the reference character used for drawing reference lines. The default value is “l”. This option is valid only for time-scaled network diagrams.

**Details: NETDRAW Procedure****Network Input Data Set**

The Network input data set contains the precedence information, namely the activity-successor information for all the nodes in the network. The minimum amount of information that is required by PROC NETDRAW is the activity-successor information for the network. Additional information in the input data set can be used by the procedure to add detail to the nodes in the diagram or control the layout of the network diagram.

Three types of data sets are typically used as the Network data set input to PROC NETDRAW. Which type of data set you use depends on the stage of the project:

- The [Activity](#) data set that is input to PROC CPM is the first type. In the initial stages of project definition, it may be useful to get a graphical representation of the project showing all the activity precedence constraints.
- The [Schedule](#) data set produced by PROC CPM (as the OUT= data set) is the second type. When a project is in progress, you may want to obtain a network diagram showing all the relevant start and finish dates for the activities in the project, in addition to the precedence constraints. You may also want to draw a time-scaled network diagram, with the activities arranged according to the start or finish times corresponding to any of the different schedules produced by PROC CPM.
- The [Layout](#) data set produced by PROC NETDRAW (as the OUT= data set) is the third type. Often, you may want to draw network diagrams of the project every week showing updated information (as the project progresses); if the network logic has not changed, it is not necessary to determine the placement of the nodes and the routing of the arcs every time. You can use the [Layout](#) data set produced by PROC NETDRAW that contains the node and arc positions, update the start and finish times of the activities or merge in additional information about each activity, and use the modified data set as the Network data set input to PROC NETDRAW. The new network diagram will have the same layout as the earlier diagram but will contain updated information about the schedule. Such a data set may also be useful if you want to modify the layout of the network by changing the positions of some of the nodes. See the section “[Controlling the Layout](#)” on page 693 for details about how the layout information is used by PROC NETDRAW. If the Layout data set is used, it contains the variables \_FROM\_ and \_TO\_; hence, it is not necessary to specify the [ACTIVITY=](#) and [SUCCESSOR=](#) options. See [Example 9.13](#) and [Example 9.14](#) for illustrations of the use of the Layout data set.

The minimum information required by PROC NETDRAW from the Network data set is the variable identifying each node in the network and the variable (or variables) identifying the immediate successors of each node. In addition, the procedure can use other optional variables in the data set to enhance the network diagram. The procedure uses the variables specified in the [ID=](#) option to label each node. The procedure also looks for default variable names in the Network data set that are added to the list of ID variables; the default variable names are E\_START, E\_FINISH, L\_START, L\_FINISH, S\_START, S\_FINISH, A\_START, A\_FINISH, T\_FLOAT, and F\_FLOAT. The format used for determining the location of these variables within each node is described in the section “[Format of the Display](#)” on page 690. See the section “[Variables in the Network Data Set](#)” on page 687 for a table of all the variables in the Network data set and their interpretations by PROC NETDRAW.

If the Network data set contains the variables [\\_X\\_](#) and [\\_Y\\_](#) identifying the *x* and *y* coordinates of each node and each turning point of each arc in the network, then this information is used by the procedure to draw the network. Otherwise, the precedence relationships among the activities are used to determine the layout of the network. It is possible to specify only the node positions and let the procedure determine the routing of all the arcs. However, partial information cannot be augmented by the procedure.

**NOTE:** If arc information is provided, the procedure assumes that it is complete and correct and uses it exactly as specified.

---

## Variables in the Network Data Set

The NETDRAW procedure expects all the network information to be contained in the Network input data set named by the DATA= option. The network information is contained in the ACTIVITY and SUCCESSOR variables. In addition, the procedure uses default variable names in the Network data set for specific purposes. For example, the \_X\_ and \_Y\_ variables, if they are present in the Network data set, represent the coordinates of the nodes, the \_SEQ\_ variable indexes the turning points of each arc of the network, and so on.

In addition to the network precedence information, the Network data set may also contain other variables that can be used to change the default layout of the network. For example, the nodes of the network can be aligned in the horizontal direction using the ALIGN= specification, or they can be divided into horizontal bands (or zones) using a ZONE variable.

Table 9.2 lists all of the variables associated with the Network data set and their interpretations by the NETDRAW procedure. Note that all the variables are identified to the procedure in the ACTNET statement. Some of the variables use default names that are recognized by the procedure to denote specific information, as explained previously. The table indicates if the variable is default or needs to be identified in the ACTNET statement.

**Table 9.2** Network Data Set and Associated Variables

Statement	Variable Name	Interpretation
ACTNET	ACTIVITY	Activity or node name
	ALIGN	Align variable for time-scaled network
	DURATION	Duration of activity
	ID	Additional variables to be displayed
	PATTERN	Pattern number
	SUCCESSOR	Immediate successor
	WEB	HTML page corresponding to activity
	ZONE	Zone variable for dividing network
Default Variable Names	A_FINISH	Default ID variable
	A_START	Default ID variable
	E_FINISH	Default ID variable
	E_START	Default ID variable
	F_FLOAT	Default ID variable
	L_FINISH	Default ID variable
	L_START	Default ID variable
	S_FINISH	Default ID variable
	S_START	Default ID variable
	T_FLOAT	Default ID variable
	_FROM_	Supersedes ACTIVITY= specification
	_PATTERN	Supersedes PATTERN= specification
	_SEQ_	Index of turning point in arc
	_TO_	Supersedes SUCCESSOR= specification
	_X_	x coordinate of node or arc turning point
	_Y_	y coordinate of node or arc turning point

---


## Missing Values

Missing values are not allowed for the **ACTIVITY**, **\_X\_**, **\_Y\_**, and **\_SEQ\_** variables. Missing values for the **SUCCESSOR** and **ID** variables are ignored. Missing values are not allowed for the **ALIGN=** variable if the **QUITMISSINGALIGN** option is specified; otherwise, the procedure determines suitable values for the **ALIGN=** variable using the topological ordering of the network nodes.

---

## Layout of the Network

The network layout is determined in two stages. First, the precedence relationships are used to determine the positions of the nodes, which are then used to determine a routing of the arcs. The positions of the nodes and arcs are identified by specifying their *x* and *y* coordinates in a grid. Figure 9.7 shows a sample grid and explains some of the conventions followed by PROC NETDRAW in determining the node and arc layout. This notation will be useful in later sections that describe the **Layout** data set and how you can control the layout of the diagram. The asterisks in the figure represent possible positions for the nodes of the network. The arcs are routed between the possible node positions. For example, node **A** has coordinates (1, 3) and node **B** has coordinates (2, 1). The arc connecting them has two turning points and is completely determined by the two pairs of coordinates (1.5, 3) and (1.5, 1); here, *x* = 1.5 implies that the position is midway between the *x* coordinates 1 and 2.

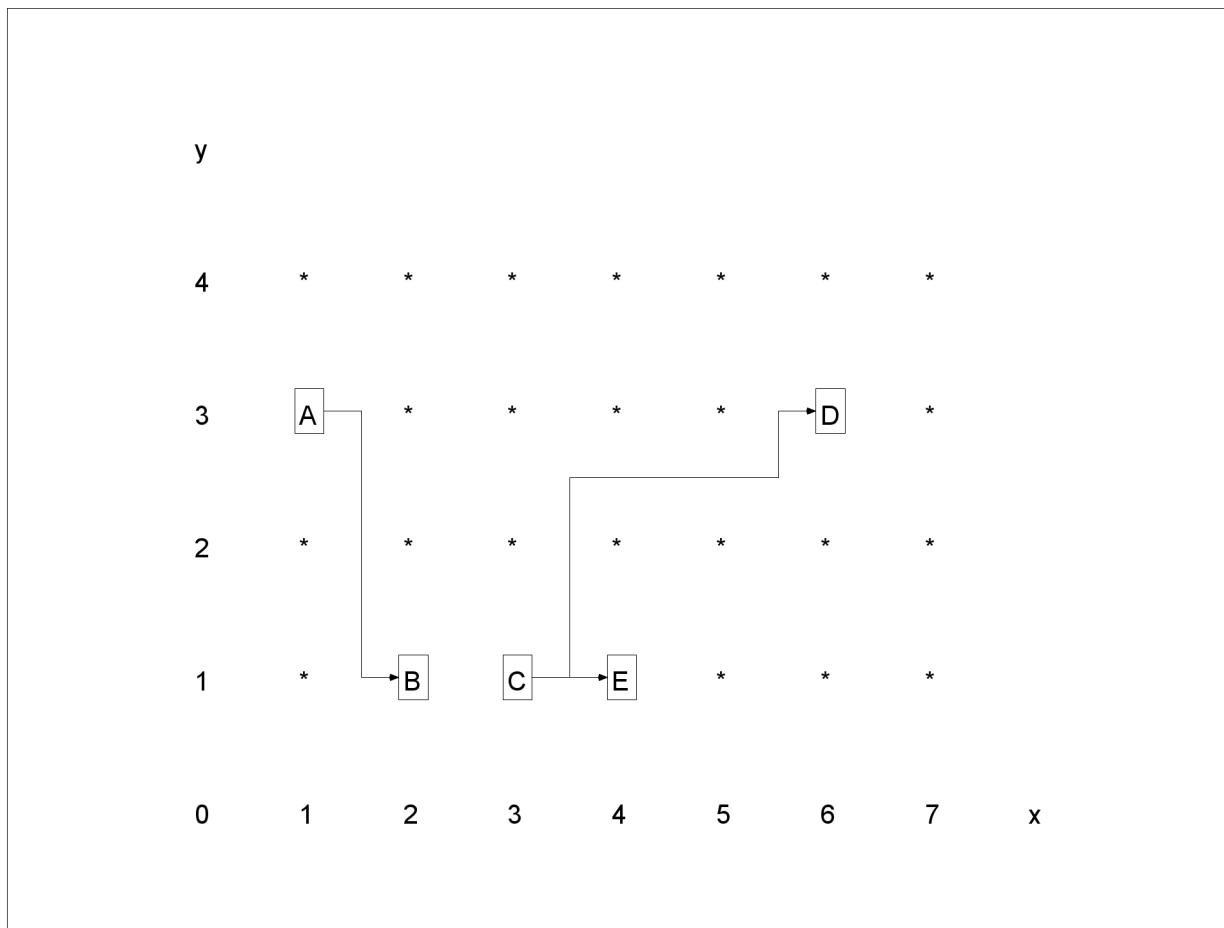**Figure 9.7** Sample Grid and Coordinates for Node and Arc Layout

PROC NETDRAW sets  $x = 1$  for all nodes with no predecessors; the  $x$  coordinates for the other nodes are determined so that each node is placed to the immediate right of all its predecessors; in other words, no node will appear to the left of any of its predecessors or to the right of any of its successors in the network diagram. The nodes are placed in topological order: a node is placed only after all its predecessors have been placed. Thus, the node-placement algorithm requires that there should be no cycles in the network. The  $y$  coordinates of the nodes are determined by the procedure using several heuristics designed to produce a reasonable compact diagram of the network. To draw a network that has cycles, use the **BREAKCYCLE** option, or you can specify the node coordinates or an **ALIGN=** variable to circumvent the requirement of a topological ordering of the nodes (see the second part of [Example 9.12](#)).

Note that the  $x$  and  $y$  coordinates fix only a relative positioning of the nodes and arcs. The actual distance between two nodes, the width and height of each node, and so on can be controlled by specifying desired values for the options that control the format of the display, namely, **BOXHT=**, **BOXWIDTH=**, and so on. See the section “[Format of the Display](#)” on page 690 for details about these options.

By default, the procedure routes the arcs using a simple heuristic that uses, at most, four turning points: the arc leaves the predecessor node from its right edge, turns up or down according to whether the successor is above or below the current node position, then tracks horizontally across to the vertical corridor just before the successor node, and then tracks in a vertical direction to meet the successor node. For example, see the tracking of the arc connecting nodes **c** and **d** in [Figure 9.7](#).

For networks that include some nonstandard precedence constraints, the arcs may be drawn from and to the appropriate edges of the nodes, depending on the type of the constraint.

The default routing of the arcs may lead to an unbalanced diagram with too many arcs in one section and too few in another. The **DP** option in the **ACTNET** statement causes the procedure to use a dynamic programming algorithm to route the arcs. This algorithm tries to route the arcs between the nodes so that not too many arcs pass through any interval between two nodes. The procedure sets the maximum number of arcs that are allowed to be routed along any corridor to be equal to the maximum number of successors for any node. The **HTRACKS=** and **VTRACKS=** options enable you to set these maximum values: **HTRACKS** specifies the maximum number of arcs that are allowed to pass horizontally through any point while **VTRACKS** specifies the same for arcs in the vertical direction. See [Example 9.7](#) for an illustration of the **HTRACKS=** option.

The layout of the network for time-scaled and zoned network diagrams is discussed in the section “[Time-Scaled Network Diagrams](#)” on page 694 and the section “[Zoned Network Diagrams](#)” on page 696, respectively. the section “[Organizational Charts or Tree Diagrams](#)” on page 696 describes the layout of the diagram when the **TREE** option is specified.

## Format of the Display

As explained in the previous section, the layout of the network is determined by the procedure in terms of *x* and *y* coordinates on a grid as shown in [Figure 9.7](#). The distance between nodes and the width and height of each node is determined by the values of the format control options: **XBETWEEN=**, **YBETWEEN=**, **BOXHT=**, and **BOXWIDTH=**. Note that if the **ROTATETEXT** option is specified (in graphics mode), then the definitions of the **BOXHT=** and **BOXWIDTH=** options are reversed.

The amount of information that is displayed within each node is determined by the variables specified by the **ID=** option, the number of default variables found in the **Network** data set, and whether the **NOLABEL** and **NODEFID** options are specified. The values of the variables specified by the **ID=** option are placed within each node on separate lines. If the **NOLABEL** option is in effect, only the values of the variables are written; otherwise, each value is preceded by the name of the **ID** variable truncated to three characters. Recall from the section “[Syntax: NETDRAW Procedure](#)” on page 668 that, in addition to the variables specified using the **ID=** option, the procedure also displays additional variables. These variables are displayed below the variables explicitly specified by the **ID=** option, in pre-determined relative positions within each node (see [Table 9.3](#).)

**Table 9.3** Display Format for the Variables within Each Node

ID1		
.		
.		
.		
ID <i>n</i>		
	Activity variable	Duration variable
E_START	E_FINISH	
L_START	L_FINISH	
S_START	S_FINISH	
A_START	A_FINISH	
T_FLOAT	F_FLOAT	

**NOTE:** If a node is identified as a successor (through a **SUCCESSOR** variable) and is never identified with the **ACTIVITY** variable, the ID values for this node are never defined in any observation; hence, this node will have missing values for all the ID variables.

If the **SHOWSTATUS** option is specified and the **Network** data set contains progress information (in either the **STATUS** variable or the **A\_START** and **A\_FINISH** variables), the procedure appropriately marks each node referring to activities that are completed or in progress. See [Example 9.8](#) for an illustration of the **SHOWSTATUS** option.

The features just described pertain to all three modes of the procedure. In addition, there are options to control the format of the display that are specific to the mode of invocation of the procedure. For graphics quality network diagrams, you can choose the color and pattern used for each node separately by specifying a different pattern number for the **PATTERN** variable, identified in the **ACTNET** statement (for details, see the section “[Graphics Version](#)” on page 700). For line-printer or full-screen network diagrams, the **FORMCHAR=** option enables you to specify special boxing characters that enhance the display; for full-screen network diagrams, you can also choose the color of the nodes using the **PATTERN=** option.

By default, all arcs are drawn along the center track between two consecutive nodes. The **SEPARATEARCS** option, which is available in the graphics version, separates arcs in the same corridor by drawing them along separate tracks, thus preventing them from being drawn on top of each other.

If the network fits on one page, it is centered on the page; in the graphics mode, you can use the **NOVCENTER** option to prevent centering in the vertical direction so that the network is drawn immediately below the title. If the network cannot fit on one page, it is split onto different pages appropriately. See the section “[Page Format](#)” on page 691 for a description of how the pages are split.

## Page Format

**Figure 9.8** Page Layout

7	8	9
4	5	6
1	2	3

As explained in the section “[Format of the Display](#)” on page 690, if the network fits on one page, it is centered on the page (unless the **NOVCENTER** option is specified); otherwise, it is split onto different pages appropriately, and each page is drawn starting at the bottom left corner. If the network is drawn on multiple pages, the procedure numbers each page of the diagram on the top right corner of the page. The pages are numbered starting with the bottom left corner of the entire picture. Thus, if the network diagram is broken

into three horizontal and three vertical levels and you want to paste all the pieces together to form one picture, they should be arranged as shown in [Figure 9.8](#).

The number of pages of graphical output produced by the NETDRAW procedure depends on several options such as the **NXNODES=**, **NYNODES=**, **HPAGES=**, **VPAGES=**, **COMPRESS**, **PCOMPRESS**, **HEIGHT=**, and the **ID=** options. The value of the **HTEXT=** option and the number of variables specified in the **ID=** options determines the size of each node in the network diagram, which in turn affects the number of horizontal and vertical pages needed to draw the entire network. The number of pages is also affected by the global specification of the **HPOS=**, **VPOS=**, **HSIZE=**, and **VSIZE=** graphics options.

The **COMPRESS** and **PCOMPRESS** options force the entire network diagram to be drawn on a single page. You can explicitly control the number of horizontal and vertical pages using the **HPAGES=** and **VPAGES=** options. The **NXNODES=** and **NYNODES=** options enable you to specify the number of nodes in the horizontal and vertical directions, respectively, on each page of the network diagram.

For examples of these options and how they affect the network diagram output, see [Example 9.5](#).

## Layout Data Set

The Layout data set produced by PROC NETDRAW contains all the information needed to redraw the network diagram for the given network data. In other words, the Layout data set contains the precedence information, the **ID** variables that are used in the current invocation of the procedure, and variables that contain the coordinate information for all the nodes and arcs in the network.

The precedence information used by the procedure is defined by two new variables named **\_FROM\_** and **\_TO\_**, which replicate the **ACTIVITY** and **SUCCESSOR** variables from the **Network** data set. Note that the Layout data set has only one **\_TO\_** variable even if the Network data set has multiple **SUCCESSOR** variables; if a given observation in the Network data set defines multiple successors for a given activity, the Layout data set defines a new observation for each of the successors. In fact, for each (node, successor) pair, a sequence of observations, defining the turning points of the arc, is saved in the Layout data set; the number of observations corresponding to each pair is equal to one plus the number of turns in the arc connecting the node to its successor. Suppose that a node ‘C’ has two successors, ‘D’ and ‘E,’ and the arcs connecting ‘C’ and ‘D’ and ‘C’ and ‘E’ are routed as shown in [Figure 9.7](#). Then, [Table 9.4](#) illustrates the format of the observations corresponding to the two (**\_FROM\_**, **\_TO\_**) pairs of nodes, (‘C’, ‘D’) and (‘C’, ‘E’).

**Table 9.4** Sample Observations in the Layout Data Set

<b>_FROM_</b>	<b>_TO_</b>	<b>_X_</b>	<b>_Y_</b>	<b>_SEQ_</b>	<b>_PATTERN</b>	ID variables
C	D	3	1	0	1	
C	D	3.5	1	1	.	
C	D	3.5	2.5	2	.	
C	D	5.5	2.5	3	.	
C	D	5.5	3	4	.	
C	E	3	1	0	1	
		.		.	.	
		.		.	.	
		.		.	.	

For every (node, successor) pair, the first observation (`_SEQ_ = '0'`) gives the coordinates of the predecessor node; the succeeding observations contain the coordinates of the turning points of the arc connecting the predecessor node to the successor. The data set also contains a variable called `_PATTERN`, which contains the pattern number that is used for coloring the node identified by the `_FROM_` variable. The value of this variable is missing for observations with `_SEQ_ > 0`.

## Controlling the Layout

As explained in the section “[Layout of the Network](#)” on page 688, the procedure uses the precedence constraints between the activities to draw a reasonable diagram of the network. A very desirable feature in any procedure of this nature is the ability to change the default layout. PROC NETDRAW provides two ways of modifying the network diagram:

- using the full-screen interface
- using the [Network](#) data set

The full-screen method is useful for manipulating the layout of small networks, especially networks that fit on a handful of screens. You can use the full-screen mode to examine the default layout of the network and move the nodes to desired locations using the `MOVE` command from the command line or by using the appropriate function key. When a node is moved, the procedure reroutes all the arcs that connect to or from the node; other arcs are unchanged. For details about the `MOVE` command, see the section “[Full-Screen Version](#)” on page 697.

You can use the [Network](#) data set to modify or specify completely the layout of the network. This method is useful if you want to draw the network using information about the network layout that has been saved from an earlier invocation of the procedure. Sometimes you may want to specify only the positions of the node and let the procedure determine the routing of the arcs. The procedure looks for three default variables in the data set: `_X_`, `_Y_`, and `_SEQ_`. The `_X_` and `_Y_` variables are assumed to denote the *x* and *y* coordinates of the nodes and all the turning points of the arcs connecting the nodes. The variable `_SEQ_` is assumed to denote the order of the turning points. This interpretation is consistent with the values assigned to the `_X_`, `_Y_`, and `_SEQ_` variables in the [Layout](#) data set produced by PROC NETDRAW. If there is no variable called `_SEQ_` in the data set, the procedure assumes that only the node positions are specified and uses the specified coordinates to place the nodes and determines the routing of the arcs corresponding to these positions. If there is a variable called `_SEQ_`, the procedure requires that the turning points for each arc be specified in the proper order, with the variable `_SEQ_` containing numbers sequentially starting with 1 and continuing onward. The procedure then draws the arcs exactly as specified, without checking for consistency or interpolating or extrapolating turning points that may be missing.

The `ALIGN=` variable provides another means of controlling the node layout (see the section “[Time-Scaled Network Diagrams](#)” on page 694). This variable can be used to specify the *x* coordinates for the different nodes of the network; the procedure then determines the *y* coordinates. Note that time-scaled network diagrams (without an `ALIGN=` specification) are equivalent to network diagrams drawn with the `ALIGN=` variable being set to the `E_START` variable.

You can also control the placement of the nodes using the `ZONE=` option (see the section “[Zoned Network Diagrams](#)” on page 696). The procedure uses the values of the `ZONE` variable to divide the network into

horizontal zones. Thus, you can control the horizontal placement of the nodes using the **ALIGN=** option and the vertical placement of the nodes using the **ZONE=** option.

For networks that have a tree structure, the **TREE** option draws the network as a tree, thus providing another layout option (see the section “[Organizational Charts or Tree Diagrams](#)” on page 696). The procedure draws the tree from left to right, with the root at the left edge of the diagram. Thus, the children of each node are drawn to the right of the node. In the graphics mode of invocation, you can use the **ROTATETEXT** option in conjunction with the **ROTATE** option in the **ACTNET** statement (or the global graphics option **ROTATE**) to obtain a top-down tree diagram.

## Time-Scaled Network Diagrams

By default, PROC NETDRAW uses the topological ordering of the activity network to determine the *x* coordinates of the nodes. As a project progresses, you may want to display the activities arranged according to their time of occurrence. Using the **TIMESCALE** option, you can draw the network with a time axis at the top and the nodes aligned according to their early start times, by default. You can use the **ALIGN=** option to specify any of the other start or finish times in the **Network** data set. In fact, PROC NETDRAW enables you to align the nodes according to any numeric variable in the data set.

If the **TIMESCALE** option is specified without any **ALIGN=** specification, the procedure chooses one of the following variables as the **ALIGN=** variable: **E\_START**, **L\_START**, **S\_START**, or **A\_START**, in that order. The first of these variables that is found is used to align the nodes. The minimum and maximum values of the **ALIGN=** variable are used to determine the time axis. The format of this variable is used to determine the default value for the **MININTERVAL=** option. The value of the **MININTERVAL=** option (or the default value) is used to determine the format of the time axis. You can override the format based on *mininterval* by specifying the desired format for the **ALIGN=** variable (using the **FORMAT** statement to indicate a standard SAS format or a special user-defined format) and the **USEFORMAT** option in the **ACTNET** statement. [Table 9.5](#) lists the valid values of *mininterval* corresponding to the type of the **ALIGN=** variable and the default format corresponding to each value of *mininterval*. For each value in the first column, the first value of *mininterval* listed is the default value of the **MININTERVAL=** option corresponding to that type of the **ALIGN=** variable.

Several options are available in PROC NETDRAW to control the spacing of the nodes and the scaling of a time-scaled network diagram:

- The **MININTERVAL=** option enables you to scale the network diagram: one tick mark is associated with one unit of *mininterval*. Thus, if *mininterval* is DAY, each column is used to represent one day and all activities that start on the same day are placed in the same column. By default, the procedure omits any column (tick mark) that does not contain any node.
- The **LINEAR** option enables you to print a tick mark corresponding to every day (or the unit of *mininterval*). Note that, for a project that has few activities spread over a large period of time, the **LINEAR** option can lead to a network diagram that is very wide.
- The **MAXNULLCOLUMN=** option specifies the maximum number of empty columns that is allowed between two consecutive nonempty columns. The **LINEAR** option is equivalent to specifying *maxncol* = infinity, while the default time-scaled network diagram is drawn with *maxncol* = 0.

- The **NLEVELSPERCOLUMN=** option enables you to contract the network diagram by combining a few columns. For example, if *mininterval* is DAY and *nlevelspercol* is 7, each column contains activities that start within seven days of each other; note that the same effect can be achieved by setting *mininterval* to be WEEK.

**Table 9.5** MININTERVAL Values and Axis Format

ALIGN Variable Type	MININTERVAL	Axis Label Format
number		numeric format
SAS time	HOUR	HHMM5.
	MINUTE	HHMM5.
	SECOND	TIME8.
SAS date	DAY	DATE7.
	WEEKDAY	DATE7.
	WEEK	DATE7.
	MONTH	MONYY5.
	QTR	MONYY5.
	YEAR	MONYY5.
SAS datetime	DTDAY	DATE7.
	WORKDAY	DATE7.
	DTWRKDAY	DATE7.
	DTSECOND	DATETIME16.
	DTMINUTE	DATETIME16.
	DTHOUR	DATETIME13.
	DTWEEK	DATE7.
	DTMONTH	MONYY5.
	DTQTR	MONYY5.
	DTYEAR	MONYY5.

The node-placement algorithm described in the section “[Layout of the Network](#)” on page 688 is modified slightly for time-scaled network diagrams. The *x* coordinate of each node is determined by the value of the ALIGN= variable. The scaling options just described are used to determine the tick mark corresponding to the node. The *y* coordinate is determined as before. Once the node placement is completed, the arc routing algorithm is the same as described earlier.

**NOTE:** Since the node placement for time-scaled networks is determined by the ALIGN= variable, it is possible that some of the arcs between the nodes may have to be routed from right to left instead of from left to right; in other words, there may be some backward arcs. Note also that, if the ALIGN= variable is used to determine the *x* coordinates of the nodes, the procedure can also draw networks that contain cycles (see the second part of [Example 9.12](#)).

Several other options are available to control the appearance of time-scaled network diagrams: AUTOREF, BRKCHAR=, CAXIS=, CREF=, CREFBRK=, FRAME, LREF=, LREFBRK=, NOREPEATAxis, NOTIMEAIXS, REFBREAK, REFCHAR=, and SHOWBREAK. These options are described in the section “[Syntax: NETDRAW Procedure](#)” on page 668.

---

## Zoned Network Diagrams

Most projects have at least one natural classification of the different activities in the project: department, type of work involved, location of the activity, and so on. The **ZONE=** option enables you to divide the network diagram into horizontal bands or zones corresponding to this classification. The procedure uses the following rules to place the nodes in a zoned network diagram:

- The values of the ZONE variable are used to define as many zones as there are distinct values of this variable.
- Each node of the network is drawn within its corresponding zone.
- The number of rows within each zone is determined by the maximum number of nodes in any given column that correspond to that zone.
- The values of the ZONE variable do not need to be sorted in any particular order, nor do they need to be grouped by distinct values.
- The zones are ordered according to the order of appearance of the different values of the ZONE variable in the **Network** data set. This enables you to choose any order for the zone values.
- For arcs that connect two nodes within the same zone, the arc lies entirely within the zone; in other words, all the turning points of the arc have y coordinates that are between the minimum and maximum y coordinates for the zone.
- Each zone is labeled by the value of the ZONE variable unless the **NOZONELABEL** option is specified.
- Each zone is separated from the next by a horizontal line drawn across the width of the network unless the **NOZONELABEL** option is specified.
- In the graphics and full-screen modes of invocation of the procedure, you can use the **ZONEPAT** option to color the nodes in each zone differently using different pattern statements. In the graphics mode, the first zone uses the first PATTERN statement, the second zone uses the second PATTERN statement, and so on; in full-screen mode, the colors available for the device are repeated in cyclic order. Note that the values of the **PATTERN** variable (or the default **\_PATTERN** variable, if it exists in the **Network** data set) override the node patterns dictated by the **ZONEPAT** option.

---

## Organizational Charts or Tree Diagrams

The NETDRAW procedure automatically draws any acyclic network; it does not have to be a representation of a project. You can also use the procedure to draw a general directed graph that has cycles, if node location is specified or if the **BREAKCYCLE** option is specified. The procedure attempts to draw the network in a compact fashion, which may not always produce the expected result. Trees form one such class of directed graphs that have an inherent natural layout that may not be produced by the default layout of PROC NETDRAW. The **TREE** option in the **ACTNET** statement exploits the tree structure of the network by laying the nodes out in the form of a tree.

A directed graph is said to be a tree if it has a root and there is a unique directed path from the root to every node in the tree. An equivalent characterization of a tree is that the root node has no predecessors and every other node has exactly one predecessor (Even 1979). Typical examples of trees that arise in project management are organizational charts or work breakdown structures. If the TREE option is specified, the NETDRAW procedure checks if the network has a tree structure and draws the network with the root at the left edge of the diagram and the children of each node appearing to the right of the node. In other words, the tree is drawn from left to right.

The NETDRAW procedure enables you to specify multiple trees in the same **Network** data set; each tree is drawn separately in the same diagram with all the roots appearing at the left edge of the diagram. Thus, you can use the TREE option as long as every node in the network has *at most* one predecessor. If you specify the TREE option and some node has multiple predecessors, the TREE option is ignored and the procedure uses the default node-layout algorithm.

There are several features that control the appearance of the tree:

- The children of each node are placed in the order of occurrence in the **Network** data set. The  $(x, y)$  coordinates of each node are required to be integers. The procedure attempts to place each node at the center of all its children, subject to the requirement that the coordinates must be integers. This requirement may cause some of the nodes to be positioned slightly off-center. See [Example 9.15](#).
- The **SEPARATESONS** option separates the children of a node, if necessary, to enable the parent node to be exactly centered with respect to its children. See the second part of [Example 9.15](#).
- The **CENTERSUBTREE** option can be used to center each node with respect to the entire subtree originating from the node instead of centering it with respect to its children.
- In graphics mode, you can change the orientation of the network to be from top to bottom instead of from left to right. To do so, use the **ROTATETEXT** option in the ACTNET statement to rotate the text within the nodes and the **ROTATE** option in the ACTNET statement (or the ROTATE global graphics option) to rotate the entire diagram by 90 degrees. See [Example 9.18](#) for an illustration of this feature.

## Full-Screen Version

You can invoke PROC NETDRAW in full-screen mode by specifying FS (or FULLSCREEN) in the PROC NETDRAW statement. The statement specifications are the same as for the line-printer mode. The full-screen mode offers you a convenient way to browse the network diagram of the project and change the layout of the network by moving the nodes of the network to desired locations. However, you cannot move a node to any position that violates the precedence constraints that must be satisfied by the node. In other words, you cannot move a node to the left of any of its predecessors or to the right of any of its successors. For time-scaled network diagrams, you cannot move a node out of the column corresponding to the value of the ALIGN= variable. For zoned network diagrams you cannot move a node out of its zone.

The format control options are treated in the same way as for the line-printer version, with some minor changes. It is assumed that the main purpose of invoking the procedure is to gain a general picture of the layout of the entire network and to modify it to some extent. In an effort to display as much of the network as possible, the initial display on the screen is drawn with only one row and three columns for each node. In other words, the **BOXHT=**, **BOXWIDTH=**, **XBETWEEN=**, and **YBETWEEN=** options are ignored by the

procedure in drawing the initial display. However, the full-screen commands supported by PROC NETDRAW enable you to change the scale of the diagram. You can display as much or as little information within each node by invoking the SCALE ROW or the SCALE COL command or both. The SCALE MAX command causes the procedure to display the diagram using the values specified in the ACTNET statement or the dimensions that would be required to display all the ID information, whichever is larger. The SCALE RESET command returns the scaling to the initial values used for display.

The nodes of the network are color coded on the basis of the PATTERN variable. If there is no PATTERN variable, then the nodes are color coded depending on whether the activities are normal, critical, or supercritical. The nodes are drawn in reverse video. By default, the nodes are drawn without an outline; however, there is an OUTLINE command that lets you toggle back and forth between an outlined or non-outlined node. Using an outline for the node is useful if you want to obtain a printout of the screen display using SPRINT; it helps mark the boundary of each node clearly.

## Commands

Table 9.6 lists the commands that can be invoked from the command line in the full-screen version of PROC NETDRAW. These commands are explained in greater detail in this section.

**Table 9.6** Full-Screen Commands and Their Purposes

<b>Scrolling</b>	<b>Controlling Display</b>	<b>Changing Network Layout</b>	<b>Exiting</b>
BACKWARD	OUTLINE	CLEAR	GEND
FORWARD	SCALE	MOVE	END
LEFT			CANCEL
RIGHT			
TOP			
BOTTOM			
VSCROLL			
HSCROLL			

### BACKWARD

scrolls toward the top of the network by the VSCROLL amount. BACKWARD MAX scrolls to the top of the network. You can specify the vertical scroll amount for the current command as BACKWARD PAGE | HALF | *n*.

### BOTTOM

scrolls to the bottom of the network.

### CANCEL

ends the current invocation of the procedure.

### CLEAR

clears any outstanding move commands.

**GEND**

ends the current invocation of the procedure after drawing the network in graphics mode with the compress option.

**END**

ends the current invocation of the procedure.

**FORWARD**

scrolls toward the bottom of the network by the VSCROLL amount. FORWARD MAX scrolls to the bottom of the network. You can also specify the vertical scroll amount for the current command as FORWARD PAGE | HALF | *n*.

**HELP**

displays a help screen listing all the full-screen commands specific to PROC NETDRAW.

**HOME**

moves the cursor to the command line.

**HSCROLL**

sets the amount that information scrolls horizontally when you execute the LEFT or RIGHT command. The format is HSCROLL PAGE | HALF | *n*. The specification is assumed to be in number of horizontal levels. HSCROLL PAGE sets the scroll amount to be the number of horizontal levels that fit on one screen; HSCROLL HALF is half that amount; HSCROLL *n* sets the horizontal scroll amount to *n* levels.

**KEYS**

displays current function key settings for the NETDRAW procedure.

**LEFT**

scrolls toward the left boundary of the network by the HSCROLL amount. LEFT MAX scrolls to the left boundary. You can specify the horizontal scroll amount for the current command as LEFT PAGE | HALF | *n*.

**MOVE**

specifies a node to be moved or a place to move a node to. You can specify these in any order. Thus, you can first position the cursor on the node that you want to move, issue the MOVE command, and then position the cursor at a target position and issue the MOVE command again. If the target position is valid, the node is moved. You can also first specify the target position and then indicate the node that is to be moved.

**NOTE:** For a standard network, a node cannot be moved to any position that violates the topological ordering of the nodes in the network. For time-scaled network diagrams, you cannot move a node to a level corresponding to a different tick mark. For zoned network diagrams, you cannot move a node out of its zone.

**OUTLINE**

causes an outline to be drawn around each node in the network. This is useful if you want to print a copy of the screen by using the SPRINT command. The OUTLINE command works like an on/off switch: you can turn it off by entering the command again.

**RIGHT**

scrolls toward the right boundary of the network by the HSCROLL amount. RIGHT MAX scrolls to the right boundary. You can also specify the horizontal scroll amount for the current command as RIGHT PAGE | HALF | *n*.

**SCALE**

controls the scaling of the nodes and the space between nodes. The format of this command is SCALE MAX | MIN | RESET | ROW MAX | COL MAX | ROW MIN | COL MIN | ROW *n* | COL *n* | +*n* | -*n*. The number *n* denotes the number of character positions. SCALE MIN displays as many nodes on the screen as can fit. SCALE MAX enables as many rows and columns per node as is required to display all the information that pertains to it. SCALE ROW MAX displays the maximum number of rows per node. SCALE COL MAX displays the maximum number of columns per node. SCALE ROW *n* sets the number of rows per node to *n*. SCALE ROW +*n* increases the number of rows per node by *n*. SCALE COL *n* sets the number of columns per node to *n*. SCALE COL +*n* increases the number of columns per node by *n*. SCALE RESET sets the values to be the same as for the initial display. Note that none of these values can be greater than the dimensions of the screen.

**TOP**

scrolls to the top of the network.

**VSCROLL**

sets the amount by which information scrolls vertically when you execute the BACKWARD or FORWARD command. The format is VSCROLL PAGE | HALF | *n*. The specification is assumed to be in number of vertical levels. VSCROLL PAGE sets the scroll amount to be the number of vertical levels that fit on one screen; VSCROLL HALF is half that amount; VSCROLL *n* sets the vertical scroll amount to *n* levels.

## Full-Screen Global Commands

Most of the global commands used in SAS/FSP software are also valid with PROC NETDRAW. Some of the commands used for printing screens are described in the section “Global Commands” on page 534 in Chapter 8, “The GANTT Procedure.”

## Graphics Version

Several options are available in the ACTNET statement to enhance the appearance of the network diagram in graphics mode. These are described in the section “Graphics Options” on page 679. The format control options **BOXWIDTH=**, **BOXHT=**, **XBETWEEN=**, and **YBETWEEN=** are also valid in this mode and can be used to control the width and height of each node and the distance between the nodes. These parameters are specified in terms of number of character cell positions. The number of positions available on one page depends on the graphics device that is used; thus, if a plotter is used with large paper, more of the network will be drawn on a single page. Further, you can control the number of character cell positions on a page by changing the values of the global graphics options (HPOS= and VPOS=). Note that the NETDRAW procedure is not supported with the ActiveX or Java series of devices on the GOPTIONS statement.

You can also control the number of nodes on a given page by specifying the **NXNODES=** and **NYNODES=** options. The **HPAGES=** and **VPAGES=** options control the number of pages in the horizontal and vertical

directions. Thus, you have a wide degree of control over the amount of information displayed on each page of the network diagram.

Another option that is available in graphics mode to control the appearance of your network diagrams is the specification of a **PATTERN** variable in the ACTNET statement. If the variable is named **\_PATTERN**, you do not need to use the **PATTERN=** option; the procedure looks for such a variable by default. You can use this variable to specify the **PATTERN** definition that is to be used for filling each node of the network. Note that if the value of the **\_PATTERN** variable is *j* for a particular node, PROC NETDRAW uses the specifications in the *jth generated PATTERN definition*, not the specifications in the **PATTERNj statement**.

The patterns that can be used with PROC NETDRAW are any of the patterns that can be used for drawing bars (not ones that are used for drawing maps). However, for the text to be visible, you may want to restrict the patterns used to be empty and change only the color of the pattern. You can also use solid fills with a light color and specify the **COUTLINE=** and **CCRITOUT=** options to mark noncritical and critical nodes with different colors for the outline.

See *SAS/GRAF Software: Reference* for details about creating, canceling, reviewing, and altering **PATTERN** definitions. For a brief description of the **PATTERN** statement and for a list of available patterns, see Chapter 8, “The GANTT Procedure.”

If a **PATTERN** variable is not specified, the procedure uses the values of the **E\_FINISH** and **L\_FINISH** variables (if these variables exist in the **Network** data set) to determine if activities in the project are normal, critical, or supercritical. The procedure then uses the first *generated PATTERN definition* to fill the nodes corresponding to noncritical activities, the second *generated PATTERN definition* for nodes corresponding to critical activities, and the third *generated PATTERN definition* for nodes corresponding to supercritical activities.

For zoned network diagrams, if there is no **PATTERN** variable, the **ZONEPAT** option enables you to color the nodes based on the values of the **ZONE=** variable.

## Using the Annotate Facility

The Annotate facility enables you to enhance graphics output produced by PROC NETDRAW. To use this facility, you must create an Annotate data set, which contains a set of graphics commands that can be superimposed on the network diagram. This data set has a specific format and must contain key variables as described in *SAS/GRAF Software: Reference*. The chapter entitled “The Annotate Data Set” lists the variables that are required in this data set and explains the coordinate systems used by the Annotate facility. The present section explains the use of data coordinates specifically with reference to the NETDRAW procedure.

When annotating a graph produced by any of the graphics procedures, it is helpful to use data coordinates that refer to the data values corresponding to the graph that is being annotated. For example, if you want to label a particular node of a network diagram with additional text, you can position the text accurately if you use data coordinates instead of screen coordinates. With respect to PROC NETDRAW, the Annotate facility uses the **\_X\_** and **\_Y\_** values in the Layout data set as the basis for the data coordinate system. To use this feature, you can invoke PROC NETDRAW (with the **NODISPLAY** option, if necessary) for the given network to produce the Layout data set that contains the **\_X\_** and **\_Y\_** coordinates for each node of the network. This data set can then be used to create the required Annotate data set containing the graphics commands positioning the primitives appropriately on the diagram using the data coordinates. See [Example 9.16](#) and [Example 9.17](#) for illustrations of this feature.

**NOTE:** The data coordinate system enables you to annotate the graph even if it spans multiple pages. However, each annotation must be entirely contained within a given page. For example, you cannot annotate a line on the network diagram that runs from one page of the diagram to another.

## Web-Enabled Network Diagrams

The **WEB** variable enables you to define a HTML reference for each activity. This HTML reference is associated with the node corresponding to the activity. The WEB variable is a character variable and the values need to be of the form “HREF=htmlpage”.

In addition, you can also store the coordinate and link information defined by the WEB= option in a SAS data set by specifying the **IMAGEMAP=** option in the **PROC NETDRAW** statement. By processing this SAS data set using a DATA step, you can generate customized HTML pages for your network diagram.

## Macro Variable \_ORNETDR

The NETDRAW procedure defines a macro variable named \_ORNETDR. This variable contains a character string that indicates the status of the procedure. It is set at procedure termination. The form of the \_ORNETDR character string is STATUS= REASON= , where STATUS= is either SUCCESSFUL or ERROR\_EXIT and REASON= (if PROC NETDRAW terminated unsuccessfully) can be one of the following:

- CYCLE
- BADDATA\_ERROR
- MEMORY\_ERROR
- IO\_ERROR
- SEMANTIC\_ERROR
- SYNTAX\_ERROR
- NETDRAW\_BUG
- UNKNOWN\_ERROR

This information can be used when PROC NETDRAW is one step in a larger program that needs to determine whether the procedure terminated successfully or not. Because \_ORNETDR is a standard SAS macro variable, it can be used in the ways that all macro variables can be used.

In addition to providing the “STATUS= REASON= ” string that indicates the status of the procedure, the macro variable \_ORNETDR also provides some information about the network diagram produced by the current invocation of PROC NETDRAW.

The information given in \_ORNETDR is described in the following list, along with the keyword that identifies it. These values refer to those actually used in producing the network diagram and are not necessarily the same as those specified in the invocation of the procedure.

- HPAGES= The number of horizontal pages
- VPAGES= The number of vertical pages
- SEGNAME= The name of the first network diagram segment in graphics mode

**NOTE:** Some of the information might be redundant or predictable in certain display modes. For example, the value of the SEGNAME= option is empty in line-printer and full-screen modes. The values of the HPAGES= and VPAGES= options are equal to 1 in full-screen mode.

## Computer Resource Requirements

There is no inherent limit on the size of the network that you can draw with the NETDRAW procedure. Naturally, a sufficient amount of core memory must be available in order to invoke and initialize the SAS system. Furthermore, the amount of memory that is required depends on the mode of invocation of the procedure. The procedure attempts to store all the data in core memory. However, if the problem is too large to fit in core memory, the procedure resorts to using utility data sets and swaps between core memory and utility data sets as necessary.

The storage requirement for the data area that the procedure requires is proportional to the number of nodes and arcs in the network. You can further increase the memory that is required by specifying the **DP** option in the **ACTNET** statement. Recall that the DP option requests the use of a dynamic programming algorithm to route the arcs between the nodes, and such algorithms tend to grow exponentially with the size of the problem being solved.

## ODS Style Templates

ODS style templates, or *styles*, control the overall look of your output. An ODS style template consists of a set of *style elements*. A style element is a collection of *style attributes* that apply to a particular feature or aspect of the output. You can specify a value for each attribute in a style. See Chapter 21, “Statistical Graphics Using ODS” (*SAS/STAT User’s Guide*), for a thorough discussion of ODS Graphics.

To create your own style or to modify a style for use with ODS Graphics, you need to understand the relationships between style elements and graph features. This information is provided in the ODS Graphics documentation at <http://support.sas.com/documentation/onlinedoc/base/>. You can create and modify style templates with the TEMPLATE procedure. For more information, see the section “TEMPLATE Procedure: Creating a Style Template” in the *SAS Output Delivery System: User’s Guide*. Kuhfeld (2010) also offers detailed information and examples.

## PROC NETDRAW Style Template

A predefined ODS style template named NETDRAW is available for the NETDRAW procedure. You can use the template to maintain a consistent appearance in all graphical output produced by the procedure.

To change the current style, specify the **STYLE=** option in an ODS destination statement. The specified style is applied to all output for that destination until you change or close the destination or start a new SAS session. For example, the following statement specifies that ODS should apply the NETDRAW style template to all HTML output:

```
ods html style=netdraw;
```

To disable the use of graphical styles, specify the SAS system option NOGSTYLE.

The parent style template for the NETDRAW style is the DEFAULT style. Table 9.7 lists the style elements (in bold) and corresponding attributes specified in the NETDRAW style. The table also indicates which, if any, PROC NETDRAW options or graphics options (in a GOPTIONS statement) can be used to override the value of a style attribute.

**Table 9.7** Style Elements and Attributes in the NETDRAW Style

Element/Attributes	Description	NETDRAW Option	GOPTION
<b>GraphColors</b>	Colors of various graph features		
gdata1	Noncritical nodes or nodes in the first zone	PATTERN=, ZONEPAT	CPATTERN=, COLORS=
gdata2	Critical nodes or nodes in the second zone	PATTERN=, ZONEPAT	CPATTERN=, COLORS=
gdata3	Nodes in the third zone	PATTERN=, ZONEPAT	CPATTERN=, COLORS=
gdata4	Nodes in the fourth zone	PATTERN=, ZONEPAT	CPATTERN=, COLORS=
gdata5	Nodes in the fifth zone	PATTERN=, ZONEPAT	CPATTERN=, COLORS=
gdata6	Nodes in the sixth zone	PATTERN=, ZONEPAT	CPATTERN=, COLORS=
gdata7	Nodes in the seventh zone	PATTERN=, ZONEPAT	CPATTERN=, COLORS=
gdata8	Nodes in the eighth zone	PATTERN=, ZONEPAT	CPATTERN=, COLORS=
gdata9	Nodes in the ninth zone	PATTERN=, ZONEPAT	CPATTERN=, COLORS=
gdata10	Nodes in the tenth zone	PATTERN=, ZONEPAT	CPATTERN=, COLORS=
gdata11	Nodes in the eleventh zone	PATTERN=, ZONEPAT	CPATTERN=, COLORS=
gdata12	Nodes in the twelfth zone	PATTERN=, ZONEPAT	CPATTERN=, COLORS=
gaxis	Borderlines		COLORS=
greferencelines	Horizontal and vertical reference lines		COLORS=
gtext	Text		CTEXT=
gtextt	Title		CTITLE=
gadata	Arcs		COLORS=
<b>GraphFonts</b>	Fonts for various graph features		
GraphDataFont	Default		FTEXT=
GraphLabelFont	Annotation text		FTEXT=
GraphTitleFont	Title text		FTITLE=
<b>GraphAxisLines</b>	Attributes related to graph axes		
Color	GraphColors('gaxis')	CAXIS=	COLORS=
<b>GraphConnectLine</b>	Attributes related to arcs		
Color	GraphColors('gadata')	CARCS=, CCRITARCS=	COLORS=
<b>GraphReference</b>	Attributes related to horizontal and vertical reference lines		
Color	GraphColors('greferencelines')	CREF=, CREFBRK=	COLORS=
<b>GraphLabelText</b>	Attributes related to general text		
Color	GraphColors('gtext')	CTEXT=	CTEXT=
Font	GraphFonts('GraphDataFont')	FONT=	FTEXT=


**Table 9.7** (continued)

<b>Element/Attributes</b>	<b>Description</b>	<b>NETDRAW Option</b>	<b>GOPTION</b>
<b>GraphTitleText</b>	Attributes related to title text		
Color	GraphColors('gtextt')	CTITLE=	
Font	GraphFonts('GraphTitleFont')	FTITLE=	
<b>GraphTitle1Text</b>	Attributes related to the first title text		
Color	GraphColors('gtextt')	CTITLE=	
Font	GraphFonts('GraphTitleFont')	FTITLE=	
<b>GraphLabelText</b>	Attributes related to annotation text		
Color	GraphColors('glabel')	CTEXT=	
Font	GraphFonts('GraphLabelFont')	FTEXT=	
<b>GraphDataDefault</b>	Default values for the attributes specified in <a href="#">Table 9.8</a>		
Color	GraphColors('gdata')	COLORS=	
<b>GraphBackground</b>	Attributes related to graph background		
Image	Background image	CBACK=	

Attributes that you do not override retain the values specified in the style template.

[Figure 9.9](#) demonstrates features of the NETDRAW graphical style. The diagram in the figure is the first output from [Example 9.11](#).

**Figure 9.9** NETDRAW Style Template: Example

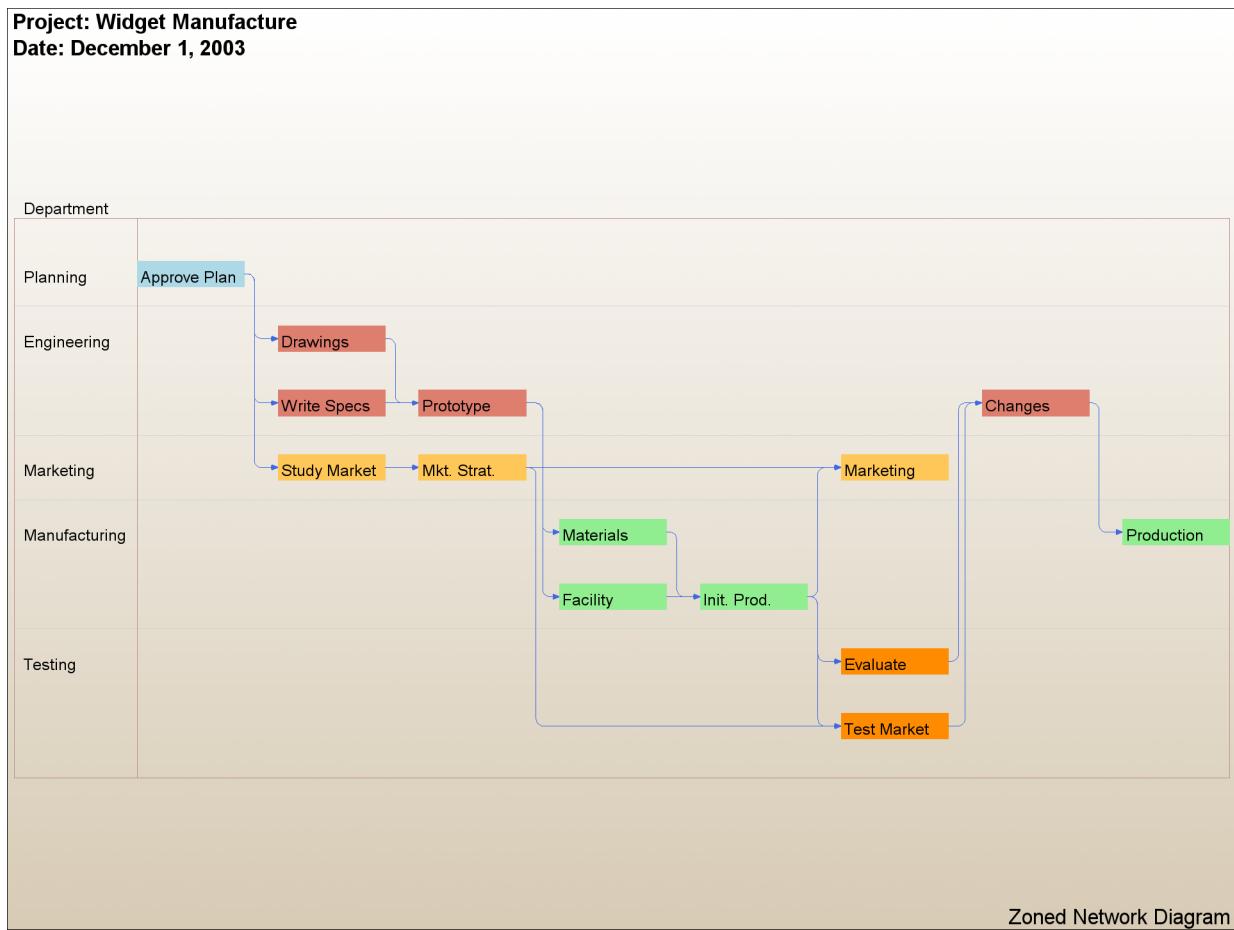

## Default Values

If the SAS system option GSTYLE is in effect (this is the default), then the default values of certain PROC NETDRAW options can depend on the current ODS style template. [Table 9.8](#) lists these PROC NETDRAW options and lists the order in which PROC NETDRAW searches for each option's default value. The order assumes that the GSTYLE system option is in effect; if that is not the case, then the steps that refer to ODS style templates are ignored. Names with arguments indicate style elements and attributes of the current ODS style template. For example, “GraphAxisLines('Color')” refers to the Color attribute of the GraphAxisLines element.

**Table 9.8** PROC NETDRAW Options: Search Orders for Default Values

<b>Option</b>	<b>Search Order for Default Value</b>
<b>CARCS=</b>	1. GraphConnectLine(Color) 2. The fourth color in the COLORS= list in the GOPTIONS statement
<b>CAXIS=</b>	1. GraphAxisLines(Color) 2. GraphDataDefault(Color) 3. The first color in the COLORS= list in the GOPTIONS statement
<b>CREF=</b>	1. GraphReference(Color) 2. GraphDataDefault(Color) 3. The first color in the COLORS= list in the GOPTIONS statement
<b>CREFBRK=</b>	1. GraphReference(Color) 2. GraphDataDefault(Color) 3. The first color in the COLORS= list in the GOPTIONS statement
<b>CTEXT=</b>	1. The value specified for the CTEXT= option in the GOPTIONS statement 2. GraphDataText(Color) 3. GraphDataDefault(Color) 4. The first color in the COLORS= list in the GOPTIONS statement
<b>FONT=</b>	1. The value specified for the FTEXT= option in the GOPTIONS statement 2. GraphDataText(Font) 3. The default hardware font for the graphics output device

---

## Examples: NETDRAW Procedure

This section contains 18 examples that illustrate several features of the NETDRAW procedure. Most of the examples use the data from the Widget Manufacturing Project described in Chapter 4, “The CPM Procedure.” Two tables, [Table 9.9](#) and [Table 9.10](#), at the end of this section list all the examples in this chapter and the options and statements in the NETDRAW procedure that are illustrated by each example.

---

### Example 9.1: Line-Printer Network Diagram

This example uses the data set WIDGET that was used in [Example 4.2](#) in Chapter 4, “The CPM Procedure,” to illustrate the Activity-on-Node representation of the project. The following program invokes PROC NETDRAW twice. First, the activity data set WIDGET is used as input to the procedure. The activity and successor information is identified using the ACTIVITY= and SUCCESSOR= options in the ACTNET statement. The LINEPRINTER option is specified, producing the line-printer network diagram shown in [Output 9.1.1](#).

```


data widget;
  format task $12. succ1-succ3 $12.;
  input task & days succ1 & succ2 & succ3 & ;
  datalines;
Approve Plan      5 Drawings          Study Market   Write Specs
Drawings          10 Prototype        .
Study Market     5 Mkt. Strat.     .
Write Specs       5 Prototype        .
Prototype         15 Materials        Facility
Mkt. Strat.      10 Test Market    Marketing
Materials         10 Init. Prod.     .
Facility          10 Init. Prod.     .
Init. Prod.       10 Test Market    Marketing   Evaluate
Evaluate          10 Changes          .
Test Market       15 Changes          .
Changes           5 Production       .
Production        0 .               .
Marketing         0 .               .
;


title 'Widget Manufacture';
options ps=32 ls=78;
proc netdraw data=widget lineprinter;
  actnet / activity=task successor=(succ1 succ2 succ3);
run;

```

**Output 9.1.1** Line-Printer Network Diagram

**Widget Manufacture**

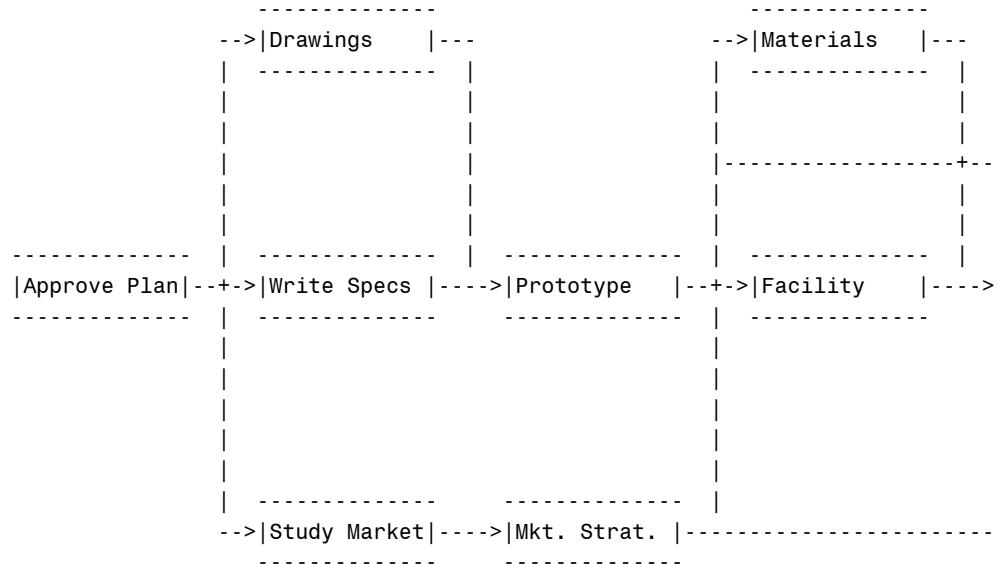

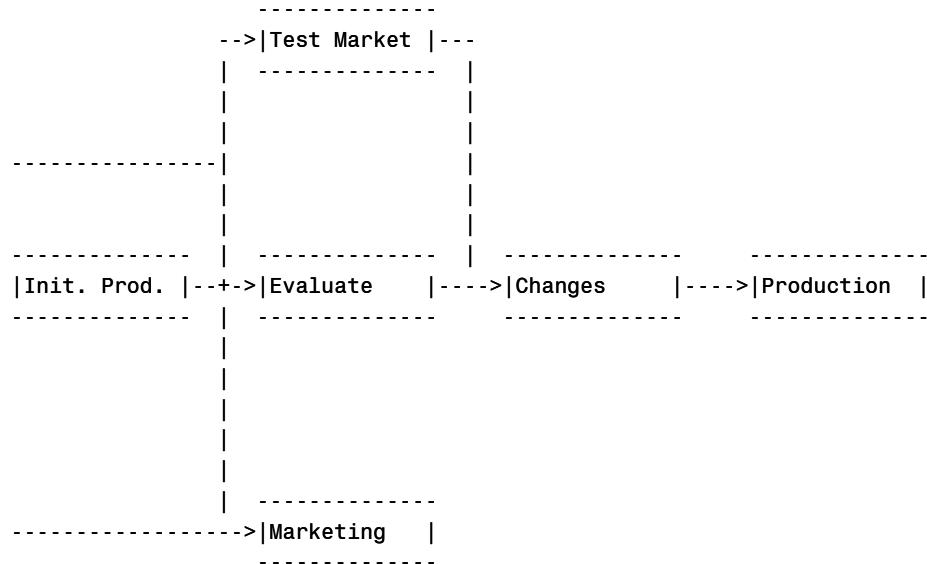**Output 9.1.1** *continued***Widget Manufacture**

Next, PROC CPM is invoked to schedule the project, and the resulting Schedule data set is used as input to the NETDRAW procedure. In addition to the ACTIVITY= and SUCCESSOR= options, the DURATION= option is used in the ACTNET statement. The DURATION= option adds the values of the DURATION variable within each node of the network. The procedure also displays the values of the E\_START, E\_FINISH, L\_START, L\_FINISH, T\_FLOAT, and F\_FLOAT variables within each node. The network is displayed in Output 9.1.2.


```


proc cpm data=widget out=sched
  date='1dec03'd;
  activity task;
  successor succ1 succ2 succ3;
  duration days;
  run;

options ps=45 ls=90;
title2 'Schedule Information';
proc netdraw data=sched lineprinter;
  actnet / activity=task
    successor=(succ1 succ2 succ3)
    duration = days;
  run;
  
```

## **Output 9.1.2 Project Schedule**

## Widget Manufacture Schedule Information

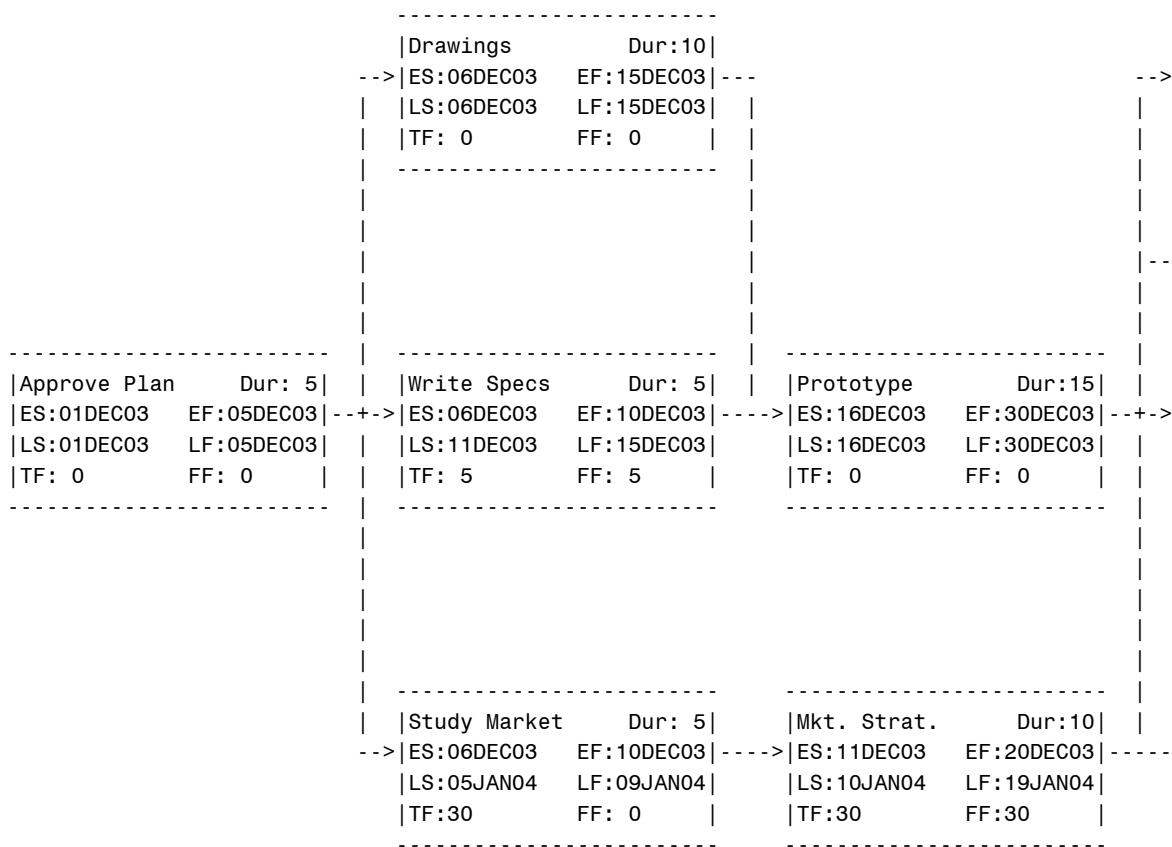

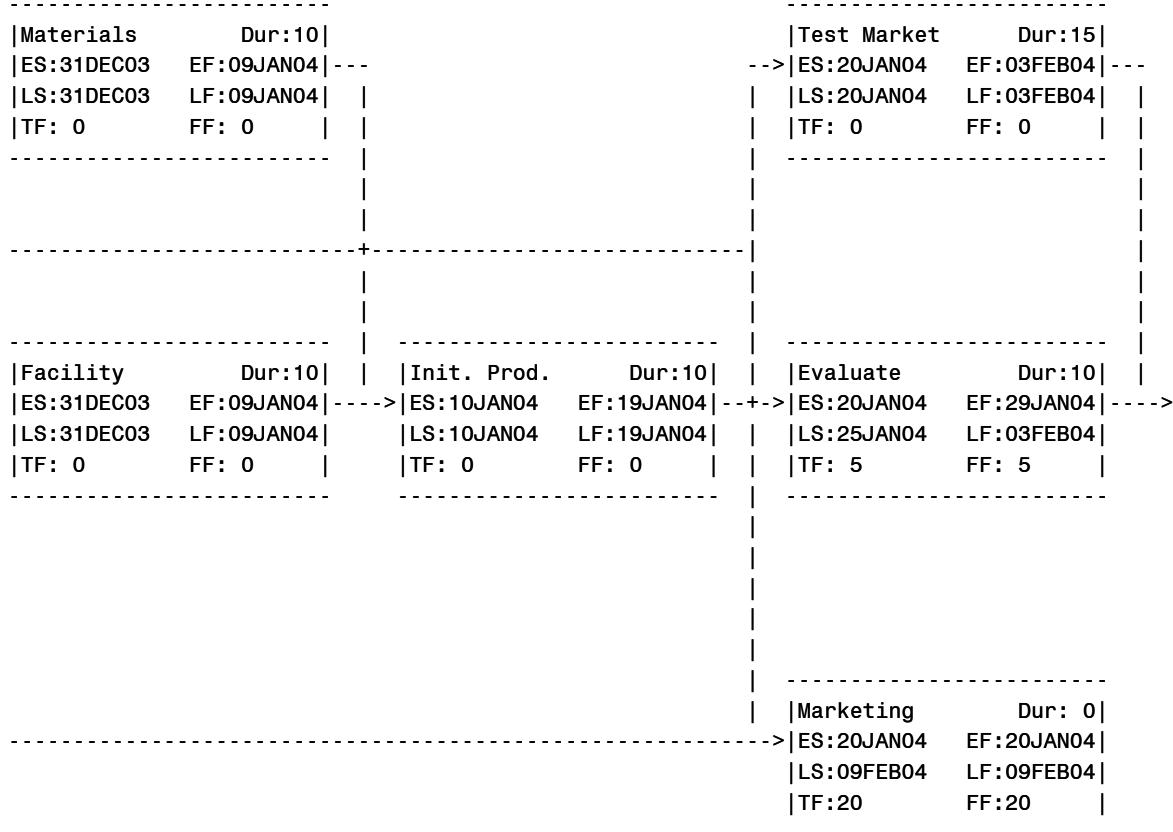**Output 9.1.2** *continued***Widget Manufacture  
Schedule Information**

**Output 9.1.2** *continued***Widget Manufacture  
Schedule Information**

Changes	Dur:	Production	Dur:
ES:04FEB04	EF:08FEB04	ES:09FEB04	EF:09FEB04
LS:04FEB04	LF:08FEB04	LS:09FEB04	LF:09FEB04
TF: 0	FF: 0	TF: 0	FF: 0

---

**Example 9.2: Graphics Version of PROC NETDRAW**

The same network used in [Example 9.1](#) is drawn here with the GRAPHICS option (which is also the default mode of output for the NETDRAW procedure). In this example, the network is drawn before scheduling the project with PROC CPM. The global options HPOS= and VPOS= are set to 100 and 70, respectively. These options control the number of character cell positions on the screen. The network is displayed in [Output 9.2.1](#). Note that all the nodes are the same color as specified by the PATTERN statement, the color of the arcs is blue as specified by the CARCS= option, the width of all lines is 3 as specified by the LWIDTH= option.


```

goptions hpos=100 vpos=70 border;
pattern1 c=green v=e;
title h=3 j=1 ' Project: Widget Manufacture';
proc netdraw data=widget graphics;
  actnet / act=task succ=(succ1 succ2 succ3)
    height=1.5 compress
    carcs=blue lwidth=3;
run;

```

Output 9.2.1 Project Network

## Project: Widget Manufacture

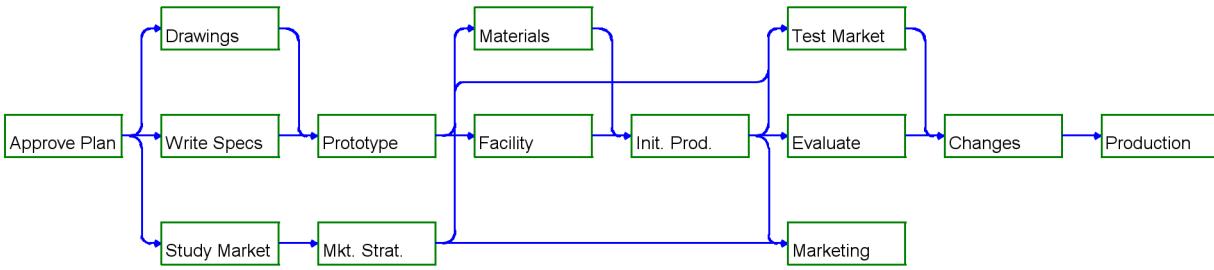


---

### Example 9.3: Spanning Multiple Pages

In this example, the Schedule data set produced by PROC CPM is displayed in a graphics network. As in the second part of Example 9.1, the procedure displays the duration as well as the early and late start and finish times and the total float and free float of each activity in the node corresponding to that activity. The network cannot fit on one page and is drawn across three pages, as shown in Output 9.3.1.

This example also illustrates several options for controlling the appearance of the network diagram. The pattern statements set a background fill color for all the nodes of the network (PATTERN1 and PATTERN2). The COUTLINE= and CCRITOUT= options set the outline colors for noncritical and critical activities, respectively. Recall that the procedure uses the values of the E\_FINISH and L\_FINISH variables to determine


if an activity is critical. The CARCS= and CCRITARCS= options color the regular arcs blue and the critical arcs (arcs connecting critical activities) red, respectively and the CTEXT= option sets the color of the text to blue. Finally, the LWIDTH= option sets the default width for all the lines in the network, and the LWCRIT= option further highlights the critical arcs by drawing them with thicker lines.


In this invocation of PROC NETDRAW, the SEPARATEARCS option is used so that the two parallel arcs leading into the activity ‘Test Market’ (one from ‘Mkt.Strat.’ and the other from ‘Init. Prod.’) are drawn along separate tracks instead of along a single track as in [Example 9.2](#).

```
/* Activity-on-Node representation of the project */
data widget;
  format task $12. succ1-succ3 $12.;
  input task & days succ1 & succ2 & succ3 & ;
  datalines;
Approve Plan      5 Drawings        Study Market   Write Specs
Drawings          10 Prototype      .
Study Market     5 Mkt. Strat.    .
Write Specs       5 Prototype      .
Prototype         15 Materials     Facility      .
Mkt. Strat.      10 Test Market   Marketing    .
Materials         10 Init. Prod.   .
Facility          10 Init. Prod.   .
Init. Prod.       10 Test Market   Marketing   Evaluate
Evaluate          10 Changes        .
Test Market       15 Changes        .
Changes           5 Production    .
Production        0 .             .
Marketing         0 .             .
;

goptions hpos=80 vpos=50 border;
pattern1 c=ltgray v=s;
pattern2 c=ltgray v=s;

title c=blue j=l h=1.5 ' Project: Widget Manufacture';
title2 c=blue j=l h=1.5 ' Schedule Information';
footnote c=blue j=r h=1.5 'Spanning Multiple Pages ';
proc netdraw data=sched graphics;
  actnet / act=task
    succ=(succ1 succ2 succ3)
    dur = days
    coutline=blue
    ccritout=red
    carcs=blue
    ccritarcs=red
    ctext=blue
    lwidth=1
    lwcrit=2
    separatearcs;
run;
```

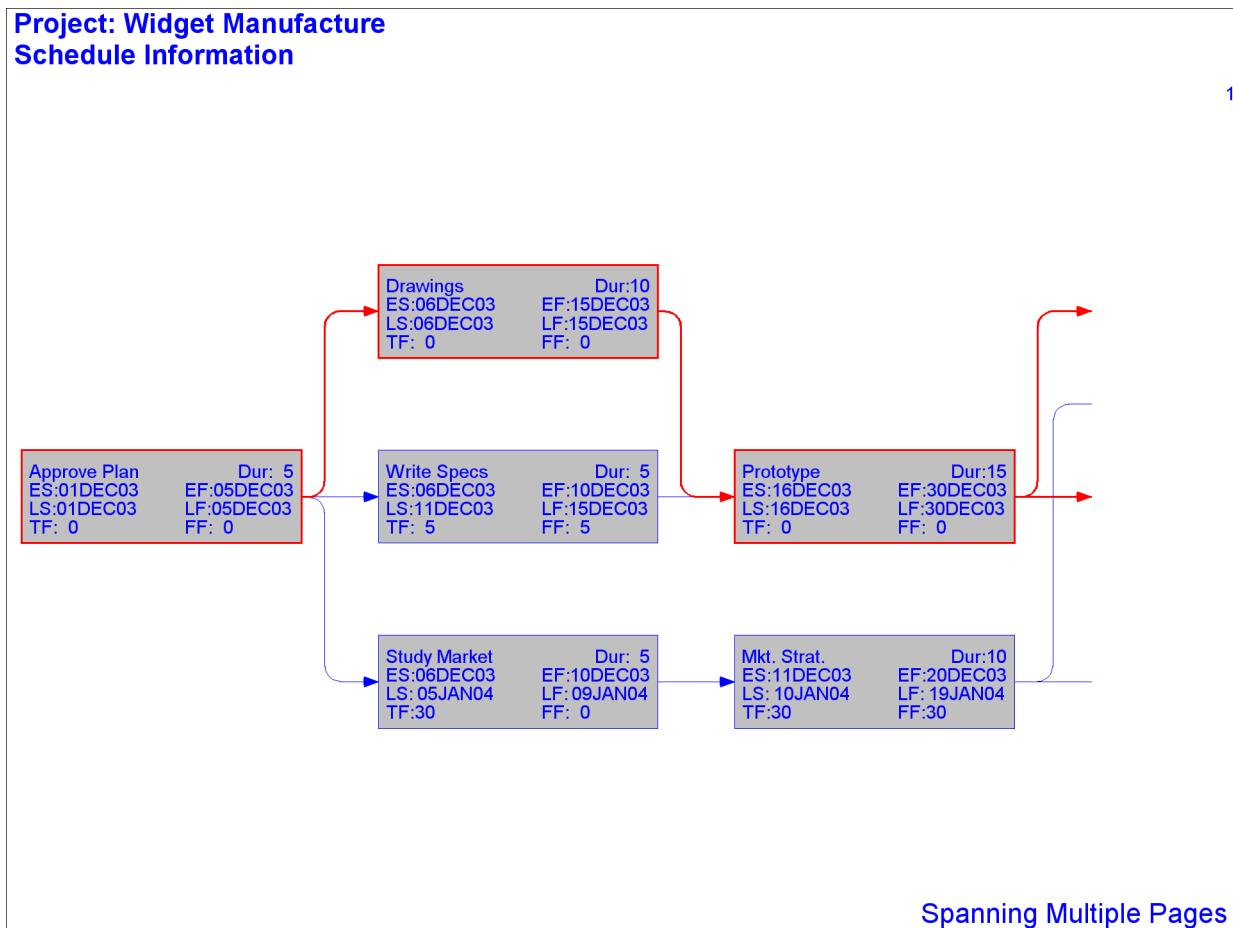**Output 9.3.1 Project Schedule**

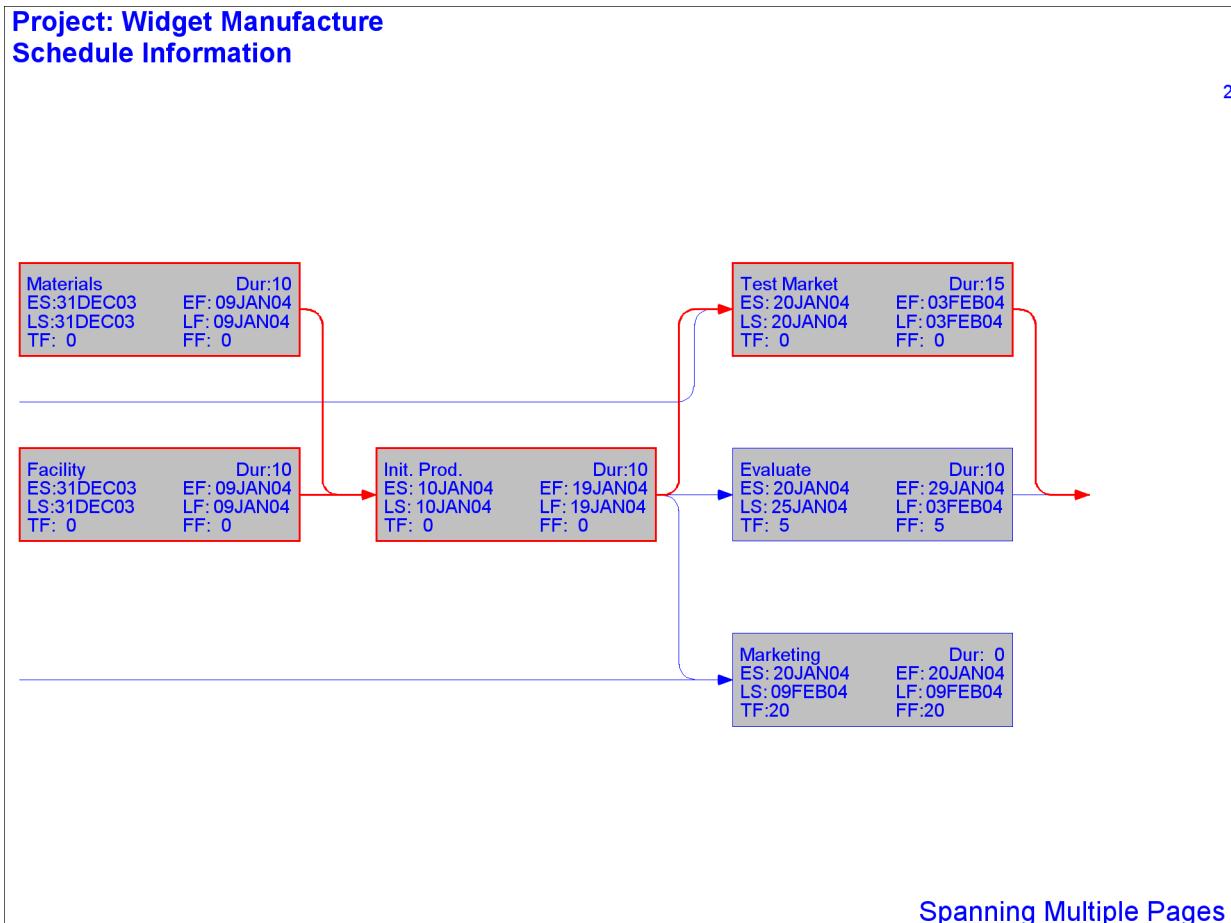Output 9.3.1 *continued*

**Output 9.3.1** *continued*

**Project: Widget Manufacture**  
**Schedule Information**

3

Changes ES: 04FEB04 LS: 04FEB04 TF: 0	Dur: 5 EF: 08FEB04 LF: 08FEB04 FF: 0	Production ES: 09FEB04 LS: 09FEB04 TF: 0	Dur: 0 EF: 09FEB04 LF: 09FEB04 FF: 0
--	---	---	---

Spanning Multiple Pages


---

### Example 9.4: The COMPRESS and PCOMPRESS Options


In Example 9.2, the number of character cell positions were specified so that the entire network fit on one page; in Example 9.3, the network spanned several pages. To force the network diagram to fit on one page automatically, you can use the COMPRESS or PCOMPRESS options. Both options use window transformations to fit the network on one page: the COMPRESS option treats the horizontal and vertical transformations independently of each other so that one direction may not be as compressed as the other; the PCOMPRESS option uses a proportional transformation so that each direction is compressed as much as the other. The following two invocations of PROC NETDRAW illustrate the differences in the diagrams produced.

In both network diagrams, PATTERN statements are used to color the nodes red or green, depending on whether the activities they represent are critical or not. The first PATTERN statement is for nodes corresponding to noncritical activities, and the second statement is for critical activities. The second invocation of PROC NETDRAW also uses the NOVCENTER option in the ACTNET statement to turn off centering in the vertical direction, so that the network is drawn immediately below the titles.

Output 9.4.1 Project Network: COMPRESS Option

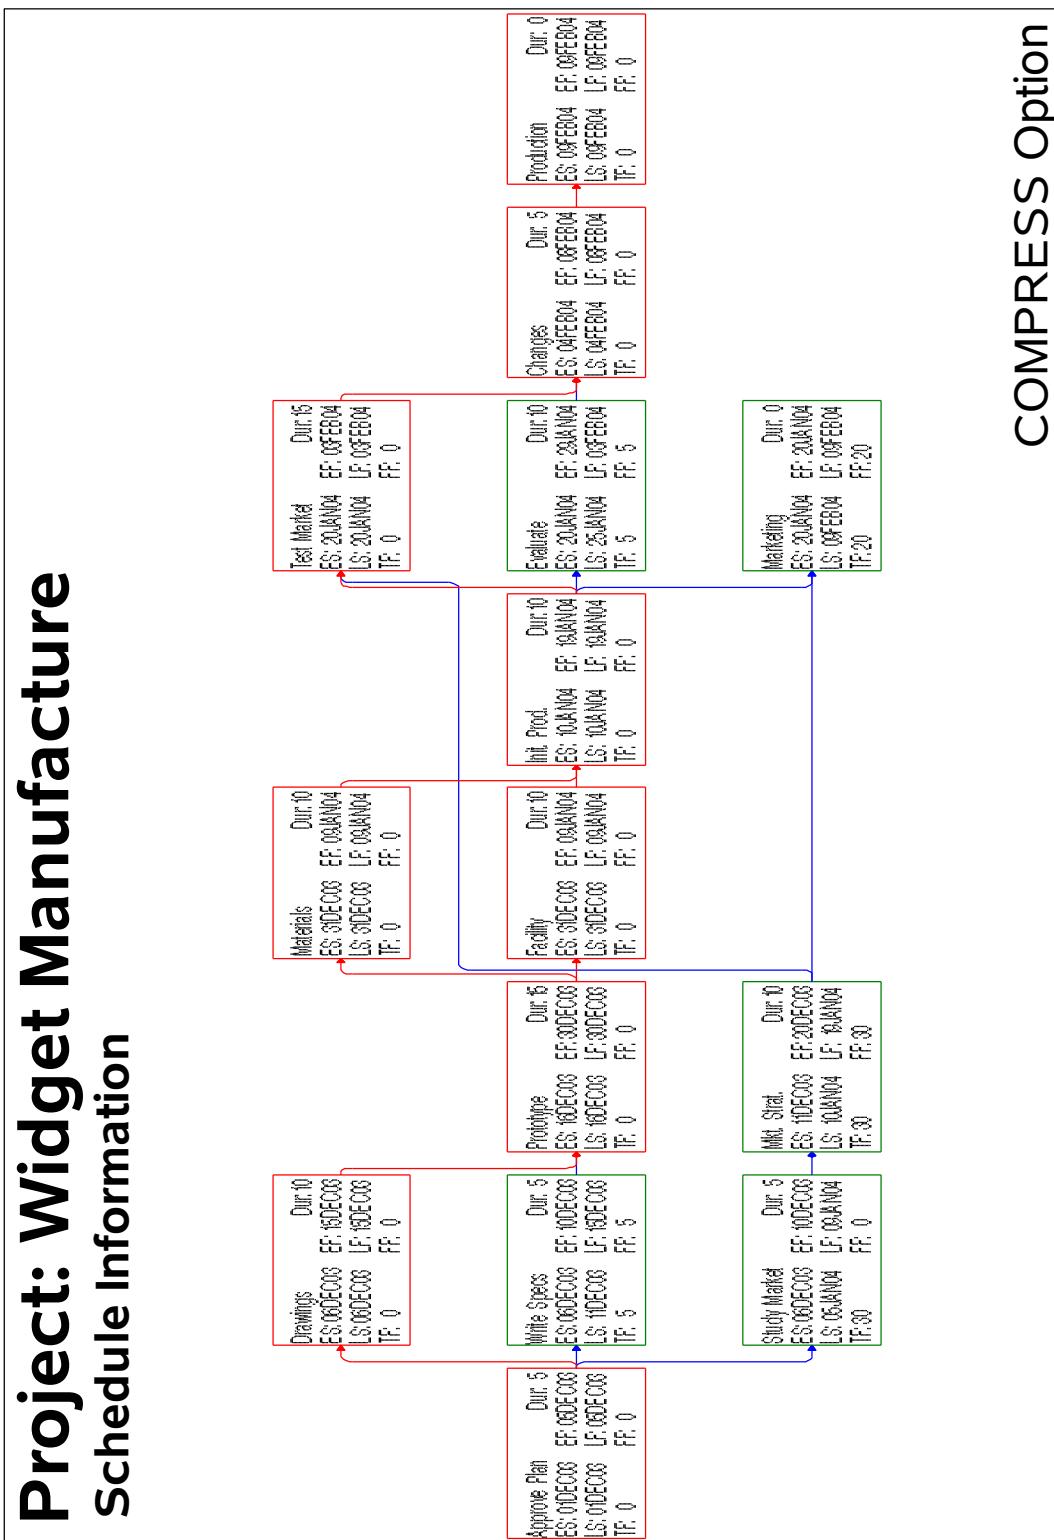

### Output 9.4.2 Project Network: PCOMPRESS Option

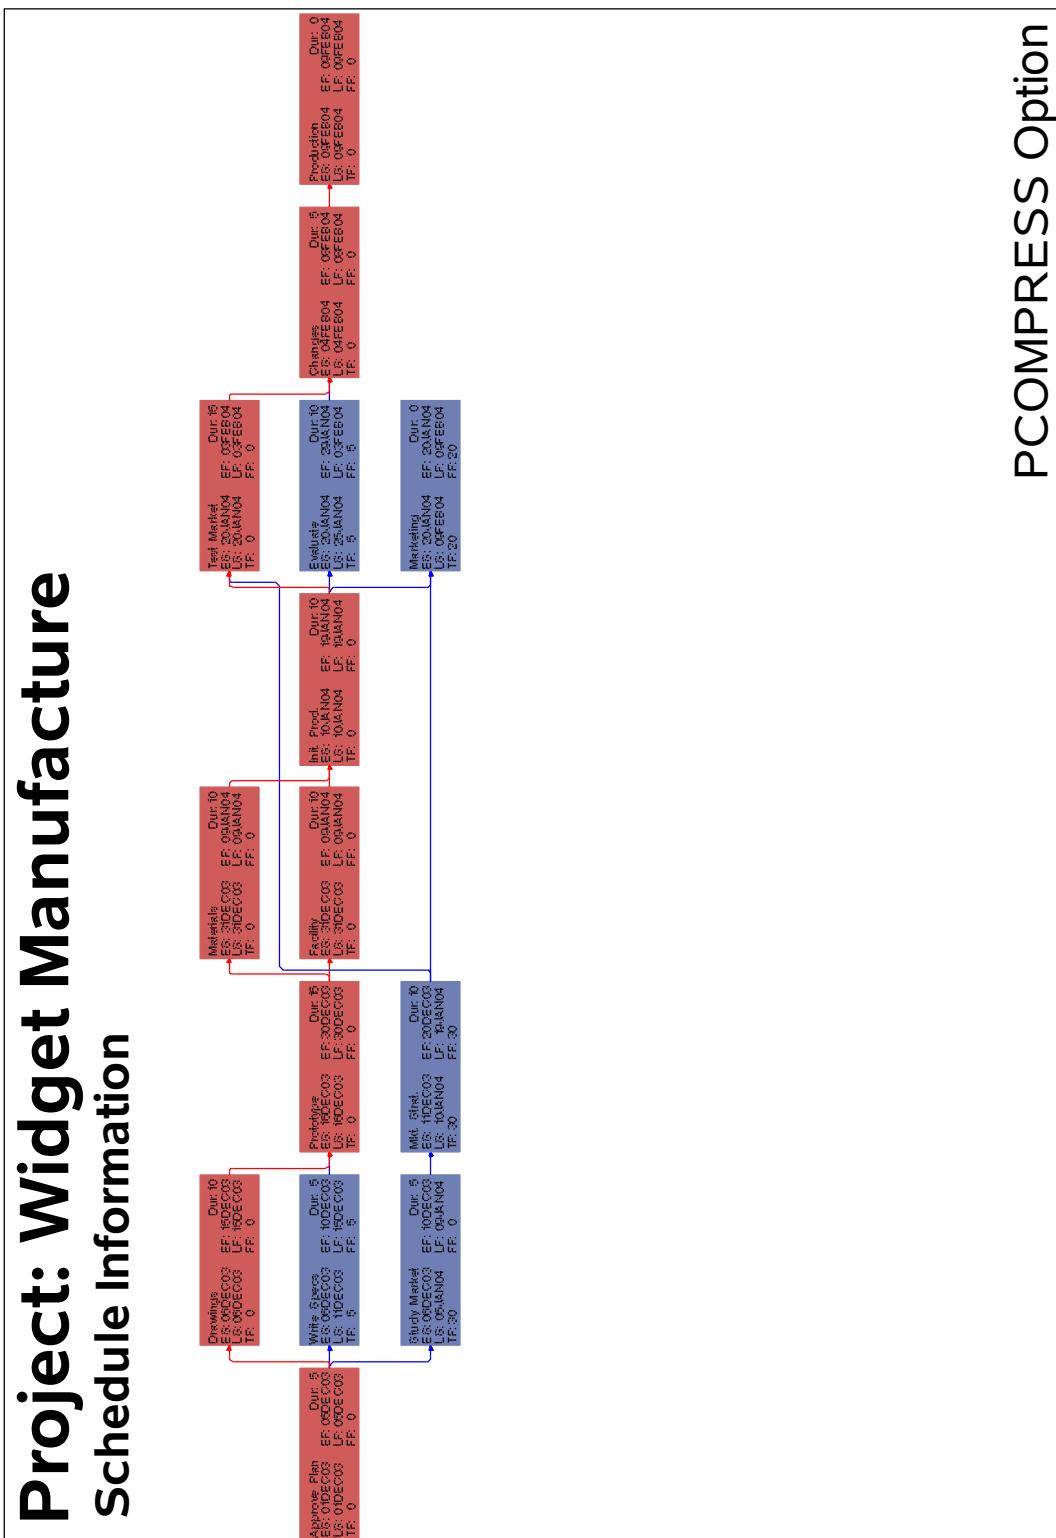

```

goptions border;

pattern1 v=e c=green;
pattern2 v=e c=red;

title j=1 h=3 ' Project: Widget Manufacture';
title2 j=1 h=2 ' Schedule Information';
footnote j=r h=2 'COMPRESS Option ';
proc netdraw data=sched graphics;
  actnet / act=task
    succ=(succ1 succ2 succ3)
    dur = days
    carcs=blue
    ccritarcs=red
    separatearcs
    font=swiss
    height=1.5
    compress;
  run;

footnote j=r h=2 'PCOMPRESS Option ';
proc netdraw data=sched graphics;
  actnet / act=task
    succ=(succ1 succ2 succ3)
    dur = days
    carcs=blue
    ccritarcs=red
    separatearcs
    font=swiss
    height=1.5
    pcompress
    novcenter;
  run;

```

## Example 9.5: Controlling the Display Format

In addition to the COMPRESS and PCOMPRESS options and the HPOS= and VPOS= global options, you can control the amount of information displayed on a single page by

- turning off the default ID variable selection (using the NODEFID option) and using the ID= option to select only a few variables of interest in the Network data set
- setting the dimensions of each node using the BOXWIDTH= and the BOXHT= options
- specifying the horizontal and vertical distances between nodes using the XBETWEEN= and YBETWEEN= options, respectively

This example uses the data from [Example 8.1](#) in Chapter 8, “The GANTT Procedure,” and some of the options just mentioned to produce the network diagram shown in [Output 9.5.1](#). The ID= and NODEFID options are used to display only the activity name and duration values within each node. The NOLABEL

option suppresses the display of the variable names within each node. Some of the activity names are truncated by the BOXWIDTH= option. Even with the restrictions imposed, the network is too large to fit on one page and spans two pages. Note that on devices with higher resolution, you can increase the values of HPOS and VPOS (still maintaining readability) to enable more of the network to be drawn on one page.

```

data ex;
  format activity $20. success1 $20. success2 $20. success3 $20.
                 success4 $20.;
  input activity dur success1-success4;
  datalines;
form          4 pour . . .
pour          2 core . . .
core          14 strip spray_fireproof insulate_walls .
strip          2 plumbing curtain_wall risers doors
strip          2 electrical_walls balance_elevator . .
curtain_wall  5 glaze_sash . . .
glaze_sash    5 spray_fireproof insulate_walls . .
spray_fireproof 5 ceil_ducts_fixture . .
ceil_ducts_fixture 5 test . . .
plumbing       10 test . . .
test           3 insulate_mechanical . . .
insulate_mechanical 3 lath . . .
insulate_walls 5 lath . . .
risers          10 ceil_ducts_fixture . .
doors           1 port_masonry . . .
port_masonry   2 lath finish_masonry . .
electrical_walls 16 lath . . .
balance_elevator 3 finish_masonry . .
finish_masonry 3 plaster marble_work . .
lath            3 plaster marble_work . .
plaster         5 floor_finish tiling acoustic_tiles .
marble_work    3 acoustic_tiles . .
acoustic_tiles 5 paint finish_mechanical . .
tiling          3 paint finish_mechanical . .
floor_finish   5 paint finish_mechanical . .
paint           5 finish_paint . . .
finish_mechanical 5 finish_paint . . .
finish_paint   2 caulking_cleanup . . .
caulking_cleanup 4 finished . . .
finished        0 . . .
;

proc cpm finishbefore date='1jan04'd out=sched;
  activity activity;
  duration dur;
  successors success1-success4;
run;

proc sort;
  by e_start;
run;

```


```


pattern1 v=e c=green;
pattern2 v=e c=red;

title j=l h=3 ' Site: Multi-Story Building'
      j=r ' Date: January 1, 2004';
footnote j=r h=2 'Controlling Display Format';

proc netdraw data=sched graphics;
  actnet / act = activity
    succ = (success1-success4)
    id = ( activity dur )
    nolabel nodefaultid
    boxwidth = 6
    ybetween = 6
    separatearcs;
run;

```

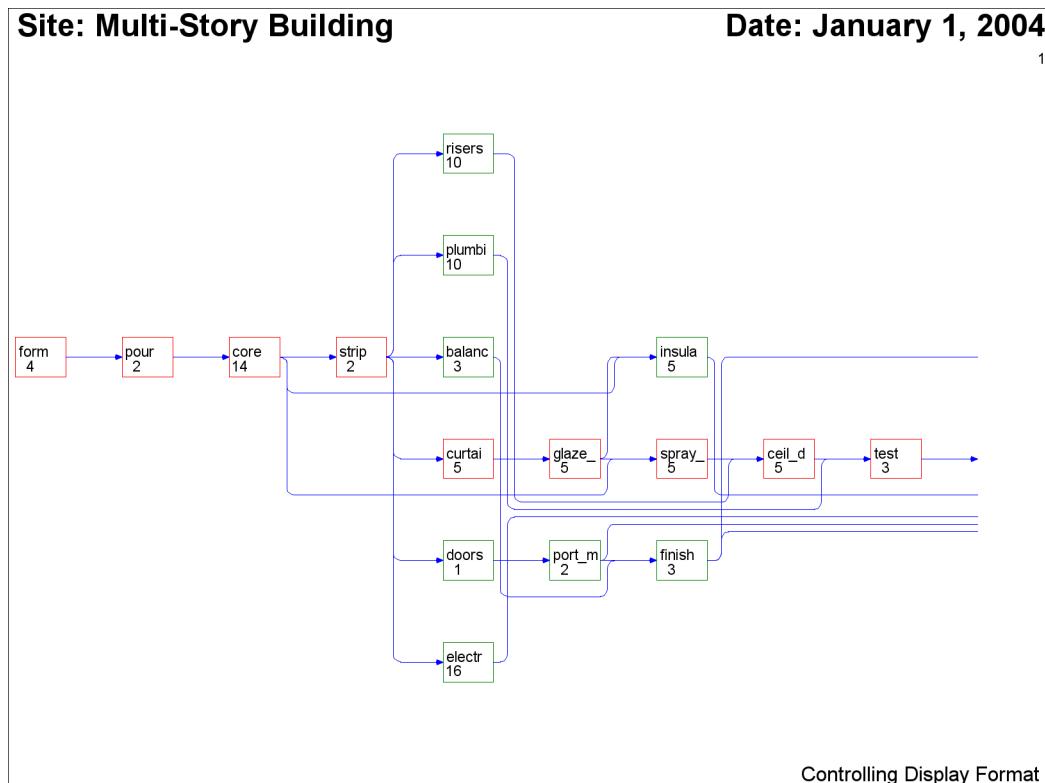**Output 9.5.1** Controlling the Display Format

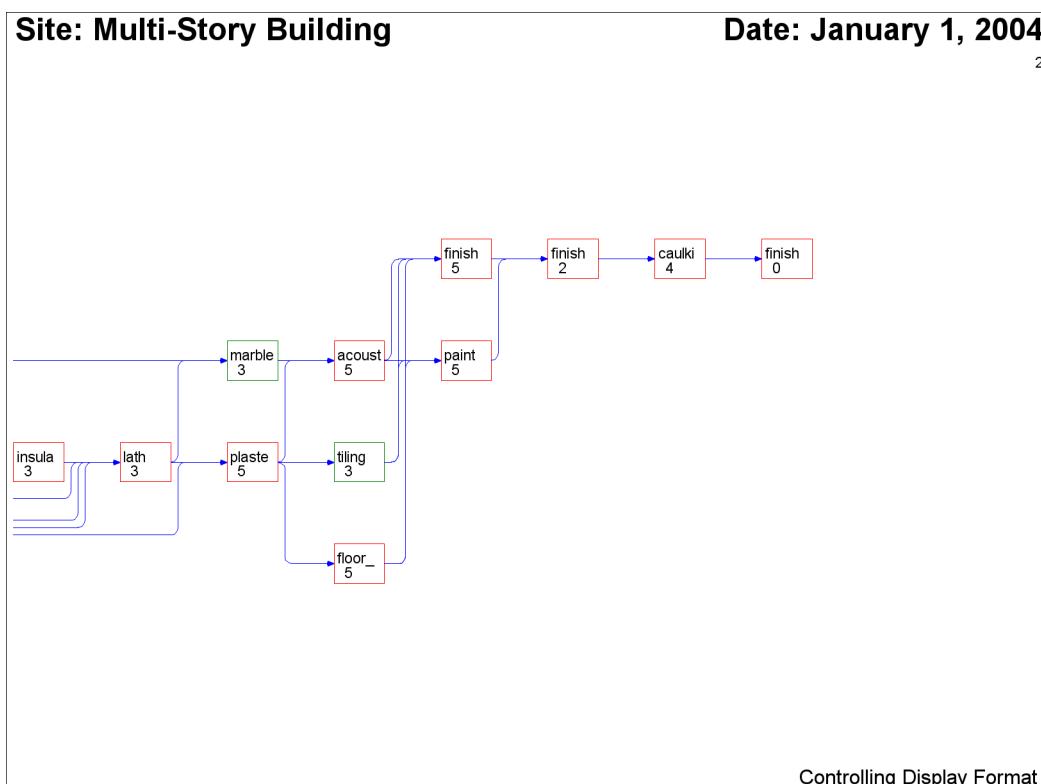**Output 9.5.1** *continued*



You can also control the format of the display by specifying the number of pages into which the network diagram should be split. You can do this by


- using the HPAGES= and VPAGES= options, which specify the number of pages in the horizontal and vertical directions, respectively
- setting the number of nodes in the horizontal and vertical directions using the NXNODES= and NYNODES= options, respectively

The following statements invoke PROC NETDRAW with some additional page control options. The HTEXT= option is also used to control the height of the text used in the diagram.

```
footnote j=r h=2 'Controlling Number of Pages';

proc netdraw data=sched graphics;
  actnet / act = activity
    succ = (success1-success4)
    id = ( activity dur )
    nolabel nodefaultid
    boxwidth = 6
    ybetween = 6
    separatearcs
    htext=2
    nopagenumber
    hpages=3 vpages=1;
run;
```

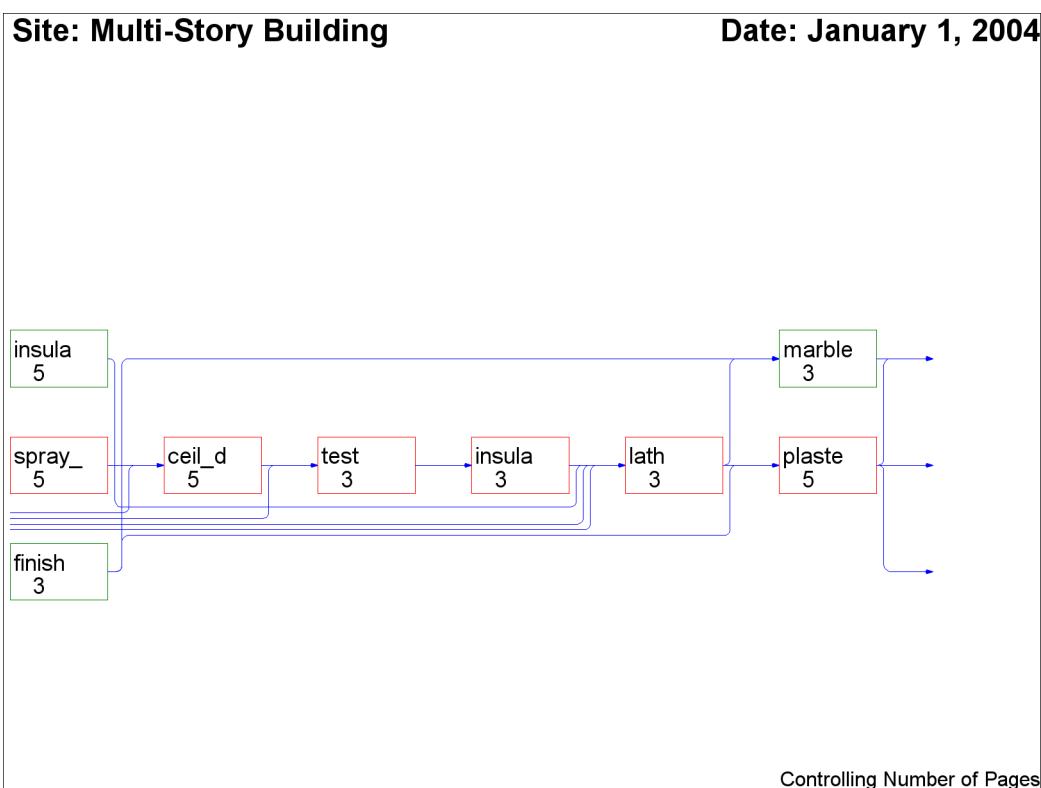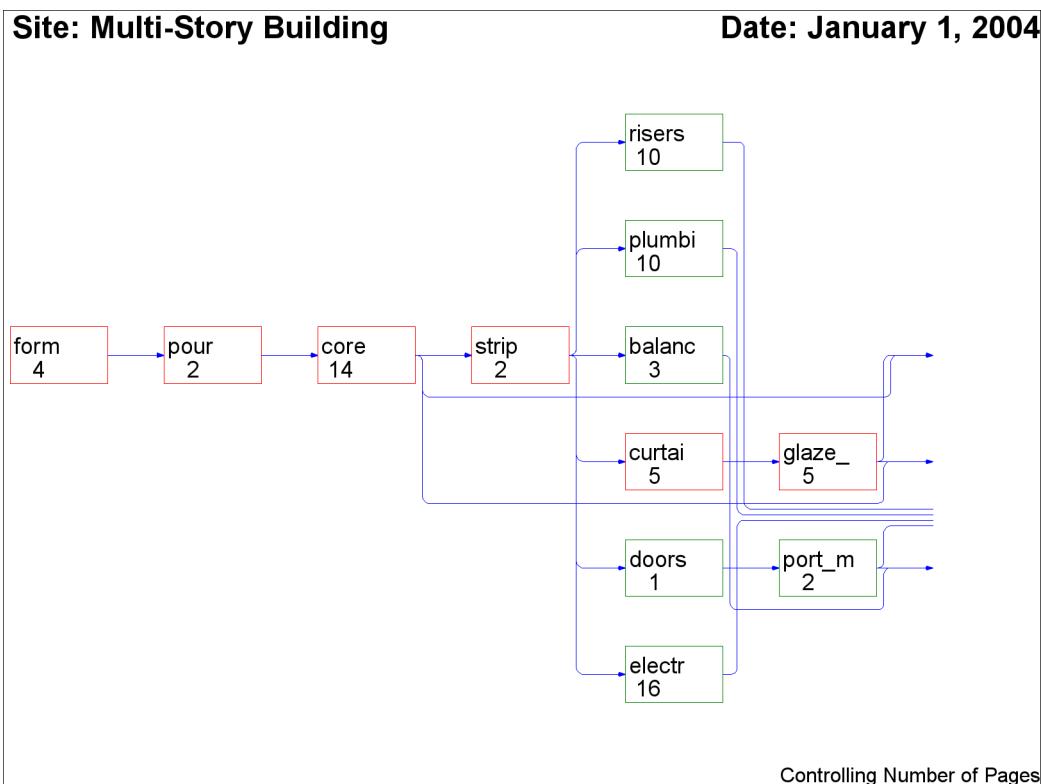**Output 9.5.2** Controlling the Number of Pages

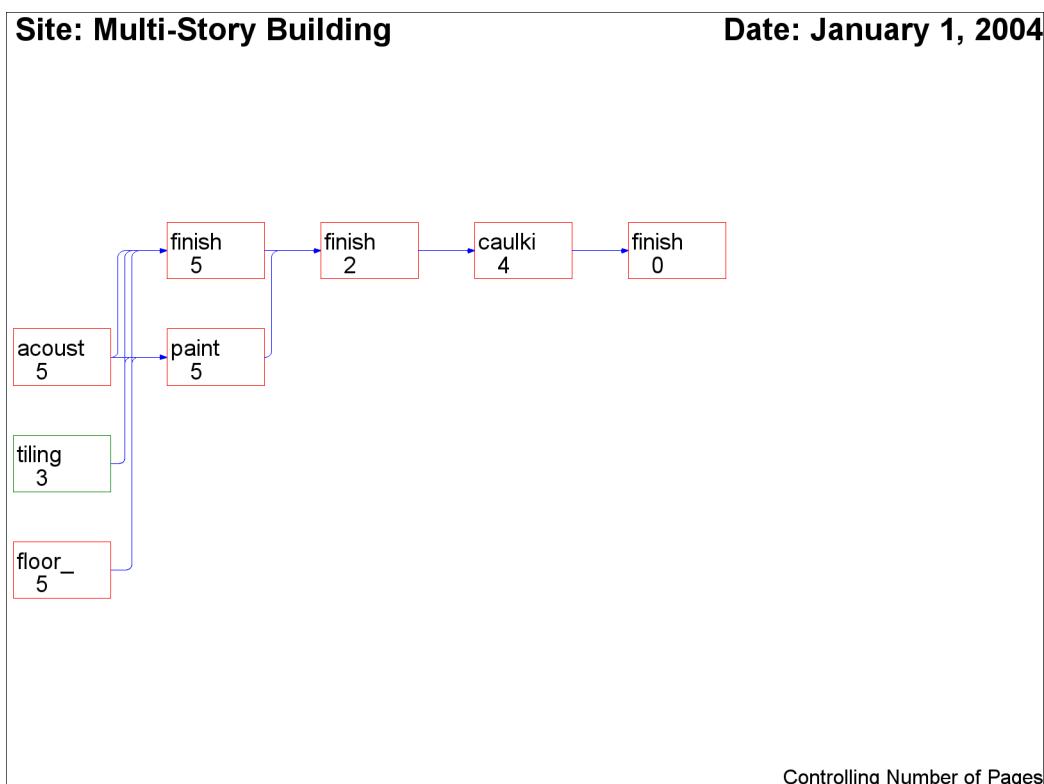**Output 9.5.2** *continued***Example 9.6: Nonstandard Precedence Relationships**

This example illustrates the use of the LAG= option to indicate nonstandard precedence relationships between activities. Consider the widget manufacturing project described in the earlier examples. Some of the precedence constraints between the activities may be nonstandard or have a nonzero lag value. For example, the activity ‘Init. Prod.’ may not be able to start until 2 days after the completion of the activity ‘Facility.’ The Network data set is displayed in [Output 9.6.1](#). The variable lagdur indicates the type of relationship between the activities specified in the variables task and succ.

The following statements invoke PROC NETDRAW with the LAG= option. The resulting network diagram is shown in [Output 9.6.2](#).

```

pattern1 v=e c=green;

title h=3 'Widget Manufacture';
title2 h=2 'Nonstandard Precedence Constraints';

proc netdraw graphics data=widglag;
  actnet / act=task
    succ=succ
    lag=lagdur
    pcompress
    htext=3 boxht=3 arrowhead=2
    xbetween=7 ybetween=9
    centerid
    separatearcs;
run;


```

**Output 9.6.1** Network with Nonstandard Precedence Constraints

**Widget Manufacture  
Network Data Set**

Obs	task	days	succ	lagdur
1	Approve Plan	5	Drawings	
2	Approve Plan	5	Study Market	
3	Approve Plan	5	Write Specs	
4	Drawings	10	Prototype	
5	Study Market	5	Mkt. Strat.	
6	Write Specs	5	Prototype	
7	Prototype	15	Materials	ss_9
8	Prototype	15	Facility	ss_9
9	Mkt. Strat.	10	Test Market	
10	Mkt. Strat.	10	Marketing	
11	Materials	10	Init. Prod.	
12	Facility	10	Init. Prod.	fs_2
13	Init. Prod.	10	Test Market	
14	Init. Prod.	10	Marketing	
15	Init. Prod.	10	Evaluate	
16	Evaluate	10	Changes	ss_6
17	Test Market	15	Changes	ff_3
18	Changes	5	Production	
19	Production	0		
20	Marketing	0		

## **Output 9.6.2** Network Diagram with Nonstandard Precedence Constraints

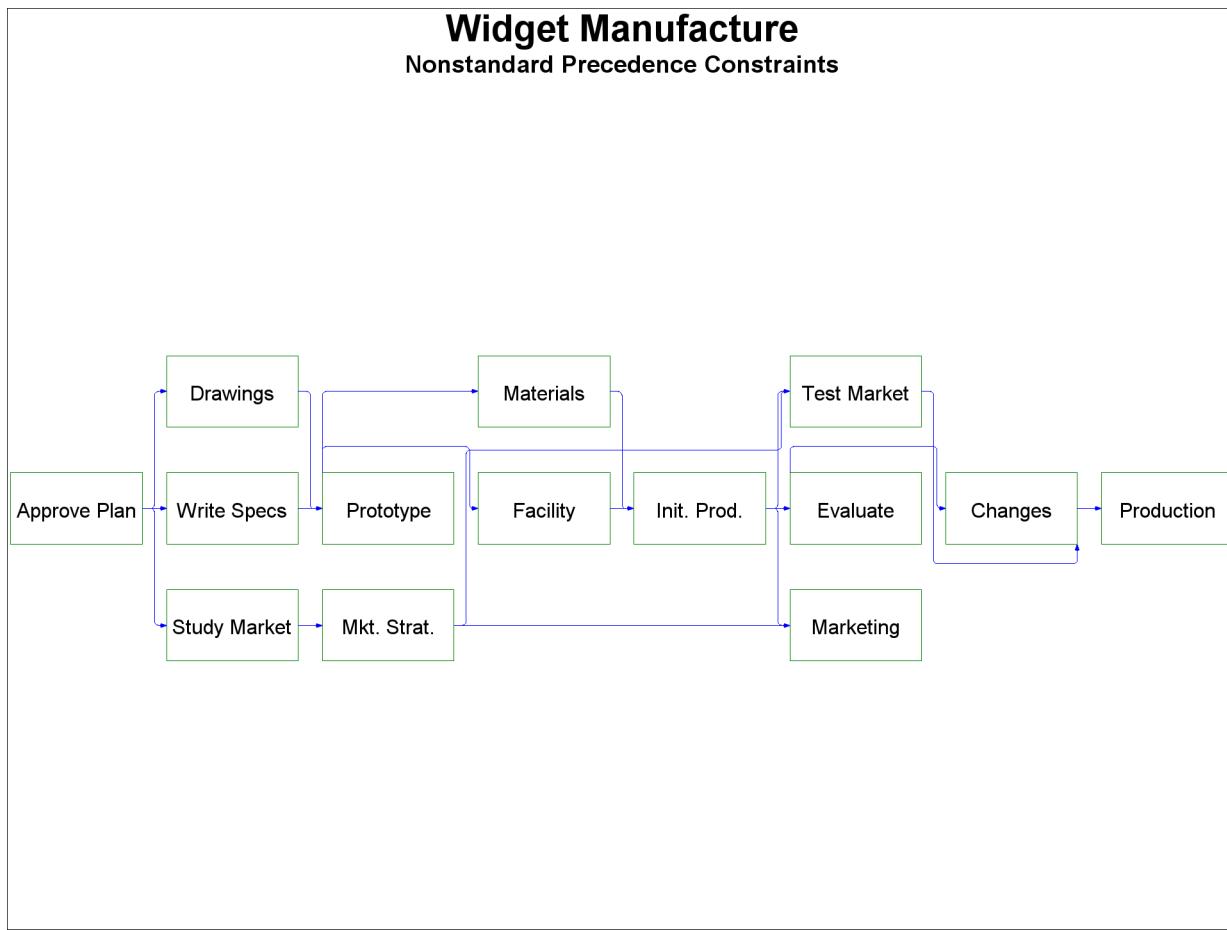

## Example 9.7: Controlling the Arc-Routing Algorithm

This example illustrates the use of the DP and HTRACKS= options to control the routing of the arcs connecting the nodes. The project is a simple construction project with the following data. A Schedule data set produced by PROC CPM is input to PROC NETDRAW. The first invocation of the procedure illustrates the default layout of the network. As explained in the section “[Layout of the Network](#)” on page 688, the NETDRAW procedure uses a simple heuristic to route the arcs between the nodes. In the resulting diagram displayed in [Output 9.7.1](#), note that the specification of BOXHT=3 limits the number of rows within each node so that the float values are not displayed.

```


data exmpl;
  input task      $ 1-16
        duration
        succesr1 $ 21-35
        succesr2 $ 36-50
        succesr3 $ 51-65;
  datalines;
Drill Well      4   Pump House
Pump House     3   Install Pipe
Power Line      3   Install Pipe
Excavate       5   Install Pipe   Install Pump   Foundation
Deliver Material 2 Assemble Tank
Assemble Tank    4   Erect Tower
Foundation       4   Erect Tower
Install Pump     6
Install Pipe     2
Erect Tower      6
;

proc cpm data=exmpl date='1jan04'd out=sched;
  activity task;
  duration duration;
  successor succesr1 succesr2 succesr3;
  run;

pattern1 v=e c=green;
pattern2 v=e c=red;

title j=1 h=3 ' Site: Old Well Road';
title2 j=1 h=2 ' Date: January 1, 2004';
footnote j=r h=2 'Default Layout ';
proc netdraw data=sched graphics;
  actnet / act = task
        dur = duration
        succ = (succesr1-succesr3)
        boxht = 3 xbetween = 10
        separatearcs
        htext=2
        pcompress;
run;

```

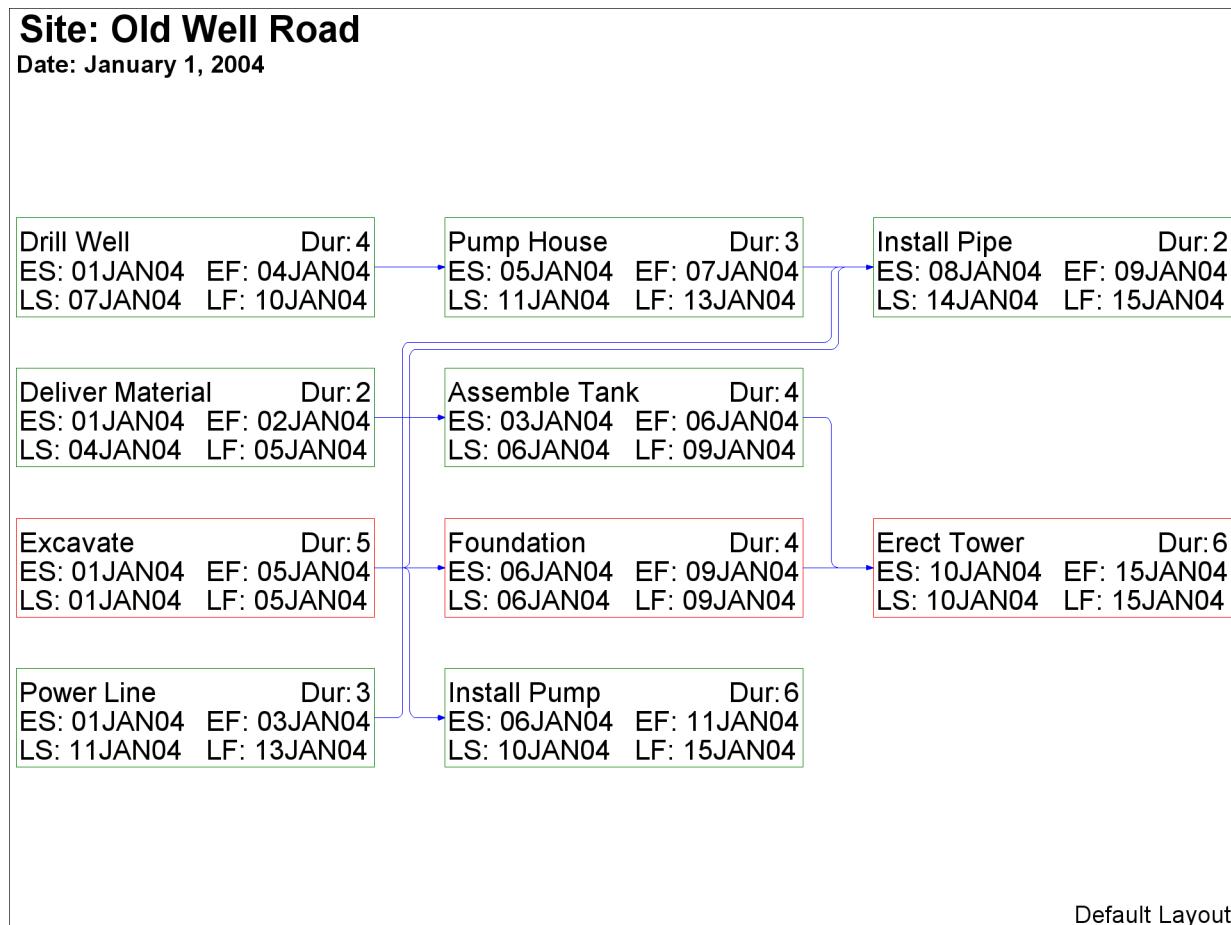
**Output 9.7.1** Arc Routing: Default Layout

Next, a different routing of the arcs is obtained by specifying the DP and the HTRACKS= options. As a result of these options, the NETDRAW procedure uses a dynamic programming algorithm to route the arcs, limiting the number of horizontal tracks used to 1. The resulting network diagram is shown in [Output 9.7.2](#). Notice that at most one arc is drawn in each horizontal track. Recall that, by default, the procedure uses a dynamic programming algorithm for arc routing if the number of tracks is restricted to be less than the maximum number of successors. Thus, for this example, the default routing option will be DP, even if it is not explicitly specified (because HTRACKS = 1 and the maximum number of successors is 3).

```

footnote j=r h=2 'Controlled Layout ';
proc netdraw data=sched graphics;
  actnet / act = task
    dur = duration
    succ = (succesr1-succesr3)
    boxht = 3 xbetween = 10
    separatearcs
    htracks=1
    htext=2
    pcompress
    dp;
run;

```

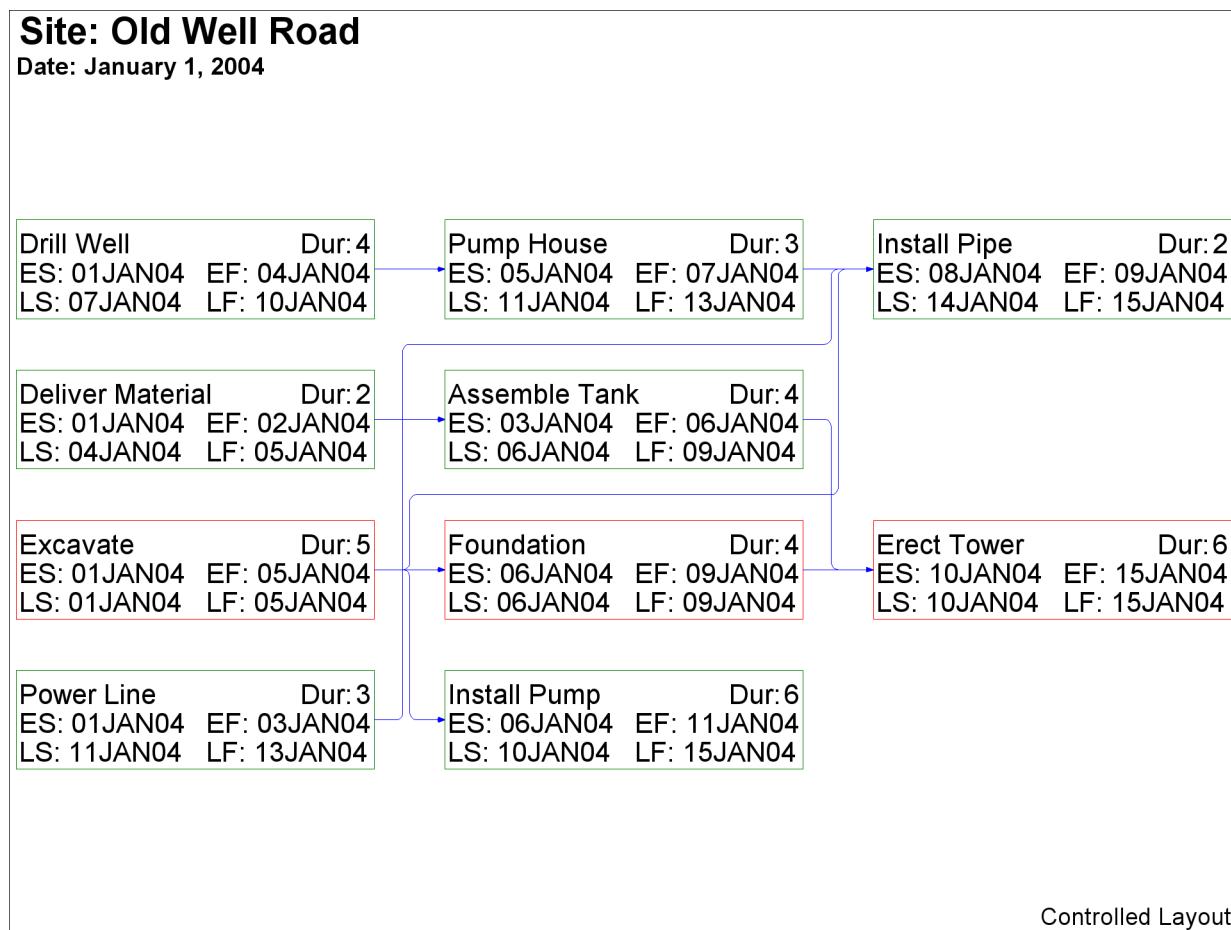**Output 9.7.2** Arc Routing: Controlled Layout**Example 9.8: PATTERN and SHOWSTATUS Options**

As a project progresses, in addition to the criticality of the activities, you may also want to display the status of the activity: whether it is in progress, has been completed, or is still to be scheduled. The SHOWSTATUS option in the ACTNET statement displays this additional information. In the current example, the same progress data as shown in Example 4.13 in Chapter 4, “The CPM Procedure,” are used to illustrate the SHOWSTATUS option. The following program shows the necessary code. First, PROC CPM schedules the project with the SHOWFLOAT option; this enables activities that are already in progress or completed also to show nonzero float. Following this, a DATA step sets the variable style to ‘3’ for activities that are completed or in progress; the remaining activities have missing values for this variable.

PROC NETDRAW is then invoked with the SHOWSTATUS option, which draws two diagonal lines across nodes referring to completed activities and one diagonal line for in-progress activities. The PATTERN= option in the ACTNET statement identifies the variable style containing the pattern information. Thus, the third pattern statement is used for in-progress or completed activities; the other activities (which have missing values for the variable style) use the second or the first pattern statement according to whether or not they are critical. However, since the first two PATTERN statements have EMPTY fill patterns specified, the nodes

representing activities that have not yet started are in fact colored on the basis of the COUTLINE= and CCRITOUT= options. The resulting network diagram is shown in Output 9.8.1.

```

data holidays;
  format holiday holifin date7.;
  input holiday & date7. holifin & date7. holidur;
  datalines;
24dec03 26dec03 4
01jan04   .
;

* actual schedule at timenow = 19dec03;
data actual;
  format task $12. sdate fdate date7. ;
  input task & sdate & date7. fdate & date7. pctc rdur;
  datalines;
Approve Plan 01dec03 05dec03   .   .
Drawings      06dec03 16dec03   .   .
Study Market 05dec03   .       100  .
Write Specs  07dec03 12dec03   .   .
Prototype     .       .       .   .
Mkt. Strat.  10dec03   .       .   3
Materials     .       .       .   .
Facility      .       .       .   .
Init. Prod.   .       .       .   .
Evaluate      .       .       .   .
Test Market   .       .       .   .
Changes       .       .       .   .
Production    .       .       .   .
Marketing     .       .       .   .
;

* merge the predicted information with network data;
data widgact;
  merge actual widget;
  run;


* estimate schedule based on actual data;
proc cpm data=widgact holidata=holidays
  out=widgupd date='1dec03'd;
  activity task;
  succ   succ1 succ2 succ3;
  duration days;
  holiday holiday / holifin=(holifin);
  actual / as=sdate af=fdate timenow='19dec03'd
    remdur=rdur pctcomp=pctc showfloat;
  run;

/* Set patterns for activities that have started */
data netin;
  set widgupd;
  if a_start ^= . then style = 3;
  run;

```

```
goptions hpos=120 vpos=70 border;
pattern1 c=green  v=e;
pattern2 c=red    v=e;
pattern3 c=ltgray v=s;

title  j=1 h=3 ' Project: Widget Manufacture';
title2 j=1 h=2 ' Date: December 19, 2003';
footnote1 j=1 h=2 ' Activity';
footnote2 j=1 h=2 ' Start';
footnote3 j=1 h=2 ' Finish'
          j=r h=2 'PATTERN and SHOWSTATUS Options   ';
proc netdraw data=netin graphics;
  actnet / act=task
    succ=(succ1 succ2 succ3)
    ybetween = 10
    separatearcs
    pcompress
    id=(task e_start e_finish)
    nodefid nolabel
    carcs=cyan
    ccritarcs=red
    coutline = green
    ccritout = red
    showstatus
    pattern = style
    htext=2;
run;
```

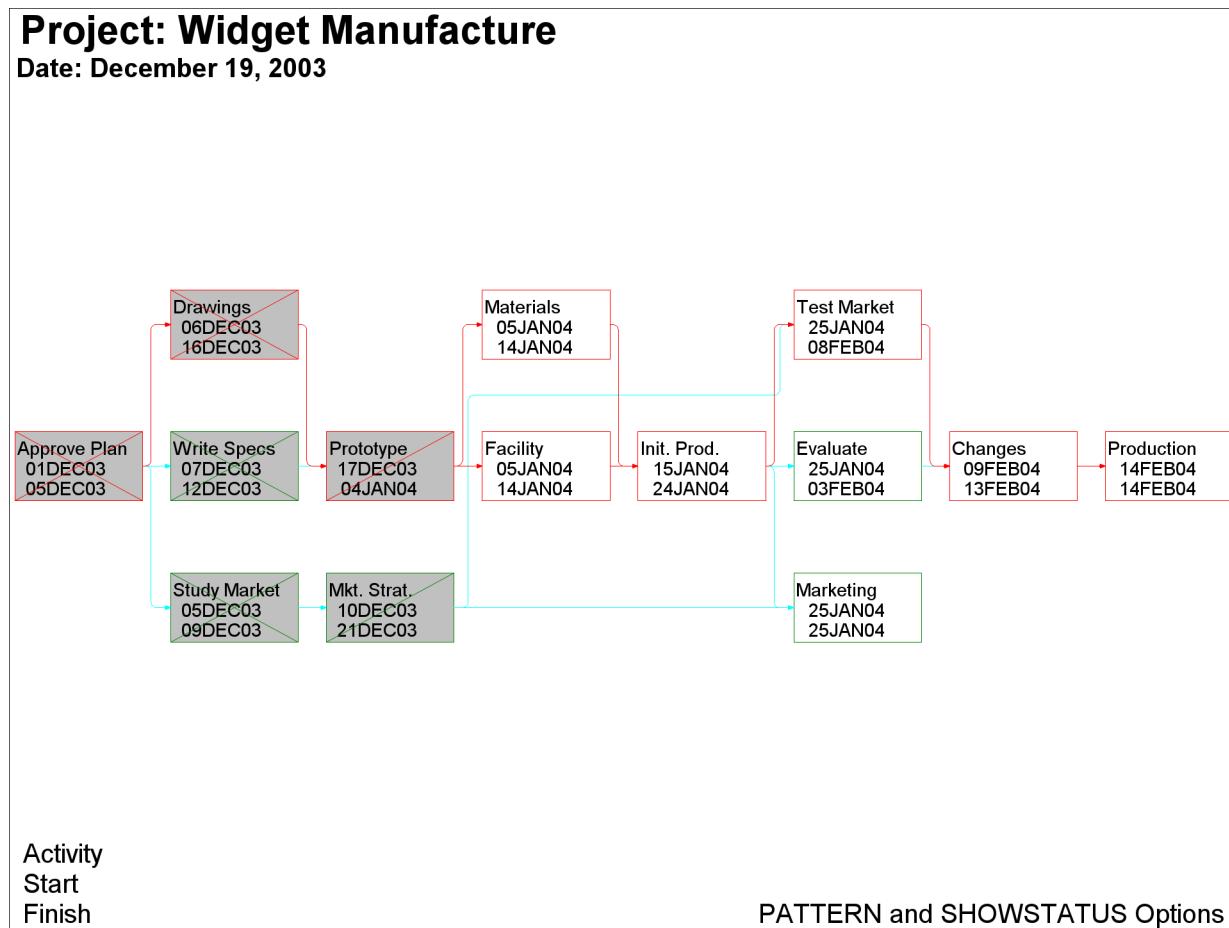**Output 9.8.1** PATTERN and SHOWSTATUS Options**Example 9.9: Time-Scaled Network Diagram**

This example illustrates the use of the TIMESCALE and ALIGN= options to draw time-scaled network diagrams. The Schedule data set WIDGUPD, produced by PROC CPM in the previous example, is used. First, PROC NETDRAW is invoked with the TIMESCALE option without any ALIGN= specification. By default, the procedure aligns the nodes to coincide with the early start times of the activities. The network spans two pages (HPAGES=2 VPAGES=1), as shown in Output 9.9.1. The HMARGIN= and VMARGIN= options add extra space around the margins.

```

pattern1 v=e c=green;
pattern2 v=e c=red;

title j=1 h=3 ' Project: Widget Manufacture';
title2 j=1 h=2 ' Date: December 19, 2003';
footnote j=1 h=2 ' Task Name / Early Finish Within Node'
      j=r h=2 ' Time Scaled: Default Alignment ';
proc netdraw data=widgupd graphics;
  actnet / act=task
    succ=(succ1 succ2 succ3)
    ybetween = 8
  
```

```

separatearcs
novcenter
id=(task e_finish) nodefid
nolabel
showstatus
carcs=darkblue
ccritarcs=red
vmargin=5
hmargin=5
timescale
htext=2 pcompress
hpages=2 vpages=1
nopagenumber;

run;


```

#### Output 9.9.1 TIMESCALE Option: Default Alignment

## Project: Widget Manufacture


Date: December 19, 2003

01DEC03	05DEC03	06DEC03	07DEC03	10DEC03	17DEC03
---------	---------	---------	---------	---------	---------

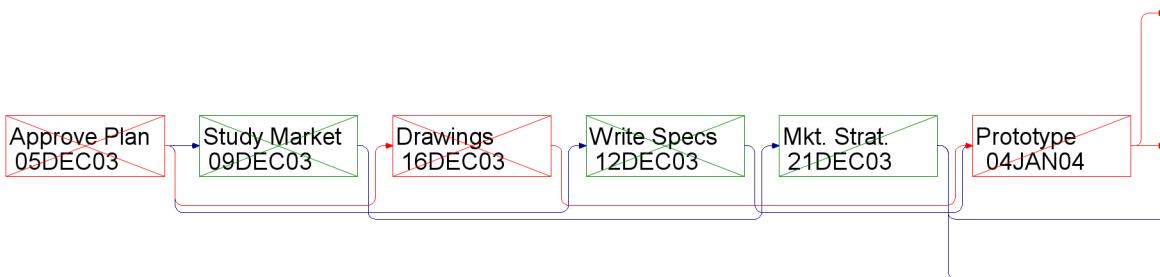

Task Name / Early Finish Within Node

Time Scaled: Default Alignment

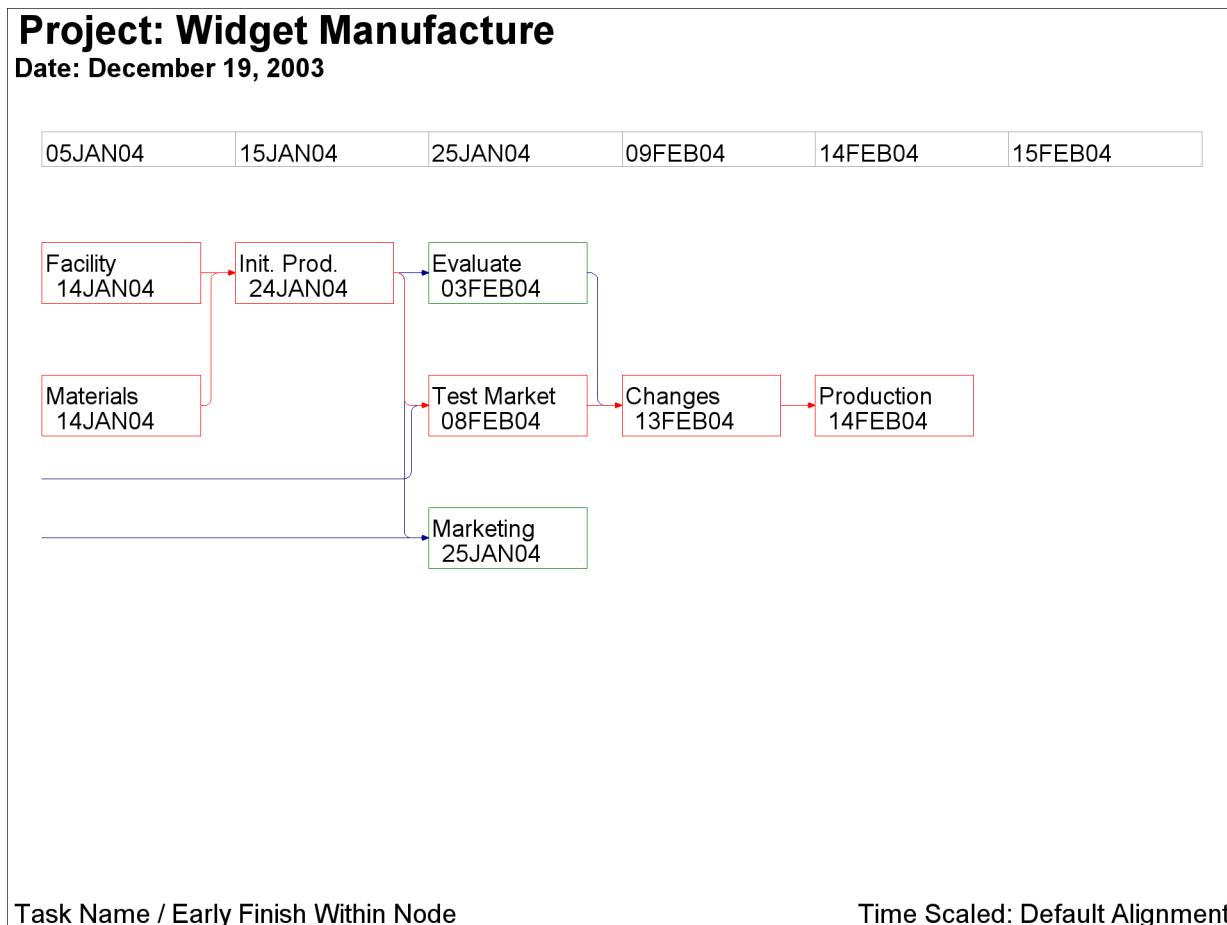**Output 9.9.1** *continued*

Next, PROC NETDRAW is invoked with several of the time-scale options:

- The ALIGN= option requests that the activities be placed according to the L\_START times.
- The FRAME option produces a border around the network diagram.
- The AUTOREF option draws reference lines at every tick mark.
- The LREF= and CREF= options specify the line style and color for the reference lines.
- The SHOWBREAK option requests that breaks in the time axis be indicated by breaks before the corresponding tick marks.

```
footnote j=1 h=2 ' Task Name / Late Finish Within Node'
      j=r h=2 'Time Scaled: Align = Late Start ';
proc netdraw data=widgupd graphics;
  actnet / act=task
    succ=(succ1 succ2 succ3)
    ybetween = 10
    separatearcs
```

```


pcompress
novcenter
id=(task l_finish) nodefid
nolabel
boxwidth=5
showstatus
carcs=darkcyan
ccritarcs=red
vmargin=10
align=l_start
frame
autoref
lref=33
cref=darkcyan
showbreak
htext=2;

run;

```

**Output 9.9.2** Timescale Option: ALIGN= L\_START**Project: Widget Manufacture**

Date: December 19, 2003

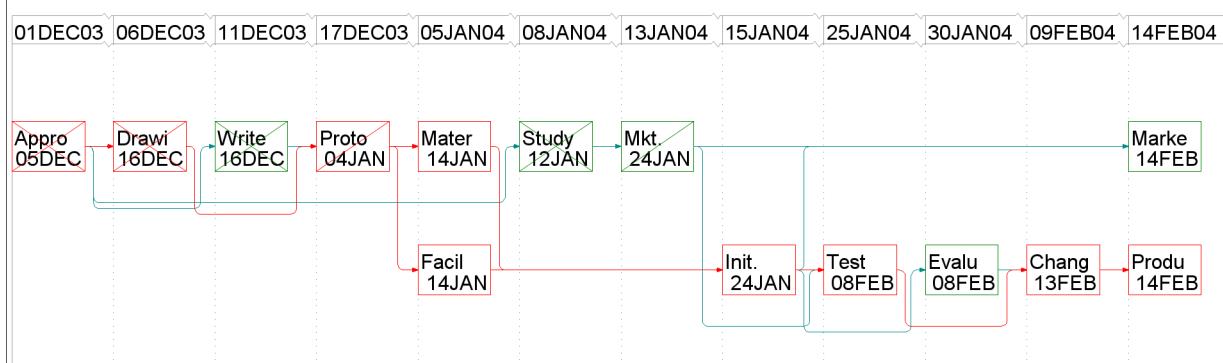

Task Name / Late Finish Within Node

Time Scaled: Align = Late Start

---

## Example 9.10: Further Time-Scale Options

In this example, the construction project described in Example 9.7 is used to illustrate some more time-scale options. First, the REFBREAK option indicates breaks in the time axis by drawing a zigzag line down the diagram before each tick mark corresponding to a break. The CREFBRK= and LREFBRK= options control the color and line style for these lines. The network diagram is shown in Output 9.10.1.

```

title j=1 h=1.5 ' Site: Old Well Road';
title2 j=1 h=1.5 ' Date: January 1, 2004';
footnote j=r h=1.5 'Time Scale Options: Reference Breaks';

proc netdraw data=sched graphics;
  actnet / act = task
    dur = duration
    succ = (succesr1-succesr3)
    dp compress separatearcs
    font=swiss htext=2
    timescale refbreak lrefbrk = 33
    carcs=cyan crefbrk = blue;
run;

```


Next, PROC NETDRAW is invoked with the LINEAR option so that there is no break in the time axis. The BOXWIDTH= option limits the size of each node. The diagram is drawn in Output 9.10.2.


```

title j=1 h=1.5 ' Site: Old Well Road';
title2 j=1 h=1.5 ' Date: January 1, 2004';
footnote j=r h=1.5 'Time Scale Options: Linear Diagram';

proc netdraw data=sched graphics;
  actnet / act = task
    dur = duration
    succ = (succesr1-succesr3)
    dp
    pcompress
    novcenter
    vmargin = 10
    separatearcs
    htext=2
    carcs=cyan
    id=(task)
    nodefid
    nolabel
    boxwidth=7
    timescale
    linear
    frame;
run;

```

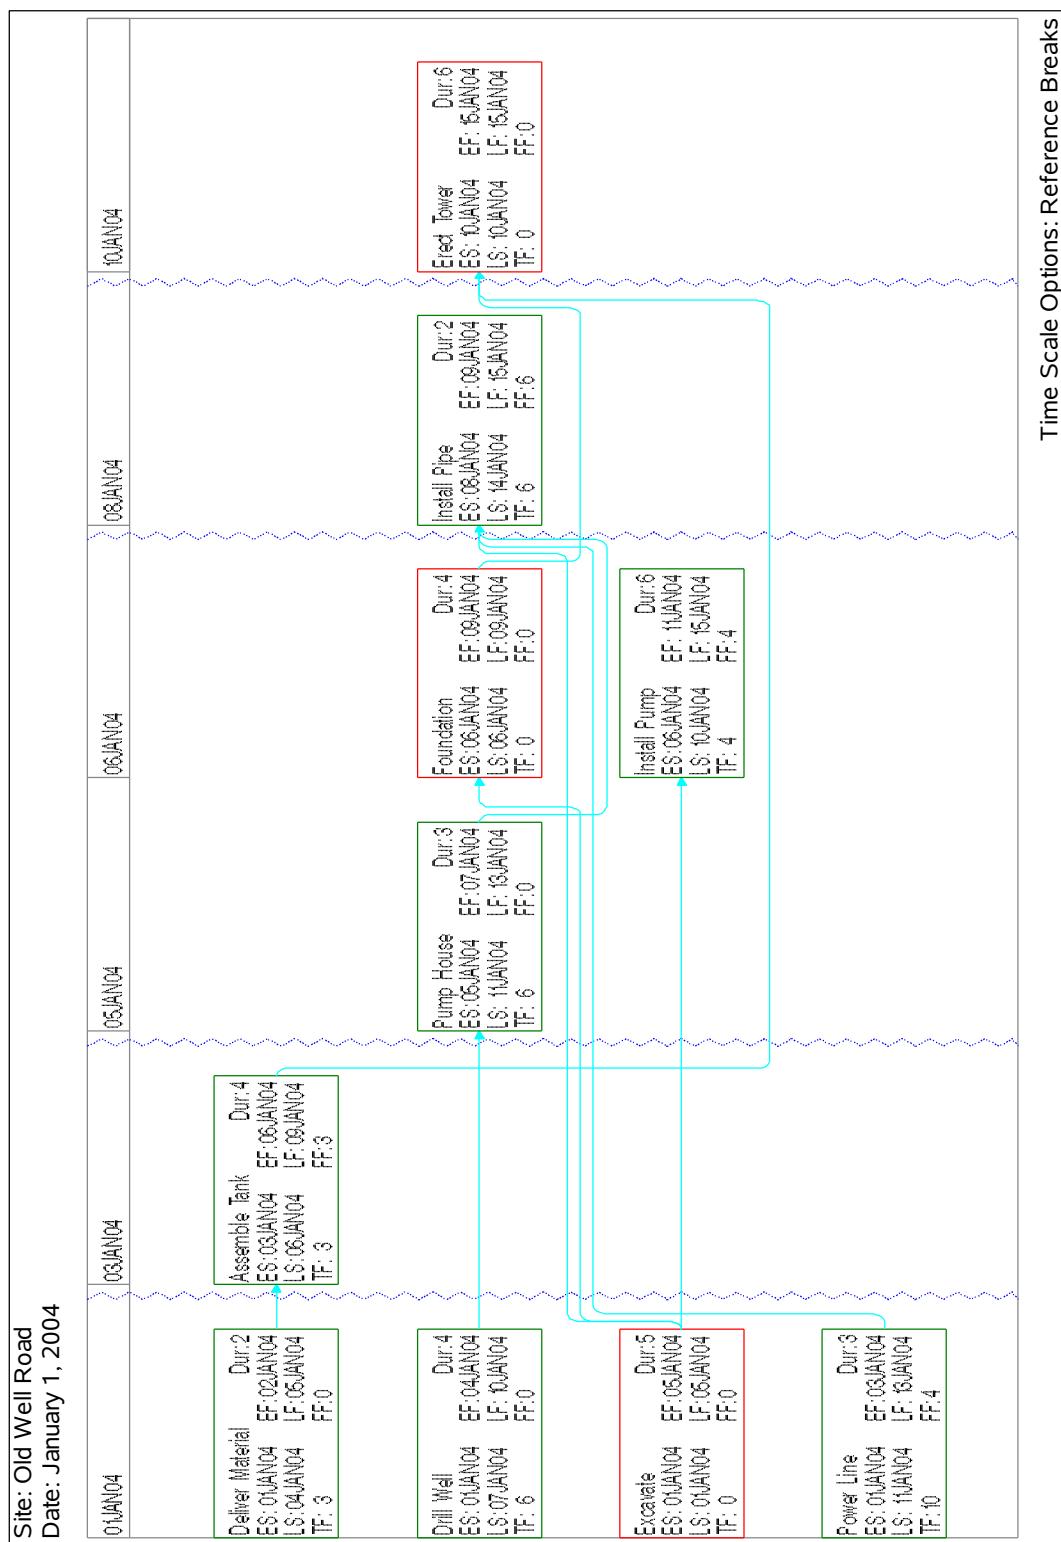**Output 9.10.1** Time-Scaled Network: Reference Breaks

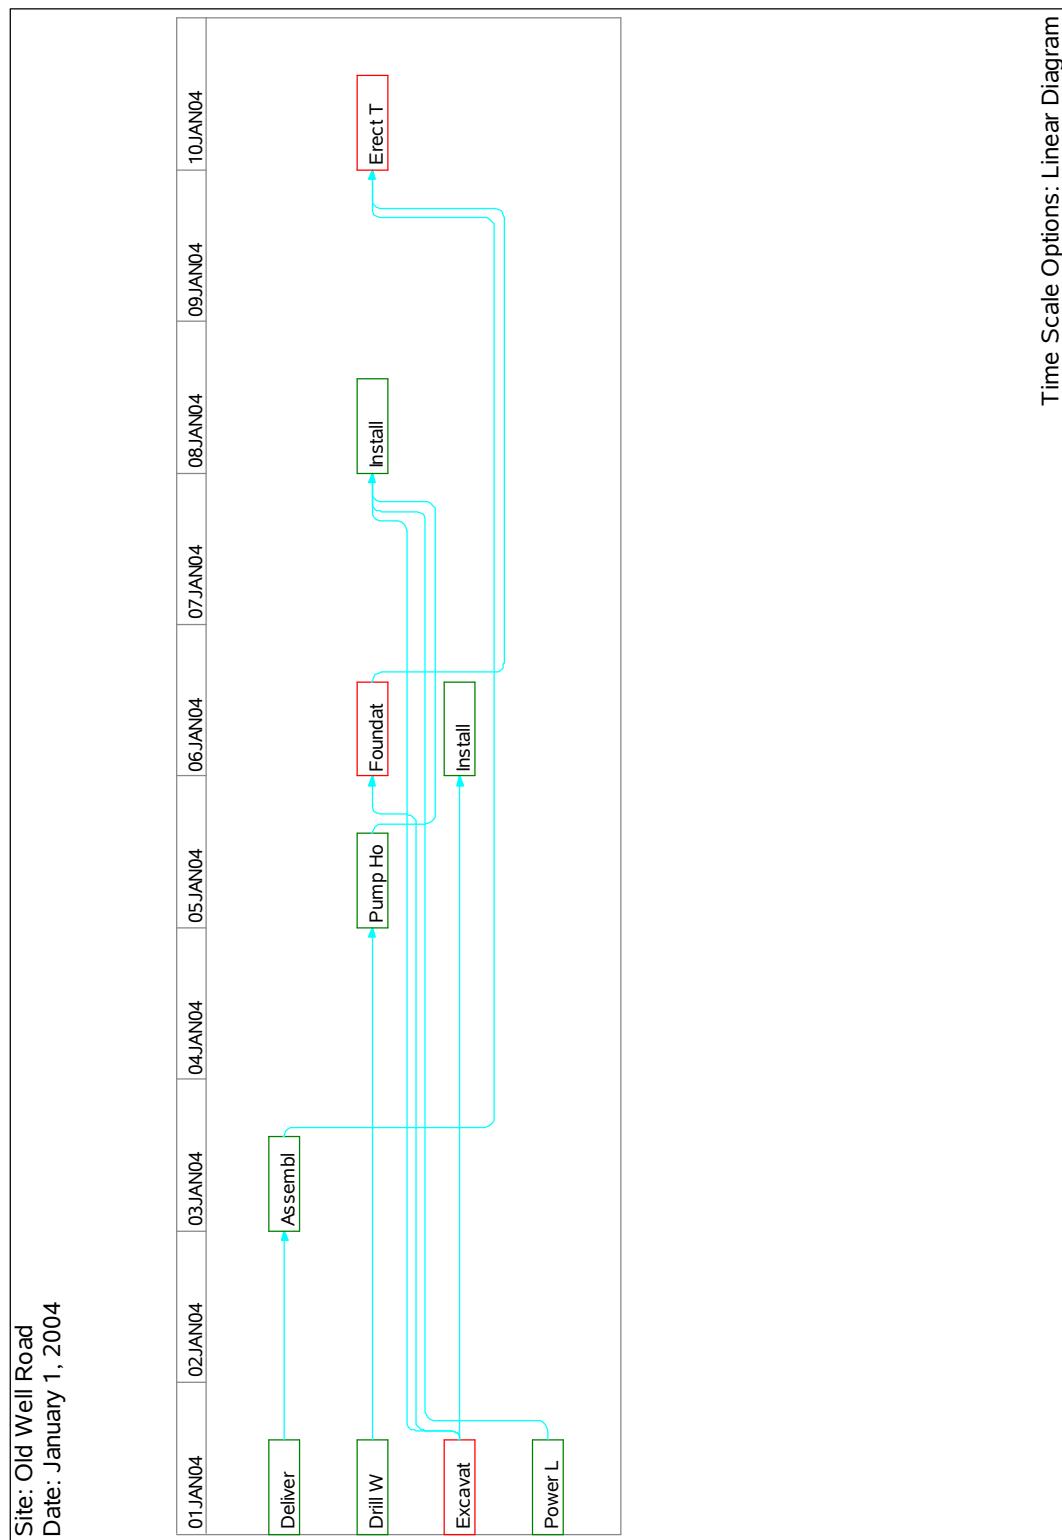
**Output 9.10.2** Time-Scaled Network: LINEAR Option

---

## Example 9.11: Zoned Network Diagram

This example illustrates zoned network diagrams. The Widget Manufacturing project is used to illustrate some aspects of this feature. The data set DETAILS contains a variable phase, which identifies the phase of each activity in the project. This data set is merged with the Activity data set from [Example 9.1](#), WIDGET, to produce the data set NETWORK that is input to PROC NETDRAW. The ZONE= option divides the network diagram into horizontal zones based on the project phase. The ZONEPAT option causes the activities in each zone to be drawn using a different pattern. The resulting network diagram is shown in [Output 9.11.1](#).

```

data details;
  format task $12. phase $13. descrpt $30. ;
  input task & phase $ descrpt & ;
  datalines;
Approve Plan   Planning      Develop Concept
Drawings       Engineering   Prepare Drawings
Study Market  Marketing     Analyze Potential Markets
Write Specs   Engineering   Write Specifications
Prototype     Engineering   Build Prototype
Mkt. Strat.   Marketing    Develop Marketing Concept
Materials     Manufacturing Procure Raw Materials
Facility      Manufacturing Prepare Manufacturing Facility
Init. Prod.   Manufacturing Initial Production Run
Evaluate      Testing       Evaluate Product In-House
Test Market   Testing       Test Product in Sample Market
Changes       Engineering   Engineering Changes
Production   Manufacturing Begin Full Scale Production
Marketing    Marketing    Begin Full Scale Marketing
;
data network;
  merge widget details;
  run;

pattern1 v=e c=green;
pattern2 v=e c=red;
pattern3 v=e c=magenta;
pattern4 v=e c=blue;
pattern5 v=e c=cyan;

title  j=l h=1.5 ' Project: Widget Manufacture';
title2 j=l h=1.5 ' Date: December 1, 2003';
footnote j=r h=1.5 'Zoned Network Diagram';

proc netdraw data=network graphics;
  actnet / act=task succ=(succ1 succ2 succ3)
           separatearcs
           zone=phase
           zonepat
           pcompress
           htext=2;
  label phase = 'Department';
  run;

```

Next, the project is scheduled with PROC CPM, and PROC NETDRAW is invoked with the ZONE= and TIMESCALE options. The nodes are placed in different zones as dictated by the ZONE variable, phase, and are aligned along the time axis as dictated by the default ALIGN variable, E\_START. The MININTERVAL= option produces one tick mark per week for the duration of the project. The LREF= option identifies the linestyle of the reference lines and the dividing lines between zones. The nodes are colored red or green according to whether or not the corresponding activities are critical (PATTERN statements 1 and 2 from the previous invocation of PROC NETDRAW are still valid).

```

proc cpm data=network interval=weekday
    out=sched date='1dec03'd;
activity task;
succ    succ1 succ2 succ3;
duration days;
id phase;
run;


title j=1 h=1.5 ' Project: Widget Manufacture';
title2 j=1 h=1.5 ' Date: December 1, 2003';
footnote j=r h=1.5 'Zone and Timescale ';
proc netdraw data=sched graphics;
actnet / act=task succ=(succ1 succ2 succ3)
pcompress
carcs = blue ccritarcs=red
cref = cyan
caxis = magenta
lref = 33
id = (task)
nodefid
nolabel
boxwidth = 8
htext=2
separatearcs
timescale
mininterval=week
autoref
linear
zone=phase
zonespace;
label phase = 'Department';
run;


```

## Example 9.12: Schematic Diagrams

You can use PROC NETDRAW to determine node placement and arc routing for any network depicting a set of nodes connected by arcs. If you want the procedure to determine the node placement, the network must be acyclic. This example illustrates the use of PROC NETDRAW to draw two networks that represent different schematic flows. The first network does not contain any cycles, while the second one has one cycle; to draw the second network, you need to use the BREAKCYCLE option.

First, a schematic representation of the data flow going in and out of the three procedures (CPM, GANTT, and NETDRAW) is drawn using PROC NETDRAW. (See Chapter 3, “Introduction to Project Management,”

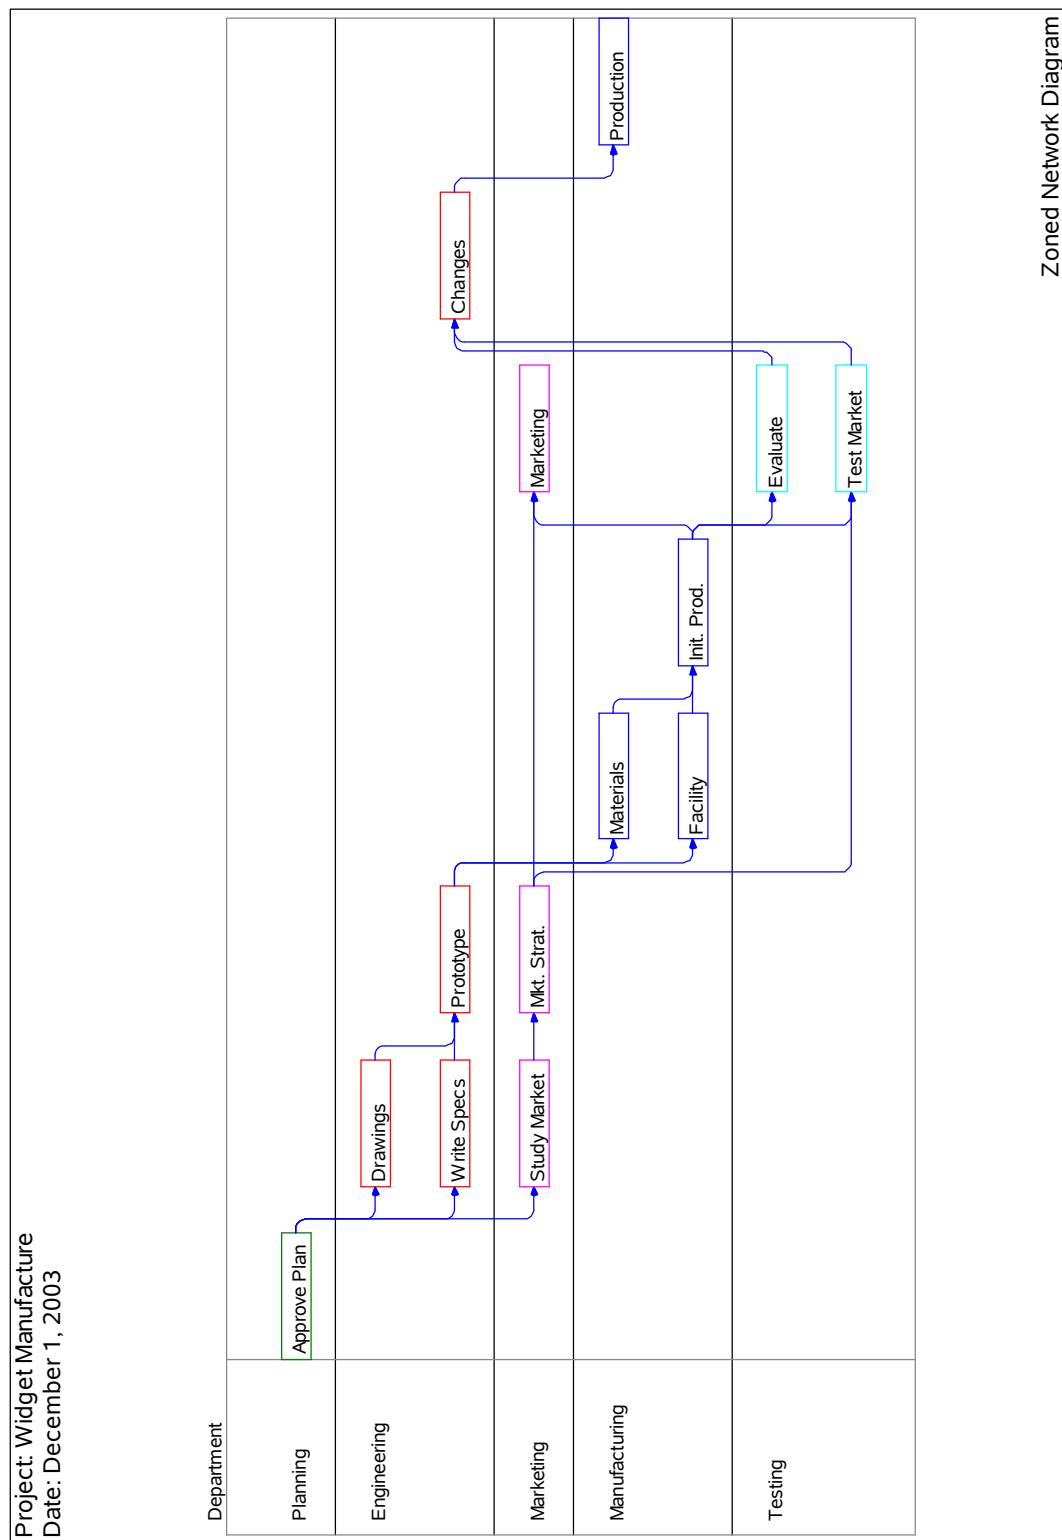**Output 9.11.1** Zoned Network Diagram

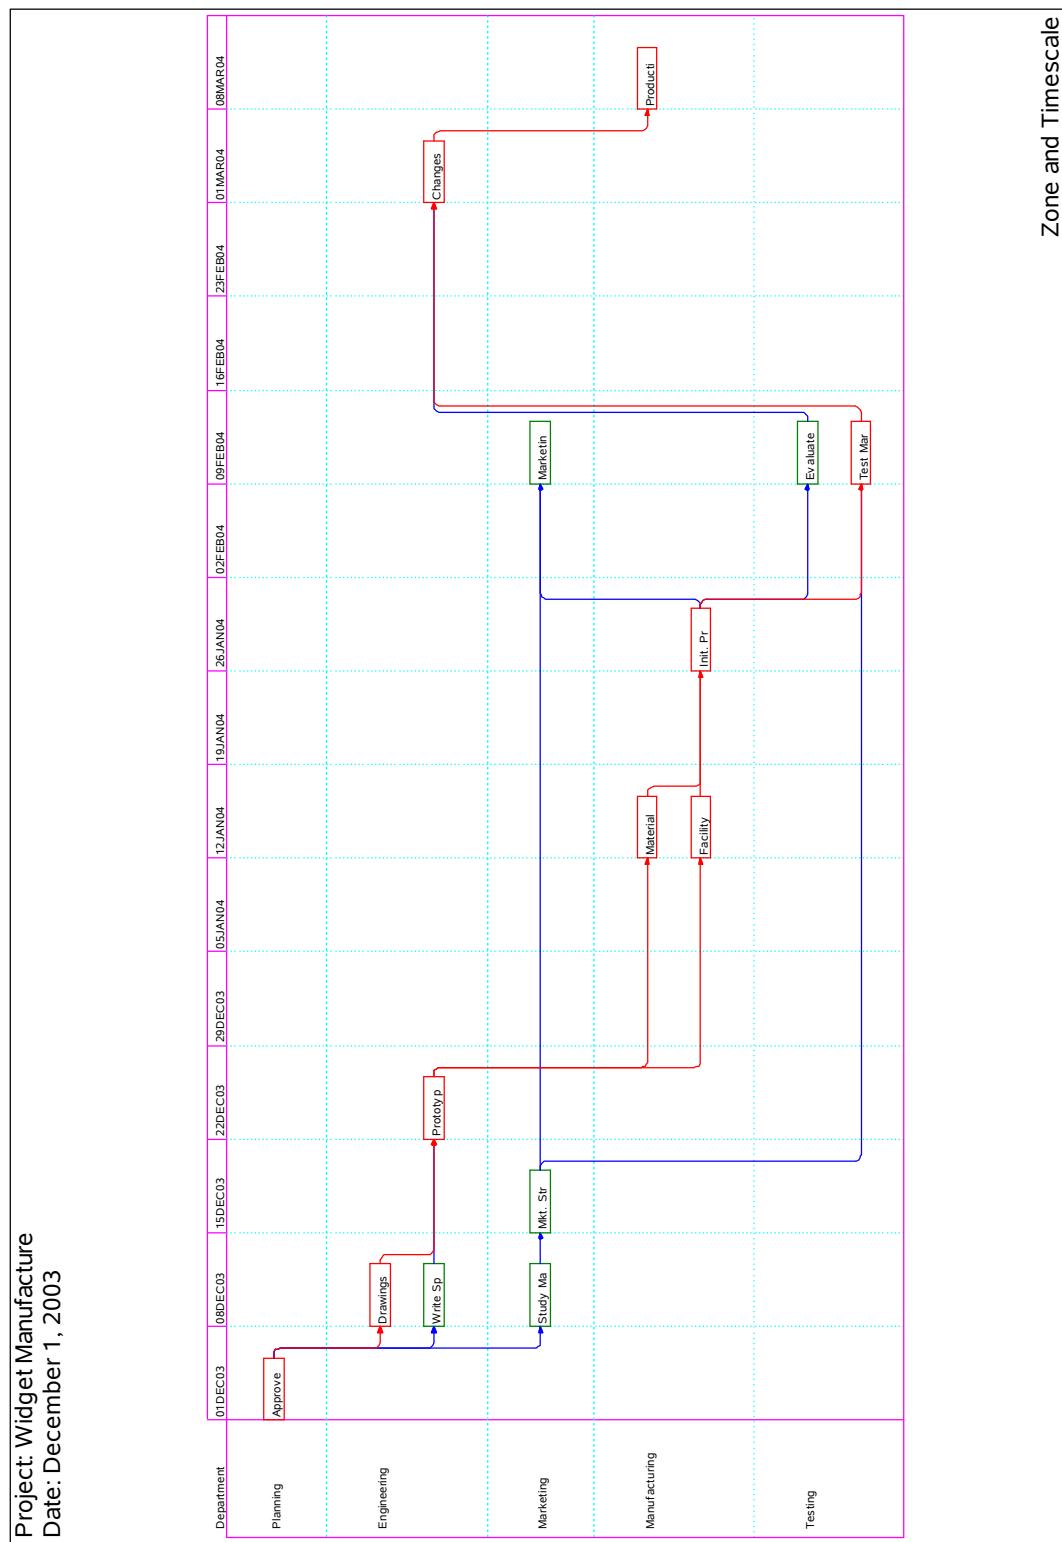**Output 9.11.2** Zoned Network Diagram with Time Axis

for a detailed discussion of such a data flow.) The PATTERN= option is used to specify the variable in the data set that identifies the color that is to be used for each node. Nodes representing SAS/OR procedures are colored red, the ones representing output data sets are colored green, and all other nodes (representing the use of other parts of the SAS System) are colored blue. Three ID variables are used to specify the text that is to be placed within each node. The flow diagram is shown in Output 9.12.1.

```


data dataflow;
  format id1 $18. id2 $14. id3 $19. ;
  input a $ b $ id1 & id2 & id3 & style;
 datalines;
A B Data Definition:    PROC FSEDIT,      SAS/AF, etc.      2
B C Data Manipulation:  Sort, Merge,     Concatenate, etc.  2
B D Data Manipulation:  Sort, Merge,     Concatenate, etc.  2
D C .                  PROC NETDRAW   .                   1
C E PROC CPM           .                  PROC PM          1
C F PROC CPM           .                  PROC PM          1
E H Resource Usage    .                  Data             3
F G .                  Schedule Data  .                   3
G I Data Manipulation: Sort, Merge,     Subset, etc.       2
G J Data Manipulation: Sort, Merge,     Subset, etc.       2
H K Data Manipulation: Sort, Merge,     Subset, etc.       2
I . Other Reporting    PROC's: PRINT,   CALENDAR, etc.    2
J . PROC GANTT         .                  PROC NETDRAW   1
K . Reporting PROC's:  PLOT, CHART,   GPLOT, GCHART, etc. 2
;


pattern1 v=s c=red;
pattern2 v=s c=blue;
pattern3 v=s c=green;

goptions hpos=110 vpos=70;
title h=3 'A Typical Project Management System';
title2 h=2.5 'Schematic Representation of Data Flow';
proc netdraw data=dataflow graphics;
  actnet / act=a succ=b id = (id1-id3)
    nodefaultid
    nolabel
    pattern=style
    carcs=black coutline=black ctext=white
    hmargin = 2
    ybetween = 15
    rectilinear
    noarrowfill
    pcompress htext=2;
run;

```

Next, a typical sequence of procedures followed at the scheduling of a nuclear power plant outage is shown using the NETDRAW procedure. Such a schematic diagram is illustrated in Chapter 3, “Introduction to Project Management.” In Figure 3.6, there is a cycle that is not normally allowed in a Network data set that is input to PROC NETDRAW. However, you can draw such networks by specifying the BREAKCYCLE option. (Note that you can also draw cyclic networks by specifying explicitly the node coordinates or an ALIGN= variable that fixes the *x* coordinates for each node.)

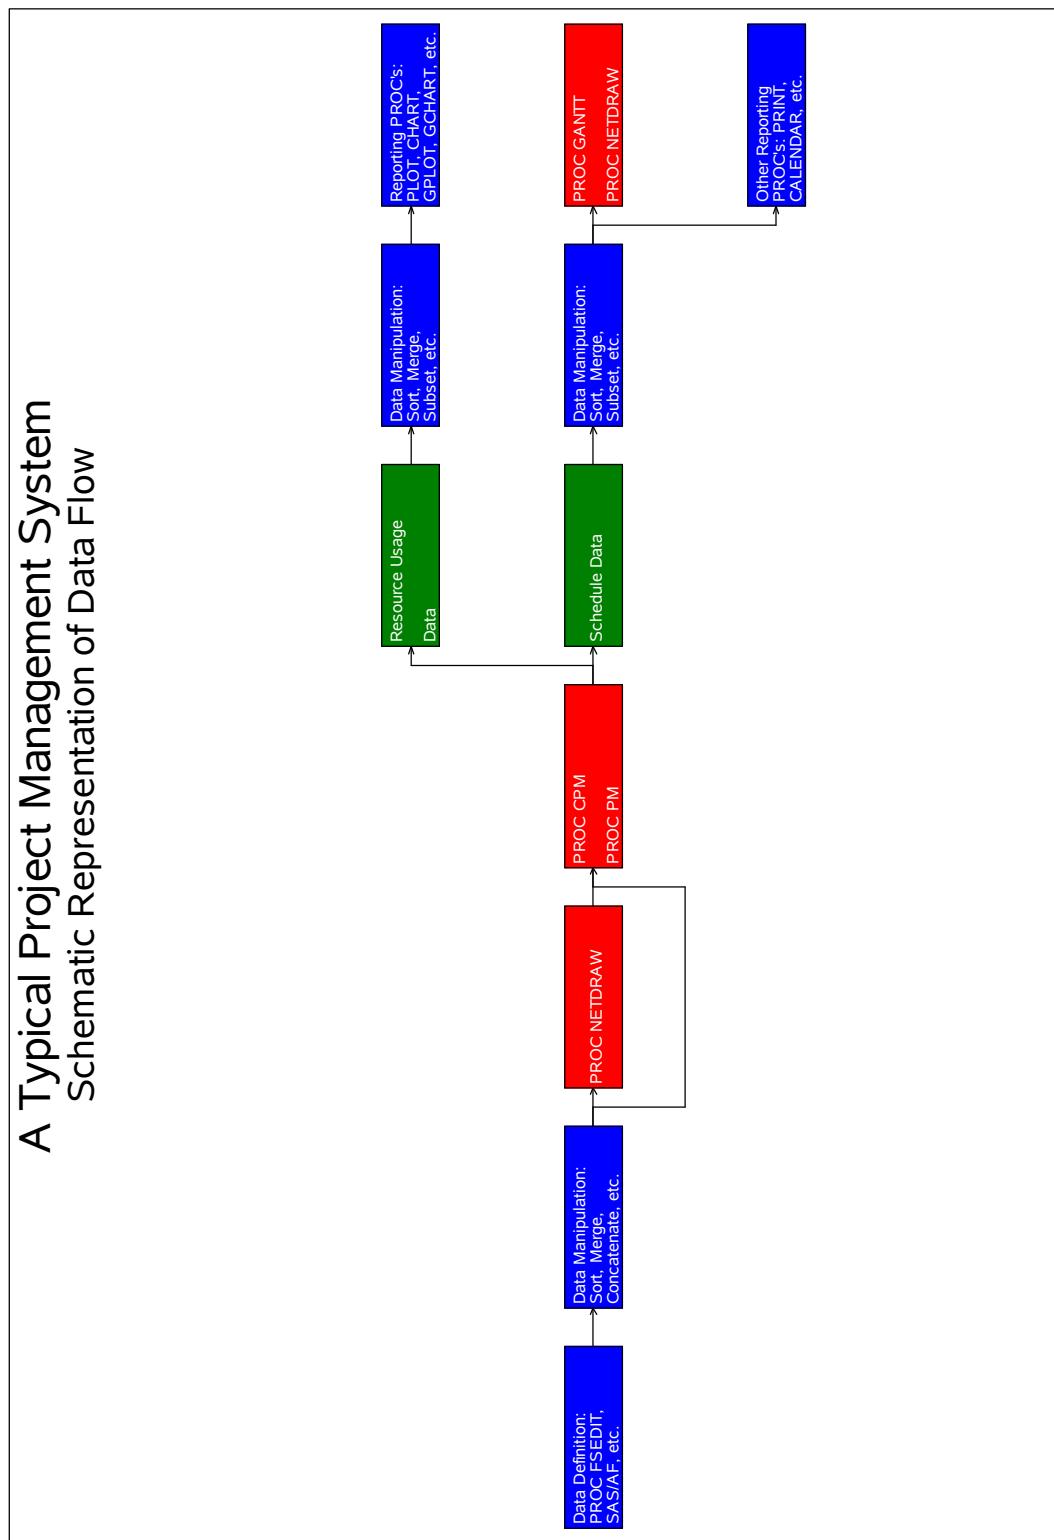**Output 9.12.1** Schematic Representation of Data Flow

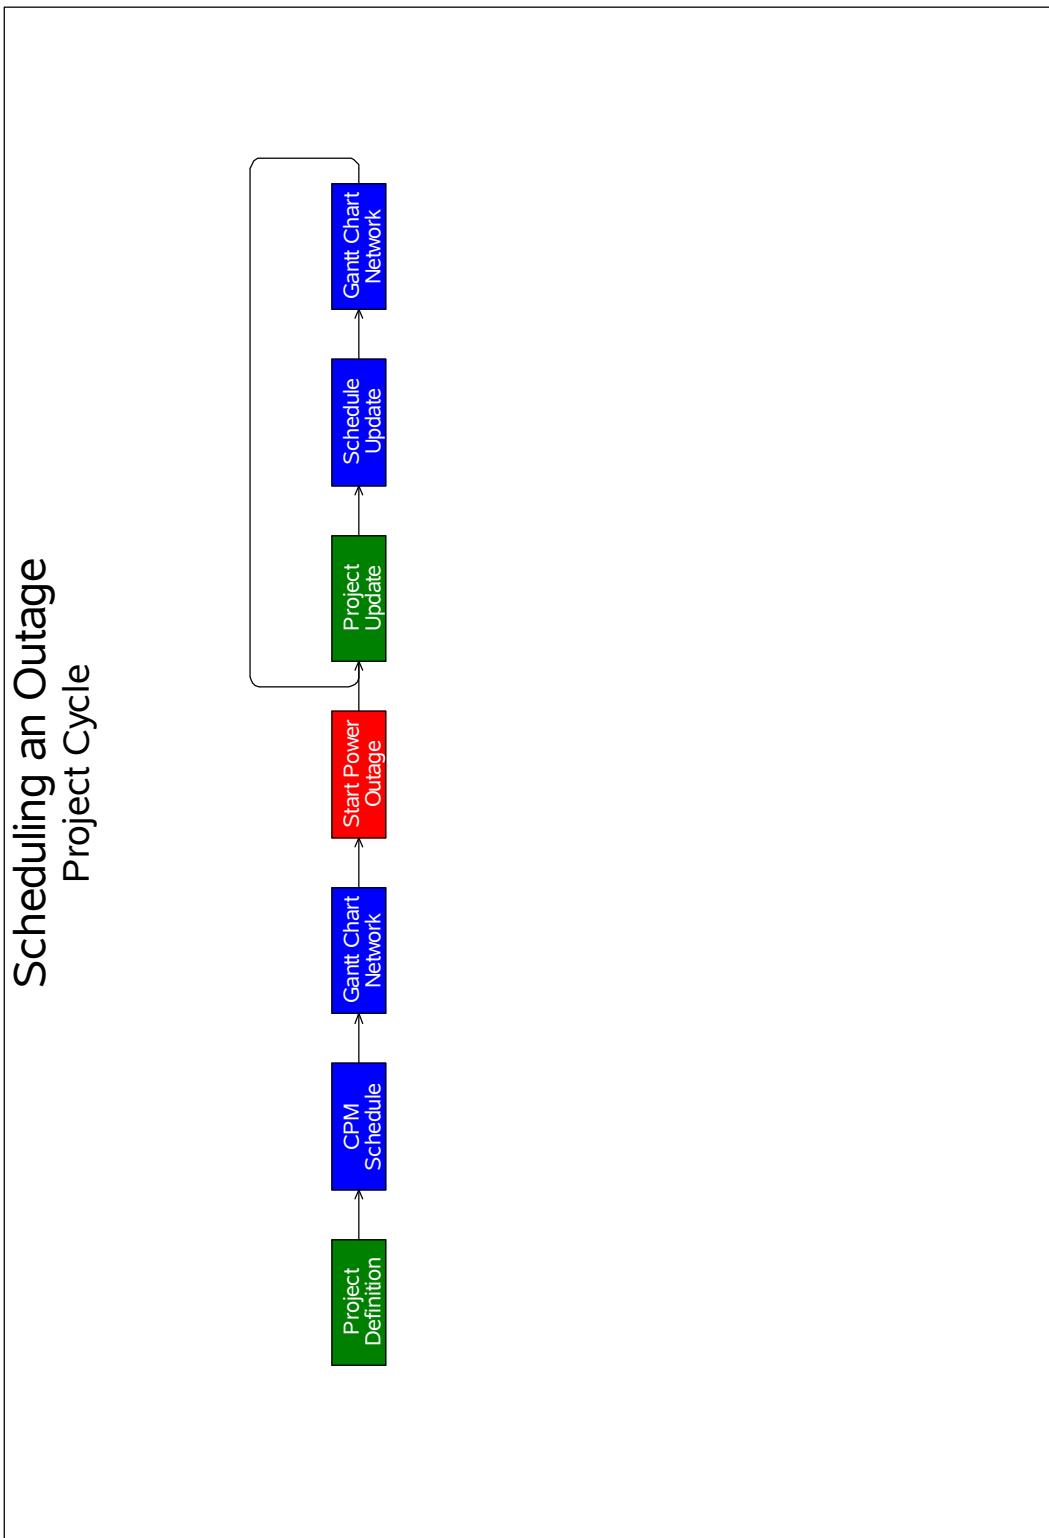**Output 9.12.2** Scheduling a Power Outage

In this example, the data set OUTAGE contains the network representation. The variable style is used to color nodes appropriately. The resulting diagram is shown in [Output 9.12.2](#).

```

data outage;
  input a $ b $ id1 $20.  id2 $20. style;
  datalines;
A   B   Project           Definition      1
B   C   CPM               Schedule        2
C   D   Gantt Chart       Network         3
D   E   Start Power       Outage          4
E   F   Project           Update          1
F   G   Schedule          Update          2
G   E   Gantt Chart       Network         3
;

goptions hpos=110 vpos=70;
title h=3 'Scheduling an Outage';
title2 h=2.5  'Project Cycle';

pattern1 v=s c=green;
pattern2 v=s c=blue;
pattern3 v=s c=blue;
pattern4 v=s c=red;

proc netdraw data=outage graphics;
  actnet / act=a succ=b id = (id1 id2)
    breakcycle
    nodefaultid centerid
    vmargin = 5 hmargin = 0
    nolabel novcenter
    pattern=style
    carcs=black coutline=black ctext=white
    ybetween = 15 xbetween=3
    noarrowfill
    pcompress htext=2;
run;

```

### Example 9.13: Modifying Network Layout

This example uses the SURVEY project described in Chapter 3, “[Introduction to Project Management](#),” to illustrate how you can modify the default layout of the network. The data set SURVEY contains the project information. PROC NETDRAW is invoked with the GRAPHICS option. The network diagram is shown in [Output 9.13.1](#).

```

data survey;
  format id $20. activity succ1-succ3 $8. phase $9. ;
  input id      &
        activity &
        duration
        succ1    &
        succ2    &
        succ3    &
        phase    $ ;
  datalines;
Plan Survey      plan sur   4 hire per  design q  .      Plan
Hire Personnel   hire per   5 trn per  .      .      Prepare
Design Questionnaire  design q  3 trn per  select h  print q  Plan
Train Personnel   trn per   3 cond sur  .      .      Prepare
Select Households  select h  3 cond sur  .      .      Prepare
Print Questionnaire  print q  4 cond sur  .      .      Prepare
Conduct Survey    cond sur  10 analyze  .      .      Implement
Analyze Results   analyze   6  .      .      .      Implement
;


pattern1 v=s c=green;

title j=1 h=3' Project: Market Survey';
title2 j=1 h=2 ' Changing Node Positions';
footnote j=r h=2 'Default Layout ';

proc netdraw data=survey graphics out=network;
  actnet / act=activity
          succ=(succ1-succ3)
          id=(id) nodefid nolabel
          carcs = blue
          ctext  = white
          coutline=red
          centerid
          boxht = 3
          htext=2
          pcompress
          separatearcs
          ybetween=8;
  run;

footnote;
title2 'NETWORK Output Data Set';
proc print data=network;
  run;

```

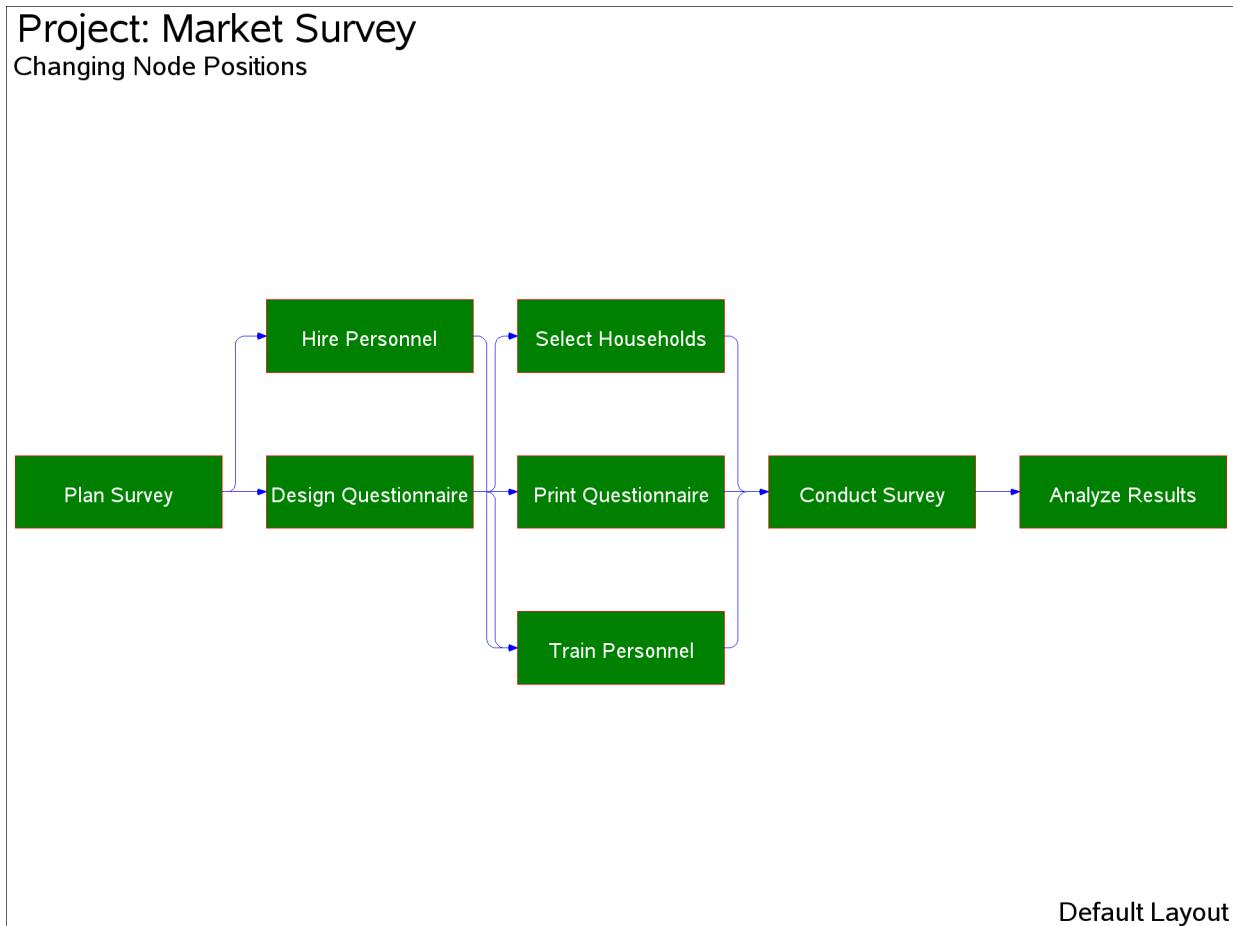**Output 9.13.1** Default Network Layout of SURVEY Project

The Layout data set produced by PROC NETDRAW (displayed in [Output 9.13.2](#)) contains the *x* and *y* coordinates for all the nodes in the network and for all the turning points of the arcs connecting them.

Suppose that you want to interchange the positions of the nodes corresponding to the two activities, ‘Select Households’ and ‘Train Personnel.’ As explained in the section “[Controlling the Layout](#)” on page 693, you can invoke the procedure in FULLSCREEN mode and use the MOVE command to move the nodes to desired locations. In this example, the data set NETWORK produced by PROC NETDRAW is used to change the *x* and *y* coordinates of the nodes. A new data set called NODEPOS is created from NETWORK by retaining only the observations containing node positions (recall that for such observations, *\_SEQ\_* = ‘0’) and by dropping the *\_SEQ\_* variable. Further, the *y* coordinates (given by the values of the *\_Y\_* variable) for the two activities ‘Select Households’ and ‘Train Personnel’ are interchanged. The new data set, displayed in [Output 9.13.3](#), is then input to PROC NETDRAW.

**Output 9.13.2** Layout Data Set**Project: Market Survey****NETWORK Output Data Set**

<b>Obs</b>	<b>_FROM_</b>	<b>_TO_</b>	<b>_X_</b>	<b>_Y_</b>	<b>_SEQ_</b>	<b>_PATTERN id</b>
<b>1</b>	plan sur	hire per	1.0	2	0	1 Plan Survey
<b>2</b>	plan sur	hire per	1.5	2	1	. Plan Survey
<b>3</b>	plan sur	hire per	1.5	3	2	. Plan Survey
<b>4</b>	plan sur	design q	1.0	2	0	1 Plan Survey
<b>5</b>	hire per	trn per	2.0	3	0	1 Hire Personnel
<b>6</b>	hire per	trn per	2.5	3	1	. Hire Personnel
<b>7</b>	hire per	trn per	2.5	1	2	. Hire Personnel
<b>8</b>	design q	trn per	2.0	2	0	1 Design Questionnaire
<b>9</b>	design q	trn per	2.5	2	1	. Design Questionnaire
<b>10</b>	design q	trn per	2.5	1	2	. Design Questionnaire
<b>11</b>	design q	select h	2.0	2	0	1 Design Questionnaire
<b>12</b>	design q	select h	2.5	2	1	. Design Questionnaire
<b>13</b>	design q	select h	2.5	3	2	. Design Questionnaire
<b>14</b>	design q	print q	2.0	2	0	1 Design Questionnaire
<b>15</b>	trn per	cond sur	3.0	1	0	1 Train Personnel
<b>16</b>	trn per	cond sur	3.5	1	1	. Train Personnel
<b>17</b>	trn per	cond sur	3.5	2	2	. Train Personnel
<b>18</b>	select h	cond sur	3.0	3	0	1 Select Households
<b>19</b>	select h	cond sur	3.5	3	1	. Select Households
<b>20</b>	select h	cond sur	3.5	2	2	. Select Households
<b>21</b>	print q	cond sur	3.0	2	0	1 Print Questionnaire
<b>22</b>	cond sur	analyze	4.0	2	0	1 Conduct Survey
<b>23</b>	analyze		5.0	2	0	1 Analyze Results

```

data nodepos;
  set network;
  if _seq_ = 0;
  drop _seq_;
  if _from_ = 'select h' then _y_=1;
  if _from_ = 'trn per' then _y_=3;
  run;

title2 'Modified Node Positions';
proc print data=nodepos;
  run;

```

### Output 9.13.3 Modified Layout Data Set

**Project: Market Survey**

**Modified Node Positions**

Obs	_FROM_	_TO_	_X_	_Y_	PATTERN	id
1	plan sur	hire per	1	2	1	Plan Survey
2	plan sur	design q	1	2	1	Plan Survey
3	hire per	trn per	2	3	1	Hire Personnel
4	design q	trn per	2	2	1	Design Questionnaire
5	design q	select h	2	2	1	Design Questionnaire
6	design q	print q	2	2	1	Design Questionnaire
7	trn per	cond sur	3	3	1	Train Personnel
8	select h	cond sur	3	1	1	Select Households
9	print q	cond sur	3	2	1	Print Questionnaire
10	cond sur	analyze	4	2	1	Conduct Survey
11	analyze		5	2	1	Analyze Results


Note that the data set NODEPOS contains variables named \_FROM\_ and \_TO\_, which specify the (activity, successor) information; hence, the call to PROC NETDRAW does not contain the ACTIVITY= and SUCCESSOR= specifications. The presence of the variables \_X\_ and \_Y\_ indicates to PROC NETDRAW that the data set contains the x and y coordinates for all the nodes. Because there is no variable named \_SEQ\_ in this data set, PROC NETDRAW assumes that only the node coordinates are given and uses these node positions to determine how the arcs are to be routed. The resulting network diagram is shown in Output 9.13.4.

```

title j=1 h=3 ' Project: Market Survey';
title2 j=1 h=2 ' Changing Node Positions';
footnote j=r h=2 'Modified Network Layout ';

proc netdraw data=nodepos graphics;
  actnet / id=(id) nodefid nolabel
    carcs = blue
    ctext = white
    coutline = red
    centerid
    boxht = 3
    htext=2
    pcompress
    separatearcs
    ybetween=8;
run;

```

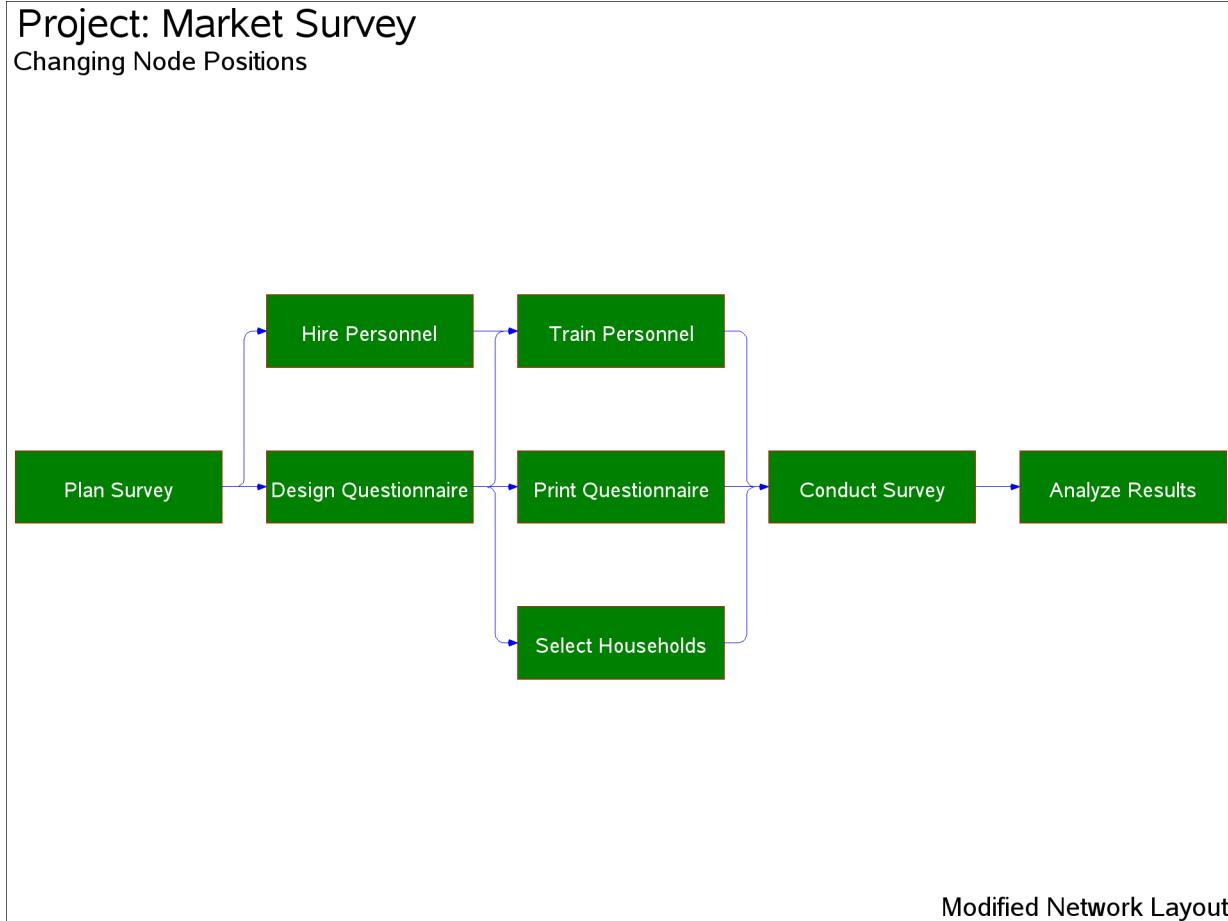**Output 9.13.4** Modified Network Layout of SURVEY Project**Example 9.14: Specifying Node Positions**

This example uses a typical problem in network flow optimization to illustrate how you can use PROC NETDRAW to draw a network by specifying completely all the node positions. Consider a simple two-period production inventory problem with one manufacturing plant (PLANT), two warehouses (DEPOT1 and DEPOT2), and one customer (CUST). In each period, the customer can receive goods directly from the plant or from the two warehouses. The goods produced at the plant can be used to satisfy directly some or all of the customer's demands or can be shipped to a warehouse. Some of the goods can also be carried over to the next period as inventory at the plant. The problem is to determine the minimum cost of satisfying the customer's demands; in particular, how much of the customer's demands in each period is to be satisfied from the inventory at the two warehouses or from the plant, and also how much of the production is to be carried over as inventory at the plant? This problem can be solved using PROC NETFLOW; the details are not discussed here. Let PLANT<sub>i</sub> represent the production at the plant in period *i*, DEPOT1<sub>i</sub> represent the inventory at DEPOT1 in period *i*, DEPOT2<sub>i</sub> represent the inventory at DEPOT2 in period *i*, and CUST<sub>i</sub> represent the customer's demand in period *i* (*i* = 1, 2). These variables can be thought of as nodes in a network with the following data representing the COST and CAPACITY of the arcs connecting them:

FROM	TO	COST	CAPACITY
PLANT_1	CUST_1	10	75
PLANT_1	DEPOT1_1	7	75
PLANT_1	DEPOT2_1	8	75
DEPOT1_1	CUST_1	3	20
DEPOT2_1	CUST_1	2	10
PLANT_1	PLANT_2	2	100
DEPOT1_1	DEPOT1_2	1	100
DEPOT2_1	DEPOT2_2	1	100
PLANT_2	CUST_2	10	75
PLANT_2	DEPOT1_2	7	75
PLANT_2	DEPOT2_2	8	75
DEPOT1_2	CUST_2	3	20
DEPOT2_2	CUST_2	2	10
CUST_1	.	.	.
CUST_2	.	.	.

Suppose that you want to use PROC NETDRAW to draw the network corresponding to the preceding network flow problem and suppose also that you require the nodes to be placed in specific positions. The following program saves the network information along with the required node coordinates in the Network data set ARCS and invokes PROC NETDRAW to draw the network diagram shown in Output 9.14.1. The Network data set also contains a variable named \_pattern, which specifies that pattern statement 1 be used for nodes relating to period 1 and pattern statement 2 be used for those relating to period 2.

```

data arcs;
  input from $  to $  _x_ _y_ _pattern;
  datalines;
PLANT_1 CUST_1      1  5  1
PLANT_1 DEPOT1_1    1  5  1
PLANT_1 DEPOT2_1    1  5  1
DEPOT1_1 CUST_1     2  6  1
DEPOT2_1 CUST_1     2  4  1
PLANT_1 PLANT_2     1  5  1
DEPOT1_1 DEPOT1_2   2  6  1
DEPOT2_1 DEPOT2_2   2  4  1
PLANT_2 CUST_2      4  2  2
PLANT_2 DEPOT1_2    4  2  2
PLANT_2 DEPOT2_2    4  2  2
DEPOT1_2 CUST_2     5  3  2
DEPOT2_2 CUST_2     5  1  2
CUST_1   .
CUST_2   .
;

title c=blue 'Distribution Network';
pattern1 v=s  c=green;
pattern2 v=s  c=red;
proc netdraw data=arcs graphics out=netout;
  actnet / act=from succ=to separatearcs
    ybetween = 4
    centerid
    ctext = white

```


```

carcs=blue
htext=2
pcompress;
run;

```

**NOTE:** This network diagram can also be drawn by using suitably defined ZONE and ALIGN variables.

#### Output 9.14.1 Distribution Network

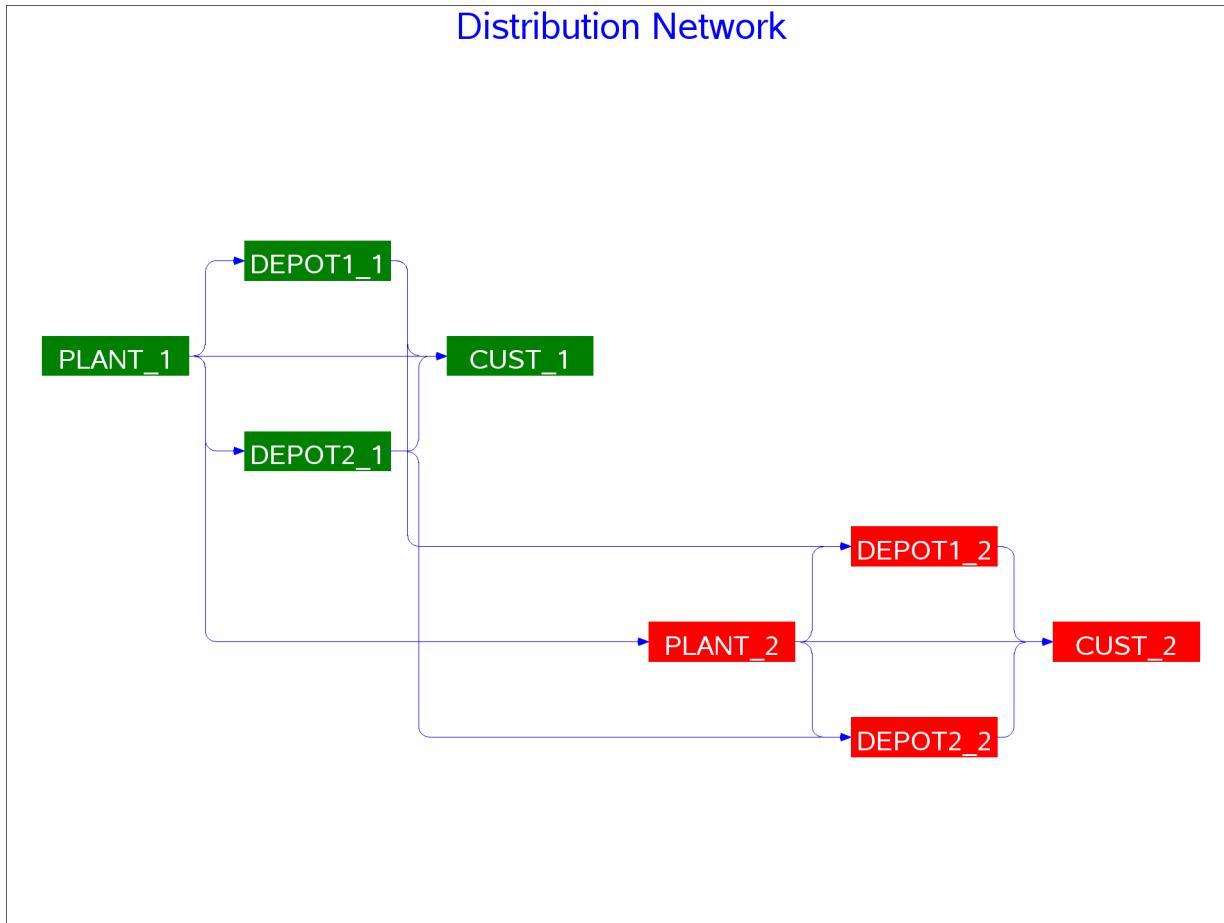


---

#### Example 9.15: Organizational Charts with PROC NETDRAW

This example illustrates using the TREE option to draw organizational charts. The Network data set, DOCUMENT, describes how the procedures are distributed between two volumes of the SAS/OR documentation. The structure can be visualized easily in a tree diagram. The data set DOCUMENT contains the parent-child relationship for each node of the diagram. For each node, a detailed description is contained in the variable ID. In addition, the variable \_pattern specifies the pattern to be used for each node. PROC NETDRAW is invoked with the TREE option, which illustrates the organization of the documentation in the form of a tree diagram drawn from left to right. The CENTERID option centers text within each node. Arrowheads are not necessary for this diagram and are suppressed by specifying ARROWHEAD=0. Output 9.15.1 shows the resulting diagram.


```

data document;
  format parent child $8. id $24.;
  input parent $ child $ id & _pattern;
  datalines;
OR      MPBOOK      Operations Research      1
OR      PMBOOK      Operations Research      1
PMBOOK  CPM        Project Management     2
PMBOOK  DTREE       Project Management     2
PMBOOK  GANTT       Project Management     2
PMBOOK  NETDRAW     Project Management     2
PMBOOK  PM         Project Management     2
PMBOOK  PROJMAN    Project Management     2
MPBOOK  OPTMODEL   Mathematical Programming 3
MPBOOK  OPTLP      Mathematical Programming 3
MPBOOK  OPTMILP    Mathematical Programming 3
MPBOOK  OPTQP      Mathematical Programming 3
CPM     .           CPM Procedure          2
DTREE   .           DTREE Procedure         2
GANTT   .           GANTT Procedure         2
NETDRAW .           NETDRAW Procedure       2
PM      .           PM Procedure           2
PROJMAN .          PROJMAN Application     2
OPTMODEL .         OPTMODEL Procedure       3
OPTLP   .           OPTLP Procedure         3
OPTMILP .          OPTMILP Procedure       3
OPTQP   .           OPTQP Procedure         3
;

pattern1 v=s c=blue;
pattern2 v=s c=red;
pattern3 v=s c=green;

title j=1 h=3 'Operations Research Documentation';
title2 j=1 h=2 'Procedures in Each Volume';
footnote j=r h=2 'Default Tree Layout ';
proc netdraw graphics data=document;
  actnet / act=parent
            succ=child
            id=(id)
            nodefid
            nolabel
            pcompress
            centerid
            tree
            xbetween=15
            ybetween=3
            arrowhead=0
            rectilinear
            carcs=black
            ctext=white
            htext=3;
run;

```

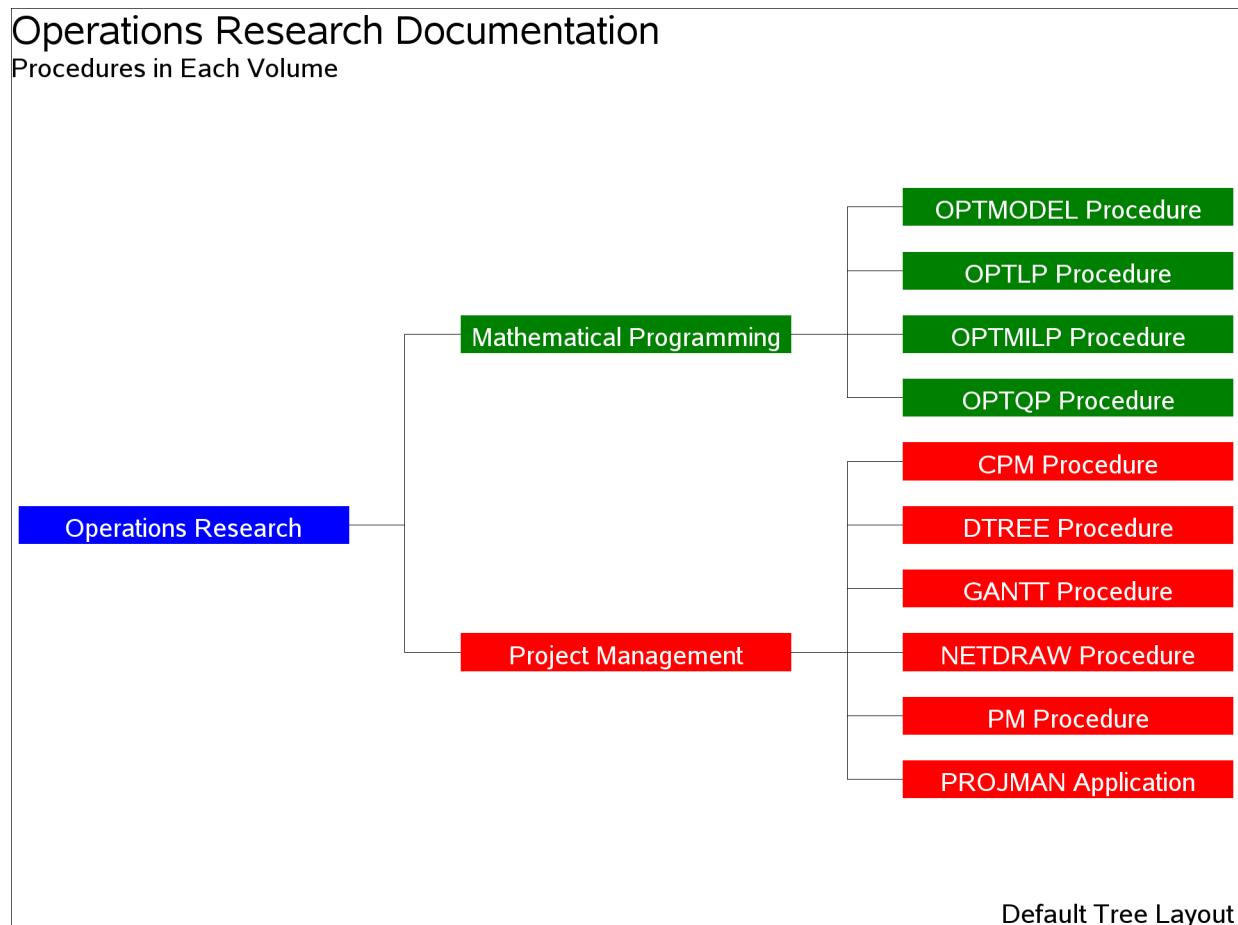**Output 9.15.1** Organization of Documentation: Default TREE Layout

The procedure draws the tree compactly with the successors of each node being placed to the immediate right of the node, ordered from top to bottom in the order of occurrence in the Network data set. The next invocation of PROC NETDRAW illustrates the effect of the SEPARATESONS and CENTERSUBTREE options on the layout of the tree (see [Output 9.15.2](#)).

```


footnote j=r h=1.5 'Centered Tree Layout ';
proc netdraw graphics data=document;
  actnet / act=parent
    succ=child
    id=(id)
    nodefid
    nolabel
    pcompress
    novcenter
    centerid
    tree
    separatesons
    centersubtree
    xbetween=15
    ybetween=3
    arrowhead=0
  
```

```

rectilinear
carcs=black
ctext=white
htext=3.5;
run;

```

#### Output 9.15.2 Organization of Documentation: Controlled TREE Layout

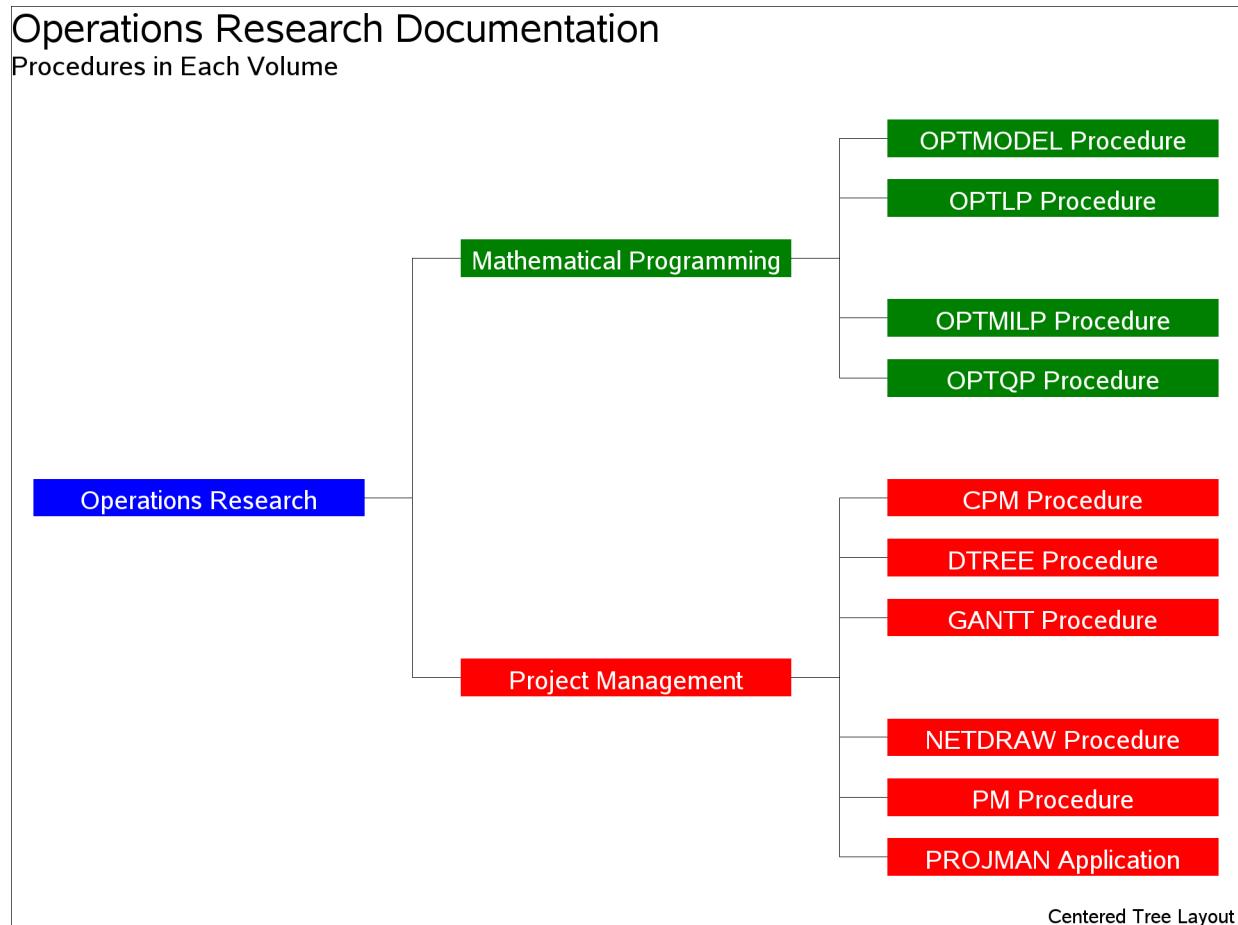

#### Example 9.16: Annotate Facility with PROC NETDRAW

This example demonstrates the use of PROC NETDRAW for a nonstandard application. The procedure is used to draw a time table for a class of students. The days of the week are treated as different zones, and the times within a day are treated as different values of an alignment variable. The following DATA step defines a total of twenty activities, ‘m1’, . . . ,‘f5’, which refer to the five different periods for the five different days of the week. The variable class contains the name of the subject taught in the corresponding period and day. Note that the periods are taught during the hours 1, 2, 3, 5, and 6; the fourth hour is set aside for lunch. The time axis is labeled with the format CLASSTIM, which is defined using PROC FORMAT. The USEFORMAT option in the ACTNET statement instructs PROC NETDRAW to use the explicit format specified for the time variable rather than the default format.

This example also illustrates the use of the Annotate facility with PROC NETDRAW. The data set ANNO labels the fourth period ‘LUNCH.’ The positions for the text are specified using data coordinates that refer to

the (\_X\_, \_Y\_) grid used by PROC NETDRAW. Thus, for example X = ‘4’ identifies the *x* coordinate for the annotated text to be the fourth period, and the *y* coordinates are set appropriately. The resulting time table is shown in [Output 9.16.1](#).

```

/* Define format for the ALIGN= variable */
proc format;
  value classtim 1 = ' 9:00 - 10:00'
    2 = '10:00 - 11:00'
    3 = '11:00 - 12:00'
    4 = '12:00 - 1:00 '
    5 = ' 1:00 - 2:00 '
    6 = ' 2:00 - 3:00 ';
run;

data schedule;
  format day $9. class $12. ;
  input day $ class & time daytime $ msucc $;
  format time classtim. ;
  label day = "Day \ Time";
  datalines;
Monday   Mathematics   1   m1   .
Monday   Language      2   m2   .
Monday   Soc. Studies  3   m3   .
Monday   Art           5   m4   .
Monday   Science       6   m5   .
Tuesday  Language      1   t1   .
Tuesday  Mathematics  2   t2   .
Tuesday  Science       3   t3   .
Tuesday  Music          5   t4   .
Tuesday  Soc. Studies  6   t5   .
Wednesday Mathematics  1   w1   .
Wednesday Language     2   w2   .
Wednesday Soc. Studies 3   w3   .
Wednesday Phys. Ed.    5   w4   .
Wednesday Science      6   w5   .
Thursday  Language     1   th1  .
Thursday  Mathematics  2   th2  .
Thursday  Science       3   th3  .
Thursday  Phys. Ed.    5   th4  .
Thursday  Soc. Studies 6   th5  .
Friday   Mathematics  1   f1   .
Friday   Language      2   f2   .
Friday   Soc. Studies  3   f3   .
Friday   Library        5   f4   .
Friday   Science       6   f5   .
;
data anno;
  /* Set up required variable lengths, etc. */
  length function color style   $8;
  length xsys ysys hsys         $1;
  length when position         $1;

  xsys      = '2';

```

```
ysys      = '2';
hsys      = '4';
when      = 'a';

function = 'label    ';
x = 4;
size = 2;
position = '5';
y=5; TEXT='L'; output;
y=4; TEXT='U'; output;
y=3; TEXT='N'; output;
y=2; TEXT='C'; output;
y=1; TEXT='H'; output;
run;

pattern1 v=s c=pink;
title 'Class Schedule: 2003-2004';
footnote j=1 h=2 ' Teacher: Mr. A. Smith Hall'
          j=r h=2 'Room: 107  ';
proc netdraw graphics data=schedule anno=anno;
  actnet / act=daytime
           succ=msucc
           id=(class)
           nodefid nolabel
           zone=day
           align=time
           useformat
           linear
           pcompress
           coutline=black
           hmargin = 2 vmargin = 2
           htext=2;
run;
```

**Output 9.16.1** Use of the Annotate Facility

Class Schedule: 2003-2004						
Day \ Time	9:00 - 10:00	10:00 - 11:00	11:00 - 12:00	12:00 - 1:00	1:00 - 2:00	2:00 - 3:00
Monday	Mathematics	Language	Soc. Studies	L	Art	Science
Tuesday	Language	Mathematics	Science	U	Music	Soc. Studies
Wednesday	Mathematics	Language	Soc. Studies	N	Phys. Ed.	Science
Thursday	Language	Mathematics	Science	C	Phys. Ed.	Soc. Studies
Friday	Mathematics	Language	Soc. Studies	H	Library	Science

Teacher: Mr. A. Smith Hall      Room: 107

**Example 9.17: AOA Network Using the Annotate Facility**

This example illustrates the use of the Annotate Facility to draw an Activity-on-Arc network. First, PROC NETDRAW is invoked with explicit node positions for the vertices of the network. The ALIGN= and ZONE= options are used to provide horizontal and vertical axes as a frame of reference. The resulting diagram is shown in [Output 9.17.1](#).

```
data widgaoa;
  format task $12. ;
  input task & days tail head _x_ _y_;
  datalines;
Approve Plan    5   1   2   1   2
Drawings        10  2   3   4   2
Study Market   5   2   4   4   2
Write Specs    5   2   3   4   2
Prototype      15  3   5   7   1
Mkt. Strat.    10  4   6   10  3
Materials       10  5   7   10  1
Facility        10  5   7   10  1
Init. Prod.    10  7   8   13  1
```

```

Evaluate      10   8   9   16  1
Test Market  15   6   9   18  2
Changes       5    9   10  20  1
Production    0   10  11  23  1
Marketing     0    6   12  19  2
Dummy        0    8   6   16  1
.          .   11   .  26  1
.          .   12   .  22  3
;

pattern1 v=e c=red;
title j=1 h=3 ' Project: Widget Manufacture';
title2 j=1 h=2 ' Network in Activity-on-Arc Format';
footnote j=r h=2 'Initial Layout';

proc netdraw graphics data=widgaoa out=netout;
  actnet / act=tail
    succ=head
    id=(tail)
    align=_x_
    zone=_y_
    ybetween = 10
    nodefid
    nolabel
    pcompress
    htext=2;
  label _y_=' Y \ X ';
run;

```


In Output 9.17.1, the arc leading from vertex ‘4’ to vertex ‘6’ has two turning points: (10.5, 3) and (10.5, 2). Suppose that you want the arc to be routed differently, to provide a more symmetric diagram. The next DATA step creates a data set, NETIN, which changes the *x* coordinates of the turning points to 16.5 instead of 10.5. Further, two Annotate data sets are created: the first one labels the nodes outside the boxes, either to the top or to the bottom, and the second one sets labels for the arcs. PROC NETDRAW is then invoked with the combined Annotate data set to produce the diagram shown in Output 9.17.2.

```

data netin;
  set netout;
  if _from_=4 and _to_=6 and _seq_>0 then _x_=16.5;
run;

data anno1;
  set netout;
  if _seq_=0;
  /* Set up required variable lengths, etc. */
  length function color style   $8;
  length xsys ysys hsys         $1;
  length when position         $1;
  length TEXT                  $12;
  xsys      = '2';
  ysys      = '2';
  hsys      = '4';
  when     = 'a';
  function = 'label    ';
  size      = 2;

```

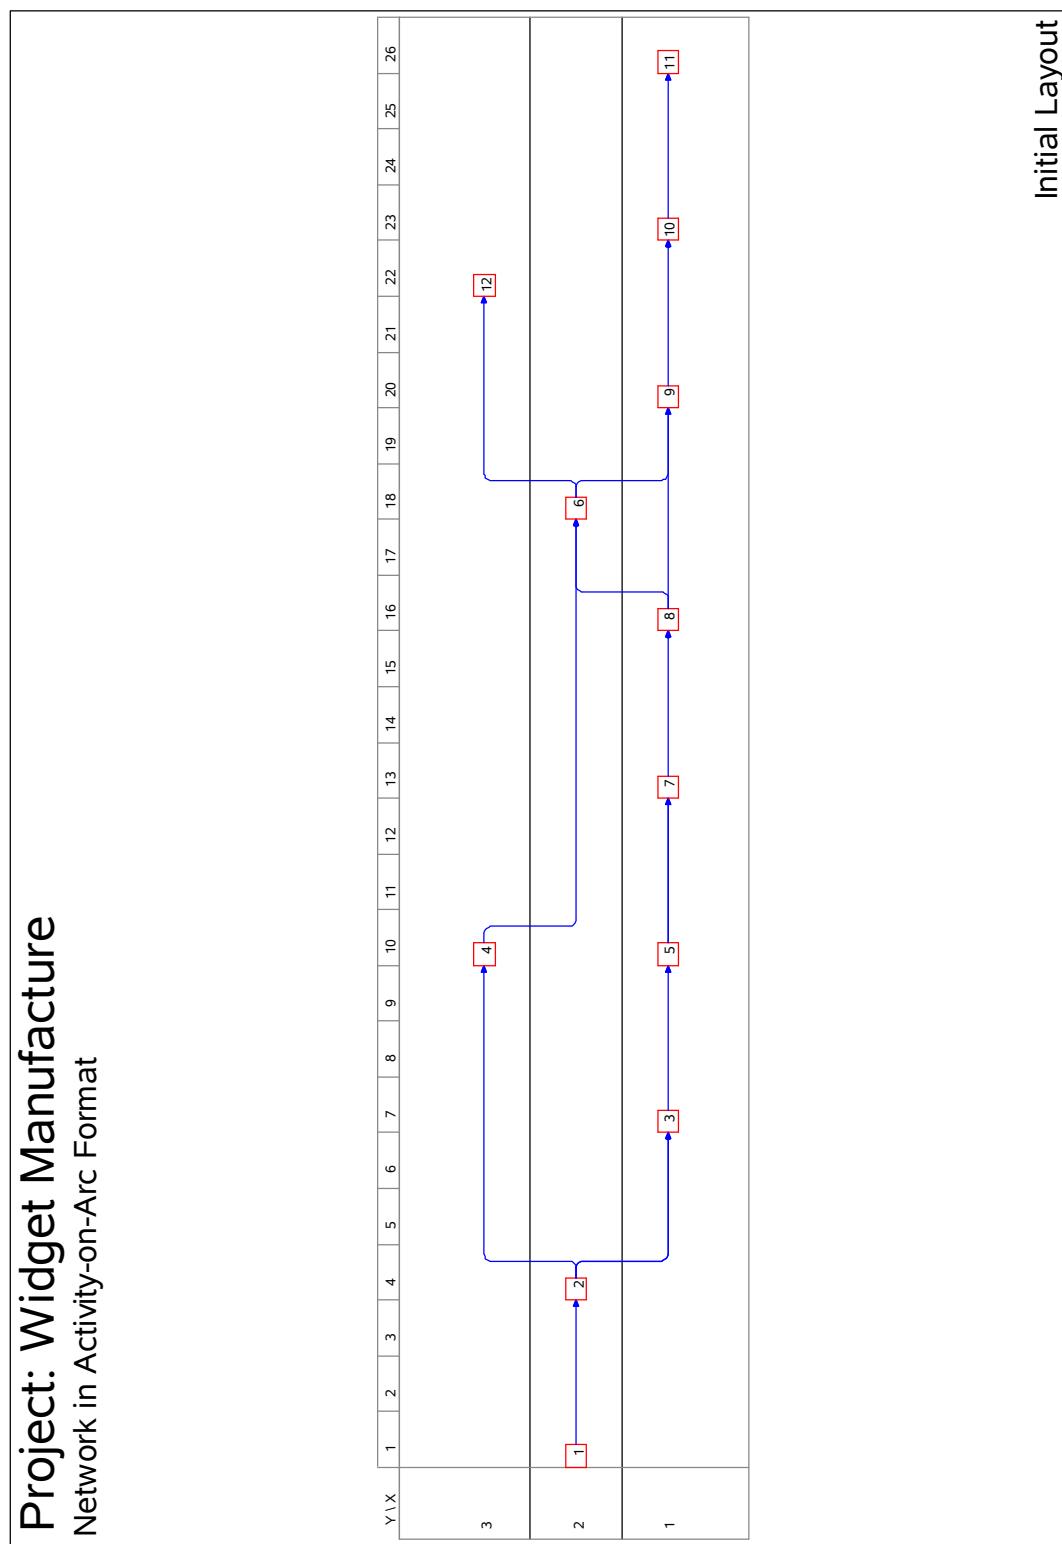**Output 9.17.1** Activity-on-Arc Format

```

position = '5';
TEXT = left(put(tail, f2.));
x=_x_;
if _y_ = 1 then y=_y_-.3;
else           y=_y_+.5;
run;

data anno2;
/* Set up required variable lengths, etc. */
length function color style   $8;
length xsys ysys hsys          $1;
length when position         $1;
length TEXT                  $12;
xsys      = '2';
ysys      = '2';
hsys      = '4';
when      = 'a';
function = 'label    ';
size = 2;
position = '5';
x=2.5;  y=1.8;  TEXT='Approve Plan'; output;
x=5.5;  y=.8;   TEXT='Drawings';       output;
x=5.7;  y=1.4;  TEXT='Write Specs';  output;
x=7;    y=3.4;  TEXT='Study Market'; output;
x=8.5;  y=.8;   TEXT='Prototype';    output;
x=11.5; y=1.4;  TEXT='Facility';     output;
x=11.5; y=.8;   TEXT='Materials';   output;
x=14.5; y=.9;   TEXT='Init. Prod';  output;
x=13.5; y=3.4;  TEXT='Mkt. Strat.'; output;
x=18;   y=.8;   TEXT='Evaluate';    output;
x=21.5; y=.8;   TEXT='Changes';     output;
x=24.5; y=.8;   TEXT='Production'; output;
x=20;   y=3.4;  TEXT='Marketing';   output;
position=6;
x=16.6; y=1.5; TEXT='Dummy';        output;
x=18.6; y=1.5; TEXT='Test Market'; output;
;

data anno;
  set anno1 anno2;
  run;

footnote j=r h=2 'Annotated and Modified Layout ';
pattern1 v=s c=red;

proc netdraw graphics data=netin anno=anno;
  actnet / nodefid
          nolabel
          boxwidth=1
          pcompress
          novcenter
          vmargin=20
          xbetween=10;
run;

```

---

## Example 9.18: Branch and Bound Trees

This example illustrates a nonstandard use of PROC NETDRAW. The TREE option in PROC NETDRAW is used to draw a branch and bound tree such as one that you obtain in the solution of an integer programming problem. Refer to Chapter 4, “The LP Procedure” (*SAS/OR User’s Guide: Mathematical Programming Legacy Procedures*) for a detailed discussion of branch and bound trees. The data used in this example were obtained from one particular invocation of PROC LP.

The data set NET (created in the following DATA step) contains information pertaining to the branch and bound tree. Each observation of this data set represents a particular iteration of the integer program, which can be drawn as a node in the tree. The variable node names the problem. The variable object gives the objective value for that problem. The variable problem identifies the *parent* problem corresponding to each node; for example, since the second and the seventh observations have problem equal to ‘-1’ and ‘1’, respectively, it indicates that the second and the seventh problems are derived from the first iteration. Finally, the variable \_pattern specifies the pattern of the nodes based on the status of the problem represented by the node.

```

data net;
  input node problem cond $10. object;
  if cond="ACTIVE"           then _pattern=1;
  else if cond="SUBOPTIMAL" then _pattern=2;
  else                      _pattern=3;
datalines;
  1      0    ACTIVE      4
  2     -1    ACTIVE      4
  3      2    ACTIVE      4
  4     -3    ACTIVE 4.3333333
  5      4  SUBOPTIMAL   5
  6      3  FATHOMED 4.3333333
  7      1    ACTIVE      4
  8     -7    ACTIVE      4
  9     -8  FATHOMED 4.3333333
  10     8  FATHOMED 4.3333333
  11     7    ACTIVE      4
  12    -11  FATHOMED 4.3333333
  13    11  FATHOMED     4.5
;

```


The next DATA step (which creates the data set LOGIC) uses this child-parent information to format the precedence relationships as expected by PROC NETDRAW. Next, the two data sets are merged together to create the Network input data set (BBTREE) for PROC NETDRAW. The ID variable in the data set BBTREE is formatted to contain both the iteration number and the objective value.

Finally, PROC NETDRAW is invoked with the TREE, ROTATE, and ROTATETEXT options to produce a branch and bound tree shown in Output 9.18.1. Note that the ROTATE and ROTATETEXT options produce a rotated graph with a top-down orientation.

```

/* set precedence relationships
   using child-parent information */
data logic;
  keep node succ;

```

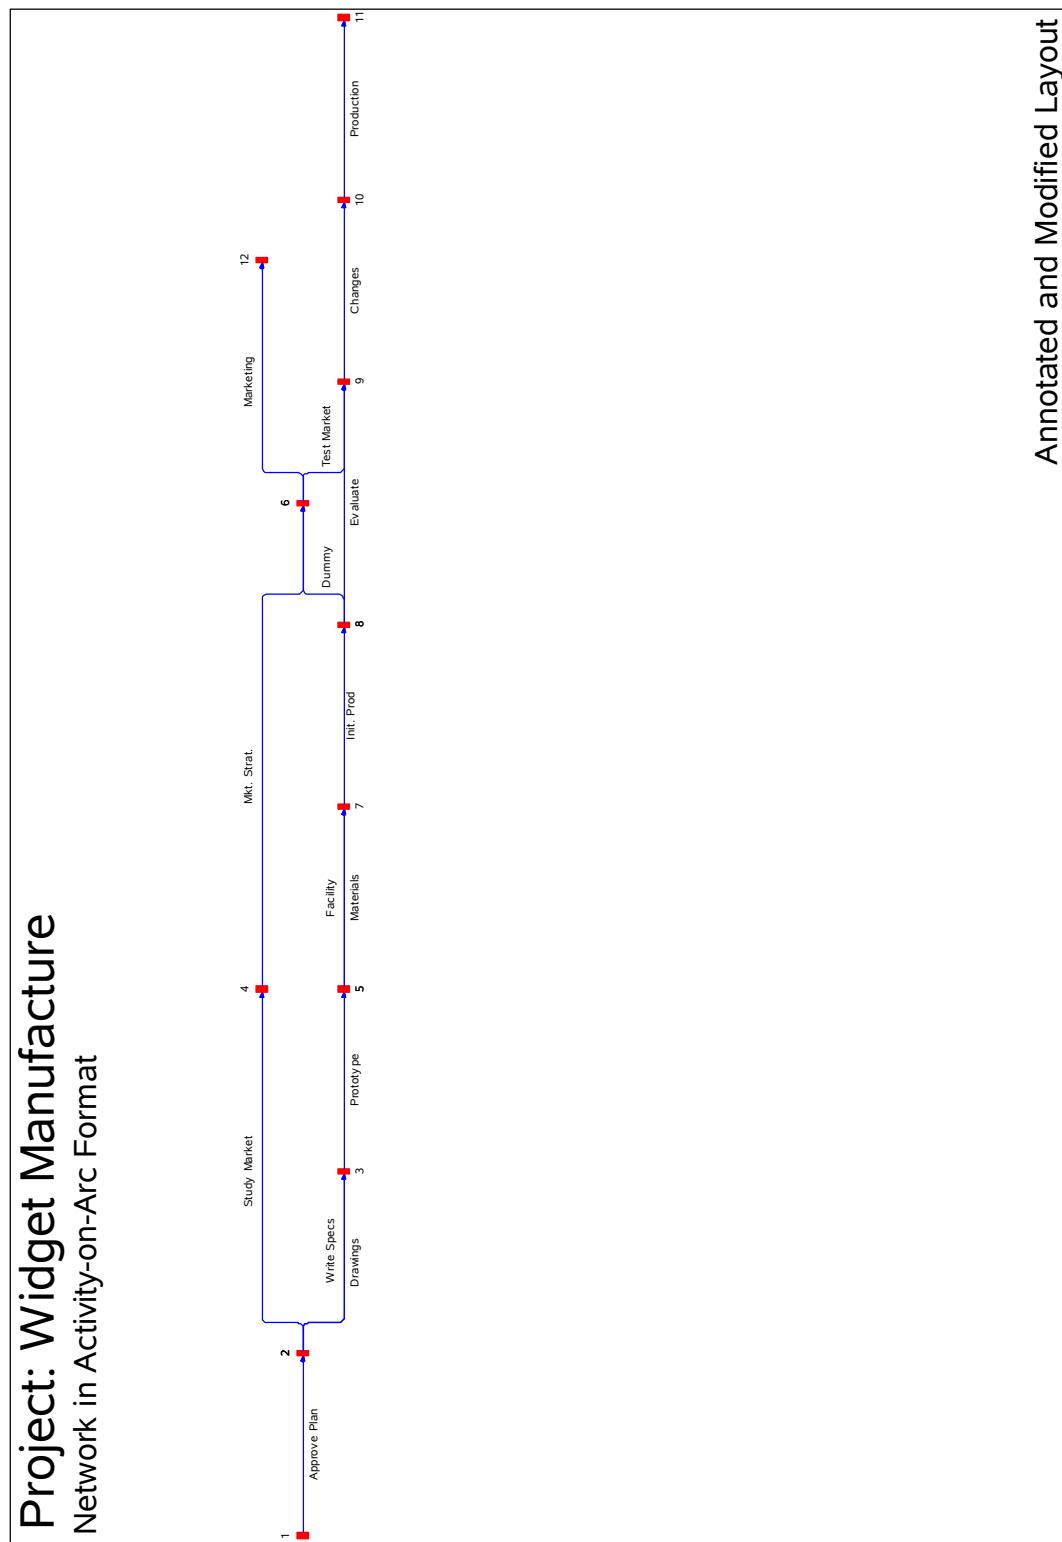**Output 9.17.2** Activity-on-Arc Format: Annotated Diagram

```

set net(firsttobs=2);
succ=node;
node=abs(problem);
run;


proc sort data=logic;
  by node;
  run;

/* combine the logic data and the node data */
/* set ID values */
data bbtree;
  length id $ 9;
  merge logic net; by node;
  if node < 10 then id=put(node,1.)||put(object,f8.2);
  else           id=put(node,2.)||put(object,f7.2);
  run;

goptions border rotate=portrait;
pattern1 v=s c=green;
pattern2 v=s c=red;
pattern3 v=s c=blue;

title h=3    j=c 'Branch and Bound Tree';
title2   ' ';
footnote1 h=1.5 j=c c=red   'Optimal   '
          c=green ' Active   '
          c=blue  ' Fathomed ';
footnote2 ' ';
footnote3 h=1.5 ' Node shows Iteration Number and Objective Value ';
proc netdraw data=bbtree graphics out=babout;
  actnet /activity=node
    successor=succ
    id=(id)
    nodefid
    nolabel
    ctext=white
    coutline=black
    carcs=black
    xbetween=15
    ybetween=3
    compress
    font=swiss
    rectilinear
    tree
    rotate
    rotatetext
    arrowhead=0
    htext=2;
  run;

```

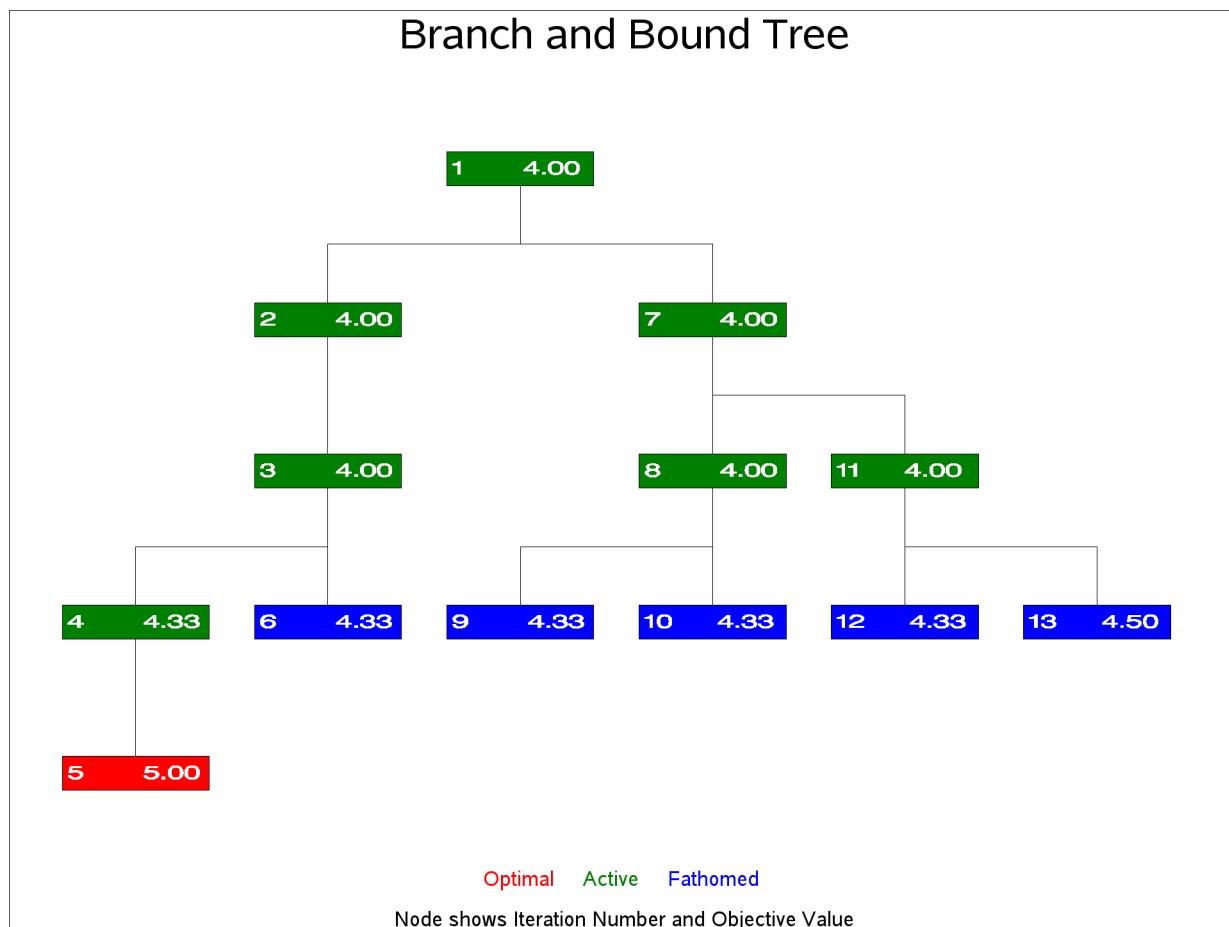**Output 9.18.1** Branch and Bound Tree

In the next invocation, PROC NETDRAW uses a modified layout of the nodes to produce a diagram where the nodes are aligned according to the iteration number. The following program uses the Layout data set produced in the previous invocation of PROC NETDRAW. The same  $y$  coordinates are used; but the  $x$  coordinates are changed to equal the iteration number. Further, the ALIGN= specification produces a time axis that labels each level of the diagram with the iteration number. Each node is labeled with the objective value. The resulting diagram is shown in Output 9.18.2.

```

data netin;
  set bbout;
  if _seq_ = 0; drop _seq_;
  _x_ = _from_;
  id = substr(id, 3);
  run;


goptions rotate=landscape;
title h=3 'Branch and Bound Tree';
title2 h=2 'Aligned by Iteration Number';
footnote1 h=1.5 j=c c=red 'Optimal '
               c=green '      Active      '
               c=blue '      Fathomed  ';
footnote2 ' ';

```

```

footnote3 j=1 h=1.5 ' Node shows Objective Value ';
pattern1 v=e c=green;
pattern2 v=e c=red;
pattern3 v=e c=blue;
proc netdraw data=netin graphics;
  actnet /id=(id)
    ctext=black
    carcs=black
    align = _from_
    frame
    pcompress
    rectilinear
    arrowhead=0
    nodefid
    nolabel
    htext=2.5
    xbetween=8;
run;

```

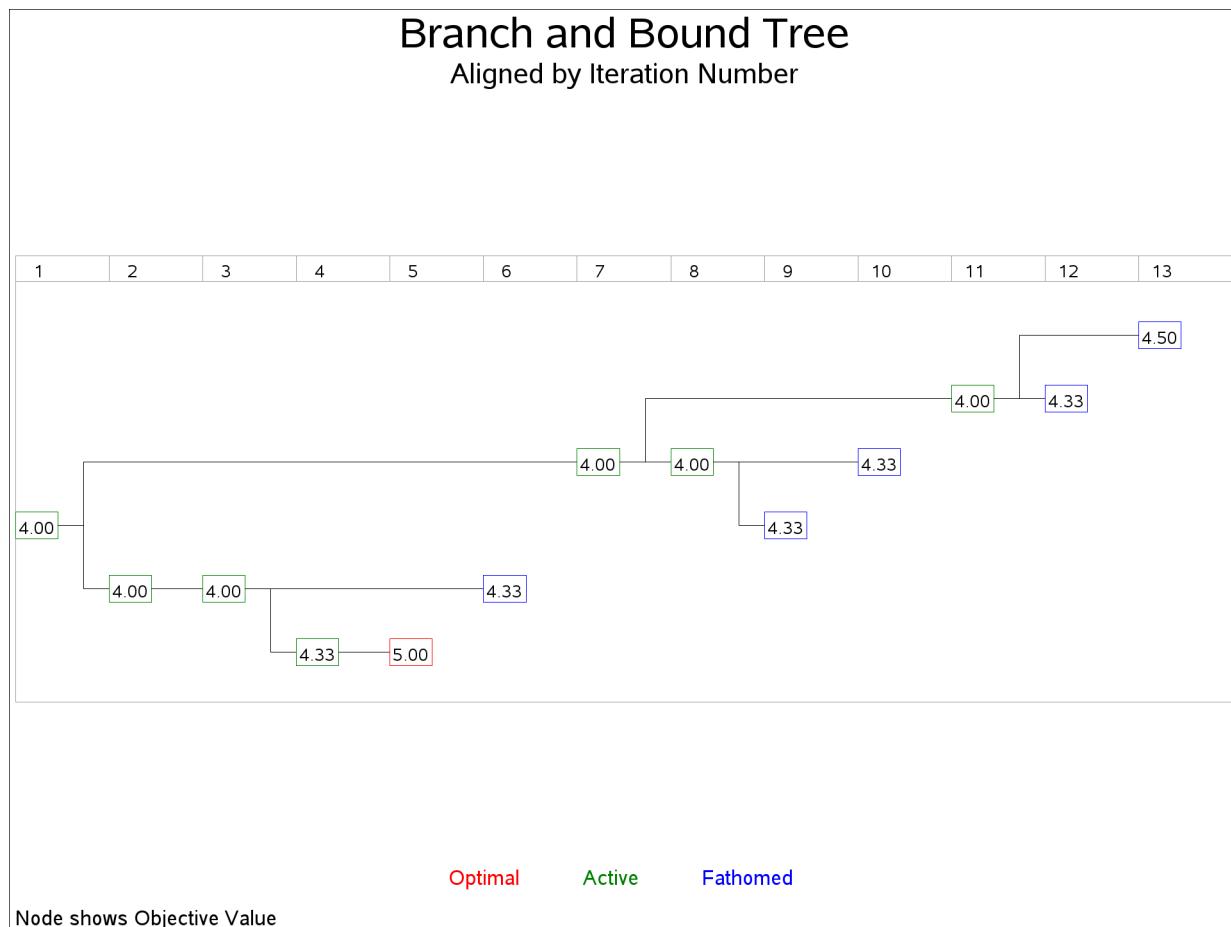**Output 9.18.2** Branch and Bound Tree: Aligned by Iteration Number

## Statement and Option Cross-Reference Tables

The next two tables reference the options in the NETDRAW procedure that are illustrated by the examples in this section. Note that all the options are specified on the ACTNET statement.

**Table 9.9** Options Specified in Examples 5.1–5.9

**Table 9.9** (continued)

<b>Option</b>	<b>1</b>	<b>2</b>	<b>3</b>	<b>4</b>	<b>5</b>	<b>6</b>	<b>7</b>	<b>8</b>	<b>9</b>
SUCCESSOR=	X	X	X	X	X	X	X	X	X
TIMESCALE									X
VMARGIN=					X				X
VPAGES=						X	X		X
XBETWEEN=					X	X	X		
YBETWEEN=						X	X	X	X

**Table 9.10** Options Specified in Examples 5.10–5.18

<b>Option</b>	<b>10</b>	<b>11</b>	<b>12</b>	<b>13</b>	<b>14</b>	<b>15</b>	<b>16</b>	<b>17</b>	<b>18</b>
ACTIVITY=	X	X	X	X	X	X	X	X	X
ALIGN=							X	X	X
ANNOTATE=							X	X	
ARROWHEAD=						X			X
AUTOREF		X							
BOXHT=				X					
BOXWIDTH=	X	X	X					X	
BREAKCYCLE			X						
CARCS=	X	X	X	X	X	X			
CAXIS=		X							
CCRITARCS=		X							
CENTERID			X	X	X	X			
CENTERSUBTREE						X	X		
COMPRESS	X								X
COUTLINE=			X	X			X		X
CREF=		X							
CREFBRK=	X								
CTEXT=			X	X	X	X			X
DATA=	X	X	X	X	X	X	X	X	X
DP	X								
DURATION=	X								
FONT=	X								X
FRAME	X								X
GRAPHICS	X	X	X	X	X	X	X	X	X
HMARGIN=			X				X		
HTEXT=	X	X	X	X	X	X	X	X	X
ID=	X	X	X	X		X	X	X	X
LINEAR	X	X					X		
LREF=		X							
LREFBRK=	X								
MININTERVAL=		X							
NOARROWFILL			X						
NODEFID	X	X	X	X		X	X	X	X
NOLABEL	X	X	X	X		X	X	X	X

**Table 9.10** (continued)

<b>Option</b>	<b>10</b>	<b>11</b>	<b>12</b>	<b>13</b>	<b>14</b>	<b>15</b>	<b>16</b>	<b>17</b>	<b>18</b>
NOVCENTER	X		X			X		X	
OUT=				X	X			X	X
PATTERN=			X						
PCOMPRESS	X	X	X	X	X	X	X	X	X
RECTILINEAR			X			X			X
REFBREAK	X								
ROTATE									X
ROTATETEXT									X
SEPARATEARCS	X	X		X	X				
SEPARATESONS						X			
SUCCESSOR=	X	X	X	X	X	X	X	X	X
TIMESCALE	X	X				X			
TREE									X
USEFORMAT							X		
VMARGIN=	X		X				X	X	
XBETWEEN=			X			X		X	X
YBETWEEN=			X	X	X	X		X	X
ZONE=	X						X		
ZONEPAT	X							X	
ZONESPACE	X								

---

## References

Even, S. (1979). *Graph Algorithms*. Rockville, MD: Computer Science Press.

Kuhfeld, W. F. (2010). *Statistical Graphics in SAS: An Introduction to the Graph Template Language and the Statistical Graphics Procedures*. Cary, NC: SAS Institute Inc.

# Chapter 10

## The Projman Application

### Contents

---

Overview: Projman Application . . . . .	774
Projman Command . . . . .	775
Projman Window . . . . .	775
Projman Options Window . . . . .	778
Import Project Window . . . . .	779
Project Information Window . . . . .	780
Project Schedule Summary Window . . . . .	781
PM Window . . . . .	782
Calendars Window . . . . .	783
Edit Calendar Window . . . . .	784
Holidays Window . . . . .	785
Edit Holiday Window . . . . .	786
Resources Window . . . . .	788
Edit Resource Window . . . . .	789
Availability Window . . . . .	791
Alternates Window . . . . .	792
Workshifts Window . . . . .	794
Edit Workshift Window . . . . .	795
Schedule Options Window . . . . .	796
Additional Options Window . . . . .	798
Additional Options . . . . .	798
Resource Options Window . . . . .	800
Resource Options . . . . .	800
Scheduling Rules . . . . .	802
Reports Window . . . . .	803
Report Options Window . . . . .	806
Tabular Report Options . . . . .	806
Graphics Report Options . . . . .	807
Title Window . . . . .	808
Footnote Window . . . . .	809
Options Window . . . . .	809
Standard Options . . . . .	810
Macro Variables . . . . .	811
Calendar Report Options Window . . . . .	815
Gantt Chart Options Window . . . . .	816

Chart Control Options . . . . .	818
Task Options . . . . .	819
Time Axis Controls . . . . .	820
Task Bar Options . . . . .	820
Color Options . . . . .	821
Network Diagram Options Window . . . . .	<b>822</b>
Page/Layout Control Options . . . . .	824
Node Options . . . . .	825
Time Scale Options . . . . .	826
Arc Options . . . . .	827
Color Options . . . . .	828
Resource Report Options Window . . . . .	<b>829</b>
Tabular Listing Options Window . . . . .	<b>829</b>
Additional Options . . . . .	831
Import Activity Data Set Window . . . . .	<b>832</b>
Standard Import Options . . . . .	832
Secondary Windows . . . . .	833
Basic Activity Information . . . . .	834
Progress/Baseline Information . . . . .	835
Resource Information . . . . .	837
Additional Information . . . . .	837
Import Calendar Data Set Window . . . . .	<b>839</b>
Import Holiday Data Set Window . . . . .	<b>840</b>
Import Resourcein Data Set Window . . . . .	<b>841</b>
Import Workshift Data Set Window . . . . .	<b>842</b>
Edit Date Window . . . . .	<b>843</b>

---

## Overview: Projman Application

The Projman application is a user-friendly graphical user interface for performing project management with the SAS System. Through the use of an interactive Gantt chart window provided by the **PM** procedure, you can easily create and manage multiple projects. For more information, see Chapter 5, “The PM Procedure.”

Projman is accessed by invoking the **projman** command in the SAS windowing environment, or by selecting **Solutions ▶ Analysis ▶ Project Management** from the primary SAS menu. When you invoke Projman, the **Projman Window** is displayed. This window is the primary window for accessing the functionality of the application. See the section “**Projman Window**” on page 775 for more information.

Projman enables you to define multiple projects, information about which is stored in a **project dictionary data set**. For more information about this data set, see the section “**PROJDICTION= Option**” on page 775. To access the data associated with a project, you use the **Project Information window**. This window provides access to interfaces for defining data corresponding to activities, calendars, holidays, resources, and workshifts. See the section “**Project Information Window**” on page 780 for more information.

Projman also provides a variety of project reports. These reports include Gantt charts, network diagrams, calendars, and tabular listings, as well as resource usage and cost reports. You can easily modify any of the standard reports to add your own personalized reports to the application. For more information about reports, see the section “[Reports Window](#)” on page 803.

For general information about project management, consult Chapter A, “[Glossary of Project Management Terms](#).”

## Projman Command

The **projman** command supports two options:

- PROJDIRCT=
- project name

### PROJDIRCT= Option

The PROJDIRCT= option is used to specify the location of the Projman project dictionary data set. The project dictionary data set stores the definition of each project created with the Projman application.

Valid values for the option are a two-level SAS data set name (that is, <library>.⟨dsname⟩, where <library> is a currently defined SAS libname and <dsname> is a valid SAS data set name).

If the data set specified with the PROJDIRCT= option does not exist, Projman attempts to create a new project dictionary data set at that location. If the data set already exists and it is not a valid project dictionary data set, Projman uses the default project dictionary data set location, SASUSER.PROJDIRCT.

### Project Name Option


The Project Name option can be used to indicate a project that is to be [opened](#) automatically when Projman is started. If the project does not exist, Projman produces a warning message.

To specify project names that contain multiple adjacent blanks (that is, “Project \_ \_ \_ ABC”), enclose the name in double quotes.

## Projman Window

The Projman Window is the initial window opened by the Projman application. When you start the application, all currently defined projects are listed in this window. To view an existing project, select the desired name in the project list and click **Open**. Projects can be opened with either *read* or *update* access.

When a new or existing project is opened, a [Project Information window](#) is displayed. Individual project data can be manipulated from that window. For more information, see the section “[Project Information Window](#)” on page 780.

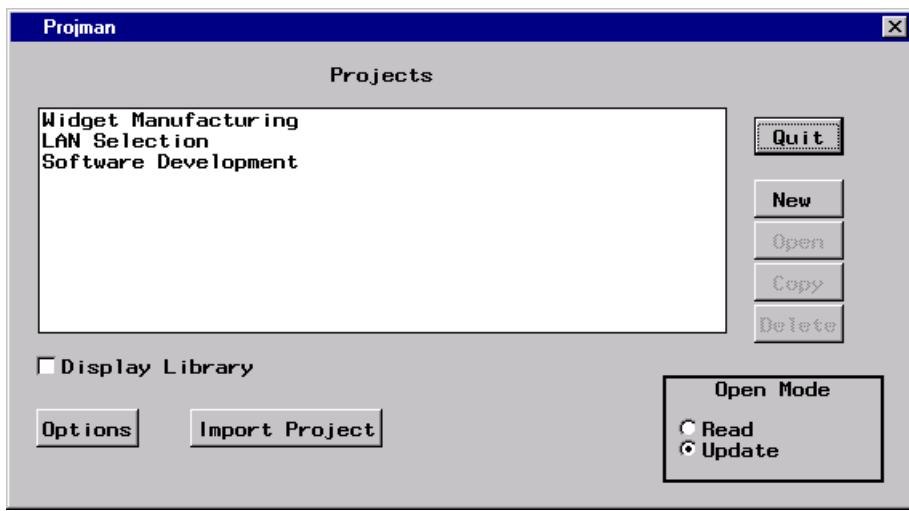

## Project List

The project list contains a list of all projects that are defined to the application.

## Quit

Clicking the **Quit** button exits the Projman application. If projects are open with **update** access and changes have been made, you are prompted to save changes.

## New

Clicking the **New** button creates a new project and opens that project with **update** access. A default project name (Projectn, where n is an integer) is automatically generated and added to the **project list**. When creating a new project, you are prompted to select the library where the project data is to be stored. After you select a library, the **Project Information window** is opened. For more information about that window, see the section “**Project Information Window**” on page 780.

## Open

Clicking the **Open** button opens the selected project with read or update access. The access level is determined by the current setting of the **Open Mode** option. In order to save modifications to a project, you must open the project with update access. While you have a project open with update access, other users are only able to obtain read access to that project.

## Copy

Clicking the **Copy** button copies the selected project. When copying a project, you are prompted to select the library where the project data is to be stored. You are also required to specify a unique project name. The new project name automatically appears in the [project list](#).

## Delete

Clicking the **Delete** button deletes the selected project. In order to delete a project, you must be able to obtain update access. In other words, no other user can have the project open with update access.

## Display Library

This check box is used to toggle the display of project library names within the [project list](#). The library name indicates the library reference to the SAS data library where a particular project's data is stored. If a project's library reference is not defined, Projman is unable to open the project.

## Options

When this button is clicked, the [Projman Options window](#) is displayed. For information about this window, see the section “[Projman Options Window](#)” on page 778.

## Import Project

When this button is clicked, the [Import Project window](#) is opened. For information about this window, see the section “[Import Project Window](#)” on page 779.

## Open Mode


The **Open Mode** option is used to specify whether projects are to be opened with read or update access. When a project is opened with read access, you may modify a *working* copy of the project data, but you are unable to save those changes when the project is closed (although you can use the **Save As** feature to save the modified project as a different project).

When a project is opened with update access, no other Projman session can open that same project with update access; however, read access is available. It is necessary to use update access if you want to save changes to the current project.

For different users to have simultaneous read access to the same project, SAS/SHARE software is required. Note that only one user can have update access to a particular project at a particular time. Access level does not affect the ability to produce project reports.

## Projman Options Window

The Projman Options window enables you to manipulate options that control the behavior of the Projman application.

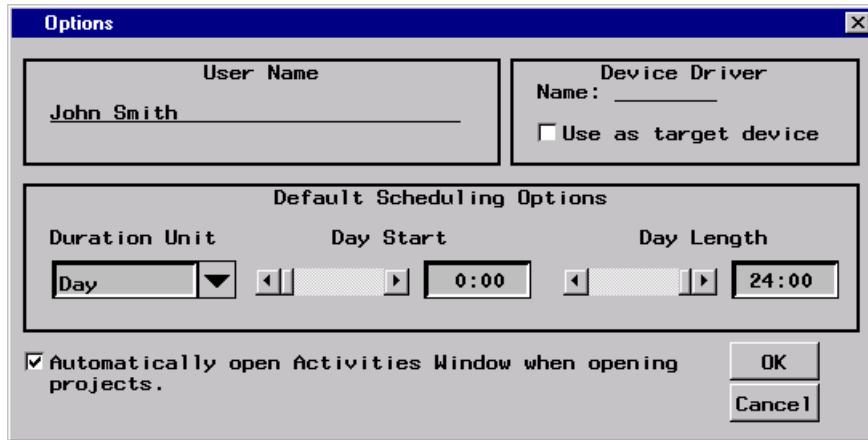

### User Name

The **User Name** field can be used to specify the user's name, which is used to indicate who last modified a project. Modification information appears in the **Project Schedule Summary** window. For information about that window, see the section “**Project Schedule Summary Window**” on page 781.

### Device Driver

The **Device Driver** field can be used to specify the name of the device driver that is to be used when printing reports. You can also indicate whether to use this device as a “target” device when reports are shown on the screen. In other words, the graphics output on the screen emulates the characteristics of the device listed in the **Device Driver** field.

### Default Scheduling Options


The **Default Scheduling Options** enable you to set default values for the project's **duration unit**, **day start**, and **day length** parameters. Note that changing the values of these options does not affect projects that already exist.

### Automatically open Activities Window when opening projects.

If this option is selected, a project's **Activities window** (an interactive Gantt chart window provided by the **PM procedure**) automatically opens when the project is opened. For more information, see the section “**PM Window**” on page 782.

## Import Project Window

The Import Project window enables you to import external project data or create sample projects.

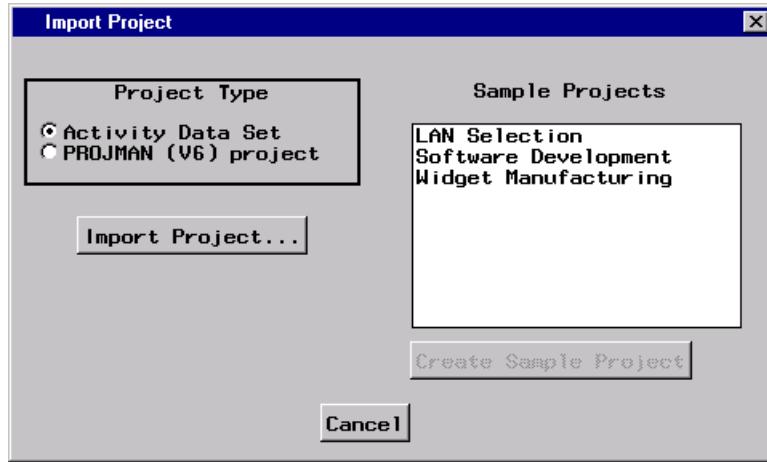

### Activity Data Set

When this check box is selected and the **Import Project** button is clicked, the Import Activity Data Set window is opened. For more information, see the section “Import Activity Data Set Window” on page 832.

### PROJMAN (V6) project

When this check box is selected and the **Import Project** button is clicked, you are presented with a list of Version 6 Projman projects to import.

### Import Project

Depending upon the setting of **Project Type** as **Activity data set** or **PROJMAN (V6) project**, clicking this button commences the appropriate import process.

### Sample Projects


This list displays the sample projects that are currently available with the Projman application. Make the desired selection and click the **Create Sample Project** button to create a sample project.

### Create Sample Project

Click this button to create the sample project that is currently selected in the **Sample Projects** list.

## Project Information Window

The Project Information window is initially displayed when a project is opened for read or update. The access control level is indicated in the window title. In this window, you can edit the project name and description as well as access windows for specifying project data and producing reports.

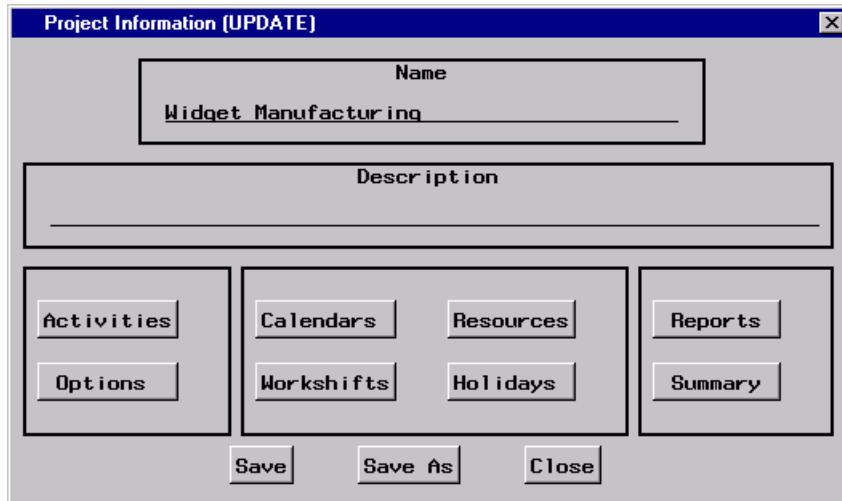

### Name

The **Name** field is used to specify the name of the project. Project names must be unique. A longer description can be given in the **Description** field.

### Description

The **Description** field is provided to give the opportunity for storing a short description of the project. A description is purely optional and is used for identification purposes only.

### Activities

When this button is clicked, the **PM window** (an interactive Gantt Chart provided by the **PM procedure**) displays the current project structure and schedule. Within this window, activities can be added and deleted and corresponding data can be modified. For more information, see the section “**PM Window**” on page 782.

### Options

This button is used to access a window for setting project **scheduling options**, as well as a window for adding variables to the Activity data set. For more information about project scheduling options, see the section “**Schedule Options Window**” on page 796.

## Calendars

When this button is clicked, the **Calendars** window is opened. For information about this window, see the section “[Calendars Window](#)” on page 783.

## Holidays

When this button is clicked, the **Holidays** window is opened. For information about this window, see the section “[Holidays Window](#)” on page 785.

## Resources

When this button is clicked, the **Resources** window is opened. For information about this window, see the section “[Resources Window](#)” on page 788.

## Workshifts

When this button is clicked, the **Workshifts** window is opened. For information about this window, see the section “[Workshifts Window](#)” on page 794.

## Reports

When this button is clicked, the **Reports** window is opened. For information about this window, see the section “[Reports Window](#)” on page 803.

## Summary


When this button is clicked, the Project Schedule Summary window is opened. For information about this window, see the section “[Project Schedule Summary Window](#)” on page 781.

---

## Project Schedule Summary Window

This window displays summary information for the different project schedules that have been computed. In addition to the start and finish times for these schedules, the **duration** and the **percent completion** of the project are also displayed. Note that these values correspond to the Resource Schedule of the project if **resource-constrained scheduling** was performed; otherwise, they correspond to the Early Schedule of the project.


This window also indicates the dates when the project was created and last modified as well as the user that last modified the project.

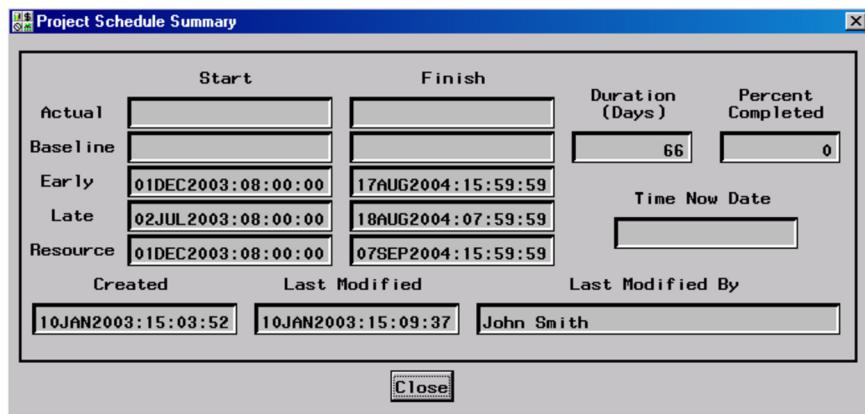

## PM Window


The PM window (also referred to as the Activities window) is an interactive Gantt chart window provided by the **PM** procedure. Within Projman, this window is used to manipulate data corresponding to the project activities. This data includes names, durations, precedence relationships, calendars, resource requirements, progress information, and baseline schedules, as well as user-defined identification fields.

While the PM window is open, all other Projman application windows are inactive. To access options that control the manner in which the PM window schedules activities, click the **Options** button on the Project Information window before opening the PM window. For additional information about the PM window, see Chapter 5, “The PM Procedure.”

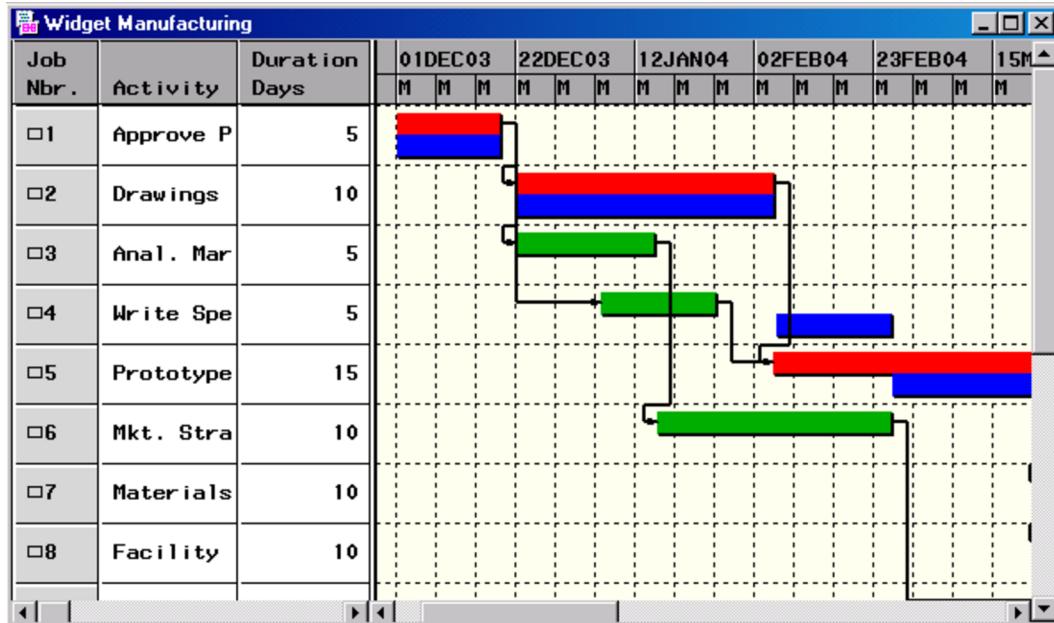

## Calendars Window

The Calendars window lists all of the [calendars](#) that have been defined for the project. From this window, you can create, edit, copy, and delete calendar definitions. Once defined, calendars can be assigned to activities as well as resources. You can define as many individual calendars as you want. Note that some actions in this window are disabled if they are not valid.



### Calendar List

This list contains all of the calendars that are defined for the project. By selecting an item in this list, you can manipulate the selected item by clicking the **Open**, **Copy**, or **Delete** buttons. The **New** button can always be clicked to add a new item to the list.

#### New

When this button is clicked, a new calendar is created and displayed in an [Edit Calendar window](#) for editing.

#### Copy

When this button is clicked, the selected calendar is copied and displayed in an [Edit Calendar window](#) for editing. If no calendar is selected, this option is disabled.

#### Open

When this button is clicked, the selected calendar is displayed in an [Edit Calendar window](#) for editing. If no calendar is selected, this option is disabled.

#### Delete

When this button is clicked, the selected item in the [calendar list](#) is deleted. A secondary window is opened to confirm the deletion. Deletions are irreversible unless the project is closed without saving the current changes. If no calendar is selected, this option is disabled.


## Import Calendar Data Set

When this button is clicked, a window is displayed for importing a CALENDAR data set. For information about this window, see the section “Import Calendar Data Set Window” on page 839. The import data set is required to be in the format appropriate for input to the CPM or PM procedure. For information about the CALENDAR data set, see the section “CALEDATA Data Set” on page 103.

## Edit Calendar Window

This window enables you to create and modify calendar definitions. You can specify a calendar name and description as well as choose the workshifts for each day of the work week.

Calendar names can take either character or numeric values, but they must be unique. If a calendar is defined with the name Default, every activity in the project will follow that calendar unless the activity has a specific calendar associated with it.

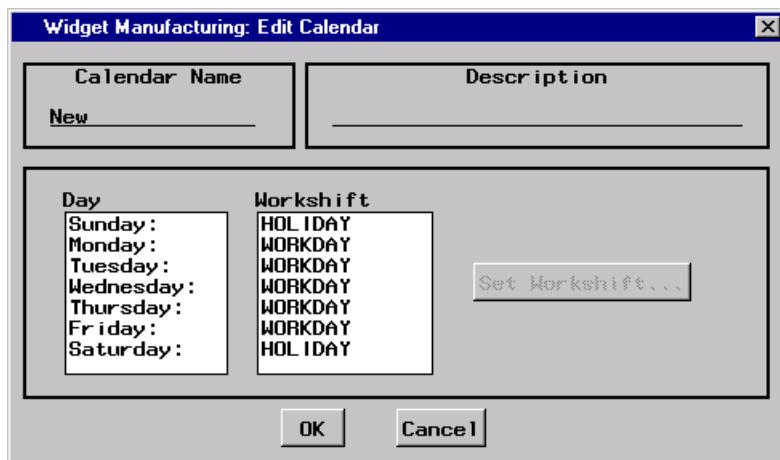

### Calendar Name

The **Calendar Name** field is used to specify the name of the calendar. The calendar name can be either character or numeric, but it must be unique. This name is the value that will be used to assign calendars to activities and resources. A longer description can be given in the **Description** field.

### Description

The **Description** field enables you to store a short description about the calendar. A description is optional and is used for identification purposes only.

### Workshift Table


The Workshift table indicates the workshifts that have been assigned to each day of the week. By default, Monday through Friday are working days (identified by the WORKDAY workshift), while Saturday and Sunday are nonworking days (identified by the HOLIDAY workshift). To change the workshift associated with a particular day or days, simply select that day (days) by selecting the corresponding workshift (workshifts) in the table and click the **Set Workshift** button.

## Set Workshift

When the **Set Workshift** button is clicked, a window is opened that displays all of the workshifts currently defined for the project. By selecting different workshifts, you can change the highlighted values in the **Workshift** table. When the desired selection has been made, click the **Close** button to close the window.

## Holidays Window

The Holidays window lists all of the **holidays** that have been defined for the project. From this window, you can create, edit, copy and delete holiday definitions. You can define as many individual holidays as you want. Note that some actions in this window are disabled if they are not valid.

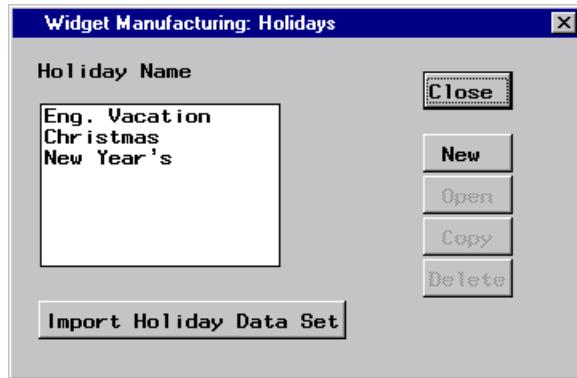

### Holiday List

This list contains all of the holidays that are defined for the project. By selecting an item in this list, you can manipulate the selected item by clicking the **Open**, **Copy**, or **Delete** buttons. The **New** button can always be clicked to add a new item to the list.

#### New

When this button is clicked, a new holiday is created and displayed in an **Edit Holiday** window for editing.

#### Copy

When this button is clicked, the selected holiday is copied and displayed in an **Edit Holiday** window for editing. If no holiday is selected, this option is disabled.

#### Open

When this button is clicked, the selected holiday is displayed in an **Edit Holiday** window for editing. If no holiday is selected, this option is disabled.

## Delete

When this button is clicked, the selected item in the **holiday list** is deleted. A secondary window is opened to confirm the deletion. Deletions are irreversible unless the project is closed without saving any changes. If no holiday is selected, this option is disabled.


## Import Holiday Data Set

When this button is clicked, a **window** is displayed for importing a **HOLIDAY data set**. For information about this window, see the section “**Import Holiday Data Set Window**” on page 840. The import data set is required to be in the format appropriate for input to the **CPM** or **PM** procedure. For information about the **HOLIDAY** data set, see the section “**HOLIDATA Data Set**” on page 104.

## Edit Holiday Window

This window enables you to create and modify **holiday** definitions. You can specify a holiday name and description as well as a start date, finish date, and the duration (or length) of the holiday. Additionally, you can indicate the calendar or calendars that the holiday is to be associated with.

Holiday names can take either character or numeric values. A start date is always required when defining a holiday.

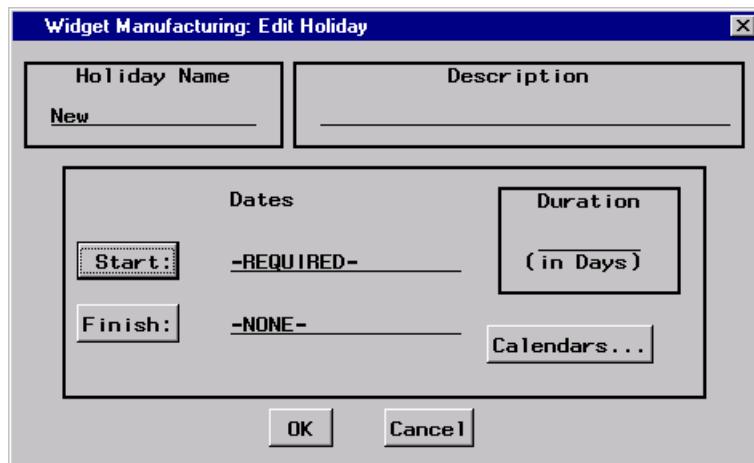

### Holiday Name

The **Holiday Name** field is used to specify the name of the holiday. The holiday name can be either character or numeric. A longer description can be given in the **Description** field.

### Description

The **Description** field enables you to store a short description about the holiday. A description is optional and is used for identification purposes only.

## Holiday Start Date

The **Holiday Start Date** is used to indicate the calendar date that represents the start of the holiday. The start date is required. The value can be entered with either a DATEw. (that is, 01MAY2004) or a DATETIMEw. (that is, 01MAY2004:08:30:00) format. Alternatively, by clicking the **Start:** button, you can access an [Edit Date window](#) to specify the desired value.

## Holiday Finish Date

The **Holiday Finish Date** can be used to indicate the calendar date that represents the finish of the holiday. The finish date is not required; however, if it is not specified, the holiday will last only one **duration unit** (as defined for the project) unless the length of the holiday is specified in the **Duration** field. The finish date value can be entered with either a DATEw. (that is, 01MAY2004) or a DATETIMEw. (that is, 01MAY2004:16:59:59) format. Alternatively, by clicking the **Finish:** button, you can access an [Edit Date window](#) to specify the desired value.


## Duration

The **Duration** field can be used to specify the length of the holiday. Duration values are specified in the units of the project's [duration unit](#). The duration is optional, but it is assumed to be 1 if the [holiday finish date](#) is not provided. If the holiday finish date is specified, the duration is ignored.

## Calendars


Clicking the **Calendars** button opens a window for indicating which project calendar or calendars the holiday is to be associated with. If no calendars are specified in the list, the holiday is assigned to *all* calendars.

The Calendars window contains a list of calendars that the current holiday is assigned to. To remove calendars, simply select the calendar to be removed and click **Remove**. To add calendars to the list, click **Add**. A list of all calendars is displayed and if you select individual calendar entries, they are added to the holiday's calendar assignments.



## Resources Window

The Resources window lists all of the resources that have been defined for the project. From this window, you can create, edit, copy and delete resource definitions. You can define as many individual resources as you want. Note that some actions in this window are disabled if they are not valid.



### Resource List

This list contains all of the resources that are defined for the project. By selecting an item in this list, you can manipulate the selected item by clicking the **Open**, **Copy**, or **Delete** buttons. The **New** button can always be clicked to add a new item to the list.

#### New

When this button is clicked, a new resource is created and displayed in an [Edit Resource window](#) for editing.

#### Copy

When this button is clicked, the selected resource is copied and displayed in an [Edit Resource window](#) for editing. If no resource is selected, this option is disabled.

#### Open

When this button is clicked, the selected resource is displayed in an [Edit Resource window](#) for editing. If no resource is selected, this option is disabled.

#### Delete

When this button is clicked, the selected item in the [resource list](#) is deleted. A secondary window is opened to confirm the deletion. Deletions are irreversible unless the project is closed without saving any changes. If no resource is selected, this option is disabled.

## Import Resourcein Data Set


When this button is clicked, a window is displayed for importing a RESOURCEIN data set. For information about this window, see the section “Import Resourcein Data Set Window” on page 841. The import data set is required to be in the format appropriate for input to the CPM or PM procedure. For information about the RESOURCEIN data set, see the section “RESOURCEIN= Input Data Set” on page 114.

---

## Edit Resource Window

This window enables you to create and modify resource definitions. You can specify a resource name and description as well as indicate the resource type and priority. Actual, budgeted, and fixed resource costs can also be specified. In two secondary windows, you can define the availability profile and a list of substitute resources.

Resource names must be valid SAS variable names and must be unique.

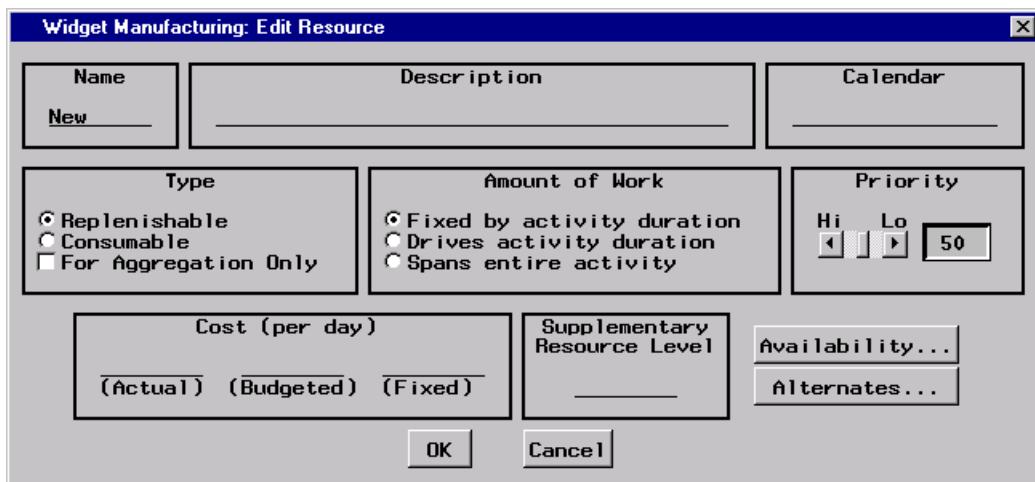

### Name

The **Name** field is used to specify the name of the resource. The resource name must be a valid SAS variable name and must be unique. A longer description can be given in the **Description** field.

### Description

The **Description** field enables you to store a short description of the resource. A description is optional and is used for reporting purposes only.

### Calendar

The **Calendar** field is used to specify the name of the [calendar](#) for the resource. Simply type the name of the desired calendar in the field and click **Enter**. If that calendar does not exist, you are asked if you would like for it to be created. If you respond affirmatively, a calendar (with default settings) is created and given the specified name. Calendars are modified by accessing the [Calendars window](#) for the project. For more information, see the section “[Calendars Window](#)” on page 783.

## Type

Resources are classified as either consumable or replenishable. A consumable resource is one that is used up by the job (such as bricks or money), while a replenishable resource becomes available again once a job using it has finished (such as laborers or machinery).

If the **For Aggregation Only** option is selected, this resource is used for [aggregation](#) rather than [resource-constrained scheduling](#). When a resource is defined as an aggregate resource, resource availability information is ignored.

## Amount of Work

This selection indicates the amount of work that a particular resource is to perform on an activity (or the manner in which the resource affects an activity's duration). When the **Fixed by activity duration** option is selected, the resource works for a fixed duration, as specified for the activity; in other words, the activity's duration is not affected by changing the rate of the resource used by the activity. The **Drives activity duration** selection indicates that the activity's work value indicates the total amount of work required by the resource for that activity; such a resource is called a *driving* resource. The **Spans entire activity** selection indicates that the resource is to be a *spanning* resource; in other words, the resource is required to work throughout the activity's duration, no matter which resource is working on it. For example, an activity might require 10 percent of a "supervisor," or the use of a particular room, throughout its duration. For such an activity, the duration used for the spanning resource is computed after determining the span of the activity for all the other resources.

## Priority

You can use the horizontal slider to specify a resource priority value between 1 and 100. Lower numbers indicate higher priority. During resource-constrained scheduling, this number is used to order activities that are waiting for resources when the [primary scheduling rule](#) is specified as [resource priority](#). For information about scheduling rules, see the section "[Scheduling Rules](#)" on page 802.

## Cost

The **Cost** fields enables you to specify an actual, budgeted, and fixed cost value for each resource. These costs are optional and are used in cost calculations for resource cost reports.

## Supplementary Resource Level

The **Supplementary Resource Level** field can be used to specify an amount of extra resource that is available for use throughout the duration of the project. This extra resource is used only if the activity cannot be scheduled without delaying it beyond its [late start](#) time.

## Availability

Clicking the **Availability** button opens the [Availability window](#) for the current resource. From this window, you can define the availability profile for the resource. For more information, see the section "[Availability Window](#)" on page 791.


## Alternates

Clicking the **Alternates** button opens the [Alternates window](#) for the current resource. From this window, you can define alternate (substitute) resources for the current resource. For more information, see the section “[Alternates Window](#)” on page 792.

## Availability Window

This window enables you to specify the availability profile for the current resource. By adding records to the profile, you can indicate when the resource availability changes over time. By default, one record is added to the list to indicate an initial availability of one unit on January 1, 1960.

It is only necessary to add records for each change in the availability. Note that, for consumable resources, the availability amount represents the cumulative amount available to date.

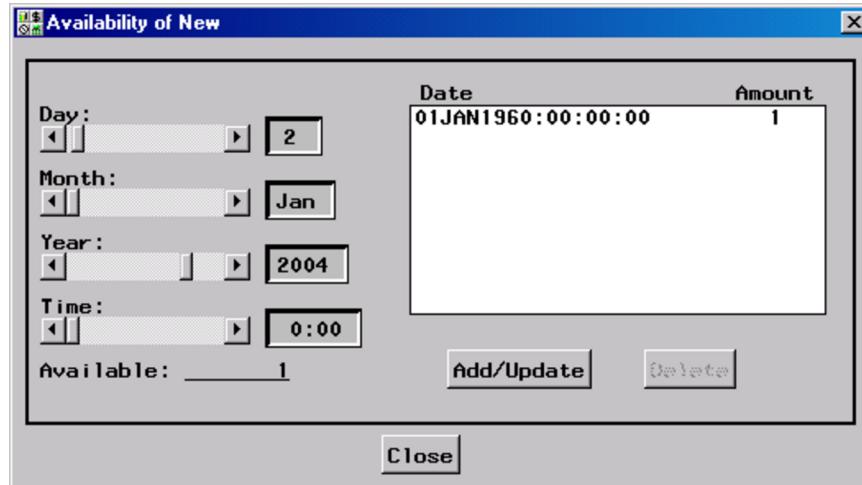

### Day

The horizontal slider is used to specify the desired day for adding an entry to the availability profile.

### Month

The horizontal slider is used to specify the desired month for adding an entry to the availability profile.

### Year

The horizontal slider is used to specify the desired year for adding an entry to the availability profile.

### Time

The horizontal slider is used to specify the desired time for adding an entry to the availability profile. Note that times are based on a 24 hour clock (that is, 13:00=1 PM).

## Available

The **Available** field is used to specify the desired available amount for adding (or updating) an entry to the availability profile.

## Availability Profile

The Availability Profile list indicates the amount of resource that is available to the project over time. To add or update records in the list, select the desired date, specify an **available** amount, and click **Add/Update**. Records in the list are sorted automatically by date. To delete records from the list, select the desired records and click **Delete**.

## Add/Update


Clicking the **Add/Update** button adds or updates a record in the **availability profile** depending on the current date setting and the **available** amount specified. Records in the availability profile are sorted automatically by date.

## Delete

Clicking the **Delete** button removes the currently selected records in the **availability profile**. Note that deletions cannot be aborted unless changes to the resource are not saved.

## Alternates Window

This window enables you to specify the alternates profile for the current resource. By adding records to the profile, you can indicate which resources can be substituted for the current resource and at what rate they can be substituted. Alternate resources are optional, but they can be very helpful in reducing resource infeasibilities. Only resources of the same type (consumable or replenishable) can be substituted for one another.

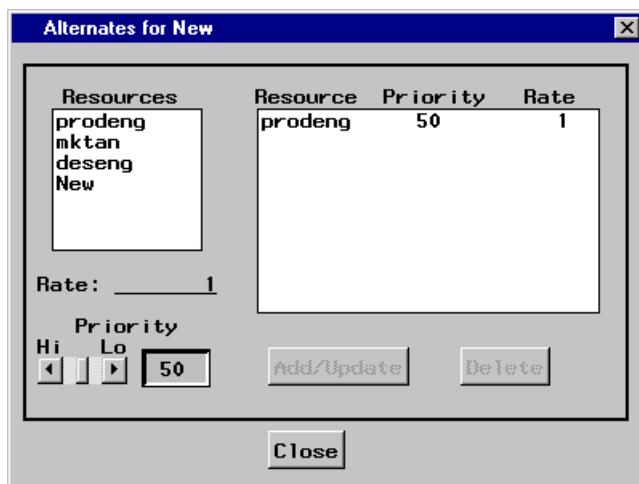

## Resources List

The Resources list contains all of the resources defined for the project that are of the same type (replenishable or consumable) as the current resource, as substitutions can only be made by like-typed resources. Selecting one or more resources in this list enables you to add records to the [alternates profile](#).

## Rate

The **Rate** field is used to specify the rate of substitution for an alternate resource specification. For example, if resource Z is to be substituted for resource X with a substitution rate of 0.5, an activity that requires 1 unit of resource X could be completed with 0.5 units of resource Z.

## Priority

The horizontal slider can be used to indicate a priority for an alternate resource specification. Lower numbers indicate higher priority. This priority is used to order the resources that are listed as alternates (substitutes) for the current resource.

## Alternates Profile

The Alternates Profile indicates the resources that are eligible to be substituted for the current resource (if the current resource is unavailable during project scheduling). Records in this list are ordered by [priority](#) to indicate the order in which substitutions would be made, if needed. To add or update records in the list, select one or more resources in the [Resources list](#), specify the [rate of substitution](#) and the [priority](#), and click the **Add/Update** button. To delete records from the list, select the desired records and click the **Delete** button.

## Add/Update


Clicking the **Add/Update** button adds or updates a record in the [alternates profile](#) depending on the current [resource](#), [rate](#), and [priority](#) settings.

## Delete

Clicking the **Delete** button removes the currently selected records in the [alternates profile](#). Note that deletions cannot be aborted unless changes to the resource are not saved.

## Workshifts Window

The Workshifts window lists all of the **workshifts** that have been defined for the project. From this window, you can create, edit, copy, and delete workshift definitions. You can define as many individual workshifts as you want. Note that some actions in this window are disabled if they are not valid.

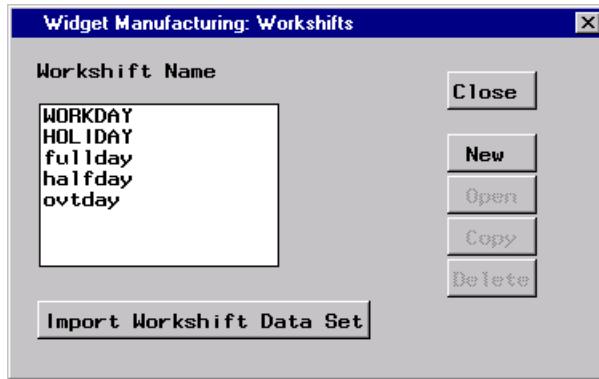

### Workshift List

This list contains all of the workshifts that are defined for the project. By selecting an item in this list, you can manipulate the selected item by clicking the **Open**, **Copy**, or **Delete** buttons. The **New** button can always be used to add a new item to the list.

#### New

When this button is clicked, a new workshift is created and displayed in an [Edit Workshift window](#) for editing.

#### Copy

When this button is clicked, the selected workshift is copied and displayed in an [Edit Workshift window](#) for editing. If no workshift is selected, this option is disabled.

#### Open

When this button is clicked, the selected workshift is displayed in an [Edit Workshift window](#) for editing. If no workshift is selected, this option is disabled.

#### Delete

When this button is clicked, the selected item in the **workshift list** is deleted. A secondary window is opened to confirm the deletion. Deletions are irreversible unless the project is closed without saving any changes. If no workshift is selected, this option is disabled.


## Import Workshift Data Set

When this button is clicked, a window is displayed for importing a **WORKSHIFT** data set. For information about this window, see the section “[Import Workshift Data Set Window](#)” on page 842. The import data set is required to be in the format appropriate for input to the **CPM** or **PM** procedure. For information about the **WORKDAY** data set, see the section “[WORKDATA Data Set](#)” on page 102.

## Edit Workshift Window

This window enables you to create and modify workshift definitions. You can specify a workshift name and description as well as define the on/off working times that make up the valid working periods within a single day.

Workshift names must be valid SAS variable names and must be unique.

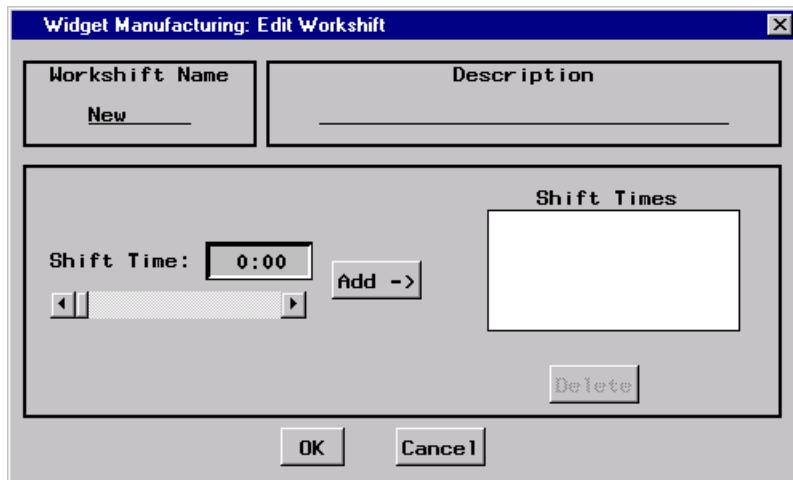

### Workshift Name

The **Workshift Name** field is used to specify the name of the workshift. The workshift name must be a valid SAS variable name and must be unique. A longer description can be given in the **Description** field.

### Description

The **Description** field enables you to store a short description of the workshift. A description is purely optional and is used for identification purposes only.

### Shift Time

The horizontal slider can be used to adjust the shift time. When the **Add ->** button is clicked, this value is added to the **Shift Times** list. The values in the Shift Times list are sorted automatically. Note that times are based on a 24 hour clock (that is, 13:00=1 PM).

**Add ->**

When this button is clicked, the current **shift time** value is added to the Shift Times list. The values in the Shift Times list are sorted automatically.

**Shift Times List**

The Shift Times list contains the on/off working times that represent the workshift (workday) definition. Times can be added to the list by setting the **Shift Time** and clicking the **Add ->** button, while times are removed by selecting items in the list and clicking the **Delete** button. Times should be added to the Shift Times list in pairs that represent on/off working times. A valid workshift will have an even number of times in the list.


**Delete**

When this button is clicked, any times selected in the Shift Times list are deleted.

**Schedule Options Window**

This window enables you to set options that control the scheduling of the active project by using the critical path method. These options are maintained separately for each project, and default values depend upon the data specified for the project. **Schedule Constraints** (such as resource leveling) can be enabled and disabled here. Secondary windows can be used to set additional options that are used to provide tighter control over the scheduling algorithm.

Some options are not available unless certain project data has been specified. For example, if no resources are defined, the **Resource Leveling** option is disabled. However, when resources are added to the project, this option is automatically enabled and selected.

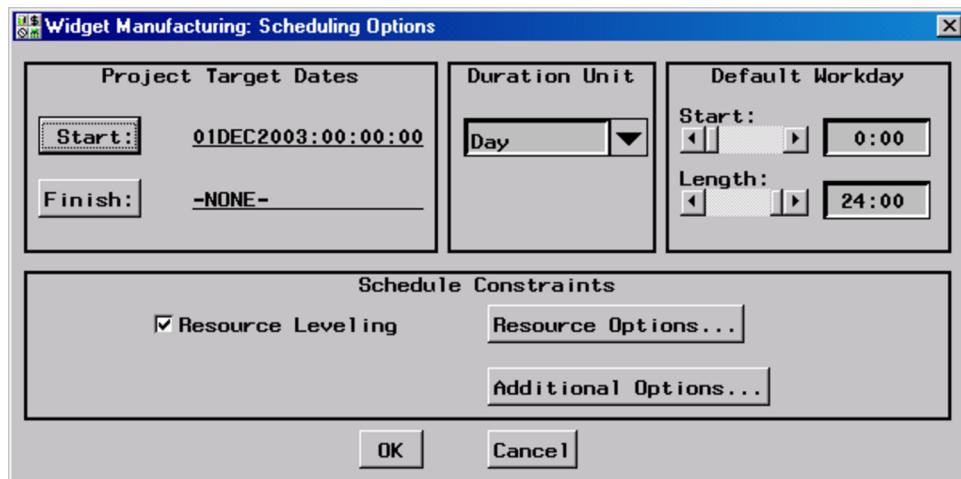

## Project Start Date

The **Project Start Date** is used to align the start of the project. This value can be entered with either a DATEw. (that is, 01MAY2004) or a DATETIMEw. (that is, 01MAY2004:08:30:00) format. Alternatively, by clicking the **Start:** button, you can access an [Edit Date window](#) to specify the desired value.

A [project finish date](#) can also be specified. If neither of these dates is specified, the project start date is automatically set to the current date upon initial scheduling.

## Project Finish Date

The **Project Finish Date** is used to align the finish of the project. This value can be entered with either a DATEw. (that is, 01MAY2004) or a DATETIMEw. (that is, 01MAY2004:17:00:00) format. Alternatively, by clicking the **Finish:** button, you can access an [Edit Date window](#) to specify the desired value.

A [project start date](#) can also be specified. If neither of these dates is specified, the project start date is automatically set to the current date upon initial scheduling.

## Duration Unit

The **Duration Unit** specifies the unit of time for the duration of each activity in the project. The following choices are available:

Second	Week
Minute	Month
Hour	Qtr
Day	Year
Weekday	

The default value is Day.

## Workday Start

This option can be used to specify the start of the default workday. Values for this option correspond to a TIME5. (hh:mm) value, where hh is in hours and mm is in minutes. Use the horizontal slider to select the desired value. Note that times are based on a 24 hour clock (that is, 13:00=1 PM).

This option is ignored when the [duration unit](#) is specified as Month, Qtr, or Year.

## Workday Length

This option can be used to specify the length of the default workday. Values for this option correspond to a TIME5. (hh:mm) value, where hh is in hours and mm is in minutes. Use the horizontal slider to select the desired value.

This option is ignored when the [duration unit](#) is specified as Month, Qtr, or Year.

## Resource Leveling

The **Resource Leveling** check box is used to indicate that the activities in the project are to be scheduled subject to the availability of required resources. If the active project contains resource data, this check box is selected by default; otherwise, the option is disabled. To schedule a project without using resource constraints, simply clear the **Resource Leveling** check box.

## Resource Options


Clicking this button opens the [Resource Options window](#), which is used to set options to control the resource allocation algorithm. For more information about this window, see the section “[Resource Options Window](#)” on page 800.

## Additional Options

Clicking this button opens the [Additional Options window](#), which is used to set basic options that control the project scheduling algorithm. For more information about this window, see the section “[Additional Options Window](#)” on page 798.

## Additional Options Window

This window enables you to control general scheduling options, such as the use of holidays and calendars. There are also controls for supertask and progress options. Note that some of these options are disabled if the required project data are not present. The settings of these options are established and maintained for each project.

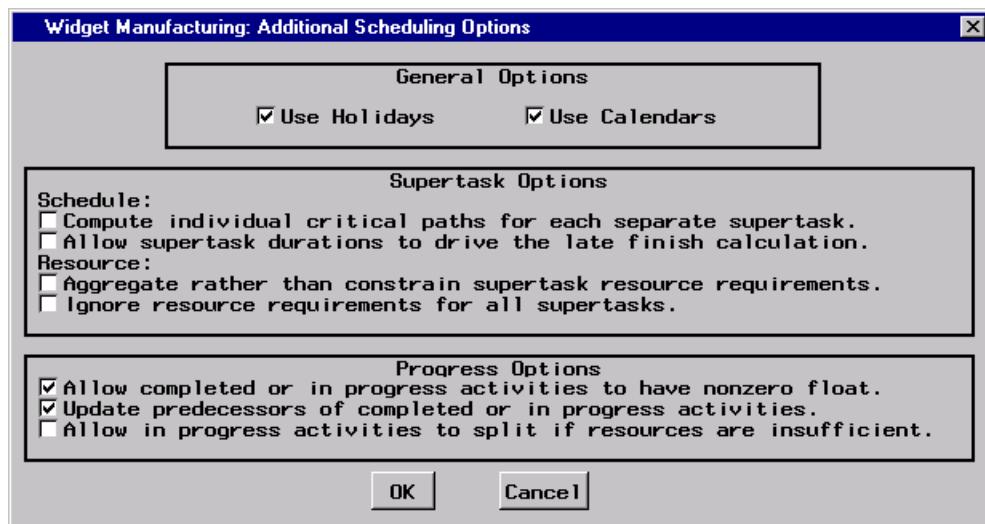

## Additional Options

### Use Holidays

When this check box is selected, [holiday](#) definitions are considered during scheduling; otherwise, all holidays are ignored. Note that this option is disabled if no holidays have been defined. This option is automatically activated when holidays are initially created.

## Use Calendars

When this check box is selected, [calendar](#) definitions are considered during scheduling; otherwise, all calendars are ignored. Note that this option is disabled if no calendars have been defined. This option is automatically activated when calendars are initially created.

### **Compute individual critical paths for each separate supertask.**

When this check box is selected, the scheduling algorithm calculates a separate [critical path](#) for each [supertask](#) in the project.

By default, the project's [early finish](#) time is treated as the starting point for the calculation of the [backward pass](#) (which calculates the late start schedule). The [late finish](#) time for each supertask is then determined during the backward pass on the basis of the precedence constraints. If a [target date](#) is placed on the finish time of a supertask, the late finish time of the supertask is further constrained by this value. However, when this option is activated, the scheduling algorithm requires that the late finish time of each subtask be less than or equal to the early finish time of the supertask.

### **Allow supertask durations to drive the late finish calculation.**

When this check box is selected, the scheduling algorithm uses the specified [supertask duration](#) to compute the maximum allowed [late finish](#) time for each supertask. Otherwise, the maximum allowed late finish time is determined by the supertask span, as computed from the span of all the [subtasks](#) of the supertask.

### **Aggregate rather than constrain supertask resource requirements.**

When this check box is selected, the resource requirements for all [supertasks](#) are used only for aggregation purposes and not for [resource-constrained scheduling](#).

### **Ignore resource requirements for all supertasks.**

When this check box is selected, the resource requirements for all [supertasks](#) are ignored.

### **Allow completed or in-progress activities to have nonzero float.**

When this check box is selected, the scheduling algorithm allows activities that are completed or in progress to have nonzero float. For more information about float, see [total float](#) and [free float](#) in Chapter A, “[Glossary of Project Management Terms](#).” By default, all completed or in-progress activities have zero float.

### **Update predecessors of completed or in-progress activities.**

When check box is selected, the scheduling algorithm assumes automatic completion (or start) of activities that are [predecessors](#) to activities already completed (or in progress). For example, if activity B is a successor of activity A, and B has an [actual start](#) time (or [actual finish](#) time or both) specified while A has no actual start or actual finish time, then the algorithm assumes that A must have already finished. Activity A is assigned an actual start time and an actual finish time consistent with the precedence constraints.

### Allow in-progress activities to split if resources are insufficient.


When check box is selected, the scheduling algorithm allows activities that are in progress at the **timenow date** to be split if they cause resource infeasibilities. During resource allocation, any activities with **early start** values less than the timenow date are scheduled even if there are not enough resources. This is true even for activities that are in progress. This option permits an activity to be split into two segments at the timenow date, allowing the second segment of the activity to be scheduled later when resource levels permit. Note that activities with a **target date alignment type** of mandatory start or mandatory finish are not allowed to be split; also, activities without resource requirements are not split.

---

## Resource Options Window

The Resource Options window enables you to control several aspects of the resource scheduling algorithm. When activities are scheduled subject to the limited availability of resources, it is possible that a feasible schedule does not exist or cannot be found. The resource options available here can be used to control and manipulate the resource allocation process. In some cases, these options might enable the algorithm to find a feasible schedule or to shorten the existing schedule.

These options settings are established and maintained for each project. Note that some options have no effect if the appropriate data has not been specified.

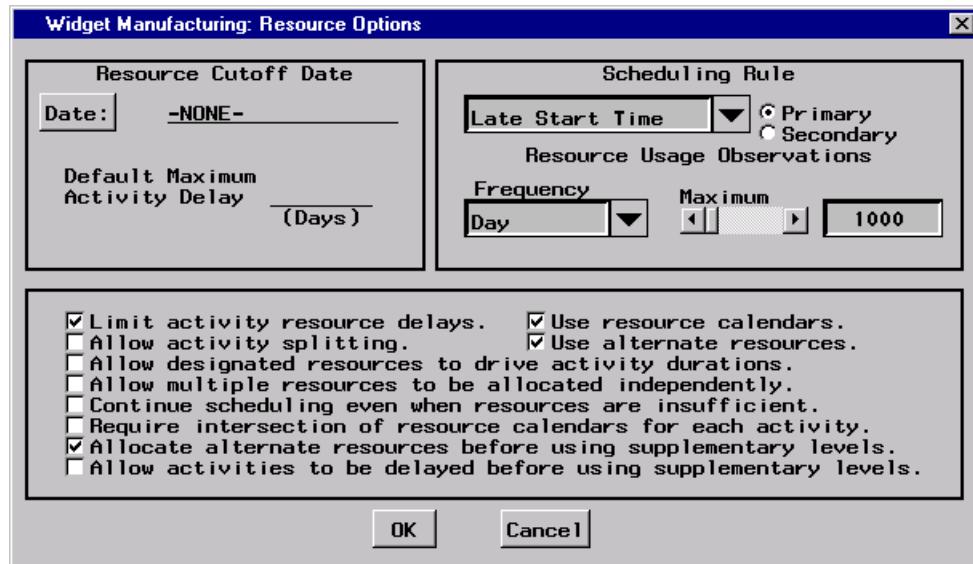


---

## Resource Options

### Resource Cutoff Date

The **Resource Cutoff Date** field can be used to specify a cutoff date for resource leveling. When this date is specified, the **scheduled start** and **finish** for activities that would occur after the cutoff date are set to missing (empty). This value can be entered with either a DATEw. (that is, 01MAY2004) or a DATETIMEw. (that

is, 01MAY2004:17:00:00) format. Alternately, by clicking the **Date:** button, you can access an [Edit Date](#) window to specify the desired value.

### **Default Maximum Activity Delay**

The **Default Maximum Activity Delay** field can be used to specify the maximum amount of time by which any activity in the project can be delayed due to lack of resources. This value acts as a default for all project activities, while individual values can be specified for each separate activity. The default value for this option is +INFINITY.

### **Resource Usage Observations**

The maximum number of resource observations sets an upper limit on the number of observations that the resource usage output data set can contain. The default value is 1000. Use the horizontal slider to increase this limit. The frequency indicates the time interval at which observations are added to the data set. Use the **Frequency** box to select the desired time interval.

#### **Limit activity resource delays.**

When this check box is selected, the [maximum activity delay](#) and each activity's [delay](#) values (if specified) are used to control activity schedule slippage when performing resource leveling; otherwise, the values are ignored and activity schedules are allowed to slip indefinitely.

#### **Use resource calendars.**

When this check box is selected, resource calendars (if specified) are used to determine on/off work periods for resources; otherwise, all resource calendars are ignored.

#### **Allow activity splitting.**

When this check box is selected, activities are allowed to be split into segments during resource allocation. The [maximum number of segments](#) and the [minimum segment duration](#) can be specified for each activity to control the extent of the splitting.

#### **Use alternate resources.**

When this check box is selected, alternate resources (if specified) are used; otherwise, they are ignored.

#### **Allow designated resources to drive activity durations.**

This check box is used to activate resource-driven durations, provided that resources have been defined as *driving* resources and work rates have been specified for the activities.

#### **Allow multiple resources to be allocated independently.**

When this check box is selected, each resource can be scheduled separately for each activity during resource allocation; otherwise, all resources (required by an activity) must be available before work on the activity can be scheduled. If this check box is selected, each resource is scheduled independently of the others. This may cause an activity's schedule to be extended if its resources cannot all start at the same time.

### **Continue scheduling even when resources are insufficient.**

When this check box is selected, the scheduling algorithm continues to schedule activities even when resources are insufficient. By default, the algorithm stops (with a partial schedule) when it cannot find sufficient resources for an activity before the activity's latest possible start time (accounting for the activity's [delay](#) value or the [maximum activity delay](#) and using supplementary or alternate resources if necessary and if allowed). This option is equivalent to specifying infinite supplementary levels for all resources under consideration.

### **Require intersection of resource calendars for each activity.**

When this check box is selected, an activity can be scheduled only during periods that are common working times for all resource calendars (corresponding to the resources used by that activity) and the activity's calendar. Use this option with caution; if an activity uses resources that have mutually disjoint calendars, that activity can never be scheduled.

If this check box is cleared and resources have independent calendars, then each resource is scheduled using its own calendar. Thus, an activity can have one resource working on a five-day calendar, while another resource is working on a seven-day calendar.

### **Allocate alternate resources before using supplementary levels.**

This check box indicates that the scheduling algorithm is to check for alternate resources before using supplementary resources. When this check box is cleared, the algorithm uses supplementary levels first (if available) and alternate resources are used only if the supplementary levels are not sufficient.

### **Allow activities to be delayed before using supplementary levels.**

When this check box is selected, the scheduling algorithm waits until an activity's [late start](#) plus [delay](#) before it is scheduled using a supplementary level of resources. Otherwise, even if an activity has a nonzero value specified for [delay](#), it can be scheduled using supplementary resources before late start plus [delay](#).

## **Scheduling Rules**

The primary scheduling rule is used to order the list of activities whose [predecessor](#) activities have been completed while scheduling activities subject to resource constraints. The secondary scheduling rule is used to break ties caused by the primary scheduling rule. The following scheduling rule choices are available :

Activity Priority	Late Finish Time
Delayed Late Start	Resource Priority
Late Start Time	Shortest Duration

The default primary scheduling rule is Late Start Time, while the default secondary scheduling rule is Shortest Duration.

### **Activity Priority**

The Activity Priority scheduling rule specifies that activities in the waiting list (for resources) are to be sorted in the order of increasing values of their priority.

## **Delayed Late Start**

The Delayed Late Start scheduling rule specifies that activities in the waiting list (for resources) are to be sorted in the order of increasing values of their [late start](#) plus their [delay](#).

## **Late Start Time**

The Late Start Time scheduling rule specifies that activities in the waiting list (for resources) are to be sorted in the order of increasing values of their [late start](#).

## **Late Finish Time**

The Late Finish Time scheduling rule specifies that activities in the waiting list (for resources) are to be sorted in the order of increasing values of their [late finish](#).

## **Resource Priority**

The Resource Priority scheduling rule specifies that activities in the waiting list (for resources) are to be sorted in the order of increasing values of the [resource priority](#) for the most important resource used by each activity. In other words, the resource priorities are used to assign priorities to the activities in the project; these activity priorities are then used to order the activities in the waiting list (in increasing order).

## **Shortest Duration**


The Shortest Duration scheduling rule specifies that activities in the waiting list (for resources) are to be sorted in the order of increasing values of their [durations](#).

# **Reports Window**

The Reports window displays a list of all project reports defined to the Projman application. Reports are divided into two categories: Standard and Custom. Standard reports are included with the application and cannot be modified or deleted. You can copy and modify standard reports to create custom reports, which can be copied, modified, and deleted.

Reports are grouped according to type. The following types are available:

Calendars	Resource Schedule
Gantt Charts	Resource Usage
Network Diagrams	Tabular
Resource Cost	

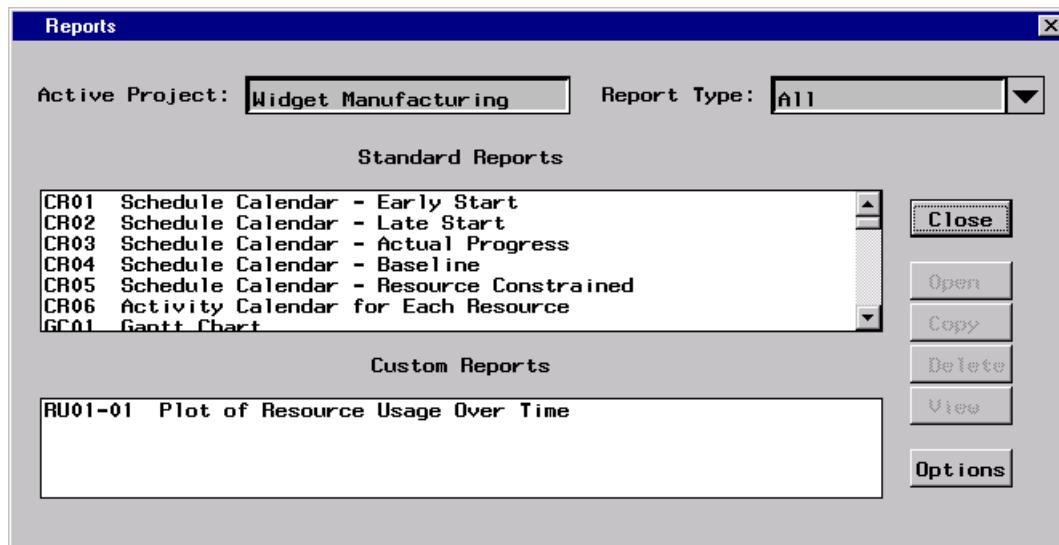

You can define as many different reports as you would like. Reports are designed to work with any project, provided that the necessary data are available. Individual report options can be set by accessing the [Options window](#) for a particular report. For more information, see the section “[Options Window](#)” on page 809.

Global report options can be set by accessing the [Report Options window](#). These options include the setting of default colors and fonts as well as the specification of report titles and footnotes. For more information, see the section “[Report Options Window](#)” on page 806.

## Active Project

The **Active Project** indicates the project that is active for the Reports window. When you generate reports, the active project provides the data for the selected report. When multiple projects are open at one time, the active project removes any confusion about which project data are used to produce the report. To change the active project, simply click on the name of the current project, and a list of open projects is displayed for selection.

## Report Type

The **Report Type** box indicates the type of reports that are currently displayed in the window. By default, all reports are initially displayed. For example, you might use this option to specify that only Gantt chart reports are to be listed in the window. To change the report type, click on the box, and a list of available report types is displayed.

## Standard Reports

This list contains all of the reports (of a particular type or types) that are defined by the Projman application. These standard reports cannot be modified or deleted. To make changes to one of these reports, you must select the desired report and click the **Copy** button. A copy of the selected report is added to the **Custom Reports** list. Click the **View** button to generate a report.

## Custom Reports

This list contains all of the reports (of a particular type or types) that have been created by the user. Custom reports are created by copying a report from the list of [standard reports](#). These reports can be manipulated by selecting the desired report in the list and clicking the **Open**, **Copy**, or **Delete** buttons. Click the **View** button to generate a particular report.

### Open

When this button is clicked, the selected custom report is displayed in the report's [Options window](#) for editing. For more information about that window, see the section "[Options Window](#)" on page 809. If no custom report is selected, this option is disabled.

### Copy

When this button is clicked, the selected report is copied and displayed in the report's [Options window](#) for editing. For more information about that window, see the section "[Options Window](#)" on page 809. If no report is selected, this option is disabled.

### Delete

When this button is clicked, the selected report in the [Custom Reports](#) list is deleted. A secondary window is opened to confirm the deletion. Note that the deletion of reports is irreversible. If no custom report is selected, this option is disabled.

### View

When this button is clicked, the currently selected report is generated. If no report is selected, the option is disabled. Note that when you modify a specific custom report, you can view the report to verify the results before saving the current changes.

### Options


When this button is clicked, the [Report Options window](#) is displayed. From that window, you can control general options that affect all project reports. For more information, see the section "[Report Options Window](#)" on page 806.

### Close

When this button is clicked, the window is closed. Also, all individual report [Options windows](#) (which are currently open) are closed.

## Report Options Window

The Report Options window provides access to various options for both tabular and graphic quality reports. You can modify output appearance features such as page headings, titles, and footnotes as well as colors and fonts. These options affect all reports generated with the Projman application.

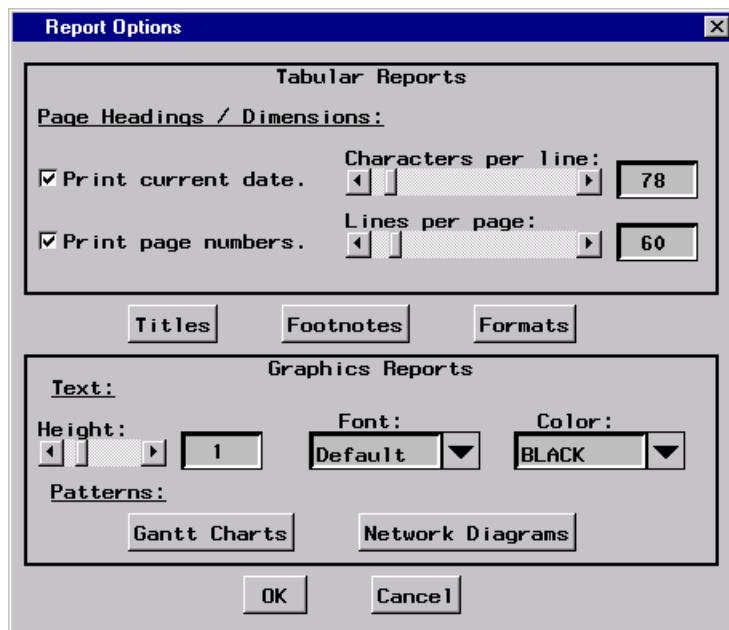

## Tabular Report Options

### **Print current date.**

When this check box is selected, the current date is displayed in the upper-right corner of each page of all tabular (nongraphics quality) reports.

### **Print page numbers.**

When this check box is selected, page numbers are displayed in the upper-right corner of each page of all tabular (nongraphics quality) reports.

### **Characters per line**

The horizontal slider can be used to specify the width of pages of tabular (nongraphics quality) reports. The number of characters per line must be an integer value between 64 and 256.

### **Lines per page**

The horizontal slider can be used to specify the length of pages of tabular (nongraphics quality) reports. The number of lines per page must be an integer value between 15 and 512.

## Titles

When the **Titles** button is clicked, a window is displayed for specifying one or more titles for project reports. You can customize any of your output from reports by adding up to four titles to the top of each page.

To create or modify a title, simply click the button corresponding to the title you want to modify. For each **title**, you can specify the type, color, and size of the font as well as the justification used to align the text. Note that the type, color, size, and justification specifications are used only when producing graphics-quality reports. For more information, see the section “[Title Window](#)” on page 808.

## Footnotes

When the **Footnotes** button is clicked, a window is displayed for specifying one or more footnotes for project reports. You can customize any of your output from reports by adding up to four footnotes to the bottom of each page.

To create or modify a footnote, simply click the button corresponding to the footnote you want to modify. For each **footnote**, you can specify the type, color, and size of the font as well as the justification used to align the text. Note that the type, color, size, and justification specifications are used only when producing graphics-quality reports. For more information, see the section “[Footnote Window](#)” on page 809.

## Formats

When the **Formats** button is clicked, a window is displayed for selecting the format to be used for displaying project schedules. You can specify whether reports are to display schedules using a DATE7. (that is, 01MAY04) or a DATETIME13. (that is, 01MAY04:12:00) format.

# Graphics Report Options

## Height

The horizontal slider can be used to specify the default height to be used for all text displayed in graphics-quality reports. The default value is 1, and valid values range from 0.1 to 5.

## Font

The **Font** box can be used to specify the default font to be used for all text displayed in graphics-quality reports.

## Color

The **Color** box can be used to specify the default color to be used for all text displayed in graphics-quality reports.

## Gantt Chart Patterns

Clicking the **Gantt Charts** button opens a window where you can specify the colors and fill patterns of the activity bars drawn on graphics-quality Gantt charts.

The various types of activity bars, along with their respective colors and fill patterns, are listed in the window. To modify the attributes for a particular activity bar, simply click the corresponding color or fill pattern, and a selection window is opened. From that window, select the desired color or fill pattern.


## Network Diagram Patterns

Clicking the **Network Diagrams** button opens a window where you can specify the colors and fill patterns of the activity nodes drawn on graphics-quality network diagram reports.

The various types of activity nodes, along with their respective colors and fill patterns, are listed in the window. To modify the attributes for a particular activity node, click the corresponding color or fill pattern, and a selection window is opened. From that window, select the desired color or fill pattern.

## Title Window

The Title window is used to modify the attributes of report titles.



### Text

The **Text** field is used to specify the text of the title or footnote. By default, Title1 contains “&projname”. When the report is generated, the macro variable, &projname, resolves to the name of the current project. Alternately, &projdesc can be used to specify the project description.

### Font

Use this selection to specify the font used to draw the **text** of the title or footnote. The font specification is used only when producing graphics-quality reports.

### Color

Use this selection to specify the color of the **text** of the title or footnote. The color specification is used only when producing graphics-quality reports.

## Justify


Use this selection to specify whether the [text](#) of the title or footnote is to be left-justified, centered, or right-justified on the page. The justification specification is used only when producing graphics-quality reports.

## Height

Use this selection to specify the height of the [text](#) of the title or footnote. The default height is 1, except for the Title1 (which has a default height of 2). The height specification is only used when producing graphics-quality reports.

## Footnote Window

The Footnote window is used to modify the attributes of report footnotes. For descriptions of the options, see the section “[Title Window](#)” on page 808.



## Options Window

A report’s Options window is used to modify the characteristics of a selected report. Options differ depending on the type of report that is being modified. All reports fall into one of the following categories:

- calendar reports
- Gantt charts
- network diagrams
- resource reports
- tabular listings

## Standard Options

The following set of options are common to several different types of reports.

### **Id**

The **Id** field displays a unique identifier label for the report. This label cannot be modified.

### **Name**

The **Name** field can be used to provide a name for the report. The report name is used for identification purposes only.

### **Identifiers**

When this button is clicked, a window is opened to enable you to add selections to the **Identifier list**. Selections are added to the bottom of the list as they are chosen. Items can be removed from the Identifier list by selecting the desired items and clicking the **Remove** button.

### **Identifier List**

The Identifier list contains the list of variables that have been selected to provide identifying information for the report. For instance, the values of these variables are used to identify (highlight) records in a tabular report or activity bars on a Gantt chart. Click the **Identifiers** button to add items to this list.

### **Sub-Groups**

When this button is clicked, a window is opened to enable you to add selections to the **Sub-Group list**. Selections are added to the bottom of the list as they are chosen. Items can be removed from the Sub-Group list by selecting the desired items and clicking the **Remove** button.

### **Sub-Group List**

The Sub-Group list contains the list of variables that have been selected to provide grouping information for the report. For instance, like values of these variables are used to group records in a tabular report for separate analysis. Similarly, like values of these variables divide activities into groups for display on separate Gantt charts. This separation (and any necessary sorting) is done automatically. Use the **Sub-Groups** button to add items to this list.

### **Remove**

When this button is clicked, highlighted selections in the **Identifier** and **Sub-Group** lists are deleted.

**OK**

If you click **OK**, the current values displayed in the window are stored and the window is closed.

**Cancel**

If you click **Cancel**, all values displayed in the window are returned to their original values (as when the window was opened) and the window is closed.

**View**

When this button is clicked, the report is generated. This option is very useful for testing modifications to a report before actually saving the changes.

**Edit Source**

When this button is clicked, a window is displayed for modifying the report source code. Changes to the source code should be made with care because incorrect changes can disable report options or cause the report to fail entirely. In the Edit Source window, type **ok** on the command line to save changes and **cancel** to cancel.

**Macro Variables**

This section describes the SAS macro variables that are defined by the Projman application during report generation. Many of these macro variables are used in the SAS source code provided with the standard reports. When you modify the source code of custom reports, this information may be helpful.

**Standard Macro Variables**

Name	Contents	Explanation
&reptname	'report name'	Current report name
&projname	'project name'	Active project name
&projdesc	'project description'	Active project description
&rdfformat	datetime7. or datetime13.	Specified by the <a href="#">Formats</a> option
&varlist	'Variables variable names'	Specified by the <a href="#">Variable list</a>
&ivarlist	'Identifier variable names'	Specified by the <a href="#">Identifier list</a>
&byvlist	BY + 'Sub-Group variable names'	Specified by the <a href="#">Sub-Group List</a>

## Calendar Reports

Name	Contents	Explanation
&start	'start variable name'	Specified by the <a href="#">Schedule</a> option
&finish	'finish variable name'	Finish corresponding to &start
	header=Small, Medium, or Large	Specified by the <a href="#">Header Size</a> option
&calopts	fill	If <a href="#">Display All Months</a> is selected
	missing	If <a href="#">Include Missing Labels</a> is selected
&caldata	caledata=work.cal workdata=	If <a href="#">calendars</a> used in scheduling
	work.shift(drop=holiday workday)	
	holidata=work.hol	If <a href="#">holidays</a> used in scheduling
&calstmt	calid calid;	If <a href="#">calendars</a> used in scheduling
	outstart monday; outfinish friday;	If <a href="#">Display Weekdays Only</a> is selected
&holstmt	holistart hstart; holidur holidur; holifin hfinish; holiname holiname;	If <a href="#">holidays</a> used in scheduling

Note that the &caldata, &calstmt, and &holstmt macro variables are not defined unless the active project's duration unit is 'DAY' or 'WEEKDAY'.

## Gantt Chart Reports

Name	Contents	Explanation
&gout	gout=work.ggseg	Graphics catalog specification
&resdict	work.resdict	Resource dictionary data set
&zonevar	'variable name'	First variable in Sub-Group List
&res	Lineprinter, Fullscreen or Graphics	Specified by the Resolution option
	caledata=work.cal workdata=	If calendars used in scheduling
	work.shift(drop=holiday workday)	
&gantdata	holodata=work.hol	If holidays used in scheduling
	labeldata=work.labels	If Mark Parent Tasks is selected
	precdat=work.repttemp	If Show Precedence is selected
	(where=(obs_type='LOGIC'))	
	mininterval='duration unit'	Specified by the Per Interval option
	scale='integer value'	Specified by the Columns option
	name="g"	Graphics catalog entry name
	maxids	Draw maximum number of identifiers
	interval='duration unit'	Duration unit used for scheduling
	dur=duration cmile='color'	If Show Milestones is selected
&ganopts	activity=actid succ=succid	
	lag=lag cprec='color'	If Show Precedence is selected
	noarrowhead	If Suppress Arrowheads is selected
	nojobnum	Unless Show Job Numbers is selected
	nolegend	Unless Show Chart Legend is selected
	compress	If Compress to One Page is selected
	hconnect chcon='color'	If Draw Task Lines is selected
	critflag	If Flag Critical Tasks is selected
	combine	If Combine Schedules is selected
	labvar=actid	If Mark Parent Tasks is selected
	markwknd	if Mark Weekends is selected
	markbreak	If Mark Work Breaks is selected
	idpages	If Print Id on Each Page is selected
	fill	If Fill Pages Completely is selected
	noframe	If Suppress Chart Frame is selected
	pcompress	If Proportional Compress is selected
	hpages='integer value'	Specified by the Horizontal Pages option
	vpages='integer value'	Specified by the Vertical Pages option
	height='numeric value'	Specified by the Text Height option
	caxis='color'	Specified by the Time Axis option
	ctext='color'	Specified by the Text option
	cframe='color'	Specified by the Chart Frame option
	holiday=(hstart) holidur=(holidur)	If holidays were used in scheduling
	holifin=(hfinish)	
	calid=calid	If calendars were used in scheduling
	timenow='timenow date'	If Draw Timenow Line is selected
	notnlabel	Unless Label Timenow Line is selected

Note that the CALEDATA=, HOLIDATA= AND WORKDATA= specifications are not added to the &gantdata macro variable unless the active project's duration unit is larger than 'DAY'.

## Network Diagram Reports

Name	Contents	Explanation
&gout	gout=work.ngseg	Graphics catalog specification
&res	Lineprinter, Fullscreen or Graphics	Specified by the <a href="#">Resolution</a> option
	name="n"	Graphics catalog entry name
	zone='variable name'	Specified by the <a href="#">Zone Variable</a> option
	nozonelabel	If <a href="#">Suppress Zone Labels</a> is selected
	zonespace	If <a href="#">Space Between Zones</a> is selected
	nodefaultid	Unless <a href="#">Show Default Vars</a> is selected
	nolabel	Unless <a href="#">Label Variables</a> is selected
	duration=duration	If <a href="#">Show Duration</a> is selected
	separatearcs	If <a href="#">Draw Separate Arcs</a> is selected
	showstatus	If <a href="#">Show Progress</a> is selected
	compress	If <a href="#">Compress to One Page</a> is selected
	centerid	If <a href="#">Center Id Values</a> is selected
	spanningtree	If <a href="#">Spanning Tree Layout</a> is selected
	lag=(lag)	If <a href="#">Show Precedence Type</a> is selected
	rectilinear	If <a href="#">Draw Rectangular Arcs</a> is selected
	pcompress	If <a href="#">Proportional Compress</a> is selected
&netopts	arrowhead=0	If <a href="#">Suppress Arrowheads</a> is selected
	noarrowfill	If <a href="#">Draw Open Arrowheads</a> is selected
	nonumber	If <a href="#">Suppress Page Numbers</a> is selected
	hpages='integer value'	Specified by the <a href="#">Horizontal Pages</a> option
	vpages='integer value'	Specified by the <a href="#">Vertical Pages</a> option
	height='numeric value'	Specified by the <a href="#">Text Height</a> option
	carcs='color'	Specified by the <a href="#">Arcs</a> option
	ccritarcs='color'	Specified by the <a href="#">Critical Arcs</a> option
	ctext='color'	Specified by the <a href="#">Node Text</a> option
	frame caxis='color'	If <a href="#">Draw Border</a> is selected
	autozone	If <a href="#">Automatic Zone Layout</a> is selected
	linear	If <a href="#">Draw Linear Time Axis</a> is selected
	autoref cref='color'	If <a href="#">Draw Reference Lines</a> is selected
	refbreak	If <a href="#">Show Ref. Line Breaks</a> is selected
	showbreak	If <a href="#">Show Time Axis Breaks</a> is selected
	notimeaxis	If <a href="#">Suppress Time Axis</a> is selected
	align='schedule variable name'	Specified by the <a href="#">Schedule</a> option

Note that the following specifications are not added to the &netopts macro variable unless the [Schedule](#) option is specified: FRAME, CAXIS=, LINEAR, AUTOREF, CREF=, REFBREAK, SHOWBREAK, AND NOTIMEAXIS.

## Resource Reports

Name	Contents	Explanation
&gout	gout=work.rgseg	Graphics catalog specification
&plotopts	name="r"	Graphics catalog entry name
&chropts	name="r"	Graphics catalog entry name
&resdict	work.resdict	Resource dictionary data set
&schedout	'data set name'	Report schedule data set
&varlist	<u>ALL</u> 'resource name'	If Scope option is set to All Resources If Scope option is set to Selected Resource
&res	Lineprinter or Graphics	Specified by the Resolution option
&interval	'duration unit'	Specified by the Frequency scheduling option
&mwhere		Not currently initialized

## Tabular Listing Reports


Name	Contents	Explanation
&prnopts	round	If Round values is selected
	double	If Double space is selected
	noobs	Unless Print observation number is selected
	label	Unless Suppress labels is selected
	n	If Print number of observations is selected
	uniform	If Format pages uniformly is selected

## Calendar Report Options Window

This window provides access to the settings and options available for calendar reports. By changing values in this window, you can create and customize calendar reports to meet your specific needs. Note that some options may be unavailable if the active project does not contain the appropriate data. Also, if data unique to a specific project are required by a report, that report may fail when generated for a different project.

Note that reports can be generated and viewed to verify the results before any changes are saved. Access to the source code is also provided.

For a description of standard report options, see the section “Standard Options” on page 810.

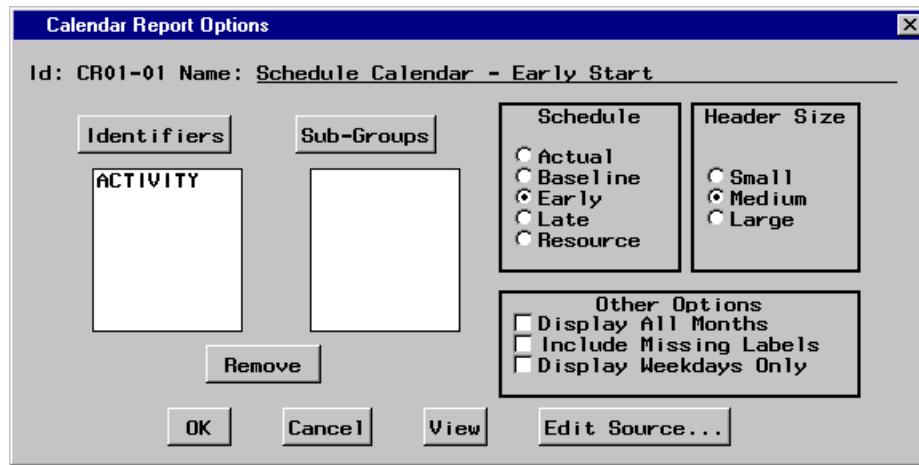

## Schedule

The setting of the **Schedule** option indicates which project schedule is to be used to mark activities on the calendar. You can choose from the actual, baseline, early, late, and resource-constrained schedules.

## Header Size

This option specifies the type of heading to use in displaying the name of the month and year on the calendar report. When **Small** is selected, the month and year are displayed on one line. For the **Medium** selection, the month and year are displayed in a box 4-lines high, while the **Large** selection will display the month name 7-lines high (the year is included if space is available).

## Display All Months

When selected, this check box specifies that all months between the first and last activity start and finish dates, inclusive, are to be displayed (including months that contain no activities). If this check box is cleared, months with no activities are omitted from the report.

## Include Missing Labels

When selected, this check box specifies that missing values of identifier variables will appear in the label of an activity. If this option is not selected, missing values are ignored in labeling activities.

## Display Weekdays Only

When selected, this check box specifies that only days from Monday through Friday are to be displayed in the calendar.

---


## Gantt Chart Options Window

This window provides access to the settings and options available for Gantt chart reports. By changing values in this window, you can create and customize Gantt chart reports to meet your specific needs. Note that some

options may be unavailable if the active project does not contain the appropriate data. Also, if data unique to a specific project are required by a report, that report may fail when generated for a different project.

Note that reports can be generated and viewed to verify the results before any changes are saved. Access to the source code is also provided.

For a description of standard report options, see the section “Standard Options” on page 810.

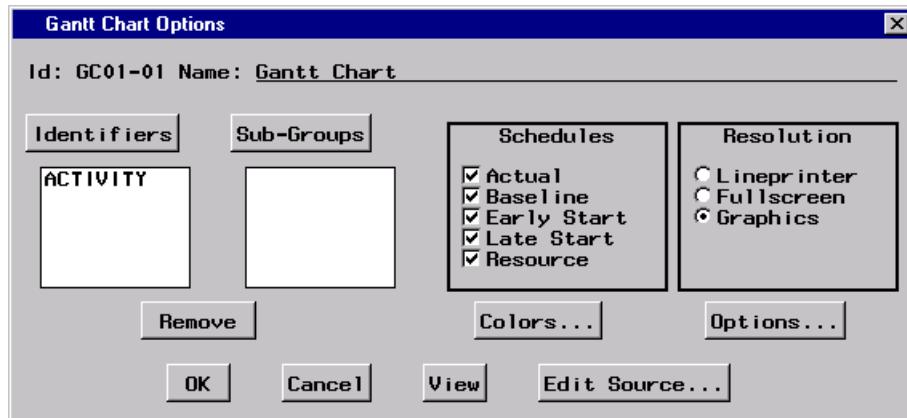

## Schedules

The **Schedules** options provide the capability to control which project schedules are to be drawn on the Gantt chart. You can choose one or more of the following schedules: actual, baseline, early start, late start, and resource-constrained. At least one schedule should be selected. If the active project does not have the indicated schedules, the extra specifications are ignored when the report is generated.

## Resolution


This option is used to specify the resolution of the Gantt chart report. The report can be produced with either lineprinter, fullscreen, or graphics-quality resolution.

## Colors

By clicking this button, you can access a window containing color options for the Gantt chart report. These options are used to control the colors of different portions of the Gantt chart output. Note that these options have no effect unless the **Resolution** option is set to produce a graphics-quality report. For more information, see the section “Color Options” on page 821.

## Options

By clicking this button, you can access a window containing additional options for the Gantt chart report.

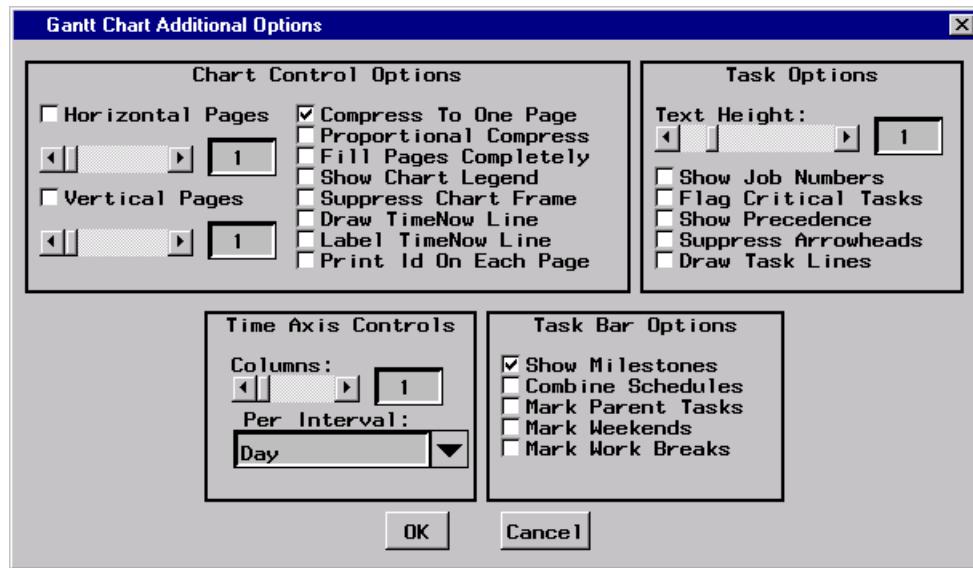

## Chart Control Options

### Horizontal Pages

When the **Horizontal Pages** check box is selected, the Gantt chart is scaled so that it spans the specified number of pages in the horizontal direction. The desired number of pages can be adjusted with the horizontal slider. Note that this option is used only when the report **Resolution** option is set for graphics-quality output. Due to intrinsic constraints on the output, the number of generated pages may not be exactly equal to the amount specified with this option.

### Vertical Pages

When the **Vertical Pages** check box is selected, the Gantt chart is scaled so that it spans the specified number of pages in the vertical direction. The desired number of pages can be adjusted with the horizontal slider. Note that this option is used only when the report **Resolution** option is set for graphics-quality output. Due to intrinsic constraints on the output, the number of generated pages may not be exactly equal to the amount specified with this option.

### Compress To One Page

When this check box is selected, the Gantt chart is compressed so that it is drawn on one physical page. Note that this option is ignored unless the report **Resolution** option is set for graphics-quality output.

### Proportional Compress

When this check box is selected, the Gantt chart is compressed so that it is drawn on one physical page. This selection is the same as the **Compress To One Page** option except that the compression of the chart is done proportionally to maintain the correct aspect ratio. In other words, the amount of horizontal and vertical compression is equal. Note that this selection is used only when the report **Resolution** option is set for graphics-quality output.

### Fill Pages Completely

When the Gantt chart spans multiple pages, this option causes each page of the Gantt chart to be filled completely before a new page is started. By default, the pages are constrained to contain an approximately equal number of activities.

### Show Chart Legend

When this check box is selected, a concise default legend is displayed at the end of each page of the Gantt chart.

### SUPPRESS CHART FRAME

When this check box is selected, the vertical boundaries to the left and right of the Gantt chart are not drawn; only the time axis and a parallel line at the bottom of the chart are drawn. If this check box is cleared, the entire chart is framed. Note that this option is ignored unless the report **Resolution** option is set for graphics-quality output.

### Draw TimeNow Line

When this check box is selected, a vertical reference line is drawn on the time axis at the **timenow date**.

### Label TimeNow Line

If the **Draw TimeNow Line** check box is selected, selecting this check box displays the value of the **timenow date** below the timenow line at the bottom of the Gantt chart.

### Print Id On Each Page

When the Gantt chart spans multiple pages, selecting this check box causes all values in the **Identifier** list to be displayed on each page of the Gantt chart.

---

## Task Options

### Text Height

When text height is specified as  $h$ , all text drawn on the Gantt chart (excluding titles and footnotes) is  $h$  times the value of the global text height option, which is specified in the **Report Options window**. For more information, see the section “**Report Options Window**” on page 806. Note that this option is used only when the report **Resolution** option is set for graphics-quality output.

### Show Job Numbers

When this check box is selected, an identifying job number is displayed beside each activity on the Gantt chart.

## Flag Critical Tasks

When this check box is selected, **critical activities** are to be flagged as critical or supercritical. Critical activities are marked CR, and supercritical activities are marked SC on the left side of the Gantt chart.

## Show Precedence

When this check box is selected, **precedence relationships** are drawn on the Gantt chart. This selection is used only when the report **Resolution** option is set for graphics-quality output.

## SUPPRESS Arrowheads

When the **Show Precedence** check box is selected, this check box indicates that arcs drawn on the Gantt chart should be drawn without arrowheads. This option is ignored unless the report **Resolution** option is set for graphics-quality output.

## Draw Task Lines

When this check box is selected, lines are drawn from the left edge of the Gantt chart to the beginning of the activity schedule bar.

## Time Axis Controls

### Columns

The horizontal slider is used to specify the number of columns (amount of space) for drawing each interval on the time axis, where interval is the value indicated with the **Per Interval** option. These options can be used to scale the size of the Gantt chart.

### Per Interval

The **Per Interval** combo box indicates the **duration unit** to use for scaling the size of the Gantt chart. The **Columns** option indicates the number of columns (amount of space) available for drawing each specified interval on the time axis.

## Task Bar Options

### Show Milestones

When this check box is selected, all activities that have zero duration are represented on the Gantt chart by a milestone symbol. This option is ignored unless the report **Resolution** option is set for graphics-quality output.

### Combine Schedules

When this check box is selected, the early/late and actual schedule bars of an activity are concatenated into a single bar on the Gantt chart. A vertical reference line is automatically drawn at the current **timenow** date. This timenow line acts to partition the Gantt chart into two regions; the region to the left of the timenow line reporting the actual schedule (events that have already taken place) and the region to the right (including the timenow line) reporting only the predicted early/late schedule.

## Mark Parent Tasks

When this check box is selected, symbols are added to the activity bars of **supertasks** on the Gantt charts. These symbols emphasize the parent-child relationship between the supertask and its **subtasks**. This option is used only when the report **Resolution** option is set for graphics-quality output.

## Mark Weekends


When this check box is selected, all weekends (or nonworked days during a week) are marked on the Gantt chart.

## Mark Work Breaks

When this check box is selected, all work breaks (nonworked periods) during a day are marked on the Gantt chart. This option automatically activates the **Mark Weekends** option.

## Color Options

This window is used to set options that control the color of various features of the Gantt chart report. Note that these options are ignored unless the report **Resolution** option is set for graphics-quality output.

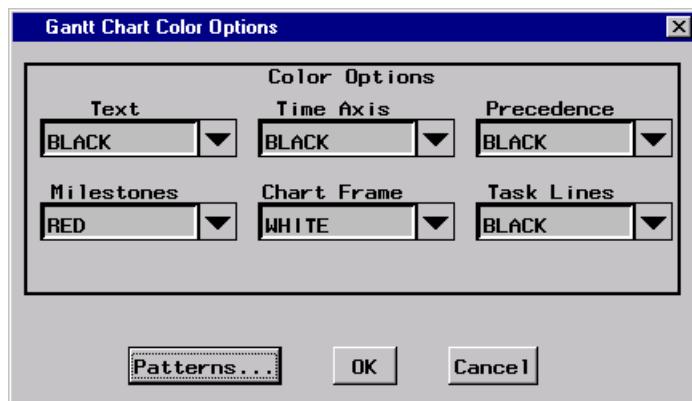

### Text

The **Text** box can be used to specify the color to use for displaying text that appears on the Gantt chart. Note that this color specification does not apply to titles, footnotes or any annotated text.

### Time Axis

The **Time Axis** box can be used to specify the color to use for displaying the time axis along the top of the Gantt chart. The same color is also used for the frame around the chart area (where the activity bars are drawn).

## Precedence

The **Precedence** box can be used to specify the color to use for drawing the precedence connections on the Gantt chart. Note that this option is used only when **precedence relationships** are to be drawn on the Gantt chart.

## Milestones

The **Milestone** box can be used to specify the color to use for drawing any milestone symbols that appear on the Gantt chart.

## Chart Frame

The **Chart Frame** box can be used to specify the background color for the chart area (where the activity bars are drawn).

## Task Lines


The **Task Lines** box can be used to specify the color to use for drawing the task lines on the Gantt chart. Note that this option is used only when task lines are to be drawn on the Gantt chart.

## Network Diagram Options Window

This window provides access to the settings and options available for network diagram reports. By changing values in this window, you can create and customize reports to meet your specific needs. Note that some options may be unavailable if the **active project** does not contain the appropriate data. Also, if data unique to a specific project are required by a report, that report may fail when generated for a different project.

Note that reports can be generated and viewed to verify the results before any changes are saved. Access to the source code is also provided.

For a description of standard report options, see the section “**Standard Options**” on page 810.

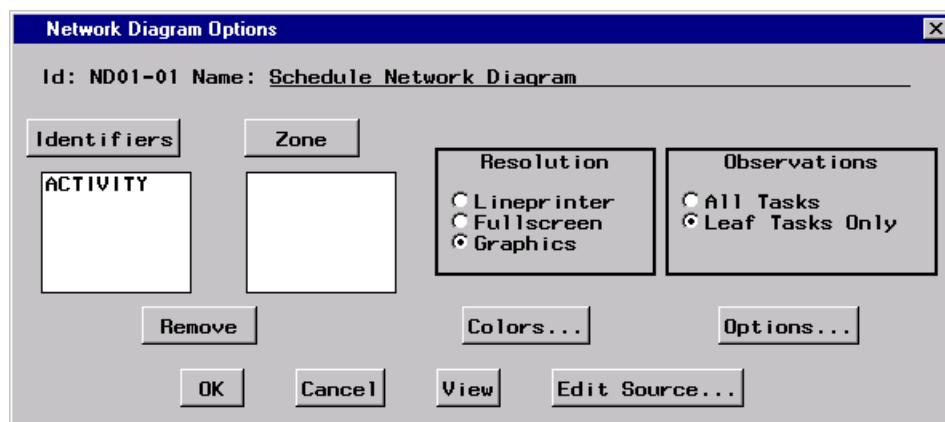

## Zone

When the **Zone** button is clicked, a window is opened to enable you to select a **Zone variable**. The selection is displayed on the window. The Zone variable can be removed by selecting the variable and clicking the **Remove** button.

## Zone Variable

The Zone variable is used to divide the network diagram into horizontal bands or zones corresponding to the distinct values of the variable. Most projects have at least one natural classification of the different activities in the project: department, type of work involved, location of the activity, and so on. By specifying a Zone variable, you can use this classification to subdivide the network diagram. The zones are automatically labeled with the Zone variable values and are separated by dividing lines. Click the **Zone** button to select a Zone variable.

## Remove

When this button is clicked, highlighted selections in the **Identifier** and **Zone** lists are deleted.

## Resolution

This option is used to specify the resolution of the network diagram report. The report can be produced with either lineprinter, fullscreen, or graphics-quality resolution.

## Observations


This option is used to specify which observations are used to produce the network diagram. For hierarchical projects, selecting **Leaf Tasks Only** means that only the lowest level tasks appear in the network diagram. When **All Tasks** is selected, all tasks (regardless of their hierarchical relationship) appear in the network diagram as separate nodes.

## Colors

By clicking this button, you can access a window containing color options for the network diagram report. These **options** are used to control the colors of different portions of the network diagram. Note that these options are ignored unless the **Resolution** option is set to produce a graphics-quality report. For more information, see the section “[Color Options](#)” on page 828.

## Options

By clicking this button, you can access a window containing additional options for the network diagram report.

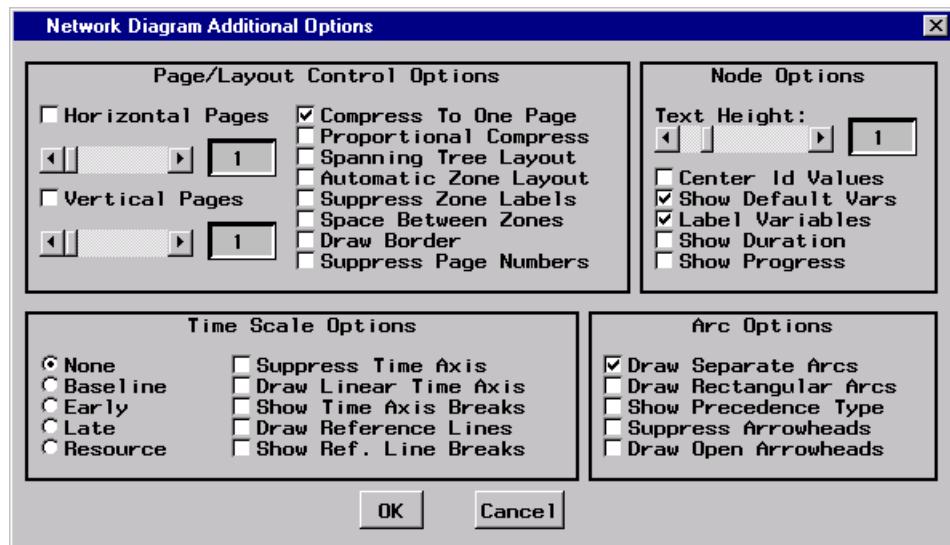

## Page/Layout Control Options

### Horizontal Pages

When the **Horizontal Pages** check box is selected, the network diagram is scaled so that it spans the specified number of pages in the horizontal direction. The desired number of pages can be adjusted with the horizontal slider. Note that this option is used only when the report **Resolution** option is set for graphics-quality output. Due to intrinsic constraints on the output, the number of generated pages may not be exactly equal to the amount specified with this option.

### Vertical Pages

When the **Vertical Pages** check box is selected, the network diagram is scaled so that it spans the specified number of pages in the vertical direction. The desired number of pages can be adjusted with the horizontal slider. Note that this option is used only when the report **Resolution** option is set for graphics-quality output. Due to intrinsic constraints on the output, the number of generated pages may not be exactly equal to the amount specified with this option.

### Compress To One Page

When this check box is selected, the network diagram is compressed so that it is drawn on one physical page. Note that this option is ignored unless the report **Resolution** option is set for graphics-quality output.

### Proportional Compress

When this check box is selected, the network diagram is compressed so that it is drawn on one physical page. This option is the same as the **Compress To One Page** option except that the compression of the diagram is done proportionally to maintain the correct aspect ratio. In other words, the amount of horizontal and vertical compression is equal. Note that this option is ignored unless the report **Resolution** option is set for graphics-quality output.

## Spanning Tree Layout

When this check box is selected, the nodes in the network diagram are positioned using a spanning tree. This method typically results in a wider layout than the default. However, for networks that have totally disjoint pieces, this option separates the network into connected components (or disjoint trees). This option is ignored if a time axis is being drawn or if the [Zone variable](#) is specified.

## Automatic Zone Layout

When selected, this check box allows automatic zoning (or dividing) of the network into connected components. This selection is equivalent to adding an automatic [Zone variable](#) that associates a tree number for each node. The tree number refers to a number assigned automatically to each distinct tree of a spanning tree of the network.

## Suppress Zone Labels

When this check box is selected and a [Zone variable](#) is specified, the zone labels and dividing lines are omitted from the network diagram.

## Space Between Zones

When this check box is selected and the [Zone variable](#) is specified, extra empty space is placed between consecutive zones.

## Draw Border

When this check box is selected, a border (or frame) is drawn around the network diagram. This option is ignored if no time axis is being drawn or if no [Zone variable](#) is specified.

## Suppress Page Numbers

When this check box is selected, no page numbers are drawn in the upper right-hand corner of a multipage network diagram. By default, pages are numbered from left to right, top to bottom.

# Node Options

## Text Height

When text height is specified as  $h$ , all text drawn on the network diagram (excluding titles and footnotes) is  $h$  times the value of the global text height option, which is specified in the [Report Options window](#). For more information about this window, see the section “[Report Options Window](#)” on page 806. Note that this option is ignored unless the report [Resolution](#) option is set for graphics-quality output.

## Center Id Values

When this check box is selected, all values of variables in the Identifier list are centered within each node in the network diagram. By default, character valued variables are left justified and numeric valued variables are right justified within each node. Note that this option is ignored unless the report [Resolution](#) option is set for graphics-quality output.

### Show Default Vars

When this check box is selected, values of the default variables are displayed within each node. These values include the activity name and any project schedule dates or float amounts. If this check box is cleared, only values appearing in the [Identifier list](#) are displayed.

### Label Variables

When this check box is selected, short (3-character) labels are displayed in front of the values that are listed within each node of the network diagram. By default, there are no labels.

### Show Duration

When this check box is selected, the duration of each activity is listed within the corresponding node in the network diagram.

### Show Progress

When this check box is selected, the current status (completed, in-progress, or pending) is indicated within each node of the network diagram. If the network diagram is created with lineprinter or fullscreen [resolution](#), activities in progress are outlined with the letter P and completed activities are outlined with the letter F; in graphics-quality resolution, in-progress activities are marked with a diagonal line across the node from the bottom left to the top right corner, while completed activities are marked with two diagonal lines. Pending activities are drawn in the default manner.

## Time Scale Options

### Schedule

Selecting a schedule indicates that a time axis is to be drawn across the top of the network diagram and nodes are to be positioned horizontally according to the values of the selected schedule start times. The minimum and maximum values are used to determine the time axis. You can choose from the baseline, early, late, and resource-constrained schedules.

### Suppress Time Axis

When this check box is selected, no time axis is drawn on the network diagram; however, nodes are still positioned horizontally according to the [Schedule](#) option.

### Draw Linear Time Axis

When a time axis is being drawn on the network diagram, the axis is divided up into even intervals based on the [duration unit](#). By default, only those intervals (columns) that contain at least one activity are drawn. When this check box is selected, all intervals are drawn. In some cases, this selection may cause the network diagram to span many pages in the horizontal direction.

### Show Time Axis Breaks

When this check box is selected, breaks in the time axis are indicated by drawing a jagged break in the time axis line just before the tick mark corresponding to the break. The time axis is determined by the setting of the **Schedule** option.

### Draw Reference Lines

When this check box is selected, a reference line is drawn at every tick mark (column) along the time axis. Reference lines are vertical lines drawn at specific positions along the time axis to indicate time intervals. The time axis is determined by the setting of the **Schedule** option.

### Show Ref. Line Breaks

When this check box is selected, breaks in the time axis are indicated by drawing a zigzag line down the network diagram just before the tick mark corresponding to the break. The time axis is determined by the setting of the **Schedule** option.

## Arc Options

### Draw Separate Arcs

When this check box is selected, arcs drawn on the network diagram are allowed to follow distinct tracks. By default, all segments of the arcs are drawn along a central track between the nodes, which may cause several arcs to be drawn on top of one another. If this check box is selected, the arcs are drawn so that they do not overlap. Note that this selection is ignored unless the report **Resolution** option is set for graphics-quality output.

### Draw Rectangular Arcs

When this check box is selected, all arcs are drawn with rectangular corners. By default, arcs are drawn with rounded corners when the report **Resolution** option is set for graphics-quality output.

### Show Precedence Type

When this check box is selected, arcs are drawn to indicate the type of **logical relationship** between the activities at either end of the arc. The start and end points of the arcs are adjusted to represent the specific relationship. By default, all arcs are drawn out of the right edge of nodes and into the left edge of nodes.

### Suppress Arrowheads


When this check box is selected, all arcs are drawn without arrowheads.

### Draw Open Arrowheads

When this check box is selected, the arrowheads on the end of the arcs are not filled. By default, the arrowheads are filled (solid). Note that this option is ignored unless the report **Resolution** option is set for graphics-quality output.

## Color Options

This window is used to set options that control the color of various features of the network diagram. Note that these options are ignored unless the report **Resolution** option is set for graphics-quality output.

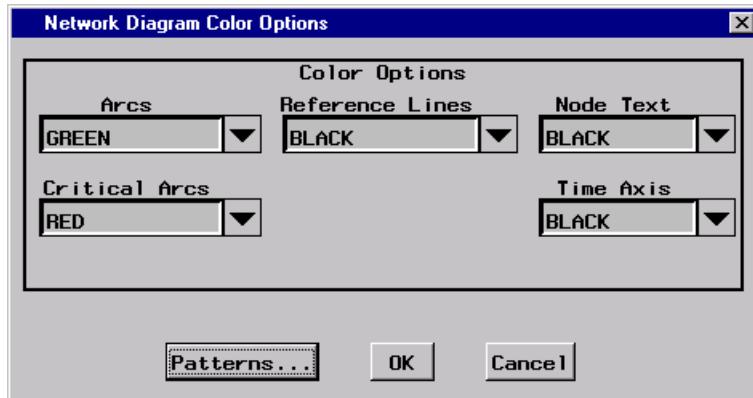

### Arcs

The **Arcs** box can be used to specify the color to use for drawing the connecting lines between the nodes in the network diagram.

### Critical Arcs

The **Critical Arcs** box can be used to specify the color to use for drawing the arcs connecting critical activities in the network diagram.

### Reference Lines

The **Reference Lines** box can be used to specify the color to use for drawing reference lines on the network diagram. Reference lines are vertical lines drawn at specific positions along the time axis to indicate time intervals. Note that this option is used only when a time axis is drawn along the top of the network diagram.

### Node Text

The **Node Text** box can be used to specify the color to use for displaying text that appears within nodes on the network diagram. Note that this color specification does not apply to titles, footnotes, or any annotated text.

### Time Axis

The **Time Axis** box can be used to specify the color to use for displaying the time axis along the top of the network diagram. The same color is also used for the frame around the chart area (where the activity bars are drawn). Note that this option is used only when a time axis is drawn along the top of the network diagram.

## Resource Report Options Window

This window provides access to the settings and options available for resource reports. By changing values in this window, you can create and customize reports to meet your specific needs. Note that some options may be unavailable if the **active project** does not contain the appropriate data. Also, if data unique to a specific project are required by a report, that report may fail when generated for a different project.

Note that reports can be generated and viewed to verify the results before any changes are saved. Access to the source code is also provided.

For a description of standard report options, see the section “Standard Options” on page 810.



### Resource

You can use the **Resource** box to select a specific resource for the report. By default, all resources are used for the report. When a resource is selected and the **Scope** option indicates that the selected resource is to be used, the resulting report contains summarized information for that resource only.

### Scope

The **Scope** option indicates whether the report is to utilize data about all project resources or only the resource specified with the **Resource** option. By default, all resources are used for the report. When a resource is selected with the **Resource** option and **Selected Resource** is chosen, the resulting report contains summarized information for the selected resource only.

### Resolution

This option is used to specify the resolution of the resource report. The report can be produced with either lineprinter or graphics quality.


## Tabular Listing Options Window

This window provides access to the settings and options available for tabular listing reports. By changing values in this window, you can create and customize reports to meet your specific needs. Note that some

options may be unavailable if the active project does not contain the appropriate data. Also, if data unique to a specific project are required by a report, that report may fail when generated for a different project.

Note that reports can be generated and viewed to verify the results before any changes are saved. Access to the source code is also provided.

For a description of standard report options, see the section “Standard Options” on page 810.

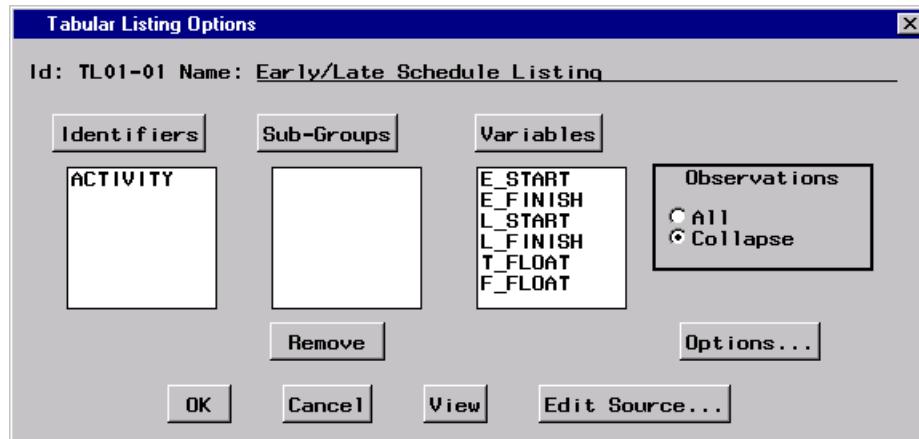

## Variables

When this button is clicked, a window is opened to allow selections to be added to the **Variable list**. Selections are added to the bottom of the list as they are chosen. Items can be removed from the Variable list by selecting the desired items and clicking the **Remove** button.

## Variable List

The Variable list contains the list of variables that are to be displayed in the tabular listing report. The information contained in these variables is displayed to the right of the information provided by the Identifier list in the report. Click the **Variables** button to add items to this list.

## Remove


When this button is clicked, highlighted selections in the Identifier, Sub-Group, and Variable lists are deleted.

## Observations

This option enables you to control which observations are used for the tabular listing report. The **All** selection indicates that all records in the input data set are to be used, while the **Collapse** selection indicates that only one observation should be displayed for each activity. When activities have multiple successors (as is usually the case), the input data set contains multiple records for some activities. Thus, when all observations are used, there can be some duplication in the resulting report.

## Options

By clicking this button, you can access a window containing additional options for the tabular listing report. These [options](#) are used to format the output.



## Additional Options

### Round values

When you select this check box, all numeric variables are rounded to two decimal places. Values are rounded before summing for totals and subtotals.

### Double space

When you select this check box, the report is double spaced. If this check box is cleared, the report is single spaced.

### Suppress labels

By default, variable labels are displayed instead of the variable names as the column heading in the tabular listing report. If you select this check box, the labels are Suppressed and the variable names are used instead.

### Print observation number

When this check box is selected, an observation (record) number is displayed for each observation in the tabular listing report. If the [Identifier list](#) is not empty, this check box has no effect.

### Print number of observations

When this check box is selected, the total number of observations (records) in the tabular listing report is displayed at the end of the report.


### Format pages uniformly

When this check box is selected, all pages of the tabular listing report are formatted uniformly. If this check box is cleared, some pages may be spaced differently (depending on the data).

## Import Activity Data Set Window

This window enables you to import a SAS data set that contains project activity information. Projman assumes that the selected data set is in the format appropriate for input to the CPM or PM procedure. For more information, refer to Chapter 4, “The CPM Procedure,” or Chapter 5, “The PM Procedure.”

When you select the data set that you want to import, you must identify certain variables within that data set. Projman attempts to recognize the variables by searching for some standard names; however, it is likely that you will need to select the required variables. When all the necessary selections have been made and the activity data set is imported, a new project is created.

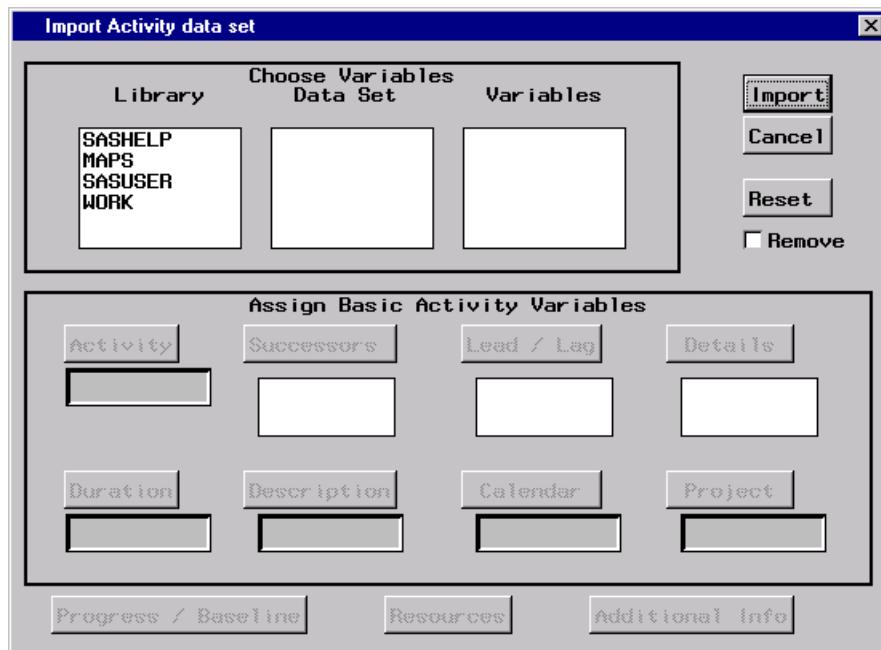

## Standard Import Options

The following set of options are common to several different import windows.

### Library

This list contains all currently defined SAS library names. Use this list to select the library that contains the data set that you want to import. Selection of a library automatically populates the **Data Set** list.

### Data Set

This list contains the names of all SAS data sets that currently reside in the selected **library**. When you select the data set that you want to import, the **Variables** list is populated automatically. When a data set is selected, some automatic variable selection may also take place.

## Variables

This list contains the names of the variables that currently exist in the selected SAS [data set](#). To import variable selections, select the desired variable or variables in this list and click the appropriate button.

### Import

When all necessary selections have been made, clicking this button causes the selected [data set](#) to be imported. If additional selections are required, an attention window is displayed.

### OK

Clicking this button accepts the current selections and closes the window.

### Cancel

Clicking this button cancels the current selections and closes the window or aborts the import process if it is selected in the primary import window.

### Reset

Clicking this button causes all variable selections in the current window to be cleared.

### Remove

When the **Remove** check box is selected, clicking a variable button causes the corresponding import variable selection to be cleared. You can click the **Reset** button to clear all import variable selections in the current window.

## Secondary Windows

### Progress / Baseline

Clicking this button opens a window that enables you to specify variables that contain activity progress information and baseline schedules. This information is optional. For information about this window, see the section “[Progress/Baseline Information](#)” on page 835.

### Resources


Clicking this button opens a window that enables you to identify the variables that contain resource requirement information for the activities. You can also specify which variable contains the activity work rate. This information is optional. For information about this window, see the section “[Resource Information](#)” on page 837.

### Additional Info

Clicking this button opens a window that enables you to specify variables that contain information about activity target (alignment) dates, limits on activity delay, activity priorities for resource scheduling, and activity splitting. This information is optional. For information about this window, see the section “[Additional Information](#)” on page 837.

## Basic Activity Information

This window is used to identify variables that contain basic activity information. For a description of standard import options, see the section “Standard Import Options” on page 832.

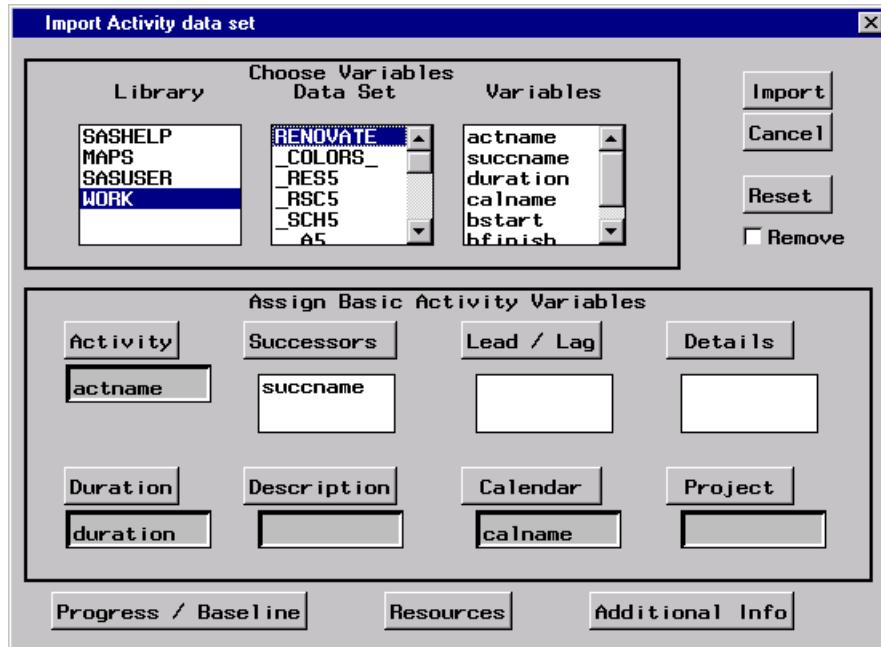

### Activity

The Activity variable should contain values that represent the names of the activities of the project. These names are assumed to be unique for each activity. This variable can contain either character or numeric values. If Successor variables are specified, the format must be the same as the Activity variable. An Activity variable is required.

### Successors

The Successor variables should contain values that represent the names of the successor activities of the project. This variable can contain either character or numeric values. If Successor variables are specified, the format must be the same as the Activity variable.

### Description

The Description variable normally will contain values that provide more detailed information (that is, longer name) about the activity. This variable can be either character or numeric.

## Project

The Project variable should contain values that represent the names of the parent (project) activities of the project. In other words, this variable indicates the parent-child (supertask-subtask) relationship between the activity named in the Project variable and the activity named in the Activity variable. This variable should be in the same format as the [Activity](#) variable.

## Duration

The Duration variable should contain values that represent the duration of each project activity. The unit of duration is assumed to be the same for each activity. This variable must be numeric.

## Lead / Lag

The Lead / Lag variables should contain values that represent the lags (or [nonstandard precedence relationships](#)) between the activities specified in the [Activity](#) and [Successor](#) variables. Although it is not required, the number of Lead / Lag variables should match the number of Successor variables. The [lag values](#) are required to follow the same naming convention as that used by the [CPM procedure](#). For more information, see the LAG= option in the section “[SUCCESSOR Statement](#)” on page 90.

## Calendar

The Calendar variable should contain values that represent the name of the calendar that the activity is to follow. Projman assumes that the calendars will be defined after the activities are imported. At that time, you can create the calendars manually or import a calendar data set. This variable can be either character or numeric.


## Details

The Details variables can be used to import nonstandard information about the activities that is stored in the import data set. For instance, you may want to import information stored in variables representing the phase of the project or the department that is responsible for the activity. These variables can be both character and numeric.

---

## Progress/Baseline Information

This window is used to identify variables that contain activity progress information and baseline schedules. For a description of standard import options, see the section “[Standard Import Options](#)” on page 832.

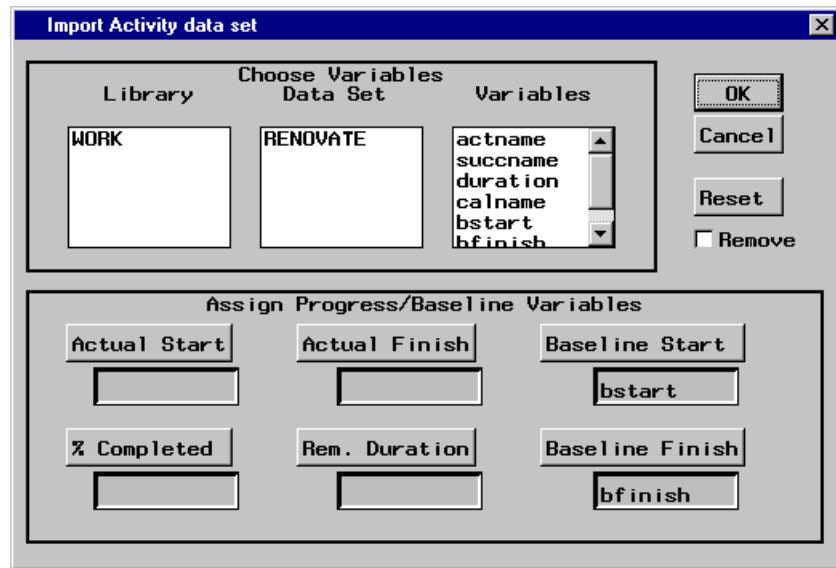

## Actual Start

The Actual Start variable should contain values that represent the actual start date of the activity. This variable must be numeric.

## Actual Finish

The Actual Finish variable should contain values that represent the actual finish date of the activity. This variable must be numeric.

## % Completed

The Percent Completed variable should contain values representing the percentage of the activity that is completed. This variable must be numeric and should contain values between 0 and 100.

## Rem. Duration

The Remaining Duration variable should contain values that represent the amount of time remaining for an activity that is in progress. This variable must be numeric and should contain nonnegative values. The unit of duration is assumed to be the same as that for the Duration variable.

## Baseline Start

The Baseline Start variable should contain values that represent the baseline start date of the activity. This variable must be numeric.


## Baseline Finish

The Baseline Finish variable should contain values that represent the baseline finish date of the activity. This variable must be numeric.

---

## Resource Information

This window is used to identify variables that contain resource requirement information. For a description of standard import options, see the section “Standard Import Options” on page 832.

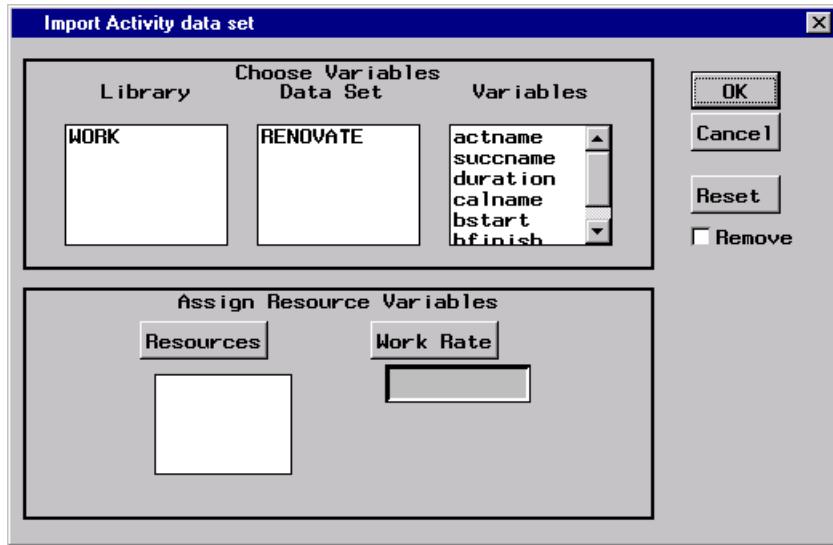

## Resources

The Resource variables should contain values that indicate the amount of resource that is needed for a particular activity. For consumable resources, this value represents the amount of resource needed per unit of duration; for replenishable resources, it indicates the amount of resource that must be available throughout the duration of the activity. These variables must be numeric.


## Work Rate

The Work Rate variable should contain values that indicate the total amount of work (time) required by one unit of a resource for a particular activity. This variable can be used to drive the activity duration for each resource required by the activity using the resource rate specified in the corresponding Resource variable.

---

## Additional Information

This window is used to identify variables that contain additional activity information. For a description of standard import options, see the section “Standard Import Options” on page 832.

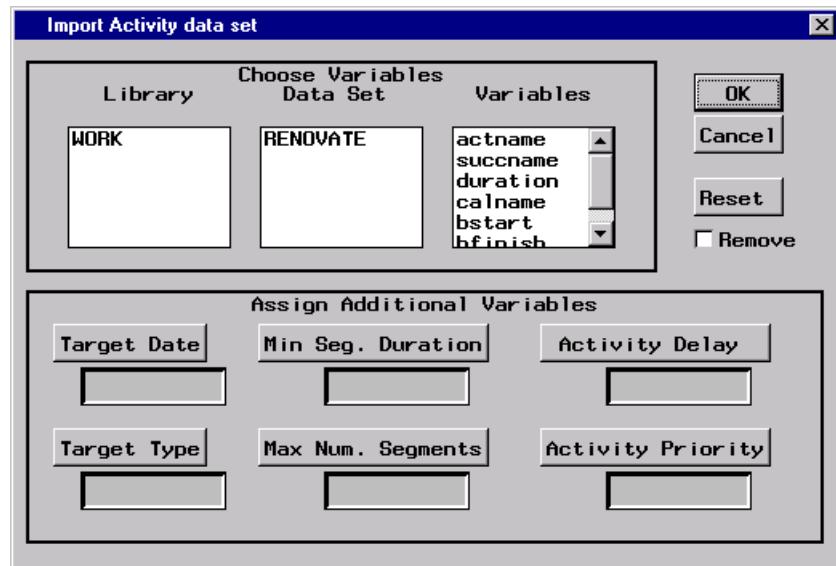

## Target Date

The Target Date variable should contain values that represent the date portion of an activity alignment constraint. For example, an activity must finish on or before a particular date. The type of alignment constraint is specified in the [Target Type](#) variable. The Target Date variable must be numeric.

## Target Type

The Target Type variable should contain values that represent the type portion of an activity alignment constraint. For example, an activity must finish on or before a particular date. The date portion of the alignment constraint is specified in the [Target Date](#) variable. The target type values are required to follow the same naming convention as that used by the [CPM procedure](#). For more information, see the section [“ALIGNTYPE Statement”](#) on page 73.

## Min Seg. Duration

The Minimum Segment Duration variable should contain values that indicate the minimum duration of a single segment of an activity (when activity splitting is allowed). This variable must be numeric.

## Max Num. Segments

The Maximum Number of Segments variable should contain values that indicate the maximum number of segments into which an activity can be split (when activity splitting is allowed). This variable must be numeric.

## Activity Delay

The Activity Delay variable should contain values that indicate the maximum amount of time by which an activity can be delayed due to resource unavailability. This variable must be numeric.

## Activity Priority

The Activity Priority variable should contain values that indicate the priority of an activity (lower values indicate higher priority). The activity priority can be used to order activities that are waiting for an unavailable resource. This variable must be numeric.


## Import Calendar Data Set Window

This window enables you to import a SAS data set that contains calendar information. Projman assumes that the selected data set is in the format appropriate for input to the **CPM** or **PM** procedure. For more information, see the section [CALEDATA Data Set](#).

When you select the data set that you want to import, you must identify certain variables within that data set. Projman attempts to recognize the variables by searching for some standard names; however, it is likely that you will need to select the required variables. When all the necessary selections have been made and the calendar data set is imported, the appropriate calendars are created.

Note that valid calendar data sets are expected to contain the following standard variables: `_SUN_`, `_MON_`, `_TUE_`, `_WED_`, `_THU_`, `_FRI_` and `_SAT_`.

For a description of standard import options, see the section “Standard Import Options” on page 832.

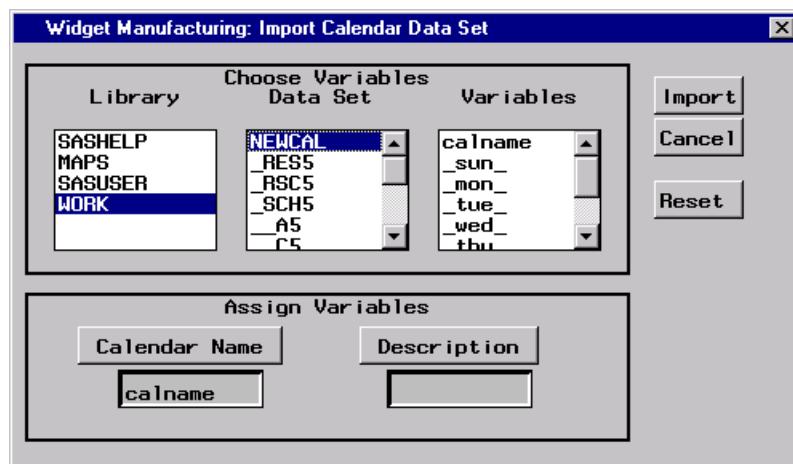

## Calendar Name

The Calendar Name variable should contain values that represent the names of the individual calendars. This variable can be either character or numeric, and it is required.

## Description


The Description variable normally contains values that provide more detailed information (that is, longer name) about the calendar. This variable can be either character or numeric.

## Import Holiday Data Set Window

This window enables you to import a SAS data set that contains holiday information. Projman assumes that the selected data set is in the format appropriate for input to the **CPM** or **PM** procedure. For more information, see the section **HOLIDATA Data Set**.

When you select the data set that you want to import, you must identify certain variables within that data set. Projman attempts to recognize the variables by searching for some standard names; however, it is likely that you will need to select the required variables. When all the necessary selections have been made and the holiday data set is imported, the appropriate holidays are created.

For a description of standard import options, see the section “Standard Import Options” on page 832.

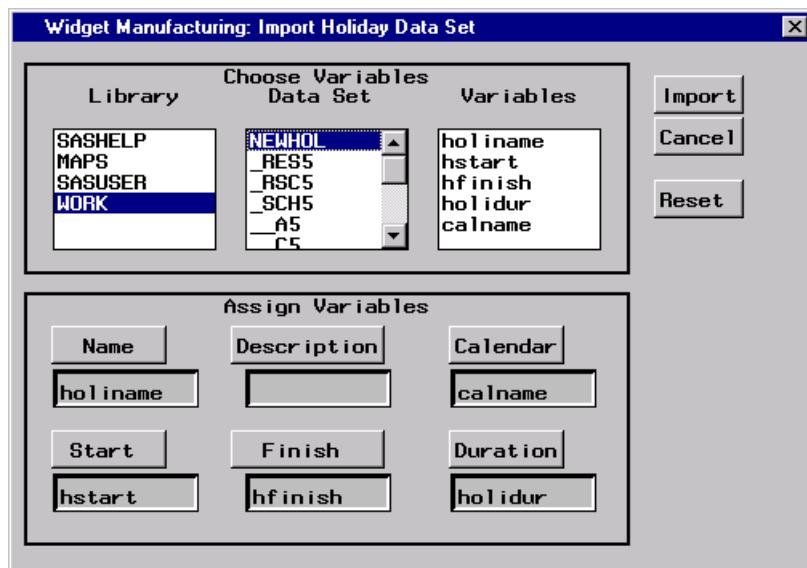

### Name

The Name variable should contain values that represent a short name for each holiday. This variable can be either character or numeric.

### Description

The Description variable normally contains values that provide more detailed information (that is, longer name) about the holiday. This variable can be either character or numeric.

### Calendar

The Calendar variable should contain values that represent the name of the calendar to which the holiday belongs. Projman assumes that the calendars already exist. If they do not, after the import, you can create the calendars or import a calendar data set. This variable can be either character or numeric.

## Start

The Start variable should contain values that indicate the start date of each holiday. This variable must be numeric, and it is required.

## Finish

The Finish variable should contain values that indicate the finish date of each holiday. This variable must be numeric. This variable is optional; however, if the Duration variable is not specified, Projman assumes that each holiday is to last one duration unit.

## Duration


The Duration variable should contain values that indicate the length of each holiday. This variable must be numeric. This variable is optional; however, if the Finish variable is not specified, Projman assumes that each holiday is to last one duration unit.

## Import Resourcein Data Set Window

This window enables you to import a SAS data set that contains resource information. Projman assumes that the selected data set is in the format appropriate for input to the CPM or PM procedure. For more information, see the section **RESOURCEIN= Input Data Set**.

When you select the data set that you want to import, you must identify certain variables within that data set. Projman attempts to recognize the variables by searching for some standard names; however, it is likely that you will need to select the required variables. When all the necessary selections have been made and the resourcein data set is imported, the appropriate resources are created.

For a description of standard import options, see the section “Standard Import Options” on page 832.

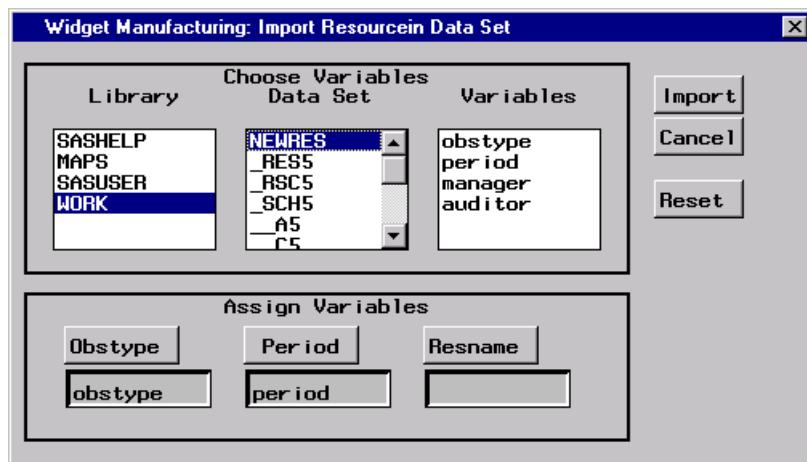

## Obstype

The Obstype variable should contain values that represent the type identifier for the particular observation. The Obstype values are required to follow the same naming convention as that used by the **CPM** procedure. For more information, see the section **OBSTYPE=variable**. This variable must be character, and it is required.

## Period

The Period variable should contain values that indicate the specific date for each observation containing resource availability information. This variable must be numeric.

## Resname

The Resname variable should contain values that represent the names of resources that have alternate (substitutable) resource specifications. This variable must be character.


## Import Workshift Data Set Window

This window enables you to import a SAS data set that contains workshift information. Projman assumes that the selected data set is in the format appropriate for input to the **CPM** or **PM** procedure. For more information, see the section **WORKDATA Data Set**.

Valid workshift data sets contain numeric variables only. If the selected data set does not contain any numeric variables, an attention window is raised.

When you have made the necessary selections, the workshift data set is imported and the appropriate workshifts are created.

For a description of standard import options, see the section “**Standard Import Options**” on page 832.



## Library

This list contains all currently defined SAS library names. Use this list to select the library that contains the data set that you want to import. Selection of a library automatically populates the [Datasets](#) list.

## Datasets

This list contains the names of all SAS data sets that currently reside in the selected [library](#). Select the data set that you want to import.

---

## Edit Date Window

This window can be used to specify and/or modify date values. If no initial date is specified, the current date is used. To modify the date value, use the horizontal sliders to select the desired Day, Month, Year, and Time. Click the **OK** button to confirm the changes or the **Cancel** button to cancel the changes. The **Clear** button can be clicked to remove the date specification.





# Chapter 11

# The Earned Value Management Macros

## Contents

---

Overview: Earned Value Management Macros . . . . .	845
Getting Started: Earned Value Management Macros . . . . .	851
Analysis . . . . .	851
Charts . . . . .	873
Syntax: Earned Value Management Macros . . . . .	879
Analysis . . . . .	879
%EVA_PLANNED_VALUE . . . . .	879
%EVA_EARNED_VALUE . . . . .	882
%EVA_METRICS . . . . .	885
%EVA_TASK_METRICS . . . . .	886
Charts . . . . .	889
%EVG_COST_PLOT . . . . .	889
%EVG_SCHEDULE_PLOT . . . . .	890
%EVG_INDEX_PLOT . . . . .	891
%EVG_VARIANCE_PLOT . . . . .	892
%EVG_GANTT_CHART . . . . .	892
%EVG_WBS_CHART . . . . .	894
Details: Earned Value Management Macros . . . . .	895
Variances . . . . .	895
Performance Indices . . . . .	896
Cost Estimates . . . . .	896
Analysis . . . . .	897
Examples: Earned Value Management Macros . . . . .	902
Example 11.1: Integrated Assembly Project . . . . .	902
Example 11.2: Construction Project . . . . .	913
References . . . . .	931

---

## Overview: Earned Value Management Macros

*Earned value* refers to the amount of work that has been completed within a project to date. In Earned Value Management (EVM), this earned value is compared to the work that was planned, in order to measure project performance and to estimate future costs and project completion.

To see why an earned value analysis might be of interest, consider a four-week project with a planned completion cost of \$10,000. After one week, the Planned Value (PV) is one quarter of \$10,000, or \$2,500. Assume that only \$2,000 has been spent so far. This is the Actual Cost (AC). Also assume that only one fifth of the project has been completed. This gives an Earned Value (EV) of \$2,000, which is one fifth of the original planned completion cost. The amount of work accomplished for the cost incurred is as expected, but the project is progressing more slowly than expected. In other words, the project is behind schedule, but within its budgetary constraints.

Based upon the performance of the project so far, EVA can be used to forecast the funds required to complete the project, and to predict the project completion date. Historically, earned value measurements have been found to be reliable indicators of future project performance as early as the 15 to 20 % completion point (see Fleming and Koppelman 2000).

The cost performance is good for the four-week project, so the project is still expected to cost \$10,000 on completion. However, based on the schedule performance, the project duration is predicted to be five weeks instead of four weeks as originally planned. Additional estimates can provide upper and lower bounds on the project costs; these estimates are discussed in the section “[Getting Started: Earned Value Management Macros](#)” on page 851.

In this chapter two distinct sets of macros are described: one for analysis and one for reporting. The first set, consisting of the %EVA\_PLANNED\_VALUE, %EVA\_EARNED\_VALUE, %EVA\_METRICS, and %EVA\_TASK\_METRICS macros, is used to analyze schedule and cost data and to derive earned value metrics. The second set, consisting of the %EVG\_COST\_PLOT, %EVG\_SCHEDULE\_PLOT, %EVG\_INDEX\_PLOT, %EVG\_VARIANCE\_PLOT, %EVG\_GANTT\_CHART and %EVG\_WBS\_CHART macros, is used to graphically represent the results from the first set.


**NOTE:** To use the graphical macros, SAS/GRAFH must be licensed.

The %EVA\_PLANNED\_VALUE macro computes the periodic planned value for the project. The periodic planned value is the periodic cost that is to be incurred by the project and is derived from the planned schedule and costs, and the workday, calendar, and holiday data sets. (These inputs are provided by the user.) The costs associated with an activity can be incurred continuously and/or at discrete time points. Continuously incurred costs are modeled by specifying a cost rate. For discretely incurred costs, the cost of the activity can be apportioned at the beginning (100-0), at the end (0-100), both equally (50-50), or both asymmetrically (custom), as desired. In general, costs can be incurred at evenly distributed time points over the duration of the associated activity, according to the number of weights specified. This macro can be run at any time —before, during, or after project execution.

Once the project is under way and actual schedule and cost information is available, the %EVA\_EARNED\_VALUE macro can be invoked to produce the revised periodic cost, along with periodic earned value. The set of periodic costs produced by %EVA\_PLANNED\_VALUE and %EVA\_EARNED\_VALUE can then be used in the %EVA\_METRICS macro to generate earned value performance measurements and summary statistics for one or more status dates. In addition, the %EVA\_METRICS macro computes cumulative costs, indices, and variances.


The %EVA\_TASK\_METRICS macro produces task-based performance measurements including Cost and Schedule Variance (CV and SV, respectively) and Cost and Schedule Performance Index (CPI and SPI, respectively).

The flow of data through the analysis macros is illustrated in [Figure 11.1](#). The large arrow indicates the passage of time between the planned schedule and budget and the updated schedule and budget.

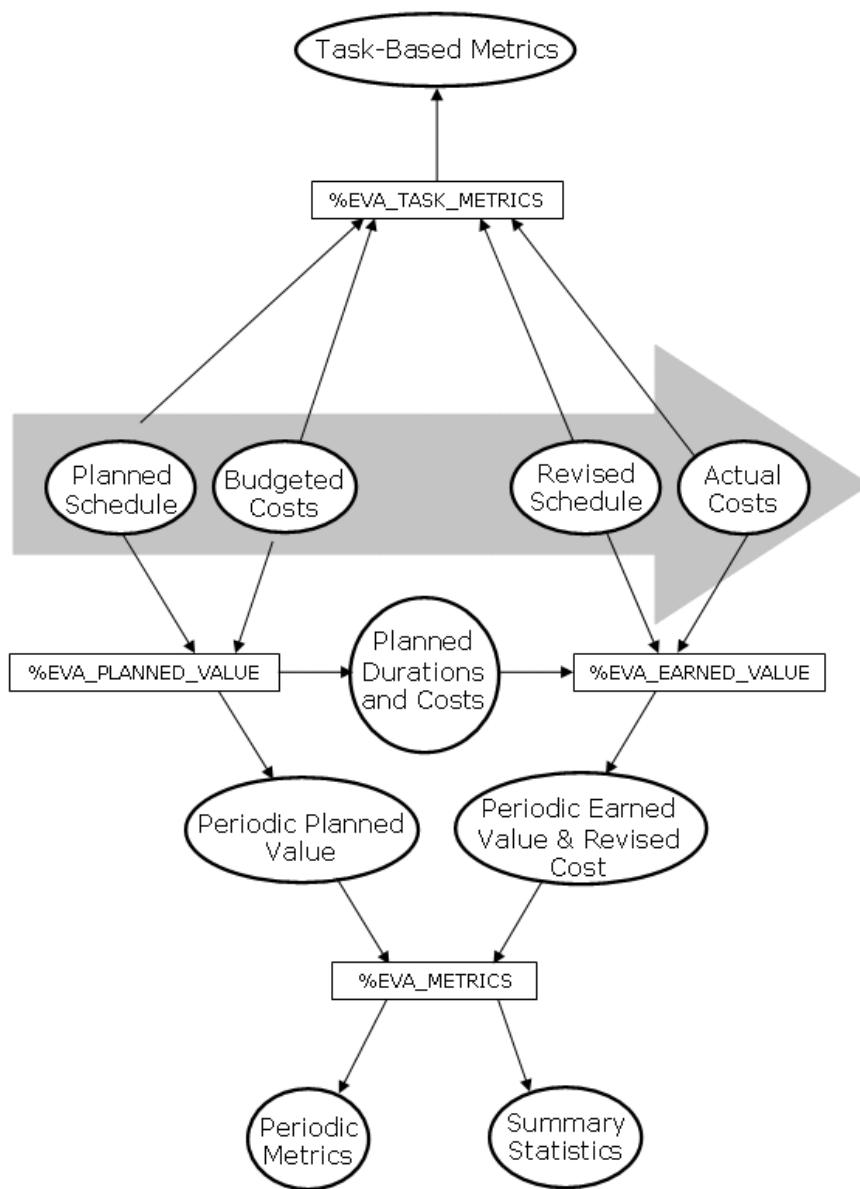**Figure 11.1** Data Flow for Analysis Macros

The first of the graphics macros are %EVG\_COST\_PLOT and %EVG\_INDEX\_PLOT. %EVG\_COST\_PLOT is used to produce line plots of planned value, earned value, actual cost, and revised cost over time, using the output from the %EVA\_METRICS macro.


The %EVG\_INDEX\_PLOT macro displays line plots of the Cost and Schedule Performance Indices (CPI and SPI, respectively), also using the output from the %EVA\_METRICS macro. The CPI is the earned value per actual cost and the SPI is the earned value per planned value. [Figure 11.2](#) shows the data flow for the %EVG\_INDEX\_PLOT and the %EVG\_COST\_PLOT macros.

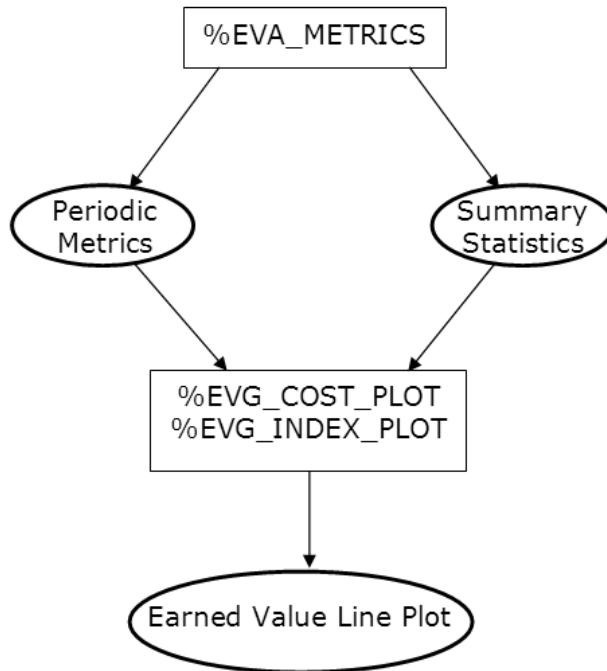**Figure 11.2** Data Flow for %EVG\_COST\_PLOT and %EVG\_INDEX\_PLOT Macros


The %EVG\_SCHEDULE\_PLOT macro is a schedule-oriented version of %EVG\_COST\_PLOT. The plot produced by %EVG\_SCHEDULE\_PLOT shows an estimate for the end date of the project. This estimate is an extrapolation of the current earned value to the BAC (Budget at Completion).

%EVG\_VARIANCE\_PLOT uses the output from %EVA\_METRICS to produce line plots for the project Cost and Schedule Variance over time. The CV is computed as the difference between the earned value and actual cost, whereas the SV is the difference between earned value and planned value. [Figure 11.3](#) shows the data flow for the %EVG\_SCHEDULE\_PLOT and %EVG\_VARIANCE\_PLOT macros.


**Figure 11.3** Data Flow for %EVG\_SCHEDULE\_PLOT and %EVG\_VARIANCE\_PLOT Macros

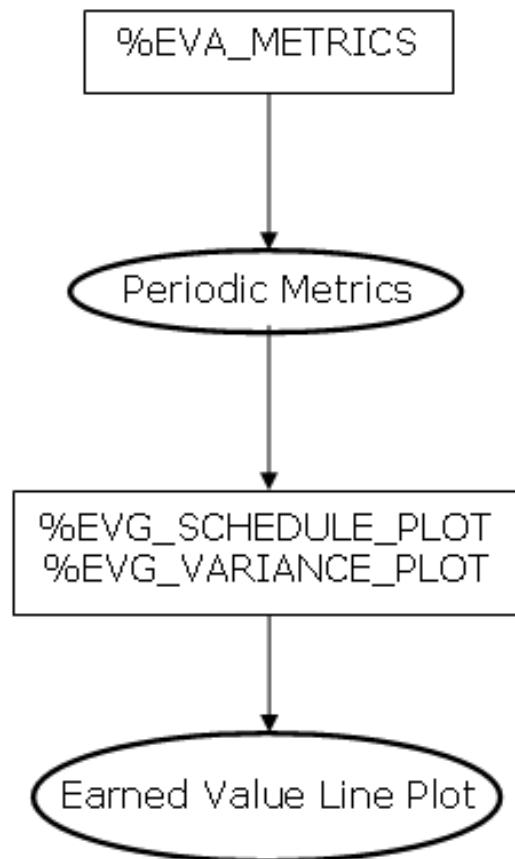

The %EVG\_GANTT\_CHART macro uses the planned and revised schedule and budget, along with the output from the %EVA\_TASK\_METRICS macro, to produce a Gantt chart of the project activities, along with the CV and SV for each activity. A pictorial description of the data flow is given in Figure 11.4.

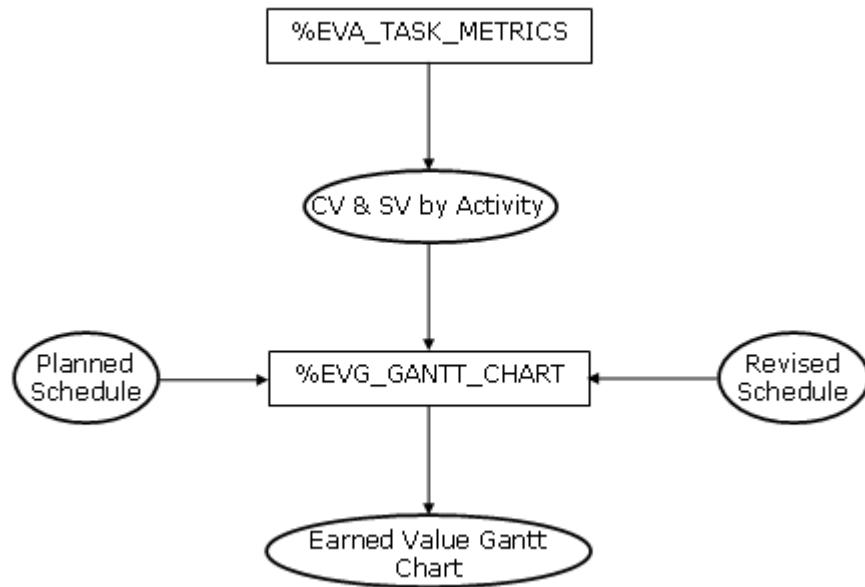**Figure 11.4** Data Flow for %EVG\_GANTT\_CHART Macro

Finally, for multiprojects, or projects with a task/subtask hierarchy, the %EVG\_WBS\_CHART macro is used to display the Work Breakdown Structure. The input data set for this macro contains the activity, the project to which it belongs (or alternatively, the Work Breakdown Structure code), and any miscellaneous data for each activity that is to be carried into the graphical output. The data flow is shown in Figure 11.5.

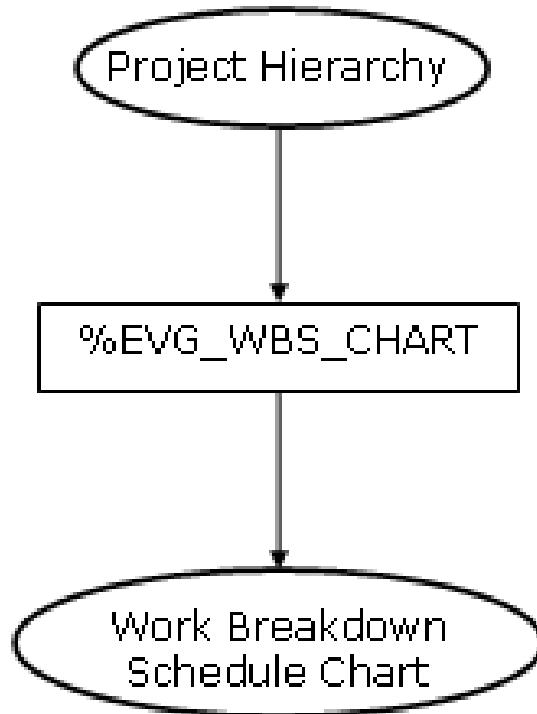**Figure 11.5** Data Flow for %EVG\_WBS\_CHART Macro


---

## Getting Started: Earned Value Management Macros

---

### Analysis

#### Generating Periodic Data Sets

Consider the following set of activities that constitute a software multiproject. The Project variable defines the project hierarchy and the Succesr1 and Succesr2 variables define the precedence relationships. The complete project data is shown in [Figure 11.6](#).

```

data softin;
  input Project  $10.
    Activity $11.
    Description $22.
    Duration
    Succesr1 $9.
    Succesr2 $9. ;
  datalines;
    SWPROJ      Software project      .
DEBUG      RECODE      Recoding          5  DOCEDREV  QATEST
DOC       DOCEDREV     Doc. Edit and Revise 10  PROD
  
```

```

DOC      PRELDOC    Prel. Documentation   15  DOCEDREV  QATEST
MISC     MEETMKT    Meet Marketing       0   RECODE
MISC     PROD        Production          1
SWPROJ   DEBUG       Debug & Code Fixes   .
SWPROJ   DOC         Doc. Subproject     .
SWPROJ   MISC        Miscellaneous      .
SWPROJ   TEST        Test Subproject     .
TEST     QATEST      QA Test Approve    10  PROD
TEST     TESTING     Initial Testing    20  RECODE
;

```

**Figure 11.6** Software Schedule Input SOFTIN**Software Schedule Input**

Obs	Project	Activity	Description	Duration	Succesr1	Succesr2
1	SWPROJ	Software project		.		
2	DEBUG	RECODE	Recoding	5	DOCEDREV	QATEST
3	DOC	DOCEDREV	Doc. Edit and Revise	10	PROD	
4	DOC	PRELDOC	Prel. Documentation	15	DOCEDREV	QATEST
5	MISC	MEETMKT	Meet Marketing	0	RECODE	
6	MISC	PROD	Production	1		
7	SWPROJ	DEBUG	Debug & Code Fixes	.		
8	SWPROJ	DOC	Doc. Subproject	.		
9	SWPROJ	MISC	Miscellaneous	.		
10	SWPROJ	TEST	Test Subproject	.		
11	TEST	QATEST	QA Test Approve	10	PROD	
12	TEST	TESTING	Initial Testing	20	RECODE	


The project network diagram showing the precedence relationships can be generated with the following code, using the NETDRAW procedure (see [Chapter 9](#) for additional information). The resulting diagram is shown in [Figure 11.7](#). (Note that the first DATA step removes the root task to simplify the diagram.)

```

data softabridged;
  set softin;
  if activity ne 'SWPROJ' and project ne 'SWPROJ' then output;
run;


proc netdraw data=softabridged out=ndout graphics;
  actnet/act=activity
  id=(description)
  nodefid
  nolabel
  succ=(succesr1 succesr2)
  lwidth=2
  coutline=black
  ctext=black
  carcs=black
  cnodefill=ltgray
  zone=project
  zonespace
  htext=3 pcompress
  centerid;
run;

```

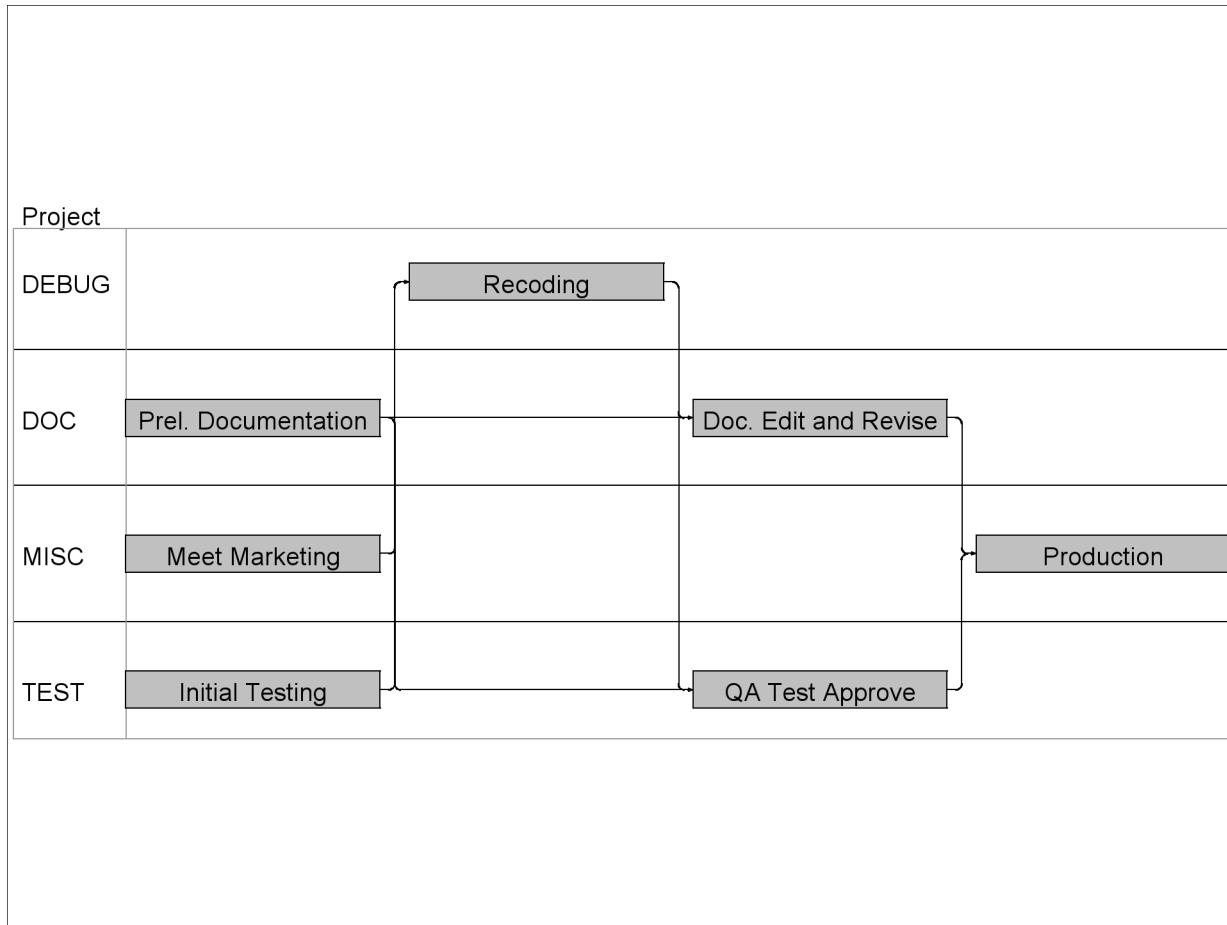**Figure 11.7** Project Network Diagram Using PROC NETDRAW

The project hierarchy, or Work Breakdown Structure (WBS), can be visualized with the following code. The graphical output is shown in Figure 11.8. The details for the use of the %EVG\_WBS\_CHART macro are given in the section “[Syntax: Earned Value Management Macros](#)” on page 879.

```
%evg_wbs_chart(
    structure=softin,
    activity=activity,
    project=project
);
```

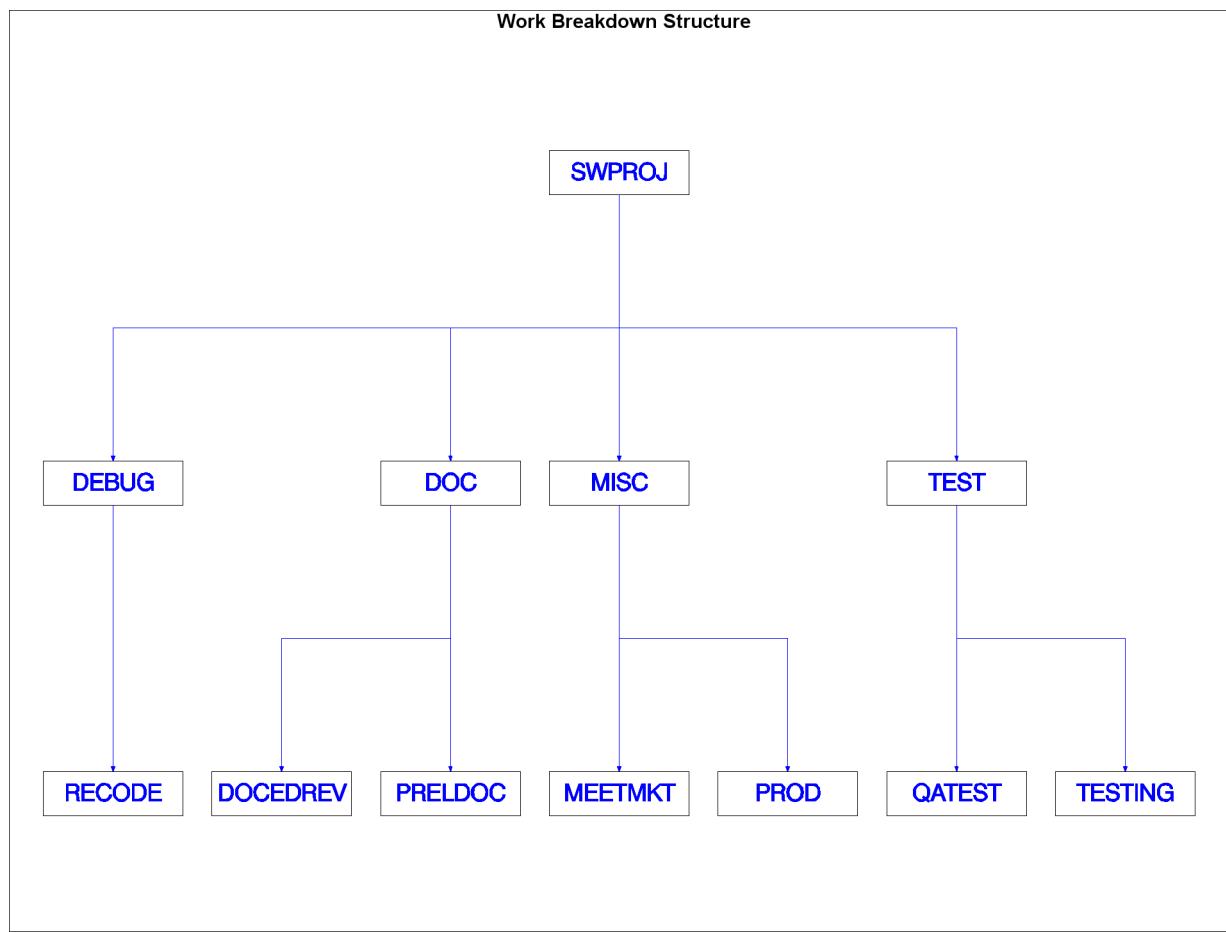**Figure 11.8** Work Breakdown Structure Using %EVG\_WBS\_CHART

The CPM procedure can be used as follows to generate a schedule based on the precedence and hierarchical constraints (see [Chapter 4](#) for more details).

```

proc cpm data=softin
  out=software
  interval=day
  date='01mar10'd;
  id description;
  project project / addwbs;
  activity activity;
  duration duration;
  successor succesr1 succesr2;
run;
  
```

The resulting schedule data set is manipulated to produce a data set containing the early and late schedules, shown in [Figure 11.9](#). The WBS\_CODE variable gives the project hierarchy. The E\_START and E\_FINISH variables represent the early schedule, and the L\_START and L\_FINISH variables give the late schedule.

```

proc sort data=software;
  by wbs_code;
run;
  
```

```

proc print data=software;
  title 'Planned Schedule';
  var activity wbs_code e_start e_finish l_start l_finish;
run;

```

**Figure 11.9 Software Schedule SOFTWARE**

### Planned Schedule

Obs	Activity	WBS_CODE	E_START	E_FINISH	L_START	L_FINISH
1	SWPROJ	0	01MAR10	05APR10	01MAR10	05APR10
2	DEBUG	0.0	21MAR10	25MAR10	21MAR10	25MAR10
3	RECODE	0.0.0	21MAR10	25MAR10	21MAR10	25MAR10
4	DOC	0.1	01MAR10	04APR10	11MAR10	04APR10
5	DOCEDREV	0.1.0	26MAR10	04APR10	26MAR10	04APR10
6	PRELDOC	0.1.1	01MAR10	15MAR10	11MAR10	25MAR10
7	MISC	0.2	01MAR10	05APR10	21MAR10	05APR10
8	MEETMKT	0.2.0	01MAR10	01MAR10	21MAR10	21MAR10
9	PROD	0.2.1	05APR10	05APR10	05APR10	05APR10
10	TEST	0.3	01MAR10	04APR10	01MAR10	04APR10
11	QATEST	0.3.0	26MAR10	04APR10	26MAR10	04APR10
12	TESTING	0.3.1	01MAR10	20MAR10	01MAR10	20MAR10

A Gantt chart of this schedule can be produced with the GANTT procedure using the following code. (See Chapter 8, for more details.)


```

goptions reset=symbol;
goptions reset=pattern;
pattern1 value=R1 color=B REPEAT=1;
pattern2 value=E color=GR REPEAT=1;
pattern3 value=S color=R REPEAT=1;
pattern4 value=X1 color=P REPEAT=1;
pattern5 value=E color=BR REPEAT=1;
pattern6 value=L1 color=GR REPEAT=1;
pattern7 value=R1 color=G REPEAT=1;
pattern8 value=X1 color=Y REPEAT=1;
pattern9 value=E color=B REPEAT=1;

title h=4pct 'Project Master Schedule';
title2 h=3pct;
proc gantt data=software;
  chart / mininterval=week pcompress
    height=1.3
    skip=2
    activity=activity
    nojobnum
    successor=(succesr1 succesr2)
    scale=10
    duration=duration;
    id description wbs_code;
run;

```

Figure 11.10 shows the output from this call to PROC GANTT.

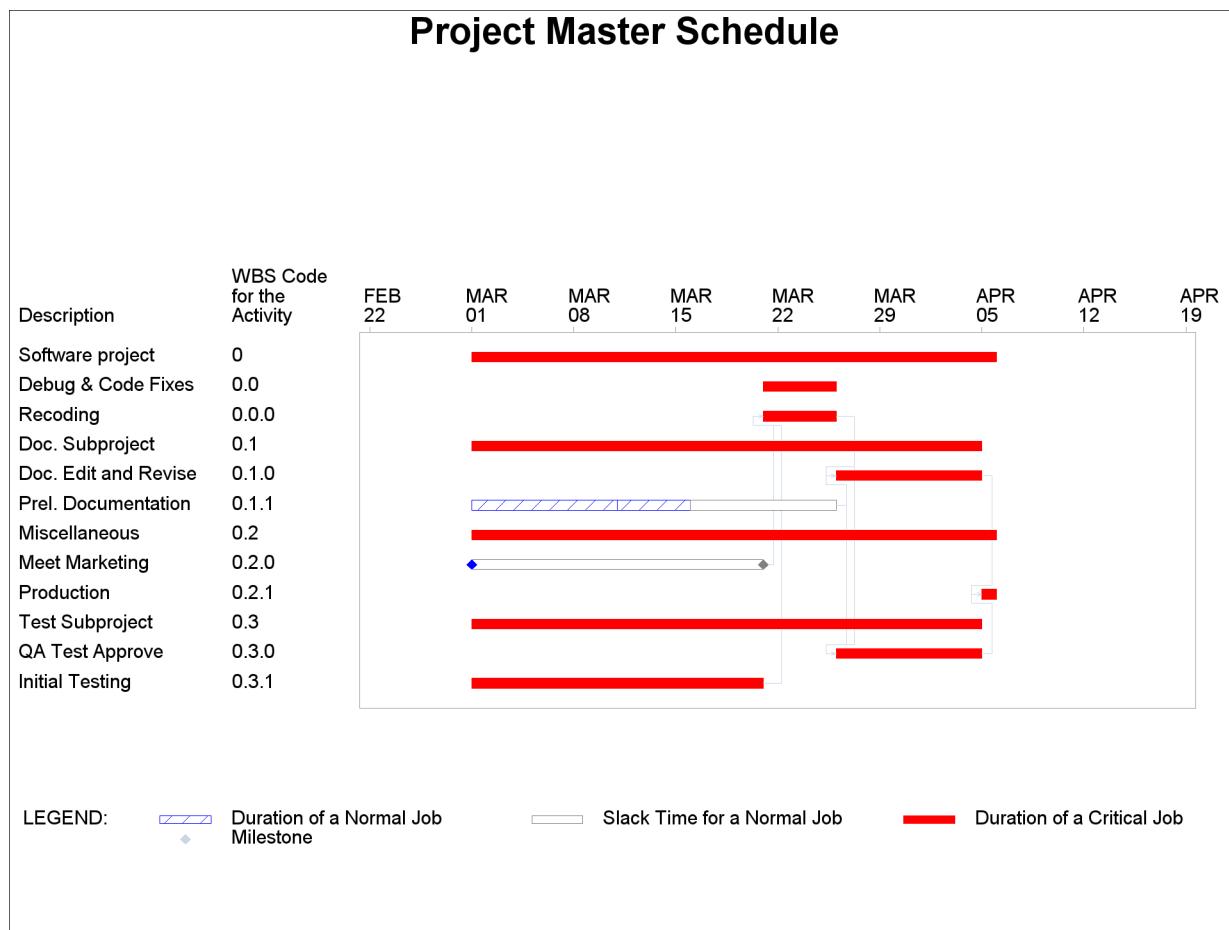**Figure 11.10** Initial Schedule Using PROC GANTT

Now suppose the early schedule is designated as the baseline. For the sake of clarity, the E\_START and E\_FINISH variables have been renamed to START and FINISH, respectively. Also, the variables required for performing the earned value analysis are retained. The modified data set is shown in Figure 11.11.

```

data software;
  set software;
  keep project activity duration description
    e_start e_finish wbs_code succesr1 succesr2;
  rename e_start = Start
    e_finish = Finish;
  label wbs_code = 'WBS Code'
    e_start = 'Start'
    e_finish = 'Finish';
  if duration eq . then duration = proj_dur;
run;

```

**Figure 11.11** Software Schedule SOFTWARE  
**Planned Schedule**

Obs	Activity	WBS		Duration	Start	Finish
		Code	Description			
1	SWPROJ	0	Software project	36	01MAR10	05APR10
2	DEBUG	0.0	Debug & Code Fixes	5	21MAR10	25MAR10
3	RECODE	0.0.0	Recoding	5	21MAR10	25MAR10
4	DOC	0.1	Doc. Subproject	35	01MAR10	04APR10
5	DOCEDREV	0.1.0	Doc. Edit and Revise	10	26MAR10	04APR10
6	PRELDOC	0.1.1	Prel. Documentation	15	01MAR10	15MAR10
7	MISC	0.2	Miscellaneous	36	01MAR10	05APR10
8	MEETMKT	0.2.0	Meet Marketing	0	01MAR10	01MAR10
9	PROD	0.2.1	Production	1	05APR10	05APR10
10	TEST	0.3	Test Subproject	35	01MAR10	04APR10
11	QATEST	0.3.0	QA Test Approve	10	26MAR10	04APR10
12	TESTING	0.3.1	Initial Testing	20	01MAR10	20MAR10

Assume also that each of the activities is budgeted to incur costs continuously at the rates shown in the RATES data set in Figure 11.12.

**Figure 11.12** Software Budget RATES

**Planned Rates**

Obs	Activity	Rate
1	SWPROJ	5
2	RECODE	6
3	PRELDOC	4
4	DOCEDREV	4
5	MEETMKT	.
6	PROD	2
7	TEST	1
8	DOC	1
9	MISC	1
10	DEBUG	1
11	TESTING	3
12	QATEST	4

To determine the periodic budgeted costs, invoke the %EVA\_PLANNED\_VALUE macro as follows:

```
%eva_planned_value(
  plansched=software,      /* schedule data */
  activity=activity,
  start=start,
  finish=finish,
  duration=duration,
  budgetcost=rates,       /* cost data */
  rate=rate
);
```

The parameters used in this call to %EVA\_PLANNED\_VALUE are described in the following list. More details are given in the section “[Syntax: Earned Value Management Macros](#)” on page 879.

- PLANSCHED= identifies the data set that contains the planned schedule.
- ACTIVITY= specifies the activity variable in the PLANSCHED= and BUDGETCOST= data sets.
- START= specifies the start date or datetime variable in the PLANSCHED= data set.
- FINISH= specifies the finish date or datetime variable in the PLANSCHED= data set.
- DURATION= specifies the task duration variable in the PLANSCHED= data set.
- BUDGETCOST= identifies the data set containing the budgeted costs.
- RATE= specifies the cost rate variable in the BUDGETCOST= data set.

The output data set generated by this call to %EVA\_PLANNED\_VALUE is shown in Figure 11.13.

**Figure 11.13** Periodic Planned Value Data Set Using %EVA\_PLANNED\_VALUE

### Daily Planned Value

Obs	Date	PV
		Rate
1	01MAR10	15
2	02MAR10	15
3	03MAR10	15
4	04MAR10	15
5	05MAR10	15
6	06MAR10	15
7	07MAR10	15
8	08MAR10	15
9	09MAR10	15
10	10MAR10	15
11	11MAR10	15
12	12MAR10	15
13	13MAR10	15
14	14MAR10	15
15	15MAR10	15
16	16MAR10	11
17	17MAR10	11
18	18MAR10	11
19	19MAR10	11
20	20MAR10	11
21	21MAR10	15
22	22MAR10	15
23	23MAR10	15
24	24MAR10	15
25	25MAR10	15
26	26MAR10	16
27	27MAR10	16
28	28MAR10	16
29	29MAR10	16
30	30MAR10	16
31	31MAR10	16
32	01APR10	16
33	02APR10	16
34	03APR10	16
35	04APR10	16
36	05APR10	8

Note that the “PV Rate” column shows the daily Planned Value (or Budgeted Cost of Work Scheduled). This is the cost incurred each day according to the plan or budget.

In general, once a project is in progress it is subject to uncertainties, the impact of which can often only be approximated in the original plan. Such uncertainties can affect the project schedule, project cost, or both. From a schedule standpoint an activity may be delayed due to a multitude of factors—a required resource being unavailable, a worker becoming sick, a machine breaking down, adverse weather conditions, etc. From a cost standpoint a contractor may revise his/her original estimate, the cost of raw materials may increase due to external factors, a sick or disabled worker might necessitate the use of a more costly contractor to minimize schedule slippage, etc.

Figure 11.14 lists the status of completed activities, and those in progress, as of March 25, 2010.

**Figure 11.14** Software Project Status SOFTACT  
Actual Dates and Percentage Complete

Obs	Activity	Start	Finish	Percent
1	MEETMKT	01MAR10	01MAR10	100
2	PRELDOC	01MAR10	14MAR10	100
3	TESTING	01MAR10	.	80

Integrating this new information with the original schedule input data set gives the updated data set shown in Figure 11.15.

```
proc sql;
  create table softupd as
    select project, softin.activity, duration,
           start, finish, percent, succesr1,
           succesr2, description
    from softin left join softact
    on softin.activity = softact.activity
    order by 1, 2
;
quit;
```

**Figure 11.15** Updated Software Schedule Input SOFTUPD

Schedule Input March 25

Obs	Project	Activity	Duration	Start	Finish	Percent	Succesr1	Succesr2
1	SWPROJ		.	.	.	.	.	.
2	DEBUG	RECODE	5	.	.	.	DOCEDREV	QATEST
3	DOC	DOCEDREV	10	.	.	.	PROD	.
4	DOC	PRELDOC	15	01MAR10	14MAR10	100	DOCEDREV	QATEST
5	MISC	MEETMKT	0	01MAR10	01MAR10	100	RECODE	.
6	MISC	PROD	1	.	.	.	.	.
7	SWPROJ	DEBUG	.	.	.	.	.	.
8	SWPROJ	DOC	.	.	.	.	.	.
9	SWPROJ	MISC	.	.	.	.	.	.
10	SWPROJ	TEST	.	.	.	.	.	.
11	TEST	QATEST	10	.	.	.	PROD	.
12	TEST	TESTING	20	01MAR10	.	80	RECODE	.

Using this updated data set, PROC CPM is then invoked to create a new schedule.

```

proc cpm data=softupd
    out=software25
    interval=day
    date='01mar10'd;
id description percent;
project project / addwbs;
activity activity;
duration duration;
actual / as=start af=finish pctcomp=percent timenow='25MAR10'd;
successor succesr1 succesr2;
run;

data software25;
set software25;
keep project activity e_start e_finish percent wbs_code duration;
rename e_start = Start
      e_finish = Finish;
label wbs_code = 'WBS Code'
      e_start = 'Start'
      e_finish = 'Finish';
run;

```

The resulting schedule is shown alongside the planned schedule in Figure 11.16.

**Figure 11.16** Updated Software Schedule SOFTWARE25

### Software Schedule as of March 25

Obs	Activity	WBS Code	Planned Start	Planned Finish	Start	Finish	Percent
1	SWPROJ	0	01MAR10	05APR10	01MAR10	15APR10	.
2	DEBUG	0.0	21MAR10	25MAR10	31MAR10	04APR10	.
3	RECODE	0.0.0	21MAR10	25MAR10	31MAR10	04APR10	.
4	DOC	0.1	01MAR10	04APR10	01MAR10	14APR10	.
5	DOCEDREV	0.1.0	26MAR10	04APR10	05APR10	14APR10	.
6	PRELDOC	0.1.1	01MAR10	15MAR10	01MAR10	14MAR10	100
7	MISC	0.2	01MAR10	05APR10	01MAR10	15APR10	.
8	MEETMKT	0.2.0	01MAR10	01MAR10	01MAR10	01MAR10	100
9	PROD	0.2.1	05APR10	05APR10	15APR10	15APR10	.
10	TEST	0.3	01MAR10	04APR10	01MAR10	14APR10	.
11	QATEST	0.3.0	26MAR10	04APR10	05APR10	14APR10	.
12	TESTING	0.3.1	01MAR10	20MAR10	01MAR10	30MAR10	80

Notice that the activity PRELDOC has completed one day ahead of schedule. Despite this encouraging bit of news, the project is showing signs of slipping. Only one other activity has completed as of the status date. The original plan called for three activities to have completed, with two additional activities completing at the end of the day. Instead, five activities are in progress. The finish date for the root parent activity, SWPROJ, shows the magnitude of the project slippage so far.

The updated cost rate information is given in Figure 11.17. Compared to the numbers listed in Figure 11.12 the rates for the PRELDOC and TESTING activities have increased, while the rate for the RECODE activity has decreased. Note that the original rates still apply for the activities that are not listed here.

**Figure 11.17** Actual Software Costs RATES25

**Actual Rates Day 25**

Obs	Activity	Rate
1	PRELDOC	5
2	RECODE	5
3	TESTING	4

To compute the impact of schedule slippage and cost overruns, data sets SOFTWARE25 and RATES25 can be specified for the %EVA\_EARNED\_VALUE macro as shown in the following SAS code. It is assumed that the %EVA\_PLANNED\_VALUE macro has been run, in which case the planned duration and costs are implicitly carried over to the %EVA\_EARNED\_VALUE macro as shown in Figure 11.1. Also, as before, the E\_START and E\_FINISH variables have been renamed to START and FINISH, respectively.

```
%eva_earned_value(
  reviseschd=software25, /* revised schedule */
  activity=activity,
  start=start,
  finish=finish,
  actualcost=rates25,    /* actual costs */
  rate=rate
);
```

The parameters used in this call to %EVA\_EARNED\_VALUE are described briefly in the following list. More details are given in the section “[Syntax: Earned Value Management Macros](#)” on page 879.

- REVISESCHED= identifies the data set that contains the revised schedule.
- ACTIVITY= specifies the activity variable in the REVISESCHED= and ACTUALCOST= data sets.
- START= specifies the start date or datetime variable in the REVISESCHED= data set.
- FINISH= specifies the finish date or datetime variable in the REVISESCHED= data set.
- ACTUALCOST= identifies the data set containing the revised cost. Activities not included are assigned the budgeted cost.
- RATE= specifies the cost rate variable in the ACTUALCOST= data set.

The variable names specified for the ACTIVITY=, START=, FINISH=, and RATE= parameters must be the same, respectively, as those previously specified for the %EVA\_PLANNED\_VALUE macro. This is to enable the later use of the %EVA\_TASK\_METRICS and %EVG\_GANTT\_CHART macros. The output generated by this call to %EVA\_EARNED\_VALUE is shown in Figure 11.18.

**Figure 11.18** Periodic Earned Value Data Set Using %EVA\_EARNED\_VALUE**Daily Earned Value and Revised Cost**

Obs	Date	EV	Rate	AC
1	01MAR10	12.5369	17	
2	02MAR10	12.5369	17	
3	03MAR10	12.5369	17	
4	04MAR10	12.5369	17	
5	05MAR10	12.5369	17	
6	06MAR10	12.5369	17	
7	07MAR10	12.5369	17	
8	08MAR10	12.5369	17	
9	09MAR10	12.5369	17	
10	10MAR10	12.5369	17	
11	11MAR10	12.5369	17	
12	12MAR10	12.5369	17	
13	13MAR10	12.5369	17	
14	14MAR10	12.5369	17	
15	15MAR10	8.2512	12	
16	16MAR10	8.2512	12	
17	17MAR10	8.2512	12	
18	18MAR10	8.2512	12	
19	19MAR10	8.2512	12	
20	20MAR10	8.2512	12	
21	21MAR10	8.2512	12	
22	22MAR10	8.2512	12	
23	23MAR10	8.2512	12	
24	24MAR10	8.2512	12	
25	25MAR10	8.2512	12	
26	26MAR10	8.2512	12	
27	27MAR10	8.2512	12	
28	28MAR10	8.2512	12	
29	29MAR10	8.2512	12	
30	30MAR10	8.2512	12	
31	31MAR10	13.2512	14	
32	01APR10	13.2512	14	
33	02APR10	13.2512	14	
34	03APR10	13.2512	14	
35	04APR10	13.2512	14	
36	05APR10	14.2512	16	
37	06APR10	14.2512	16	
38	07APR10	14.2512	16	
39	08APR10	14.2512	16	
40	09APR10	14.2512	16	
41	10APR10	14.2512	16	
42	11APR10	14.2512	16	
43	12APR10	14.2512	16	
44	13APR10	14.2512	16	
45	14APR10	14.2512	16	
46	15APR10	6.6957	8	

The “EV Rate” column shows the daily Earned Value (or Budgeted Cost of Work Performed). This is the budgeted cost for the work that was actually accomplished each day. Up to the status date (TIMENOW) of March 25, 2010, the “AC Rate” column depicts the daily Actual Cost (or Actual Cost of Work Performed). After this date, this column represents estimated costs. For this estimate, it is assumed that activities that are in progress at the status date continue at the same cost rate, rather than reverting to the budgeted cost rate. This assumption ultimately yields the revised Estimate At Completion (EAC<sub>rev</sub>). Figure 11.19 shows the daily Planned Value, Earned Value, and Actual Cost together. The disparity in the number of observations (47 here versus the former 37 for the %EVA\_PLANNED\_VALUE macro) reflects a schedule slippage of 10 days.

**Figure 11.19** Periodic Planned Value, Earned Value, and Actual Cost**Daily Planned Value, Earned Value, and Revised Cost**

Obs	DATE	PV Rate	EV Rate	AC Rate
1	01MAR10	15	12.5369	17
2	02MAR10	15	12.5369	17
3	03MAR10	15	12.5369	17
4	04MAR10	15	12.5369	17
5	05MAR10	15	12.5369	17
6	06MAR10	15	12.5369	17
7	07MAR10	15	12.5369	17
8	08MAR10	15	12.5369	17
9	09MAR10	15	12.5369	17
10	10MAR10	15	12.5369	17
11	11MAR10	15	12.5369	17
12	12MAR10	15	12.5369	17
13	13MAR10	15	12.5369	17
14	14MAR10	15	12.5369	17
15	15MAR10	15	8.2512	12
16	16MAR10	11	8.2512	12
17	17MAR10	11	8.2512	12
18	18MAR10	11	8.2512	12
19	19MAR10	11	8.2512	12
20	20MAR10	11	8.2512	12
21	21MAR10	15	8.2512	12
22	22MAR10	15	8.2512	12
23	23MAR10	15	8.2512	12
24	24MAR10	15	8.2512	12
25	25MAR10	15	8.2512	12
26	26MAR10	16	8.2512	12
27	27MAR10	16	8.2512	12
28	28MAR10	16	8.2512	12
29	29MAR10	16	8.2512	12
30	30MAR10	16	8.2512	12
31	31MAR10	16	13.2512	14
32	01APR10	16	13.2512	14
33	02APR10	16	13.2512	14
34	03APR10	16	13.2512	14
35	04APR10	16	13.2512	14
36	05APR10	8	14.2512	16
37	06APR10	.	14.2512	16
38	07APR10	.	14.2512	16
39	08APR10	.	14.2512	16
40	09APR10	.	14.2512	16
41	10APR10	.	14.2512	16
42	11APR10	.	14.2512	16
43	12APR10	.	14.2512	16
44	13APR10	.	14.2512	16
45	14APR10	.	14.2512	16
46	15APR10	.	6.6957	8

## Results

The earned value metrics can now be computed using the following code:

```
%eva_metrics(timenow='25MAR10'd);
```

It is assumed that the %EVA\_PLANNED\_VALUE and %EVA\_EARNED\_VALUE macros have been run and that the default output data sets, PV and EV, were used. This enables the %EVA\_METRICS macro to implicitly use those data sets as input (see [Figure 11.1](#)). If the default data set names were not used, you must specify the correct names using the PV= and EV= options.

The TIMENOW= parameter specifies the date or datetime to which the updated schedule and rates apply.

[Figure 11.20](#) shows the output from the %EVA\_METRICS macro.

**Figure 11.20** Earned Value Summary Metrics Using %EVA\_METRICS

**Earned Value Analysis  
as of March 25, 2010**

Metric	Value
Percent Complete	50.91
PV (Planned Value)	355.00
EV (Earned Value)	266.28
AC (Actual Cost)	370.00
CV (Cost Variance)	-103.72
CV%	-38.95
SV (Schedule Variance)	-88.72
SV%	-24.99
CPI (Cost Performance Index)	0.72
SPI (Schedule Performance Index)	0.75
BAC (Budget At Completion)	523.00
EAC (Revised Estimate At Completion)	668.00
EAC (Overrun to Date)	626.72
EAC (Cumulative CPI)	726.72
EAC (Cumulative CPI X SPI)	845.57
ETC (Estimate To Complete)*	356.72
VAC (Variance At Completion)*	-203.72
VAC%*	-38.95
TCPI (BAC) (To-Complete Performance Index)	1.68
TCPI (EAC) (To-Complete Performance Index)*	0.72

\* The CPI form of the EAC is used.

The metrics in Figure 11.20 reflect the condition of the project at the status date (TIMENOW). “Percent Complete” is the percentage of the planned work that has been accomplished. Values for this entry range from 0 to 100. PV is the Planned Value, or Budgeted Cost of Work Scheduled (BCWS). This is the work that was projected to have been completed. EV is the Earned Value, or Budgeted Cost of Work Performed (BCWP). This measure represents the value of work completed so far, in terms of budgeted cost. AC is the Actual Cost of Work Performed (ACWP), and represents the actual cost of the work so far.

At first glance, one might compare the Planned Value of \$355 to the Actual Cost of \$370, and conclude that costs are nearly on track. However, the Earned Value figure of \$266.28 puts these numbers in the proper perspective. This project is careening out of control with respect to schedule and costs.

CV and SV are the Cost and Schedule Variance, respectively. CV is the earned value less the amount spent. SV is the earned value less the planned value. CPI and SPI are the Cost and Schedule Performance indices, respectively, and are analogous to the CV and SV. The CPI and SPI are expressed as ratios, rather than differences. The value of 0.72 for CPI indicates a cost overrun situation in which the project has earned 72 cents for every dollar spent. The value of 0.75 for SPI foretells a late project, as only 75% of the planned work has been accomplished on the status date. BAC is the Budget at Completion and is the total budgeted cost of the project. EAC is the Estimate at Completion, and represents the projected total cost, given the current state of the project. For the first of the EAC metrics,  $EAC_{rev}$ , it is assumed that future work is performed at the revised rates.  $EAC_{rev}$  is computed by accumulating the “AC Rate” data found in the output data set from the %EVA\_EARNED\_VALUE macro. For  $EAC_{OTD}$ , the overrun to date estimate, it is assumed that future work will be done at the budgeted rate, which is typically not very realistic. The next two estimates take into account the performance of the project so far.  $EAC_{CPI}$ , or the cumulative CPI EAC, is widely regarded as one of the more accurate and reliable estimates, and is frequently used to provide a quick forecast of the project costs. By default, the  $EAC_{CPI}$  is used to compute the Variance at Completion (VAC) and one of the To-Complete Performance Index (TCPI) formulations, to follow. The cumulative CPI-times-SPI EAC, denoted  $EAC_{CPI \times SPI}$ , is often used to provide a high-end estimate of the project costs. ETC is the Estimate to Complete, or a projection of remaining costs. The VAC represents the financial impact of the expenditures to date on the original budget.

The TCPI is the cost performance factor that must be achieved in order to complete the remaining work using the available funds. The available funds can be defined to be either the remaining budget ( $BAC - AC$ ) or remaining costs ( $EAC - AC$ ). For example, the  $TCPI_{BAC}$  of 1.68 indicates that the project needs to earn 1.68 dollars for each dollar spent to stay within the budget. The  $TCPI_{EAC}$  is a far lower value (0.72) because the revised costs are much larger than the budgeted costs for the remaining work. See Table 11.11, Table 11.12, and Table 11.13 for formula expressions of the preceding metrics.

Figure 11.21 gives a listing of the earned value summary statistics data set produced by the %EVA\_METRICS macro. This data set is used to generate the %EVA\_METRICS report as well as some of the charts to be described in later sections.

**Figure 11.21** Summary Earned Value Data Set Using %EVA\_METRICS**Earned Value Summary Statistics**

<b>Obs</b>	<b>Name</b>		<b>March 25, 2010</b>
1	_pctcomp_	Percent Complete	50.914
2	_pv_	PV (Planned Value)	355.000
3	_ev_	EV (Earned Value)	266.280
4	_ac_	AC (Actual Cost)	370.000
5	_cv_	CV (Cost Variance)	-103.720
6	_cvp_	CV%	-38.951
7	_sv_	SV (Schedule Variance)	-88.720
8	_svp_	SV%	-24.991
9	_cpi_	CPI (Cost Performance Index)	0.720
10	_spi_	SPI (Schedule Performance Index)	0.750
11	_bac_	BAC (Budget At Completion)	523.000
12	_eacrev_	EAC (Revised Estimate At Completion)	668.000
13	_eacotd_	EAC (Overrun to Date)	626.720
14	_eaccpi_	EAC (Cumulative CPI)	726.716
15	_eaccpispi_	EAC (Cumulative CPI X SPI)	845.567
16	_etc_	ETC (Estimate To Complete)*	356.716
17	_vac_	VAC (Variance At Completion)*	-203.716
18	_vacp_	VAC%*	-38.951
19	_tcpi_	TCPI (BAC) (To-Complete Performance Index)	1.678
20	_etcpi_	TCPI (EAC) (To-Complete Performance Index)*	0.720

The %EVA\_METRICS macro also produces the cumulative periodic earned value data set shown in [Figure 11.22](#). This data set contains the cumulative planned value, earned value, and actual and revised costs, together with the associated variances and performance indices.

**Figure 11.22** Cumulative Earned Value Data Set Using %EVA\_METRICS

**Earned Value Cumulative Periodic Metrics  
Values, Costs, Variances and Indices**

Obs	Date	PV			Revised Cost		CV	SV	CPI	SPI
			EV	AC						
1	01MAR10	15	12.537	17	17	-4.463	-2.4631	0.73747	0.83579	
2	02MAR10	30	25.074	34	34	-8.926	-4.9262	0.73747	0.83579	
3	03MAR10	45	37.611	51	51	-13.389	-7.3892	0.73747	0.83579	
4	04MAR10	60	50.148	68	68	-17.852	-9.8523	0.73747	0.83579	
5	05MAR10	75	62.685	85	85	-22.315	-12.3154	0.73747	0.83579	
6	06MAR10	90	75.222	102	102	-26.778	-14.7785	0.73747	0.83579	
7	07MAR10	105	87.758	119	119	-31.242	-17.2415	0.73747	0.83579	
8	08MAR10	120	100.295	136	136	-35.705	-19.7046	0.73747	0.83579	
9	09MAR10	135	112.832	153	153	-40.168	-22.1677	0.73747	0.83579	
10	10MAR10	150	125.369	170	170	-44.631	-24.6308	0.73747	0.83579	
11	11MAR10	165	137.906	187	187	-49.094	-27.0939	0.73747	0.83579	
12	12MAR10	180	150.443	204	204	-53.557	-29.5569	0.73747	0.83579	
13	13MAR10	195	162.980	221	221	-58.020	-32.0200	0.73747	0.83579	
14	14MAR10	210	175.517	238	238	-62.483	-34.4831	0.73747	0.83579	
15	15MAR10	225	183.768	250	250	-66.232	-41.2319	0.73507	0.81675	
16	16MAR10	236	192.019	262	262	-69.981	-43.9807	0.73290	0.81364	
17	17MAR10	247	200.271	274	274	-73.729	-46.7295	0.73091	0.81081	
18	18MAR10	258	208.522	286	286	-77.478	-49.4783	0.72910	0.80822	
19	19MAR10	269	216.773	298	298	-81.227	-52.2271	0.72743	0.80585	
20	20MAR10	280	225.024	310	310	-84.976	-54.9758	0.72588	0.80366	
21	21MAR10	295	233.275	322	322	-88.725	-61.7246	0.72446	0.79076	
22	22MAR10	310	241.527	334	334	-92.473	-68.4734	0.72313	0.77912	
23	23MAR10	325	249.778	346	346	-96.222	-75.2222	0.72190	0.76855	
24	24MAR10	340	258.029	358	358	-99.971	-81.9710	0.72075	0.75891	
25	25MAR10	355	266.280	370	370	-103.720	-88.7198	0.71968	0.75009	
26	26MAR10	371			382					
27	27MAR10	387			394					
28	28MAR10	403			406					
29	29MAR10	419			418					
30	30MAR10	435			430					
31	31MAR10	451			444					
32	01APR10	467			458					
33	02APR10	483			472					
34	03APR10	499			486					
35	04APR10	515			500					
36	05APR10	523			516					
37	06APR10				532					
38	07APR10				548					
39	08APR10				564					
40	09APR10				580					
41	10APR10				596					
42	11APR10				612					
43	12APR10				628					
44	13APR10				644					

**Figure 11.22** *continued*

**Earned Value Cumulative Periodic Metrics  
Values, Costs, Variances and Indices**

Obs	Date	PV			Revised Cost	CV	SV	CPI	SPI
			EV	AC					
45	14APR10	.	.	.	660	.	.	.	.
46	15APR10	.	.	.	668	.	.	.	.

The cost and schedule variance by activity can now be produced using the following call to %EVA\_TASK\_METRICS.

```
%eva_task_metrics(
  plansched=software,
  reviseschd=software25,
  activity=activity,
  start=start,
  finish=finish,
  budgetcost=rates,
  actualcost=rates25,
  rate=rate,
  aggregate=Y,
  timenow='25MAR10'd
);
```

The parameters used in this call to %EVA\_TASK\_METRICS are described briefly in the following list. More details are given in the section “Syntax: Earned Value Management Macros” on page 879.

- PLANSCHED= identifies the data set that contains the planned schedule.
- REVISESCHED= identifies the data set that contains the updated schedule.
- ACTIVITY= specifies the activity variable in the PLANSCHED= and REVISESCHED= data sets.
- START= specifies the start date or datetime variable in the PLANSCHED= and REVISESCHED= data sets.
- FINISH= specifies the finish date or datetime variable in the PLANSCHED= and REVISESCHED= data sets.
- BUDGETCOST= identifies the data set containing the budgeted cost.
- ACTUALCOST= identifies the data set containing the revised cost.
- RATE= specifies the cost rate variable in the BUDGETCOST= and ACTUALCOST= data sets.
- AGGREGATE= indicates whether or not to roll up values along the project hierarchy; a value of Y indicates that aggregation is to be performed.
- TIMENOW= specifies the date or datetime of the updated schedule and costs.

Note that the variable names specified for the ACTIVITY=, START=, FINISH=, and RATE= parameters must be the same, respectively, as those previously specified for the %EVA\_PLANNED\_VALUE and %EVA\_EARNED\_VALUE macros.

The output produced by this invocation of the %EVA\_TASK\_METRICS macro is shown in Figure 11.23.

**Figure 11.23** Cost and Schedule Variance by Activity Using %EVA\_TASK\_METRICS

**Earned Value Analysis by Activity  
as of March 25, 2010**

Obs	Activity	WBS Code	PV	EV	AC	CV	CV%	SV	SV%	CPI	SPI
1	SWPROJ	0	355.00	266.28	370.00	-103.72	-38.95	-88.72	-24.99	0.72	0.75
2	DEBUG	0.0	35.00	0.00	0.00	0.00	0.00	-35.00	-100.00	.	0.00
3	RECODE	0.0.0	30.00	0.00	0.00	0.00	0.00	-30.00	-100.00	.	0.00
4	DOC	0.1	85.00	79.44	95.00	-15.56	-19.58	-5.56	-6.54	0.84	0.93
5	DOCEDREV	0.1.0	0.00	0.00	0.00	0.00	0.00	0.00	0.00	.	.
6	PRELDOC	0.1.1	60.00	60.00	70.00	-10.00	-16.67	0.00	0.00	0.86	1.00
7	MISC	0.2	25.00	19.57	25.00	-5.43	-27.78	-5.43	-21.74	0.78	0.78
8	MEETMKT	0.2.0	0.00	0.00	0.00	0.00	0.00	0.00	0.00	.	.
9	PROD	0.2.1	0.00	0.00	0.00	0.00	0.00	0.00	0.00	.	.
10	TEST	0.3	85.00	69.44	125.00	-55.56	-80.00	-15.56	-18.30	0.56	0.82
11	QATEST	0.3.0	0.00	0.00	0.00	0.00	0.00	0.00	0.00	.	.
12	TESTING	0.3.1	60.00	50.00	100.00	-50.00	-100.00	-10.00	-16.67	0.50	0.83


Note that by specifying Y for the AGGREGATE= parameter, the values have been rolled up along the project hierarchy; otherwise, the values would represent the corresponding activity only.

## Charts

In Figure 11.24, cost and schedule variance are plotted against time using a default invocation of the %EVG\_VARIANCE\_PLOT macro. Notice that the variances lie outside the plus or minus 10% Planned Value thresholds, which is a cause for concern.

```
%evg_variance_plot;
```

**Figure 11.24** CV and SV versus Time Using %EVG\_VARIANCE\_PLOT

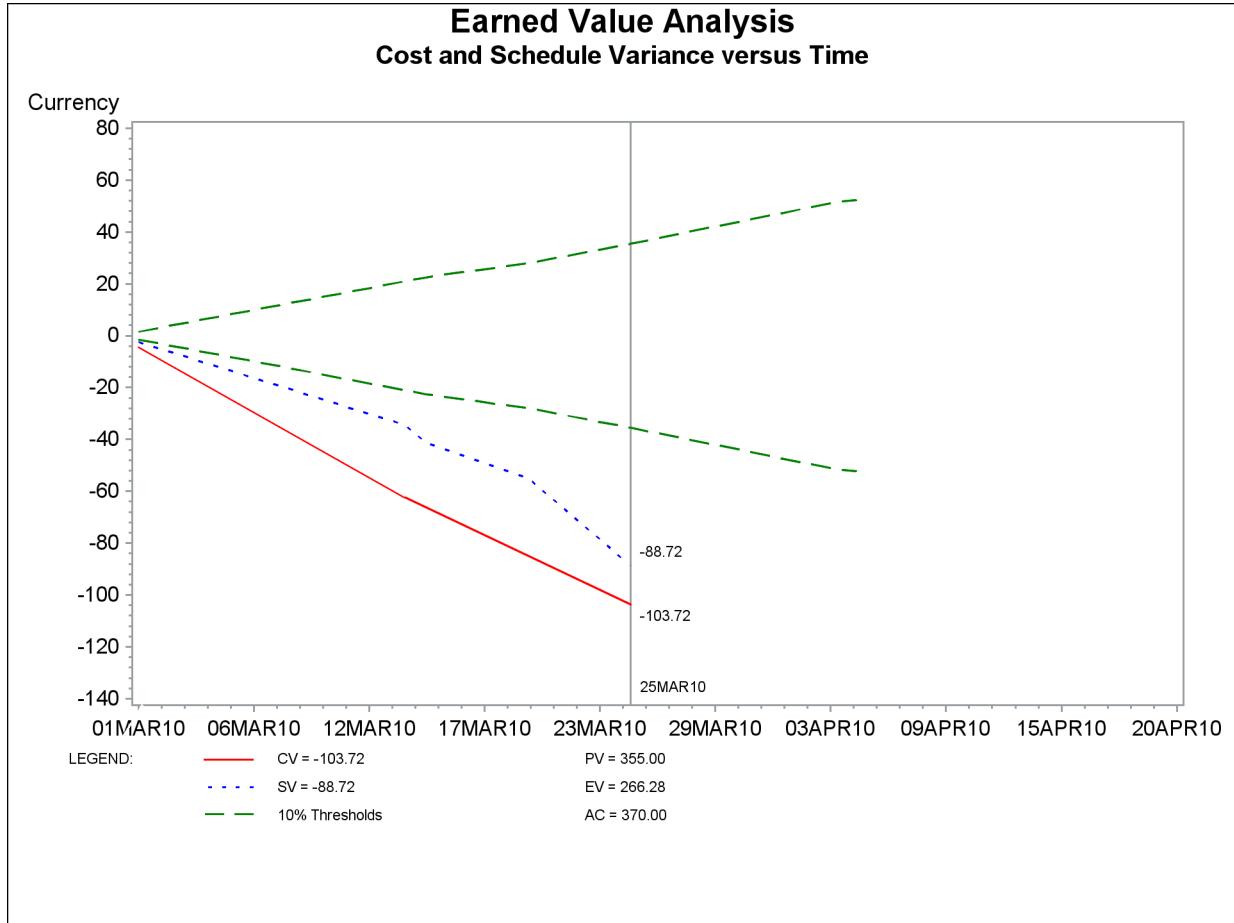

Although not apparent from the preceding chart, as any project nears completion its schedule variance tends toward zero. This is because the earned value eventually converges to the planned value.


Note that the %EVA\_METRICS macro must have been called prior to this invocation in order to generate the METRICS= data set.

The cost and schedule variance can also be displayed by activity on a Gantt chart with the %EVG\_GANTT\_CHART macro, as follows.

```
%evg_gantt_chart(
    plansched=software,
    reviseschd=software25,
    duration=duration,
    start=start,
    finish=finish,
    activity=activity,
    timenow='25MAR10'd,
    id=wbs cv sv cpi spi,
    height=3,
    scale=20
);
```

Figure 11.25 depicts cost and schedule variance, in addition to the cost and schedule performance indices, with a Gantt-style schedule. Note that two bars are used to represent each activity. The top bar is the revised schedule and the bottom bar is the baseline schedule.

**Figure 11.25** CV and SV by Task Using %EVG\_GANTT\_CHART

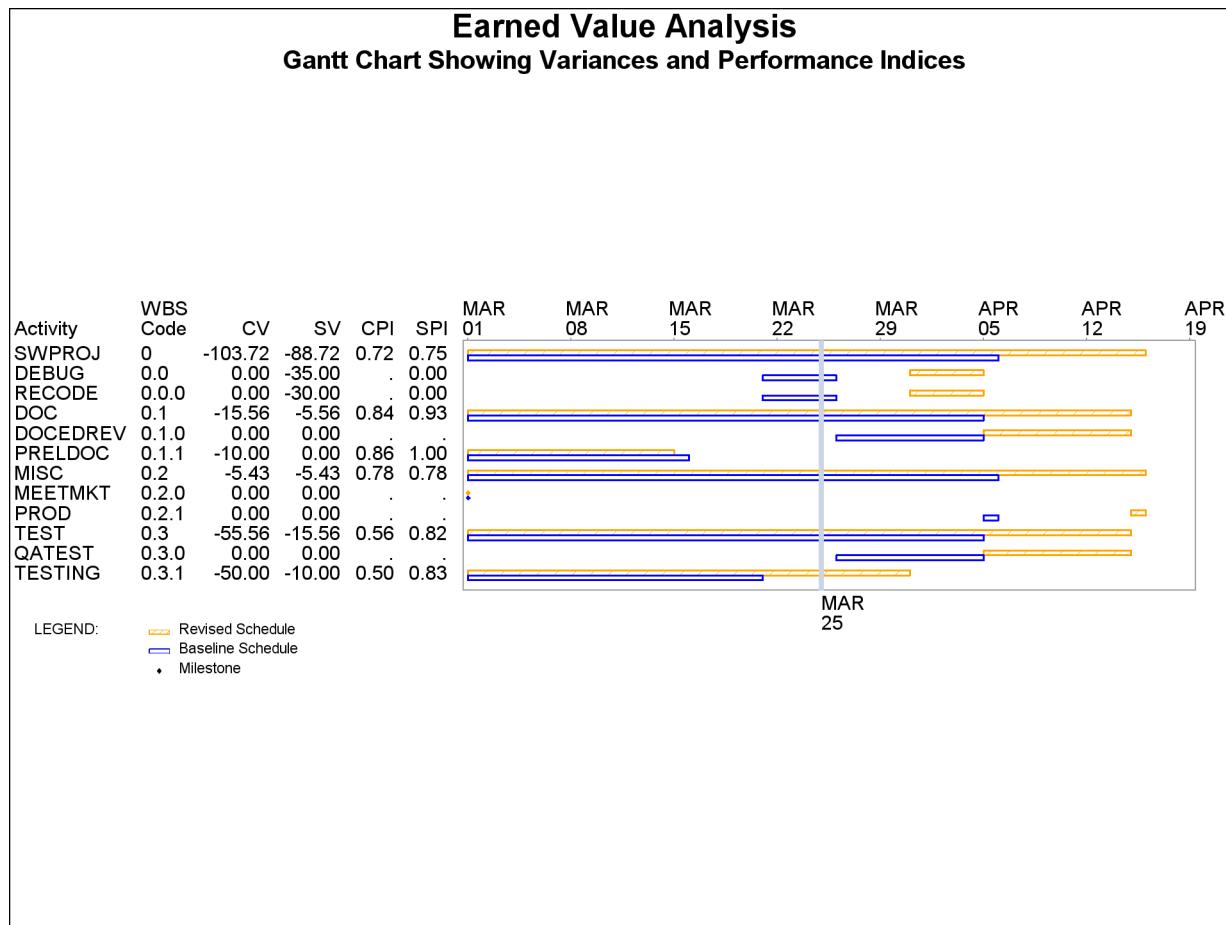


The parameters used in this call to %EVG\_GANTT\_CHART are described briefly in the following list. More details are given in the section “[Syntax: Earned Value Management Macros](#)” on page 879.

- PLANSCHED= identifies the data set containing the planned schedule.
- REVISESCHED= identifies the data set that contains the updated schedule.
- ACTIVITY= specifies the activity variable in the PLANSCHED= and REVISESCHED= data sets.
- START= specifies the start date or datetime variable in the PLANSCHED= and REVISESCHED= data sets.
- FINISH= specifies the finish date or datetime variable in the PLANSCHED= and REVISESCHED= data sets.
- DURATION= specifies a duration variable in the PLANSCHED= or REVISESCHED= data set. If the variable is present in both data sets, the REVISESCHED= data set is chosen as the source for the variable values. This variable is only used for differentiating milestones from single day tasks.
- TIMENOW= specifies the date or datetime of the updated schedule and costs.
- ID= specifies the variable(s) to be included in the Gantt chart.
- HEIGHT= specifies a height factor for all text in PROC GANTT. (See the HEIGHT= option for the CHART statement of PROC GANTT ([Chapter 8](#)) for more details.)
- SCALE= specifies the relative size adjustment of the data columns and chart. (See the SCALE= option for the CHART statement of PROC GANTT ([Chapter 8](#)) for more details.)

This macro relies on the output data set (named TASKMETS by default) that is generated by %EVA\_TASK\_METRICS. The TASKMETRICS= parameter is used by both %EVA\_TASK\_METRICS and %EVG\_GANTT\_CHART to specify a different data set name. More details are given in the section “[Syntax: Earned Value Management Macros](#)” on page 879.

The %EVG\_INDEX\_PLOT macro is used to generate a line plot of the cost and schedule performance indices, along with the to-complete performance index. The output generated by a default invocation is shown in [Figure 11.26](#). Recall that CPI is the ratio of earned value to actual cost, and SPI is the ratio of earned value to planned value. Also, TCPI<sub>BAC</sub> is the ratio of work remaining to the remaining budget.

```
%evg_index_plot;
```

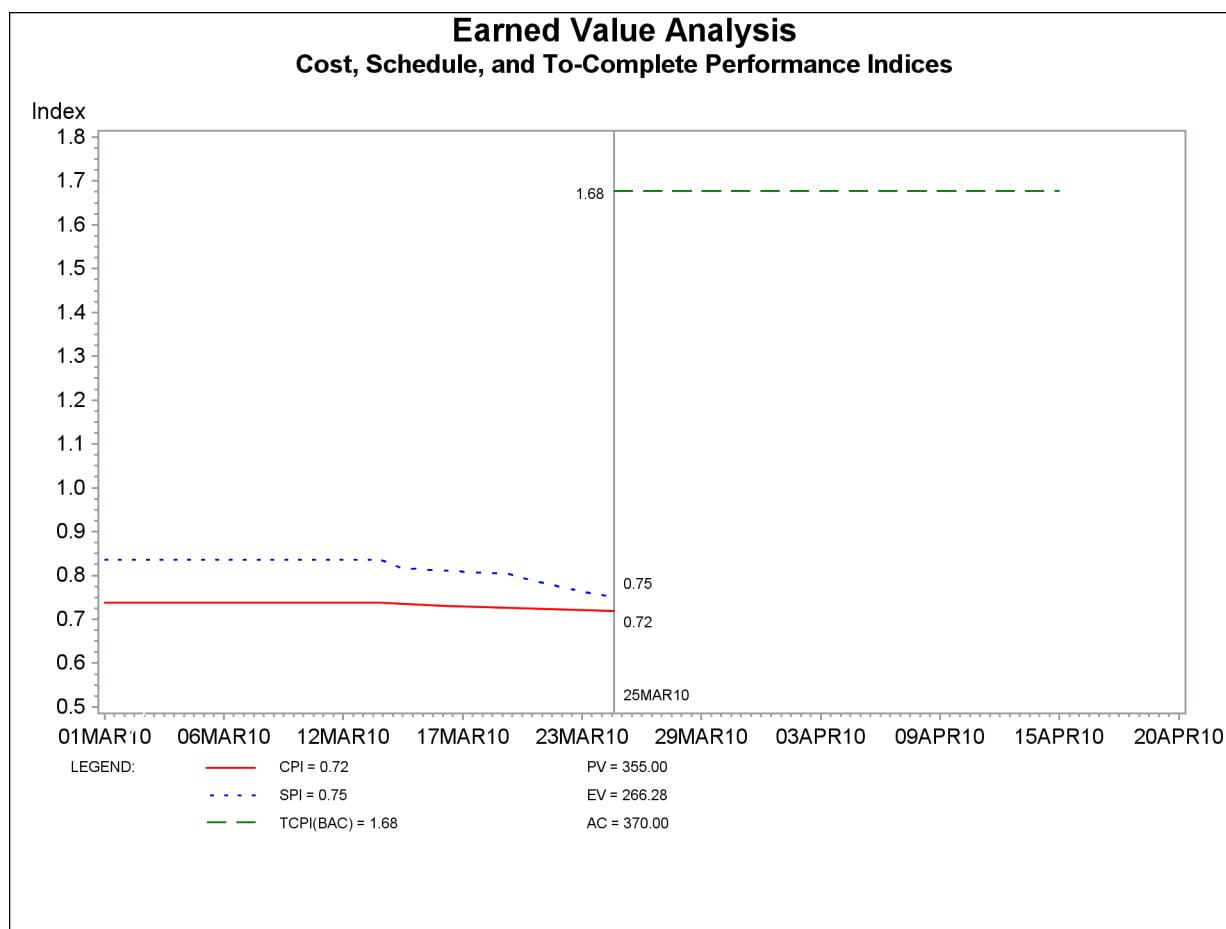
**Figure 11.26** CPI, SPI, and TCPI Using %EVG\_INDEX\_PLOT

The CPI and SPI plots show a poor cost and schedule performance. Therefore the  $\text{TCPI}_{\text{BAC}}$ , an indicator of the performance required to get back on track, is relatively high.

Note that the %EVA\_METRICS macro must have been called prior to this invocation in order to generate the METRICS= and SUMMARY= data sets.

The %EVG\_COST\_PLOT macro is used to plot the Budgeted Cost of Work Scheduled (or Planned Value), Budgeted Cost of Work Performed (or Earned Value), Actual Cost of Work Performed (or simply Actual Cost), and revised Estimate at Completion ( $\text{EAC}_{\text{rev}}$ ) against time. The output from this macro is shown in Figure 11.27.

```
%evg_cost_plot;
```

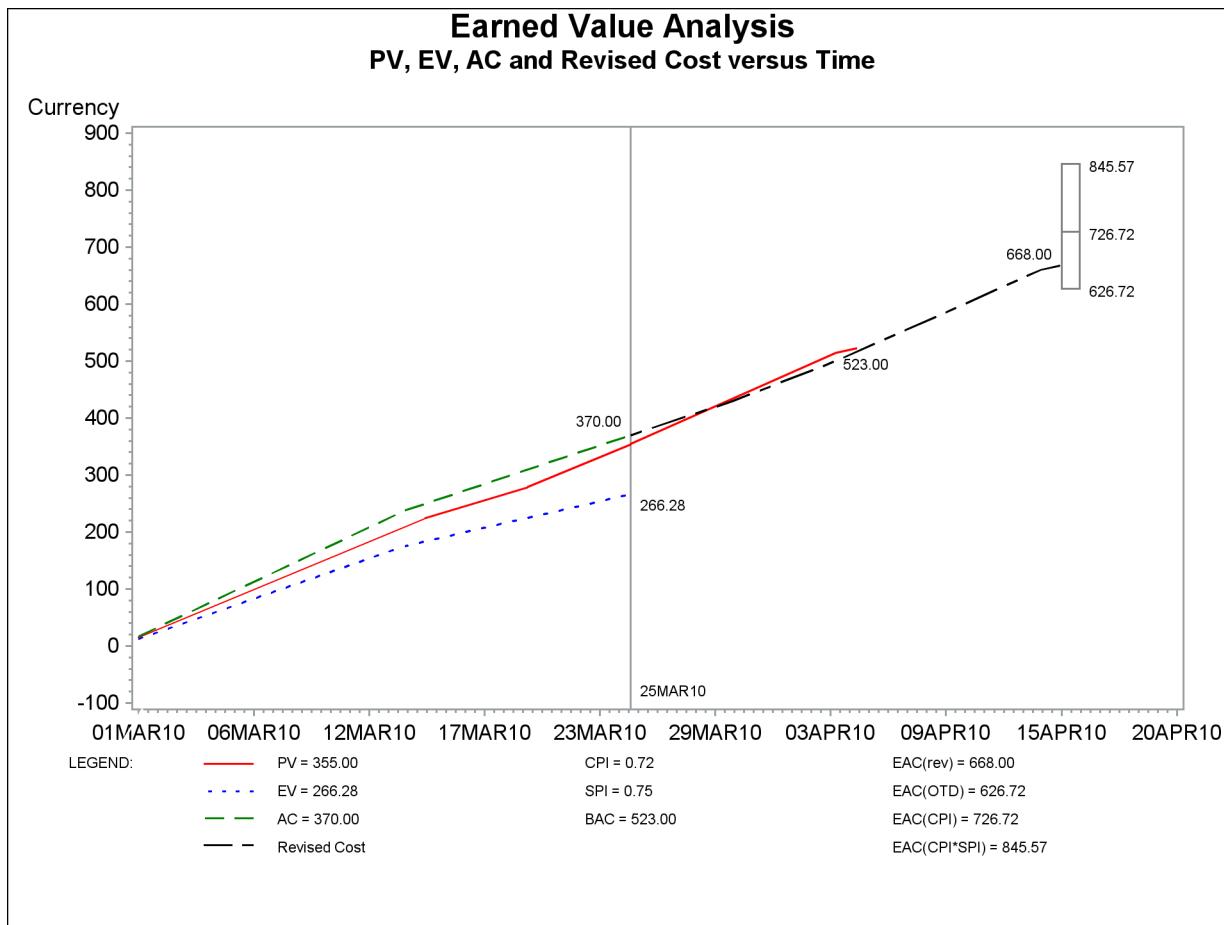
**Figure 11.27** PV, EV, AC, and EAC<sub>rev</sub> versus Time Using %EVG\_COST\_PLOT

The EAC<sub>rev</sub> value of \$668 depicted in Figure 11.27 is the sum of the actual costs so far and the revised cost of the future work. In other words, it is the sum of the “AC Rate” column in the output data set of the %EVA\_EARNED\_VALUE macro. With the optimistic EAC<sub>OTD</sub> value of \$626.72, it is assumed that the remaining work will be completed according to the original budget. A more realistic value of \$726.72 is shown for the EAC<sub>CPI</sub>. Finally, the “upper bound” estimate of \$845.57 is given by the EAC<sub>CPI\*SPI</sub>.

Note that the %EVA\_METRICS macro must have been called prior to this invocation in order to generate the METRICS= and SUMMARY= data sets.

The %EVG\_SCHEDULE\_PLOT macro can be used to show planned, revised, and projected completion dates as pictured in Figure 11.28.

```
%evg_schedule_plot;
```

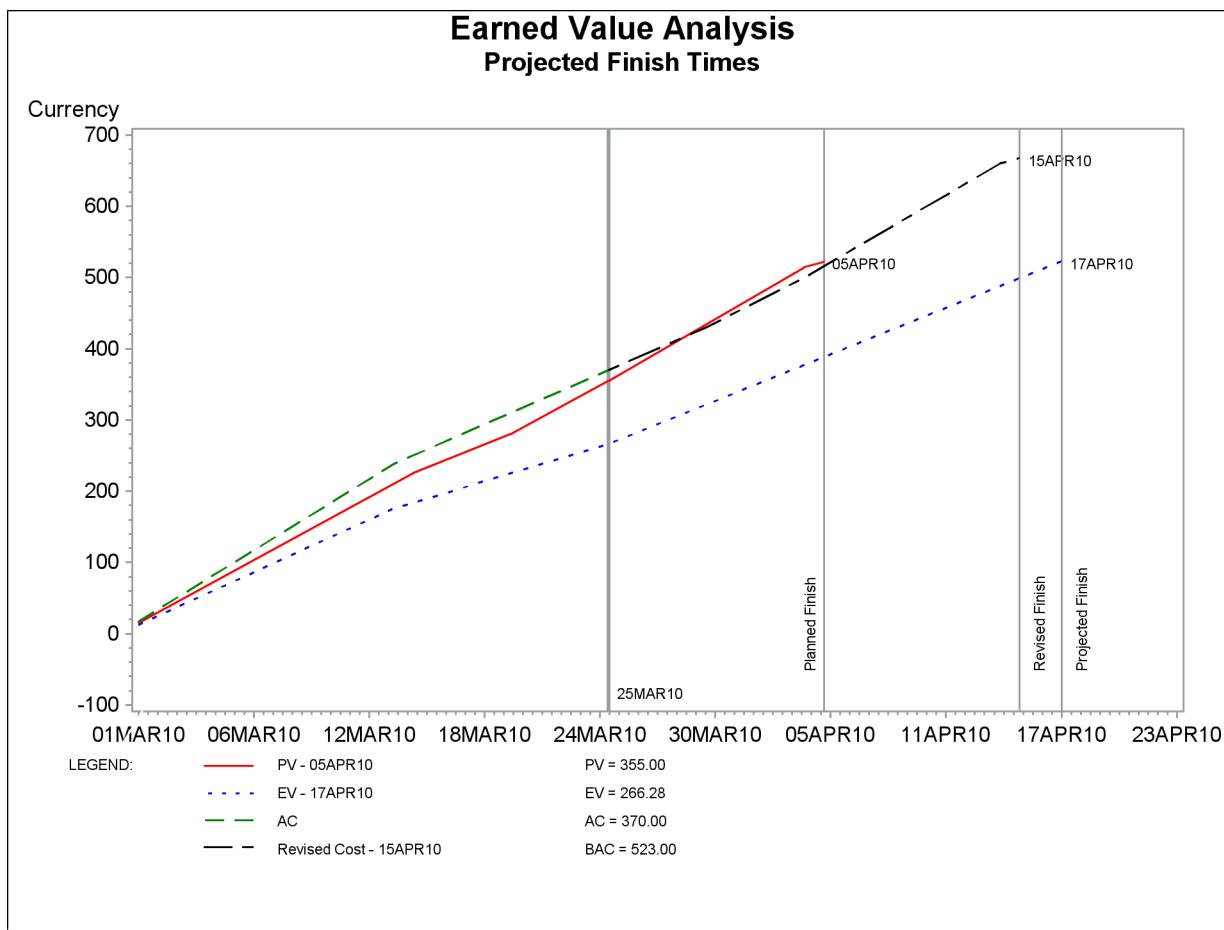**Figure 11.28** Projected Completion Dates Using %EVG\_SCHEDULE\_PLOT

In Figure 11.28, the current date (25MAR10) and planned end date (05APR10) are marked with vertical lines, as is the completion date according to the revised schedule (15APR10). The rightmost vertical line marks the projected finish time based upon the rate at which earned value has accumulated so far. This slope is used to extend the current earned value to the Budget at Completion (BAC) value of \$523, providing a prediction of the completion date.

Note that the %EVA\_METRICS macro must have been called prior to this invocation in order to generate the METRICS= data set.

Using the software schedule data set as input, the %EVG\_WBS\_CHART macro can be utilized to produce the Work Breakdown Structure seen in Figure 11.8.

---

## Syntax: Earned Value Management Macros

---

### Analysis

The following macros are available for earned value analysis.

```
%EVA_PLANNED_VALUE (parameters);
%EVA_EARNED_VALUE (parameters);
%EVA_METRICS <(parameters)>;
%EVA_TASK_METRICS (parameters);
```

This section provides syntactical information for each of these macros. The macros are described in further detail in the section “[Analysis](#)” on page 897.

The role of each macro is illustrated in [Figure 11.29](#). Each arrow entering a macro is associated with a *required* parameter specifying an input SAS data set. Each arrow leaving a macro is associated with an *optional* parameter specifying an output SAS data set. If an optional parameter does not receive an argument, then a default name is given to the output data set.

---

### %EVA\_PLANNED\_VALUE

This macro is used to produce the periodic planned value.

```
%EVA_PLANNED_VALUE (parameters);
```

#### Required Parameters

**ACTIVITY=variable**

specifies the activity variable in the PLANSCHED= and BUDGETCOST= data sets.

**BUDGETCOST=SAS-data-set**

**PLAN COST=SAS-data-set**


identifies the input data set containing the budgeted cost rates for each activity.

**PLANSCHED=SAS-data-set**

identifies the input data set containing the planned schedule.

**START=variable**

specifies the start date or datetime variable in the PLANSCHED= data set.

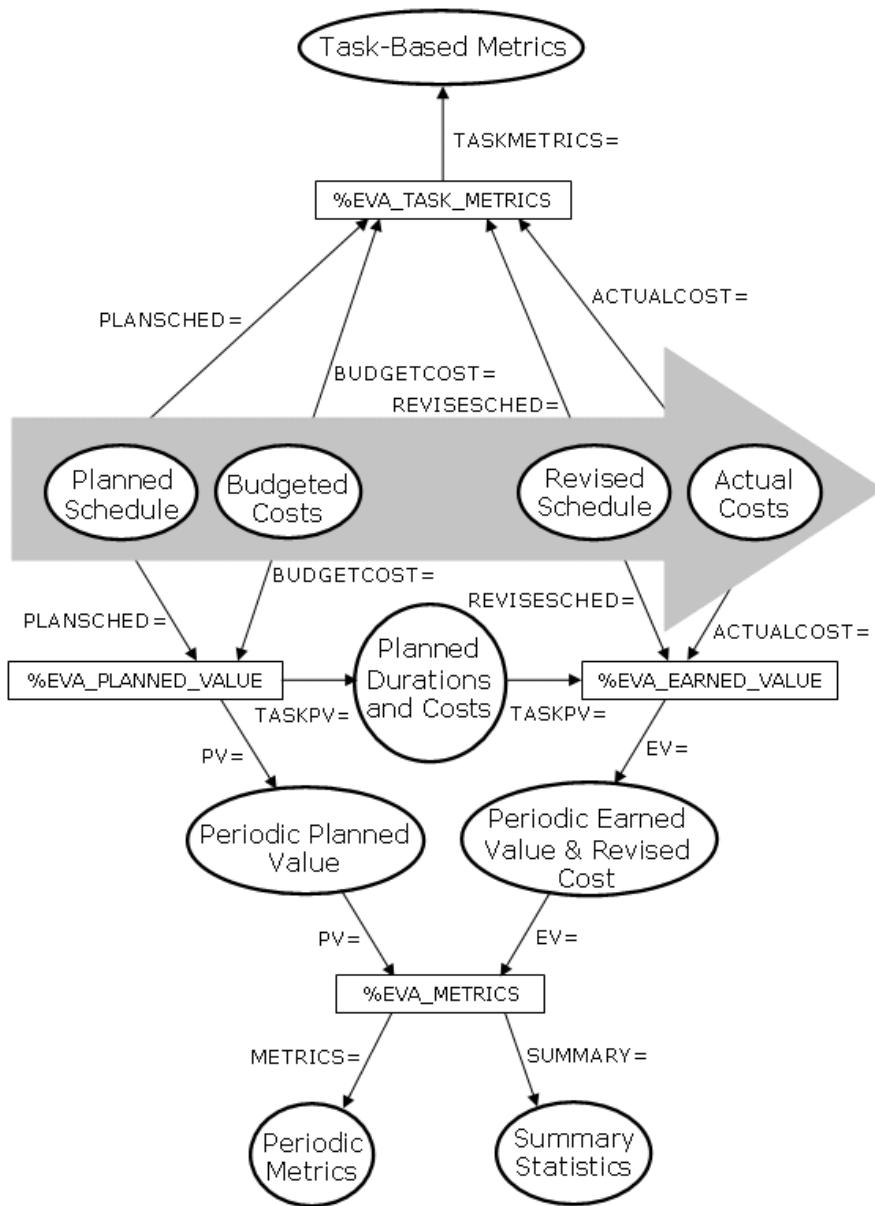**Figure 11.29** Analysis Macro Data Flow

## Optional Parameters

**CALENDAR=SAS-data-set**

identifies the calendar input data set. (See the CALENDAR= option in [Chapter 4](#) for more details.)

**COST=variable**

specifies the cost variable in the BUDGETCOST= data set. This is the total of the start and finish costs associated with the given task. At least COST= or RATE= must be specified.

**DURATION=variable**

specifies the task duration variable in the PLANSCHED= data set. At least DURATION= or FINISH= must be specified. If both parameters are specified, the FINISH= variable value overrides a nonzero DURATION= variable value; i.e., duration is only used to indicate a milestone task.

**FINISH=variable**

specifies the finish date or datetime variable in the PLANSCHED= data set. At least FINISH= or DURATION= must be specified. If both parameters are specified, the FINISH= variable value overrides a nonzero DURATION= variable value; i.e., duration is only used to indicate a milestone task.

**HOLIDATA=SAS-data-set**

identifies the input data set that contains the holiday schedule. (See the HOLIDATA= option in [Chapter 4](#) for more details.)

**HOLIDAY=statement**

specifies the HOLIDAY statement to use for PROC CPM. For example:

```
%eva_planned_value(\ldots, holiday=holiday start / holifin=finish, ...);
```

(See the HOLIDAY statement in [Chapter 4](#) for more details.)

**INTERVAL=interval**

specifies the units to use for the DURATION= variable values. (See the INTERVAL= option in [Chapter 4](#) for more details.)

**MAXOBS=max**

sets the limit on the number of allowable observations for the PV= data set. (See the MAXOBS= option of the RESOURCE statement and CPM procedure in [Chapter 4](#) for more details.)

**NROUTCAL=variable**

indicates which calendar is to be used for incrementing the \_TIME\_ variable in the BCOSTOUT= data set. (See the NROUTCAL= option of the RESOURCE statement and CPM procedure in [Chapter 4](#) for more details.)

**PV=SAS-data-set**

identifies the output data set that contains the periodic planned value. The frequency is determined by the INTERVAL= and ROUTINTERVAL= parameters. The default data set name is PV.

**RATE=variable**

specifies the cost rate variable in the BUDGETCOST= data set. This is the rate at which cost is incurred over the duration of the task. The variable that contains this duration is specified with the DURATION= parameter. At least RATE= or COST= must be specified.

**ROUTINTERVAL=interval**

specifies the period between values in the PV= data set. (See the ROUTINTERVAL= option in [Chapter 4](#) for more details.)

**SPCT=variable**

specifies the start percentage variable in the BUDGETCOST= data set. This is the percentage of the COST= amount that is incurred at the beginning of the task. The default is zero, in which case the

entire COST= amount is incurred at the completion of the task. The specified variable may also contain a comma-delimited list of weights to be used for distributing the cost at equal working intervals over the duration of the activity.

#### **TASKPV=SAS-data-set**

identifies the output data set that is used as input to the %EVA\_EARNED\_VALUE macro. This data set is used to store the planned duration and costs by activity, which are used by the %EVA\_EARNED\_VALUE macro to compute earned value (see Figure 11.29). The default data set name is TASKPV.

#### **WORKDAY=SAS-data-set**

identifies the workday input data set. (See the WORKDAY= option in Chapter 4 for more details.)

Note that if a WORKDAY=, CALENDAR=, or HOLIDAY= data set is specified, the default variable name, \_CAL\_, is assumed for calendar identification.

Table 11.1 summarizes the parameters used for managing input and output data sets in the %EVA\_PLANNED\_VALUE macro.

**Table 11.1** %EVA\_PLANNED\_VALUE I/O Parameter Summary

Type	Data Set	Variables
INPUT	BUDGETCOST	COST, RATE, SPCT
INPUT	CALENDAR	
INPUT	HOLIDATA	
INPUT	PLANSCHED	ACTIVITY, DURATION, FINISH, START
INPUT	WORKDAY	
OUTPUT	PV	
OUTPUT	TASKPV	

## **%EVA\_EARNED\_VALUE**

This macro is used to produce the periodic earned value and actual cost.

**%EVA\_EARNED\_VALUE (parameters);**

**NOTE:** %EVA\_EARNED\_VALUE requires output from %EVA\_PLANNED\_VALUE.

### **Required Parameters**

#### **ACTIVITY=variable**

specifies the activity variable in the REVISESCHED=, ACTUALCOST=, and BUDGETCOST= data sets.

#### **ACTUALCOST=SAS-data-set**

#### **REVISECOST=SAS-data-set**

identifies the updated costs input data set.

**REVISESCHED=SAS-data-set**

identifies the input data set containing the updated schedule.

**START=variable**

specifies the start date or datetime variable in the REVISESCHED= data set.

**Optional Parameters****CALENDAR=SAS-data-set**

identifies the calendar input data set. (See the CALENDAR= option in [Chapter 4](#) for more details.)

**COST=variable**

specifies the cost variable in the ACTUALCOST= data set. This is the total of the start and finish costs associated with the given task. At least COST= or RATE= must be specified. This parameter is only allowed if used for %EVA\_PLANNED\_VALUE; further, the variable specified must be the same as that specified for %EVA\_PLANNED\_VALUE. If a variable is specified for this parameter, but the value for the variable is missing for a given observation, the corresponding value from the BUDGETCOST= data set is used.

**DURATION=variable**

specifies the task duration variable in the REVISESCHED= data set. At least DURATION= or FINISH= must be specified. If both parameters are specified, the FINISH= variable value overrides a nonzero DURATION= variable value; i.e., duration is only used to indicate a milestone task.

**EV=SAS-data-set**

identifies the output data set, which contains the periodic earned value and revised cost. The frequency is determined by the INTERVAL= and ROUTINTERVAL= parameters. The default data set name is EV.

**FINISH=variable**

specifies the finish date or datetime variable in the REVISESCHED= data set. At least FINISH= or DURATION= must be specified. If both parameters are specified, the FINISH= variable value overrides a nonzero DURATION= variable value; i.e., duration is only used to indicate a milestone task.

**HOLIDAData=SAS-data-set**

identifies the input data set that contains the holiday schedule. (See the HOLIDAData= option in [Chapter 4](#) for more details.)

**HOLIDAY=statement**

specifies the HOLIDAY statement to use for PROC CPM. For example:

```
%eva_earned_value(..., holiday=holiday start / holifin=finish, ...);
```

(See the HOLIDAY statement in [Chapter 4](#) for more details.)

**INTERVAL=interval**

specifies the units to use for the DURATION= variable values. (See the INTERVAL= option in [Chapter 4](#) for more details.)

**MAXOBS=max**

sets the limit on the number of allowable observations for the EV= data set. (See the MAXOBS= option of the RESOURCE statement and CPM procedure in [Chapter 4](#) for more details.)

**NROUTCAL=variable**

indicates which calendar is to be used for incrementing the \_TIME\_ variable in the ACOSTOUT= data set. (See the NROUTCAL= option of the RESOURCE statement and CPM procedure in [Chapter 4](#) for more details.)

**RATE=variable**

specifies the cost rate variable in the ACTUALCOST= data set. This is the rate at which cost is incurred over the duration of the task. The variable that contains this duration is specified with the DURATION= parameter. At least RATE= or COST= must be specified. This parameter is only allowed if used with %EVA\_PLANNED\_VALUE; further, the variable specified must be the same as that specified for %EVA\_PLANNED\_VALUE. If a variable is specified for this parameter, but the value for the variable is missing for a given observation, the corresponding value from the BUDGETCOST= data set is used.

**ROUTINTERVAL=interval**

specifies the period between values in the EV= data set. (See the ROUTINTERVAL= option in [Chapter 4](#) for more details.)

**SPCT=variable**

specifies the start percentage variable in the ACTUALCOST= data set. This is the percentage of the COST= amount that is incurred at the beginning of the task. The default is zero, in which case the entire COST= amount is incurred at the completion of the task. The specified variable may also contain a comma-delimited list of weights to be used for distributing the cost at equal working intervals over the duration of the activity. This parameter is only allowed if used for %EVA\_PLANNED\_VALUE; further, the variable specified must be the same as that specified for %EVA\_PLANNED\_VALUE. If a variable is specified for this parameter, but the value for the variable is missing for a given observation, the corresponding value from the BUDGETCOST= data set will be used.

**TASKPV=SAS-data-set**

identifies the input data set containing the planned duration and costs by activity, which are used to compute earned value. This data set is generated by the %EVA\_PLANNED\_VALUE macro, with name specified by the TASKPV= parameter of the %EVA\_PLANNED\_VALUE macro (see [Figure 11.29](#)). The default data set name is TASKPV.

**WORKDAY=SAS-data-set**

identifies the workday input data set. (See the WORKDAY= option in [Chapter 4](#) for more details.)

Note that if a WORKDAY=, CALENDAR=, or HOLIDAY= data set is specified, the default variable name, \_CAL\_, is assumed for calendar identification.

Also note that the variable names specified for the ACTIVITY=, START=, FINISH=, and RATE= parameters must be the same, respectively, as those previously specified for the %EVA\_PLANNED\_VALUE macro. This is to enable the subsequent use of the %EVA\_TASK\_METRICS and %EVG\_GANTT\_CHART macros.

[Table 11.2](#) summarizes the parameters used for managing input and output data sets in the %EVA\_EARNED\_VALUE macro.

**Table 11.2** %EVA\_EARNED\_VALUE I/O Parameter Summary

Type	Data Set	Variables
INPUT	ACTUALCOST	COST, RATE, SPCT
INPUT	CALENDAR	
INPUT	HOLIDATA	
INPUT	REVISESCHED	ACTIVITY, DURATION, FINISH, START
INPUT	TASKPV	COST, RATE, SPCT
INPUT	WORKDAY	
OUTPUT	EV	

## %EVA\_METRICS

This macro is used to generate summary statistics for the status date(s) requested, along with periodic metrics.

**%EVA\_METRICS < ( parameters ) > ;**

**NOTE:** %EVA\_METRICS requires output from both %EVA\_PLANNED\_VALUE and %EVA\_EARNED\_VALUE.

### Optional Parameters

**ACRONYMS=***long*

specifies whether the long form of the earned value acronyms is to be used—e.g., BCWP versus EV. The short form is used unless the macro variable \_ACRONYMS\_ is set to “long” or ACRONYMS=long is specified. The parameter overrides the macro variable setting; i.e., specifying any non-null value other than “long” for the ACRONYMS= parameter produces short forms.

**EACFORM=***integer*

indicates the form of the EAC to be used in computing ETC, VAC, VAC percentage, and TCPI<sub>EAC</sub>. The values are assigned as follows:

- 1 - EAC<sub>rev</sub>
- 2 - EAC<sub>OTD</sub>
- 3 - EAC<sub>CPI</sub>
- 4 - EAC<sub>CPI×SPI</sub>

The default value is 3 for EAC<sub>CPI</sub>.

**EV=SAS-data-set**

identifies the input data set containing the periodic earned value and actual cost. It is generated by the %EVA\_EARNED\_VALUE macro, with name specified by the EV= parameter of the %EVA\_EARNED\_VALUE macro. The default data set name is EV.

**METRICS=SAS-data-set**

identifies the periodic output data set containing earned value metrics. The default name of the periodic output data set is METRICS.

**PV=SAS-data-set**

identifies the input data set containing the periodic planned value. It is generated by the %EVA\_PLANNED\_VALUE macro, with name specified by the PV= parameter of the %EVA\_PLANNED\_VALUE macro. The default data set name is PV.

**SUMMARY=SAS-data-set**

identifies the output data set, which contains a summary of metrics derived with respect to the last time given by the TIMENOW= parameter. The default name of the summary output data set is SUMMARY.

**TIMENOW=time(s)**

specifies one or more reference dates ('ddmmmyy'd) or datetimes ('ddmmmyy:hh:mm:ss'dt) delimited by white space, for the summary output. For example:

```
%eva_metrics(timenow='01SEP11'd '15SEP11:12:00:00'dt);
```

The list of dates or datetimes must be in chronological order. The default value is today's date, unless the macro variable \_TIMENOW\_ has been set, in which case the default is the latter.

**Table 11.3** summarizes the parameters used for managing input and output data sets in the %EVA\_METRICS macro.

**Table 11.3** %EVA\_METRICS I/O Parameter Summary

Type	Data Set
INPUT	EV
INPUT	PV
OUTPUT	METRICS
OUTPUT	SUMMARY

## %EVA\_TASK\_METRICS

This macro is used to produce earned value measures for each task; these measures include Planned Value, Earned Value, Actual Cost, Cost and Schedule Variance, and Cost and Schedule Performance Index.

```
%EVA_TASK_METRICS (parameters) ;
```

### Required Parameters

**ACTIVITY=variable**

specifies the activity variable in the PLANSCHED= and REVISESCHED= data sets.

**ACTUALCOST=SAS-data-set****REVISECOST=SAS-data-set**

identifies the updated costs data set.

**BUDGETCOST=SAS-data-set**

**PLANCOST=SAS-data-set**

identifies the budgeted costs data set.

**PLANSCHED=SAS-data-set**

identifies the input data set that contains the planned schedule.

**REVISESCHED=SAS-data-set**

identifies the input data set that contains the updated schedule.

**START=variable**

specifies the start date or datetime variable in the PLANSCHED= and REVISESCHED= data sets.

## Optional Parameters

**ACRONYMS=long**

specifies whether the long form of the earned value acronyms is to be used—e.g., BCWP versus EV. The short form is used unless the macro variable \_ACRONYMS\_ is set to “long” or ACRONYMS=long is specified. The parameter overrides the macro variable setting; i.e., specifying any non-null value other than “long” for the ACRONYMS= parameter produces short forms.

**AGGREGATE=Y or otherwise**

specifies whether or not to roll up values along the project hierarchy; a value of Y indicates that aggregation is to be carried out. No rollup is performed for the default behavior. The WBSCODE= parameter is required if AGGREGATE=Y is specified.

**CALENDAR=SAS-data-set**

identifies the calendar data set. (See the CALENDAR= option in [Chapter 4](#) for more details.)

**COST=variable**

specifies the cost variable in the BUDGETCOST= and ACTUALCOST= data sets. This is the total of the start and finish costs associated with the given task. At least COST= or RATE= must be specified. If a variable is specified for this parameter, but the value for the variable is missing for a given observation, the corresponding value from the BUDGETCOST= data set is used.

**DURATION=variable**

specifies the task duration variable in the PLANSCHED= and REVISESCHED= data sets. At least DURATION= or FINISH= must be specified. If both parameters are specified, the FINISH= variable value overrides a nonzero DURATION= variable value; i.e., duration is only used to indicate a milestone task.

**FINISH=variable**

specifies the finish date or datetime variable in the PLANSCHED= and REVISESCHED= data sets. At least FINISH= or DURATION= must be specified. If both parameters are specified, the FINISH= variable value overrides a nonzero DURATION= variable value; i.e., duration is only used to indicate a milestone task.

**HOLIDATA=SAS-data-set**

identifies the holiday data set. (See the HOLIDATA= option in [Chapter 4](#) for more details.)

**HOLIDAY=***statement*

specifies the HOLIDAY statement to use for PROC CPM. For example:

```
%eva_task_metrics(\ldots, holiday=holiday_start / holifin=finish, ...);
```

(See the HOLIDAY statement in [Chapter 4](#) for more details.)

**INTERVAL=***interval*

specifies the units to use for the DURATION= variable values. (See the INTERVAL= option in [Chapter 4](#) for more details.)

**PCTCOMP=***variable*

specifies the percentage complete variable of the REVISESCHED= data set. Note that for a given activity, the specified percentage complete can appear to be in conflict with the amount of time spent, relative to the projected finish time for that activity. For example, even though 5 of 10 working days have elapsed, maybe only 30% of the activity has been completed. The input data reflects an anticipated acceleration in progress over the next five days. Also, if there is no value for the PCTCOMP= variable for a given activity, a computed value is substituted.

**RATE=***variable*

specifies the cost rate variable in the BUDGETCOST= and ACTUALCOST= data sets. This is the rate at which cost is incurred over the DURATION= variable value for the given task. At least RATE= or COST= must be specified. If a variable is specified for this parameter, but the value for the variable is missing for a given observation, the corresponding value from the BUDGETCOST= data set is used.

**SPCT=***variable*

specifies the start percentage variable in the BUDGETCOST= and ACTUALCOST= data sets. This is the percentage of the COST= amount that is incurred at the beginning of the task. The default is zero, in which case the entire COST= amount is incurred at the completion of the task. The specified variable may also contain a comma-delimited list of weights to be used for distributing the cost at equal working intervals over the duration of the activity. If a variable is specified for this parameter, but the value for the variable is missing for a given observation, the corresponding value from the BUDGETCOST= data set is used.

**TASKMETRICS=SAS-data-set**

identifies the output data set. The default data set name is TASKMETS.

**TIMENOW=***time*

specifies the date ('ddmmmyy'd) or datetime ('ddmmmyy:hh:mm:ss'dt) of the updated schedule and costs. The default value is today's date unless the macro variable \_TIMENOW\_ has been set, in which case the default is the latter.

**WBSCODE=***variable*

specifies the variable that contains the Work Breakdown Structure code in the PLANSCHED= or REVISESCHED= data set. The default variable name is WBS\_CODE.

**WORKDAY=SAS-data-set**

identifies the workday input data set. (See the WORKDAY= option in [Chapter 4](#) for more details.)

Note that if a WORKDAY=, CALENDAR=, or HOLIDAY= data set is specified, the default variable name, \_CAL\_, is assumed for calendar identification.

Table 11.4 summarizes the parameters used for managing input and output data sets in the %EVA\_TASK\_METRICS macro.

**Table 11.4** %EVA\_TASK\_METRICS I/O Parameter Summary

Type	Data Set	Variables
INPUT	ACTUALCOST	COST, RATE, SPCT
INPUT	BUDGETCOST	COST, RATE, SPCT
INPUT	CALENDAR	
INPUT	HOLIDATA	
INPUT	PLANSCHED	ACTIVITY, DURATION, FINISH, START, WBSCODE
INPUT	REVISESCHED	ACTIVITY, DURATION, FINISH, PCT-COMP, START, WBSCODE
INPUT	WORKDAY	
OUTPUT	TASKMETRICS	

## Charts

The following macros are available for earned value charts and reports.

```
%EVG_COST_PLOT <(parameters)> ;
%EVG_SCHEDULE_PLOT <(parameters)> ;
%EVG_INDEX_PLOT <(parameters)> ;
%EVG_VARIANCE_PLOT <(parameters)> ;
%EVG_GANTT_CHART (parameters) ;
%EVG_WBS_CHART (parameters) ;
```

## %EVG\_COST\_PLOT

This macro is used to produce a plot of earned value measures over time. The plots include Planned Value, Earned Value, Actual Cost, and revised cost.

```
%EVG_COST_PLOT <(parameters)> ;
```

**NOTE:** %EVG\_COST\_PLOT requires output from %EVA\_METRICS.

## Optional Parameters

**ACRONYMS=***long*

specifies whether the long form of the earned value acronyms is to be used—e.g., BCWP versus EV. The short form is used unless the macro variable \_ACRONYMS\_ is set to “long” or ACRONYMS=long is specified. The parameter overrides the macro variable setting; i.e., specifying any non-null value other than “long” for the ACRONYMS= parameter produces short forms.

**METRICS=SAS-data-set**

identifies the periodic metrics data set produced by the %EVA\_METRICS macro, the name of which is determined by the METRICS= parameter of %EVA\_METRICS. The default data set name is METRICS.

**PLOT=SAS-data-set**

specifies the name of the output data set. This is an internal data set that is used as input to the plotting procedure. The default data set name is PLOT.

**SUMMARY=SAS-data-set**

identifies the summary data set from the %EVA\_METRICS macro, the name of which is determined by the SUMMARY= parameter of %EVA\_METRICS. The default data set name is SUMMARY.

**Table 11.5** summarizes the parameters used for managing input and output data sets in the %EVG\_COST\_PLOT macro.

**Table 11.5** %EVG\_COST\_PLOT I/O Parameter Summary

Type	Data Set
INPUT	METRICS
INPUT	SUMMARY
OUTPUT	PLOT

## %EVG\_SCHEDULE\_PLOT

This macro is used to display planned and projected completion times for the project. Specifically, the status date is shown, along with the planned finish time, the revised finish time, and the projected finish time.

**%EVG\_SCHEDULE\_PLOT < (parameters) >** ;

**NOTE:** %EVG\_SCHEDULE\_PLOT requires output from %EVA\_METRICS.

### Optional Parameters

**ACRONYMS=long**

specifies whether the long form of the earned value acronyms is to be used—e.g., BCWP versus EV. The short form is used unless the macro variable \_ACRONYMS\_ is set to “long” or ACRONYMS=long is specified. The parameter overrides the macro variable setting; i.e., specifying any non-null value other than “long” for the ACRONYMS= parameter produces short forms.

**METRICS=SAS-data-set**

identifies the periodic metrics data set produced by the %EVA\_METRICS macro, the name of which is determined by the METRICS= parameter of %EVA\_METRICS. The default data set name is METRICS.

**PLOT=SAS-data-set**

specifies the name of the output data set. This is an internal data set that is used as input to the plotting procedure. The default data set name is PLOT.

**Table 11.6** summarizes the parameters used for managing input and output data sets in the %EVG\_SCHEDULE\_PLOT macro.

**Table 11.6** %EVG\_SCHEDULE\_PLOT I/O Parameter Summary

Type	Data Set
INPUT	METRICS
OUTPUT	PLOT

## %EVG\_INDEX\_PLOT

This macro is used to obtain a plot of the cost and schedule performance indices over time. If the project has not been completed, the To-Complete Performance Index (Budget at Completion version) is also displayed. The legend includes the Planned Value, Earned Value, and Actual Cost.

**%EVG\_INDEX\_PLOT < (parameters) > ;**

**NOTE:** %EVG\_INDEX\_PLOT requires output from %EVA\_METRICS.

### Optional Parameters

#### **ACRONYMS=***long*

specifies whether the long form of the earned value acronyms is to be used—e.g., BCWP versus EV. The short form is used unless the macro variable \_ACRONYMS\_ is set to “long” or ACRONYMS=long is specified. The parameter overrides the macro variable setting; i.e., specifying any non-null value other than “long” for the ACRONYMS= parameter produces short forms.

#### **METRICS=SAS-data-set**

identifies the periodic metrics data set produced by the %EVA\_METRICS macro, the name of which is determined by the METRICS= parameter of %EVA\_METRICS. The default data set name is METRICS.

#### **PLOT=SAS-data-set**

specifies the name of the output data set. This is an internal data set that is used as input to the plotting procedure. The default data set name is PLOT.

#### **SUMMARY=SAS-data-set**

identifies the summary data set from the %EVA\_METRICS macro, the name of which is determined by the SUMMARY= parameter of %EVA\_METRICS. The default data set name is SUMMARY.

Table 11.7 summarizes the parameters used for managing input and output data sets in the %EVG\_INDEX\_PLOT macro.

**Table 11.7** %EVG\_INDEX\_PLOT I/O Parameter Summary

Type	Data Set
INPUT	METRICS
INPUT	SUMMARY
OUTPUT	PLOT

## %EVG\_VARIANCE\_PLOT

This macro is used to generate a plot of the cost and schedule variance against time; it features threshold plots obtained from the Planned Value, plus or minus 10%. The vital statistics of Planned Value, Earned Value, and Actual Cost are listed in the legend.

**%EVG\_VARIANCE\_PLOT <(parameters)> ;**

**NOTE:** %EVG\_VARIANCE\_PLOT requires output from %EVA\_METRICS.

### Optional Parameters

#### **ACRONYMS=***long*

specifies whether the long form of the earned value acronyms is to be used—e.g., BCWP versus EV. The short form is used unless the macro variable \_ACRONYMS\_ is set to “long” or ACRONYMS=long is specified. The parameter overrides the macro variable setting; i.e., specifying any non-null value other than “long” for the ACRONYMS= parameter produces short forms.

#### **METRICS=SAS-data-set**

identifies the periodic metrics data set produced by the %EVA\_METRICS macro, the name of which is determined by the METRICS= parameter of %EVA\_METRICS. The default data set name is METRICS.

#### **PLOT=SAS-data-set**

specifies the name of the output data set. This is an internal data set that is used as input to the plotting procedure.

The default data set name is PLOT.

Table 11.8 summarizes the parameters used for managing input and output data sets in the %EVG\_VARIANCE\_PLOT macro.

**Table 11.8** %EVG\_VARIANCE\_PLOT I/O Parameter Summary

Type	Data Set
INPUT	METRICS
OUTPUT	PLOT

---

## %EVG\_GANTT\_CHART

This macro is used to produce a Gantt chart of the planned and revised schedule, along with selected earned value metrics for each task.

**%EVG\_GANTT\_CHART** (*parameters*) ;

**NOTE:** %EVG\_GANTT\_CHART requires output from %EVA\_METRICS.

## Required Parameters

**ACTIVITY=variable**

specifies the activity variable in the PLANSCHED= and REVISESCHED= data sets.

**FINISH=variable**

specifies the finish date or datetime variable in the PLANSCHED= and REVISESCHED= data sets.

**PLANSCHED=SAS-data-set**

identifies the data set containing the planned schedule.

**REVISESCHED=SAS-data-set**

identifies the data set that contains the updated schedule.

**START=variable**

specifies the start date or datetime variable in the PLANSCHED= and REVISESCHED= data sets.

## Optional Parameters

**CHART=SAS-data-set**

specifies the name of the output data set. This is an internal data set that is used as input to the GANTT procedure. The default data set name is CHART.

**DURATION=variable**

specifies a duration variable in the PLANSCHED= or REVISESCHED= data set. The specified variable in the REVISESCHED= data set is used if the variable is present in both data sets. This variable is used only for differentiating milestones from single-day tasks.

**HEIGHT=h**

specifies a height factor for all text in PROC GANTT. (See the HEIGHT= option for the CHART statement of PROC GANTT ([Chapter 8](#)) for more details.)

**HPAGES=h**

specifies that the Gantt chart is to be produced using *h* horizontal pages. (See the HPAGES= option for the CHART statement of PROC GANTT ([Chapter 8](#)) for more details.)

**VPAGES=v**

specifies that the Gantt chart is to be produced using *v* vertical pages. (See the VPAGES= option for the CHART statement of PROC GANTT ([Chapter 8](#)) for more details.)

**ID=variable(s)**

specifies a space-delimited list of the variables from the TASKS= data set to be included in the chart. The choices are: WBS, PV, EV, AC, CV, CVP, SV, SVP, CPI, and SPI. The default value is “CV SV”.

**SCALE=scale**

specifies the relative size adjustment of the data columns and chart. (See the SCALE= option for the CHART statement of PROC GANTT ([Chapter 8](#)) for more details.)

**TASKMETRICS=SAS-data-set**

specifies the name of the output data set from the %EVA\_TASK\_METRICS macro. The default data set name is TASKMETS.

**TIMENOW=***time*

specifies the date ('ddmmmyy'd) or datetime ('ddmmmyy:hh:mm:ss'dt) of the updated schedule and costs. The default value is today's date, unless the macro variable \_TIMENOW\_ has been set, in which case the default is the latter. A vertical line and label indicate the value.

Table 11.9 summarizes the parameters used for managing input and output data sets in the %EVG\_GANTT\_CHART macro.

**Table 11.9** %EVG\_GANTT\_CHART I/O Parameter Summary

Type	Data Set	Variables
INPUT	PLANSCHED	ACTIVITY, DURATION, FINISH, START
INPUT	REVISESCHED	ACTIVITY, DURATION, FINISH, START
INPUT	TASKMETRICS	
OUTPUT	CHART	

## %EVG\_WBS\_CHART

This macro is used to generate a Work Breakdown Structure chart. The parameters can be used to control the data that appears within the boxes of the display.

**%EVG\_WBS\_CHART** (*parameters*) ;

### Required Parameters

**ACTIVITY=***variable*

specifies the activity variable in the STRUCTURE= data set.

**PROJECT=***variable*

specifies the STRUCTURE= data set variable that identifies the project to which the current task belongs.

**STRUCTURE=SAS-data-set**

identifies the data set that defines the Work Breakdown Structure.

### Optional Parameters

**DEFID=Y or otherwise**

specifies whether or not to include the default identification variables that are present in the STRUCTURE= data set in the boxes of the display. Default variable names are: E\_START, E\_FINISH, L\_START, L\_FINISH, S\_START, S\_FINISH, A\_START, A\_FINISH, T\_FLOAT, and F\_FLOAT. The default value for the DEFID= parameter is Y, meaning the default variables are displayed. (See the NODEFID option of the ACTNET statement of the NETDRAW procedure (Chapter 9) for more details.)

**ID=***variable list*

specifies the STRUCTURE= data set variables that appear in the boxes of the display.

**REVERSEY=Y or otherwise**

specifies whether or not to reverse the order in which the output pages appear. The default value is Y, which orders the pages from top to bottom. (See the REVERSEY option of the ACTNET statement of the NETDRAW procedure ([Chapter 9](#)) for more details.)

**ROTATE=Y or otherwise**

specifies whether or not to rotate the display by 90 degrees. The default value is Y, which performs the rotation. (See the ROTATE option of the ACTNET statement of the NETDRAW procedure ([Chapter 9](#)) for more details.)

**ROTATETEXT=Y or otherwise**

specifies whether or not to rotate the text that appears within the boxes of the display by 90 degrees. The default value is Y, which rotates the text. (See the ROTATETEXT option of the ACTNET statement of the NETDRAW procedure ([Chapter 9](#)) for more details.)

**VPAGES=integer**

specifies the number of vertical pages to produce. The default value is 1. (See the VPAGES= parameter of the ACTNET statement of the NETDRAW procedure ([Chapter 9](#)) for more details.)

[Table 11.10](#) summarizes the parameters used for managing input and output data sets in the %EVG\_WBS\_CHART macro.

**Table 11.10** %EVG\_WBS\_CHART I/O Parameter Summary

Type	Data Set	Variables
INPUT	STRUCTURE	ACTIVITY, ID, PROJECT

## Details: Earned Value Management Macros

### Variances

[Table 11.11](#) shows the formulas for the Cost Variance, Schedule Variance, and Variance at Completion, along with the associated percentages.

**Table 11.11** Variance Formulas

Acronym	Formula
CV	EV - AC
CV%	$\frac{CV}{EV}$
SV	EV - PV
SV%	$\frac{SV}{PV}$
VAC	BAC - EAC
VAC%	$\frac{VAC}{BAC}$

---

## Performance Indices

Table 11.12 shows the formulas for Cost, Schedule, and To-Complete Performance Indices. WR is Work Remaining and is given by:  $WR = BAC - EV$ . The section “Cost Estimates” on page 896 gives different expressions for the EAC (Estimate at Completion).

**Table 11.12** Performance Index Formulas

Acronym	Formula
CPI	$\frac{EV}{AC}$
SPI	$\frac{EV}{PV}$
$TCPI_{BAC}$	$\frac{WR}{BAC - AC}$
$TCPI_{EAC}$	$\frac{WR}{EAC - AC}$

---

## Cost Estimates

The ETC, or Estimate to Complete, and the EAC, or Estimate at Completion, are two metrics that are central to Earned Value Analysis. The ETC is a projection of the additional funds needed to finish the project. The EAC can be derived as follows (where AC represents the actual costs to date):

$$EAC = AC + ETC.$$

For the purposes of this document, each of these two cost estimates takes four forms, illustrated by the following table for ETC:

**Table 11.13** ETC Formulas

Acronym	Description	Formula
$ETC_{rev}$	Revised	$EAC_{rev} - AC$
$ETC_{OTD}$	Overrun to date	$BAC - EV = WR$
$ETC_{CPI}$	CPI	$\frac{WR}{CPI}$
$ETC_{CPI \times SPI}$	CPI times SPI	$\frac{WR}{CPI \times SPI}$

The  $ETC_{rev}$  is derived directly from the revised schedule, revised costs, and actual costs to date. This form does not make allowances for past performance. It is assumed that this information has already been factored into the updated schedule and costs. Analogous to the  $ETC_{rev}$ , the  $ETC_{OTD}$  is taken to be the remaining planned value (Budget at Completion less Earned Value), also known as Work Remaining (WR). This form can be thought of as having a performance factor of 1.

The  $ETC_{CPI}$  form is the remaining planned value divided by the CPI. In this way favorable cost performance (CPI greater than 1) forces the estimate downward. The performance factor in this case is the inverse of the CPI. Similarly, the  $ETC_{CPI \times SPI}$  form employs the inverse of the product of the CPI and SPI as the performance factor. In this case, both cost and schedule performance affect the estimate. For example, if both CPI and SPI are favorable (greater than 1), the estimate is lower.

---

## Analysis

This section describes each macro in the earned value macro set in further detail.

### **%EVA\_PLANNED\_VALUE**

This macro is used to establish periodic planned value. The first input data set for this macro (identified using the PLANSCHED= parameter) provides an initial baseline schedule. The second input data set (identified using the BUDGETCOST= parameter) contains the budgeted costs data set. One of the output data sets (identified using the PV= parameter) consists of two pertinent variables: \_TIME\_ and \_PV\_RATE\_. The latter variable lists the budgeted cost for the date or datetime indicated by the former variable. Another output data set is identified using the TASKPV= parameter, and provides the planned duration and costs by activity, for later use by the %EVA\_EARNED\_VALUE macro.

Upon completion, the status of the macro is saved in a global macro variable named \_EVA\_PLANNED\_VALUE\_, which can take one of the following three values:

- STATUS=SUCCESSFUL indicates successful completion of the macro.
- STATUS=SYNTAX\_ERROR indicates that macro execution was halted due to an error in the macro invocation syntax.
- STATUS=RUNTIME\_ERROR indicates that the macro invocation failed.

### **%EVA\_EARNED\_VALUE**

This macro is used to establish periodic earned value and actual cost. The first of the input data sets for this macro (identified using the REVISESCHED= parameter) contains a schedule that has been updated to reflect the current status of the project. A second input data set (identified using the ACTUALCOST= parameter) specifies the revised cost. The third input data set, from the %EVA\_PLANNED\_VALUE macro, is identified using the TASKPV= parameter, and supplies the planned duration and costs by activity. These are needed for computing the earned value. The output data set (identified using the EV= parameter) contains three relevant variables: \_TIME\_, \_EV\_RATE\_, and \_AC\_RATE\_. \_EV\_RATE\_ lists the Earned Value, and \_AC\_RATE\_ the Actual Cost of Work Performed, for the date or datetime indicated by the \_TIME\_ variable.

Upon completion, the status of the macro is saved in a global macro variable named \_EVA\_EARNED\_VALUE\_, which can take one of the following three values:

- STATUS=SUCCESSFUL indicates successful completion of the macro.
- STATUS=SYNTAX\_ERROR indicates that macro execution was halted due to an error in the macro invocation syntax.
- STATUS=RUNTIME\_ERROR indicates that the macro invocation failed.

## %EVA\_METRICS

This macro is used to compute the periodic metrics and summary statistics in reference to the date(s) or datetime(s) specified by the TIMENOW= parameter. The periodic planned value data set (generated by the %EVA\_PLANNED\_VALUE macro) and the periodic earned value data set (generated by the %EVA\_EARNED\_VALUE macro) are the inputs to the %EVA\_METRICS macro. These two data sets are identified using the PV= and EV= parameters, respectively. The METRICS= parameter identifies the periodic output data set, and the SUMMARY= parameter identifies the summary output data set. An output listing is also produced, which is derived from the summary output data set. The two output data sets are described next.

### **Periodic Output Data Set**

The variables in this data set are as follows:

- \_TIME\_ is the date or datetime reference point for the other variables.
- \_PV\_ is the cumulative Planned Value (Budgeted Cost of Work Scheduled).
- \_EV\_ is the cumulative Earned Value (Budgeted Cost of Work Performed).
- \_AC\_ is the cumulative Actual Cost (Actual Cost of Work Performed).
- \_EACREV\_ is the EAC<sub>rev</sub>. This variable is simply an accumulation of costs to project completion, according to the revised budget and schedule.
- \_SV\_ is the cumulative Schedule Variance, calculated as  $SV = EV - PV$ .
- \_CV\_ is the cumulative Cost Variance, calculated as  $CV = EV - AC$ .
- \_CPI\_ is the Cost Performance Index, calculated as  $CPI = \frac{EV}{AC}$ .
- \_SPI\_ is the Schedule Performance Index, calculated as  $SPI = \frac{EV}{PV}$ .

### **Summary Output Data Set**

The variables in this data set are as follows:

- \_NAME\_ is the internal variable name.
- \_LABEL\_ is the label used for the variable in the output listing.
- \_VALUEn\_ gives the value of the variable for the reference date or datetime given by the respective TIMENOW= parameter value.

Each row of the data set corresponds to one of the summary statistics as follows:

- \_pctcomp\_ is the percentage complete for the entire project, calculated as  $Percentage\ Complete = \frac{EV}{BAC}$ .
- \_ev\_ is the cumulative Budgeted Cost of Work Performed (Earned Value).

- `_pv_` is the cumulative Budgeted Cost of Work Scheduled (Planned Value).
- `_ac_` is the cumulative Actual Cost of Work Performed (Actual Cost).
- `_cpi_` is the Cost Performance Index.
- `_spi_` is the Schedule Performance Index.
- `_cv_` is the Cost Variance, calculated as  $CV = EV - AC$ .
- `_cvp_` is the Cost Variance percentage, calculated as  $CV\% = \frac{CV}{EV}$ .
- `_sv_` is the Schedule Variance, calculated as  $SV = EV - PV$ .
- `_svp_` is the Schedule Variance percentage, calculated as  $SV\% = \frac{SV}{PV}$ .
- `_bac_` is the Budget at Completion (BAC).
- `_etc_` is the Estimate To Complete (ETC). The form of EAC used to compute the ETC is specified by the EACFORM= parameter of the %EVA\_METRICS macro.
- `_eacrev_` is the revised Estimate at Completion (EAC<sub>rev</sub>).
- `_eacotd_` is the Overrun to Date form of the EAC, calculated as  $EAC_{OTD} = AC + WR$ , where WR is the Work Remaining ( $WR = BAC - EV$ ).
- `_eaccpi_` is the Cumulative CPI form of the EAC, calculated as  $EAC_{CPI} = AC + \frac{WR}{CPI}$ .
- `_eaccpispi_` is the Cumulative CPI times SPI form of the EAC, calculated as  $EAC_{CPI \times SPI} = AC + \frac{WR}{CPI \times SPI}$ .
- `_vac_` is the Variance at Completion, calculated as  $VAC = BAC - EAC$ . The form of EAC used is specified by the EACFORM= parameter of the %EVA\_METRICS macro.
- `_vacp_` is the CPI Variance at Completion percentage, calculated as  $VAC\% = \frac{VAC}{BAC}$ . The form of EAC used to compute the VAC is specified by the EACFORM= parameter of the %EVA\_METRICS macro.
- `_tcpi_` is the BAC To-Complete Performance Index, calculated as  $TCPI = \frac{WR}{BAC - AC}$ .
- `_etcpi_` is the EAC To-Complete Performance Index, calculated as  $TCPI = \frac{WR}{EAC - AC}$ . The form of EAC used is specified by the EACFORM= parameter of the %EVA\_METRICS macro.

Upon completion, the status of the macro is saved in a global macro variable named `_EVA_METRICS_`, which can take one of the following three values:

- STATUS=SUCCESSFUL indicates successful completion of the macro.
- STATUS=SYNTAX\_ERROR indicates that macro execution was halted due to an error in the macro invocation syntax.
- STATUS=RUNTIME\_ERROR indicates that the macro invocation failed.

## **%EVA\_TASK\_METRICS**

This macro uses the budgeted schedule and costs (identified using the PLANSCHED= and BUDGETCOST= parameters, respectively), along with the updated schedule and costs (identified using the REVISESCHED= and ACTUALCOST= parameters, respectively), to produce Cost Variance and Schedule Variance by task. The corresponding output data set is specified using the TASKMETRICS= parameter and is represented in the output listing. The variables in this data set are as follows:

- Activity is the reference task for the given row.
- WBS\_CODE is the Work Breakdown Structure code for the given task.
- \_CV\_ is the Cost Variance for the given task.
- \_CVP\_ is the Cost Variance percentage for the given task.
- \_SV\_ is the Schedule Variance for the given task.
- \_SVP\_ is the Schedule Variance percentage for the given task.
- \_CPI\_ is the Cost Performance Index for the given task.
- \_SPI\_ is the Schedule Performance Index for the given task.
- \_PV\_ is the Planned Value (BCWS) for the given task.
- \_EV\_ is the Earned Value (BCWP) for the given task.
- \_AC\_ is the Actual Cost (ACWP) for the given task.

Specifying “AGGREGATE=Y” with the WBSCODE= option forces the preceding metrics to be rolled up along the project hierarchy.

Upon completion, the status of the macro is saved in a global macro variable named \_EVA\_TASK\_METRICS\_, which can take one of the following three values:

- STATUS=SUCCESSFUL indicates successful completion of the macro.
- STATUS=SYNTAX\_ERROR indicates that macro execution was halted due to an error in the macro invocation syntax.
- STATUS=RUNTIME\_ERROR indicates that the macro invocation failed.

## **%EVG\_COST\_PLOT**

This macro is used to generate a line plot of the Earned Value, Planned Value, Actual Cost, and revised cost over time. If the project has not been completed, three Estimates at Completion are also delineated by a three-tiered box at the right-hand side of the plot area. In addition, several vital statistics appear as part of the legend: Planned Value, Earned Value, Actual Cost, revised cost, Cost and Schedule Performance Indices, Budget At Completion, and Estimates at Completion.

Upon completion, the status of the macro is saved in a global macro variable named \_EVG\_COST\_PLOT\_, which can take one of the following three values:

- STATUS=SUCCESSFUL indicates successful completion of the macro.
- STATUS=SYNTAX\_ERROR indicates that macro execution was halted due to an error in the macro invocation syntax.
- STATUS=RUNTIME\_ERROR indicates that the macro invocation failed.

### **%EVG\_SCHEDULE\_PLOT**

This macro is used to visualize planned and projected completion times for the project. To this end, plots of the planned value and actual and revised cost are displayed. To arrive at a projected finish time, the earned value plot is extended to the Budget at Completion with a slope equal to the ratio of Earned Value to time elapsed at the status date. The slope of this extension is the average rate at which Earned Value has accumulated up to the status date. Vital statistics displayed in the legend include Planned Value, Earned Value, Actual Cost, and Budget at Completion.

Upon completion, the status of the macro is saved in a global macro variable named \_EVG\_SCHEDULE\_PLOT\_, which can take one of the following three values:

- STATUS=SUCCESSFUL indicates successful completion of the macro.
- STATUS=SYNTAX\_ERROR indicates that macro execution was halted due to an error in the macro invocation syntax.
- STATUS=RUNTIME\_ERROR indicates that the macro invocation failed.

### **%EVG\_INDEX\_PLOT**

This macro is used to plot the Cost and Schedule Performance Indices over time. The To-Complete Performance Index is also shown.

Upon completion, the status of the macro is saved in a global macro variable named \_EVG\_INDEX\_PLOT\_, which can take one of the following three values:

- STATUS=SUCCESSFUL indicates successful completion of the macro.
- STATUS=SYNTAX\_ERROR indicates that macro execution was halted due to an error in the macro invocation syntax.
- STATUS=RUNTIME\_ERROR indicates that the macro invocation failed.

### **%EVG\_VARIANCE\_PLOT**

This macro is used to plot the Cost and Schedule Variances over time. Upon completion, the status of the macro is saved in a global macro variable named \_EVG\_VARIANCE\_PLOT\_, which can take one of the following three values:

- STATUS=SUCCESSFUL indicates successful completion of the macro.

- STATUS=SYNTAX\_ERROR indicates that macro execution was halted due to an error in the macro invocation syntax.
- STATUS=RUNTIME\_ERROR indicates that the macro invocation failed.

### **%EVG\_GANTT\_CHART**

This macro is used to show the Cost and Schedule Variances and the Cost and Schedule Performance Indices by activity, along with a Gantt chart of the schedule. For each task, the bottom bar depicts the baseline schedule and the top bar represents the updated schedule.

Upon completion, the status of the macro is saved in a global macro variable named \_EVG\_GANTT\_CHART\_, which can take one of the following three values:

- STATUS=SUCCESSFUL indicates successful completion of the macro.
- STATUS=SYNTAX\_ERROR indicates that macro execution was halted due to an error in the macro invocation syntax.
- STATUS=RUNTIME\_ERROR indicates that the macro invocation failed.

### **%EVG\_WBS\_CHART**

This macro is used to display the Work Breakdown Structure, in addition to any other data associated with an activity.

Upon completion, the status of the macro is saved in a global macro variable named \_EVG\_WBS\_CHART\_, which can take one of the following three values:

- STATUS=SUCCESSFUL indicates successful completion of the macro.
- STATUS=SYNTAX\_ERROR indicates that macro execution was halted due to an error in the macro invocation syntax.
- STATUS=RUNTIME\_ERROR indicates that the macro invocation failed.

## **Examples: Earned Value Management Macros**

In this section, a series of examples illustrates the usage and results of the earned value macro set.

### **Example 11.1: Integrated Assembly Project**

The planned schedule for an assembly project is shown in [Output 11.1.1](#). This schedule can be computed by either of the CPM or PM procedures. (For more details, see [Chapter 4](#) or [Chapter 5](#), respectively.)

**Output 11.1.1 Schedule IOUT1****Integrated Assembly Test Project  
Initial Schedule**

<b>Obs</b>	<b>Activity</b>	<b>Duration</b>	<b>Description</b>	<b>Planned Start</b>	<b>Planned Finish</b>
<b>1</b>	S	0	Start	01OCT09	01OCT09
<b>2</b>	PD	105	Preliminary Design	01OCT09	13JAN10
<b>3</b>	PDR	21	Prelim Design Review	14JAN10	03FEB10
<b>4</b>	FD	168	Final Design	04FEB10	21JUL10
<b>5</b>	PM	126	Procure Material	10JUN10	13OCT10
<b>6</b>	FDR	21	Final Design Review	22JUL10	11AUG10
<b>7</b>	FP	273	Facility Preparation	01OCT10	30JUN11
<b>8</b>	FC	273	Fabricate Components	12AUG10	11MAY11
<b>9</b>	DA	26	Deliver Assembly	26JUN11	21JUL11
<b>10</b>	FRR	21	Facil Readiness Rvw	01JUL11	21JUL11
<b>11</b>	IA	42	Install Assembly	22JUL11	01SEP11
<b>12</b>	RR	21	Readiness Review	02SEP11	22SEP11
<b>13</b>	T	126	Test	01OCT11	03FEB12
<b>14</b>	TV	63	Test Validation	07JAN12	09MAR12

The budgeted cost rates are given in Output 11.1.2. It is assumed that the activities incur costs continuously.

**Output 11.1.2 Cost Rates IATCOST****Budgeted Costs**

<b>Obs</b>	<b>Activity</b>	<b>Rate</b>
<b>1</b>	S	0.0000
<b>2</b>	PD	4.7619
<b>3</b>	PDR	7.1429
<b>4</b>	FD	1.7857
<b>5</b>	PM	6.0317
<b>6</b>	FDR	7.1429
<b>7</b>	FP	4.0293
<b>8</b>	FC	5.1282
<b>9</b>	DA	13.0769
<b>10</b>	FRR	7.1429
<b>11</b>	IA	5.9524
<b>12</b>	RR	7.1429
<b>13</b>	T	7.1429
<b>14</b>	TV	7.9365

The budgeted periodic cost can now be generated with the following specification of the %EVA\_PLANNED\_VALUE macro:

```
%eva_planned_value(
  plansched=iout1,
  activity=activity,
  start=start,
  finish=finish,
  duration=duration,
  budgetcost=iatcost,
  rate=rate
);
```

For brevity, only the first 17 rows of the output data set are shown in [Output 11.1.3](#).

**Output 11.1.3** %EVA\_PLANNED\_VALUE: Periodic Data Set

**Daily Planned Value**

Obs	Identifier	Period	PV Rate
1	01OCT09	4.76190	
2	02OCT09	4.76190	
3	03OCT09	4.76190	
4	04OCT09	4.76190	
5	05OCT09	4.76190	
6	06OCT09	4.76190	
7	07OCT09	4.76190	
8	08OCT09	4.76190	
9	09OCT09	4.76190	
10	10OCT09	4.76190	
11	11OCT09	4.76190	
12	12OCT09	4.76190	
13	13OCT09	4.76190	
14	14OCT09	4.76190	
15	15OCT09	4.76190	
16	16OCT09	4.76190	
17	17OCT09	4.76190	

Next, the actual progress of the project through September 30, 2010, is entered. The ACTUAL data set is shown in [Output 11.1.4](#).

**Output 11.1.4** Current Status ACTUAL**Status**

Obs	Activity	Actual Start	Actual Finish	Actual Rate	Pct. Comp.
1	S	01OCT09	01OCT09	0.0	100
2	PD	01OCT09	29JAN10	6.0	100
3	PDR	30JAN10	19FEB10	8.2	100
4	FD	20FEB10	10SEP10	3.1	100
5	PM	10AUG10	.	6.4	40
6	FDR	11SEP10	.	8.0	80

These inputs are then used by the CPM procedure with the original schedule to produce an updated schedule, given in **Output 11.1.5**. (For information about using the CPM procedure, see [Chapter 4](#).)

**Output 11.1.5** Updated Schedule UPDSCHED**Updated Schedule**

Obs	Activity	Actual Duration	Description	Pct. Comp.	Start	Finish
1	S	0	Start	100	01OCT09	01OCT09
2	PD	121	Preliminary Design	100	01OCT09	29JAN10
3	PDR	21	Prelim Design Review	100	30JAN10	19FEB10
4	FD	203	Final Design	100	20FEB10	10SEP10
5	PM	.	Procure Material	40	10AUG10	17DEC10
6	FDR	.	Final Design Review	80	11SEP10	05OCT10
7	FP	.	Facility Preparation	.	06OCT10	05JUL11
8	FC	.	Fabricate Components	.	12OCT10	11JUL11
9	DA	.	Deliver Assembly	.	07JUL11	01AUG11
10	FRR	.	Facil Readiness Rvw	.	06JUL11	26JUL11
11	IA	.	Install Assembly	.	02AUG11	12SEP11
12	RR	.	Readiness Review	.	13SEP11	03OCT11
13	T	.	Test	.	04OCT11	06FEB12
14	TV	.	Test Validation	.	10JAN12	12MAR12

The %EVA\_EARNED\_VALUE macro can then be used to generate the updated periodic cost, as follows:

```
%eva_earned_value(
  reviseschd=updsched,
  activity=activity,
  start=start,
  finish=finish,
  actualcost=iatupd,
  rate=rate
);
```

Again, for brevity only the first 17 rows of the output data set are shown in Output 11.1.6.

**Output 11.1.6 %EVA\_EARNED\_VALUE: Periodic Data Set**

**Daily Earned Value and Revised Cost**

Obs	Period Identifier	EV Rate	AC Rate
1	01OCT09	4.13223	6
2	02OCT09	4.13223	6
3	03OCT09	4.13223	6
4	04OCT09	4.13223	6
5	05OCT09	4.13223	6
6	06OCT09	4.13223	6
7	07OCT09	4.13223	6
8	08OCT09	4.13223	6
9	09OCT09	4.13223	6
10	10OCT09	4.13223	6
11	11OCT09	4.13223	6
12	12OCT09	4.13223	6
13	13OCT09	4.13223	6
14	14OCT09	4.13223	6
15	15OCT09	4.13223	6
16	16OCT09	4.13223	6
17	17OCT09	4.13223	6

The %EVA\_METRICS macro can be called with a current date of September 30, 2010, as follows:

```
%eva_metrics(
  timenow='30sep10'd,
  acronyms=long
);
```

Output 11.1.7 shows the output listing from %EVA\_METRICS. Notice that “ACRONYMS=long” is specified, which results in the long version of the earned value acronyms being used.

**Output 11.1.7 %EVA\_METRICS: Summary Statistics****Earned Value Analysis  
as of September 30, 2010**

Metric	Value
Percent Complete	20.66
BCWS (Budgeted Cost of Work Scheduled)	2038.00
BCWP (Budgeted Cost of Work Performed)	1374.00
ACWP (Actual Cost of Work Performed)	2020.30
CV (Cost Variance)	-646.30
CV%	-47.04
SV (Schedule Variance)	-664.00
SV%	-32.58
CPI (Cost Performance Index)	0.68
SPI (Schedule Performance Index)	0.67
BAC (Budget At Completion)	6650.00
EAC (Revised Estimate At Completion)	7349.50
EAC (Overrun to Date)	7296.30
EAC (Cumulative CPI)	9778.02
EAC (Cumulative CPI X SPI)	13527.00
ETC (Estimate To Complete)*	7757.72
VAC (Variance At Completion)*	-3128.02
VAC%*	-47.04
TCPI (BAC) (To-Complete Performance Index)	1.14
TCPI (EAC) (To-Complete Performance Index)*	0.68

\* The CPI form of the EAC is used.

Next, the %EVA\_TASK\_METRICS macro is used to produce Cost and Schedule Variance by task.

```
%eva_task_metrics(
  plansched=iout1,
  revisesched=updsched,
  activity=activity,
  start=start,
  finish=finish,
  pctcomp=pctcomp,
  budgetcost=iatcost,
  actualcost=iatupd,
  rate=rate,
  timenow='30sep10'd,
  acronyms=long
);
```

The output listing is shown in [Output 11.1.8](#).


#### **Output 11.1.8 %EVA\_TASK\_METRICS: CV and SV by Activity**

#### **Earned Value Analysis by Activity as of September 30, 2010**

Obs	Activity	BCWS	BCWP	ACWP	CV	CV%	SV	SV%	CPI	SPI
1	S	0.00	0.00	0.00	0.00	0.00	0.00	0.00	.	.
2	PD	500.00	500.00	726.00	-226.00	-45.20	0.00	0.00	0.69	1.00
3	PDR	150.00	150.00	172.20	-22.20	-14.80	0.00	0.00	0.87	1.00
4	FD	300.00	300.00	629.30	-329.30	-109.77	0.00	0.00	0.48	1.00
5	PM	681.59	304.00	332.80	-28.80	-9.47	-377.59	-55.40	0.91	0.45
6	FDR	150.00	120.00	160.00	-40.00	-33.33	-30.00	-20.00	0.75	0.80
7	FP	0.00	0.00	0.00	0.00	0.00	0.00	0.00	.	.
8	FC	256.41	0.00	0.00	0.00	0.00	-256.41	-100.00	.	0.00
9	DA	0.00	0.00	0.00	0.00	0.00	0.00	0.00	.	.
10	FRR	0.00	0.00	0.00	0.00	0.00	0.00	0.00	.	.
11	IA	0.00	0.00	0.00	0.00	0.00	0.00	0.00	.	.
12	RR	0.00	0.00	0.00	0.00	0.00	0.00	0.00	.	.
13	T	0.00	0.00	0.00	0.00	0.00	0.00	0.00	.	.
14	TV	0.00	0.00	0.00	0.00	0.00	0.00	0.00	.	.

[Output 11.1.9](#) through [Output 11.1.13](#) show charts that are produced using the earned value analysis reporting macros. First, the %EVG\_COST\_PLOT macro is used to generate the plot in [Output 11.1.9](#).


```
%evg_cost_plot(acronyms=long);
```

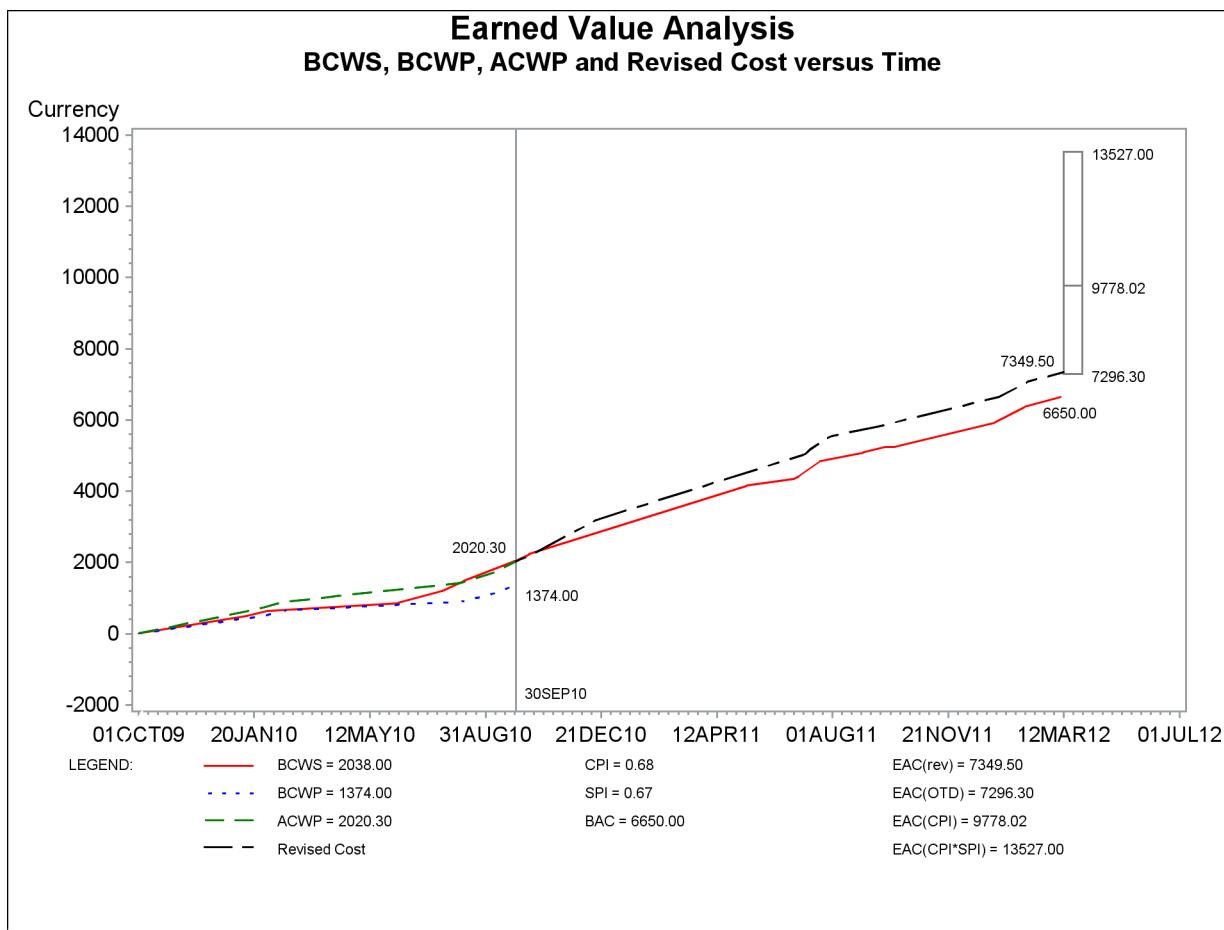**Output 11.1.9 %EVG\_COST\_PLOT, EV, PV, AC, and EAC<sub>rev</sub>**

According to the plan, the earned value percentage complete at the status date of September 30, 2010 (shown by the BCWS plot) should have been 2049/6650, or 30.81%. Instead, the percentage complete (shown by the BCWP plot) is only 1374/6650, or 20.66%.


Next, the %EVG\_SCHEDULE\_PLOT macro is used to produce the plot in Output 11.1.10. The resulting output shows a disastrous projected completion date of August 1, 2014, based upon the current earned value. This is two years and four months behind the planned schedule end date of March 10, 2012. Based on the performance of the project so far, it is estimated to cost \$9793 at completion (EAC<sub>CPI</sub>), amounting to nearly a 50% overrun.

```
%evg_schedule_plot;
```

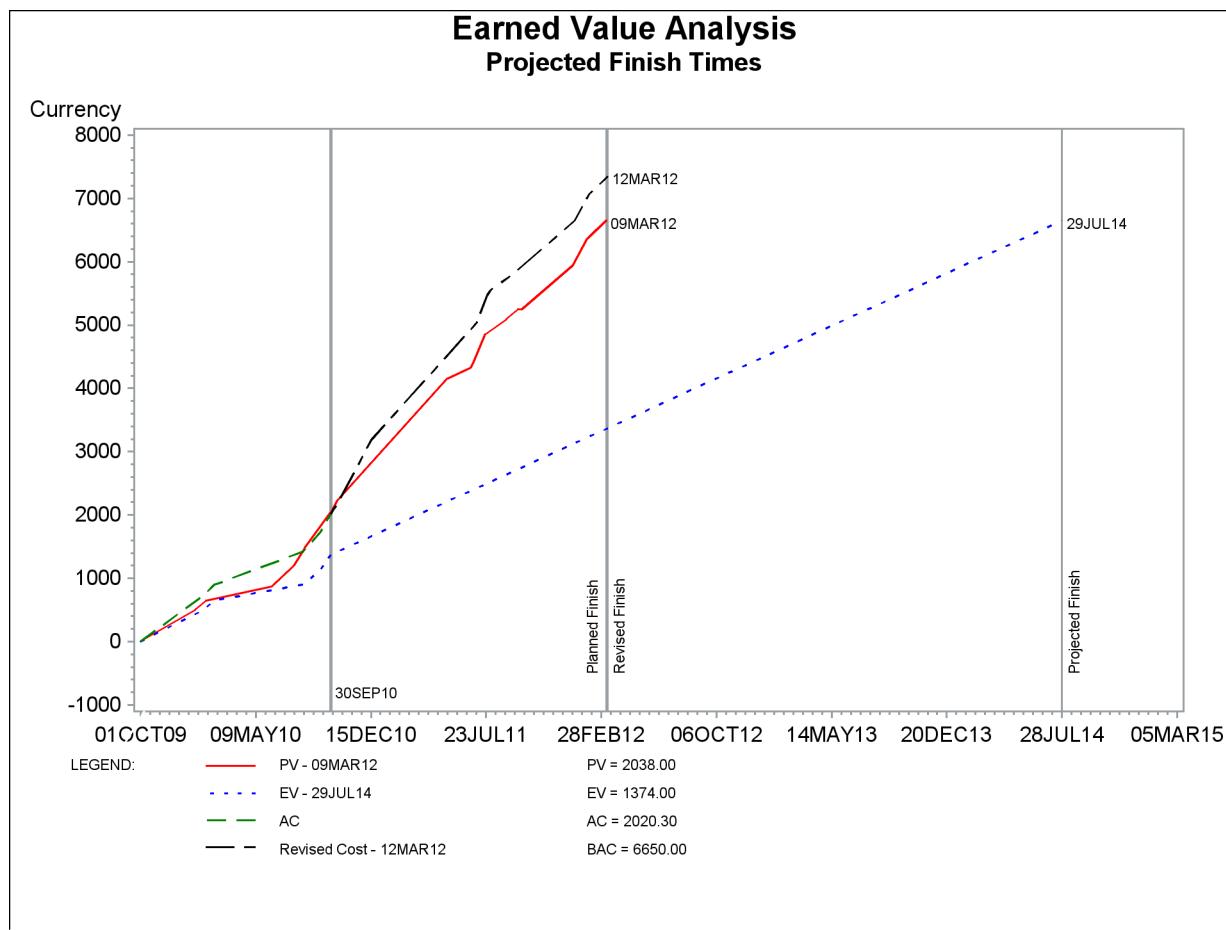**Output 11.1.10** %EVG\_SCHEDULE\_PLOT: Projected Completion Date

The %EVG\_INDEX\_PLOT macro is then used to produce the plot in Output 11.1.11.


```
%evg_index_plot;
```

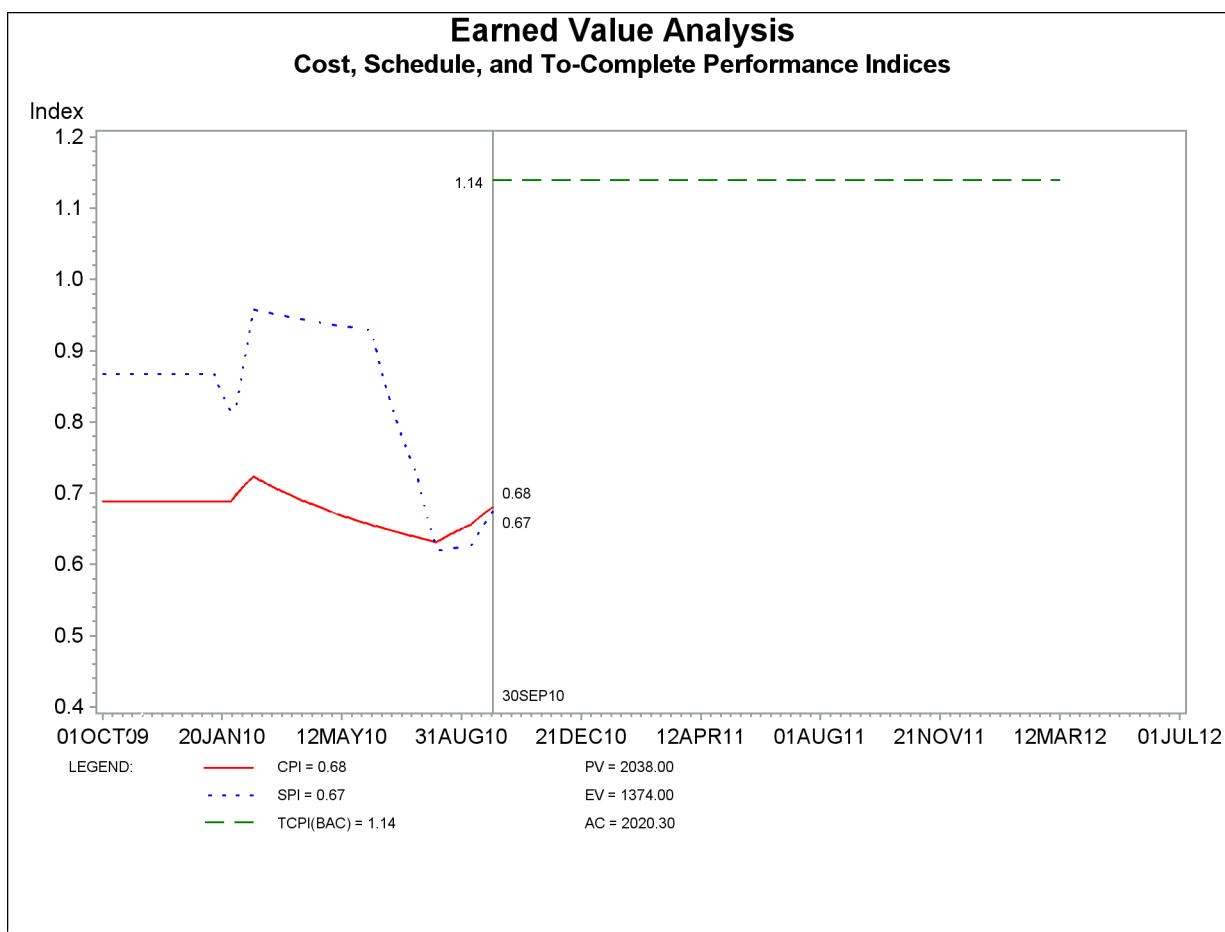**Output 11.1.11 %EVG\_INDEX\_PLOT: Cost and Schedule Performance Index**

The plot in Output 11.1.11 shows that the performance factor must be increased from 0.68 to 1.14 in order to stay within the budget.

The %EVG\_VARIANCE\_PLOT macro is used to produce the plot in Output 11.1.12.


```
%evg_variance_plot;
```

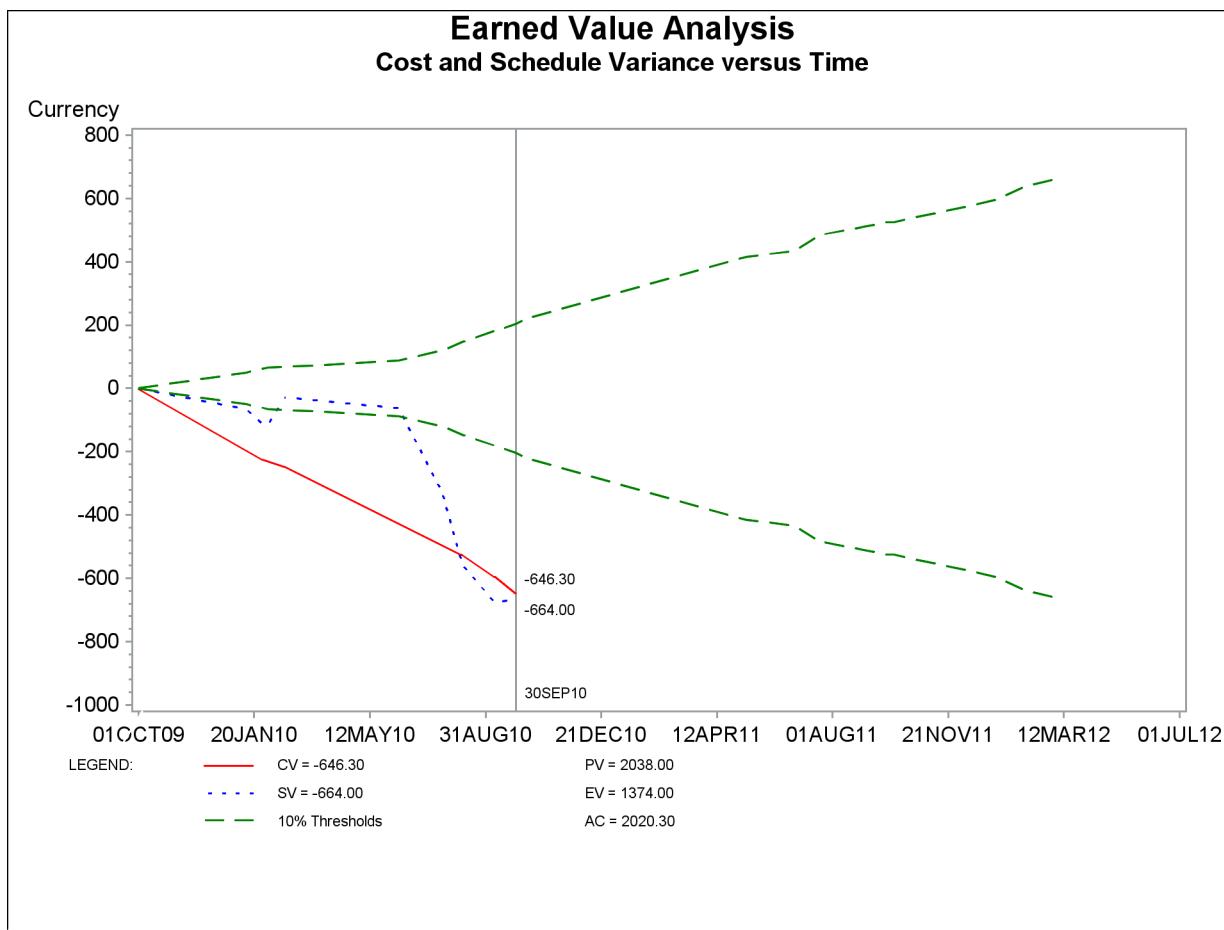**Output 11.1.12 %EVG\_VARIANCE\_PLOT: Cost and Schedule Variance**

The plot in Output 11.1.12 shows that both the cost and schedule variance have strayed outside of the area between the 10% threshold plots of the planned value.

Finally, the %EVG\_GANTT\_CHART macro is used to produce the Gantt chart shown in Output 11.1.13.

```
%evg_gantt_chart(
  plansched=iout1,
  revisesched=updsched,
  activity=activity,
  start=start,
  finish=finish,
  duration=duration,
  timenow='30sep10'd,
  id=pv ev ac cv cvp sv svp,
  height=3,
  scale=1.5
);
```

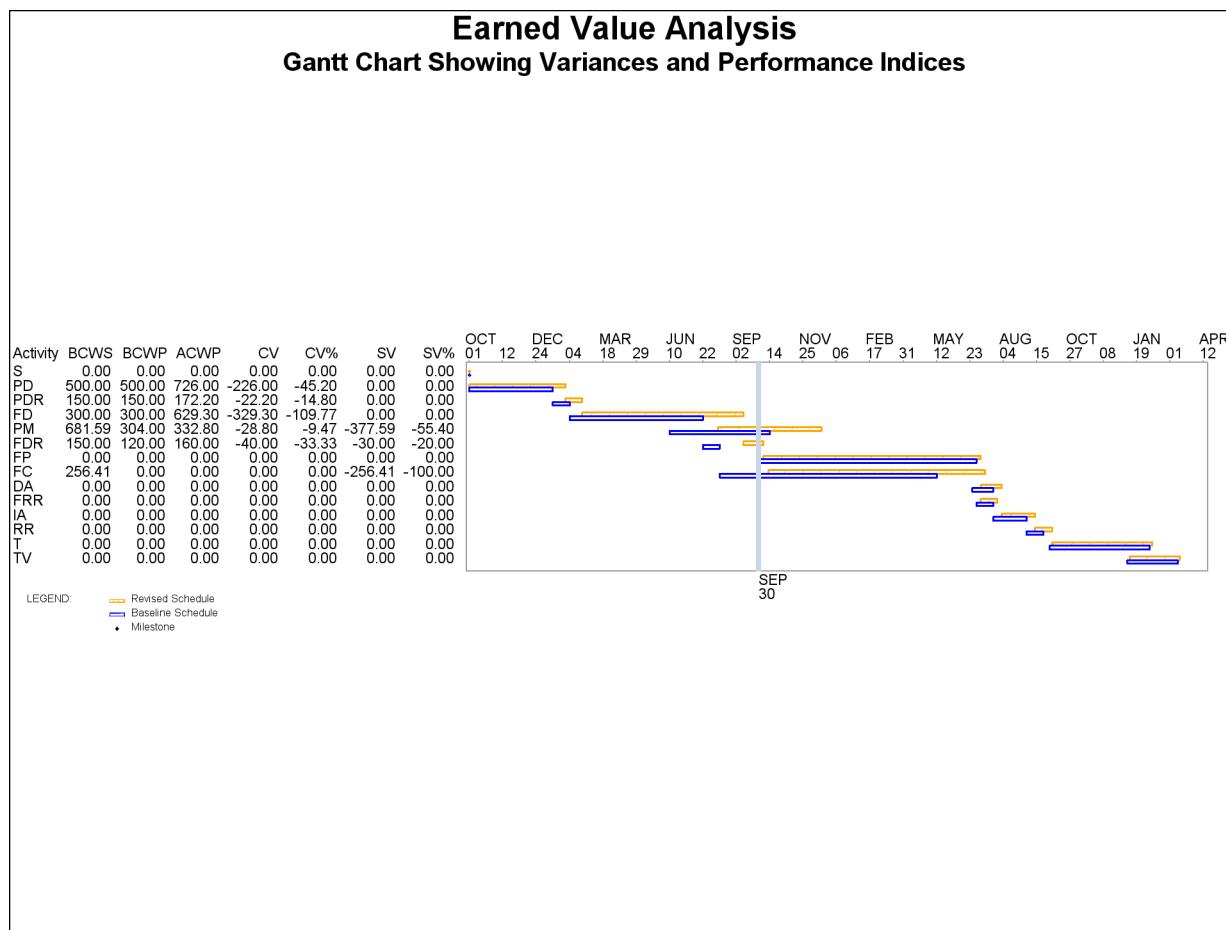**Output 11.1.13 %EVG\_GANTT\_CHART: Cost and Schedule Variance by Task****Example 11.2: Construction Project**

This example illustrates a home building multiproject. The cost structure of the multiproject consists of both rates and fixed costs. This example also demonstrates how to accommodate multiple status dates. The initial schedule is shown in Output 11.2.1.


**Output 11.2.1** Initial Schedule GBSCHED**Planned Construction Schedule**

<b>Obs</b>	<b>Activity</b>	<b>WBS Code</b>	<b>Scheduled Duration</b>	<b>Scheduled Start</b>	<b>Scheduled Finish</b>
1	Build House	0	1	04SEP10	12OCT10
2	Landscaping	0.00	1	29SEP10	10OCT10
3	Finish Grading	0.00.0	2	29SEP10	30SEP10
4	Walks & Landscape	0.00.1	5	06OCT10	10OCT10
5	Drainage	0.01	1	28SEP10	29SEP10
6	Gutters & Downspouts	0.01.0	1	28SEP10	28SEP10
7	Storm Drains	0.01.1	1	29SEP10	29SEP10
8	Wiring	0.02	1	14SEP10	05OCT10
9	Initial Wiring	0.02.0	2	14SEP10	15SEP10
10	Kitchen Fixtures	0.02.1	1	03OCT10	03OCT10
11	Finish Electrical	0.02.2	1	04OCT10	04OCT10
12	Finish Carpentry	0.02.3	3	03OCT10	05OCT10
13	Plumbing	0.03	1	10SEP10	04OCT10
14	Rough Plumbing	0.03.0	3	11SEP10	13SEP10
15	Basement Plumbing	0.03.1	1	10SEP10	10SEP10
16	Finish Plumbing	0.03.2	2	03OCT10	04OCT10
17	Foundation	0.04	1	04SEP10	15SEP10
18	Excavate & Footers	0.04.0	4	04SEP10	07SEP10
19	Pour Foundation	0.04.1	2	08SEP10	09SEP10
20	Pour Basement	0.04.2	2	14SEP10	15SEP10
21	Roofing	0.05	1	10SEP10	27SEP10
22	Finish Roof	0.05.0	2	26SEP10	27SEP10
23	Frame & Roof	0.05.1	4	10SEP10	13SEP10
24	Flooring	0.06	1	30SEP10	12OCT10
25	Varnish Floor	0.06.0	2	11OCT10	12OCT10
26	Finish Flooring	0.06.1	3	30SEP10	02OCT10
27	Heat & Ventilation	0.07	4	16SEP10	19SEP10
28	Plaster	0.08	10	20SEP10	29SEP10
29	Brickwork	0.09	6	20SEP10	25SEP10
30	Paint	0.10	3	06OCT10	08OCT10

The Work Breakdown Structure for the project is given in Output 11.2.2; this chart was created using the %EVG\_WBS\_CHART macro.

```
%evg_wbs_chart(
  structure=gbshed,
  activity=activity,
  project=project,
  id=wbs_code id,
  rotate=N,
  rotatetext=N,
  defid=N
);
```

### Output 11.2.2 %EVG\_WBS\_CHART: Work Breakdown Structure

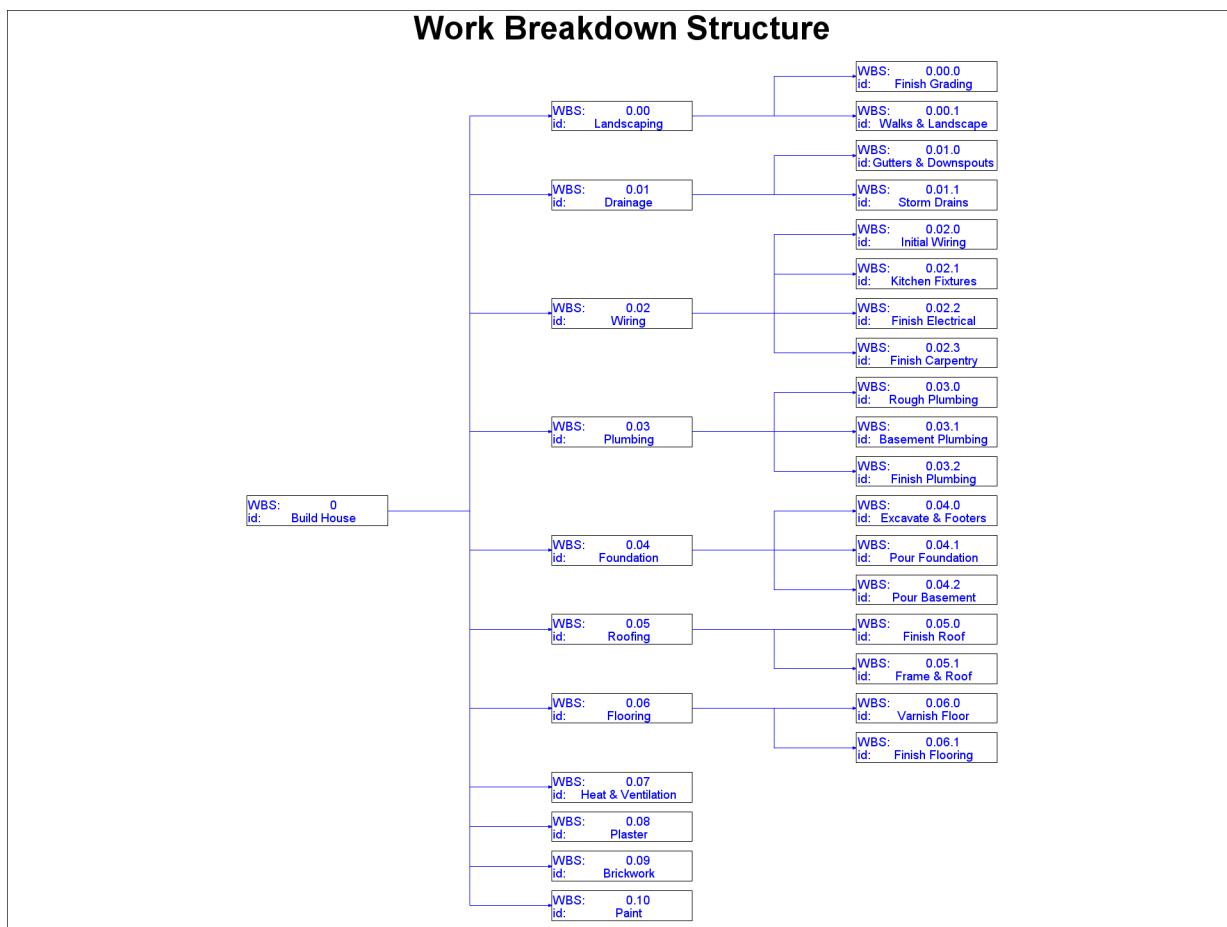

Output 11.2.3 lists the budgeted costs for each task.

### Output 11.2.3 Budgeted Cost Rates GBASE

#### Planned Construction Costs

Obs Activity		Start cost	Pct./Weights	rate
1 Build House		0 0		0
2 Landscaping		0 0		0
3 Drainage		0 0		0
4 Wiring		0 0		0
5 Plumbing		0 0		0
6 Foundation		0 0		0
7 Roofing		0 0		0
8 Flooring		0 0		0
9 Heat & Ventilation		325 50		40
10 Plaster		14500	1,2,3,4	20
11 Brickwork		9500	1,2,3	45
12 Paint		3250 50		30
13 Finish Grading		425 25		25
14 Walks & Landscape		2475 25		25
15 Gutters & Downspouts		1200 50		15
16 Storm Drains		150 25		15
17 Initial Wiring		575 25		45
18 Kitchen Fixtures		375 25		25
19 Finish Electrical		550 25		50
20 Finish Carpentry		1450 25		20
21 Rough Plumbing		1025 25		30
22 Basement Plumbing		1000 25		50
23 Finish Plumbing		350 25		20
24 Excavate & Footers		5250 50		20
25 Pour Foundation		1500 25		15
26 Pour Basement		950 50		20
27 Finish Roof		725 50		40
28 Frame & Roof		9500 25		35
29 Varnish Floor		750 25		15
30 Finish Flooring		425 50		25

Note that the “Storm Drains” task, in the sixteenth observation, costs one quarter (25%) of \$150 upon initiation and continues at a rate of \$15/day. When complete, the balance (75%) of the \$150 is charged. Weighted milestones are specified for the “Plaster” activity, given in Observation 10. At the start, one tenth ( $\frac{1}{1+2+3+4}$ ) of \$14,500, or \$1,450, is incurred. The rate is \$20/day. When the task is one third complete, another fifth ( $\frac{2}{1+2+3+4}$ ) of \$14,500, or \$2,900, is incurred. At completion, the cost is two fifths ( $\frac{4}{1+2+3+4}$ ) of \$14,500, or \$5,800.

The %EVA\_PLANNED\_VALUE macro is next invoked to compute the periodic planned value.

```
%eva_planned_value(
  plansched=gbshed,
  activity=activity,
  start=start,
  finish=finish,
  budgetcost=gbase,
  rate=rate,
  cost=cost,
  spct=spct,
  taskpv=bout,
  pv=gbcost
);
```

The periodic planned value data set is shown in [Output 11.2.4](#).

**Output 11.2.4 %EVA\_PLANNED\_VALUE: Periodic Data Set****Daily Planned Value**

<b>Obs</b>	<b>Identifier</b>	<b>Period</b>	<b>PV Rate</b>
1	04SEP10	2645.00	
2	05SEP10	20.00	
3	06SEP10	20.00	
4	07SEP10	2645.00	
5	08SEP10	390.00	
6	09SEP10	1140.00	
7	10SEP10	3460.00	
8	11SEP10	321.25	
9	12SEP10	65.00	
10	13SEP10	7958.75	
11	14SEP10	683.75	
12	15SEP10	971.25	
13	16SEP10	202.50	
14	17SEP10	40.00	
15	18SEP10	40.00	
16	19SEP10	202.50	
17	20SEP10	3098.33	
18	21SEP10	65.00	
19	22SEP10	3231.67	
20	23SEP10	2965.00	
21	24SEP10	65.00	
22	25SEP10	4815.00	
23	26SEP10	4772.50	
24	27SEP10	422.50	
25	28SEP10	1235.00	
26	29SEP10	6116.25	
27	30SEP10	581.25	
28	01OCT10	25.00	
29	02OCT10	237.50	
30	03OCT10	890.00	
31	04OCT10	902.50	
32	05OCT10	1107.50	
33	06OCT10	2298.75	
34	07OCT10	55.00	
35	08OCT10	1680.00	
36	09OCT10	25.00	
37	10OCT10	1881.25	
38	11OCT10	202.50	
39	12OCT10	577.50	

Notice that the TASKPV= parameter has been used to ultimately pass the planned activity duration and costs to %EVA\_EARNED\_VALUE. Assume that the schedule has been updated to reflect actual start and finish times, as of the status date September 15, 2010. The updated schedule is shown in [Output 11.2.5](#).

**Output 11.2.5 Updated Schedule GASCHED****Updated Construction Schedule**

<b>Obs</b>	<b>Activity</b>	<b>WBS Code</b>	<b>Scheduled Duration</b>	<b>Scheduled Start</b>	<b>Scheduled Finish</b>
1	Build House	0	1	04SEP10	17OCT10
2	Landscaping	0.00	1	04OCT10	15OCT10
3	Drainage	0.01	1	03OCT10	04OCT10
4	Wiring	0.02	1	19SEP10	10OCT10
5	Plumbing	0.03	1	15SEP10	09OCT10
6	Foundation	0.04	1	04SEP10	20SEP10
7	Roofing	0.05	1	15SEP10	02OCT10
8	Flooring	0.06	1	05OCT10	17OCT10
9	Heat & Ventilation	0.07	4	21SEP10	24SEP10
10	Plaster	0.08	10	25SEP10	04OCT10
11	Brickwork	0.09	6	25SEP10	30SEP10
12	Paint	0.10	3	11OCT10	13OCT10
13	Finish Grading	0.00.0	2	04OCT10	05OCT10
14	Walks & Landscape	0.00.1	5	11OCT10	15OCT10
15	Gutters & Downspouts	0.01.0	1	03OCT10	03OCT10
16	Storm Drains	0.01.1	1	04OCT10	04OCT10
17	Initial Wiring	0.02.0	2	19SEP10	20SEP10
18	Kitchen Fixtures	0.02.1	1	08OCT10	08OCT10
19	Finish Electrical	0.02.2	1	09OCT10	09OCT10
20	Finish Carpentry	0.02.3	3	08OCT10	10OCT10
21	Rough Plumbing	0.03.0	3	16SEP10	18SEP10
22	Basement Plumbing	0.03.1	1	15SEP10	15SEP10
23	Finish Plumbing	0.03.2	2	08OCT10	09OCT10
24	Excavate & Footers	0.04.0	4	04SEP10	11SEP10
25	Pour Foundation	0.04.1	2	12SEP10	14SEP10
26	Pour Basement	0.04.2	2	19SEP10	20SEP10
27	Finish Roof	0.05.0	2	01OCT10	02OCT10
28	Frame & Roof	0.05.1	4	15SEP10	18SEP10
29	Varnish Floor	0.06.0	2	16OCT10	17OCT10
30	Finish Flooring	0.06.1	3	05OCT10	07OCT10

The updated cost rates are given in [Output 11.2.6](#).

### Output 11.2.6 Updated Cost Rates GACT

#### Updated Construction Costs

Obs	Activity	Start		
		Rate	Cost	Pct./Weights
1	Build House	0	0 0	
2	Landscaping	0	0 0	
3	Drainage	0	0 0	
4	Wiring	0	0 0	
5	Plumbing	0	0 0	
6	Foundation	0	0 0	
7	Roofing	0	0 0	
8	Flooring	0	0 0	
9	Heat & Ventilation	40	325 50	
10	Plaster	20	14500 1,2,3,4	
11	Brickwork	45	9500 1,2,3	
12	Paint	30	3250 50	
13	Finish Grading	25	425 25	
14	Walks & Landscape	25	2475 25	
15	Gutters & Downspouts	15	1200 50	
16	Storm Drains	15	150 25	
17	Initial Wiring	45	575 25	
18	Kitchen Fixtures	25	375 25	
19	Finish Electrical	50	550 25	
20	Finish Carpentry	20	1450 25	
21	Rough Plumbing	30	1025 25	
22	Basement Plumbing	50	1000 25	
23	Finish Plumbing	20	350 25	
24	Excavate & Footers	30	6350 50	
25	Pour Foundation	30	2700 25	
26	Pour Basement	20	950 50	
27	Finish Roof	40	725 50	
28	Frame & Roof	35	9500 25	
29	Varnish Floor	15	750 25	
30	Finish Flooring	25	425 50	

The %EVA\_EARNED\_VALUE macro can then be called as follows:

```
%eva_earned_value(
  reviseschd=gasched,
  activity=activity,
  start=start,
  finish=finish,
  actualcost=gact,
  rate=rate,
  cost=cost,
  spct=spct,
  taskpv=bout,
  ev=gacost
);
```

The periodic earned value data set that is generated by %EVA\_EARNED\_VALUE is shown in [Output 11.2.7](#).

**Output 11.2.7 %EVA\_EARNED\_VALUE: Periodic Data Set****Daily Earned Value and Revised Cost**

<b>Obs</b>	<b>Identifier</b>	<b>Period</b>	<b>EV Rate</b>	<b>AC Rate</b>
<b>1</b>	04SEP10	2635.00	3205.00	
<b>2</b>	05SEP10	10.00	30.00	
<b>3</b>	06SEP10	10.00	30.00	
<b>4</b>	07SEP10	10.00	30.00	
<b>5</b>	08SEP10	10.00	30.00	
<b>6</b>	09SEP10	10.00	30.00	
<b>7</b>	10SEP10	10.00	30.00	
<b>8</b>	11SEP10	2635.00	3205.00	
<b>9</b>	12SEP10	385.00	705.00	
<b>10</b>	13SEP10	10.00	30.00	
<b>11</b>	14SEP10	1135.00	2055.00	
<b>12</b>	15SEP10	3460.00	3460.00	
<b>13</b>	16SEP10	321.25	321.25	
<b>14</b>	17SEP10	65.00	65.00	
<b>15</b>	18SEP10	7958.75	7958.75	
<b>16</b>	19SEP10	683.75	683.75	
<b>17</b>	20SEP10	971.25	971.25	
<b>18</b>	21SEP10	202.50	202.50	
<b>19</b>	22SEP10	40.00	40.00	
<b>20</b>	23SEP10	40.00	40.00	
<b>21</b>	24SEP10	202.50	202.50	
<b>22</b>	25SEP10	3098.33	3098.33	
<b>23</b>	26SEP10	65.00	65.00	
<b>24</b>	27SEP10	3231.67	3231.67	
<b>25</b>	28SEP10	2965.00	2965.00	
<b>26</b>	29SEP10	65.00	65.00	
<b>27</b>	30SEP10	4815.00	4815.00	
<b>28</b>	01OCT10	4772.50	4772.50	
<b>29</b>	02OCT10	422.50	422.50	
<b>30</b>	03OCT10	1235.00	1235.00	
<b>31</b>	04OCT10	6116.25	6116.25	
<b>32</b>	05OCT10	581.25	581.25	
<b>33</b>	06OCT10	25.00	25.00	
<b>34</b>	07OCT10	237.50	237.50	
<b>35</b>	08OCT10	890.00	890.00	
<b>36</b>	09OCT10	902.50	902.50	
<b>37</b>	10OCT10	1107.50	1107.50	
<b>38</b>	11OCT10	2298.75	2298.75	
<b>39</b>	12OCT10	55.00	55.00	
<b>40</b>	13OCT10	1680.00	1680.00	
<b>41</b>	14OCT10	25.00	25.00	
<b>42</b>	15OCT10	1881.25	1881.25	
<b>43</b>	16OCT10	202.50	202.50	
<b>44</b>	17OCT10	577.50	577.50	

The BUDGETCOST= parameter has been employed to capture the planned duration and costs for each activity. Next, the %EVA\_METRICS macro is used to produce statistics for the entire project. For illustrative purposes, a range of times from the start of the project to the revised projected end date is used. Typically, only actual status dates would be used; in this case, perhaps September 4, 2010 and September 15, 2010. Unless otherwise noted, the latter is the assumption for the remainder of the macros in this example.

```
%eva_metrics(  
  pv=gbcost,  
  ev=gacost,  
  timenow='04SEP10'd '15SEP10'd '01OCT10'd '17OCT10'd  
) ;
```

The output listing is given in [Output 11.2.8](#).

**Output 11.2.8 %EVA\_METRICS: Summary Statistics****Earned Value Analysis**

Metric	September 4, 2010	September 15, 2010	October 1, 2010	October 17, 2010
Percent Complete	4.54	17.78	68.59	100.00
PV (Planned Value)	2645.00	20320.00	48197.50	58055.00
EV (Earned Value)	2635.00	10320.00	39817.50	58055.00
AC (Actual Cost)	3205.00	12840.00	42337.50	60575.00
CV (Cost Variance)	-570.00	-2520.00	-2520.00	-2520.00
CV%	-21.63	-24.42	-6.33	-4.34
SV (Schedule Variance)	-10.00	-10000.00	-8380.00	0.00
SV%	-0.38	-49.21	-17.39	0.00
CPI (Cost Performance Index)	0.82	0.80	0.94	0.96
SPI (Schedule Performance Index)	1.00	0.51	0.83	1.00
BAC (Budget At Completion)	58055.00	58055.00	58055.00	58055.00
EAC (Revised Estimate At Completion)	60575.00	60575.00	60575.00	60575.00
EAC (Overrun to Date)	58625.00	60575.00	60575.00	60575.00
EAC (Cumulative CPI)	70613.39	72231.22	61729.23	60575.00
EAC (Cumulative CPI X SPI)	70869.21	129780.85	65810.42	60575.00
ETC (Estimate To Complete)*	67408.39	59391.22	19391.73	0.00
VAC (Variance At Completion)*	-12558.39	-14176.22	-3674.23	-2520.00
VAC%*	-21.63	-24.42	-6.33	-4.34
TCPI (BAC) (To-Complete Performance Index)	1.01	1.06	1.16	0.00
TCPI (EAC) (To-Complete Performance Index)*	0.82	0.80	0.94	0.94

\* The CPI form of the EAC is used.

Observe that the Estimate To Complete (ETC) and Schedule Performance Index (SPI) converge to 0 and 1, respectively, over time. Also, the Actual Cost (AC) agrees with the various Estimates At Completion (EAC's) at the projected completion date.

Next, the %EVA\_TASK\_METRICS macro is used to show an activity-level view of the progress of the project.

```
%eva_task_metrics(
  activity=id,
  plansched=gbsched,
  revisesched=gasched,
  start=start,
  finish=finish,
  budgetcost=gbase,
  actualcost=gact,
  cost=cost,
  spct=spct,
  rate=rate,
  timenow='15SEP10'd,
  aggregate=Y
);
```

The AGGREGATE= parameter is specified in order to roll up the values with respect to the project hierarchy. The output from this macro is shown in [Output 11.2.9](#) and [Output 11.2.10](#).

**Output 11.2.9 %EVA\_TASK\_METRICS: Metrics by Activity****Earned Value Analysis by Activity  
as of September 15, 2010**

<b>WBS Obs Code</b>	<b>PV</b>	<b>EV</b>	<b>AC</b>
1 0	20320.00	10320.00	12840.00
2 0.00	0.00	0.00	0.00
3 0.01	0.00	0.00	0.00
4 0.02	665.00	0.00	0.00
5 0.03	2165.00	1050.00	1050.00
6 0.04	7850.00	6860.00	9380.00
7 0.05	9640.00	2410.00	2410.00
8 0.06	0.00	0.00	0.00
9 0.07	0.00	0.00	0.00
10 0.08	0.00	0.00	0.00
11 0.09	0.00	0.00	0.00
12 0.10	0.00	0.00	0.00
13 0.00.0	0.00	0.00	0.00
14 0.00.1	0.00	0.00	0.00
15 0.01.0	0.00	0.00	0.00
16 0.01.1	0.00	0.00	0.00
17 0.02.0	665.00	0.00	0.00
18 0.02.1	0.00	0.00	0.00
19 0.02.2	0.00	0.00	0.00
20 0.02.3	0.00	0.00	0.00
21 0.03.0	1115.00	0.00	0.00
22 0.03.1	1050.00	1050.00	1050.00
23 0.03.2	0.00	0.00	0.00
24 0.04.0	5330.00	5330.00	6590.00
25 0.04.1	1530.00	1530.00	2790.00
26 0.04.2	990.00	0.00	0.00
27 0.05.0	0.00	0.00	0.00
28 0.05.1	9640.00	2410.00	2410.00
29 0.06.0	0.00	0.00	0.00
30 0.06.1	0.00	0.00	0.00

**Output 11.2.10 %EVA\_TASK\_METRICS: Metrics by Activity (continued)**

**Earned Value Analysis by Activity  
as of September 15, 2010**


<b>Obs</b>	<b>CV</b>	<b>CV%</b>	<b>SV</b>	<b>SV%</b>	<b>CPI</b>	<b>SPI</b>
<b>1</b>	-2520.00	-24.42	-10000.00	-49.21	0.80	0.51
<b>2</b>	0.00	0.00	0.00	0.00	.	.
<b>3</b>	0.00	0.00	0.00	0.00	.	.
<b>4</b>	0.00	0.00	-665.00	-100.00	.	0.00
<b>5</b>	0.00	0.00	-1115.00	-51.50	1.00	0.48
<b>6</b>	-2520.00	-36.73	-990.00	-12.61	0.73	0.87
<b>7</b>	0.00	0.00	-7230.00	-75.00	1.00	0.25
<b>8</b>	0.00	0.00	0.00	0.00	.	.
<b>9</b>	0.00	0.00	0.00	0.00	.	.
<b>10</b>	0.00	0.00	0.00	0.00	.	.
<b>11</b>	0.00	0.00	0.00	0.00	.	.
<b>12</b>	0.00	0.00	0.00	0.00	.	.
<b>13</b>	0.00	0.00	0.00	0.00	.	.
<b>14</b>	0.00	0.00	0.00	0.00	.	.
<b>15</b>	0.00	0.00	0.00	0.00	.	.
<b>16</b>	0.00	0.00	0.00	0.00	.	.
<b>17</b>	0.00	0.00	-665.00	-100.00	.	0.00
<b>18</b>	0.00	0.00	0.00	0.00	.	.
<b>19</b>	0.00	0.00	0.00	0.00	.	.
<b>20</b>	0.00	0.00	0.00	0.00	.	.
<b>21</b>	0.00	0.00	-1115.00	-100.00	.	0.00
<b>22</b>	0.00	0.00	0.00	0.00	1.00	1.00
<b>23</b>	0.00	0.00	0.00	0.00	.	.
<b>24</b>	-1260.00	-23.64	0.00	0.00	0.81	1.00
<b>25</b>	-1260.00	-82.35	0.00	0.00	0.55	1.00
<b>26</b>	0.00	0.00	-990.00	-100.00	.	0.00
<b>27</b>	0.00	0.00	0.00	0.00	.	.
<b>28</b>	0.00	0.00	-7230.00	-75.00	1.00	0.25
<b>29</b>	0.00	0.00	0.00	0.00	.	.
<b>30</b>	0.00	0.00	0.00	0.00	.	.

Next, the %EVG\_COST\_PLOT macro is called to show the Planned Value (PV), Earned Value (EV), Actual Cost (AC), and revised cost plots.

```
%evg_cost_plot;
```

The plot is shown in Output 11.2.11.

#### Output 11.2.11 %EVG\_COST\_PLOT, PV, EV, AC and Revised Cost

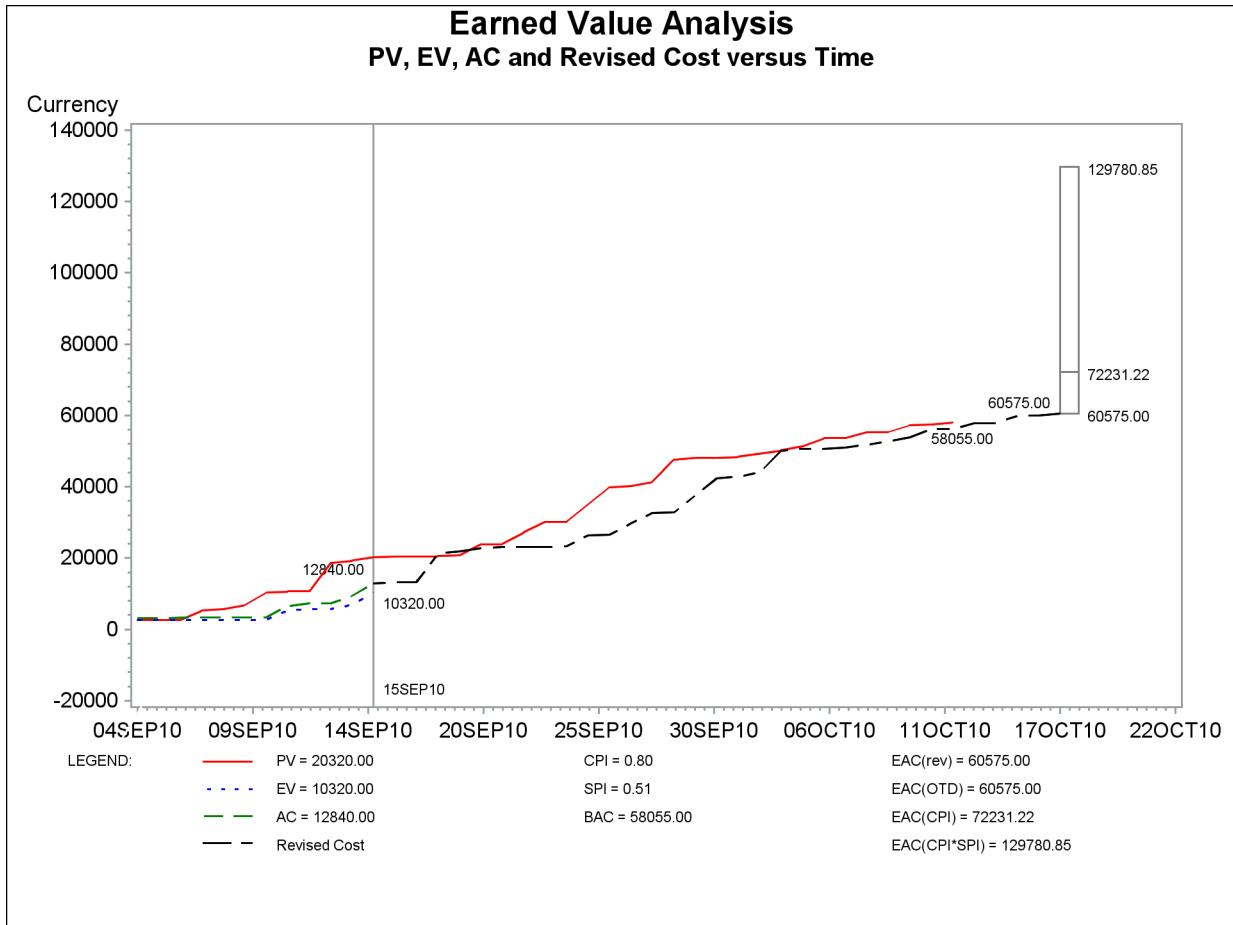


The %EVG\_SCHEDULE\_PLOT macro is used to show different estimates of the project completion date.

```
%evg_schedule_plot;
```

The plot is shown in [Output 11.2.12](#).


**Output 11.2.12 %EVG\_SCHEDULE\_PLOT: Estimated Completion Dates**

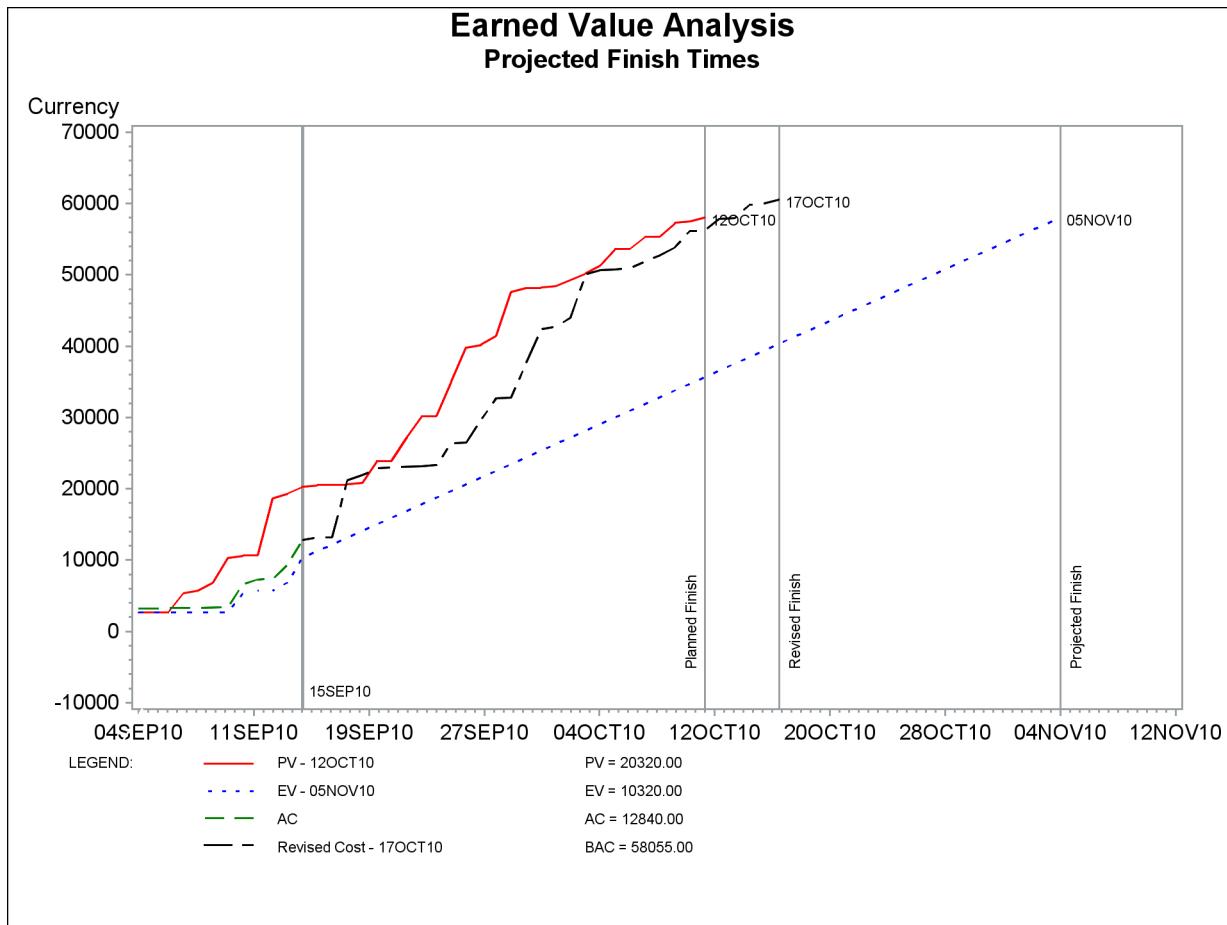

The %EVG\_INDEX\_PLOT macro is used to graphically display the performance indices for the project.


```
%evg_index_plot;
```

The plot is shown in [Output 11.2.13](#). As in the previous example, the cost performance needs to increase from 0.8 to 1.06 in order to stay within the budget.

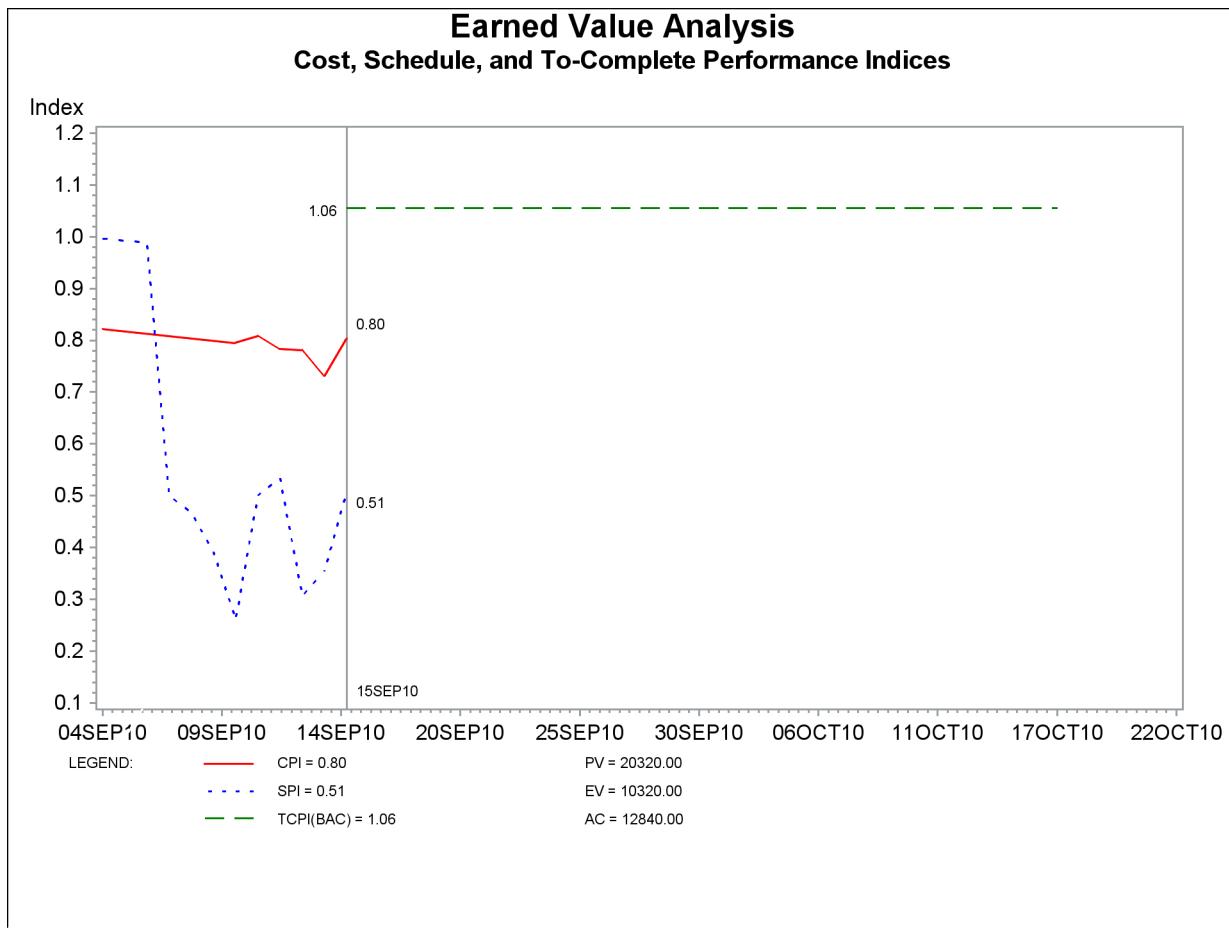**Output 11.2.13 %EVG\_INDEX\_PLOT: CPI, SPI, and TCPI**

The Cost and Schedule Variance for the project is shown in Output 11.2.14 using the following call to the %EVG\_VARIANCE\_PLOT macro:

```
%evg_variance_plot;
```

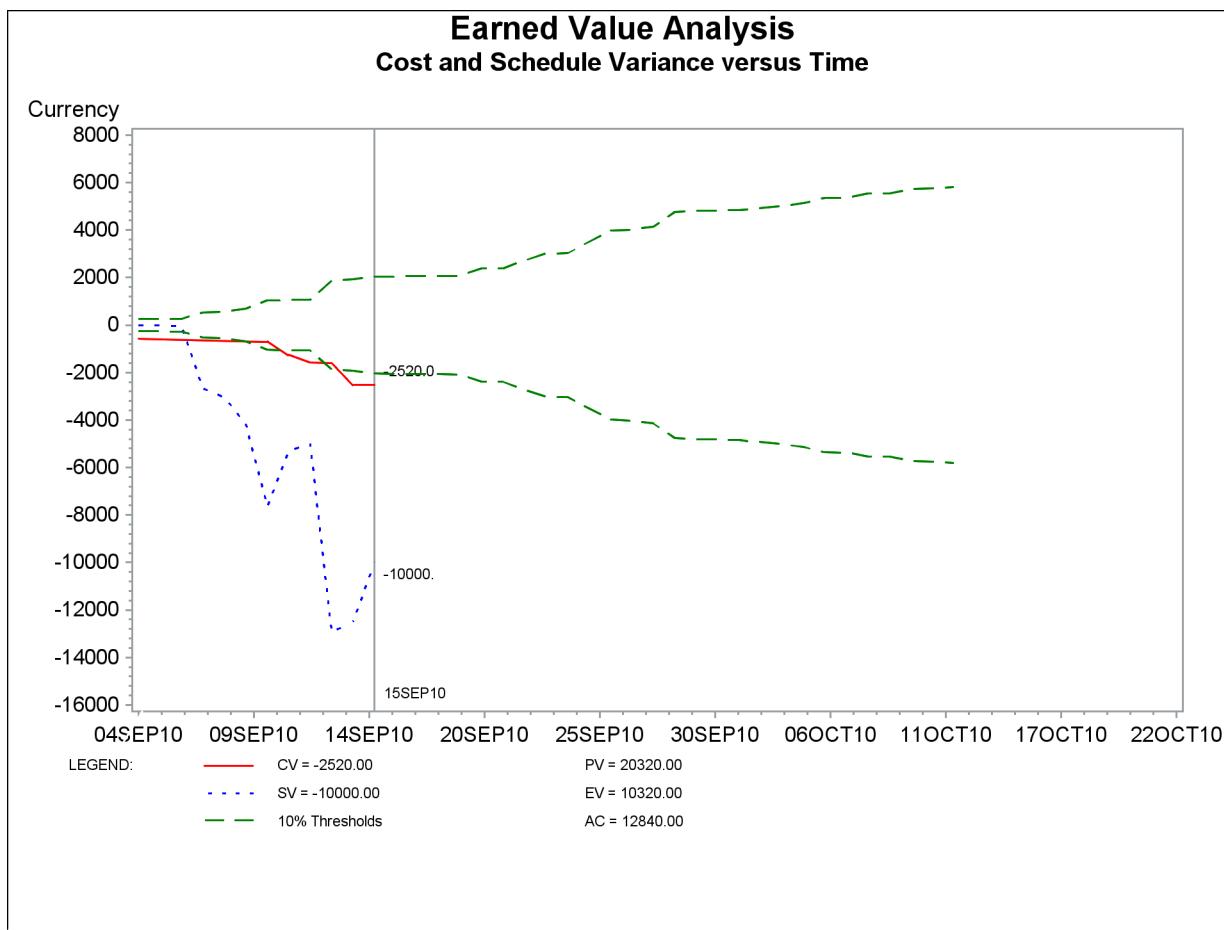**Output 11.2.14 %EVG\_VARIANCE\_PLOT: Cost and Schedule Variance**


While the Cost Variance is just outside the 10% threshold, the Schedule Variance is significantly outside and should be a warning signal that the project is slipping significantly. The plan called for \$20,320 of work to be completed, but only \$10,320 has been accomplished so far (roughly 50% of the goal).

Finally, the %EVG\_GANTT\_CHART macro is used to show a Gantt view of the project along with some metrics by task. In this case, only the Work Breakdown Structure code and Cost Variance (CV) and Schedule Variance (SV) are selected.

```
%evg_gantt_chart(
  activity=id,
  plansched=gbsched,
  reviseschd=gasched,
  start=start,
  finish=finish,
  timenow='15SEP10'd,
  id=wbs cv sv,
  height=3,
  scale=40
);
```

The resulting Gantt chart is shown in Output 11.2.15.

#### Output 11.2.15 %EVG\_GANTT\_CHART: Cost and Schedule Variance by Task

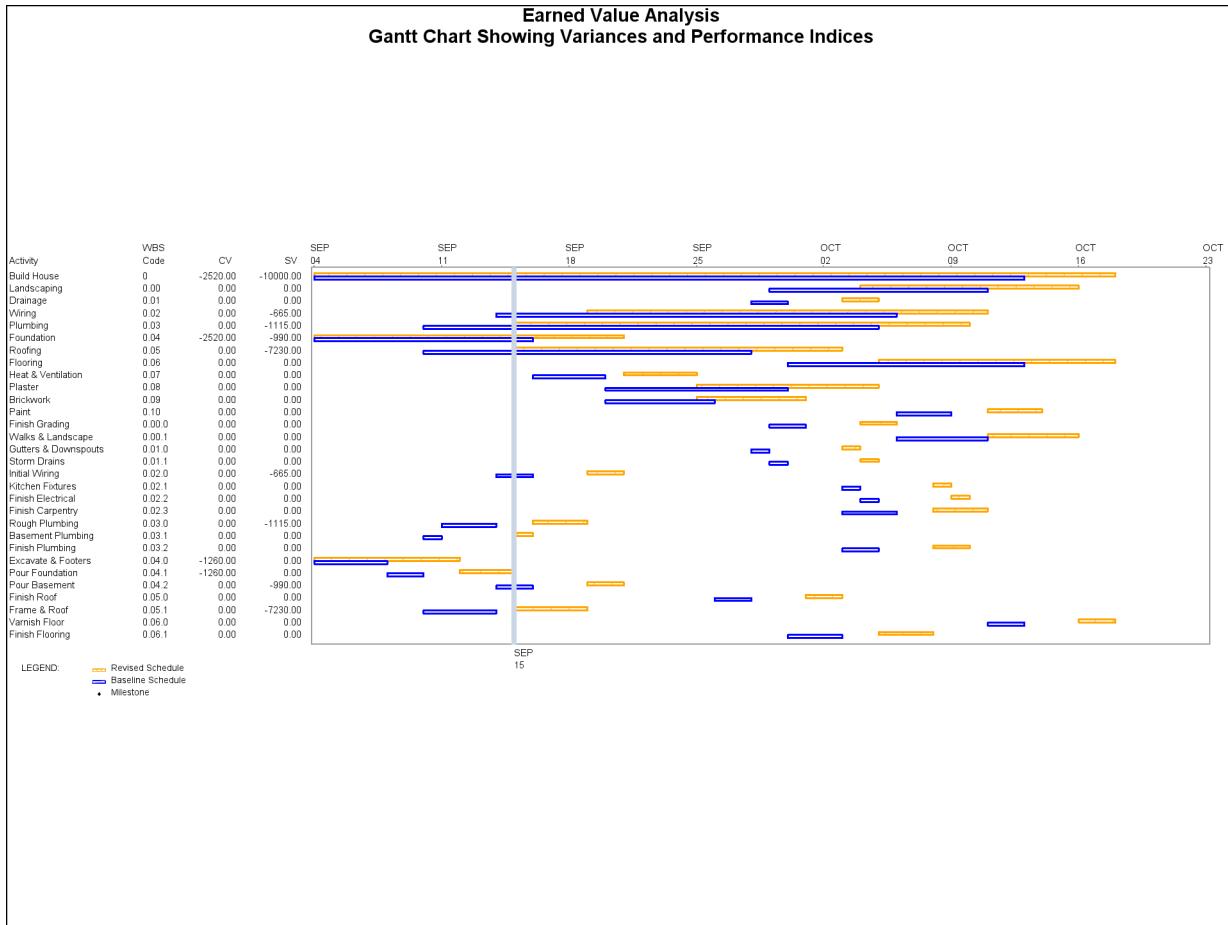

## References

- Fleming, Q. W., and Koppelman, J. M. (2000). *Earned Value Project Management*. 2nd ed. Newtown Square, PA: Project Management Institute.
- Project Management Institute (1996). *A Guide to the Project Management Body of Knowledge*. Upper Darby, PA: Project Management Institute.
- SAS Institute Inc. (1993). *SAS/OR Software: Project Management Examples*. Cary, NC: SAS Institute Inc.



# Appendix A

## Glossary of Project Management Terms

---

### Glossary

---

#### A

##### **activity**

an element of work performed during the course of a project. An activity normally has an expected duration, an expected cost, and expected resource requirements. Activities are often subdivided into tasks.

##### **activity delay**

the maximum amount of time that an activity can be delayed due to lack of resources.

##### **activity-on-arrow (AOA)**

see *arrow diagramming method*.

##### **activity-on-node (AON)**

see *precedence diagramming method*.

##### **activity priority**

a priority value that is assigned to activities to provide an ordering for activities that are waiting for resources (during resource-constrained scheduling).

##### **activity splitting**

The act of dividing activities into segments during resource allocation. In some cases, preemption of activity segments can free a resource to be used by a more **critical activity**.

##### **actual cost of work performed (ACWP)**

total costs incurred (direct and indirect) in accomplishing work during a given time period. See also *earned value*.

**actual finish date (AF)**

the calendar date when work on an activity actually ended. The AF date must be prior to the [timenow](#) date.

**actual start date (AS)**

the calendar date when work on an activity actually began. The AS date must be prior to the [timenow](#) date.

**aggregation**

the use of activity resource requirements to calculate total resource needs rather than to constrain the project schedule. Normally, resource requirements are used to perform [resource-constrained scheduling](#).

**alignment type**

an identification of the type of constraint that is associated with a [target date](#). The following types are available:

- finish on
- finish on or after
- finish on or before
- start on
- start on or after
- start on or before
- mandatory start
- mandatory finish

**arrow**

the graphic representation of an activity. See also [arrow diagramming method](#).

**arrow diagramming method**

a network diagramming technique in which activities are represented by arrows. The tail of the arrow represents the start of the activity, and the head represents the finish of the activity (the length of the arrow does not represent the expected [duration](#) of the activity). Activities are connected at points called nodes (usually drawn as small circles) to illustrate the sequence in which the activities are expected to be performed. See also [precedence diagramming method](#).

**as-of date**

see [timenow date](#).

---

**B****backward pass**

the calculation of late finish dates and late start dates for the uncompleted portions of all network activities, determined by working backwards through the network logic from the project end date. The end date can be specified, although it is usually calculated in a [forward pass](#).

**baseline schedule**

a project schedule that consists of baseline [start](#) and [finish](#) dates, which represent an estimated or expected schedule, or both. This schedule is often derived from an initial set of [early](#), [late](#), or [scheduled](#) finish dates. Typically, once a baseline schedule is established, it does not change over the course of a project.

**baseline finish date (BF)**

the calendar date when work on an activity is scheduled to end. This date is usually estimated, or it can be derived from the [early](#), [late](#), or [scheduled](#) finish dates. Typically, once a [baseline schedule](#) is established, it does not change over the course of the project.

**baseline start date (BS)**

the calendar date when work on an activity is scheduled to begin. This date is usually estimated, or it can be derived from the [early](#), [late](#), or [scheduled](#) start dates. Typically, once a [baseline schedule](#) is established, it does not change over the course of the project.

**budget at completion (BAC)**

the estimated total cost of the project when done.

**budgeted cost of work performed (BCWP)**

the sum of the approved cost estimates (including any overhead allocation) for activities (or portions of activities) that are completed during a given period (usually project-to-date). See also [earned value](#).

**budgeted cost of work scheduled (BCWS)**

the sum of the approved cost estimates (including any overhead allocation) for activities (or portions of activities) that are scheduled to be performed during a given period (usually project-to-date). See also [earned value](#).

## C

### calendar

a method of identifying project work days that can be altered so that weekends, holidays, vacation, weather days, and so forth are not included.

### cost performance index (CPI)

the ratio of budgeted costs to actual costs (BCWP/ACWP). The CPI is often used to predict the magnitude of a possible cost overrun using the following formula: original cost estimate/CPI = projected cost at completion. See also *earned value*.

### cost variance (CV)

- (1) any difference between the estimated cost of an activity and the actual cost of an activity.
- (2) in *earned value*, BCWP less ACWP.

### critical activity

any activity on the *critical path*.

### critical path

the series of activities of a project that determines the earliest completion of the project. The critical path generally changes from time to time as activities are completed ahead of or behind schedule. The critical path is usually defined as those activities with total float less than or equal to zero. See also *critical path method*.

### critical path method (CPM)

a network analysis technique used to predict project duration by analyzing which sequence of activities (which *path*) has the least amount of scheduling flexibility (the least amount of *total float*). Early dates are calculated by means of a *forward pass* using a specified start date. Late dates are calculated by means of a *backward pass* starting from a specified completion date (usually the calculated project *early finish date* of the forward pass).

### cycle

see *loop*.

---

**D****data date**

see *timenow date*.

**dependency**

see *logical relationship*.

**duration**

the number of work periods (not including [holidays](#) or other nonworking periods) required to complete an activity or set of activities. All activity durations are specified with the same [duration unit](#).

**duration unit**

the unit of time that each activity in the project lasts. The following choices are available:

- second
- minute
- hour
- day
- weekday
- week
- month
- qtr
- year

---

**E****early finish date (EF)**

in the [critical path method](#), the earliest possible point in time at which the uncompleted portions of an activity (or the project) can finish, based on the network logic and any schedule constraints. Early finish dates can change as the project progresses and changes are made to the project plan.

**early start date (ES)**

in the [critical path method](#), the earliest possible point in time at which the uncompleted portions of an activity (or the project) can start, based on the network logic and any schedule constraints. Early start dates can change as the project progresses and changes are made to the project plan.

**earned value (EV)**

(1) a method for measuring project performance that compares the amount of work that was planned with what was actually accomplished to determine whether cost and schedule performance are as planned. See also [actual cost of work performed](#), [budgeted cost of work performed](#), [budgeted cost of work scheduled](#), [cost variance](#), [cost performance index](#), [schedule variance](#), and [schedule performance index](#).

(2) the [budgeted cost of work performed](#), for an activity or group of activities.

**earned value analysis**

see definition (1) under [earned value](#).

**effort**

the number of labor units required to complete an activity or other project element. Usually expressed as staffhours, staffdays, or staffweeks. Should not be confused with [duration](#).

**estimate at completion (EAC)**

the expected total cost of an activity, group of activities, or the project when the defined scope of work has been completed. Most techniques for forecasting EAC include some adjustment of the original cost estimate based on project performance to date. Also called “estimated at completion.” Often shown as EAC = Actuals-to-date + ETC. See also [earned value](#) and [estimate to complete](#).

**estimate to complete (ETC)**

the expected additional cost needed to complete an activity, a group of activities, or the project. Most techniques for forecasting ETC include some adjustment to the original cost estimate based on project performance to date. Also called “estimated to complete.” See also [earned value](#) and [estimate at completion](#).

**F****float**

see [total float](#).

**forward pass**

the calculation of the early start and early finish dates for the uncompleted portions of all network activities. See also [backward pass](#).

**free float (FF)**

the amount of time an activity can be delayed without delaying the [early start](#) of any immediate [successor](#) activities. See also [total float](#).

---

**G****Gantt chart**

a graphic representation of work activities shown by a time-scaled bar chart.

**graphical evaluation and review technique (GERT)**

a [network analysis](#) technique that allows for conditional and probabilistic treatment of [logical relationships](#) (that is, some activities might not be performed).

---

**H****holiday**

a period of time within the project timeframe when work cannot be scheduled. Holidays can be assigned to one or more [calendars](#).

---

**L****lag**

a modification of a [logical relationship](#) that directs a delay of the successor task. For example, in a finish-to-start dependency with a 10-day lag, the successor activity can start 10 days after the predecessor has finished. See also [lead](#).

**late finish date (LF)**

in the [critical path method](#), the latest possible point in time that an activity can be completed without delaying a specified milestone (usually the project finish date).

**late start date (LS)**

in the [critical path method](#), the latest possible point in time that an activity can begin without delaying a specified milestone (usually the project finish date).

**lead**

a modification of a [logical relationship](#) that allows an acceleration of the successor task. For example, in a finish-to-start dependency with a 10-day lead, the successor activity can start 10 days before the predecessor has finished. See also [lag](#).

**logic**

the collection of activity dependencies that make up a project network diagram.

**logic diagram**

see [network diagram](#).

**logical relationship**

a dependency between two project activities. The four possible types of logical relationships are:

- finish-to-start—the “from” activity must finish before the “to” activity can start.
- finish-to-finish—the “from” activity must finish before the “to” activity can finish.
- start-to-start—the “from” activity must start before the “to” activity can start.
- start-to-finish—the “from” activity must start before the “to” activity can finish.

Finish-to-start is defined as the standard (or default) logical relationship.

**loop**

a [network path](#) that passes the same [node](#) twice. Loops cannot be analyzed by using traditional [network analysis](#) techniques such as [CPM](#) and [PERT](#). Loops are allowed in [GERT](#).

**M****maximum number of segments**

the maximum number of segments that an activity can be split into when [activity splitting](#) is allowed.

**milestone**

a significant event in the project, usually completion of a major deliverable.

**minimum segment duration**

the minimum duration of a segment of an activity when [activity splitting](#) is allowed.

---

**N****near-critical activity**

an activity that has low total float.

**network**

see *network diagram*.

**network analysis**

the process of identifying early and late start and finish dates for the uncompleted portions of project activities. See also *critical path method*, *program evaluation and review technique*, and *graphical evaluation and review technique*.

**network diagram**

a schematic display of the logical relationships of project activities. Always drawn from left to right to reflect project chronology. Often incorrectly referred to as a “PERT chart.”

**network logic**

see *logic*.

**network path**

any continuous series of connected activities that make up a project *network diagram*.

**node**

one of the defining points of a network; a junction point joined to some or all of the other dependency lines. Also, the graphic representation of an activity. See also *arrow diagramming method* and *precedence diagramming method*.

**nonstandard logical relationship**

a dependency between two project activities that is not the standard finish-to-start relationship. See *logical relationship* for the four possible types of relationships.

**O****organizational breakdown structure (OBS)**

a depiction of the project organization arranged so as to relate work packages to organizational units.

**overlap**

see *lead*.

---

**P****parent task**

see *supertask*.

**path**

a set of sequentially connected activities in a project network diagram.

**path float**

see *total float*.

**percent complete**

an estimate, expressed as a percent, of the amount of work that has been completed on an activity or group of activities.

**PERT chart**

a specific type of project network diagram. See *program evaluation and review technique*.

**precedence diagramming method (PDM)**

a network diagramming technique in which activities are represented by boxes (or nodes). Activities are linked together by **precedence relationships** to show the sequence in which the activities are to be performed.

**precedence relationship**

the term used in the precedence diagramming method for a logical relationship. In current usage, precedence relationship, logical relationship, and dependency are widely used interchangeably regardless of the diagramming method in use.

**predecessor activity**

any activity that exists on a common path with the activity in question and occurs before the activity in question.

**preemption**

see *activity splitting*.

**program evaluation and review technique (PERT)**

an event-oriented [network analysis](#) technique that is used to estimate project duration when there is a high degree of uncertainty with the individual activity duration estimates. PERT applies the [critical path method](#) to a weighted average duration estimate.

**project**

a temporary endeavor undertaken to create a unique product or service. A project consists of one or more activities.

**project management**

the application of knowledge, skills, tools, and techniques to project activities in order to meet or exceed stakeholder needs and expectations from a project.

**project management body of knowledge (PMBOK)**

an inclusive term that describes the sum of knowledge within the profession of project management. As with other professions such as law, medicine, and accounting, the body of knowledge rests with the practitioners and academics who apply and advance it. The PMBOK includes proven, traditional practices that are widely applied in addition to innovative and advanced ones that have seen more limited use.

**project network diagram**

see *network diagram*.

**project schedule**

the planned dates for performing activities and the planned dates for meeting milestones.

**R****remaining duration**

the amount of time needed to complete an activity.

**resource-constrained scheduling**

the scheduling of activities in a project with the knowledge of certain resource constraints and requirements. This process adjusts activity [scheduled start](#) and [finish](#) dates to conform to resource availability and use.

**resource leveling**

any form of [network analysis](#) in which scheduling decisions (start and finish dates) are driven by resource management concerns (for example, limited resource availability or difficult-to-manage changes in resource levels).

---

**S****schedule**

see [project schedule](#).

**schedule analysis**

see [network analysis](#).

**schedule performance index (SPI)**

the ratio of work that is performed to work that is scheduled (BCWP/BCWS). See [earned value](#).

**schedule variance**

- (1) any difference between the scheduled completion of an activity and the actual completion of that activity.
- (2) in [earned value](#), BCWP less BCWS.

**scheduled finish date (SF)**

the date when the activity is scheduled to be completed using the [resource-constrained scheduling](#) process.

**scheduled start date (SS)**

the date when the activity is scheduled to begin using the [resource-constrained scheduling](#) process. This date is equal to or greater than the [early start date](#).

**slack**

term used in PERT for float (see also *total float*).

**subtask**

an activity that is contained within a [supertask](#).

**successor activity**

any activity that exists on a common path with the activity in question and occurs after the activity in question.

**supertask**

an aggregate or summary activity that contains one or more activities ([subtasks](#)) such that no subtask can begin until the supertask has begun. The supertask cannot end until all of the subtasks have ended.

---

**T****target date**

date that is used to constrain the start or finish of an activity. The type of constraint is identified by an alignment type.

**task**

see [activity](#).

**timenow date**

the calendar date that separates actual (historical) data from future (scheduled) data.

**total float (TF)**

the amount of time that an activity can be delayed from its [early start](#) without delaying the project finish date. Total float is a mathematical calculation and can change as the project progresses and changes are made to the project plan. Also called “float,” “slack,” and “path float.” See also [free float](#).

---

**W****work breakdown structure (WBS)**

a deliverable-oriented grouping of project elements that organizes and defines the total scope of the project. Each descending level represents an increasingly detailed definition of a project component. Project components can be products or services.

### **work packages**

a deliverable at the lowest level of the [work breakdown structure](#). A work package can be divided into activities.

### **workshift**

one or more pairs of on/off working times that define the valid working periods within a single day.

---

## **References**

Project Management Institute (1996). *A Guide to the Project Management Body of Knowledge*. Upper Darby, PA: Project Management Institute.

# Appendix B

## Glossary of Earned Value Management Terms

---

### Glossary

---

#### A

##### AC

see *actual cost*.

##### ACWP

see *actual cost*.

##### actual cost

total costs incurred that must relate to whatever cost was budgeted within the *planned value* and *earned value* (which can sometimes be direct labor hours alone, direct costs alone, or all costs including indirect costs) in accomplishing work during a given time period.

##### actual cost of work performed

see *actual cost*.

---

#### B

##### BAC

see *budget at completion*.

##### BCWP

see *earned value*.

##### BCWS

see *planned value*.

**budget at completion**

the sum of the total budgets for a project.

**budgeted cost of work performed**

see *earned value*.

**budgeted cost of work scheduled**

see *planned value*.

**C****CPI**

see *cost performance index*.

**CV**

see *cost variance*.

**CV%**

see *cost variance percentage*.

**cost performance index (CPI)**

the cost efficiency ratio of *earned value* to *actual cost*. CPI is often used to predict the magnitude of a possible cost overrun by using the following formula:  $\frac{BAC}{CPI}$  = projected cost at completion.  $CPI = \frac{EV}{AC}$ .

**cost variance (CV)**

the difference between the *earned value* of an activity and the *actual cost* of that activity; that is,  $CV = EV - AC$ .

**cost variance percentage (CV%)**

cost variance relative to earned value:  $CV\% = \frac{CV}{EV}$ .

**E****EAC**

see *estimate at completion*.

**ETC**

see *estimate to complete*.

**EV**

see *earned value*.

**earned value**

the physical work that is accomplished plus the authorized budget for this work. The sum of the approved cost estimates (which might include overhead allocation) for activities (or portions of activities) that are completed during a given period (usually project-to-date). This term was previously called the budgeted cost of work performed (BCWP) for an activity or group of activities.

**earned value management**

a method for integrating scope, schedule, and resources, and for measuring project performance. It compares the value of work that was planned, the value of work that was actually completed, and the amount of money that was actually spent, to determine if cost and schedule performance are as planned.

**estimate at completion (EAC)**

the expected total cost of an activity, a group of activities, or the project when the defined scope of work has been completed. Most techniques for producing the EAC include some adjustment of the original cost estimate, based on actual project performance to date. This metric is derived from the ETC as follows:  $EAC = AC + ETC$ . See *estimate to complete*.

**estimate to complete (ETC)**

the expected additional cost needed to complete an activity, a group of activities, or the project. Most techniques for producing the ETC factor in the project performance to date. The revised ETC, or  $ETC_{rev}$ , is the cumulative cost from the status date to the project completion date, according to the revised schedule and costs. The other three formulations used in this document are as follows:

$$ETC_{OTD} = BAC - EV$$

$$ETC_{CPI} = \frac{BAC - EV}{CPI}$$

$$ETC_{CPI \times SPI} = \frac{BAC - EV}{CPI \times SPI}$$

**P****PV**

see *planned value*.

**percentage complete**

the percentage of total earned value that has been accumulated for a project:

$$\text{percentage complete} = \frac{EV}{BAC}$$

**planned value**

the physical work that is scheduled, plus the authorized budget to accomplish the scheduled work. Previously, this term was called the budgeted cost of work scheduled (BCWS).

---

**S****SPI**

see *schedule performance index*.

**SV**

see *schedule variance*.

**SV%**

see *schedule variance percentage*.

**schedule performance index (SPI)**

the schedule efficiency ratio of *earned value* that was accomplished against the *planned value*. The SPI describes what portion of the planned schedule was actually accomplished.  $SPI = \frac{EV}{PV}$ .

**schedule variance (SV)**

the difference between the *earned value* and the *planned value* of the project at any point in time; that is,  $SV = EV - PV$ .

**schedule variance percentage (SV%)**

schedule variance relative to planned value:

$$SV\% = \frac{SV}{PV}$$

**T****TCPI**

see *to-complete performance index*.

**to-complete performance index (TCPI)**

the cost of remaining work divided by the remaining budget or estimated budget:

$$TCPI(BAC) = \frac{BAC - EV}{BAC - AC}$$

$$TCPI(EAC) = \frac{BAC - EV}{EAC - AC}$$

**V****VAC**

see *variance at completion*.

**VAC%**

see *variance at completion percentage*.

**variance at completion (VAC)**

the difference between the original budget and the current estimate at completion:  $VAC = BAC - EAC$ .

**variance at completion percentage (VAC%)**

the variance at completion relative to the budget at completion:  $VAC\% = \frac{VAC}{BAC}$ .

**W****WBS**

see *work breakdown structure*.

**work breakdown structure (WBS)**

the project hierarchy.



# Subject Index

- AC\_variable
  - periodic data set (%EVA\_METRICS), 898
  - task data set (%EVA\_TASK\_METRICS), 900
- AC\_RATE\_variable
  - periodic data set (%EVA\_EARNED\_VALUE), 897
- ACRONYMS\_macro variable
  - %EVA\_METRICS macro, 885
  - %EVA\_TASK\_METRICS macro, 887
  - %EVG\_COST\_PLOT macro, 889
  - %EVG\_INDEX\_PLOT macro, 891
  - %EVG\_SCHEDULE\_PLOT macro, 890
  - %EVG\_VARIANCE\_PLOT macro, 892
- ACT variables, *see* ACTION variables
  - Payoff data set (DTREE), 417
- ACTDELAY variable
  - Activity data set (CPM), 81, 223
- ACTID variable
  - Schedule data set (PM), 328
- ACTION variables
  - Payoff data set (DTREE), 417
- actions, decision stage, 382
- activities
  - limiting the number per page (GANTT), 520
- activity align types, 73
- activity axis
  - GANTT procedure, 485, 537
- activity calendar, 75, 175
- Activity data set
  - as input to NETDRAW procedure, 686
  - CPM procedure, 55, 57, 66, 487
  - missing values, 137
  - %MSPTOSAS macro, 356
  - resource requirement specification (CPM), 118
  - %SASTOMSP macro, 356
  - variables, 135
- activity delay
  - analysis, 82, 99, 200
  - and supplementary resources, 121
  - example (CPM), 214, 217, 218, 223
  - specification, 81, 82
  - wait until, 82
- activity duration, *see* duration
- activity information, *see* Activity data set
  - additional variables, 78
- activity numbers
  - PM procedure, 325
  - PM window, 325
- Activity-on-Arc
  - network diagram, 56
  - specification, CPM procedure, 76, 91
  - specification, Logic Gantt charts, 545
- Activity-on-Edge, *see* Activity-on-Arc
- Activity-on-Node
  - network diagram, 57
  - specification, CPM procedure, 70, 90
  - specification, Logic Gantt charts, 545
- Activity-on-Vertex, *see* Activity-on-Node
- activity splitting
  - at TIMENOW (CPM), 72, 112, 123
  - CPM procedure, 84, 85, 89, 122, 123
  - example (CPM), 225
  - example (GANTT), 604
  - GANTT procedure, 525, 558
  - maximum number of segments, 84
  - minimum duration of segment, 85
  - option to allow default, 89
- activity status
  - flags indicating, 501, 559
  - indicating within node, 677, 731
  - setting in CPM procedure, 100
- activity text
  - color, 513
  - font baseline, 536
- ACTIVITY variable
  - Activity data set (CPM), 70
  - Network data set (NETDRAW), 673, 687
  - Precedence data set (GANTT), 486, 498, 510, 517, 523, 546
- ACTIVITY variable
  - %SASTOMSP macro parameters, 361
- ACTIVITY variable
  - task data set (%EVA\_TASK\_METRICS), 900
- ACTIVITYPRTY variable
  - Activity data set (CPM), 81
- actual bar
  - height, 510
  - offset, 510
- actual cost, 846, 847, 862, 868, 869, 876, 897–900
- actual schedule
  - CPM procedure, 70, 110–112
  - example (CPM), 188
  - example (GANTT), 598
  - fill pattern for (GANTT), 537
  - finish times (CPM), 71
  - GANTT procedure, 525, 558

- start times (CPM), 71
- ACWP**, 41
- add activities
  - PM procedure, 319
  - PM window, 319
- add activity records
  - CPM procedure, 65
- add subtasks
  - PM window, 321
- add tasks
  - Table View (PM), 310
- A\_DUR** variable
  - Schedule data set (CPM), 99, 110, 111, 190
- A\_FINISH** variable
  - Activity data set (CPM), 71, 94, 110
  - input data set (%EVG\_WBS\_CHART), 894
  - Network data set (NETDRAW), 674, 687, 691
  - Schedule data set (CPM), 99, 100, 110, 111, 190
  - Schedule data set (GANTT), 500, 508, 525, 526, 601
- AFINMILE** variable
  - Schedule data set (CPM), 99
- \_ALABEL** variable
  - Label data set (GANTT), 555, 556
- ALIGN** variable
  - Network data set (NETDRAW), 673, 676, 687, 693
- ALIGNDATE** variable
  - Activity data set (CPM), 73, 94, 96, 97
- \_ALIGNDATE** variable
  - %SASTOMSP macro parameters, 361
- alignment constraints
  - CPM procedure, 73, 96, 97
  - Gantt View, 316
  - PM window, 321
  - pop-up menu, 312
- ALIGNTYPE** variable
  - Activity data set (CPM), 73, 96, 97
- \_ALIGNTYPE** variable
  - %SASTOMSP macro parameters, 361
- alternate resources
  - CPM procedure, 81, 85, 87, 123, 124
  - example (CPM), 230
- alternatives, decision stage, 382
- Annotate data set
  - DTREE procedure, 403
  - GANTT procedure, 486, 496, 510, 537
  - NETDRAW procedure, 662, 701
  - processing (DTREE), 405
  - suppress processing (DTREE), 405
- Annotate facility
  - coordinate systems (GANTT), 537
  - coordinate systems (NETDRAW), 701
  - drawing legend of decision tree diagram, 459
- DTREE procedure, 458
- example (GANTT), 631
- example (NETDRAW), 758, 761
- GANTT procedure, 537
- NETDRAW procedure, 701, 702
- AOA**, *see* Activity-on-Arc
- AOE**, *see* Activity-on-Arc
- AON**, *see* Activity-on-Node
- AOV**, *see* Activity-on-Node
- arc routing, 688, 689
- arrow diagramming method, *see* Activity-on-Arc
- arrowheads
  - length of, 680
  - no fill, 682
  - suppress display (GANTT), 520, 550
  - suppress display (NETDRAW), 680, 755
- A\_START** variable
  - Activity data set (CPM), 71, 94, 110
  - input data set (%EVG\_WBS\_CHART), 894
  - Network data set (NETDRAW), 674, 687, 691
  - Schedule data set (CPM), 99, 100, 110, 111, 190
  - Schedule data set (GANTT), 500, 508, 525, 526, 601
- attitudes toward risk, 388
- Automatic Text Annotation, *see* labeled Gantt charts, 526, 552–556
- auxiliary resources
  - CPM procedure, 127
  - example (CPM), 289, 293
- axis
  - activity (GANTT), 485, 537
  - time (GANTT), 485, 503, 504, 506, 507, 512, 529, 530, 537
- BAC**, 848, 868, 878, 896, 899
- baseline bar
  - height, 511
  - offset, 511
- baseline schedule
  - comparing, 74, 109, 223
  - fill pattern for (GANTT), 537
  - GANTT procedure, 525, 558
  - measuring project progress, example (GANTT), 600
  - PM window, 319, 321
  - setting, 74, 75, 188
  - specifying, 74, 75, 109
  - updating, 75
- baseline schedule
  - treatment of SEGMT\_NO variable (GANTT), 558
- BCWP**, 41
- BCWS**, 41
- B\_FINISH** variable

- Activity data set (CPM), 74
- Schedule data set (CPM), 75, 188
- Schedule data set (GANTT), 500, 508, 525, 526, 601
- break and shift information
  - defining, 497, 499, 501
  - discussion, CPM procedure, 101–105, 109
  - displaying, 501, 504, 531
- B\_START variable
  - Activity data set (CPM), 74
  - Schedule data set (CPM), 75, 188
  - Schedule data set (GANTT), 500, 508, 525, 526, 601
- BY processing
  - example (GANTT), 610, 613
  - GANTT procedure, 528
- BY variables
  - Schedule data set (GANTT), 499, 526, 610
- C/SCSC, 45
- \_CAL\_variable, *see* CALID variable, *see* CALID variable
  - Activity data set (CPM), 75
  - calendar data set (%EVA\_EARNED\_VALUE), 884
  - calendar data set (%EVA\_PLANNED\_VALUE), 882
  - calendar data set (%EVA\_TASK\_METRICS), 888
  - Calendar data set (CPM), 75
  - Holiday data set (CPM), 75
  - Resource Schedule data set (CPM), 81
  - Schedule data set (GANTT), 501
- calculations, 898
- Calendar data set
  - calendars example (CPM), 103
  - CPM procedure, 55, 65, 101, 103, 168, 172
  - GANTT procedure, 486, 497, 530, 531
  - missing values, 137
  - %MSPTOSAS macro, 357
  - %SASTOMSP macro, 357
  - treatment of CALID variable, 501, 530
  - variables, 135
- calendar data set
  - variables, 882, 884, 888
- calendar information, *see* Calendar data set
  - lag dialog box, 318
  - PM window, 322
  - pop-up menu, 312
  - Table View, 312
- calendars, *see* Calendar data set, *see* Holiday data set, *see* holidays, *see* multiple calendars and holidays, *see* Workday data set
  - associated with activity, 59
- default, CPM procedure, 102
- discussion, 101–105, 109
- in Usage data set, 128
- length of workday (CPM), 66, 94, 102, 103
- multiple calendars, 101–105, 109
- start of workday (CPM), 66, 94, 102
- work shifts, 102
- work unit specification (CPM), 67
- CALID variable
  - Activity data set (CPM), 75, 101, 102
  - Calendar data set (CPM), 75, 101–104
  - Calendar data set (GANTT), 501, 530
  - example (CPM), 175, 179
  - Holiday data set (CPM), 75, 101, 102, 104, 105
  - Holiday data set (GANTT), 501, 530
  - Schedule data set (GANTT), 501, 530
- \_CALID variable
  - %SASTOMSP macro parameters, 362
- center
  - ID variables (NETDRAW), 680
  - turning off vertical (NETDRAW), 683, 691, 718
- certain equivalent
  - calculation, 426
  - DTREE procedure, 399, 423, 424
  - exponential utility function, 424
- chance nodes
  - character, 408
  - color, 403, 408
  - font, 408
  - height, 408
  - symbol, 409
- chance stage
  - decision tree model, 382
  - outcomes, 382
  - probabilities, 382
- character specification, *see* symbol specification
  - chance nodes (DTREE), 408
  - decision nodes (DTREE), 408
  - end nodes (DTREE), 409
- chart format
  - controlling, 529
- chart outlines and dividers, 507
- CHART variables, 499
  - example (GANTT), 582
  - project management symbols, 545
  - Schedule data set (GANTT), 499, 509, 526, 558
  - SYMBOL statements and, 541
- chart width, 512
- charts
  - %EVG\_COST\_PLOT macro, 876, 908, 927
  - %EVG\_GANTT\_CHART macro, 874, 912, 931
  - %EVG\_INDEX\_PLOT macro, 875, 910, 928
  - %EVG\_SCHEDULE\_PLOT macro, 877, 909, 928

- %EVG\_VARIANCE\_PLOT macro, 873, 911, 929
- %EVG\_WBS\_CHART macro, 853, 914
- GANTT procedure, 855
- CIRCLE, special symbol table
  - DTREE procedure, 409
- \_CLABEL variable
  - Label data set (GANTT), 555, 556
- clip labels
  - labeling facility (GANTT), 517
- collapse supertasks
  - Table View, 312
- color specification
  - activity text (GANTT), 513
  - arcs (NETDRAW), 679, 680
  - axis (NETDRAW), 679, 680
  - break lines along time axis (NETDRAW), 679, 681
  - chance nodes (DTREE), 403, 408
  - connect line (GANTT), 512
  - critical arcs (NETDRAW), 679, 680
  - decision nodes (DTREE), 404, 408
  - end nodes (DTREE), 404, 409
  - frame fill (GANTT), 512
  - links of optimal decisions (DTREE), 403, 406
  - links on decision tree (DTREE), 403, 406
  - milestone (GANTT), 512
  - nodes (NETDRAW), 698, 701
  - outline for all nodes (NETDRAW), 681
  - outline for critical nodes (NETDRAW), 680
  - precedence connections (GANTT), 513
  - reference lines (GANTT), 513
  - reference lines (NETDRAW), 679, 681
  - symbol (DTREE), 403, 404, 408, 409
  - text (DTREE), 404
  - text (GANTT), 513
  - text (NETDRAW), 681
  - time axis (GANTT), 512
  - timenow line (GANTT), 514
  - zone line (GANTT), 514
- column headings
  - splitting, 498
- column, change order
  - Table View, 311
- column, change width
  - Table View, 311
- common working calendar, 87
- comparison of schedules, 74
- compress in graphics mode
  - decision tree diagram, 403, 454
  - Gantt chart, 512, 522, 585
  - network diagram, 664, 680, 683, 718
- computer resource requirements
  - CPM procedure, 68, 139
  - DTREE procedure, 435
- GANTT procedure, 561
- NETDRAW procedure, 703
- concatenate early, late, and actual schedule bars, 501, 558
  - example (GANTT), 603
- conditional probability, 382
- connect line, 503
  - character for drawing, 508
  - color, 512
  - line style, 518
- consumable resource, 115
- contract bidding decision problem, 452
- convert Microsoft Project data to SAS code, 51
- coordinate system
  - annotate processing (GANTT), 537
  - annotate processing (NETDRAW), 701
- copy activities
  - PM window, 320
- corners, rectangular
  - decision tree diagram, 408
  - network diagram, 683
- corners, rounded
  - decision tree diagram, 408
  - network diagram, 683
- corporate risk tolerance, 425
  - assessing, 425
  - estimating, 425
- COST variables, *see* REWARD variables
- COST= option, *see* REWARD= option
- costs
  - specifying, 858, 862, 871, 880, 881, 883, 884, 887, 888, 903–905, 908, 916, 917, 920, 924
- CPI, 846, 847, 868, 875, 893, 896, 898–900, 910, 928
- \_CPI\_variable
  - periodic data set (%EVA\_METRICS), 898
  - task data set (%EVA\_TASK\_METRICS), 900
- CPM, *see* critical path method
- CPM examples, 854, 861
  - activity splitting, 225
  - Activity-on-Arc format, 146
  - Activity-on-Node format, 142
  - alternate resources, 230
  - analyzing resource delay, 197
  - auxiliary resources, 289, 293
  - basic project schedule, 140
  - changing length of workday, 159
  - changing start of workday, 159
  - course scheduling, 241
  - finish milestone, 278
  - incorporating actual schedule, 188
  - infeasibility diagnostics, 211
  - meeting project deadlines, 149
  - multiproject scheduling, 245
  - negative resource requirements, 286, 289, 293

- nonstandard precedence constraints, 181
- PERT analysis, 238
- resource calendars, 255, 293
- resource-driven durations, 255, 293
- resource-constrained scheduling, 197
- saving a target schedule, 188
- scheduling around holidays, 161
- scheduling courses, 241
- scheduling only on weekdays, 155
- scheduling over nonstandard day and week, 167, 172
- setting activity delay, 217
- setting project finish date, 149
- setting project start date, 143
- substitutable resources, 230
- summarizing resources used by project, 193
- supplementary resources, 207
- time-constrained scheduling, 186
- TIMENOW option, 188
- use of PROC CALENDAR to print schedule, 151
- CPM procedure**
  - Activity data set, 66, 487
  - Activity-on-Arc, 56
  - Activity-on-Node, 57
  - actual schedule, 70
  - add activity records, 65
  - alternate resources, 123
  - auxiliary resources, 127
  - baseline schedules, 109
  - Calendar data set, 65, 101, 103
  - computer resource requirements, 68, 139
  - default calendar, 102
  - definitions of Schedule data set variables, 99–101
  - details, 92
  - duration specification, 94
  - finish milestone, 98, 99
  - float times, 93
  - formatting details, 139
  - functional summary, 61
  - Holiday data set, 67, 101, 104, 105
  - input data sets, 135
  - missing values, treatment of, 137
  - multiple alternates, 125
  - multiple calendars, 101–105, 109
  - multiproject scheduling, 131–134
  - negative resource requirements, 119
  - options classified by function, 61
  - output data sets, 99, 127, 131
  - overview, 10, 55
  - precedence relationships, 95, 96
  - progress updating, 109–112
  - progress variables, 70, 110, 111
  - random activity durations, 240
  - resource allocation, 113, 114, 116–125, 128–131
  - Resource data set, 68, 114
  - resource-driven durations, 126
  - Resource Schedule data set, 69
  - resource usage, 129
  - SAS date, time, and datetime values, 66, 94, 95, 105, 139
  - Schedule data set, 68, 99–101
  - scheduling subject to precedence constraints, 93, 94
  - serial-parallel scheduling method, 119, 120
  - specifying resource requirements, 118, 119
  - syntax skeleton, 61
  - table of syntax elements, 61
  - target schedules, 109
  - time-constrained scheduling, 96, 97
  - Usage data set, 69
  - variables, 99, 135
  - Workday data set, 70, 101, 102
- CPM procedure**
  - macro variable \_ORCPM\_, 134
  - \_ORCPM\_ macro variable, 11
- CPU requirement**, *see* computer resource requirements, *see also* computer resource requirements
- critical activities**
  - CPM procedure, 58, 59, 93, 97, 101
  - fill pattern for duration of (GANTT), 537
  - GANTT procedure, 501, 508
  - node pattern (NETDRAW), 701
  - status flags to indicate, 570
- critical path**, 93, 101
- critical path method**, 56
- critical path method (CPM)**, 58
- cumulative resource usage, 82
- cumulative reward, 421
  - on decision tree diagram, 400, 401, 413
  - optimal decision summary, 401
- current time**, *see* TIMENOW
- CV**, 846, 848, 849, 868, 873, 874, 893, 895, 898, 911, 929, 931
- CV percentage**, 895
- \_CV\_variable**
  - periodic data set (%EVA\_METRICS), 898
  - task data set (%EVA\_TASK\_METRICS), 900
- \_CVP\_variable**
  - task data set (%EVA\_TASK\_METRICS), 900
- cycles**
  - definition, CPM procedure, 94
  - in network diagrams, 663, 695, 745
- data flow**
  - between procedures, 10, 14
  - CPM procedure, 11
  - DTREE procedure, 17
  - GANTT procedure, 12

- NETDRAW procedure, 13
- PM procedure, 13
- data sets, *see also* SAS data sets, *see* SAS data sets
- data storage requirements, *see* computer resource requirements
- \_DATE variable
  - %SASTOMSP macro parameters, 362
- day
  - length of, 66, 94, 102, 103, 160, 501, 531
  - start of, 66, 94, 102, 103, 160, 501, 531
- \_DAYLENGTH variable
  - %SASTOMSP macro parameters, 362
- \_DAYSTART variable
  - %SASTOMSP macro parameters, 362
- deadlines, *see* milestones
  - finish-before date, 66
- decision analysis
  - example, 47
  - introduction, 16
- decision criterion, 399
  - specifying, 389
- decision model, *see* decision tree model
- decision nodes
  - character, 408
  - color, 404, 408
  - font, 408
  - height, 408
  - symbol, 409
- decision stage
  - decision tree model, 382
  - outcomes, 382
- decision support systems, 16
- decision tree diagram
  - cumulative reward, 400, 413
  - displaying, 383, 387, 413, 423, 427
  - drawing on one page, 403, 454
  - evaluating value, 400, 413
  - graphics version, 429
  - information displayed, 400, 414
  - labels, 400, 414
  - line-printer version, 429
  - number of pages, 428
  - outcome name, 400, 413
  - page format, 427
  - probability, 400, 413
  - reward, 400, 413
  - stage name, 400, 413
- decision tree model, 382
  - difference between rewards and payoffs, 419
  - evaluating, 383, 387
  - modifying, 383
  - outcomes, 382
  - recalling, 383, 412
  - representing, 401
- saving, 383, 413, 423
- scenario, 413
- stages, 382
- default calendar
  - CPM procedure, 75, 102, 175
  - GANTT procedure, 530
- default data set name
  - CHART, 893
  - EV, 883, 885
  - METRICS, 885, 889–892
  - PLOT, 890–892
  - PV, 881, 885
  - SUMMARY, 886, 890, 891
  - TASKMETS, 888, 893
  - TASKPV, 882, 884
- default variable name
  - \_CAL\_, 882, 884, 888
  - WBS\_CODE, 888
- delay diagnostics, *see* activity delay
- DELAY\_R variable
  - Schedule data set (CPM), 82, 99, 200
- delete activities
  - PM window, 321
- delete duplicate observations, 66
- delete precedence constraints
  - PM window, 321
- delete tasks
  - Table View (PM), 310
- diagnose resource infeasibilities, *see* infeasibility
  - diagnostics
- diagrams
  - NETDRAW procedure, 853
- dialog box
  - edit lag, 308, 318
  - edit lag calendar, 318
  - task information, 309
- discount rate
  - example (DTREE), 471
- display
  - information in decision tree diagram, 400, 413
  - information in network diagram, 690
  - schedule bar, Gantt View, 315
  - task information, Gantt View, 315
- displayed output
  - DTREE procedure, 426
  - GANTT procedure, 558
  - NETDRAW procedure, 690
- dividers and outlines
  - Gantt chart, 507
- D\_LENGTH variable
  - Calendar data set (CPM), 103
- DOT, special symbol table
  - DTREE procedure, 409

- draw and display networks, *see* network layout,  
NETDRAW procedure
- drill-down Gantt charts  
graphics example (GANTT), 646
- DTREE examples, 435  
contract bidding decision problem, 452  
loan grant decision problem, 461  
oil wildcatter's decision problem, 436, 441  
petroleum distributor's decision problem, 471  
research and development decision problem, 457
- DTREE procedure  
computer resource requirements, 435  
displayed output, 426  
displaying decision tree, 427  
error handling, 434  
evaluating decision tree, 423  
functional summary, 396  
general options, 399–402  
graphics options, 403–409  
Imagemap data set, 406, 431  
input data sets, 418  
interactivity, 422  
line-printer options, 410  
missing values, 421  
ODS style template, 432  
ODS table names, 432  
options classified by function, 396  
output data sets, 383  
Output Delivery System (ODS), 383  
overview, 17, 382  
syntax skeleton, 395  
table of syntax elements, 396  
terminating, 383, 412, 422  
variables, 415–417
- duplicate ID values, 502, 524
- duplicate observations  
deleting (CPM), 66
- DUR variable  
%SASTOMSP macro parameters, 362
- DUR\_ variable, *see* DURATION variable, *see* DURATION variable  
Resource Schedule data set (CPM), 131  
Schedule data set (GANTT), 502
- duration  
calculated, 76  
estimates of, 238  
multiplier, CPM procedure, 67  
resource-driven, 90, 99, 112  
specification, CPM procedure, 76, 94  
units, CPM procedure, 59, 67, 94, 155
- DURATION variable  
Activity data set (CPM), 76, 112, 113  
Network data set (NETDRAW), 674  
Schedule data set (GANTT), 502, 528
- DUR\_TYPE variable  
Resource Schedule data set (CPM), 131
- dynamic programming algorithm, 674, 690, 730
- EAC, 896  
CPI, 868, 877, 885, 896, 899  
CPI-times-SPI, 868, 877, 885, 896, 899  
OTD, 868, 877, 885, 896, 899  
revised, 864, 868, 876, 877, 885, 896, 898, 899, 908
- \_EACREV\_ variable  
periodic data set (%EVA\_METRICS), 898
- early bar  
height, 514  
offset, 514
- early schedule  
GANTT procedure, 525, 558
- early start schedule computation, *see* schedule computation
- earned value, 846, 847, 862, 868, 869, 876, 878, 897, 898, 900
- Earned Value Analysis, 45
- earned value analysis, 845
- earned value macros  
introduction, 52
- edit  
alignment constraints, Table View, 311  
calendars, Table View, 312  
durations, Gantt View, 317  
durations, PM window, 320  
durations, Table View, 311  
lag, Gantt View, 318  
project, PM procedure, 318
- E\_FINISH variable  
input data set (%EVG\_WBS\_CHART), 894  
Network data set (NETDRAW), 674, 687, 691  
Schedule data set (CPM), 59, 83, 93, 99, 100  
Schedule data set (GANTT), 502, 508, 525, 526, 528, 607
- EFINMILE variable  
Schedule data set (CPM), 99
- end nodes  
character, 409  
color, 404, 409  
font, 409  
height, 409  
symbol, 409
- end stage  
decision tree model, 382
- equity  
estimating corporate risk tolerance, 425
- errors  
CPM procedure, 134, 137  
DTREE procedure, 400, 420–423, 435

- GANTT procedure, 526, 559
- NETDRAW procedure, 702
- ES\_ASC variable
  - Schedule data set (CPM), 78
- ES\_DESC variable
  - Schedule data set (CPM), 78
- E\_START variable
  - input data set (%EVG\_WBS\_CHART), 894
  - Network data set (NETDRAW), 674, 687, 691
  - Schedule data set (CPM), 59, 83, 93, 97, 99, 100
  - Schedule data set (GANTT), 502, 508, 525, 526, 607
- estimates
  - cost, 864, 866, 868, 876, 885, 896, 898, 908, 924, 927
  - schedule, 877, 909, 928
- ETC, 868, 896, 899
- CPI, 896
- CPI-times-SPI, 896
- OTD, 896
- revised, 896
- \_EV\_variable
  - periodic data set (%EVA\_METRICS), 898
  - task data set (%EVA\_TASK\_METRICS), 900
- \_EV\_RATE\_variable
  - periodic data set (%EVA\_EARNED\_VALUE), 897
- %EVA\_EARNED\_VALUE examples, 862, 905, 920
- %EVA\_EARNED\_VALUE macro
  - macro variable \_EVA\_EARNED\_VALUE\_, 897
- \_EVA\_EARNED\_VALUE macro variable, 897
- %EVA\_METRICS examples, 866, 906, 922
- %EVA\_METRICS macro
  - macro variable \_EVA\_METRICS\_, 899
- \_EVA\_METRICS macro variable, 899
- %EVA\_PLANNED\_VALUE examples, 858, 904, 917
- %EVA\_PLANNED\_VALUE macro
  - macro variable \_EVA\_PLANNED\_VALUE\_, 897
- \_EVA\_PLANNED\_VALUE macro variable, 897
- %EVA\_TASK\_METRICS examples, 871, 908, 924
- %EVA\_TASK\_METRICS macro
  - macro variable \_EVA\_TASK\_METRICS\_, 900
- \_EVA\_TASK\_METRICS macro variable, 900
- evaluating value
  - decision tree diagram, 401
  - DTREE procedure, 417, 424
  - on decision tree diagram, 400, 413
  - on optimal decision summary, 401
  - optimal, 411
  - represented with Payoff data set (DTREE), 401
    - selecting the best alternative, 426
- \_EVEN variables, *see* EVENT variables
  - Probability data set (DTREE), 416
- EVENT variables
  - Probability data set (DTREE), 416
- events, 382
- %EVG\_COST\_PLOT examples, 876, 908, 927
- %EVG\_COST\_PLOT macro
  - macro variable \_EVG\_COST\_PLOT\_, 900
- \_EVG\_COST\_PLOT macro variable, 900
- %EVG\_GANTT\_CHART examples, 874, 912, 930
- %EVG\_GANTT\_CHART macro
  - macro variable \_EVG\_GANTT\_CHART\_, 902
- \_EVG\_GANTT\_CHART macro variable, 902
- %EVG\_INDEX\_PLOT examples, 875, 910, 928
- %EVG\_INDEX\_PLOT macro
  - macro variable \_EVG\_INDEX\_PLOT\_, 901
- \_EVG\_INDEX\_PLOT macro variable, 901
- %EVG\_SCHEDULE\_PLOT examples, 877, 909, 928
- %EVG\_SCHEDULE\_PLOT macro
  - macro variable \_EVG\_SCHEDULE\_PLOT\_, 901
- \_EVG\_SCHEDULE\_PLOT macro variable, 901
- %EVG\_VARIANCE\_PLOT examples, 873, 911, 929
- %EVG\_VARIANCE\_PLOT macro
  - macro variable \_EVG\_VARIANCE\_PLOT\_, 901
- \_EVG\_VARIANCE\_PLOT macro variable, 901
- %EVG\_WBS\_CHART examples, 853, 914
- %EVG\_WBS\_CHART macro
  - macro variable \_EVG\_WBS\_CHART\_, 902
- \_EVG\_WBS\_CHART macro variable, 902
- examples, *see also* CPM examples, *see also* DTREE
  - examples, *see also* GANTT examples, *see also* introductory examples, *see also* NETDRAW examples, *see also* PM examples, *see* CPM examples, *see* DTREE examples
- %EVA\_EARNED\_VALUE macro, 862, 905, 920
- %EVA\_METRICS macro, 866, 906, 922
- %EVA\_PLANNED\_VALUE macro, 858, 904, 917
- %EVA\_TASK\_METRICS macro, 871, 908, 924
- %EVG\_COST\_PLOT macro, 876, 908, 927
- %EVG\_GANTT\_CHART macro, 874, 912, 930
- %EVG\_INDEX\_PLOT macro, 875, 910, 928
- %EVG\_SCHEDULE\_PLOT macro, 877, 909, 928
- %EVG\_VARIANCE\_PLOT macro, 873, 911, 929
- %EVG\_WBS\_CHART macro, 853, 914
- CPM procedure, 854, 861
- earned value analysis, 845, 851, 902, 913
- GANTT chart, 855
- GANTT procedure, 855
- NETDRAW procedure, 852
- statement and option cross-reference tables (CPM), 298–300
- statement and option cross-reference tables (DTREE), 480

- statement and option cross-reference tables (GANTT), 658–660
- statement and option cross-reference tables (NETDRAW), 770
- expand supertasks
  - Table View, 312
- expected utility, DTREE procedure, 423
- expected value, DTREE procedure, 423, 424
- exponential utility function
  - DTREE procedure, 388, 400, 424, 426
  - example (DTREE), 440
- \_FBDAT**E variable
  - %SASTOMSP macro parameters, 362
- F\_FLOAT** variable
  - input data set (%EVG\_WBS\_CHART), 894
  - Network data set (NETDRAW), 674, 687, 691
  - Schedule data set (CPM), 59, 83, 99, 100
- fill patterns
  - limiting PATTERN variable to specific schedules, 521
  - suppress using PATTERN variable (GANTT), 520
  - using PATTERN variable (GANTT), 521, 536, 537
- filling page area, 503, 528, 570
- filters, 322
- financial decisions, *see* loan grant decision problem
- finish-before date
  - CPM procedure, 66
- finish milestone
  - CPM procedure, 98, 99
  - example (CPM), 278
- finish times
  - computation of, CPM procedure, 93
  - format of, 526
  - interpretation of, CPM procedure, 94
  - padding, 526
  - treatment of, 526
- FINISH** variable
  - Activity data set (CPM), 76
- \_FLABEL** variable
  - Label data set (GANTT), 555, 556
- flags
  - activity status, 501, 559
- float
  - free, 59, 93, 100
  - total, 59, 93, 101
- font baseline of activity text, 516, 536
- font specification, *see* symbol specification
  - baseline of activity text (GANTT), 516
  - chance nodes (DTREE), 408
  - decision nodes (DTREE), 408
  - end nodes (DTREE), 409
  - milestones (GANTT), 514
- symbol (DTREE), 408, 409
- text (DTREE), 405
- text (GANTT), 514
- text (NETDRAW), 681
- font, hardware
  - for text on decision tree, 405
- fonts for Gantt charts
  - ORFONT (filled), 543
  - ORFONTE (empty), 543, 545
- fonts for project management and decision analysis, 543
- forced finish, *see* time constraints
- forced start, *see* time constraints
- forecasts
  - cost, 864, 866, 868, 876, 896, 898, 908, 927
  - schedule, 877, 909, 928
- format control options
  - DTREE procedure, 401, 428
  - GANTT procedure, 529
  - NETDRAW procedure, 674, 676–678, 690, 692
- formatting
  - details, CPM procedure, 139
  - numerical values on decision tree diagram, 401
  - outcome names on decision tree diagram, 401
  - time axis (GANTT), 507
- formulas, 898
- frame fill
  - color, 512
- framing chart
  - suppress, 520
- free float, *see* float
- \_FRI** variable
  - Calendar data set (CPM), 103
- \_FROM** variable
  - Layout data set (NETDRAW), 692, 693
  - Network data set (NETDRAW), 673
- full-screen version
  - changing the scale (NETDRAW), 697
  - differences with line-printer version (GANTT), 531
  - GANTT procedure, 497, 531
  - global commands (GANTT), 534
  - global commands (NETDRAW), 700
  - local commands (GANTT), 532
  - local commands (NETDRAW), 698
  - modifying the network layout, 693
  - NETDRAW procedure, 697, 698, 700
  - options specific to (GANTT), 507
  - options specific to (NETDRAW), 672, 678, 679
  - output format, 532
  - routing images to a file, 534
  - routing images to a printer, 535
  - use of the PATTERN variable (NETDRAW), 698
- functional summary

- CPM procedure, 61
- DTREE procedure, 396
- GANTT procedure, 492
- NETDRAW procedure, 668
- future certain equivalent value, *see* evaluating value
- future funds
  - example (DTREE), 471
- F\_VAR variable
  - Schedule data set (CPM), 74, 190, 223
- GANTT charts, 855, 874
- Gantt charts, 485
- GANTT examples, 566, 855
  - activity filtering, 613
  - actual schedule, 598
  - annotate facility (graphics), 631
  - BY processing, 610
  - compressing chart to fit on one page (graphics), 585
  - concatenating early, late, and actual schedules, 603
  - customizing the Gantt chart, 570
  - direct specification of schedule data, 606
  - drawing Gantt charts by resource usage, 613
  - drawing Gantt charts by task code, 610
  - drill-down Gantt charts (graphics), 646
  - fitting the chart on one page (graphics), 585
  - graphics mode, 575
  - height and placement of text (graphics), 617
  - holidays in scheduling, 576
  - introductory, 487
  - labeled Gantt charts (graphics), 636
  - layout controls for Logic Gantt charts (graphics), 621
  - line-printer mode, 566
  - Logic Gantt chart, AOA representation (graphics), 621
  - Logic Gantt chart, AON representation (graphics), 619
  - Logic Gantt charts, layout control (graphics), 621
  - milestones and special dates, 582
  - monitoring project progress against a baseline schedule, 600
  - multiple calendars, 595
  - multiproject Gantt charts (graphics), 638
  - multisegment Gantt charts (graphics), 641
  - nonstandard precedence relationships, 628
  - printing a Gantt chart, 566
  - resource-constrained schedule, 604
  - smallest identifiable time unit, 586
  - statement and option cross-reference tables, 658–660
  - time axis, altering range (graphics), 590
  - variable length holidays, 592
- Web-enabled Gantt charts (graphics), 646
- zoned Gantt charts (graphics), 645
- GANTT procedure
  - activity axis, 485, 537
  - Annotate data set, 486, 496, 510, 537
  - annotate processing, 537
  - automatic text annotation, 486
  - Calendar data set, 486, 497, 501, 530, 531
  - computer resource requirements, 561
  - coordinate systems in annotate processing, 537
  - data storage requirements, 561
  - description of, 484
  - direct input of schedule data, 606
  - displayed output, 558
  - functional summary, 492
  - graphics examples, 575
  - Holiday data set, 486, 497, 530, 531
  - holidays in scheduling, 497, 503, 530, 576, 599
  - HTML Imagemap data set, 498
  - Imagemap data set, 487, 498, 556
  - input data sets, 486
  - justification, 511, 518, 522, 523
  - Label data set, 486, 498
  - labeling, 486
  - line-printer examples, 566
  - macro variable \_ORGANTT, 516
  - memory requirements, 561
  - missing value handling, 526
  - nonstandard precedence relationships, 486, 487, 545, 546, 548–550
  - ODS style template, 561
  - options classified by function, 492
  - ORFONT font, 543
  - ORFONTE font, 543, 545
  - \_ORGANTT macro variable, 516
  - output, 558
  - overview, 11, 484
  - Precedence data set, 486, 498, 526, 546
  - precedence relationships, 486, 487, 545–551
  - Schedule data set, 486, 487, 497, 525, 546, 558
  - scheduling holidays, 576
  - table of syntax elements, 492
  - time axis, 485, 529, 537
  - variables, 526
  - Workday data set, 486, 497, 499, 530, 531
  - GANTT procedure
    - macro variable \_ORGANTT, 523, 559
    - \_ORGANTT macro variable, 12, 523, 559
  - Gantt View, 313
    - alignment constraints, 316
    - display schedule bar, 315
    - display task information, 315
    - edit durations, 317
    - edit lag, 318

- hide schedule bar, 315
- lag calendar, 318
- nonstandard precedence relationships, 317, 319, 321
- PM procedure, 313
- PM window, 313
- progress information, 318
- time axis format, 314
- time axis units, 315
- time increment, 314
- time scale, 315
- general options
  - DTREE procedure, 399–402
  - GANTT procedure, 499
  - NETDRAW procedure, 673–678
- \_GIVE variables, *see* GIVEN variables
  - Probability data set (DTREE), 416
- GIVEN variables
  - Probability data set (DTREE), 416
- global commands
  - full-screen version (GANTT), 534
  - full-screen version (NETDRAW), 700
- global graphics options
  - color of symbol, 403, 404
  - color of text, 404
  - controlling the appearance of decision tree, 429, 457
  - font of text, 405
  - height, 405
  - number of columns, 429
  - number of rows, 429
  - unit of measure, 402
- global options
  - DTREE procedure, 422
- global verticals, *see* Logic Gantt charts, 519, 548
- graphics catalog
  - DTREE procedure, 405
  - GANTT procedure, 497
  - NETDRAW procedure, 672
  - segment description (GANTT), 514
  - segment description (NETDRAW), 681
  - segment name (GANTT), 520
  - segment name (NETDRAW), 682
- graphics version
  - activity text placement (GANTT), 515, 516
  - effects of HPOS and VPOS, 535
  - example (DTREE), 452
  - examples (GANTT), 575
  - fitting Gantt chart on a single page, 512, 522, 535
  - formatting the chart, 535
  - GANTT procedure, 497, 535
  - introductory example (GANTT), 489
  - NETDRAW procedure, 700–702
  - options specific to (DTREE), 403–409
- options specific to (GANTT), 509
- options specific to (NETDRAW), 672, 679–685
- text font baseline (GANTT), 516
- use of the PATTERN variable (NETDRAW), 701
- graphs
  - %EVG\_COST\_PLOT macro, 876, 908, 927
  - %EVG\_GANTT\_CHART macro, 874, 912, 931
  - %EVG\_INDEX\_PLOT macro, 875, 910, 928
  - %EVG\_SCHEDULE\_PLOT macro, 877, 909, 928
  - %EVG\_VARIANCE\_PLOT macro, 873, 911, 929
- hardware font
  - for text on decision tree, 405
- HEAD variable
  - Activity data set (CPM), 76
  - Schedule data set (GANTT), 515, 545
- \_HEAD variable
  - %SASTOMSP macro parameters, 362
- height specification
  - actual bar (GANTT), 510
  - baseline bar (GANTT), 511
  - chance nodes (DTREE), 408
  - decision nodes (DTREE), 408
  - early bar (GANTT), 514
  - end nodes (DTREE), 409
  - holiday bar (GANTT), 515
  - late bar (GANTT), 514
  - milestones (GANTT), 515
  - nodes on decision tree (DTREE), 405
  - resource-constrained schedule bar (GANTT), 522
  - schedule bar (GANTT), 511
  - symbol (DTREE), 405, 408, 409
  - text (DTREE), 405
  - text (GANTT), 515, 516
- hide
  - schedule bar, Gantt View, 315
  - tasks, Table View, 313
- hierarchical charts, *see* organizational charts
- \_HLABEL variable
  - Label data set (GANTT), 555, 556
- holiday bar
  - height, 515
  - offset, 515
- Holiday data set
  - CPM procedure, 55, 67, 77, 101, 104, 105, 161, 172
  - GANTT procedure, 486, 497, 530, 531
  - holidays example (CPM), 105
  - missing values, 137
  - %MSPTOSAS macro, 357
  - %SASTOMSP macro, 357
  - treatment of CALID variable, 530

- treatment of holiday related variables, 77, 503, 530
- variables, 135
- holiday information, *see* Holiday data set
- HOLIDAY variable
  - Holiday data set (CPM), 77, 104
  - Holiday data set (GANTT), 503, 530
- holidays, *see* Holiday data set
  - character to represent (GANTT), 508
  - defining, 77, 497, 530
  - displaying, 531
  - duration units, 503, 530
  - durations, 77, 503
  - examples (GANTT), 576
  - fill pattern for (GANTT), 537
  - finish times, 77, 503
  - GANTT procedure, 503
  - graphics example (GANTT), 599
  - scheduling around, 59, 530
  - start times, 77, 503
  - variable length, example (GANTT), 592
- HOLIDUR variable
  - Holiday data set (CPM), 77, 104
  - Holiday data set (GANTT), 503, 530
- \_HOLIDUR variable
  - %SASTOMSP macro parameters, 362
- \_HOLIEND variable
  - %SASTOMSP macro parameters, 362
- HOLIFIN variable
  - Holiday data set (CPM), 77, 104
  - Holiday data set (GANTT), 503, 530
- \_HOLISTART= parameter
  - %SASTOMSP macro parameters, 362
- horizontal banding, *see* zoned network diagrams
- horizontal space
  - around margin (NETDRAW), 681, 734
  - between ID columns (GANTT), 500
  - between nodes (NETDRAW), 678, 690, 728
- \_ID variable
  - %SASTOMSP macro parameters, 362
- ID variables
  - Activity data set (CPM), 78
  - column headings, 559
  - displaying as many as possible, 504
  - displaying on multiple pages, 503, 559
  - duplicate values, 502, 524, 558
  - format of (GANTT), 526
  - labels for headings, 559
  - labels, suppress displaying, 559
  - NETDRAW procedure, 690, 691
  - Network data set (NETDRAW), 674, 687, 691
  - omission of, 559
- Schedule data set (GANTT), 498, 500, 502, 524, 526, 558, 559
- space between columns, 500
- split character for labels, 498
- splitting column headings, 498
- stripping leading blanks, 506
- Imagemap data set
  - DTREE procedure, 383
  - GANTT procedure, 487
- independent resource scheduling, 84, 122
- indices
  - CPI, 846, 847, 868, 875, 893, 898–900, 910, 928
  - CV, 899, 900, 908, 912
  - SPI, 846, 847, 868, 875, 893, 898–900, 910, 928
  - SV, 899, 900, 908, 912
  - TCPI, 868, 875, 899, 910, 928
- infeasibility diagnostics
  - CPM procedure, 84, 121, 211
- input data sets, *see also* Activity data set, *see also*
  - Annotate data set, *see also* Calendar data set, *see also* Holiday data set, *see also* Label data set, *see also* Layout data set, *see also* Network data set, *see also* Payoff data set, *see also* Precedence data set, *see also* Probability data set, *see also* Resource data set, *see also* Schedule data set, *see also* Stage data set, *see also* Workday data set, *see also* Activity data set, *see also* Calendar data set, *see also* Holiday data set, *see also* Resource data set, *see also* Workday data set, *see also* Probability data set, *see also* Stage data set, *see also* Payoff data set, *see also* Annotate data set, *see also* Payoff data set, *see also* Probability data set, *see also* Stage data set, *see also* Annotate data set, *see also* Calendar data set, *see also* Holiday data set, *see also* Label data set, *see also* Precedence data set, *see also* Schedule data set, *see also* Workday data set
- CPM procedure, 11, 55, 135
- DTREE procedure, 17, 382, 383, 415, 418
- GANTT procedure, 12, 486
- NETDRAW procedure, 13, 662
- PM procedure, 14
- %SASTOMSP macro, 355, 360
- interactivity
  - DTREE procedure, 422
- \_INTERVAL variable
  - %SASTOMSP macro parameters, 363
- introductory examples
  - decision analysis, 47
  - multiple projects, 30
  - project cost control, 40
  - project definition, 18
  - project reports, 21

- resource-constrained schedule, 25
- scheduling a project, 21
- sequential scheduling of projects, 38
- summarizing project information, 23
- work breakdown structure, 20
  
- JLABEL variable
  - Label data set (GANTT), 555, 556, 637
- job axis, *see* activity axis
- job number
  - displaying on multiple pages, 559
  - suppress displaying, 505, 559
- justification
  - Gantt charts, 511, 518, 522, 523
  
- label clipping rules
  - labeling facility (GANTT), 517
- Label data set
  - GANTT procedure, 486, 498, 516, 526, 552
- label splitting
  - labeling facility (GANTT), 517
- LABEL variable
  - Label data set (GANTT), 517, 552, 555, 556
- LABEL\_ variable
  - summary data set (%EVA\_METRICS), 898
- labeled Gantt charts, 486, 516, 537, 552
  - clipping rules, 517
  - control on common tickmarks, 555
  - determining the label string, 554
  - formatting the label, 555
  - graphics example (GANTT), 636
  - justifying the strings, 555
  - positional information, 516
  - specifying character baseline angle, 555
  - specifying character rotation angle, 555
  - specifying colors, 555
  - specifying fonts, 555
  - specifying heights, 555
  - specifying placement offsets, 555
  - specifying the coordinate system, 554
  - specifying the horizontal placement position, 553
  - specifying the labels, 553
  - specifying the vertical placement position, 553
  - splitting labels, 517
  - text string information, 516
  - variables in the Label data set, 556
- labels on decision tree diagram, 401, 413
  - displaying, 400
  - suppress displaying, 400, 414
- LABVAR variable
  - Label data set (GANTT), 516, 552, 553, 556, 636, 639
  - Schedule data set (GANTT), 516, 639
- lag calendar, 318
  
- lag dialog box, 308, 318
- lag types, 90, 96, 318, 517, 545, 549
- LAG variable
  - %SASTOMSP macro parameters, 363
- LAG variables, *see* nonstandard precedence relationships
  - Activity data set (CPM), 90
  - example (CPM), 181
  - Network data set (NETDRAW), 675
  - Precedence data set (GANTT), 486, 487, 517, 546
- late bar
  - height, 514
  - offset, 514
- late schedule
  - GANTT procedure, 525, 558
- late start schedule computation, *see* schedule computation
- layout controls, *see* Logic Gantt charts, 549, *see also* network layout, NETDRAW procedure
- Layout data set
  - as input to NETDRAW procedure, 686
  - NETDRAW procedure, 662, 673, 686, 692
- legend
  - customized with Annotate data set (DTREE), 403, 459
  - GANTT procedure, 558
  - on decision tree diagram, 406
  - suppress displaying (DTREE), 406
  - suppress displaying (GANTT), 505
- L\_FINISH variable
  - input data set (%EVG\_WBS\_CHART), 894
  - Network data set (NETDRAW), 674, 687, 691
  - Schedule data set (CPM), 59, 84, 93, 99, 100
  - Schedule data set (GANTT), 504, 508, 525, 526
- LFINMILE variable
  - Schedule data set (CPM), 99
- limiting number of activities per page
  - GANTT procedure, 520
- limiting number of horizontal pages
  - GANTT procedure, 515
- limiting number of vertical pages
  - GANTT procedure, 523
- line-printer version
  - examples (GANTT), 566
  - GANTT procedure, 498
  - introductory example (GANTT), 488
  - options specific to (DTREE), 410
  - options specific to (GANTT), 507
- line style specification
  - break lines along time axis (NETDRAW), 682
  - connect lines (GANTT), 518
  - links across pages (DTREE), 406, 407
  - links of optimal decisions (DTREE), 406, 407
  - links on decision tree (DTREE), 406, 407

- precedence connections (GANTT), 518
- reference lines (GANTT), 518
- reference lines (NETDRAW), 682
- timenow line (GANTT), 518
- zone line (GANTT), 518
- line width specification
  - arcs and nodes (NETDRAW), 682
  - critical arcs and nodes (NETDRAW), 682
  - GANTT procedure, 518
  - links of optimal decisions (DTREE), 406, 407
  - links on decision tree (DTREE), 406, 407
  - node outlines (NETDRAW), 682
  - precedence connections (GANTT), 524
  - timenow line (GANTT), 524
  - zone line (GANTT), 524
- line-printer version
  - options specific to (NETDRAW), 672, 685
- linear utility function, 424
- links across pages
  - color, 406
  - style, 407
  - thickness, 406
  - type, 406, 407
- links of optimal decisions
  - color, 403, 406
  - style, 407
  - thickness, 406, 407
  - type, 406, 407
- links on decision tree
  - color, 403, 406
  - style, 407
  - thickness, 406, 407
  - type, 406, 407
- litigation decisions, *see* petroleum distributor's decision problem
- loan grant decision problem, 461
- local commands
  - full-screen version (GANTT), 532
  - full-screen version (NETDRAW), 698
- local options
  - DTREE procedure, 422
- local verticals, *see* Logic Gantt charts, 519, 549
- logic bar, 546, 549
  - graphics example (GANTT), 619, 621
- Logic Gantt charts, 545
  - 3-segment connection, 546, 548, 550
  - 5-segment connection, 546, 551
  - AOA representation, graphics example (GANTT), 621
  - AOA specification, 515, 523, 545
  - AON representation, graphics example (GANTT), 619
  - AON specification, 510, 523, 545, 546
  - arrowheads, 520, 550
- arrowheads, suppress display, 550
- controlling the layout, 548
- drawing the precedence connections, 546
- error handling, 522
- finish global vertical, 548
- finish local vertical, 549
- framing chart, suppress, 520
- global verticals, 519, 548
- global verticals, illustration of, 549
- global verticals, minimum interdistance of, 519, 549
- global verticals, minimum offset from logic bar, 519, 549
- horizontal tracks for segment placement, 549
- introductory example, 490
- lag types, 517, 546, 549
- layout controls, 519, 546, 548, 549
- linking Precedence data set and Schedule data set, 546
- local verticals, 519, 549
- local verticals, illustration of, 549
- local verticals, maximum displacement from minimum offset location, 519, 550
- local verticals, minimum offset from logic bar, 520, 550
- logic bar, 518, 546, 547, 549
- nonstandard precedence relationships, 486, 487, 545, 546, 548–550
- placement of horizontal segments, 549
- placement of vertical segments, 548, 549
- precedence connections, illustration, 547
- Precedence data set, 510, 523, 546
- Precedence data set, linking to Schedule data set, 546
- precedence information, 510, 515, 517, 518, 523, 545
- precedence information using PROC CPM, 545
- precedence relationships, 486, 487, 545–551
- routing sequence, 546
- routing the connection, 550
- Schedule data set, 546
- Schedule data set, linking to Precedence data set, 546
- start global vertical, 548
- start local vertical, 549
- time axis, extension of, 548
- time axis, suppress extension of, 520, 548
- turning points, 546, 548
- vertical tracks for segment placement, 548, 549
- Logic options, 526, 545
- loop, *see* cycles
- LOSS variables, *see* VALUE variables
- LS\_ASC variable
  - Schedule data set (CPM), 78, 79

LS\_DESC variable  
     Schedule data set (CPM), 78

L\_START variable  
     input data set (%EVG\_WBS\_CHART), 894  
     Network data set (NETDRAW), 674, 687, 691  
     Schedule data set (CPM), 59, 84, 93, 97, 99, 100  
     Schedule data set (GANTT), 504, 508, 525, 526

\_LVAR variable  
     Label data set (GANTT), 517, 552, 555, 556

machine epsilon, 402

macro data flow  
     %EVA\_EARNED\_VALUE, 846, 879  
     %EVA\_METRICS, 846, 879  
     %EVA\_PLANNED\_VALUE, 846, 879  
     %EVA\_TASK\_METRICS, 846, 879  
     %EVG\_COST\_PLOT, 847  
     %EVG\_GANTT\_CHART, 849  
     %EVG\_INDEX\_PLOT, 847  
     %EVG\_SCHEDULE\_PLOT, 848  
     %EVG\_VARIANCE\_PLOT, 848  
     %EVG\_WBS\_CHART, 850

macro variable  
     TIMENOW, 326

macro variable  
     \_EVA\_EARNED\_VALUE\_, 897  
     \_EVA\_METRICS\_, 899  
     \_EVA\_PLANNED\_VALUE\_, 897  
     \_EVA\_TASK\_METRICS\_, 900  
     \_EVG\_COST\_PLOT\_, 900  
     \_EVG\_GANTT\_CHART\_, 902  
     \_EVG\_INDEX\_PLOT\_, 901  
     \_EVG\_SCHEDULE\_PLOT\_, 901  
     \_EVG\_VARIANCE\_PLOT\_, 901  
     \_EVG\_WBS\_CHART\_, 902  
     \_ORCPM\_, 134  
     \_ORGANTT, 516, 523, 559  
     \_ORNETDR, 702

mandatory time constraints, *see* time constraints

maximum allowable text height (GANTT), 515

maximum number of observations (CPM), 85

MAXNSEGMT variable  
     Activity data set (CPM), 84

memory requirements, *see* computer resource requirements

menu  
     edit, 318

menu systems for project management, 50

Microsoft Project  
     converting to PM, 51

Microsoft Project conversion macros  
     callpm.sas file, 356  
     examples, 364  
     exporting calendars and holidays, 373

exporting data set and variable names, 372

exporting resource-constrained schedules, 376

exporting to Microsoft Project, 359

importing activity attributes, 366

importing Microsoft Project files, 354

importing multiple projects, 368

importing xml files, 369

MSPOUT library reference, 354

%MSPTOSAS, 354

overview, 353

round trip between SAS and Microsoft Project, 378

running on UNIX, 355, 363

%SASTOMSP, 359

simple %MSPTOSAS conversion, 365

simple %SASTOMSP conversion, 370

milestones, 502, 528  
     character to represent, 508  
     color, 512  
     examples (GANTT), 582  
     font, 514  
     height, 515  
     PM window, 321  
     project management symbols, 545  
     set finish (CPM), 69  
     symbol value, 523

MINSEGMTDUR variable  
     Activity data set (CPM), 85

missing values  
     CPM procedure, 137  
     DTREE procedure, 421, 422  
     GANTT procedure, 526  
     NETDRAW procedure, 688

mode specific differences, 557  
     graphics options, 557  
     line-printer and full-screen options, 557

\_MON\_variable  
     Calendar data set (CPM), 103

most likely value, DTREE procedure, 423

move tasks  
     Table View, 313

%MSPTOSAS macro parameters  
     MAPFILE= parameter, 354  
     MDBFILE= parameter, 354  
     XMLFILE= parameter, 354

multiple alternates  
     CPM procedure, 85, 125

multiple calendars and holidays  
     common working calendar, 87  
     CPM procedure, 101–105, 109  
     example (CPM), 172  
     example (GANTT), 595  
     GANTT procedure, 530  
     scheduling during common working times, 87

- syntax differences between PROC CPM and PROC GANTT, 530
- multiple pages
  - displaying decision tree diagram, 427
  - GANTT procedure, 528
  - NETDRAW procedure, 691
- multiproject Gantt charts
  - graphics example (GANTT), 638
- multiproject scheduling, 131–134
  - example (CPM), 245
  - introductory example, 30
  - sequential scheduling example, 38
- multisegment Gantt charts
  - graphics example (GANTT), 641
- \_NAME\_ variable
  - summary data set (%EVA\_METRICS), 898
- negative float, 508
- negative requirements
  - specifying, CPM procedure, 119
- negative resource requirements
  - example (CPM), 286, 289, 293
- negative slack duration, 508
- net income
  - estimating corporate risk tolerance, 425
- net present value, 474
- net sales
  - estimating corporate risk tolerance, 425
- NETDRAW examples, 852
  - branch and bound trees, 765
  - compressing graphics version to fit on a page, 718
  - controlling information within nodes, 721
  - controlling the number of pages, 721
  - controlling the routing of the arcs, 728
  - displaying status of the activities, 731
  - drawing an AOA network using the Annotate facility, 761
  - drawing organizational charts, 755
  - drawing schematic diagrams, 742
  - graphics version, 713
  - illustrating data flow, 742
  - illustrating several time-scale options, 738
  - illustrating the Annotate facility, 758
  - line-printer version, 708
  - modifying network layout, 748
  - nonstandard precedence relationships, 726
  - spanning several pages, 714
  - specifying node layout through the Network data set, 753
  - time-scaled network diagram, 734
  - zoned network diagram, 741
- NETDRAW procedure
  - Annotate data set, 672, 679
  - Annotate facility, 701, 702
- arc layout options, 674, 676–678
- arc routing, 688, 689
- backward arcs in networks, 695
- computer resource requirements, 703
- controlling the network layout, 693
- cyclic networks, 663, 689, 695
- default ID variables, 690
- details, 685
- dynamic programming, 690
- format control, 674, 676–678, 690, 692
- full-screen options, 672, 678, 679
- full-screen version, 693, 697, 698, 700
- functional summary, 668
- graphics catalog specification, 672
- graphics options, 672, 679–685
- graphics version, 700–702
- hierarchical charts, 696
- horizontal placement of nodes, 693
- HTML Imagemap data set, 672
- Imagemap data set, 672
- information within node, 690
- input data sets, 662, 685
- Layout data set, 673, 692
- layout specification, 693
- line-printer options, 672, 685
- missing values, 688, 691
- modes of display, 663, 672, 691
- modifying the network layout, 663, 693
- moving nodes, 697
- Network data set, 672
- network layout, 663, 664, 688–694
- network specification, 673, 677
- node coordinates and layout, 688
- node layout, 663
- number of pages, 692
- ODS style template, 703
- options classified by function, 668
- organizational charts, 696
- \_ORNETDR macro variable, 702
- output data sets, 662
- overview, 12, 13, 662
- page format details, 691
- restricting number of tracks, 690
- rotating the network, 694, 697
- saving network layout information, 686
- showing activity progress, 691
- splitting across pages, 691
- syntax skeleton, 668
- table of syntax elements, 668
- time-axis format, 694, 695
- time-scaled networks, 663, 667, 673–678, 694, 695
- top-down networks, 694, 697
- topological ordering, 689

- tree diagrams, 674, 677, 678, 696
  - using full-screen to modify layout, 693
  - variables, list of, 687
  - vertical placement of nodes, 693
  - zoned networks, 663, 676, 678, 696
- NETDRAW procedure
  - \_ORNEDR macro variable, 13
- Network data set
  - description, 686
  - list of variables, 687
  - NETDRAW procedure, 662, 672, 685
- network diagrams, *see* NETDRAW procedure
  - Activity-on-Arc, 56
  - Activity-on-Node, 57
- network layout, NETDRAW procedure
  - discussion, 688–694
  - modifications for time-scaled networks, 695
  - modifications for zoned networks, 696
  - use of dynamic programming, 690
- nodes on decision tree, 397, *see* chance nodes, *see also* decision nodes, *see also* end nodes
- nodes on network diagram
  - coordinates, 688
  - height, 674, 690, 728
  - layout, 688
  - width, 674, 690, 722
- noncritical activities
  - fill pattern for duration of (GANTT), 537
  - fill pattern for slack time of (GANTT), 537
- nonstandard precedence relationships
  - CPM procedure, 95, 96
  - example (CPM), 181
  - GANTT procedure, 486, 487, 545, 546, 548–550
  - Gantt View, 317, 319, 321
  - graphics example (GANTT), 628
  - lag calendar, 90, 91, 182, 183
  - lag duration, 90
  - lag types, 90
  - lag variables, 90, 181
  - specification, CPM procedure, 90, 91
- NPV, *see* net present value
- number of columns, global graphics options
  - DTREE procedure, 429
- number of nodes
  - horizontal (NETDRAW), 683
  - vertical (NETDRAW), 683
- number of pages
  - displaying decision tree diagram, 428
  - displaying network diagram, 676
  - horizontal (NETDRAW), 681
  - NETDRAW procedure, 692
  - vertical (NETDRAW), 684
- number of rows, global graphics options
  - DTREE procedure, 429
- number pages
  - GANTT procedure, 520, 521
  - numerical precision, DTREE procedure, 434
- OBSTYPE variable
  - Resource data set (CPM), 86, 114
- OBS\_TYPE variable
  - Usage data set (CPM), 81
- offset specification
  - actual bar (GANTT), 510
  - baseline bar (GANTT), 511
  - early bar (GANTT), 514
  - holiday bar (GANTT), 515
  - late bar (GANTT), 514
  - resource-constrained schedule bar (GANTT), 522
  - schedule bar (GANTT), 511
  - zone line (GANTT), 524
- oil wildcatter's decision problem, 418, 423
  - a risk-averse setting, 441
  - an insurance option, 436
  - example, 383
  - sounding test option, 391
  - value of perfect control, 390
  - value of perfect information, 389
- online documentation, 7
- optimal decision
  - determining, 389
- optimal decision summary
  - displaying, 383, 387, 401, 402, 413, 422, 426
  - example, 387, 393, 420, 421
  - suppress displaying, 401
- optimal evaluating value, 411
- options
  - not changed, 412
  - resetting, 383, 412, 422
  - specified on multiple statements, 422
- options classified by function, *see* functional summary, *see also* functional summary
- \_ORCPM\_ macro variable, 11, 14, 134
- order of stages
  - determining, 423
  - limitations to modifying, 412
  - modifying, 383, 412, 423
  - structuring decision problems, 422
- order of statements
  - DTREE procedure, 422
- ORFONT font (filled), 544
- ORFONTE font (empty), 545
- organizational charts
  - NETDRAW procedure, 696, 755
- \_ORGANTT macro variable, 12, 516, 523, 559
- \_ORNEDR macro variable, 13, 702
- \_OUT variables, *see* OUTCOME variables
  - Stage data set (DTREE), 415

- outcome name
  - on decision tree diagram, 400, 413
- OUTCOME variables
  - Stage data set (DTREE), 415
- outcomes
  - chance stage, 382
  - decision stage, 382
  - decision tree model, 382
  - name, 382
  - reward, 382
  - successor, 382
- outlines and arcs
  - network diagrams, 679, 685
- outlines and dividers
  - Gantt chart, 507
- output, *see* displayed output, *see* output data sets
- output data sets, *see also* Imagemap data set, *see also*
  - Layout data set, *see also* Resource Schedule data set, *see also* Schedule data set, *see also* Usage data set, *see* Resource Schedule data set, *see* Schedule data set, *see* Usage data set, *see* Imagemap data set
  - CPM procedure, 11, 55
  - DTREE procedure, 383
  - GANTT procedure, 487, 498
  - %MSPTOSAS macro, 355
  - NETDRAW procedure, 13, 662
  - PM procedure, 14
- Output Delivery System (ODS)
  - DTREE procedure, 383, 432
  - DTREE style template, 432
  - GANTT procedure, 561, 646
  - GANTT style template, 562
  - NETDRAW procedure, 703
  - NETDRAW style template, 703
  - table names, 432
- overprint character
  - for CHART variables, 508
  - for schedule variables, 508
- overview
  - CPM procedure, 55
  - DTREE procedure, 382
  - GANTT procedure, 484
  - NETDRAW procedure, 662
  - PM procedure, 301
  - Projman, 774
- padding finish times, 502, 505, 526, 528, 582
  - default behavior, 528
- page
  - drawing decision tree on a single, 403, 454
  - drawing Gantt chart on a single, 585
  - drawing network on a single, 680, 683, 718
  - format of decision tree diagram, 427
- format of Gantt chart, 528
- format of network diagram, 691
- page numbers
  - in NETDRAW procedure, 683
  - on decision tree diagram, 408
  - on Gantt charts, 521
  - suppress displaying (DTREE), 408
  - suppress displaying (GANTT), 520
  - suppress displaying (NETDRAW), 682
- \_PAGEBRK variable
  - Label data set (GANTT), 555, 556
- pages
  - display page number (GANTT), 521
  - limiting number of (GANTT), 505, 515, 523, 535
  - limiting number of (NETDRAW), 676
  - limiting number of horizontal (GANTT), 515
  - limiting number of vertical (GANTT), 523
  - needed in displaying decision tree diagram, 428
  - suppress page number (GANTT), 520
- pattern specification
  - GANTT procedure, 522, 536
  - NETDRAW procedure, 701
  - pattern selection guide, 540
  - table of assignments (GANTT), 537
- PATTERN variable
  - Network data set (NETDRAW), 679, 683, 696, 698, 701
  - Schedule data set (GANTT), 513, 521, 536, 537
- \_PATTERN variable, *see* PATTERN variable
  - Network data set (NETDRAW), 679, 683, 693, 696, 701
  - Schedule data set (GANTT), 521, 537, 638, 642
- Payoff data set
  - DTREE procedure, 383, 401, 418, 419
  - example, 385
  - redundant observations, 462
  - variables, 417
- payoffs
  - decision tree model, 419
  - different from rewards, 419
  - warning if unassigned, 402
- PAYOFFS variables, *see* VALUE variables
- PCTCOMP variable
  - Activity data set (CPM), 72, 110, 190
- PCT\_COMP variable
  - Schedule data set (CPM), 71
- percent complete, 72, 110, 868, 888, 898, 908
- percentages
  - CV%, 899
  - SV%, 899
  - VAC%, 899
- PERIOD variable
  - Resource data set (CPM), 86, 94, 114
- periodic data set

- variables, 897
- periodic data sets
  - %EVA\_EARNED\_VALUE macro, 862, 906, 920
  - %EVA\_METRICS macro, 869, 898
  - %EVA\_PLANNED\_VALUE macro, 859, 904, 917
  - variables, 897, 898
- petroleum distributor's decision problem, 471
- placement of activity text (GANTT), 515, 516
- placement of ID variables (NETDRAW), 691
- planned value, 846, 847, 858, 868, 869, 876, 897, 898, 900
- plots
  - %EVG\_COST\_PLOT macro, 876, 908, 927
  - %EVG\_GANTT\_CHART macro, 874, 912, 931
  - %EVG\_INDEX\_PLOT macro, 875, 910, 928
  - %EVG\_SCHEDULE\_PLOT macro, 877, 909, 928
  - %EVG\_VARIANCE\_PLOT macro, 873, 911, 929
- PM examples
  - adding subtasks, 334
  - baseline schedules, 336
  - new project, 329
- PM procedure
  - activity numbers, 325
  - add activities, 319
  - edit project, 318
  - Gantt View, 313
  - overview, 13, 14, 301
  - PM window, 307
  - progress updating, 326
  - progress variables, 326
  - project hierarchy, 309
  - Schedule data set, 327
  - Summary of Differences, 327
  - Table View, 310
  - TIMENOW macro variable, 326
- PM procedure
  - \_ORCPM\_ macro variable, 14
- PM window, 307
  - activity numbers, 325
  - add activities, 319
  - add subtasks, 321
  - alignment constraints, 321
  - baseline schedule, 319, 321
  - calendar information, 322
  - copy activities, 320
  - delete activities, 321
  - delete precedence constraints, 321
  - edit durations, 320
  - filters, 322
  - Gantt View, 313
  - milestones, 321
  - PM procedure, 307
- print options, 326
- print preview, 326
- printing, 325
- progress information, 320
- project font, 325
- project preferences, 323
- resource requirements, 322
- saving printed output, 326
- sorting activities, 324
- Table View, 310
- user interface features, 307
- PNTID variable
  - Schedule data set (PM), 328
- pop-up menu
  - alignment constraints, 312
  - arc, 308, 317
  - calendar, 312
  - Gantt View, 313, 315
  - increment, 314
  - major axis, 314
  - minor axis, 314
  - scale, 315
  - schedule bar, 316
  - Table View, 311
  - target type, 312
  - task information, 316
  - Time Axis, 313
  - units, 315
- PRATCVAL variable
  - PROJECT data set (PM), 324
- PRATNVAL variable
  - PROJECT data set (PM), 324
- precedence connections
  - color, 513
  - GANTT procedure, 545
  - line style, 518
  - line width, 524
- Precedence data set, 486, 487, 498, 510, 523, 526, 546
  - graphics example (GANTT), 628
  - linking to Schedule data set, 546
- precedence diagramming method, *see*
  - Activity-on-Node
- precedence information, 510, 515, 517, 518, 523
- precedence relationships
  - CPM procedure, 95, 96
  - GANTT procedure, 486, 487, 545–551
  - scheduling subject to, 93, 94
- preference, DTREE procedure, 423
- Preferences data set
  - %MSPTOSAS macro, 359
- print options
  - PM window, 326
- print preview
  - PM window, 326

- printing
  - PM window, 325
- PROB variables
  - Probability data set (DTREE), 417
  - \_PROB variables, *see* PROB variables
    - Probability data set (DTREE), 417
- probabilities
  - decision tree model, 382
  - do not sum to 1, 399
  - on decision tree diagram, 400, 401, 413
  - scaled by DTREE procedure, 399
  - warning when rescaled, 402
- Probability data set
  - DTREE procedure, 382, 401, 418, 419, 421
  - example, 385
  - variables, 416, 417
- problem size specification
  - CPM procedure, 139
  - number of activities (CPM), 67
  - number of adjacencies (CPM), 67
  - resource requirement array (CPM), 68
  - size of symbolic table (CPM), 67
  - utility data sets (CPM), 68, 139
- progress information
  - Gantt View, 318
  - PM window, 320
  - Table View, 312
- progress updating
  - allow nonzero float, 72, 111
  - automatic updating of progress information, 71, 111, 190, 191, 305
  - CPM procedure, 109–112
  - current time, 72, 110
  - estimate percent completion time, 71, 305
  - example (CPM), 188
  - interrupt activities in progress, 72, 112
  - PM procedure, 326
  - resource allocation during, 123
  - specifying information, 70–72
- progress variables, 110
  - CPM procedure, 70, 110, 111
  - PM procedure, 326
- PROJATTR variable
  - PROJECT data set (PM), 324
- PROJ\_DUR variable
  - Schedule data set (CPM), 134
- project
  - cost control, example, 40
  - definition, 9, 56
  - finish date, 66, 93, 149
  - graphical representation, 664
  - introductory example, 18, 57
  - multiple projects, 30, 38
  - network diagram, example, 18
  - resource-constrained schedule, 25
  - schedule comparison, 74
  - scheduling and reporting, 21
  - start date, 66, 93, 144, 149
  - summary, 24
  - work breakdown structure (WBS) example, 20
- project cost control, 40
  - ACWP, 41
  - BCWP, 41
  - BCWS, 41
  - definition of measures, 41
  - example, 40
  - plot of measures, 45
- PROJECT data set (PM)
  - PRATCVAL variable, 324
  - PRATNVAL variable, 324
  - PROJATTR variable, 324
- project deadlines, *see* deadlines
- project font
  - PM window, 325
- project hierarchy
  - PM procedure, 309
- project management
  - decision analysis in, 10
  - examples, 17
  - introduction, 9–17, 51
  - scheduling example, 22, 25
- project management systems, 50
- project monitoring
  - using baseline schedule, 600
- project network diagram, 852
- project preferences
  - PM window, 323
  - pull-down menu, 324, 325
- project progress, *see* progress updating
  - measuring using baseline schedule, 600
- PROJECT variable
  - Activity data set (CPM), 78, 131
  - Schedule data set (CPM, 134
- \_PROJECT variable
  - %SASTOMSP macro parameters, 363
- PROJLEV variable
  - Schedule data set (CPM), 134
- Projman
  - accessing reports, 781
  - application options, 778
  - calendar report options, 815
  - calendars, 783, 784
  - editing activities, 780
  - editing calendars, 781, 783, 784
  - editing holidays, 781, 785, 786
  - editing resources, 781, 788, 789
  - editing workshifts, 781, 794, 795
  - Gantt chart options, 816

- holidays, 785, 786
- importing activity data set, 779, 832
- importing calendar data set, 784, 839
- importing holiday data set, 786, 840
- importing projects, 779
- importing resourcein data set, 789, 841
- importing workshift data set, 795, 842
- introduction, 51
- network diagram options, 822
- overview, 774
- project information, 780
- project name option, 775
- project summary, 781
- projman command, 775
- Projman Window, 775
- report macro variables, 811
- report options, 806
- reports, 803
- resource report options, 829
- resources, 788, 789
- sample projects, 779
- scheduling options, 796
- tabular listing options, 829
- workshifts, 794, 795
- proportional compression
  - Gantt chart, 522
- pull-down menu
  - file, 326
  - filters, 323
  - move column, 311
  - preferences, 324, 325
  - project, 308
  - project preferences, 324, 325
  - set baseline, 320
  - sort, 324
  - View, 310, 322
- \_PV\_ variable
  - periodic data set (%EVA\_METRICS), 898
  - task data set (%EVA\_TASK\_METRICS), 900
- \_PV\_RATE\_ variable
  - periodic data set (%EVA\_PLANNED\_VALUE), 897
- R\_DELAY variable
  - Schedule data set (CPM), 82, 99, 200
- rectangular corners
  - decision tree diagram, 408
  - network diagram, 683
- reference lines, 505
  - automatic at every tick mark, 673
  - break character, 678
  - character to represent, 508, 679, 685
  - color, 513, 679, 681
  - labels, 505
- line style, 518, 682
- remaining duration, 72, 110
- REMDUR variable
  - Activity data set (CPM), 72, 190
- replenishable resource, 115
- rescale probabilities
  - DTREE procedure, 399
  - warning in DTREE procedure, 402
- research and development decision problem, 457
- RESID variable
  - Resource data set (CPM), 87, 114
- \_RESOBSTYPE variable
  - %SASTOMSP macro parameters, 363
- resource allocation, *see* resource allocation control, 113, 114, 116–125, 128–131
  - activity splitting, 122, 123, 225
  - actual dates, 123
  - alternate resources, 116, 123, 124, 126, 230
  - analyzing infeasibilities, 84, 121, 211
  - auxiliary resources, 127
  - effect of the TIMENOW option, 123
  - example (CPM), 197
  - multiple alternates, 125
  - negative resource requirements, 119
  - progress updating, 123
  - resource availability profile, 117
  - resource calendars, 255
  - resource dictionary, 114
  - resource-driven durations, 122, 126
  - resource levels, 114
  - resource priority, 114, 116, 121
  - resource usage variables, 128
  - scheduling method, 119–121
  - scheduling rule, 88, 120, 198
  - secondary scheduling rule, 89, 120
  - specifying resource requirements, 118, 119
  - substitutable resources, 116, 123
  - supplementary levels, 114, 116
  - supplementary resources, 121
- resource allocation control
  - activity-splitting options, 84, 85, 89
  - alternate resources, 81, 85, 87
  - checking levels needed, 84
  - cutoff date, 89
  - options related to, 81, 82, 84, 85, 87–89
  - scheduling rules, 88, 89
- resource calendars
  - example (CPM), 255
- resource-constrained schedule, 25
  - example (GANTT), 604
  - fill pattern for (GANTT), 537
  - GANTT procedure, 525, 558
  - split activities, 525, 558

- treatment of SEGMT\_NO variable (GANTT), 558
- resource-constrained schedule bar
  - height, 522
  - offset, 522
- resource constraints, *see* resource allocation
- Resource data set
  - alternate resource specification, 124
  - CPM procedure, 55, 68, 114, 197, 198
  - missing values, 137
  - %MSPTOSAS macro, 357
  - multiple alternates, 125
  - observation type, 86
  - resource specification example (CPM), 117
  - %SASTOMSP macro, 357
  - variables, 114, 135
- resource-driven durations, 90, 99, 112
  - and resource allocation (CPM), 122
  - CPM procedure, 126
  - example (CPM), 255, 293
- resource infeasibilities, 84, 121, 211, 213, 218, 223
- resource requirements
  - PM window, 322
  - specifying, CPM procedure, 118, 119
  - Table View, 312
- Resource Schedule data set
  - CPM procedure, 55, 69
- resource type
  - consumable, 115, 197
  - replenishable, 115
- resource usage, *see* Usage data set
  - CPM procedure, 113, 129
  - cumulative usage, 82, 129
  - cumulative usage example, 207, 214
  - daily usage, 129
  - example of reports, 194
  - variables in Usage data set, 128
- \_RESOURCE variable
  - %SASTOMSP macro parameters, 363
- RESOURCE variables
  - Activity data set (CPM), 80, 118
  - example (CPM), 193
  - Resource data set (CPM), 80, 114
  - Resource Schedule data set (CPM), 131
- \_RESPERIOD variable
  - %SASTOMSP macro parameters, 363
- \_REW variables, *see* REWARD variables
  - Stage data set (DTREE), 415
- REWARD variables
  - Stage data set (DTREE), 415, 419, 420
- rewards
  - decision tree model, 419
  - different from payoffs, 419
  - label on decision tree diagram, 401
- modifying, 411
- on decision tree diagram, 400, 413
- risk, 424
- risk averse, 440, 441
- risk aversion
  - coefficient, 424
  - DTREE procedure, 424
- risk tolerance
  - DTREE procedure, 388, 424, 425
  - estimation, 424
  - example (DTREE), 440, 441
  - specifying, 389, 401, 426
- \_RLABEL variable
  - Label data set (GANTT), 555, 556
- rotating the network diagram, 664, 684, 690, 694, 697, 765
  - used for top-down trees, 694, 697
- rounded corners
  - decision tree diagram, 408
  - network diagram, 683
- rows in Gantt chart
  - between activities, 506, 557
- R\_RATE variable
  - Resource Schedule data set (CPM), 131
- RSCHEDID variables
  - Activity data set (CPM), 88
  - Resource Schedule data set (CPM), 88
- RT, *see* risk tolerance
- SAS catalogs, *see* graphics catalog, *see* graphics catalog
- SAS data sets, *see* input data sets, *see* output data sets
  - CPM procedure, 55
  - DTREE procedure, 382–384, 418
  - GANTT procedure, 486, 487
  - NETDRAW procedure, 662
  - PM procedure, 13
  - used to model project information, 10
- SAS date, time, and datetime values
  - CPM procedure, 66, 94, 95, 105, 139
- %SASTOMSP macro parameters
  - \_ACTIVITY variable, 361
  - \_ALIGNDATE variable, 361
  - \_ALIGNTYPE variable, 361
  - \_CALID variable, 362
  - \_DATE variable, 362
  - \_DAYLENGTH variable, 362
  - \_DAYSTART variable, 362
  - \_DUR variable, 362
  - \_FBDATE variable, 362
  - \_HEAD variable, 362
  - \_HOLIDUR variable, 362
  - \_HOLIEND variable, 362
  - \_HOLISTART variable, 362

- \_ID variable, 362
- \_INTERVAL variable, 363
- \_LAG variable, 363
- \_PROJECT variable, 363
- \_RESOBSTYPE variable, 363
- \_RESOURCE variable, 363
- \_RESPERIOD variable, 363
- \_SUCCESSOR variable, 363
- \_TAIL variable, 363
- \_SAT\_ variable
  - Calendar data set (CPM), 103
- saving printed output
  - PM window, 326
- scenario of decision tree, 382, 413
- schedule
  - character string to represent duration (GANTT), 508
  - character string to represent times (GANTT), 509
  - fill patterns to represent duration (GANTT), 537
  - variables format (GANTT), 526
- schedule bar
  - height, 511
  - offset, 511
- schedule computation
  - finish milestone, 98
  - multiproject, 133
  - nonstandard precedence constraints, 96
  - progress updating, 111
  - resource constraints, 119–121
  - standard precedence constraints, 93
  - time constraints, 96, 97
- Schedule data set
  - as input to NETDRAW procedure, 686
  - CPM procedure, 55, 58, 68, 99–101, 124
  - direct specification of schedule data (GANTT), 606
  - GANTT procedure, 486, 487, 497, 525
  - generated by PROC CPM, 486, 487, 525, 545, 547
  - linking to Precedence data set, 546
  - %MSPTOSAS macro, 358
  - multiproject, 134
  - options to control, 66, 70, 82–84, 86, 87, 89, 90
  - PM procedure, 327
  - progress variables, 112, 326
  - resources used, 124, 234
  - sort variables, 78, 79, 134, 246
  - treatment of finish times, 526
  - treatment of ID variables, 558
  - treatment of schedule variables, 525
  - treatment of start times, 526
  - variables, 59, 99–101, 112, 123, 124
- Schedule data set
  - treatment of \_DUR\_ variable, 502, 528
- treatment of SEGMT\_NO variable (GANTT), 525, 558
- schedule information, *see* Schedule data set
- scheduling
  - around weekends and holidays, 59, 155, 159, 161, 167
  - multiple projects, example, 31, 40
  - projects, example, 22
  - resource-constrained, example, 25
  - rule for breaking ties, 89
  - rule for ordering activities, 88, 120, 121
  - sequential scheduling of multiple projects, 38
  - serial parallel method, CPM procedure, 119, 120
  - secondary levels of resource
    - CPM procedure, 121
  - segments, *see* activity splitting
- SEGMT\_NO variable
  - Schedule data set (CPM), 101, 123, 228
  - Schedule data set (GANTT), 522, 525, 558, 607, 641
- \_SEQ\_ variable
  - Layout data set (NETDRAW), 693
  - Network data set (NETDRAW), 687, 693
- serial-parallel scheduling method
  - CPM procedure, 119, 120
- S\_FINISH variable
  - input data set (%EVG\_WBS\_CHART), 894
  - Network data set (NETDRAW), 674, 687, 691
  - Schedule data set (CPM), 99, 100, 123
  - Schedule data set (GANTT), 505, 508, 525, 526
- SFINMILE variable
  - Schedule data set (CPM), 99
- shift variables, *see* Workday data set
- shifts, *see* break and shift information
- slack duration, 508
  - fill patterns for (GANTT), 537
- slack time, *see* float
- smallest identifiable time unit, 504, 529
  - default values, 529
  - example (GANTT), 586
  - number of columns representing, 506, 529
  - time axis labeling corresponding to, 529
- sort variables
  - Schedule data set (CPM), 78, 79, 134, 246
- sorting activities
  - PM window, 324
- spacing between
  - activity plots, 506
  - ID columns, 500
  - nodes, 678
  - time axis labels, 503
  - two successive end nodes, 402
- special symbol table
  - DTREE procedure, 409

- GANTT procedure, 523
- SPI, 846, 847, 868, 875, 893, 896, 898–900, 910, 928
- \_SPI\_variable
  - periodic data set (%EVA\_METRICS), 898
  - task data set (%EVA\_TASK\_METRICS), 900
- split activities, *see* activity splitting
- split character for ID labels, 498
- split ID column headings, 498
- split labels
  - labeling facility (GANTT), 517
- SQUARE, special symbol table
  - DTREE procedure, 409
- SS\_ASC variable
  - Schedule data set (CPM), 78, 79
- SS\_DESC variable
  - Schedule data set (CPM), 78
- S\_START variable
  - input data set (%EVG\_WBS\_CHART), 894
  - Network data set (NETDRAW), 674, 687, 691
  - Schedule data set (CPM), 99, 100, 123
  - Schedule data set (GANTT), 506, 508, 525, 526
- Stage data set
  - DTREE procedure, 382, 401, 418–420, 423
  - example, 384
  - variables, 415, 416
- stage name
  - on decision tree diagram, 400, 413
- stage type
  - modifying, 411
- STAGE variable
  - Stage data set (DTREE), 415
- stages
  - chance, 382
  - decision, 382
  - decision tree model, 382
  - end, 382
  - name, 382
  - order, 412, 422, 423
  - outcomes, 382
  - type, 382, 411
- start times
  - format of, 526
  - interpretation of, CPM procedure, 94
  - treatment of, 526
- START variable
  - Activity data set (CPM), 76
- \_STAT variables, *see* STATE variables
  - Payoff data set (DTREE), 417
- STATE variables
  - Payoff data set (DTREE), 417
- statement order
  - DTREE procedure, 422
- status flags, 501
  - displaying on multiple pages, 559
- STATUS variable
  - Network data set (NETDRAW), 691
  - Resource Schedule data set (CPM), 131
  - Schedule data set (CPM), 99, 100, 112, 190, 677
- \_STNAME\_variable, *see* STAGE variable
  - Stage data set (DTREE), 415
- straight-line utility function, 401
- \_STTYPE\_variable, *see* TYPE variable
  - Stage data set (DTREE), 416
- style of lines, *see* line style specification
- subcontracting decisions, 47
- subprojects, *see* multiproject scheduling
  - individual critical paths for (CPM), 79
  - ordering activities within (CPM), 78, 79
- substitutable resources, *see* alternate resources
- \_SUCC variables, *see* SUCCESSOR variables
  - Stage data set (DTREE), 416
- \_SUCCESSOR variable
  - %SASTOMSP macro parameters, 363
- SUCCESSOR variables
  - Activity data set (CPM), 90
  - Network data set (NETDRAW), 677, 687
  - Precedence data set (GANTT), 517, 523, 546
  - Schedule data set (GANTT), 523
  - Stage data set (DTREE), 416
- SUCCID variable
  - Schedule data set (PM), 328
- summary data sets
  - %EVA\_METRICS macro, 868, 898, 906, 922
  - variables, 898
- summary of Gantt chart symbols, 506, 558, 570
- summary output
  - %EVA\_METRICS macro, 866
- \_SUN\_variable
  - Calendar data set (CPM), 103
- supercritical activities
  - definition of, 93, 97
  - example of, 187
  - fill pattern for duration of (GANTT), 537
  - fill pattern for slack time of (GANTT), 537
  - GANTT procedure, 501, 508
  - node pattern (NETDRAW), 701
- supplementary resources
  - CPM procedure, 121
  - example (CPM), 207
  - infinite levels, 211
- SUPPL\_R variable
  - Schedule data set (CPM), 82, 99, 200
- SV, 846, 848, 849, 868, 873, 874, 893, 895, 898, 911, 929, 931
- SV percentage, 895
- \_SV\_variable
  - periodic data set (%EVA\_METRICS), 898
  - task data set (%EVA\_TASK\_METRICS), 900

- S\_VAR variable
  - Schedule data set (CPM), 74, 190, 223
- \_SVP\_variable
  - task data set (%EVA\_TASK\_METRICS), 900
- symbol specification
  - chance nodes (DTREE), 408, 409
  - controlling the appearance of decision tree, 429
  - decision nodes (DTREE), 408, 409
  - DTREE procedure, 406–409
  - end nodes (DTREE), 409
  - example (DTREE), 457, 459
  - GANTT procedure, 536, 541
  - identifying symbols for links on decision tree, 406
  - identifying symbols for nodes on decision tree, 408, 409
  - milestones (GANTT), 523
  - project management fonts, 545
  - special symbol table, 542
- symbols for project management and decision analysis, 543
- syntax skeleton
  - CPM procedure, 61
  - DTREE procedure, 395
  - GANTT procedure, 492
  - NETDRAW procedure, 668
- table of syntax elements, *see* functional summary, *see also* functional summary
- Table View, 310
  - add tasks, 310
  - collapse supertasks, 312
  - column, change order, 311
  - column, change width, 311
  - delete tasks, 310
  - edit alignment constraints, 311
  - edit calendars, 312
  - edit durations, 311
  - expand supertasks, 312
  - hide tasks, 313
  - move tasks, 313
  - PM procedure, 310
  - PM window, 310
  - pop-up menu, 311
  - progress information, 312
  - resource requirements, 312
  - target date, 311
  - target type, 311
  - time constraints, 311
- TAIL variable
  - Activity data set (CPM), 91
  - Schedule data set (GANTT), 523, 545
- \_TAIL variable
  - %SASTOMSP macro parameters, 363
- target completion dates, *see* deadlines
- target date
  - Table View, 311
- target schedule, *see* baseline schedule
- target type
  - Table View, 311
- target variables, *see* CHART variables
- Task Attributes data set
- %MSPTOSAS macro, 358
- task axis, *see* activity axis
- task data sets
  - %EVA\_TASK\_METRICS macro, 900
  - variables, 900
- task information dialog box, 309
- task output
  - %EVA\_TASK\_METRICS macro, 872, 908, 924
- TCPI, 868, 875, 910, 928
  - BAC, 868, 875, 896, 899
  - EAC, 868, 896, 899
- text
  - color (DTREE), 404
  - color (GANTT), 513
  - color (NETDRAW), 681
  - font (DTREE), 405
  - font (GANTT), 514
  - font (NETDRAW), 681
  - font baseline (activity), 516
  - height (DTREE), 405
  - height (GANTT), 515
  - height (NETDRAW), 681
  - height, graphics example (GANTT), 617
  - maximum allowable height, 515
  - placement (GANTT), 516
  - placement, graphics example (GANTT), 617
- T\_FLOAT variable
  - input data set (%EVG\_WBS\_CHART), 894
  - Network data set (NETDRAW), 674, 687, 691
  - Schedule data set (CPM), 59, 89, 99, 101
- thickness of lines, *see* line width specification
- thresholds, 873, 892, 912, 929
- \_THU\_variable
  - Calendar data set (CPM), 103
- tickmark label
  - suppress time portion, 520
- tickmarks
  - limiting the number on first page (GANTT), 521
- time axis
  - altering range, graphics example (GANTT), 590
  - color, 512
  - extension of, 548
  - format (Gantt View), 314
  - formatting, 504, 507, 678, 694, 695, 760
  - GANTT procedure, 485, 529, 537
  - increments on, 503, 529
  - inter-label spacing, 503

- labeling, 529, 530
- largest time value, 504
- maximum and minimum values, 673
- NETDRAW procedure, 694, 695
  - scaling, 675, 694, 695
  - show break in, 677
  - smallest interval represented, 675
  - smallest time value, 504
  - suppress extension of, 520, 548
  - suppress printing, 676
  - suppress printing on every page, 676
  - units (Gantt View), 315
- time-constrained scheduling
  - CPM procedure, 73, 94, 96, 97
  - example (CPM), 186
- time constraints
  - activity align dates (CPM), 73, 186
  - activity align dates (PM), 311
  - activity align types (CPM), 73, 186
  - activity align types (PM), 311
  - fix finish time (CPM), 67
  - Mandatory Finish, MF, 97, 187
  - Mandatory Start, MS, 97, 187
  - project finish date (CPM), 66, 67, 93
  - project start date (CPM), 66, 93
  - scheduling subject to, 96, 97
  - Table View, 311
- time increment
  - Gantt View, 314
- time scale
  - Gantt View, 315
- \_TIME\_ variable
  - periodic data set (%EVA\_EARNED\_VALUE), 897
  - periodic data set (%EVA\_METRICS), 898
  - periodic data set (%EVA\_PLANNED\_VALUE), 897
  - Usage data set (CPM), 81, 84–86, 88, 89, 128–130
- time-scaled network diagrams, 663, 667, 694, 734, 738
  - default ALIGN variable, 694
  - spacing of nodes, 694
  - tick marks, 694
- TIMENOW, 72, *see* progress updating
  - allow activity splitting at, 72
  - macro variable (PM), 326
- timenow line, 501, 506
  - character for drawing, 509
  - color, 514
  - line style, 518
  - line width, 524
- produced by COMBINE, 501, 558
- produced by COMBINE, example (GANTT), 603
- suppress label, 505
- \_TIMENOW\_ macro variable
  - %EVA\_METRICS macro, 886
  - %EVA\_TASK\_METRICS macro, 888
  - %EVG\_GANTT\_CHART macro, 893
- \_TO\_ variable
  - Layout data set (NETDRAW), 692, 693
  - Network data set (NETDRAW), 677
- top-down hierarchical diagram, 683
- total float, *see* float
- total probability
  - DTREE procedure, 399
  - is not equal to 1, 399
- tree diagrams
  - NETDRAW procedure, 663, 696, 697, 755
- \_TUE\_ variable
  - Calendar data set (CPM), 103
- turning points
  - Logic Gantt charts, 546, 548
- type of lines, *see* line style specification
- TYPE variable
  - Stage data set (DTREE), 416
- unassigned payoffs
  - warning in DTREE procedure, 402
- uncertain factor
  - represented as chance stage, 382
- uncertainty, decision tree model, 382, 423, 424
- unconditional probability
  - DTREE procedure, 383
- unit of measure, global graphics options
  - DTREE procedure, 402
- units of duration
  - CPM procedure, 59
- units of vertical space
  - DTREE procedure, 402
  - graphics version (DTREE), 402
  - line-printer version, 402
- Usage data set
  - CPM procedure, 55, 69, 127, 129, 193, 194
  - description, 127, 128
  - GPLOT example, 28
  - options, 81–88
  - rate of usage, 81, 89
  - resource usage and availability profile, 129
  - total usage, 81, 89
  - variables, 127, 129, 130
- user interface features
  - PM window, 307
- utility, 423
- utility curve, 400, 423
- utility function
  - DTREE procedure, 388, 423, 424
  - exponential, 388, 400, 424, 426
  - straight-line, 401, 424

- utility value, 423
- UTILITY variables, *see* VALUE variables
- VAC, 868, 895, 899
- VAC percentage, 895
- VAC%, 899
- vacations, *see* holidays
- \_VALU variables, *see* VALUE variables
  - Payoff data set (DTREE), 417
- value of imperfect information, *see* value of sample information
- value of perfect control, 390, 418
  - evaluating, 383, 390, 466, 467
  - misleading, 467
- oil wildcatter's decision problem, 390
- value of perfect information, 389, 418
  - evaluating, 383, 389, 390, 423, 466
  - misleading, 466
- oil wildcatter's decision problem, 389
- value of sample information, 393
  - evaluating, 394
- VALUE variables
  - Payoff data set (DTREE), 417
- variables
  - format of (CPM), 139
  - format of (GANTT), 526
  - list of, CPM procedure, 135
  - list of, DTREE procedure, 415
  - list of, GANTT procedure, 526
  - list of, NETDRAW procedure, 687
  - treatment of missing values (CPM), 137
  - treatment of missing values (DTREE), 421
  - treatment of missing values (GANTT), 526
  - treatment of missing values (NETDRAW), 688
- variances
  - CV, 846, 848, 849, 868, 873, 874, 893, 898, 911, 929, 931
  - SV, 846, 848, 849, 868, 873, 874, 893, 898, 911, 929, 931
  - VAC, 868, 899
- vertical space
  - around margin (NETDRAW), 684, 734
  - between activities (GANTT), 506, 557
  - between nodes (NETDRAW), 678, 690, 722
  - between two end nodes (DTREE), 402
  - units (DTREE), 402
- View pull-down menu, 310
- warning
  - suppress displaying (CPM), 70
  - suppress displaying (DTREE), 402, 420
- WBS, 20, 79, 80
- WBS\_CODE variable
  - task data set (%EVA\_TASK\_METRICS), 900
- WBS\_CODE variable
  - Schedule data set (CPM), 80
- Web-enabled decision tree, 406, 416, 431
- Web-enabled Gantt charts, 498, 523, 556
  - graphics example (GANTT), 646
- Web-enabled network diagram, 672, 684, 702
- WEB variable
  - Imagemap data set (DTREE), 406
  - Imagemap data set (GANTT), 498
  - Network data set (NETDRAW), 684
  - Schedule data set (GANTT), 523, 556, 647
  - Stage data set (DTREE), 416, 431
- \_WED\_variable
  - Calendar data set (CPM), 103
- weekends and non-worked days, *see* break and shift information
  - displaying, 504, 531
  - scheduling around, 59
- weighted milestones, 916
- width of lines, *see* line width specification
- work breakdown structure, 20, 663, 853, 854, 878, 887, 888, 893, 894, 900, 902, 914
- work pattern, 486, *see* break and shift information, *see* weekends and non-worked days
- work shifts, *see* break and shift information
- WORK variable
  - Activity data set (CPM), 90, 112, 113
- \_WORK\_variable
  - Resource Schedule data set (CPM), 131
- workday
  - length of, 66, 94, 102, 103, 160, 501, 531
  - start of, 66, 94, 102, 103, 160, 501, 531
- Workday data set
  - CPM procedure, 55, 70, 101, 102, 172
  - GANTT procedure, 486, 497, 499, 530, 531
  - missing values, 137
  - %MSPTOSAS macro, 357
  - %SASTOMSP macro, 357
  - shift variables, 102
  - variables, 135
    - work shift example (CPM), 102
- workshift information, *see* Workday data set
- \_X variable
  - Label data set (GANTT), 517, 552, 554, 556
- \_X\_variable
  - Layout data set (NETDRAW), 693
  - Network data set (NETDRAW), 687, 693
- \_XOFFSET variable
  - Label data set (GANTT), 553, 555, 556
- \_XSYS variable
  - Label data set (GANTT), 554, 556
- \_XVAR variable
  - Label data set (GANTT), 517, 552, 554, 556, 637

- Y variable
    - Label data set (GANTT), 516, 552–554, 556
  - Y\_ variable
    - Layout data set (NETDRAW), 693
    - Network data set (NETDRAW), 687, 693
  - YOFFSET variable
    - Label data set (GANTT), 553, 555, 556, 636
  - YSYS variable
    - Label data set (GANTT), 553, 556
- zero duration activities, *see* milestones
- zone line
  - color, 514
  - line style, 518
  - line width, 524
- ZONE variable
  - Network data set (NETDRAW), 678, 687, 693
  - Schedule data set (GANTT), 524, 559, 645
- zoned Gantt charts
  - display ZONE variable only for new zones, 521
  - graphics example (GANTT), 645
  - line offset, 524
  - line span, 524
  - suppress ZONE variable column, 520
  - ZONE Variable, 524
- zoned network diagrams, 663, 696, 741

# Syntax Index

- ABARHT= option
  - CHART statement (GANTT), 510, 536
- ABAROFF= option
  - CHART statement (GANTT), 510
- ACRONYMS= parameter
  - %EVA\_METRICS macro, 885
  - %EVA\_TASK\_METRICS macro, 887
  - %EVG\_COST\_PLOT macro, 889
  - %EVG\_INDEX\_PLOT macro, 891
  - %EVG\_SCHEDULE\_PLOT macro, 890
  - %EVG\_VARIANCE\_PLOT macro, 892
- ACT statement, *see* ACTIVITY statement
- ACT= option, *see* ACTIVITY= option
- ACTDELAY= option
  - RESOURCE statement (CPM), 81, 121, 218
- ACTDS= parameter
  - %SASTOMSP macro parameters, 360
- ACTION= option
  - VARIABLES statement (DTREE), 417
- ACTIVITY statement
  - CPM procedure, 57, 70, 142
- ACTIVITY= option
  - ACTNET statement (NETDRAW), 673, 708
  - CHART statement (GANTT), 490, 510, 546, 619
- ACTIVITY= parameter
  - %EVA\_EARNED\_VALUE macro, 882
  - %EVA\_PLANNED\_VALUE macro, 879
  - %EVA\_TASK\_METRICS macro, 886
  - %EVG\_GANTT\_CHART macro, 893
  - %EVG\_WBS\_CHART macro, 894
- ACTIVITYPRTY= option
  - RESOURCE statement (CPM), 81
- ACTNET statement (NETDRAW), 673
  - full-screen options, 678, 679
  - general options, 673–678
  - graphics options, 679–685
  - line-printer options, 685
- ACTPRTY keyword
  - SCHEDRULE= option (CPM), 88, 120
- ACTPRTY= option, *see* ACTIVITYPRTY= option
- ACTUAL keyword
  - COMPARE= option (CPM), 74
  - PATLEVEL= option (GANTT), 521
  - SET= option (CPM), 75
  - UPDATE= option (CPM), 75
- ACTUAL statement
  - CPM procedure, 70, 188
- ACTUALCOST= parameter
  - %EVA\_EARNED\_VALUE macro, 882
  - %EVA\_TASK\_METRICS macro, 886
- ADATE statement, *see* ALIGNDATE statement
- ADDACT option
  - PROC CPM statement, 65
  - PROC PM statement, 305
- ADDALLACT option, *see* ADDACT option
- ADDCAL option
  - RESOURCE statement (CPM), 81
- ADDWBS option, *see* WBSCODE option
- AF= option, *see* A\_FINISH= option, *see* A\_FINISH= option
- A\_FINISH= option
  - ACTUAL statement (CPM), 71, 190
  - CHART statement (GANTT), 500, 598, 606
- AFTER keyword
  - MOVE statement (DTREE), 412
- AGGREGATE= parameter
  - %EVA\_TASK\_METRICS macro, 887
- AGGREGATEPARENTRES option
  - PROJECT statement (CPM), 78
- AGGREGATEP\_RES option, *see* AGGREGATEPARENTRES option
- AGGREGPR option, *see* AGGREGATEPARENTRES option
- ALAGCAL= option
  - SUCCESSOR statement (CPM), 90, 183
- ALIGN statement, *see* ALIGNTYPE statement
- ALIGN= option
  - ACTNET statement (NETDRAW), 673, 694, 736
- ALIGNDATE statement
  - CPM procedure, 73, 186
- ALIGNTYPE statement
  - CPM procedure, 73, 186
- ALL keyword
  - CTEXTCOLS= option (GANTT), 513
  - DISPLAY= option (DTREE), 400
  - PATLEVEL= option (GANTT), 521
  - ZONESPAN= option (GANTT), 524
- ALL option, *see* ORDERALL option
  - RESOURCE statement (CPM), 81, 128
- ALTBEFORESUP option
  - RESOURCE statement (CPM), 81, 234
- ALTPRTY keyword
  - OBSTYPE variable (CPM), 86, 87, 114, 116, 123
- ALTRATE keyword
  - OBSTYPE variable (CPM), 86, 87, 114, 116, 123

ANNO= option, *see ANNOTATE= option, see ANNOTATE= option, see ANNOTATE= option*

ANNOTATE= option

- ACTNET statement (NETDRAW), 679
- CHART statement (GANTT), 510
- PROC DTREE statement, 403, 459
- PROC GANTT statement, 496, 631
- PROC NETDRAW statement, 672, 760
- TREEPLOT statement (DTREE), 414

AOA option

- CHART statement (GANTT), 511, 546

APPEND option

- RESOURCE statement (CPM), 81

APPENDINTXRATE option, *see APPEND option*

APPENDRATEXINT option, *see APPEND option*

APPENDUSAGE option, *see APPEND option*

AROUTCAL= option

- RESOURCE statement (CPM), 81, 128

ARROWHEAD= option

- ACTNET statement (NETDRAW), 680

AS= option, *see A\_START= option, see A\_START= option*

A\_START= option

- ACTUAL statement (CPM), 71, 190
- CHART statement (GANTT), 500, 598, 606

ATYPE statement, *see ALIGNTYPE statement*

AUTOREF option

- ACTNET statement (NETDRAW), 673, 736, 742

AUTOSCALE option

- PROC DTREE statement, 399

AUTOUPDT option

- ACTUAL statement (CPM), 71, 111, 191
- ACTUAL statement (PM), 305

AUTOZONE option

- ACTNET statement (NETDRAW), 673

AUXRES keyword

- OBSTYPE variable (CPM), 86, 87, 114, 116, 127

AVL option, *see AVPROFILE option*

AVP option, *see AVPROFILE option*

AVPROFILE option

- RESOURCE statement (CPM), 82, 128, 214

AWAITDELAY option

- RESOURCE statement (CPM), 82

BARHT= option

- CHART statement (GANTT), 511, 514, 536

BAROFF= option

- CHART statement (GANTT), 511, 514, 536

BASELINE keyword

- PATLEVEL= option (GANTT), 521

BASELINE statement

- CPM procedure, 74, 188

BBARHT= option

CHART statement (GANTT), 511

BBAROFF= option

- CHART statement (GANTT), 511

BEFORE keyword

- MOVE statement (DTREE), 412

BETWEEN= option

- CHART statement (GANTT), 500, 570

BF= option, *see B\_FINISH= option, see B\_FINISH= option*

B\_FINISH= option

- BASELINE statement (CPM), 74
- CHART statement (GANTT), 500

BJUST option, *see BOTTOM option*

BOTTOM option

- CHART statement (GANTT), 511, 523

BOTTOMUP keyword

- CHILDORDER= option (NETDRAW), 674

BOXHT= option

- ACTNET statement (NETDRAW), 674, 690, 728

BOXWIDTH= option

- ACTNET statement (NETDRAW), 674, 690, 722

BREAKCYCLE option

- ACTNET statement (NETDRAW), 673, 748

BRKCHAR= option

- ACTNET statement (NETDRAW), 678, 685

BS= option, *see B\_START= option, see B\_START= option*

B\_START= option

- BASELINE statement (CPM), 74
- CHART statement (GANTT), 500

BUDGETCOST= parameter

- %EVA\_PLANNED\_VALUE macro, 879
- %EVA\_TASK\_METRICS macro, 886

BY statement

- GANTT procedure, 499, 528, 545, 610, 613

CA= option, *see CAXIS= option*

CACTTEXT= option, *see CTEXTCOLS= option*

CALDS= parameter

- %SASTOMSP macro parameters, 360

CALENDAR keyword

- OBSTYPE variable (CPM), 86, 114, 116

CALENDAR= option, *see CALEDATA= option, see CALEDATA= option*

CALEDATA= option

- PROC CPM statement, 65
- PROC GANTT statement, 497, 501, 597

CALENDAR= parameter

- %EVA\_EARNED\_VALUE macro, 883
- %EVA\_PLANNED\_VALUE macro, 880
- %EVA\_TASK\_METRICS macro, 887

CALID statement

- CPM procedure, 75, 175

CALID= option  
   CHART statement (GANTT), 497, 501, 597

CARCS= option  
   ACTNET statement (NETDRAW), 679, 680, 713, 715

CAXES= option, *see* CAXIS= option

CAXIS= option  
   ACTNET statement (NETDRAW), 679, 680, 742  
   CHART statement (GANTT), 512, 583

CB= option, *see* CBEST= option

CBEST= option  
   PROC DTREE statement, 403  
   TREEPLOT statement (DTREE), 414

CC= option, *see* CSYMBOLC= option

CCNODEFILL= option  
   ACTNET statement (NETDRAW), 680

CCRITARCS= option  
   ACTNET statement (NETDRAW), 679, 680, 715

CCRITOUT= option  
   ACTNET statement (NETDRAW), 680, 701, 715

CD= option, *see* CSYMBOLD= option

CE= option, *see* CSYMBOLE= option

CELL units  
   YBETWEEN= option (DTREE), 402

CENTERID option  
   ACTNET statement (NETDRAW), 680, 748

CENTERSUBTREE option  
   ACTNET statement (NETDRAW), 674, 697, 758

CFR= option, *see* CFRAVE= option

CFRAVE= option  
   CHART statement (GANTT), 512, 583, 590

CHANCE keyword  
   TYPE variable (DTREE), 416

CHART statement (GANTT), 499  
   full-screen options, 507  
   general options, 499  
   graphics options, 509  
   line-printer options, 507

CHART= parameter  
   %EVG\_GANTT\_CHART macro, 893

CHARTPCT= option, *see* CHARTWIDTH= option

CHARTWIDTH= option  
   CHART statement (GANTT), 512

CHCON= option  
   CHART statement (GANTT), 508, 512, 599

CHILDORDER= option  
   ACTNET statement (NETDRAW), 674

CL= option, *see* CLINK= option

CLINK= option  
   PROC DTREE statement, 403  
   TREEPLOT statement (DTREE), 414

CM units  
   YBETWEEN= option (DTREE), 402

CMILE= option

CHART statement (GANTT), 502, 512, 583, 586

CNODEFILL= option  
   ACTNET statement (NETDRAW), 680

COLLAPSE option  
   PROC CPM statement, 66, 181, 486, 498

COLORS= option, GOPTIONS statement  
   GANTT procedure, 512–514, 536  
   NETDRAW procedure, 681

COMBINE option  
   CHART statement (GANTT), 501, 545, 558, 603

COMPARE= option  
   BASELINE statement (CPM), 74, 190

COMPRESS option  
   ACTNET statement (NETDRAW), 680, 718  
   CHART statement (GANTT), 486, 512, 516, 523, 535, 559, 585, 590  
   PROC DTREE statement, 403  
   TREEPLOT statement (DTREE), 414, 455, 459, 475

COST= parameter  
   %EVA\_EARNED\_VALUE macro, 883  
   %EVA\_PLANNED\_VALUE macro, 880  
   %EVA\_TASK\_METRICS macro, 887

COUTLINE= option  
   ACTNET statement (NETDRAW), 681, 701, 715

CP option, *see* COMPRESS option

CPATTERN= option, GOPTIONS statement  
   GANTT procedure, 539

CPATTEXT= option, *see* CTEXTCOLS= option

CPM procedure, 61  
   ACTIVITY statement, 57, 70  
   ACTUAL statement, 70, 188  
   ALIGNDATE statement, 73, 186  
   ALIGNTYPE statement, 73, 186  
   BASELINE statement, 74, 188  
   CALID statement, 75, 175, 179  
   DURATION statement, 56, 57, 76  
   HEADNODE statement, 56, 76  
   HOLIDAY statement, 77  
   ID statement, 78, 487  
   PROC CPM statement, 65  
   PROJECT statement, 78  
   RESOURCE statement, 80, 193  
   SUCCESSOR statement, 57, 90  
   TAILNODE statement, 56, 91

CPREC= option  
   CHART statement (GANTT), 513, 619, 628

CR keyword  
   DISPLAY= option (DTREE), 400

CREF= option  
   ACTNET statement (NETDRAW), 679, 681, 736  
   CHART statement (GANTT), 505, 513, 590

CREFBRK= option  
   ACTNET statement (NETDRAW), 679, 681, 738

CRITERION= option  
 EVALUATE statement (DTREE), 411  
 PROC DTREE statement, 399, 448, 459  
 RESET statement (DTREE), 440

CRITFLAG option  
 CHART statement (GANTT), 501, 559, 570

CSYMBOL= option, GOPTIONS statement  
 GANTT procedure, 542

CSYMBOLC= option  
 PROC DTREE statement, 403  
 TREEPLOT statement (DTREE), 414

CSYMBOLD= option  
 PROC DTREE statement, 404  
 TREEPLOT statement (DTREE), 414

CSYMBOLE= option  
 PROC DTREE statement, 404  
 TREEPLOT statement (DTREE), 414

CT= option, *see* CTEXT= option, *see* CTEXT= option,  
*see* CTEXT= option

CTEXT= option  
 ACTNET statement (NETDRAW), 681  
 CHART statement (GANTT), 513, 536, 555, 583  
 PROC DTREE statement, 404  
 TREEPLOT statement (DTREE), 414

CTEXT= option, GOPTIONS statement  
 GANTT procedure, 513, 536  
 NETDRAW procedure, 681

CTEXTCOLS= option  
 CHART statement (GANTT), 513

CTNOW= option  
 CHART statement (GANTT), 507, 514, 601, 603

CUMUSAGE option  
 RESOURCE statement (CPM), 82, 129, 207

CURRDATE= option, *see* TIMENOW= option

CZLINE= option, *see* CZONE= option

CZONE= option  
 CHART statement (GANTT), 514, 524, 645

DATA= option  
 PROC CPM statement, 66, 144  
 PROC GANTT statement, 497, 501  
 PROC NETDRAW statement, 672, 708

DATE statement, *see* ALIGNDATE statement

DATE= option  
 PROC CPM statement, 66, 93, 144

DAY keyword  
 INTERVAL= option (CPM), 67  
 INTERVAL= option (GANTT), 503, 531  
 MININTERVAL= option (GANTT), 529  
 MININTERVAL= option (NETDRAW), 675  
 PADDING= option (GANTT), 505, 528  
 ROUTINTERVAL= option (CPM), 88

DAYLENGTH= option  
 CHART statement (GANTT), 501, 531

PROC CPM statement, 66, 94, 159

DAYSTART= option  
 CHART statement (GANTT), 501, 531  
 PROC CPM statement, 66, 159

DBMS= parameter  
 %MSPTOSAS macro parameters, 355  
 %SASTOMSP macro parameters, 364

DECISION keyword  
 TYPE variable (DTREE), 416

DEFID= parameter  
 %EVG\_WBS\_CHART macro, 894

DELAY= option  
 RESOURCE statement (CPM), 82, 121, 207

DELAYANALYSIS option  
 RESOURCE statement (CPM), 82, 99, 197

DELAYLST keyword  
 SCHEDRULE= option (CPM), 88, 120

DES= option, *see* DESCRIPTION= option, *see*  
 DESCRIPTION= option, *see*  
 DESCRIPTION= option

DESC option, *see* DESCENDING option

DESCENDING option  
 PROJECT statement (CPM), 78

DESCRIPTION= option  
 ACTNET statement (NETDRAW), 681  
 CHART statement (GANTT), 514  
 PROC DTREE statement, 404  
 TREEPLOT statement (DTREE), 414

DISPLAY= option  
 PROC DTREE statement, 400  
 TREEPLOT statement (DTREE), 414

DOANNO option, *see* DOANNOTATE option

DOANNOTATE option  
 PROC DTREE statement, 405  
 TREEPLOT statement (DTREE), 414

DP option  
 ACTNET statement (NETDRAW), 674, 690, 730

DRAIN keyword  
 ERRHANDLE= option (DTREE), 400

DTDAY keyword  
 INTERVAL= option (CPM), 67  
 INTERVAL= option (GANTT), 503, 531  
 MININTERVAL= option (GANTT), 529  
 ROUTINTERVAL= option (CPM), 88

DTHOUR keyword  
 INTERVAL= option (CPM), 67  
 INTERVAL= option (GANTT), 503, 531  
 MININTERVAL= option (GANTT), 529  
 PADDING= option (GANTT), 505, 528  
 ROUTINTERVAL= option (CPM), 88

DTMINUTE keyword  
 INTERVAL= option (CPM), 67  
 INTERVAL= option (GANTT), 503, 531  
 MININTERVAL= option (GANTT), 529

- PADDING= option (GANTT), 505, 528  
 ROUTINTERVAL= option (CPM), 88
- DTMONTH keyword  
 INTERVAL= option (CPM), 94  
 INTERVAL= option (CPM), 67  
 MININTERVAL= option (GANTT), 529  
 PADDING= option (GANTT), 505, 528  
 ROUTINTERVAL= option (CPM), 88
- DTQTR keyword  
 INTERVAL= option (CPM, 94  
 INTERVAL= option (CPM), 67  
 MININTERVAL= option (GANTT), 529  
 PADDING= option (GANTT), 505, 528  
 ROUTINTERVAL= option (CPM), 88
- DTREE procedure, 395  
 EVALUATE statement, 411  
 MODIFY statement, 411  
 MOVE statement, 412  
 PROC DTREE statement, 399  
 QUIT statement, 412  
 RECALL statement, 412  
 RESET statement, 412  
 SAVE statement, 413  
 SUMMARY statement, 413  
 TREEPLOT statement, 413  
 VARIABLES statement, 414  
 VPC statement, 417  
 VPI statement, 418
- DTSECOND keyword  
 INTERVAL= option (CPM), 67  
 INTERVAL= option (GANTT), 503, 531  
 MININTERVAL= option (GANTT), 529  
 PADDING= option (GANTT), 505, 528  
 ROUTINTERVAL= option (CPM), 88
- DTWEEK keyword  
 INTERVAL= option (CPM, 94  
 INTERVAL= option (CPM), 67  
 MININTERVAL= option (GANTT), 529  
 PADDING= option (GANTT), 505, 528  
 ROUTINTERVAL= option (CPM), 88
- DTWRKDAY keyword  
 INTERVAL= option (CPM), 67, 94  
 INTERVAL= option (GANTT), 503, 531  
 ROUTINTERVAL= option (CPM), 88
- DTYEAR keyword  
 INTERVAL= option (CPM, 94  
 INTERVAL= option (CPM), 67  
 MININTERVAL= option (GANTT), 529  
 PADDING= option (GANTT), 505, 528  
 ROUTINTERVAL= option (CPM), 88
- DUPOK option  
 CHART statement (GANTT), 502, 524
- DUR statement, *see* DURATION statement  
 DUR= option, *see* DURATION= option
- DURATION statement  
 CPM procedure, 56, 57, 76, 142
- DURATION= option  
 ACTNET statement (NETDRAW), 674, 710  
 CHART statement (GANTT), 502, 505, 526, 528, 582, 583, 607
- DURATION= parameter  
 %EVA\_EARNED\_VALUE macro, 883  
 %EVA\_PLANNED\_VALUE macro, 880  
 %EVA\_TASK\_METRICS macro, 887  
 %EVG\_GANTT\_CHART macro, 893
- EACFORM= parameter  
 %EVA\_METRICS macro, 885
- EARLY keyword  
 COMPARE= option (CPM), 74  
 PATLEVEL= option (GANTT), 521  
 SET= option (CPM), 75  
 UPDATE= option (CPM), 75
- Earned Value Analysis macros  
 syntax, 879
- EBARHT= option  
 CHART statement (GANTT), 514
- EBAROFF= option  
 CHART statement (GANTT), 514
- EF= option, *see* E\_FINISH= option  
 E\_FINISH= option  
 CHART statement (GANTT), 502
- END keyword  
 TYPE variable (DTREE), 416
- ERRHANDLE= option  
 PROC DTREE statement, 400
- ES= option, *see* E\_START= option  
 ESO option, *see* ESORDER option  
 ESORDER option  
 PROJECT statement (CPM), 78
- ESP option, *see* ESPROFILE option  
 ESPROFILE option  
 RESOURCE statement (CPM), 83, 128
- ESS option, *see* ESPROFILE option  
 E\_START option  
 RESOURCE statement (CPM), 83
- E\_START= option  
 CHART statement (GANTT), 502
- ESTIMATEPCTC option  
 ACTUAL statement (CPM), 71  
 ACTUAL statement (PM), 305
- ESTPCTC option, *see* ESTIMATEPCTC option  
 ESTPCTCOMP option, *see* ESTIMATEPCTC option  
 ESTPROG option, *see* ESTIMATEPCTC option  
 EV keyword  
 DISPLAY= option (DTREE), 400
- EV= parameter  
 %EVA\_EARNED\_VALUE macro, 883

%EVA\_METRICS macro, 885  
 EVA\_EARNED\_VALUE macro, 882, 897  
 EVA\_METRICS macro, 885, 898  
 EVA\_PLANNED\_VALUE macro, 879, 897  
 EVA\_TASK\_METRICS macro, 886, 900  
 EVALUATE statement  
     DTREE procedure, 411  
 EVENT= option  
     VARIABLES statement (DTREE), 416, 439  
 EVG\_COST\_PLOT macro, 889, 900  
 EVG\_GANTT\_CHART macro, 892, 902  
 EVG\_INDEX\_PLOT macro, 891, 901  
 EVG\_SCHEDULE\_PLOT macro, 890, 901  
 EVG\_VARIANCE\_PLOT macro, 892, 901  
 EVG\_WBS\_CHART macro, 894, 902  
 EXCLUNSCHED option  
     RESOURCE statement (CPM), 83  
 EXPAND option, *see* ADDACT option  
  
 FBDATE= option  
     PROC CPM statement, 66, 93, 149  
 FEQ keyword  
     ALIGNTYPE variable (CPM), 73  
 FF keyword  
     LAG variable (CPM), 91  
     LAG variable (GANTT), 517  
     LAG variable (NETDRAW), 675  
 F\_FLOAT option  
     RESOURCE statement (CPM), 83, 226  
 FGE keyword  
     ALIGNTYPE variable (CPM), 73  
 FILL option  
     CHART statement (GANTT), 503, 528, 531, 570  
 FILLMISSING option, *see* FILLUNSCHED option  
 FILLPAGE option  
     ACTNET statement (NETDRAW), 681  
 FILLUNSCHED option  
     RESOURCE statement (CPM), 83  
 FINISH= option  
     DURATION statement (CPM), 76  
 FINISH= parameter  
     %EVA\_EARNED\_VALUE macro, 883  
     %EVA\_PLANNED\_VALUE macro, 881  
     %EVA\_TASK\_METRICS macro, 887  
     %EVG\_GANTT\_CHART macro, 893  
 FINISHBEFORE option  
     PROC CPM statement, 67  
 FINPAD= option, *see* PADDING= option  
 FIXASTART option  
     ACTUAL statement (CPM), 71  
 FIXFINISH option  
     PROC CPM statement, 67  
 FLAG keyword  
     CTEXTCOLS= option (GANTT), 513  
 FLAG option, *see* CRITFLAG option  
 FLE keyword  
     ALIGNTYPE variable (CPM), 73  
 FMILE= option  
     CHART statement (GANTT), 502, 514, 523, 583  
 FONT= option, *see* FTEXT= option  
     ACTNET statement (NETDRAW), 681, 713  
     CHART statement (GANTT), 514, 536, 555, 586,  
         592  
 FORMCHAR= option  
     ACTNET statement (NETDRAW), 679, 685  
     CHART statement (GANTT), 507, 557  
     PROC DTREE statement, 410  
     TREEPLOT statement (DTREE), 414  
 FRAMCLIP keyword  
     LABRULE= option (GANTT), 517  
 FRAME option  
     ACTNET statement (NETDRAW), 674, 736, 738  
 FROM statement, *see* TAILNODE statement  
 FS keyword  
     LAG variable (CPM), 91  
     LAG variable (GANTT), 517  
     LAG variable (NETDRAW), 675  
 FS option, *see* FULLSCREEN option, *see*  
     FULLSCREEN option  
 FTEXT= option  
     PROC DTREE statement, 405  
     TREEPLOT statement (DTREE), 414, 455, 475  
 FTEXT= option, GOPTIONS statement  
     GANTT procedure, 514, 536  
     NETDRAW procedure, 681  
 FULLSCREEN option  
     PROC GANTT statement, 485, 497, 531  
     PROC NETDRAW statement, 663, 672, 697  
  
 GANTT procedure, 492  
     BY statement, 499, 545, 610, 613  
     CHART statement, 499  
     ID statement, 524, 545, 558, 570, 604  
     PROC GANTT statement, 496  
 GIVEN= option  
     VARIABLES statement (DTREE), 416  
 GOPTIONS statement  
     COLORS= option, 512–514, 536, 681  
     CPATTERN= option, 539  
     CSYMBOL= option, 542  
     CTEXT= option, 513, 536, 681  
     FTEXT= option, 514, 536, 681  
     GUNIT= option, 536  
     HPOS= option, 535, 557, 701, 713, 721  
     HTEXT= option, 515, 536  
     RESET= option, 539, 541  
     VPOS= option, 515, 535, 701, 713, 721  
 GOUT= option

PROC DTREE statement, 405  
 PROC GANTT statement, 497  
 PROC NETDRAW statement, 672  
 TREEPLOT statement (DTREE), 414  
**GRAPHICS option**  
   PROC DTREE statement, 400, 455, 459  
   PROC GANTT statement, 485, 497, 575  
   PROC NETDRAW statement, 663, 672, 713  
   TREEPLOT statement (DTREE), 414, 475  
**GUNIT= option, GOPTIONS statement**  
   GANTT procedure, 536  
  
**HBARHT= option**  
   CHART statement (GANTT), 514, 515  
**HBAROFF= option**  
   CHART statement (GANTT), 514, 515  
**HBETWEEN= option, *see* XBETWEEN= option**  
**HBY option, GOPTIONS statement**  
   GANTT procedure, 610  
**HCONCHAR= option**  
   CHART statement (GANTT), 508, 518, 557  
**HCONNECT option**  
   CHART statement (GANTT), 503, 508, 518, 599  
**HDURATION= option, *see* HOLIDUR= option, *see* HOLIDUR= option**  
**HEAD statement, *see* HEADNODE statement**  
**HEAD= option**  
   CHART statement (GANTT), 515, 545, 621  
**HEADNODE statement**  
   CPM procedure, 56, 76, 146  
**HEADNODE= option, *see* HEAD= option**  
**HEIGHT= option**  
   ACTNET statement (NETDRAW), 681  
   CHART statement (GANTT), 515, 516, 536, 617  
**HEIGHT= parameter**  
   %EVG\_GANTT\_CHART macro, 893  
**HMARGIN= option**  
   ACTNET statement (NETDRAW), 681, 734, 745  
**HMILE= option**  
   CHART statement (GANTT), 502, 515  
**HOLDS= parameter**  
   %SASTOMSP macro parameters, 360  
**HOLICHAR= option**  
   CHART statement (GANTT), 504, 508, 557  
**HOLIDATA= option**  
   PROC CPM statement, 67, 161  
   PROC GANTT statement, 497, 501, 576  
**HOLIDATA= parameter**  
   %EVA\_EARNED\_VALUE macro, 883  
   %EVA\_PLANNED\_VALUE macro, 881  
   %EVA\_TASK\_METRICS macro, 887  
**HOLIDAY statement**  
   CPM procedure, 77, 161  
**HOLIDAY= option, *see* HOLIDATA= option**  
  
**CHART statement (GANTT), 497, 503, 576, 599**  
**HOLIDAY= parameter**  
   %EVA\_EARNED\_VALUE macro, 883  
   %EVA\_PLANNED\_VALUE macro, 881  
   %EVA\_TASK\_METRICS macro, 887  
**HOLIDAYS statement, *see* HOLIDAY statement**  
**HOLIDAYS= option, *see* HOLIDAY= option**  
**HOLIDUR= option**  
   CHART statement (GANTT), 503, 592  
   HOLIDAY statement (CPM), 77, 161  
**HOLIEND= option, *see* HOLIFIN= option, *see* HOLIFIN= option**  
**HOLIFIN= option**  
   CHART statement (GANTT), 503, 576, 599  
   HOLIDAY statement (CPM), 77, 161  
**HOLINTERVAL= option, *see* INTERVAL= option**  
**HOUR keyword**  
   INTERVAL= option (CPM), 67  
   MININTERVAL= option (GANTT), 529  
   MININTERVAL= option (NETDRAW), 675  
   PADDING= option (GANTT), 505, 528  
   ROUTINTERVAL= option (CPM), 88  
**HPAGES= option**  
   ACTNET statement (NETDRAW), 681  
   CHART statement (GANTT), 512, 515, 522, 523,  
     535, 559, 585  
**HPAGES= parameter**  
   %EVG\_GANTT\_CHART macro, 893  
**HPOS= option, GOPTIONS statement**  
   GANTT procedure, 535, 557  
   NETDRAW procedure, 701, 713, 721  
**HS= option, *see* HSYMBOL= option**  
**HSYMBOL= option**  
   PROC DTREE statement, 405  
   TREEPLOT statement (DTREE), 414, 455, 475  
**HT= option, *see* HTEXT= option**  
**HTEXT= option, *see* HEIGHT= option**  
   PROC DTREE statement, 405  
   TREEPLOT statement (DTREE), 414  
**HTEXT= option, GOPTIONS statement**  
   GANTT procedure, 515, 536  
**HTML= option, *see* WEB= option, *see* WEB= option, *see* WEB= option**  
**HTOFF= option**  
   CHART statement (GANTT), 515, 516, 536, 617  
**HTRACKS= option**  
   ACTNET statement (NETDRAW), 674, 690, 730  
  
**ID keyword**  
   CTEXTCOLS= option (GANTT), 513  
**ID statement**  
   CPM procedure, 78, 144, 487  
   GANTT procedure, 524, 545, 558, 570, 604  
**ID= option**

- ACTNET statement (NETDRAW), 674, 690
- ID= parameter
  - %EVG\_GANTT\_CHART macro, 893
  - %EVG\_WBS\_CHART macro, 894
- IDPAGES option
  - CHART statement (GANTT), 503, 525, 559
- IGNOREPARENTRES option
  - PROJECT statement (CPM), 79
- IGNOREPR option, *see* IGNOREPARENTRES option
- IGNOREP\_RES option, *see* IGNOREPARENTRES option
- IMAGEMAP= option
  - PROC DTREE statement, 406, 431
  - PROC GANTT statement, 498, 556
  - PROC NETDRAW statement, 672
  - TREEPLOT statement (DTREE), 414
- INCH units
  - YBETWEEN= option (DTREE), 402
- INCLUNSCHED option
  - RESOURCE statement (CPM), 83
- INCREMENT= option
  - CHART statement (GANTT), 503, 529
- INDEPALLOC option, *see* INDEPENDENTALLOC option
- INDEPENDENTALLOC option
  - RESOURCE statement (CPM), 84, 122
- INFEASDIAG option, *see* INFEASDIAGNOSTIC option
- INFEASDIAGNOSTIC option
  - RESOURCE statement (CPM), 84, 121, 130, 211
- INTERVAL= option
  - CHART statement (GANTT), 497, 501, 503, 504, 530, 531, 592
  - PROC CPM statement, 66, 67, 94, 95, 155
- INTERVAL= parameter
  - %EVA\_EARNED\_VALUE macro, 883
  - %EVA\_PLANNED\_VALUE macro, 881
  - %EVA\_TASK\_METRICS macro, 888
- INTPER= option
  - PROC CPM statement, 67
- INTUSAGE option, *see* TOTUSAGE option
- INTXRATE option, *see* TOTUSAGE option
- JOBNUM keyword
  - CTEXTCOLS= option (GANTT), 513
- JOINCHAR= option
  - CHART statement (GANTT), 508, 557
- L= option, *see* LSTYLE= option
- LABDATA= option
  - PROC GANTT statement, 498, 552, 556
- LABEL option
  - PROC DTREE statement, 400
  - TREEPLOT statement (DTREE), 414
- LABEL= option, *see* LABDATA= option
- LABELDATA= option, *see* LABDATA= option
- LABELSPLIT= option, *see* LABSPLIT= option
- LABFMT= option, *see* LABRULE= option
- LABMAXINT= option
  - PROC GANTT statement, 498, 555
- LABRULE= option
  - CHART statement (GANTT), 517
- LABSPLIT= option
  - CHART statement (GANTT), 517, 636
- LABVAR= option
  - CHART statement (GANTT), 516, 552, 553, 636, 639
- LAG= option
  - ACTNET statement (NETDRAW), 675
  - CHART statement (GANTT), 517, 546, 619, 628
  - PROC GANTT statement, 546
  - SUCCESSOR statement (CPM), 90, 91, 95, 181
- LATE keyword
  - COMPARE= option (CPM), 74
  - PATLEVEL= option (GANTT), 521
  - SET= option (CPM), 75
  - UPDATE= option (CPM), 75
- LB= option, *see* LSTYLEB= option
- LBARHT= option
  - CHART statement (GANTT), 514
- LBAROFF= option
  - CHART statement (GANTT), 514
- LC= option, *see* LSTYLEC= option
- LEFT keyword
  - ZONESPAN= option (GANTT), 524
- LEFT option
  - CHART statement (GANTT), 518, 522
- LEFTRGHT keyword
  - CHILDORDER= option (NETDRAW), 674
- LEGEND option
  - PROC DTREE statement, 406
  - TREEPLOT statement (DTREE), 414
- LEVEL= option
  - CHART statement (GANTT), 514, 518, 546, 619
- LF= option, *see* L\_FINISH= option
- L\_FINISH= option
  - CHART statement (GANTT), 504, 607
- LFT keyword
  - SCHEDRULE= option (CPM), 88, 120
- LG option, *see* LEGEND option
- LHCON= option
  - CHART statement (GANTT), 508, 518, 557, 599
- LIBRARY= parameter
  - %MSPTOSAS macro parameters, 354
  - %SASTOMSP macro parameters, 360
- LINEAR option
  - ACTNET statement (NETDRAW), 675, 694, 738
- LINEPRINTER option

- PROC DTREE statement, 401
- PROC GANTT statement, 485, 498
- PROC NETDRAW statement, 672
- TREEPLOT statement (DTREE), 414
- LINESIZE system option, 528
- LINK keyword
  - DISPLAY= option (DTREE), 400
- LINKA= option
  - PROC DTREE statement, 406
  - TREEPLOT statement (DTREE), 414, 459
- LINKB= option
  - PROC DTREE statement, 406
  - TREEPLOT statement (DTREE), 414, 459
- LINKC= option
  - PROC DTREE statement, 406
  - TREEPLOT statement (DTREE), 414
- LJUST option, *see* LEFT option
- LMI= option, *see* LABMAXINT= option
- LOSS= option, *see* VALUE= option
- LP option, *see* LINEPRINTER option, *see*
  - LINEPRINTER option, *see* LINEPRINTER option
- LPREC= option
  - CHART statement (GANTT), 518, 619
- LREF= option
  - ACTNET statement (NETDRAW), 682, 736
  - CHART statement (GANTT), 505, 518, 557, 590, 628
- LREFBRK= option
  - ACTNET statement (NETDRAW), 682, 738
- LS= option, *see* L\_START= option
- LSO option, *see* LSORDER option
- LSORDER option
  - PROJECT statement (CPM), 79
- LSP option, *see* LSPPROFILE option
- LSPPROFILE option
  - RESOURCE statement (CPM), 84, 128
- LSS option, *see* LSPPROFILE option
- LST keyword
  - SCHEDRULE= option (CPM), 88, 121
- L\_START option
  - RESOURCE statement (CPM), 84
- L\_START= option
  - CHART statement (GANTT), 504, 607
- LSTYLE= option
  - PROC DTREE statement, 407
  - TREEPLOT statement (DTREE), 414
- LSTYLEB= option
  - PROC DTREE statement, 407
  - TREEPLOT statement (DTREE), 414, 455
- LSTYLEC= option
  - PROC DTREE statement, 407
  - TREEPLOT statement (DTREE), 414
- LTHICK= option, *see* LWIDTH= option
- LTHICKB= option, *see* LWIDTHB= option
- LTNOW= option
  - CHART statement (GANTT), 507, 518, 557, 601, 603
- LWCRT= option
  - ACTNET statement (NETDRAW), 682, 715
- LWIDTH= option
  - ACTNET statement (NETDRAW), 682, 713, 715
  - CHART statement (GANTT), 505, 518
  - PROC DTREE statement, 407
  - TREEPLOT statement (DTREE), 414, 455, 475
- LWIDTHB= option
  - PROC DTREE statement, 407
  - TREEPLOT statement (DTREE), 414, 455, 475
- LWOUTLINE= option
  - ACTNET statement (NETDRAW), 682
- LZLINE= option, *see* LZONE= option
- LZONE= option
  - CHART statement (GANTT), 518, 524, 645
- M= option, *see* MAXDEC= option
- MAPFILE= parameter
  - %MSPTOSAS macro parameters, 354
- MARKBREAK option
  - CHART statement (GANTT), 501, 504, 531, 594
- MARKWKND option
  - CHART statement (GANTT), 504, 531
- MAXCE keyword
  - CRITERION= option (DTREE), 400, 401
- MAXDATE= option
  - CHART statement (GANTT), 504, 507, 520, 548, 590, 594, 597, 610, 624
  - RESOURCE statement (CPM), 84, 128, 194
- MAXDEC= option
  - PROC GANTT statement, 498, 555
- MAXDISLV= option
  - CHART statement (GANTT), 519, 546, 548, 550, 624, 625
- MAXEMPTY= option, *see* MAXNULLCOLUMN= option
- MAXEV keyword
  - CRITERION= option (DTREE), 400
- MAXIDS option
  - CHART statement (GANTT), 504, 525
- MAXMLV keyword
  - CRITERION= option (DTREE), 400
- MAXNCOL= option, *see* MAXNULLCOLUMN= option
- MAXNSEG= option, *see* MAXNSEGMT= option
- MAXNSEGMT= option
  - RESOURCE statement (CPM), 84, 89, 122
- MAXNULLCOLUMN= option
  - ACTNET statement (NETDRAW), 675, 694
- MAXOBS= option

RESOURCE statement (CPM), 85  
 MAXOBS= parameter  
   %EVA\_EARNED\_VALUE macro, 883  
   %EVA\_PLANNED\_VALUE macro, 881  
 MAXPREC= option  
   EVALUATE statement (DTREE), 411  
   PROC DTREE statement, 401  
   SUMMARY statement (DTREE), 413  
   TREEPLOT statement (DTREE), 414  
 MAXWIDTH= option  
   EVALUATE statement (DTREE), 411  
   PROC DTREE statement, 401  
   SUMMARY statement (DTREE), 413  
   TREEPLOT statement (DTREE), 414  
 MAXZCOL= option, *see* MAXNULLCOLUMN= option  
 MDBFILE= parameter  
   %MSPTOSAS macro parameters, 354  
   %SASTOMSP macro parameters, 360  
 METRICS= parameter  
   %EVA\_METRICS macro, 885  
   %EVG\_COST\_PLOT macro, 889  
   %EVG\_INDEX\_PLOT macro, 891  
   %EVG\_SCHEDULE\_PLOT macro, 890  
   %EVG\_VARIANCE\_PLOT macro, 892  
 MF keyword  
   ALIGNTYPE variable (CPM), 73  
 MILECHAR= option  
   CHART statement (GANTT), 502, 508, 557  
 MILESTONEORESOURCE  
   RESOURCE statement (CPM), 85  
 MILESTONERESOURCE  
   RESOURCE statement (CPM), 85  
 MINARATE keyword  
   OBSTYPE variable (CPM), 86, 114, 116, 125  
 MINCE keyword  
   CRITERION= option (DTREE), 400, 401  
 MINDATE= option  
   CHART statement (GANTT), 504, 520, 548, 590, 594, 597, 610  
   RESOURCE statement (CPM), 85, 128  
 MINEV keyword  
   CRITERION= option (DTREE), 400  
 MININTERVAL= option  
   ACTNET statement (NETDRAW), 675, 694, 742  
   CHART statement (GANTT), 501, 504–506, 529, 536, 586, 594, 597  
 MININTGV= option  
   CHART statement (GANTT), 519, 546, 548, 549, 622, 624  
 MINMLV keyword  
   CRITERION= option (DTREE), 400  
 MINOFFGV= option  
   CHART statement (GANTT), 519, 546, 548, 549, 622, 624  
 CHART statement (GANTT), 519, 546, 548, 549, 622  
 MINOFFLV= option  
   CHART statement (GANTT), 520, 546, 548, 550, 624, 626  
 MINSEGD= option, *see* MINSEGMDUR= option  
 MINSEGMDUR= option  
   RESOURCE statement (CPM), 85, 89, 122, 228  
 MINUTE keyword  
   INTERVAL= option (CPM), 67  
   MININTERVAL= option (GANTT), 529  
   MININTERVAL= option (NETDRAW), 675  
   PADDING= option (GANTT), 505, 528  
   ROUTINTERVAL= option (CPM), 88  
 MODIFY statement  
   DTREE procedure, 411, 463, 466, 468  
 MONTH keyword  
   INTERVAL= option (CPM), 67  
   MININTERVAL= option (GANTT), 529  
   MININTERVAL= option (NETDRAW), 675  
   PADDING= option (GANTT), 505, 528  
   ROUTINTERVAL= option (CPM), 88  
 MOVE statement  
   DTREE procedure, 412, 465  
 MS keyword  
   ALIGNTYPE variable (CPM), 73  
 %MSPTOSAS macro parameters  
   DBMS= parameter, 355  
   LIBRARY= parameter, 354  
   PORT= parameter, 355  
   SERVER= parameter, 355  
   VERSION= parameter, 355  
   VIEWPM= parameter, 355  
 MULTALT keyword  
   OBSTYPE variable (CPM), 86, 114, 116, 125  
 MULTALT option, *see* MULTIPLEALTERNATES option  
 MULTIPLEALTERNATES option  
   RESOURCE statement (CPM), 85, 124, 125  
 NACTS= option, *see* NJOBS= option  
   PROC CPM statement, 67  
 NADJ= option  
   PROC CPM statement, 67  
 NAME= option, *see* PROJECTNAME= option  
   ACTNET statement (NETDRAW), 682  
   CHART statement (GANTT), 520  
   PROC DTREE statement, 408  
   TREEPLOT statement (DTREE), 414, 455  
 NETDRAW procedure, 668  
   ACTNET statement, 673  
   PROC NETDRAW statement, 672  
 NINCRS= option, *see* NTICKS= option  
 NJOBS= option

CHART statement (GANTT), 520  
**NLAGCAL=** option  
  SUCCESSOR statement (CPM), 91  
**NLEVELSPERCOLUMN=** option  
  ACTNET statement (NETDRAW), 675, 694  
**NNODES=** option  
  PROC CPM statement, 67  
**NOANNO** option, *see* NOANNOTATE option  
**NOANNOTATE** option  
  PROC DTREE statement, 405  
  TREEPLOT statement (DTREE), 414  
**NOARRHD** option, *see* NOARROWHEAD option  
**NOARROWFILL** option  
  ACTNET statement (NETDRAW), 682, 745  
**NOARROWHEAD** option  
  CHART statement (GANTT), 520, 550  
**NOAUTOUPTD** option  
  ACTUAL statement (CPM), 71, 111, 190  
**NOBYLINE** option, OPTIONS statement  
  GANTT procedure, 610, 613  
**NOCOMPRESS** option  
  PROC DTREE statement, 403  
  TREEPLOT statement (DTREE), 414  
**NOCP** option, *see* NOCOMPRESS option  
**NODEFID** option  
  ACTNET statement (NETDRAW), 676, 690, 722  
**NODETRACK** option  
  ACTNET statement (NETDRAW), 676  
**NODISPLAY** option  
  PROC NETDRAW statement, 672  
  PROC PM statement, 304  
**NOE\_START** option  
  RESOURCE statement (CPM), 86  
**NOEXTRANGE** option  
  CHART statement (GANTT), 504, 520, 548  
**NOFLOAT** option  
  RESOURCE statement (CPM), 86  
**NOFR** option, *see* NOFRAME option  
**NOFRAME** option  
  CHART statement (GANTT), 512, 520, 557  
**NOJOBNUM** option  
  CHART statement (GANTT), 505, 570  
**NOLABEL** option  
  ACTNET statement (NETDRAW), 676, 690, 722  
  CHART statement (GANTT), 559  
  PROC DTREE statement, 400  
  TREEPLOT statement (DTREE), 414  
**NOLEGEND** option  
  CHART statement (GANTT), 505, 531, 558, 570  
  PROC DTREE statement, 406, 459  
  TREEPLOT statement (DTREE), 414, 475  
**NOLG** option, *see* NOLEGEND option  
**NOL\_START** option  
  RESOURCE statement (CPM), 86  
**NONDP** option  
  ACTNET statement (NETDRAW), 676  
**NONE** keyword  
  PADDING= option (GANTT), 505, 528  
  ZONESPAN= option (GANTT), 524  
**NONODETRACK** option  
  ACTNET statement (NETDRAW), 676  
**NONNUMBER** option, *see* NOPAGENUMBER option  
**NOPAGENUM** option  
  CHART statement (GANTT), 520  
  PROC DTREE statement, 408  
  TREEPLOT statement (DTREE), 414  
**NOPAGENUMBER** option, *see* NOPAGENUM option  
  ACTNET statement (NETDRAW), 682  
**NOPATBAR** option  
  CHART statement (GANTT), 520  
**NORC** option  
  PROC DTREE statement, 408  
  TREEPLOT statement (DTREE), 414  
**NOREPEATAXIS** option  
  ACTNET statement (NETDRAW), 676  
**NORESOURCEVARS** option  
  RESOURCE statement (CPM), 86  
**NORESVARS** option, *see* NORESOURCEVARS option  
  NORESVARSOOUT option, *see* NORESOURCEVARS option  
**NOSCALE** option  
  PROC DTREE statement, 399  
**NOSUMMARY** option  
  EVALUATE statement (DTREE), 411  
  PROC DTREE statement, 401  
**NOT\_FLOAT** option  
  RESOURCE statement (CPM), 86  
**NOTIMEAXIS** option  
  ACTNET statement (NETDRAW), 676  
**NOTMTIME** option  
  CHART statement (GANTT), 520  
**NOTNLABEL** option  
  CHART statement (GANTT), 505, 601  
**NOUTIL** option  
  PROC CPM statement, 68  
**NOVCENTER** option  
  ACTNET statement (NETDRAW), 683, 691, 734  
**NOWARNING** option  
  PROC DTREE statement, 402  
**NOXTRNG** option, *see* NOEXTRANGE option  
**NOZONECOL** option  
  CHART statement (GANTT), 520, 524, 559  
**NOZONEDESCR** option, *see* NOZONELABEL option  
**NOZONELABEL** option  
  ACTNET statement (NETDRAW), 676

NPERCOL= option, *see* NLEVELSPERCOLUMN= option  
 NRESREQ= option  
   PROC CPM statement, 68  
 NROUTCAL= option  
   RESOURCE statement (CPM), 86, 128  
 NROUTCAL= parameter  
   %EVA\_EARNED\_VALUE macro, 884  
   %EVA\_PLANNED\_VALUE macro, 881  
 NTICKS= option  
   CHART statement (GANTT), 521  
 NWIDTH= option  
   EVALUATE statement (DTREE), 411  
   PROC DTREE statement, 401  
   SUMMARY statement (DTREE), 413  
   TREEPLOT statement (DTREE), 414  
 NXNODES= option  
   ACTNET statement (NETDRAW), 683  
 NXPAGES= option, *see* HPAGES= option  
 NYNODES= option  
   ACTNET statement (NETDRAW), 683  
 NYPAGES= option, *see* VPAGES= option  
 OBSTYPE= option  
   RESOURCE statement (CPM), 86, 198  
 ODS HTML statement, 646  
   ANCHOR= option, 648  
   CLOSE option, 649  
   FILE= option, 647  
 ONEZONEVAL option  
   CHART statement (GANTT), 521  
 ORDERALL option  
   PROJECT statement (CPM), 79  
 OUT= option  
   PROC CPM statement, 68, 146  
   PROC NETDRAW statement, 673  
 OUTCOME= option  
   VARIABLES statement (DTREE), 415, 439  
 OVERLAPCH= option  
   CHART statement (GANTT), 508, 509  
 OVERRIDEDEDUR option  
   DURATION statement (CPM), 76  
 OVPCHAR= option  
   CHART statement (GANTT), 508  
 P keyword  
   DISPLAY= option (DTREE), 400  
 PADDING= option  
   CHART statement (GANTT), 505, 526, 528, 582  
 PAGECLIP keyword  
   LABRULE= option (GANTT), 517  
 PAGELIMIT= option  
   CHART statement (GANTT), 505  
 PAGENUM option, *see* PAGENUMBER option  
 CHART statement (GANTT), 521  
 PROC DTREE statement, 408  
 TREEPLOT statement (DTREE), 414  
 PAGENUMBER option, *see* PAGENUM option  
   ACTNET statement (NETDRAW), 683  
 PAGES= option, *see* PAGELIMIT= option  
   ACTNET statement (NETDRAW), 676  
 PAGESIZE system option, 528  
 PARENT statement, *see* PROJECT statement  
 PATLEVEL= option  
   CHART statement (GANTT), 513, 521, 536  
 PATTERN statement, 503, 537, 557, 575  
   options, 539  
   syntax, 538  
 PATTERN= option  
   ACTNET statement (NETDRAW), 679, 683, 696, 698, 701, 732  
   CHART statement (GANTT), 521, 536, 537  
 PATVAR= option, *see* PATTERN= option  
 PAYOFFS= option, *see* VALUE= option  
   PROC DTREE statement, 401  
 PCOMP= option, *see* PCTCOMP= option  
 PCOMPRESS option  
   ACTNET statement (NETDRAW), 683, 718  
   CHART statement (GANTT), 486, 512, 516, 522, 523, 535, 559, 585  
 PCT units  
   YBETWEEN= option (DTREE), 402  
 PCTCOMP= option  
   ACTUAL statement (CPM), 72, 190  
 PCTCOMP= parameter  
   %EVA\_TASK\_METRICS macro, 888  
 PCTCOMPLETE= option, *see* PCTCOMP= option  
 PER= option, *see* PERIOD= option  
 PERIOD= option  
   RESOURCE statement (CPM), 86, 198  
 PLANCOST= parameter  
   %EVA\_PLANNED\_VALUE macro, 879  
   %EVA\_TASK\_METRICS macro, 886  
 PLANSCHED= parameter  
   %EVA\_PLANNED\_VALUE macro, 879  
   %EVA\_TASK\_METRICS macro, 887  
   %EVG\_GANTT\_CHART macro, 893  
 PLOT= parameter  
   %EVG\_COST\_PLOT macro, 890  
   %EVG\_INDEX\_PLOT macro, 891  
   %EVG\_SCHEDULE\_PLOT macro, 890  
   %EVG\_VARIANCE\_PLOT macro, 892  
 PM procedure  
   PROC PM statement, 304  
 PORT= parameter  
   %MSPTOSAS macro parameters, 355  
   %SASTOMSP macro parameters, 364  
 PRECDATA= option

- PROC GANTT statement, 487, 498, 510, 517, 523, 526, 628
- PROB= option
  - VARIABLES statement (DTREE), 417, 439
- PROBIN= option
  - PROC DTREE statement, 401
- PROC CPM statement, *see* CPM procedure
  - statement options, 65
- PROC DTREE statement, *see* DTREE procedure
  - general options, 399–402
  - graphics options, 403–409
  - line-printer options, 410
- PROC GANTT statement, *see* GANTT procedure
  - statement options, 496
- PROC NETDRAW statement, *see* NETDRAW procedure
  - statement options, 672
- PROC PM statement, *see* PM procedure
  - statement options, 304
- PROJ\_NAME= parameter
  - %SASTOMSP macro parameters, 360
- PROJDICT= option
  - Projman, 775
- PROJECT statement
  - CPM procedure, 78
- PROJECT= option
  - PROC PM statement, 304
- PROJECT= parameter
  - %EVG\_WBS\_CHART macro, 894
- PROJECTNAME= option
  - PROC PM statement, 304
- PROJECTSUMMARY= option, *see* SUMMARYNAME= option
- Projman
  - PROJDICT= option, 775
  - project name option, 775
  - projman command, 775
- PROJMAN Application, 774
- PROJNAME= option, *see* PROJECTNAME= option
- PV= parameter
  - %EVA\_METRICS macro, 885
  - %EVA\_PLANNED\_VALUE macro, 881
- QTR keyword
  - INTERVAL= option (CPM), 67
  - MININTERVAL= option (GANTT), 529
  - MININTERVAL= option (NETDRAW), 675
  - PADDING= option (GANTT), 505, 528
  - ROUTINTERVAL= option (CPM), 88
- QUIT keyword
  - ERRHANDLE= option (DTREE), 400
- QUIT statement
  - DTREE procedure, 412
- QUITMISSINGALIGN option
- ACTNET statement (NETDRAW), 676
- R keyword
  - DISPLAY= option (DTREE), 400
- RATE= parameter
  - %EVA\_EARNED\_VALUE macro, 884
  - %EVA\_PLANNED\_VALUE macro, 881
  - %EVA\_TASK\_METRICS macro, 888
- RATEXINT option, *see* TOTUSAGE option
- RBARHT= option
  - CHART statement (GANTT), 522
- RBAROFF= option
  - CHART statement (GANTT), 522
- RC option
  - PROC DTREE statement, 408
  - TREEPLOT statement (DTREE), 414
- RCI option, *see* RESCALINTERSECT option
- RCP option, *see* RCPROFILE option
- RCPROFILE option
  - RESOURCE statement (CPM), 87, 128, 214
- RCS option, *see* RCPROFILE option
- RDUR= option, *see* REMDUR= option
- RDURATION= option, *see* REMDUR= option
- RECALL statement
  - DTREE procedure, 412, 465, 468
- RECTILINEAR option
  - ACTNET statement (NETDRAW), 683, 756
- REF= option
  - CHART statement (GANTT), 505, 508, 570, 590, 628
- REFBREAK option
  - ACTNET statement (NETDRAW), 676, 738
- REFCHAR= option
  - ACTNET statement (NETDRAW), 679, 685
  - CHART statement (GANTT), 505, 508, 518, 557
- REFLABEL option
  - CHART statement (GANTT), 505, 590
- REMDUR= option
  - ACTUAL statement (CPM), 72, 190
- RES statement, *see* RESOURCE statement
- RESCALINT option, *see* RESCALINTERSECT option
- RESCALINTERSECT option
  - RESOURCE statement (CPM), 87
- RESDS= parameter
  - %SASTOMSP macro parameters, 361
- RESET statement
  - DTREE procedure, 412, 440
- RESET= option, GOPTIONS statement
  - GANTT procedure, 539, 541
- RESID= option
  - RESOURCE statement (CPM), 87, 232
- RESIN= option, *see* RESOURCEIN= option
- RESLEVEL keyword

OBSTYPE variable (CPM), 86, 114, 115  
 RESLEVEL= option, *see* RESOURCEIN= option  
 RESOURCE keyword  
   COMPARE= option (CPM), 74  
   PATLEVEL= option (GANTT), 521  
   SET= option (CPM), 75  
   UPDATE= option (CPM), 75  
 RESOURCE statement  
   CPM procedure, 80, 193  
 RESOURCEIN= option  
   PROC CPM statement, 68, 197  
 RESOURCEOUT= option  
   PROC CPM statement, 69, 193  
 RESOURCESCHED= option  
   PROC CPM statement, 69  
 RESOURCEVARS option  
   RESOURCE statement (CPM), 87  
 RESOUT= option, *see* RESOURCEOUT= option  
 RESPTY keyword  
   OBSTYPE variable (CPM), 86, 114, 116  
   SCHEDRULE= option (CPM), 88, 121  
 RESRCDUR keyword  
   OBSTYPE variable (CPM), 86, 114, 116  
 RESSCHED= option, *see* RESOURCESCHED= option  
 RESTRICTSEARCH option  
   ACTNET statement (NETDRAW), 677  
 RESTYPE keyword  
   OBSTYPE variable (CPM), 86, 114, 115  
 RESUSAGE keyword  
   OBSTYPE variable (CPM), 86, 114, 115  
 RESUSAGE= option, *see* RESOURCEOUT= option  
 RESVARSOUT option, *see* RESOURCEVARS option  
 REVERSEY option  
   ACNET statement (NETDRAW), 683  
 REVERSEY= parameter  
   %EVG\_WBS\_CHART macro, 894  
 REVISECOST= parameter  
   %EVA\_EARNED\_VALUE macro, 882  
   %EVA\_TASK\_METRICS macro, 886  
 REVISESCHED= parameter  
   %EVA\_EARNED\_VALUE macro, 882  
   %EVA\_TASK\_METRICS macro, 887  
   %EVG\_GANTT\_CHART macro, 893  
 REWARD keyword  
   MODIFY statement (DTREE), 411  
 REWARD= option  
   VARIABLES statement (DTREE), 415, 439  
 RGHTLEFT keyword  
   CHILDORDER= option (NETDRAW), 674  
 RIGHT keyword  
   ZONESPAN= option (GANTT), 524  
 RIGHT option  
   CHART statement (GANTT), 518, 522


RIN= option, *see* RESOURCEIN= option  
 RJUST option, *see* RIGHT option  
 ROTATE option  
   ACTNET statement (NETDRAW), 683, 697, 765, 767  
 ROTATE= parameter  
   %EVG\_WBS\_CHART macro, 895  
 ROTATETEXT option  
   ACTNET statement (NETDRAW), 684, 694, 697, 765, 767  
 ROTATETEXT= parameter  
   %EVG\_WBS\_CHART macro, 895  
 ROUT= option, *see* RESOURCEOUT= option  
 ROUTCONT option, *see* ROUTNOBREAK option  
 ROUTINTERVAL= option  
   RESOURCE statement (CPM), 88, 128  
 ROUTINTERVAL= parameter  
   %EVA\_EARNED\_VALUE macro, 884  
   %EVA\_PLANNED\_VALUE macro, 881  
 ROUTINTPER= option  
   RESOURCE statement (CPM), 88, 128, 129  
 ROUTNOBREAK option  
   RESOURCE statement (CPM), 88, 128, 207  
 RSCHDORD option, *see* RSCHEDORDER option  
 RSCHDWBS option, *see* RSCHEDWBS option  
 RSCHED= option, *see* RESOURCESCHED= option  
 RSCHEDID= option  
   RESOURCE statement (CPM), 88  
 RSCHEDORDER option  
   PROJECT statement (CPM), 79  
 RSCHEDULE= option, *see* RESOURCESCHED= option  
 RSCHEDWBS option  
   PROJECT statement (CPM), 79  
 RSEARCH option, *see* RESTRICTSEARCH option  
 RSID= option, *see* RSCHEDID= option  
 RSORDER option, *see* RSCHEDORDER option  
 RSWBS option, *see* RSCHEDWBS option  
 RT= option  
   EVALUATE statement (DTREE), 411  
   PROC DTREE statement, 401, 448, 459  
   RESET statement (DTREE), 440  
 RTEXT option, *see* ROTATETEXT option  
 RULE2= option, *see* SCHEDRULE2= option  
 RULE= option, *see* SCHEDRULE= option  
 S= option, *see* SPLIT= option, *see* SKIP= option  
 %SASTOMSP macro parameters  
   ACTDS= parameter, 360  
   CALDS= parameter, 360  
   DBMS= parameter, 364  
   HOLDS= parameter, 360  
   LIBRARY= parameter, 360  
   MDBFILE= parameter, 360

PORT= parameter, 364  
 PROJ\_NAME= parameter, 360  
 RESDS= parameter, 361  
 SCHEDULEDS= parameter, 361  
 SERVER= parameter, 364  
 WORKDS= parameter, 361  
**SAVE** statement  
 DTREE procedure, 413, 465, 468  
**SBARHT**= option, *see* RBARHT= option  
**SBAROFF**= option, *see* RBAROFF= option  
**SCALE**= option  
 CHART statement (GANTT), 501, 504–506, 531, 536, 557, 586, 597  
**SCALE**= parameter  
 %EVG\_GANTT\_CHART macro, 893  
**SCHEDRULE2**= option  
 RESOURCE statement (CPM), 89, 120  
**SCHEDRULE**= option  
 RESOURCE statement (CPM), 88, 120, 198  
**SCHEDULEDS**= parameter  
 %SASTOMSP macro parameters, 361  
**SECOND** keyword  
 INTERVAL= option (CPM), 67  
 MININTERVAL= option (GANTT), 529  
 MININTERVAL= option (NETDRAW), 675  
 PADDING= option (GANTT), 505, 528  
 ROUTINTERVAL= option (CPM), 88  
**SEPARATEARCS** option  
 ACTNET statement (NETDRAW), 684, 691, 715  
**SEPARATESONS** option  
 ACTNET statement (NETDRAW), 677, 697, 758  
**SEPCRIT** option  
 PROJECT statement (CPM), 79  
**SEQ** keyword  
 ALIGNTYPE variable (CPM), 73  
**SERVER**= parameter  
 %MSPTOSAS macro parameters, 355  
 %SASTOMSP macro parameters, 364  
**SET**= option  
 BASELINE statement (CPM), 75, 188  
**SETFINISH**= option  
 RESOURCE statement (CPM), 89  
**SETFINISHMILESTONE** option  
 PROC CPM statement, 69  
**SF** keyword  
 LAG variable (CPM), 91  
 LAG variable (GANTT), 517  
 LAG variable (NETDRAW), 675  
**SF**= option, *see* S\_FINISH= option  
**S\_FINISH**= option  
 CHART statement (GANTT), 505, 607  
**SGE** keyword  
 ALIGNTYPE variable (CPM), 73  
**SHORTDUR** keyword  
 SCHEDRULE= option (CPM), 88, 121  
**SHOWBREAK** option  
 ACTNET statement (NETDRAW), 677, 736  
**SHOWFLOAT** option  
 ACTUAL statement (CPM), 72, 111, 191  
 ACTUAL statement (PM), 305  
**SHOWPREC** option  
 CHART statement (GANTT), 522  
**SHOWSTATUS** option  
 ACTNET statement (NETDRAW), 677, 691, 732  
**SKIP**= option  
 CHART statement (GANTT), 506, 515, 557, 570  
**SLE** keyword  
 ALIGNTYPE variable (CPM), 73  
**SLIPINF** option, *see* DELAYANALYSIS option  
**SPACE** units  
 YBETWEEN= option (DTREE), 402  
**SPANNINGTREE** option  
 ACTNET statement (NETDRAW), 677  
**SPCT**= parameter  
 %EVA\_EARNED\_VALUE macro, 884  
 %EVA\_PLANNED\_VALUE macro, 881  
 %EVA\_TASK\_METRICS macro, 888  
**SPLIT**= option  
 PROC GANTT statement, 498, 610  
**SPLITFLAG** option  
 RESOURCE statement (CPM), 89  
**SS** keyword  
 LAG variable (CPM), 91  
 LAG variable (GANTT), 517  
 LAG variable (NETDRAW), 675  
**SS**= option, *see* S\_START= option  
**SSO** option, *see* SSORDER option  
**SSORDER** option  
 PROJECT statement (CPM), 79  
**S\_START**= option  
 CHART statement (GANTT), 506, 607  
**STAGE** keyword  
 DISPLAY= option (DTREE), 400  
**STAGE**= option  
 VARIABLES statement (DTREE), 415, 439  
**STAGEIN**= option  
 PROC DTREE statement, 401  
**START**= option  
 DURATION statement (CPM), 76  
**START**= parameter  
 %EVA\_EARNED\_VALUE macro, 883  
 %EVA\_PLANNED\_VALUE macro, 879  
 %EVA\_TASK\_METRICS macro, 887  
 %EVG\_GANTT\_CHART macro, 893  
**STATE**= option  
 VARIABLES statement (DTREE), 417, 439  
**STEP**= option, *see* ROUTINTPER= option  
**STEPINT**= option, *see* ROUTINTERVAL= option

STEPSIZE= option, *see* ROUTINPER= option  
 STOPDATE= option  
     RESOURCE statement (CPM), 89, 242  
 STRIPID option, *see* STRIPIDBLANKS option  
 STRIPIDBLANKS option  
     CHART statement (GANTT), 506  
 STRUCTURE= parameter  
     %EVG\_WBS\_CHART macro, 894  
 SUCC statement, *see* SUCCESSOR statement  
 SUCC= option, *see* SUCCESSOR= option, *see*  
     SUCCESSOR= option  
 SUCCESSOR statement  
     CPM procedure, 57, 90, 142  
 SUCCESSOR= option  
     ACTNET statement (NETDRAW), 677, 708  
     CHART statement (GANTT), 490, 523, 546, 619,  
         639  
     VARIABLES statement (DTREE), 416, 439  
 SUMMARY option  
     CHART statement (GANTT), 506, 531, 558, 570  
     EVALUATE statement (DTREE), 411, 468, 475  
     PROC DTREE statement, 401, 463  
 SUMMARY statement  
     DTREE procedure, 413, 439, 448, 463  
 SUMMARY= option, *see* SUMMARYNAME= option  
 SUMMARY= parameter  
     %EVA\_METRICS macro, 886  
     %EVG\_COST\_PLOT macro, 890  
     %EVG\_INDEX\_PLOT macro, 891  
 SUMMARYNAME= option  
     PROC PM statement, 305  
 SUPLEVEL keyword  
     OBSTYPE variable (CPM), 86, 114, 116  
 SUPPRESSOBSWARN option  
     PROC CPM statement, 70  
 SYMBC= option, *see* SYMBOLC= option  
 SYMBD= option, *see* SYMBOLD= option  
 SYMBE= option, *see* SYMBOLE= option  
 SYMBOL statement, 509, 541, 557, 575  
     options, 541  
     syntax, 541  
 SYMBOLC= option  
     PROC DTREE statement, 408  
     TREEPLOT statement (DTREE), 414, 459  
 SYMBOLD= option  
     PROC DTREE statement, 408  
     TREEPLOT statement (DTREE), 414, 459  
 SYMBOLE= option  
     PROC DTREE statement, 409  
     TREEPLOT statement (DTREE), 414, 459  
 SYMCHAR= option  
     CHART statement (GANTT), 508, 509, 557  
 TAIL statement, *see* TAILNODE statement  
 TAIL= option  
     CHART statement (GANTT), 523, 545, 621  
 TAILNODE statement  
     CPM procedure, 56, 91, 146  
 TAILNODE= option, *see* TAIL= option  
 TARGET= option  
     EVALUATE statement (DTREE), 411, 468  
     PROC DTREE statement, 402, 463  
     SUMMARY statement (DTREE), 413, 439, 448,  
         463  
 TASKMETRICS= parameter  
     %EVA\_TASK\_METRICS macro, 888  
     %EVG\_GANTT\_CHART macro, 893  
 TASKPV= parameter  
     %EVA\_EARNED\_VALUE macro, 884  
     %EVA\_PLANNED\_VALUE macro, 882  
 T\_FLOAT option  
     RESOURCE statement (CPM), 89, 226  
 TIMEAXISFORMAT option  
     CHART statement (GANTT), 506  
 TIMENOW= option  
     ACTUAL statement (CPM), 72, 190  
     CHART statement (GANTT), 501, 506, 601, 603  
 TIMENOW= parameter  
     %EVA\_METRICS macro, 886  
     %EVA\_TASK\_METRICS macro, 888  
     %EVG\_GANTT\_CHART macro, 893  
 TIMENOWSPLT option  
     ACTUAL statement (CPM), 72, 112  
 TIMESCALE option  
     ACTNET statement (NETDRAW), 677, 694, 734  
 TJUST option, *see* TOP option  
 TNCHAR= option  
     CHART statement (GANTT), 507, 509, 557  
 TO statement, *see* HEADNODE statement  
 TOLERANCE= option  
     PROC DTREE statement, 402  
 TOP option  
     CHART statement (GANTT), 523  
 TOPDOWN keyword  
     CHILDORDER= option (NETDRAW), 674  
 TOTUSAGE option  
     RESOURCE statement (CPM), 89  
 TREE option  
     ACTNET statement (NETDRAW), 678, 696, 756  
 TREELAYOUT option, *see* TREE option  
 TREEPLOT statement  
     DTREE procedure, 413, 414, 455, 459, 475  
 TYPE keyword  
     MODIFY statement (DTREE), 411  
 TYPE= option  
     VARIABLES statement (DTREE), 416, 439  
 UNSCHEDMISS option

RESOURCE statement (CPM), 90  
 UPDATE= option  
   BASELINE statement (CPM), 75  
 UPDTUNSCHED option  
   RESOURCE statement (CPM), 90  
 USEFORMAT option  
   ACTNET statement (NETDRAW), 678, 760  
   CHART statement (GANTT), 507  
 USEPROJDUR option  
   PROJECT statement (CPM), 80  
 USEPROJDURSPEC option, *see* USEPROJDUR option  
 USESPECUDR option, *see* USEPROJDUR option  
 UTILITY= option, *see* VALUE= option  
 VALUE= option  
   VARIABLES statement (DTREE), 417  
 VARIABLES statement  
   DTREE procedure, 414–417, 439  
 VBETWEEN= option, *see* YBETWEEN= option  
 VC= option, *see* VSYMBOLC= option  
 VD= option, *see* VSYMBOLD= option  
 VE= option, *see* VSYMBOLE= option  
 VERSION= parameter  
   %MSPTOSAS macro parameters, 355  
 VIEWPM= parameter  
   %MSPTOSAS macro parameters, 355  
 VMARGIN= option  
   ACTNET statement (NETDRAW), 684, 734  
 VMILE= option  
   CHART statement (GANTT), 502, 514, 523, 557, 583  
 VPAGES= option  
   ACTNET statement (NETDRAW), 684  
   CHART statement (GANTT), 512, 515, 520, 522, 523, 535, 559, 585  
 VPAGES= parameter  
   %EVG\_GANTT\_CHART macro, 893  
   %EVG\_WBS\_CHART macro, 895  
 VPC statement  
   DTREE procedure, 417, 467  
 VPI statement  
   DTREE procedure, 418, 466  
 VPOS= option, GOPTIONS statement  
   GANTT procedure, 515, 535  
   NETDRAW procedure, 701, 713, 721  
 VSYMBOLC= option  
   PROC DTREE statement, 409  
   TREEPLOT statement (DTREE), 414  
 VSYMBOLD= option  
   PROC DTREE statement, 409  
   TREEPLOT statement (DTREE), 414  
 VSYMBOLE= option  
   PROC DTREE statement, 409  
 WZLINE= option, *see* WZONE= option  
 WZONE= option  
   CHART statement (GANTT), 524, 645  
 XBETWEEN= option  
   ACTNET statement (NETDRAW), 678, 690, 728  
 XFERVARS option

- PROC CPM statement, 70, 186, 487
- PROC PM statement, 305
- XMLFILE= parameter
  - %MSPTOSAS macro parameters, 354
- YBETWEEN= option
  - ACTNET statement (NETDRAW), 678, 690, 722
  - PROC DTREE statement, 402
  - TREEPLOT statement (DTREE), 414, 455, 475
- YEAR keyword
  - INTERVAL= option (CPM), 67
  - MININTERVAL= option (GANTT), 529
  - MININTERVAL= option (NETDRAW), 675
  - PADDING= option (GANTT), 505, 528
  - ROUTINTERVAL= option (CPM), 88
- ZONE keyword
  - CTEXTCOLS= option (GANTT), 513
- ZONE= option
  - ACTNET statement (NETDRAW), 678, 696, 742
  - CHART statement (GANTT), 524, 559
- ZONEDESCR option, *see* ZONELABEL option
- ZONELABEL option
  - ACTNET statement (NETDRAW), 678
- ZONELEVADD option, *see* ZONESPACE option
- ZONELINE= option, *see* ZONESPAN= option
- ZONEOFF= option
  - CHART statement (GANTT), 524, 645
- ZONEOFFSET= option, *see* ZONEOFF= option
- ZONEPAT option
  - ACTNET statement (NETDRAW), 679, 685, 696, 742
- ZONESPACE option
  - ACTNET statement (NETDRAW), 678, 742
- ZONESPAN= option
  - CHART statement (GANTT), 524, 645
- ZONEVAR= option, *see* ZONE= option

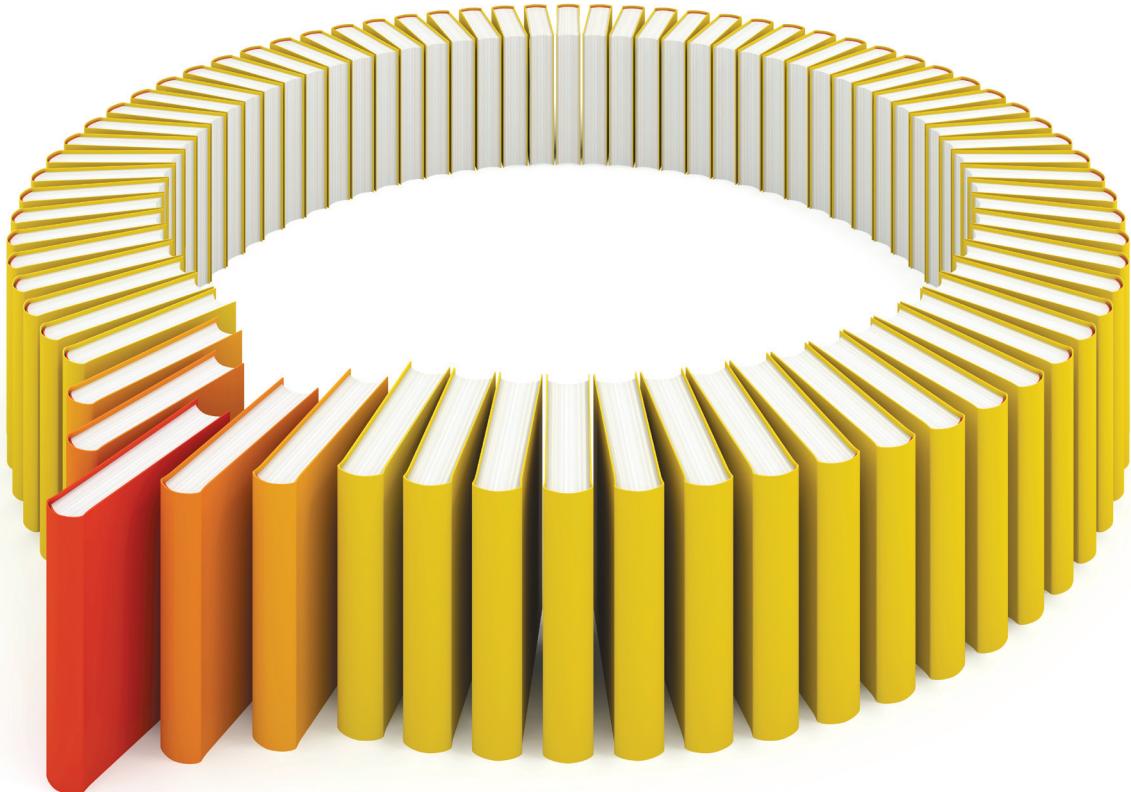

# Gain Greater Insight into Your SAS® Software with SAS Books.

Discover all that you need on your journey to knowledge and empowerment.

 support.sas.com/bookstore  
for additional books and resources.

  
sas®  
THE POWER TO KNOW®
